

District I
1625 N. French Dr., Hobbs, NM 88240
District II
811 S. First St., Artesia, NM 88210
District III
1000 Rio Brazos Rd., Aztec, NM 87410
District IV
1220 S. St. Francis Dr., Santa Fe, NM 87505

State of New Mexico
Energy, Minerals & Natural Resources

Form C-104
Revised August 1, 2011

Oil Conservation Division
1220 South St. Francis Dr.
Santa Fe, NM 87505

Submit one copy to appropriate District Office

☐ AMENDED REPORT

I. REQUEST FOR ALLOWABLE AND AUTHORIZATION TO TRANSPORT

¹ Operator name and Address Franklin Mountain Energy, LLC 44 Cook Street, Suite 1000 Denver, CO 80206		² OGRID Number 373910	
		³ Reason for Filing Code/ Effective Date RT - Test Allowable	
⁴ API Number 30 – 025-47663	⁵ Pool Name WC-025 G-09 S253502D; UPR WOLFCAMP		⁶ Pool Code 98187
⁷ Property Code 329324	⁸ Property Name BLUE RIBBON FED COM		⁹ Well Number 703H

II. ¹⁰ Surface Location

UL or lot no. C	Section 2	Township 25S	Range 35E	Lot Idn 3	Feet from the 675	North/South Line FNL	Feet from the 2623	East/West line FWL	County Lea
--------------------	--------------	-----------------	--------------	--------------	----------------------	-------------------------	-----------------------	-----------------------	---------------

¹¹ Bottom Hole Location

UL or lot no. N	Section 11	Township 25S	Range 35E	Lot Idn	Feet from the 150	North/South line FSL	Feet from the 2610	East/West line FWL	County Lea
¹² Lse Code S & F	¹³ Producing Method Code F	¹⁴ Gas Connection Date TBD	¹⁵ C-129 Permit Number N/A		¹⁶ C-129 Effective Date N/A		¹⁷ C-129 Expiration Date N/A		


III. Oil and Gas Transporters

¹⁸ Transporter OGRID	¹⁹ Transporter Name and Address	²⁰ O/G/W
35246	SHELL TRADING US COMPANY 1000 Main, 12th Floor, Houston, TX 77002	O
371960	LUCID ENERGY DELAWARE, LLC 3100 McKinnon St, Suite 800 Dallas, Texas 75201	G
	** TEST ALLOWABLE **	

IV. Well Completion Data

²¹ Spud Date 10/20/2020	²² Ready Date 3/2/2021	²³ TD 22,144'	²⁴ PBTD 22,028'	²⁵ Perforations	²⁶ DHC, MC
²⁷ Hole Size		²⁸ Casing & Tubing Size	²⁹ Depth Set		³⁰ Sacks Cement
17 1/2"		13 3/8"	1,332'		1230
12 1/4"		9 5/8"	5,434'		700
8 1/2"		7 5/8"	12,129'		872
6 3/4"		5 1/2"	22,120'		916

V. Well Test Data

³¹ Date New Oil	³² Gas Delivery Date	³³ Test Date	³⁴ Test Length	³⁵ Tbg. Pressure	³⁶ Csg. Pressure
³⁷ Choke Size	³⁸ Oil	³⁹ Water	⁴⁰ Gas		⁴¹ Test Method
⁴² I hereby certify that the rules of the Oil Conservation Division have been complied with and that the information given above is true and complete to the best of my knowledge and belief. Signature: 			OIL CONSERVATION DIVISION		
Printed name: Rachael Overbey			Approved by: KURT SIMMONS		
Title: Director, Ops Planning & Regulatory			Title: NMOCD, SANTA FE		
E-mail Address: roverbey@femllc.com			Approval Date: 09/08/2021		
Date: 7/29/2021		Phone: 303-570-4057	RT C-104 EXPIRES 11/08/2021		

District I
1625 N. French Dr., Hobbs, NM 88240
Phone: (575) 393-6161 Fax: (575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone: (575) 748-1283 Fax: (575) 748-9720
District III
1000 Rio Brazos Road, Aztec, NM 87410
Phone: (505) 334-6178 Fax: (505) 334-6170
District IV
1220 S. St. Francis Dr., Santa Fe, NM 87505
Phone: (505) 476-3460 Fax: (505) 476-3462

State of New Mexico
Energy, Minerals & Natural Resources Department
OIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, NM 87505

Form C-102
Revised August 1, 2011
Submit one copy to appropriate
District Office
☐ AMENDED REPORT

WELL LOCATION AND ACREAGE DEDICATION PLAT

¹ API Number 30-025-47663		² Pool Code 98187		³ Pool Name WC-025 G-09 S253502D; UPR WOLFCAMP	
⁴ Property Code 329324		⁵ Property Name BLUE RIBBON FED COM			⁶ Well Number 703H
⁷ OGRID No. 373910		⁸ Operator Name FRANKLIN MOUNTAIN ENERGY LLC			⁹ Elevation 3246.1'


¹⁰ Surface Location

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
3	2	25S	35E		674	NORTH	2623	WEST	LEA

¹¹ Bottom Hole Location If Different From Surface

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
N	11	25S	35E		153	SOUTH	2262	WEST	LEA
¹² Dedicated Acres 320.87		¹³ Joint or Infill		¹⁴ Consolidation Code		¹⁵ Order No.			

No allowable will be assigned to this completion until all interests have been consolidated or a non-standard unit has been approved by the division.

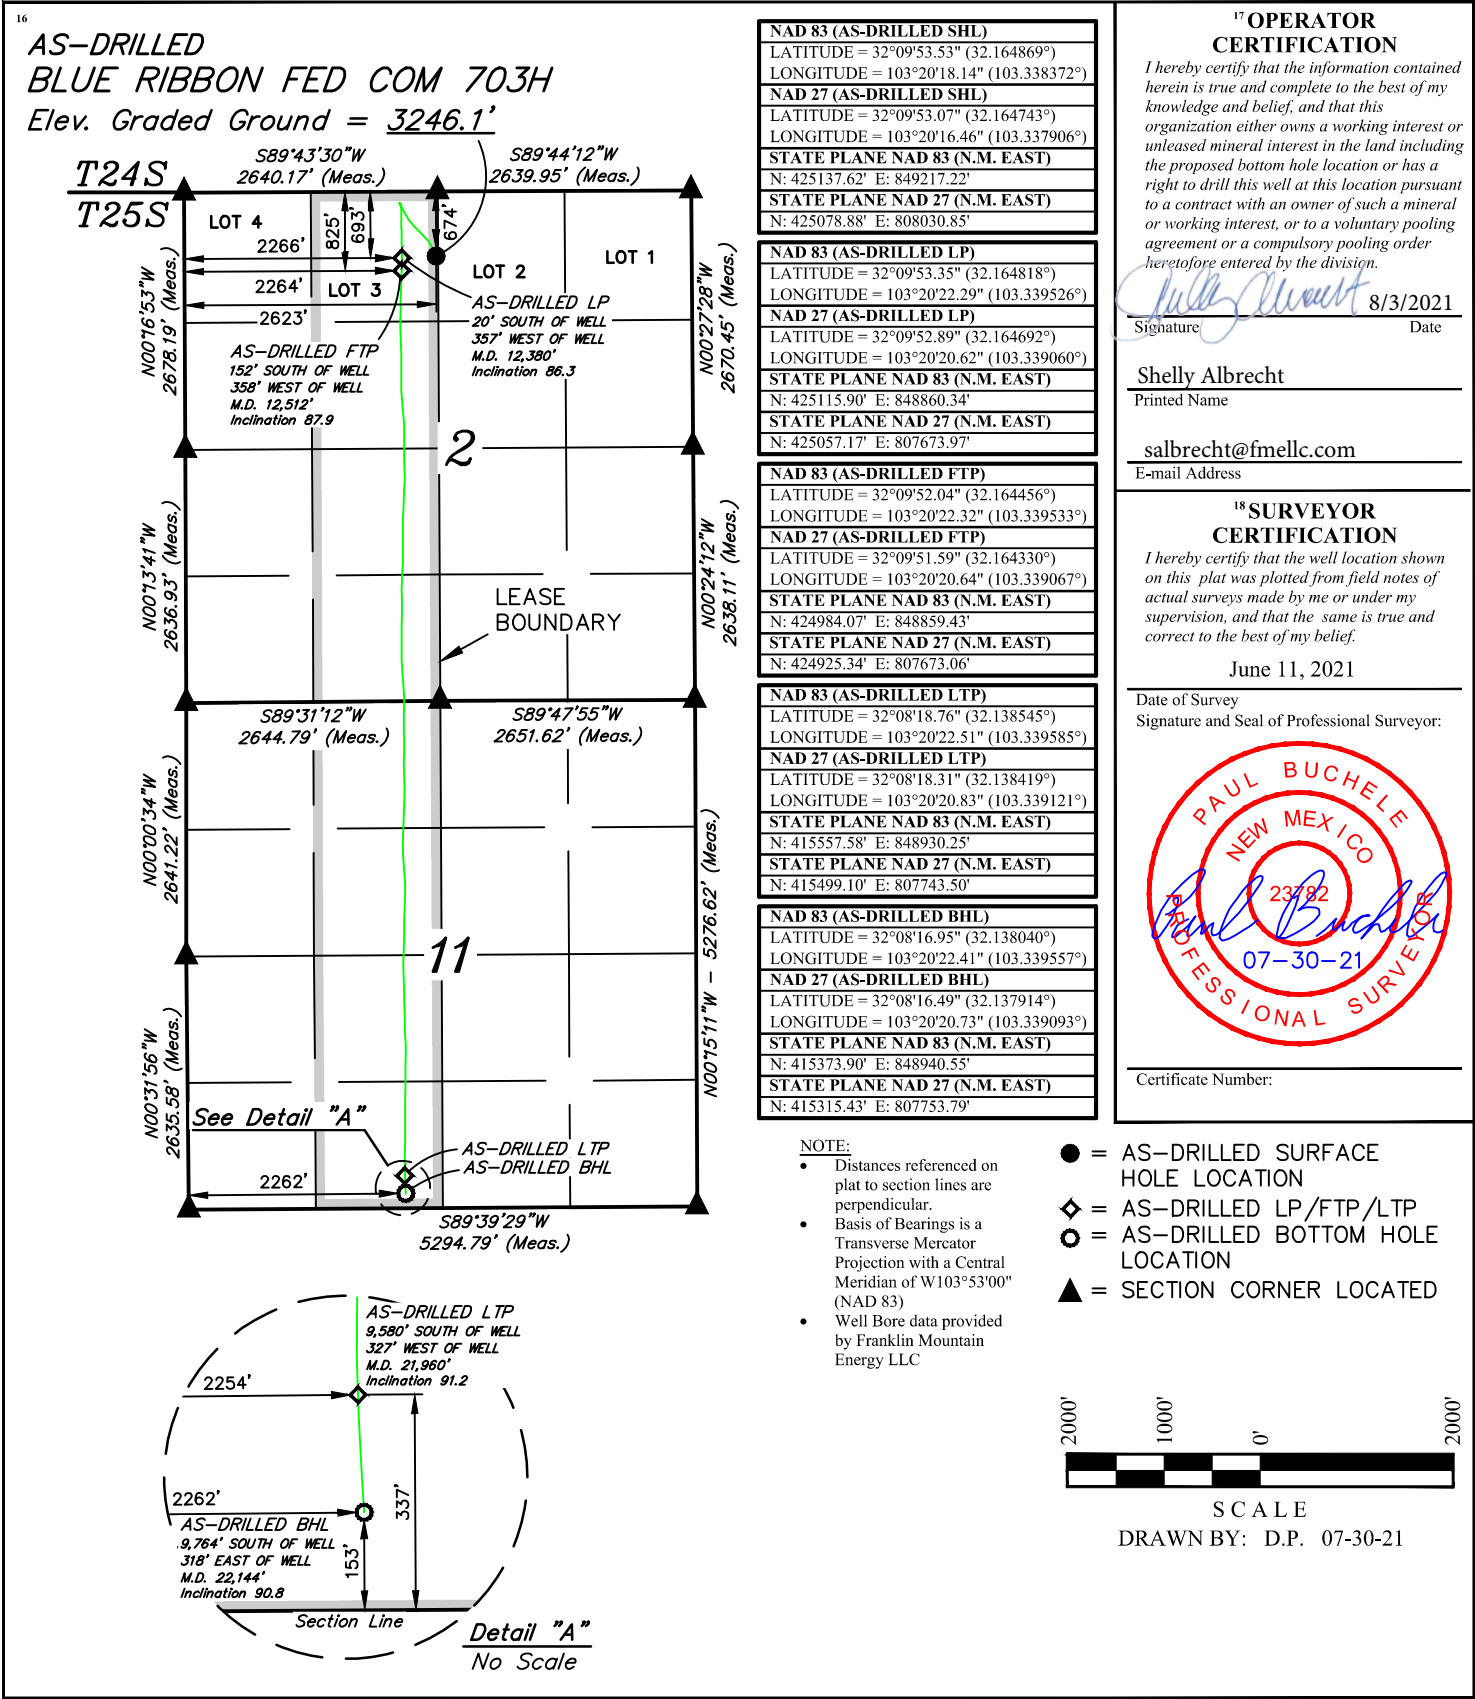



Franklin Mountain Energy

Lea County, NM (NAD83)

Blue Ribbon/Parade State

Blue Ribbon Fed Com 703H

OH

Design: OH

Standard Survey Report

09 March, 2021





Total Directional Services

Survey Report



Company:	Franklin Mountain Energy	Local Co-ordinate Reference:	Well Blue Ribbon Fed Com 703H
Project:	Lea County, NM (NAD83)	TVD Reference:	3245.2' GE + 30' KB @ 3275.20usft
Site:	Blue Ribbon/Parade State	MD Reference:	3245.2' GE + 30' KB @ 3275.20usft
Well:	Blue Ribbon Fed Com 703H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM 5000.15 Single User Db

Project	Lea County, NM (NAD83)		
Map System:	US State Plane 1983	System Datum:	Mean Sea Level
Geo Datum:	North American Datum 1983		
Map Zone:	New Mexico Eastern Zone		

Site		Blue Ribbon/Parade State			
Site Position:		Northing:	425,136.81 usft	Latitude:	32.164867
From:	Map	Easting:	849,217.25 usft	Longitude:	-103.338372
Position Uncertainty:	0.00 usft	Slot Radius:	13-3/16 "	Grid Convergence:	0.53 °

Well	Blue Ribbon Fed Com 703H					
Well Position	+N/-S	0.00 usft	Northing:	425,136.81 usft	Latitude:	32.164867
	+E/-W	0.00 usft	Easting:	849,217.25 usft	Longitude:	-103.338372
Position Uncertainty		0.00 usft	Wellhead Elevation:	usft	Ground Level:	3,245.20 usft

Wellbore	OH				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	IGRF2020	1/16/2021	6.48	59.90	47,526.52564307

Design	OH				
Audit Notes:					
Version:	1.0	Phase:	ACTUAL	Tie On Depth:	0.00
Vertical Section:	Depth From (TVD) (usft)	+N/-S (usft)	+E/-W (usft)	Direction (°)	
	0.00	0.00	0.00	179.50	

Survey Program	Date	3/9/2021			
From (usft)	To (usft)	Survey (Wellbore)	Tool Name	Description	
64.00	1,289.00	Survey #1 - MWD (OH)	MWD	OWSG MWD - Standard	
1,327.00	22,089.00	Survey #2 - MWD (OH)	OWSG (Rev2) MWD	OWSG MWD - Standard	
22,144.00	22,144.00	Survey #3 - Proj to TD (OH)	BLIND	OWSG BLIND	

Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
SHL (Blue Ribbon Fed Com 703H)										
64.00	0.50	320.52	64.00	0.22	-0.18	-0.22	0.78	0.78	0.00	
92.00	0.40	55.52	92.00	0.37	-0.17	-0.37	2.38	-0.36	339.29	
125.00	0.60	186.52	125.00	0.26	-0.10	-0.26	2.77	0.61	396.97	
236.00	0.50	183.52	235.99	-0.80	-0.20	0.80	0.09	-0.09	-2.70	
333.00	1.00	190.52	332.98	-2.06	-0.38	2.05	0.52	0.52	7.22	
427.00	1.50	171.52	426.96	-4.08	-0.34	4.08	0.68	0.53	-20.21	
522.00	1.80	185.52	521.92	-6.80	-0.30	6.79	0.53	0.32	14.74	



Total Directional Services

Survey Report



Company:	Franklin Mountain Energy	Local Co-ordinate Reference:	Well Blue Ribbon Fed Com 703H
Project:	Lea County, NM (NAD83)	TVD Reference:	3245.2' GE + 30' KB @ 3275.20usft
Site:	Blue Ribbon/Parade State	MD Reference:	3245.2' GE + 30' KB @ 3275.20usft
Well:	Blue Ribbon Fed Com 703H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM 5000.15 Single User Db

Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
584.00	1.60	186.52	583.90	-8.62	-0.50	8.62	0.33	-0.32	1.61	
647.00	1.60	183.52	646.87	-10.38	-0.65	10.37	0.13	0.00	-4.76	
679.00	1.70	168.52	678.86	-11.29	-0.58	11.28	1.38	0.31	-46.88	
710.00	1.70	183.52	709.84	-12.20	-0.52	12.19	1.43	0.00	48.39	
742.00	1.80	175.52	741.83	-13.17	-0.51	13.17	0.82	0.31	-25.00	
773.00	2.20	182.52	772.81	-14.25	-0.50	14.25	1.51	1.29	22.58	
805.00	2.00	168.52	804.79	-15.41	-0.41	15.41	1.72	-0.63	-43.75	
836.00	1.50	180.52	835.77	-16.35	-0.31	16.34	1.99	-1.61	38.71	
867.00	1.40	168.52	866.77	-17.12	-0.24	17.12	1.03	-0.32	-38.71	
899.00	1.80	180.52	898.75	-18.01	-0.16	18.01	1.62	1.25	37.50	
930.00	2.00	173.52	929.74	-19.03	-0.11	19.03	0.99	0.65	-22.58	
962.00	1.70	158.52	961.72	-20.03	0.13	20.03	1.77	-0.94	-46.88	
993.00	1.70	176.52	992.71	-20.92	0.33	20.92	1.72	0.00	58.06	
1,025.00	2.00	165.52	1,024.69	-21.93	0.49	21.94	1.45	0.94	-34.38	
1,056.00	1.80	172.52	1,055.67	-22.94	0.69	22.94	0.99	-0.65	22.58	
1,088.00	1.70	180.52	1,087.66	-23.91	0.75	23.92	0.82	-0.31	25.00	
1,119.00	1.10	190.52	1,118.65	-24.66	0.69	24.67	2.08	-1.94	32.26	
1,151.00	0.70	164.52	1,150.64	-25.15	0.69	25.16	1.76	-1.25	-81.25	
1,182.00	0.70	175.52	1,181.64	-25.53	0.76	25.53	0.43	0.00	35.48	
1,214.00	0.50	157.52	1,213.64	-25.85	0.82	25.86	0.85	-0.63	-56.25	
1,245.00	0.40	189.52	1,244.64	-26.08	0.86	26.09	0.86	-0.32	103.23	
1,277.00	0.70	243.52	1,276.64	-26.28	0.67	26.28	1.77	0.94	168.75	
1,289.00	0.70	196.52	1,288.64	-26.38	0.58	26.39	4.65	0.00	-391.67	
1,327.00	0.70	99.60	1,326.64	-26.64	0.74	26.65	2.76	0.00	-255.05	
1,421.00	0.70	203.40	1,420.63	-27.27	1.08	27.27	1.17	0.00	110.43	
1,515.00	0.60	226.60	1,514.63	-28.13	0.49	28.13	0.30	-0.11	24.68	
1,609.00	0.60	212.10	1,608.62	-28.89	-0.12	28.88	0.16	0.00	-15.43	
1,703.00	0.50	213.10	1,702.62	-29.65	-0.61	29.64	0.11	-0.11	1.06	
1,797.00	0.40	195.90	1,796.61	-30.31	-0.92	30.30	0.18	-0.11	-18.30	
1,892.00	0.20	113.80	1,891.61	-30.69	-0.86	30.68	0.44	-0.21	-86.42	
1,987.00	0.30	101.50	1,986.61	-30.81	-0.47	30.80	0.12	0.11	-12.95	
2,081.00	0.30	63.40	2,080.61	-30.75	-0.01	30.75	0.21	0.00	-40.53	
2,175.00	0.40	74.50	2,174.61	-30.55	0.53	30.55	0.13	0.11	11.81	
2,270.00	0.50	52.70	2,269.60	-30.21	1.18	30.22	0.21	0.11	-22.95	
2,364.00	0.50	59.80	2,363.60	-29.75	1.86	29.77	0.07	0.00	7.55	
2,458.00	0.60	42.30	2,457.60	-29.18	2.55	29.21	0.21	0.11	-18.62	
2,552.00	0.60	48.20	2,551.59	-28.49	3.24	28.52	0.07	0.00	6.28	
2,647.00	1.60	344.70	2,646.58	-26.88	3.26	26.91	1.51	1.05	-66.84	
2,741.00	3.80	340.50	2,740.47	-22.68	1.88	22.69	2.35	2.34	-4.47	
2,835.00	5.10	341.20	2,834.18	-15.79	-0.51	15.78	1.38	1.38	0.74	
2,930.00	6.10	336.00	2,928.73	-7.18	-3.92	7.14	1.18	1.05	-5.47	
3,024.00	7.40	326.30	3,022.08	2.42	-9.31	-2.50	1.83	1.38	-10.32	
3,118.00	9.30	327.10	3,115.08	13.84	-16.80	-13.98	2.03	2.02	0.85	



Total Directional Services

Survey Report



Company:	Franklin Mountain Energy	Local Co-ordinate Reference:	Well Blue Ribbon Fed Com 703H
Project:	Lea County, NM (NAD83)	TVD Reference:	3245.2' GE + 30' KB @ 3275.20usft
Site:	Blue Ribbon/Parade State	MD Reference:	3245.2' GE + 30' KB @ 3275.20usft
Well:	Blue Ribbon Fed Com 703H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM 5000.15 Single User Db

Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
3,213.00	9.90	334.60	3,208.75	27.66	-24.47	-27.87	1.46	0.63	7.89	
3,307.00	9.40	342.00	3,301.42	42.26	-30.31	-42.52	1.42	-0.53	7.87	
3,401.00	9.30	350.60	3,394.18	57.05	-33.92	-57.35	1.49	-0.11	9.15	
3,496.00	8.80	348.60	3,487.99	71.75	-36.61	-72.07	0.62	-0.53	-2.11	
3,590.00	9.30	336.10	3,580.83	85.74	-41.11	-86.10	2.15	0.53	-13.30	
3,685.00	9.70	334.30	3,674.53	99.97	-47.69	-100.39	0.52	0.42	-1.89	
3,779.00	9.70	329.00	3,767.19	113.90	-55.20	-114.38	0.95	0.00	-5.64	
3,873.00	9.40	327.10	3,859.89	127.13	-63.45	-127.68	0.46	-0.32	-2.02	
3,968.00	8.70	329.90	3,953.70	139.86	-71.27	-140.48	0.87	-0.74	2.95	
4,062.00	7.80	327.80	4,046.73	151.41	-78.23	-152.09	1.01	-0.96	-2.23	
4,157.00	9.10	318.90	4,140.70	162.53	-86.61	-163.28	1.94	1.37	-9.37	
4,251.00	10.30	313.60	4,233.36	173.92	-97.58	-174.77	1.59	1.28	-5.64	
4,345.00	9.50	314.80	4,325.96	185.19	-109.17	-186.13	0.88	-0.85	1.28	
4,440.00	9.00	315.30	4,419.72	195.99	-119.96	-197.03	0.53	-0.53	0.53	
4,534.00	9.60	316.90	4,512.48	206.94	-130.49	-208.07	0.69	0.64	1.70	
4,629.00	9.80	319.10	4,606.13	218.84	-141.20	-220.06	0.44	0.21	2.32	
4,723.00	9.00	316.60	4,698.86	230.23	-151.49	-231.54	0.96	-0.85	-2.66	
4,818.00	8.40	315.20	4,792.77	240.55	-161.48	-241.95	0.67	-0.63	-1.47	
4,912.00	9.80	315.20	4,885.59	251.10	-171.96	-252.59	1.49	1.49	0.00	
5,006.00	10.40	316.00	4,978.13	262.88	-183.49	-264.47	0.66	0.64	0.85	
5,101.00	9.90	315.90	5,071.64	274.91	-195.13	-276.60	0.53	-0.53	-0.11	
5,195.00	8.90	315.90	5,164.38	285.93	-205.81	-287.72	1.06	-1.06	0.00	
5,290.00	8.10	315.30	5,258.33	295.97	-215.63	-297.84	0.85	-0.84	-0.63	
5,381.00	8.00	315.10	5,348.44	305.01	-224.61	-306.96	0.11	-0.11	-0.22	
5,483.00	7.90	312.90	5,449.46	314.81	-234.76	-316.85	0.31	-0.10	-2.16	
5,577.00	8.80	318.80	5,542.46	324.62	-244.23	-326.74	1.32	0.96	6.28	
5,671.00	9.10	318.40	5,635.32	335.59	-253.90	-337.79	0.33	0.32	-0.43	
5,765.00	9.10	317.10	5,728.13	346.59	-263.89	-348.88	0.22	0.00	-1.38	
5,860.00	9.40	322.10	5,821.90	358.22	-273.77	-360.59	0.90	0.32	5.26	
5,954.00	8.90	320.80	5,914.70	369.91	-283.08	-372.37	0.58	-0.53	-1.38	
6,049.00	9.90	332.20	6,008.43	382.83	-291.54	-385.36	2.22	1.05	12.00	
6,143.00	10.10	331.80	6,101.01	397.24	-299.20	-399.84	0.23	0.21	-0.43	
6,237.00	10.50	330.40	6,193.49	411.95	-307.33	-414.62	0.50	0.43	-1.49	
6,332.00	10.70	329.60	6,286.87	427.09	-316.06	-429.83	0.26	0.21	-0.84	
6,426.00	11.00	328.30	6,379.19	442.24	-325.19	-445.06	0.41	0.32	-1.38	
6,520.00	11.00	327.40	6,471.46	457.43	-334.74	-460.33	0.18	0.00	-0.96	
6,615.00	11.10	327.20	6,564.70	472.75	-344.57	-475.74	0.11	0.11	-0.21	
6,709.00	9.90	330.10	6,657.13	487.36	-353.50	-490.43	1.39	-1.28	3.09	
6,803.00	9.90	330.70	6,749.73	501.41	-361.49	-504.55	0.11	0.00	0.64	
6,897.00	8.40	334.90	6,842.53	514.68	-368.35	-517.87	1.75	-1.60	4.47	
6,992.00	7.40	331.80	6,936.63	526.35	-374.19	-529.60	1.14	-1.05	-3.26	
7,086.00	6.20	329.80	7,029.96	536.08	-379.60	-539.37	1.30	-1.28	-2.13	
7,180.00	3.90	332.00	7,123.59	543.29	-383.66	-546.61	2.46	-2.45	2.34	
7,275.00	3.30	335.80	7,218.41	548.63	-386.30	-551.98	0.68	-0.63	4.00	



Total Directional Services

Survey Report



Company:	Franklin Mountain Energy	Local Co-ordinate Reference:	Well Blue Ribbon Fed Com 703H
Project:	Lea County, NM (NAD83)	TVD Reference:	3245.2' GE + 30' KB @ 3275.20usft
Site:	Blue Ribbon/Parade State	MD Reference:	3245.2' GE + 30' KB @ 3275.20usft
Well:	Blue Ribbon Fed Com 703H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM 5000.15 Single User Db

Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
7,369.00	1.60	338.10	7,312.32	552.32	-387.89	-555.68	1.81	-1.81	2.45
7,464.00	0.40	321.10	7,407.30	553.81	-388.60	-557.18	1.29	-1.26	-17.89
7,558.00	0.30	258.80	7,501.30	554.02	-389.04	-557.39	0.40	-0.11	-66.28
7,652.00	0.40	256.60	7,595.30	553.89	-389.61	-557.27	0.11	0.11	-2.34
7,747.00	0.70	61.90	7,690.29	554.09	-389.42	-557.47	1.15	0.32	174.00
7,841.00	0.70	77.50	7,784.29	554.48	-388.35	-557.85	0.20	0.00	16.60
7,936.00	0.70	86.90	7,879.28	554.64	-387.20	-558.00	0.12	0.00	9.89
8,030.00	0.70	100.80	7,973.27	554.56	-386.07	-557.91	0.18	0.00	14.79
8,125.00	0.80	108.20	8,068.27	554.25	-384.87	-557.59	0.15	0.11	7.79
8,220.00	0.80	113.10	8,163.26	553.78	-383.63	-557.11	0.07	0.00	5.16
8,314.00	1.00	124.90	8,257.25	553.05	-382.35	-556.37	0.29	0.21	12.55
8,409.00	1.00	125.00	8,352.23	552.10	-380.99	-555.41	0.00	0.00	0.11
8,503.00	1.10	132.60	8,446.21	551.02	-379.65	-554.32	0.18	0.11	8.09
8,597.00	1.20	140.10	8,540.20	549.66	-378.36	-552.94	0.19	0.11	7.98
8,692.00	0.90	153.80	8,635.18	548.22	-377.39	-551.50	0.41	-0.32	14.42
8,786.00	0.90	156.50	8,729.17	546.89	-376.77	-550.15	0.05	0.00	2.87
8,880.00	0.70	164.00	8,823.16	545.66	-376.32	-548.92	0.24	-0.21	7.98
8,974.00	0.70	181.00	8,917.15	544.53	-376.17	-547.79	0.22	0.00	18.09
9,069.00	0.70	190.40	9,012.15	543.38	-376.28	-546.64	0.12	0.00	9.89
9,163.00	0.80	199.10	9,106.14	542.19	-376.60	-545.46	0.16	0.11	9.26
9,257.00	0.90	200.90	9,200.13	540.88	-377.08	-544.15	0.11	0.11	1.91
9,352.00	0.80	192.40	9,295.12	539.54	-377.49	-542.81	0.17	-0.11	-8.95
9,446.00	0.10	240.50	9,389.11	538.86	-377.70	-542.13	0.78	-0.74	51.17
9,540.00	0.50	306.10	9,483.11	539.06	-378.10	-542.34	0.50	0.43	69.79
9,635.00	0.60	337.40	9,578.11	539.76	-378.63	-543.05	0.33	0.11	32.95
9,729.00	0.60	341.10	9,672.10	540.68	-378.98	-543.97	0.04	0.00	3.94
9,824.00	0.60	327.40	9,767.10	541.57	-379.41	-544.86	0.15	0.00	-14.42
9,918.00	1.30	300.30	9,861.08	542.53	-380.59	-545.83	0.87	0.74	-28.83
10,012.00	0.75	242.73	9,955.07	542.78	-382.06	-546.09	1.17	-0.59	-61.24
10,106.00	0.97	203.53	10,049.06	541.77	-382.93	-545.09	0.65	0.23	-41.70
10,201.00	0.48	180.41	10,144.05	540.63	-383.25	-543.96	0.59	-0.52	-24.34
10,295.00	0.48	129.26	10,238.05	539.99	-382.95	-543.31	0.44	0.00	-54.41
10,389.00	0.97	119.86	10,332.04	539.35	-381.95	-542.66	0.53	0.52	-10.00
10,484.00	1.32	123.81	10,427.02	538.34	-380.35	-541.64	0.38	0.37	4.16
10,578.00	0.66	108.69	10,521.01	537.56	-378.93	-540.85	0.75	-0.70	-16.09
10,673.00	0.97	122.76	10,616.00	536.95	-377.74	-540.23	0.39	0.33	14.81
10,767.00	1.23	104.74	10,709.98	536.26	-376.09	-539.53	0.46	0.28	-19.17
10,861.00	0.62	76.09	10,803.97	536.13	-374.63	-539.38	0.80	-0.65	-30.48
10,955.00	0.92	295.29	10,897.97	536.57	-374.81	-539.82	1.55	0.32	-149.79
11,049.00	1.54	299.77	10,991.94	537.52	-376.59	-540.79	0.67	0.66	4.77
11,143.00	1.93	60.71	11,085.92	538.93	-376.31	-542.19	3.22	0.41	128.66
11,238.00	1.85	109.66	11,180.88	539.19	-373.47	-542.43	1.65	-0.08	51.53
11,332.00	2.55	158.88	11,274.81	536.73	-371.29	-539.95	2.06	0.74	52.36



Total Directional Services

Survey Report



Company:	Franklin Mountain Energy	Local Co-ordinate Reference:	Well Blue Ribbon Fed Com 703H
Project:	Lea County, NM (NAD83)	TVD Reference:	3245.2' GE + 30' KB @ 3275.20usft
Site:	Blue Ribbon/Parade State	MD Reference:	3245.2' GE + 30' KB @ 3275.20usft
Well:	Blue Ribbon Fed Com 703H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM 5000.15 Single User Db

Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
11,426.00	2.86	164.59	11,368.71	532.52	-369.91	-535.73	0.44	0.33	6.07
11,477.00	3.12	164.94	11,419.64	529.95	-369.21	-533.15	0.51	0.51	0.69
11,522.00	5.27	177.95	11,464.52	526.70	-368.82	-529.90	5.20	4.78	28.91
11,569.00	8.79	175.05	11,511.16	520.97	-368.43	-524.16	7.52	7.49	-6.17
11,616.00	12.44	175.93	11,557.35	512.34	-367.76	-515.53	7.77	7.77	1.87
11,663.00	16.31	176.37	11,602.87	500.70	-366.99	-503.88	8.24	8.23	0.94
11,711.00	19.25	178.66	11,648.57	486.06	-366.37	-489.24	6.29	6.13	4.77
11,758.00	23.08	179.09	11,692.39	469.09	-366.05	-472.27	8.16	8.15	0.91
11,805.00	27.52	178.83	11,734.87	449.02	-365.68	-452.19	9.45	9.45	-0.55
11,852.00	32.92	181.73	11,775.47	425.38	-365.84	-428.55	11.90	11.49	6.17
11,900.00	38.07	182.35	11,814.54	397.53	-366.84	-400.72	10.76	10.73	1.29
11,947.00	43.52	179.36	11,850.11	366.85	-367.26	-370.04	12.32	11.60	-6.36
11,994.00	48.35	177.25	11,882.79	333.10	-366.23	-336.29	10.77	10.28	-4.49
12,041.00	53.98	177.34	11,912.25	296.55	-364.51	-299.72	11.98	11.98	0.19
12,085.00	58.11	178.04	11,936.82	260.09	-363.04	-263.25	9.48	9.39	1.59
12,132.00	62.33	178.39	11,960.16	219.33	-361.77	-222.47	9.00	8.98	0.74
12,179.00	70.33	180.06	11,979.01	176.32	-361.21	-179.47	17.33	17.02	3.55
12,226.00	79.60	178.83	11,991.19	130.98	-360.76	-134.13	19.88	19.72	-2.62
12,271.00	81.98	178.48	11,998.40	86.58	-359.72	-89.71	5.34	5.29	-0.78
12,318.00	82.77	178.13	12,004.63	40.01	-358.34	-43.14	1.84	1.68	-0.74
12,363.00	85.89	178.48	12,009.08	-4.74	-357.02	1.62	6.98	6.93	0.78
12,380.87	86.35	178.89	12,010.28	-22.56	-356.61	19.45	3.45	2.60	2.27
LP (Blue Ribbon Fed Com 703H)									
12,456.00	88.31	180.59	12,013.78	-97.61	-356.26	94.49	3.45	2.60	2.27
12,548.00	87.65	182.52	12,017.03	-189.51	-358.76	186.37	2.22	-0.72	2.10
12,639.00	88.04	182.35	12,020.45	-280.36	-362.62	277.19	0.47	0.43	-0.19
12,732.00	88.31	182.26	12,023.41	-373.24	-366.36	370.03	0.31	0.29	-0.10
12,826.00	88.22	180.15	12,026.26	-467.17	-368.34	463.94	2.25	-0.10	-2.24
12,919.00	89.01	180.76	12,028.50	-560.14	-369.07	556.90	1.07	0.85	0.66
13,012.00	89.80	181.56	12,029.47	-653.12	-370.96	649.85	1.21	0.85	0.86
13,104.00	89.45	178.04	12,030.07	-745.10	-370.64	741.84	3.84	-0.38	-3.83
13,197.00	91.16	177.78	12,029.58	-838.03	-367.25	834.79	1.86	1.84	-0.28
13,290.00	92.31	178.22	12,026.76	-930.93	-364.00	927.72	1.32	1.24	0.47
13,383.00	93.32	178.57	12,022.19	-1,023.78	-361.40	1,020.59	1.15	1.09	0.38
13,476.00	92.40	180.68	12,017.55	-1,116.66	-360.79	1,113.47	2.47	-0.99	2.27
13,570.00	86.99	179.27	12,018.05	-1,210.62	-360.75	1,207.42	5.95	-5.76	-1.50
13,650.03	86.88	179.19	12,022.33	-1,290.53	-359.68	1,287.34	0.17	-0.14	-0.10
TGT 1 (1287' VS)									
13,664.00	86.86	179.18	12,023.10	-1,304.47	-359.48	1,301.29	0.17	-0.14	-0.10
13,756.00	87.25	178.74	12,027.82	-1,396.34	-357.81	1,393.16	0.64	0.42	-0.48
13,850.00	87.30	175.23	12,032.29	-1,490.09	-352.88	1,486.95	3.73	0.05	-3.73
13,943.00	87.82	173.65	12,036.25	-1,582.56	-343.87	1,579.50	1.79	0.56	-1.70
14,035.00	91.56	174.17	12,036.75	-1,674.02	-334.12	1,671.04	4.10	4.07	0.57
14,128.00	94.86	178.48	12,031.54	-1,766.65	-328.16	1,763.72	5.83	3.55	4.63



Total Directional Services

Survey Report



Company:	Franklin Mountain Energy	Local Co-ordinate Reference:	Well Blue Ribbon Fed Com 703H
Project:	Lea County, NM (NAD83)	TVD Reference:	3245.2' GE + 30' KB @ 3275.20usft
Site:	Blue Ribbon/Parade State	MD Reference:	3245.2' GE + 30' KB @ 3275.20usft
Well:	Blue Ribbon Fed Com 703H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM 5000.15 Single User Db

Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
14,221.00	90.73	179.89	12,027.01	-1,859.51	-326.84	1,856.59	4.69	-4.44	1.52
14,315.00	93.41	180.24	12,023.61	-1,953.44	-326.95	1,950.51	2.88	2.85	0.37
14,408.00	90.73	180.24	12,020.25	-2,046.37	-327.34	2,043.43	2.88	-2.88	0.00
14,502.00	91.69	177.60	12,018.27	-2,140.32	-325.57	2,137.40	2.99	1.02	-2.81
14,596.00	91.74	176.63	12,015.45	-2,234.16	-320.84	2,231.27	1.03	0.05	-1.03
14,690.00	91.38	181.91	12,012.89	-2,328.08	-319.64	2,325.21	5.63	-0.38	5.62
14,783.00	92.31	182.87	12,009.90	-2,420.95	-323.52	2,418.04	1.44	1.00	1.03
14,845.97	91.21	182.46	12,007.97	-2,483.82	-326.44	2,480.88	1.87	-1.75	-0.66
TGT 2 (2480' VS)									
14,876.00	90.68	182.26	12,007.47	-2,513.82	-327.68	2,510.87	1.87	-1.75	-0.66
14,970.00	89.63	182.52	12,007.22	-2,607.74	-331.60	2,604.75	1.15	-1.12	0.28
15,045.00	92.92	181.20	12,005.55	-2,682.67	-334.03	2,679.65	4.73	4.39	-1.76
15,091.00	94.55	181.91	12,002.55	-2,728.55	-335.28	2,725.52	3.86	3.54	1.54
15,184.00	91.96	179.36	11,997.27	-2,821.38	-336.30	2,818.34	3.90	-2.78	-2.74
15,277.00	89.27	179.36	11,996.27	-2,914.36	-335.26	2,911.33	2.89	-2.89	0.00
15,370.00	87.74	179.18	11,998.70	-3,007.32	-334.08	3,004.29	1.66	-1.65	-0.19
15,463.00	87.16	179.89	12,002.84	-3,100.23	-333.33	3,097.20	0.99	-0.62	0.76
15,557.00	90.64	183.31	12,004.64	-3,194.14	-335.95	3,191.09	5.19	3.70	3.64
15,650.00	91.96	182.61	12,002.53	-3,286.99	-340.75	3,283.89	1.61	1.42	-0.75
15,743.00	91.65	181.99	11,999.60	-3,379.87	-344.48	3,376.74	0.75	-0.33	-0.67
15,836.00	88.00	179.97	11,999.89	-3,472.84	-346.07	3,469.68	4.49	-3.92	-2.17
15,929.00	86.73	177.69	12,004.16	-3,565.71	-344.18	3,562.57	2.80	-1.37	-2.45
16,022.00	92.31	180.06	12,004.94	-3,658.65	-342.35	3,655.52	6.52	6.00	2.55
16,115.00	95.38	180.15	11,998.71	-3,751.43	-342.52	3,748.29	3.30	3.30	0.10
16,208.00	93.89	180.94	11,991.19	-3,844.11	-343.40	3,840.97	1.81	-1.60	0.85
16,302.00	94.33	180.32	11,984.45	-3,937.87	-344.44	3,934.71	0.81	0.47	-0.66
16,395.00	91.96	180.24	11,979.35	-4,030.72	-344.89	4,027.55	2.55	-2.55	-0.09
16,488.00	89.98	179.18	11,977.78	-4,123.70	-344.42	4,120.53	2.41	-2.13	-1.14
16,582.00	90.42	177.86	11,977.45	-4,217.66	-341.99	4,214.52	1.48	0.47	-1.40
16,633.35	90.69	176.31	11,976.95	-4,268.94	-339.38	4,265.81	3.07	0.52	-3.02
TGT 3 (4265' VS)									
16,675.00	90.90	175.05	11,976.38	-4,310.47	-336.24	4,307.37	3.07	0.52	-3.02
16,768.00	89.01	174.88	11,976.45	-4,403.11	-328.08	4,400.08	2.04	-2.03	-0.18
16,862.00	86.77	176.72	11,979.91	-4,496.78	-321.20	4,493.81	3.08	-2.38	1.96
16,955.00	87.87	177.51	11,984.26	-4,589.56	-316.52	4,586.62	1.46	1.18	0.85
16,999.80	88.10	179.21	11,985.84	-4,634.31	-315.24	4,631.38	3.82	0.51	3.79
S2/11 Crossing									
17,048.00	88.35	181.03	11,987.33	-4,682.49	-315.34	4,679.56	3.82	0.52	3.78
17,141.00	88.44	180.32	11,989.93	-4,775.44	-316.44	4,772.50	0.77	0.10	-0.76
17,235.00	88.09	180.06	11,992.78	-4,869.40	-316.75	4,866.45	0.46	-0.37	-0.28
17,328.00	88.84	178.92	11,995.27	-4,962.36	-315.92	4,959.41	1.47	0.81	-1.23
17,421.00	86.59	179.18	11,998.98	-5,055.27	-314.38	5,052.33	2.44	-2.42	0.28
17,514.00	86.95	181.03	12,004.22	-5,148.11	-314.55	5,145.17	2.02	0.39	1.99



Total Directional Services

Survey Report



Company:	Franklin Mountain Energy	Local Co-ordinate Reference:	Well Blue Ribbon Fed Com 703H
Project:	Lea County, NM (NAD83)	TVD Reference:	3245.2' GE + 30' KB @ 3275.20usft
Site:	Blue Ribbon/Parade State	MD Reference:	3245.2' GE + 30' KB @ 3275.20usft
Well:	Blue Ribbon Fed Com 703H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM 5000.15 Single User Db

Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
17,607.00	86.99	180.15	12,009.14	-5,240.98	-315.51	5,238.03	0.95	0.04	-0.95
17,701.00	87.25	179.09	12,013.86	-5,334.86	-314.88	5,331.90	1.16	0.28	-1.13
17,794.00	86.95	177.34	12,018.56	-5,427.69	-311.99	5,424.76	1.91	-0.32	-1.88
17,887.00	86.20	179.01	12,024.12	-5,520.47	-309.03	5,517.56	1.97	-0.81	1.80
17,980.00	87.38	180.24	12,029.33	-5,613.32	-308.43	5,610.41	1.83	1.27	1.32
18,074.00	87.67	182.79	12,033.39	-5,707.19	-310.91	5,704.26	2.73	0.31	2.71
18,167.00	89.60	182.43	12,035.60	-5,800.06	-315.14	5,797.09	2.11	2.08	-0.39
18,260.00	89.91	181.03	12,036.00	-5,893.02	-317.95	5,890.02	1.54	0.33	-1.51
18,353.00	87.93	182.79	12,037.75	-5,985.94	-321.05	5,982.91	2.85	-2.13	1.89
18,447.00	87.54	180.15	12,041.47	-6,079.83	-323.46	6,076.77	2.84	-0.41	-2.81
18,540.00	83.45	177.69	12,048.77	-6,172.50	-321.72	6,169.46	5.13	-4.40	-2.65
18,633.00	86.48	176.28	12,056.94	-6,265.00	-316.84	6,261.99	3.59	3.26	-1.52
18,726.00	85.87	175.05	12,063.14	-6,357.52	-309.83	6,354.58	1.47	-0.66	-1.32
18,746.04	85.91	175.29	12,064.58	-6,377.44	-308.15	6,374.51	1.22	0.18	1.21
TGT 4 (6375' VS)									
18,820.00	86.04	176.19	12,069.77	-6,451.01	-302.67	6,448.13	1.22	0.18	1.21
18,914.00	85.17	178.39	12,076.97	-6,544.63	-298.24	6,541.77	2.51	-0.93	2.34
19,007.00	85.91	180.59	12,084.21	-6,637.33	-297.41	6,634.49	2.49	0.80	2.37
19,101.00	88.86	182.52	12,088.50	-6,731.19	-299.96	6,728.31	3.75	3.14	2.05
19,194.00	86.18	181.29	12,092.52	-6,824.04	-303.05	6,821.13	3.17	-2.88	-1.32
19,288.00	83.85	180.68	12,100.69	-6,917.66	-304.66	6,914.74	2.56	-2.48	-0.65
19,381.00	81.69	178.92	12,112.39	-7,009.91	-304.34	7,006.99	2.99	-2.32	-1.89
19,474.00	84.73	179.62	12,123.39	-7,102.24	-303.17	7,099.32	3.35	3.27	0.75
19,567.00	91.14	184.72	12,126.74	-7,195.03	-306.69	7,192.08	8.80	6.89	5.48
19,660.00	89.34	182.17	12,126.35	-7,287.85	-312.28	7,284.85	3.36	-1.94	-2.74
19,753.00	85.21	179.62	12,130.77	-7,380.71	-313.73	7,377.69	5.22	-4.44	-2.74
19,847.00	82.44	176.72	12,140.88	-7,474.10	-310.76	7,471.10	4.25	-2.95	-3.09
19,940.00	82.75	178.22	12,152.87	-7,566.23	-306.69	7,563.26	1.63	0.33	1.61
20,034.00	82.44	177.69	12,164.98	-7,659.39	-303.36	7,656.45	0.65	-0.33	-0.56
20,127.00	83.54	179.10	12,176.33	-7,751.65	-300.78	7,748.73	1.91	1.18	1.52
20,220.00	83.41	177.34	12,186.90	-7,844.00	-297.91	7,841.10	1.89	-0.14	-1.89
20,312.00	82.62	178.92	12,198.09	-7,935.26	-294.92	7,932.39	1.91	-0.86	1.72
20,406.00	85.08	179.01	12,208.16	-8,028.70	-293.24	8,025.84	2.62	2.62	0.10
20,499.00	82.49	176.11	12,218.23	-8,121.05	-289.31	8,118.22	4.17	-2.78	-3.12
20,593.00	87.93	178.57	12,226.08	-8,214.58	-284.97	8,211.78	6.35	5.79	2.62
20,686.00	87.45	180.59	12,229.83	-8,307.50	-284.29	8,304.70	2.23	-0.52	2.17
20,779.00	84.95	181.91	12,235.99	-8,400.26	-286.31	8,397.44	3.04	-2.69	1.42
20,872.00	85.91	178.83	12,243.40	-8,492.95	-286.91	8,490.13	3.46	1.03	-3.31
20,966.00	91.63	180.15	12,245.42	-8,586.89	-286.07	8,584.06	6.24	6.09	1.40
21,060.00	89.25	180.24	12,244.70	-8,680.88	-286.39	8,678.05	2.53	-2.53	0.10
21,152.69	87.73	179.97	12,247.14	-8,773.53	-286.57	8,770.70	1.66	-1.64	-0.29
TGT 5 (8770' VS)									
21,154.00	87.71	179.97	12,247.19	-8,774.84	-286.57	8,772.00	1.66	-1.64	-0.29
21,247.00	86.40	180.76	12,251.97	-8,867.71	-287.16	8,864.87	1.64	-1.41	0.85



Total Directional Services

Survey Report



Company:	Franklin Mountain Energy	Local Co-ordinate Reference:	Well Blue Ribbon Fed Com 703H
Project:	Lea County, NM (NAD83)	TVD Reference:	3245.2' GE + 30' KB @ 3275.20usft
Site:	Blue Ribbon/Parade State	MD Reference:	3245.2' GE + 30' KB @ 3275.20usft
Well:	Blue Ribbon Fed Com 703H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM 5000.15 Single User Db

Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
21,340.00	87.01	179.36	12,257.31	-8,960.56	-287.25	8,957.71	1.64	0.66	-1.51
21,434.00	88.42	180.24	12,261.06	-9,054.48	-286.93	9,051.63	1.77	1.50	0.94
21,502.41	89.70	180.11	12,262.18	-9,122.87	-287.13	9,120.02	1.88	1.87	-0.19
TGT 6 (9120' VS)									
21,528.00	90.18	180.06	12,262.21	-9,148.47	-287.17	9,145.61	1.88	1.87	-0.19
21,621.00	91.89	180.15	12,260.53	-9,241.45	-287.34	9,238.59	1.84	1.84	0.10
21,715.00	93.74	180.76	12,255.91	-9,335.33	-288.09	9,332.46	2.07	1.97	0.65
21,809.00	92.46	180.41	12,250.83	-9,429.18	-289.05	9,426.30	1.41	-1.36	-0.37
21,902.00	92.37	179.36	12,246.91	-9,522.10	-288.86	9,519.21	1.13	-0.10	-1.13
21,995.00	90.44	176.90	12,244.63	-9,615.01	-285.82	9,612.15	3.36	-2.08	-2.65
22,089.00	90.75	176.28	12,243.66	-9,708.84	-280.23	9,706.02	0.74	0.33	-0.66
22,144.00	90.75	176.28	12,242.94	-9,763.72	-276.67	9,760.93	0.00	0.00	0.00
BHL - PBHL (Blue Ribbon Fed Com 703H)									

Design Annotations				
Measured Depth (usft)	Vertical Depth (usft)	Local Coordinates		Comment
		+N/-S (usft)	+E/-W (usft)	
16,999.80	11,985.84	-4,634.31	-315.24	S2/11 Crossing
22,144.00	12,242.94	-9,763.72	-276.67	BHL

Checked By: _____ Approved By: _____ Date: _____

District I

1625 N. French Dr., Hobbs, NM 88240
Phone:(575) 393-6161 Fax:(575) 393-0720

District II

811 S. First St., Artesia, NM 88210
Phone:(575) 748-1283 Fax:(575) 748-9720

District III

1000 Rio Brazos Rd., Aztec, NM 87410
Phone:(505) 334-6178 Fax:(505) 334-6170

District IV

1220 S. St Francis Dr., Santa Fe, NM 87505
Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

ACKNOWLEDGMENTS

Action 40461

ACKNOWLEDGMENTS

Operator: Franklin Mountain Energy LLC 44 Cook Street Denver, CO 80206	OGRID: 373910
	Action Number: 40461
	Action Type: [C-104] Completion Packet (C-104C)

ACKNOWLEDGMENTS

☒	I hereby certify that the required Water Use Report has been, or will be, submitted for this wells completion.
☒	I hereby certify that the required FracFocus disclosure has been, or will be, submitted for this wells completion.

District I
1625 N. French Dr., Hobbs, NM 88240
Phone:(575) 393-6161 Fax:(575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone:(575) 748-1283 Fax:(575) 748-9720
District III
1000 Rio Brazos Rd., Aztec, NM 87410
Phone:(505) 334-6178 Fax:(505) 334-6170
District IV
1220 S. St Francis Dr., Santa Fe, NM 87505
Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 40461

CONDITIONS

Operator: Franklin Mountain Energy LLC 44 Cook Street Denver, CO 80206	OGRID: 373910
	Action Number: 40461
	Action Type: [C-104] Completion Packet (C-104C)

CONDITIONS

Created By	Condition	Condition Date
ksimmons	RT C-104 expires 11/08/2021; submit all drilling, casing, and completion sundries/reports.	9/8/2021
