

Form 3160-3
(June 2015)FORM APPROVED
OMB No. 1004-0137
Expires: January 31, 2018

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
APPLICATION FOR PERMIT TO DRILL OR REENTER

1a. Type of work: <input type="checkbox"/> DRILL <input type="checkbox"/> REENTER 1b. Type of Well: <input type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input type="checkbox"/> Other 1c. Type of Completion: <input type="checkbox"/> Hydraulic Fracturing <input type="checkbox"/> Single Zone <input type="checkbox"/> Multiple Zone		5. Lease Serial No. 6. If Indian, Allottee or Tribe Name 7. If Unit or CA Agreement, Name and No. 8. Lease Name and Well No.
2. Name of Operator		9. API Well No. 30-015-49706
3a. Address	3b. Phone No. (include area code)	10. Field and Pool, or Exploratory
4. Location of Well (Report location clearly and in accordance with any State requirements. *) At surface At proposed prod. zone		11. Sec., T. R. M. or Blk. and Survey or Area
14. Distance in miles and direction from nearest town or post office*		12. County or Parish
13. State		
15. Distance from proposed* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any)	16. No of acres in lease	17. Spacing Unit dedicated to this well
18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft.	19. Proposed Depth	20. BLM/BIA Bond No. in file
21. Elevations (Show whether DF, KDB, RT, GL, etc.)	22. Approximate date work will start*	23. Estimated duration
24. Attachments		

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, and the Hydraulic Fracturing rule per 43 CFR 3162.3-3 (as applicable)

- | | |
|---|---|
| 1. Well plat certified by a registered surveyor.
2. A Drilling Plan.
3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office). | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).
5. Operator certification.
6. Such other site specific information and/or plans as may be requested by the BLM. |
|---|---|

25. Signature	Name (Printed/Typed)	Date
Title		
Approved by (Signature)	Name (Printed/Typed)	Date
Title		
Office		

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
 Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Continued on page 2)

*(Instructions on page 2)



District I
1625 N. French Dr., Hobbs, NM 88240
Phone: (575) 393-6161 Fax: (575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone: (575) 748-1283 Fax: (575) 748-9720
District III
1000 Rio Brazos Road, Aztec, NM 87410
Phone: (505) 334-6178 Fax: (505) 334-6170
District IV
1220 S. St. Francis Dr., Santa Fe, NM 87505
Phone: (505) 476-3460 Fax: (505) 476-3462

State of New Mexico
Energy, Minerals & Natural Resources Department
OIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, NM 87505

Form C-102
Revised August 1, 2011
Submit one copy to appropriate
District Office

☐ AMENDED REPORT

WELL LOCATION AND ACREAGE DEDICATION PLAT

¹ API Number 30-015-49706	² Pool Code 98220	³ Pool Name PURPLE SAGE; WOLFCAMP (GAS)
⁴ Property Code 333039	⁵ Property Name TROJAN HORSE 35 WXY FED COM	⁶ Well Number 4H
⁷ OGRID No. 372098	⁸ Operator Name MARATHON OIL PERMIAN LLC	⁹ Elevation 3090'

¹⁰ Surface Location


UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
M	26	22S	28E		233	SOUTH	1302	WEST	EDDY

¹¹ Bottom Hole Location If Different From Surface

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
N	2	23S	28E		100	SOUTH	2310	WEST	EDDY

¹² Dedicated Acres 639.17	¹³ Joint or Infill	¹⁴ Consolidation Code	¹⁵ Order No.
---	-------------------------------	----------------------------------	-------------------------

No allowable will be assigned to this completion until all interests have been consolidated or a non-standard unit has been approved by the division.

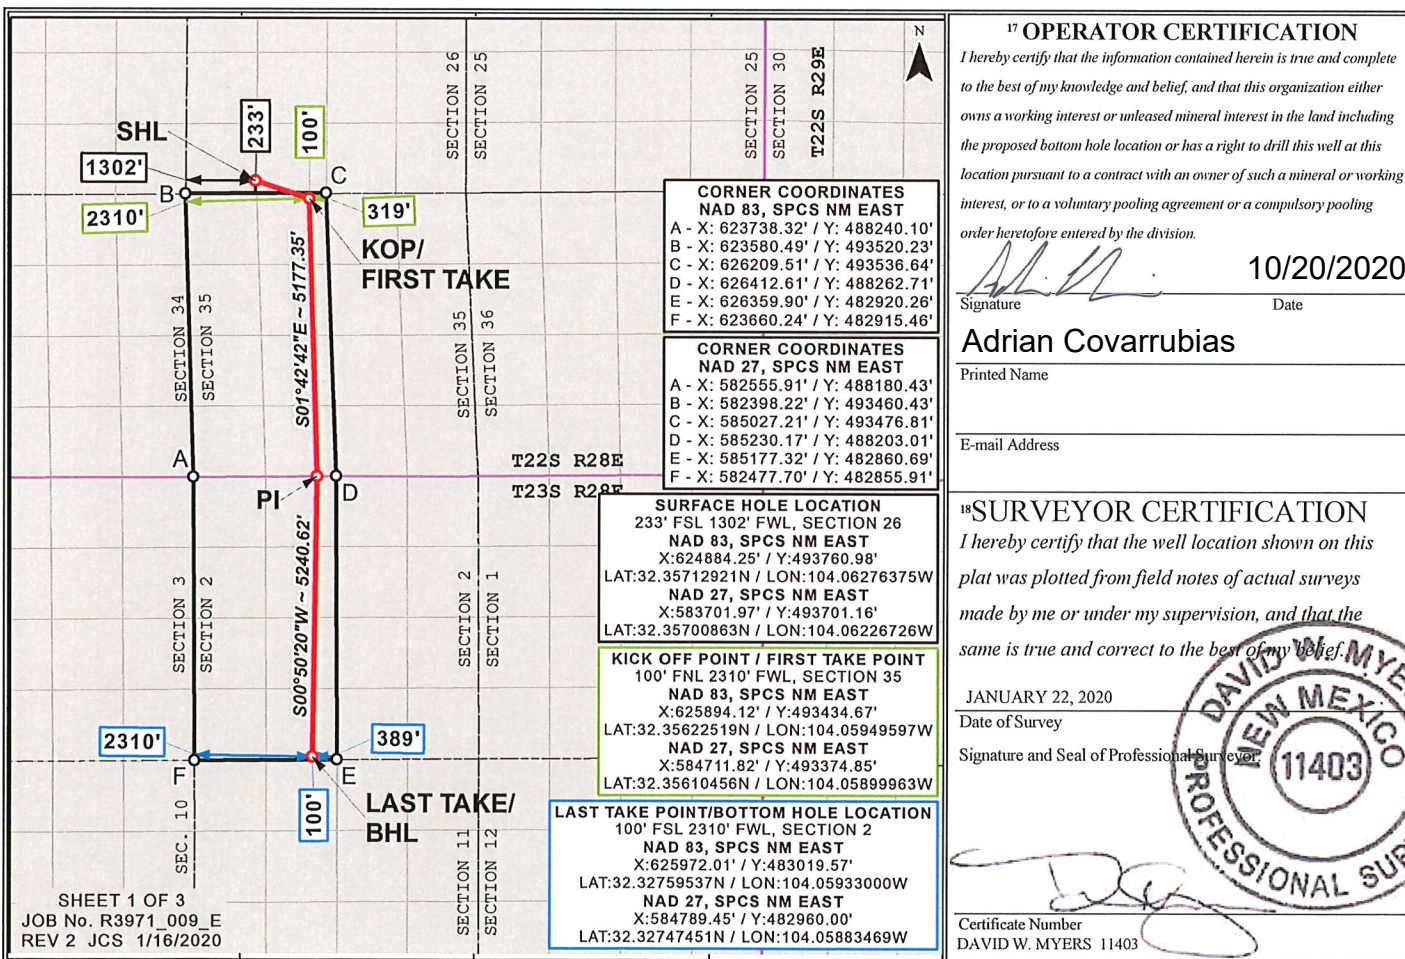

Distances/areas relative to NAD 83 Combined Scale Factor: 0.99977431 Convergence: 00°08'50.61001"

State of New Mexico
Energy, Minerals and Natural Resources Department

Submit Electronically
Via E-permitting

Oil Conservation Division
1220 South St. Francis Dr.
Santa Fe, NM 87505

NATURAL GAS MANAGEMENT PLAN

This Natural Gas Management Plan must be submitted with each Application for Permit to Drill (APD) for a new or recompleted well.

Section 1 – Plan Description

Effective May 25, 2021

I. Operator: Marathon Oil Permian, LLC. **OGRID:** 372098 **Date:** 06 / 30 / 2022

II. Type: ☒ Original ☐ Amendment due to ☐ 19.15.27.9.D(6)(a) NMAC ☐ 19.15.27.9.D(6)(b) NMAC ☐ Other.

If Other, please describe: _____

III. Well(s): Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	API	ULSTR	Footages	Anticipated Oil BBL/D	Anticipated Gas MCF/D	Anticipated Produced Water BBL/D
Trojan Horse 35 WB Fed Com 3H		M-26-22S-28E	233 FSL 1272 FWL	1800	3750	6500
Trojan Horse 35 WXY Fed Com 2H		M-26-22S-28E	233 FSL 1242 FWL	1800	3750	6500
Trojan Horse 35 WXY Fed Com 4H		M-26-22S-28E	233 FSL 1302 FWL	1800	3750	6500

IV. Central Delivery Point Name: Trojan Horse CTB [See 19.15.27.9(D)(1) NMAC]

V. Anticipated Schedule: Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	API	Spud Date	TD Reached Date	Completion Commencement Date	Initial Flow Back Date	First Production Date
Trojan Horse 35 WB Fed Com 3H		02/15/2023	03/07/2023	05/17/2023	06/02/2023	06/02/2023
Trojan Horse 35 WXY Fed Com 2H		02/15/2023	03/26/2023	05/23/2023	06/02/2023	06/02/2023
Trojan Horse 35 WXY Fed Com 4H		02/15/2023	04/14/2023	05/29/2023	06/02/2023	06/02/2023

VI. Separation Equipment: ☒ Attach a complete description of how Operator will size separation equipment to optimize gas capture.

VII. Operational Practices: ☒ Attach a complete description of the actions Operator will take to comply with the requirements of Subsection A through F of 19.15.27.8 NMAC.

VIII. Best Management Practices: ☒ Attach a complete description of Operator's best management practices to minimize venting during active and planned maintenance.

Section 2 – Enhanced Plan

EFFECTIVE APRIL 1, 2022

Beginning April 1, 2022, an operator that is not in compliance with its statewide natural gas capture requirement for the applicable reporting area must complete this section.

☒ Operator certifies that it is not required to complete this section because Operator is in compliance with its statewide natural gas capture requirement for the applicable reporting area.

IX. Anticipated Natural Gas Production:

Well	API	Anticipated Average Natural Gas Rate MCF/D	Anticipated Volume of Natural Gas for the First Year MCF

X. Natural Gas Gathering System (NGGS):

Operator	System	ULSTR of Tie-in	Anticipated Gathering Start Date	Available Maximum Daily Capacity of System Segment Tie-in

XI. Map. ☐ Attach an accurate and legible map depicting the location of the well(s), the anticipated pipeline route(s) connecting the production operations to the existing or planned interconnect of the natural gas gathering system(s), and the maximum daily capacity of the segment or portion of the natural gas gathering system(s) to which the well(s) will be connected.

XII. Line Capacity. The natural gas gathering system ☐ will ☐ will not have capacity to gather 100% of the anticipated natural gas production volume from the well prior to the date of first production.

XIII. Line Pressure. Operator ☐ does ☐ does not anticipate that its existing well(s) connected to the same segment, or portion, of the natural gas gathering system(s) described above will continue to meet anticipated increases in line pressure caused by the new well(s).

☐ Attach Operator's plan to manage production in response to the increased line pressure.

XIV. Confidentiality: ☐ Operator asserts confidentiality pursuant to Section 71-2-8 NMSA 1978 for the information provided in Section 2 as provided in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and attaches a full description of the specific information for which confidentiality is asserted and the basis for such assertion.

Section 3 - Certifications

Effective May 25, 2021

Operator certifies that, after reasonable inquiry and based on the available information at the time of submittal:

☒ Operator will be able to connect the well(s) to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system; or

☐ Operator will not be able to connect to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system.

If Operator checks this box, Operator will select one of the following:

Well Shut-In. ☐ Operator will shut-in and not produce the well until it submits the certification required by Paragraph (4) of Subsection D of 19.15.27.9 NMAC; or

Venting and Flaring Plan. ☐ Operator has attached a venting and flaring plan that evaluates and selects one or more of the potential alternative beneficial uses for the natural gas until a natural gas gathering system is available, including:

- (a) power generation on lease;
- (b) power generation for grid;
- (c) compression on lease;
- (d) liquids removal on lease;
- (e) reinjection for underground storage;
- (f) reinjection for temporary storage;
- (g) reinjection for enhanced oil recovery;
- (h) fuel cell production; and
- (i) other alternative beneficial uses approved by the division.

Section 4 - Notices

1. If, at any time after Operator submits this Natural Gas Management Plan and before the well is spud:


(a) Operator becomes aware that the natural gas gathering system it planned to connect the well(s) to has become unavailable or will not have capacity to transport one hundred percent of the production from the well(s), no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised venting and flaring plan containing the information specified in Paragraph (5) of Subsection D of 19.15.27.9 NMAC; or

(b) Operator becomes aware that it has, cumulatively for the year, become out of compliance with its baseline natural gas capture rate or natural gas capture requirement, no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised Natural Gas Management Plan for each well it plans to spud during the next 90 days containing the information specified in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and shall file an update for each Natural Gas Management Plan until Operator is back in compliance with its baseline natural gas capture rate or natural gas capture requirement.

2. OCD may deny or conditionally approve an APD if Operator does not make a certification, fails to submit an adequate venting and flaring plan which includes alternative beneficial uses for the anticipated volume of natural gas produced, or if OCD determines that Operator will not have adequate natural gas takeaway capacity at the time a well will be spud.

I certify that, after reasonable inquiry, the statements in and attached to this Natural Gas Management Plan are true and correct to the best of my knowledge and acknowledge that a false statement may be subject to civil and criminal penalties under the Oil and Gas Act.

Signature:



Printed Name: Melissa Szudera

Title: Sr. Regulatory Compliance Representative

E-mail Address: mszudera@marathonoil.com

Date: 06/30/2022

Phone: 713-296-3179

OIL CONSERVATION DIVISION
(Only applicable when submitted as a standalone form)

Approved By:

Title:

Approval Date:

Conditions of Approval:

APPENDIX

Section 1 - Parts VI, VII, and VIII

VI. Separation Equipment: ☒ Attach a complete description of how Operator will size separation equipment to optimize gas capture.

- Separation equipment is sized to allow for retention time and velocity to adequately separate oil, gas, and water at anticipated peak rates.
- All central tank battery equipment is designed to efficiently capture the remaining gas from the liquid phase.
- Valves and meters are designed to service without flow interruption or venting of gas.

VII. Operational Practices: ☒ Attach a complete description of the actions Operator will take to comply with the requirements of Subsection A through F of 19.15.27.8 NMAC.

◆ **19.15.27.8 (A) – Venting and Flaring Of Natural Gas**

- Marathon Oil Permian's field operations are designed with the goal of minimizing flaring and preventing venting of natural gas. If capturing the gas is not possible then the gas is combusted/flared using properly sized flares or combustors in accordance with state air permit rules.

◆ **19.15.27.8 (B) – Venting and Flaring During Drilling Operations**

- A properly-sized flare stack will be located at a minimum 100' from the nearest surface hole location on the pad.
- All natural gas produced during drilling operations will be flared. Venting will only occur if there is an equipment malfunction and/or to avoid risk of an immediate and substantial adverse impact on safety, public health, or the environment.

◆ **19.15.27.8 (C) – Venting and Flaring During Completion or Recompletion Operations**

- During all phases of flowback, wells will flow through a sand separator, or other appropriate flowback separation equipment, and the well stream will be directed to a central tank battery (CTB) through properly sized flowlines.
- The CTB will have properly sized separation equipment for maximum anticipated flow rates.
- Multiple stages of separation will be used to separate gas from liquids. All gas will be routed to a sales outlet. Fluids will be routed to tanks equipped with a closed loop system that will recover any residual gas from the tanks and route such gas to a sales outlet.

◆ **19.15.27.8 (D) – Venting and Flaring During Production Operations**

- During production, the well stream will be routed to the CTB where multiple stages of separation will separate gas from liquids. All gas will be routed to a sales outlet. Fluids will be routed to tanks equipped with a closed loop system that will recover any residual gas from the tanks and route such gas to a sales outlet, minimizing tank emissions.
- Flares are equipped with auto-ignition systems and continuous pilot operations.
- Automatic gauging equipment is installed on all tanks.

◆ **19.15.27.8 (E) – Performance Standards**

- Production equipment will be designed to handle maximum anticipated rates and pressure.
- Automatic gauging equipment is installed on all tanks to minimize venting.
- All flared gas will be combusted in a flare stack that is properly sized and designed to ensure proper combustion.
- Flares are equipped with continuous pilots and auto-ignitors along with remote monitoring of the pilot status.
- Weekly AVOs and monthly LDAR inspections will be performed on all wells and facilities that produce more than 60 MCFD.
- Gas/H₂S detectors will be installed throughout the facilities and wellheads to detect leaks and enable timely repairs.

◆ 19.15.27.8 (F) – Measurement or Estimation of Vented and Flared Natural Gas

- All high pressure flared gas is measured by equipment conforming to API 14.10.
- No meter bypasses are installed.
- When metering is not practical due to low pressure/low rate, the vented or flared volume will be estimated through flare flow curves with the assistance of air emissions consultants, as necessary.

VIII. Best Management Practices: ☒ Attach a complete description of Operator's best management practices to minimize venting during active and planned maintenance.

- Marathon Oil Permian will use best management practices to vent as minimally as possible during well intervention operations and downhole well maintenance.
- All natural gas is routed into the gas gathering system and directed to one of Marathon Oil Permian's multiple gas sales outlets.
- All venting events will be recorded and all start-up, shutdown, maintenance logs will be kept for control equipment.
- All control equipment will be maintained to provide highest run-time possible.
- All procedures are drafted to keep venting and flaring to the absolute minimum.

Company Name: Marathon Oil Permian LLC
Trojan Horse 35 WXY Fed Com #4H
Eddy County, New Mexico (NAD 27)
Rig: NA
Created By: Chase Chambers
Date: 15:30, October 08 2020



PROJECT DETAILS: Eddy County, New Mexico (NAD 27)
Geodetic System: US State Plane 1927 (Exact solution)
Datum: NAD 1927 (NADCON CONUS)
Ellipsoid: Clarke 1866
Zone: New Mexico East 3001
System Datum: Mean Sea Level






Trojan Horse 35 WXY Fed Com #4H
Eddy County, New Mexico (NAD 27)
Q20*** & WT-20***
Design #2


WELL DETAILS: Trojan Horse 35 WXY Fed Com #4H					
			3090.0		
+N/-S	+E/-W	Northing	Easting	Latitude	Longitude
0.0	0.0	493701.16	583701.97 32° 21' 25.231 N 104° 3' 44.162 W		

DESIGN ANNOTATIONS							
MD	Inc	Azi	TVD	+N/-S	+E/-W	Vsect	Departure
2500.0	0.00	0.00	2500.0	0.0	0.0	0.0	0.0
3241.5	14.83	107.91	3233.2	-29.3	90.8	38.3	95.4
5778.6	14.83	107.91	5685.8	-229.0	708.7	299.2	744.8
6642.3	14.83	107.91	6520.8	-237.0	919.1	388.0	965.8
7383.8	0.00	0.00	7254.0	-326.3	1009.8	426.4	1061.3
9260.8	0.00	0.00	9131.0	-326.3	1009.8	426.4	1061.3
10155.8	89.50	178.29	9703.9	-894.1	1026.8	992.9	1629.3
14765.3	89.50	178.29	9743.8	-5501.3	1164.5	5590.7	6238.6
14894.6	89.50	180.87	9744.9	-5630.6	1165.4	5719.4	6367.9
18772.5	89.50	180.87	9778.5	-9507.9	1106.3	9571.0	10245.6
20006.0	89.50	180.87	9789.2	-10741.2	1087.5	10796.1	11479.0


DESIGN TARGET DETAILS							
Name	TVD	+N/-S	+E/-W	Northing	Easting	Latitude	Longitude
T H 35 WXY FC #4H - Enter	5685.8	-228.2	708.7	493472.97	584410.71 32° 21' 22.955 N 104° 3' 35.906 W		
T H 35 WXY FC #4H - VP/KOP	7254.0	-326.3	1009.8	493374.85	584711.82 32° 21' 21.976 N 104° 3' 32.399 W		
T H 35 WXY FC #4H - PPP2	9743.8	-5501.3	1164.5	488199.81	584866.47 32° 20' 30.760 N 104° 3' 30.751 W		
T H 35 WXY FC #4H - PPP3	9778.5	-9507.9	1106.3	484193.32	584807.54 32° 19' 51.113 N 104° 3' 31.557 W		
T H 35 WXY FC #4H - PBHL	9789.2	-10741.2	1087.5	482960.00	584789.45 32° 19' 38.908 N 104° 3' 31.805 W		

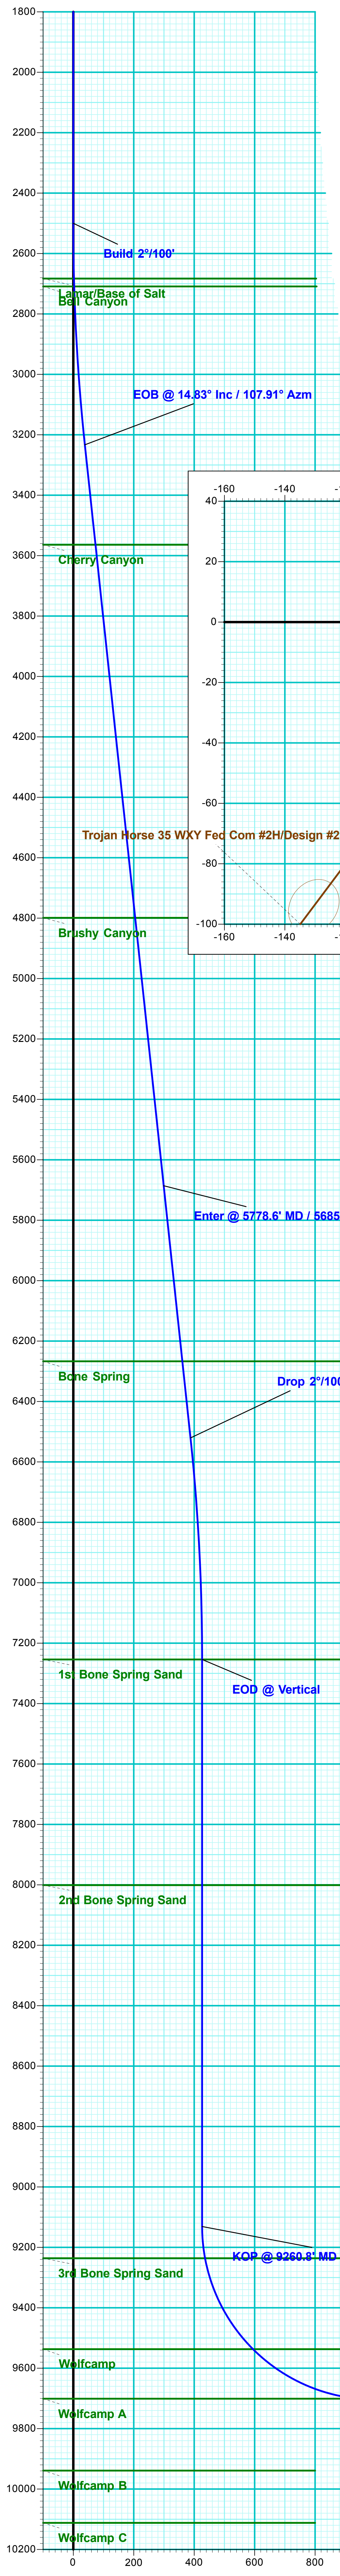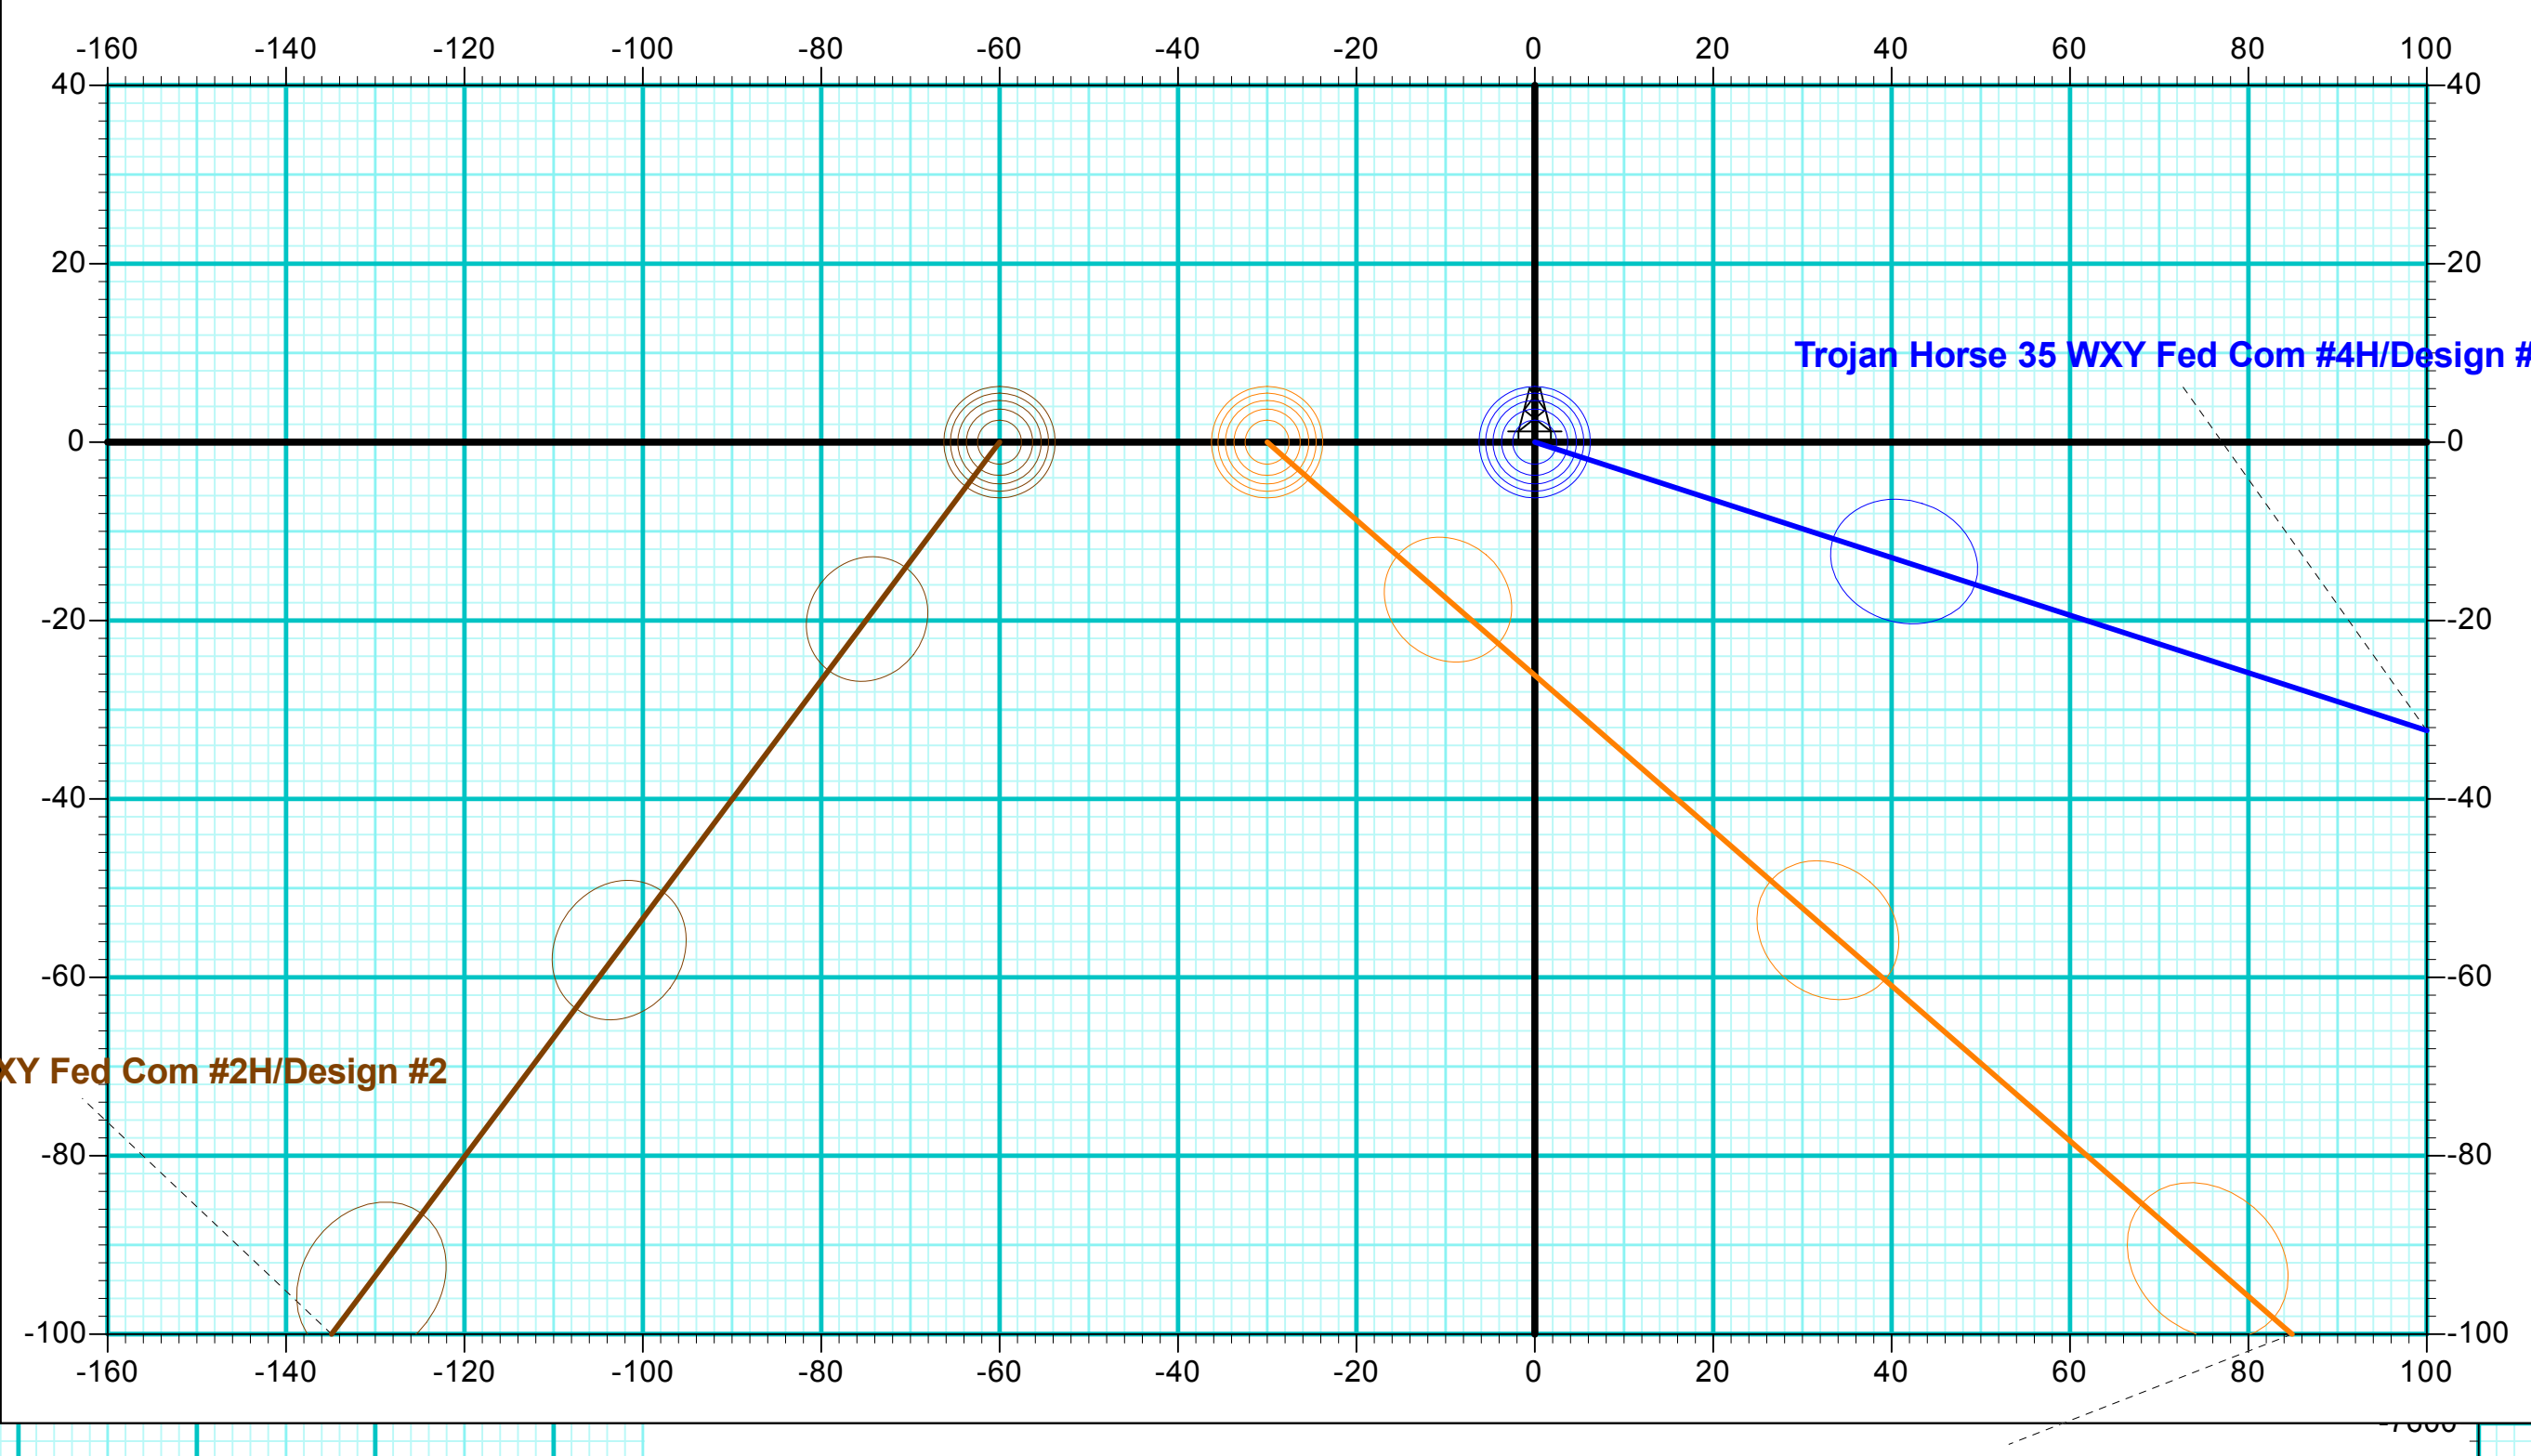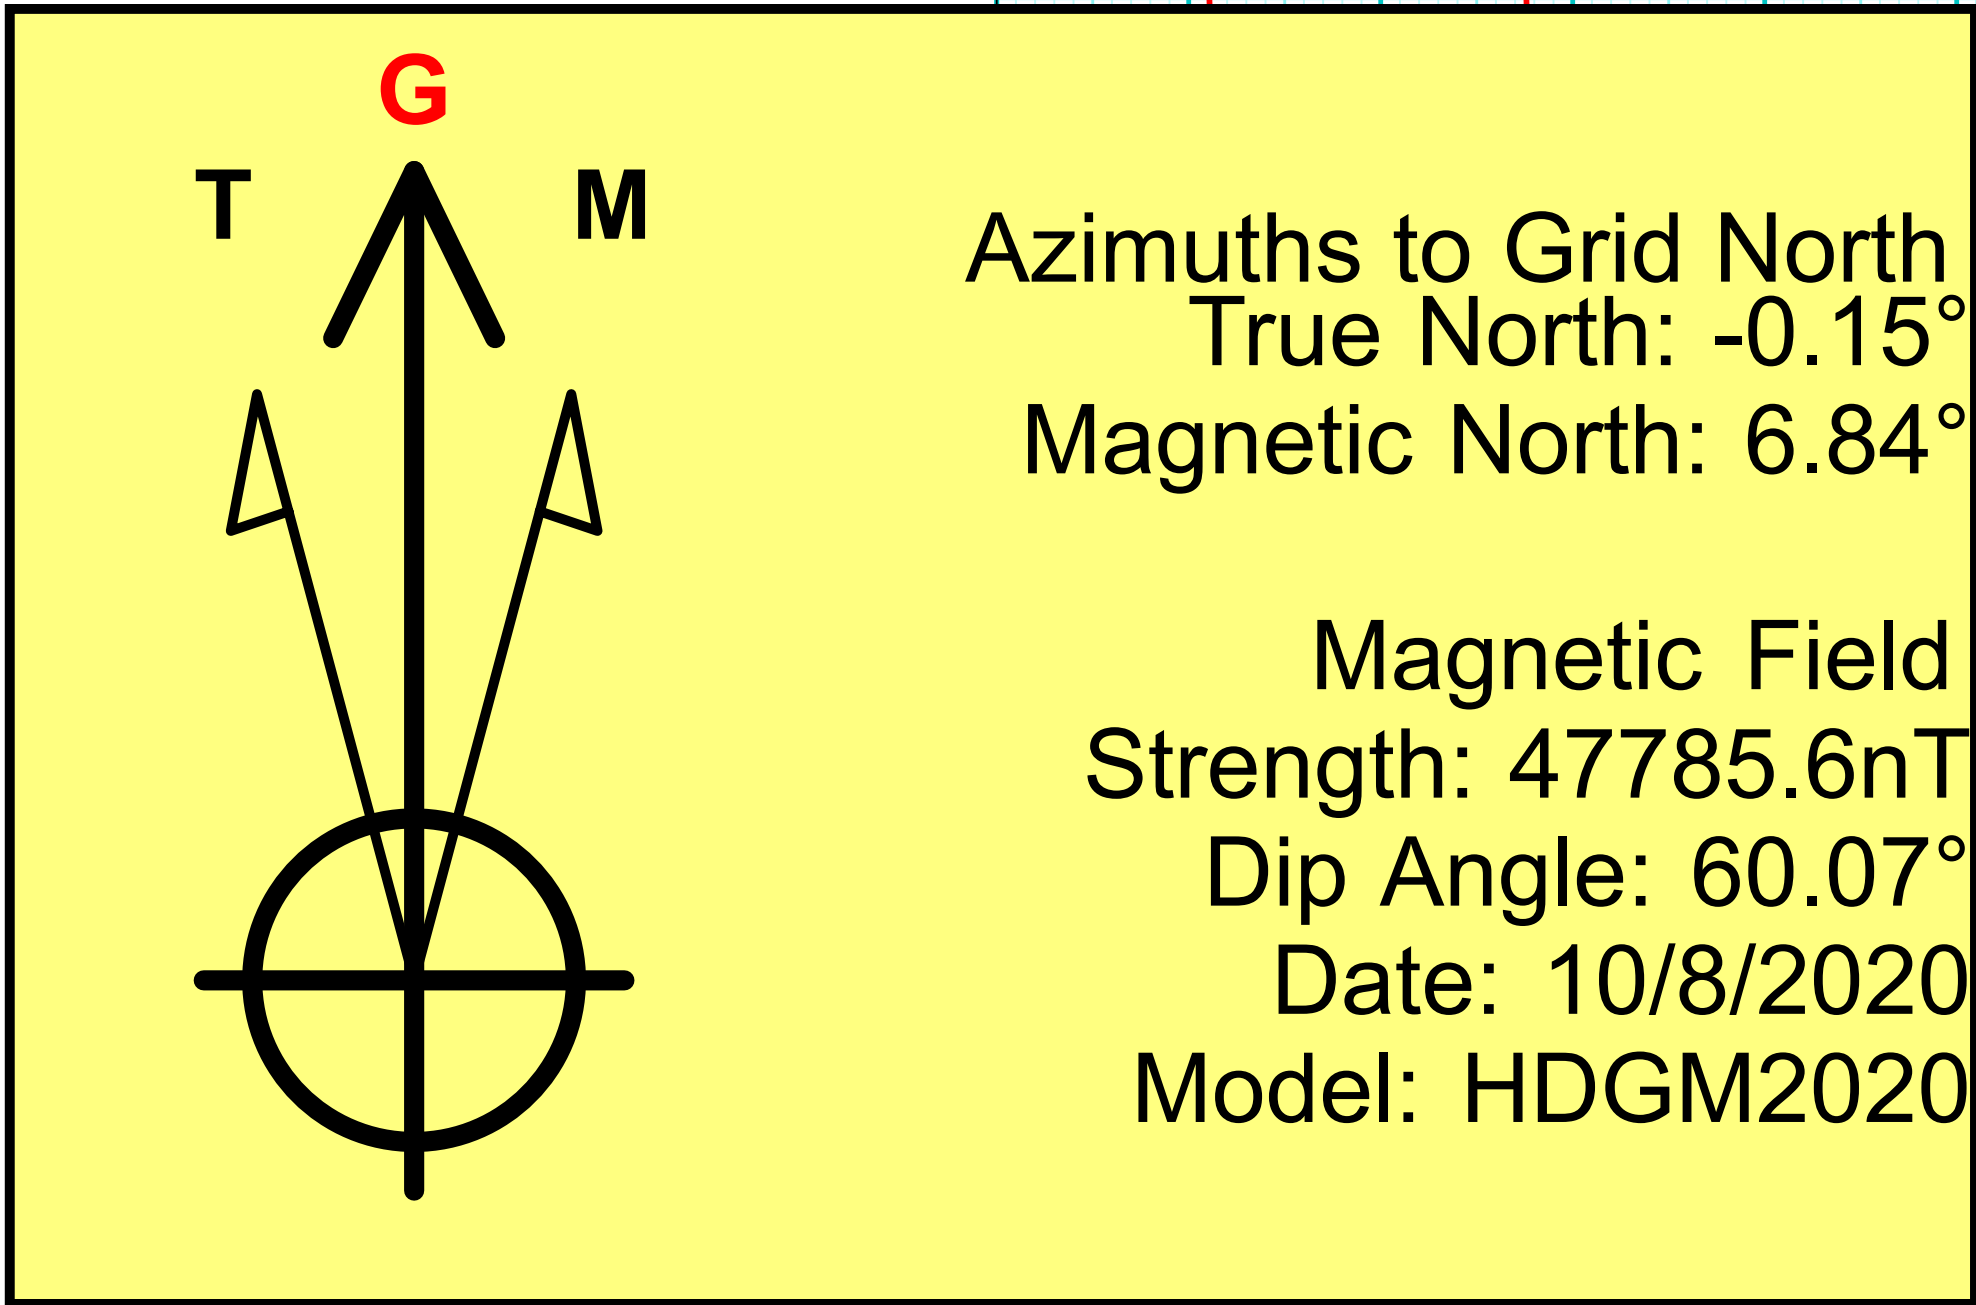

Target Line: 9695' TVD @ 0° VS: 89.5° INC

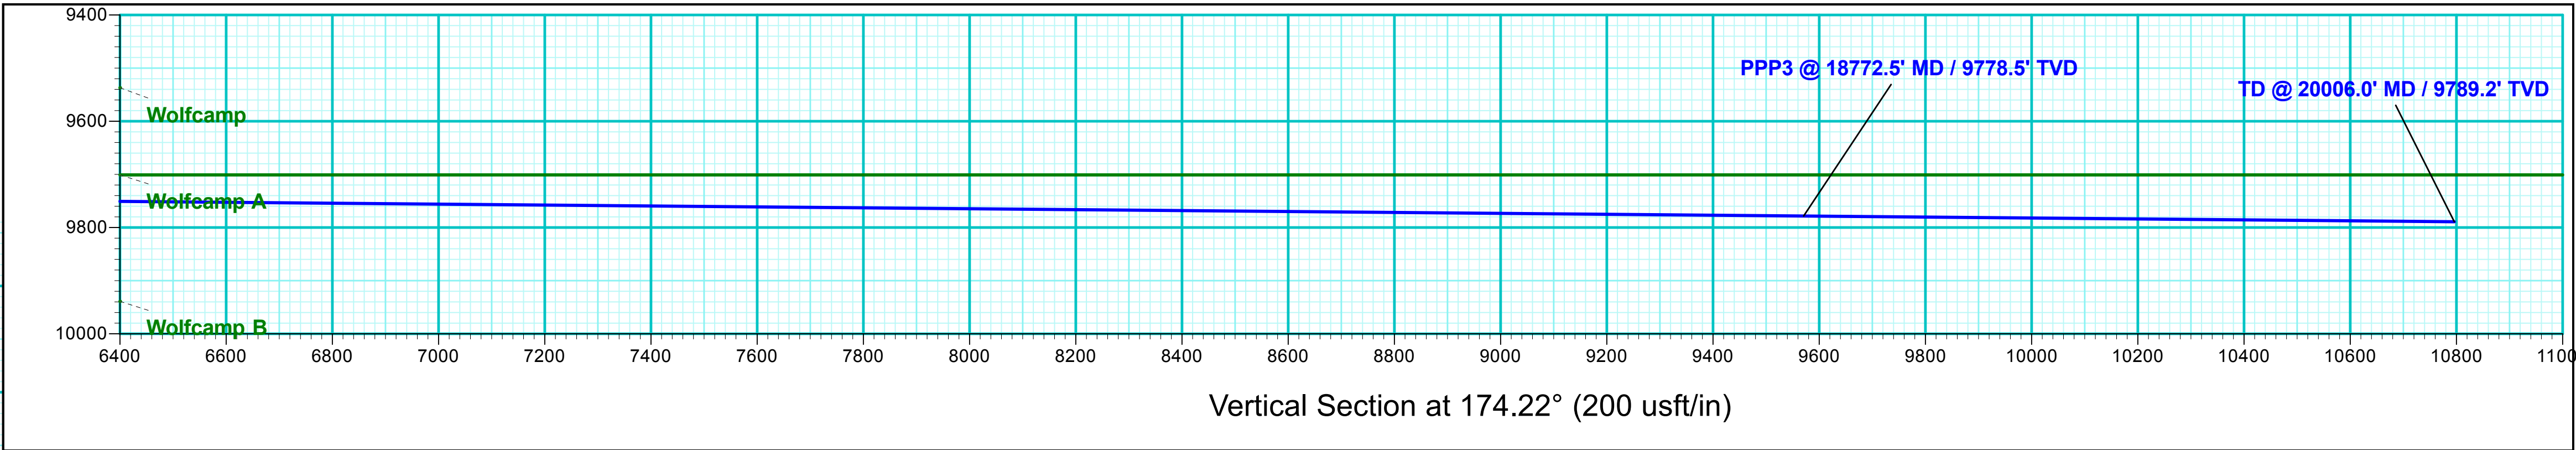

Vertical Section at 174.22° (200 usf/in)



Vertical Section at 174.22° (200 usf/in)



Marathon Oil Permian LLC

Eddy County, New Mexico (NAD 27)

Sec 26, T22S, R28E

Trojan Horse 35 WXY Fed Com #4H

Wellbore #1

Plan: Design #2

QES Well Planning Report

08 October, 2020





Well Planning Report



Database:	EDM 5000.1 Single User Db	Local Co-ordinate Reference:	Well Trojan Horse 35 WXY Fed Com #4H
Company:	Marathon Oil Permian LLC	TVD Reference:	WELL @ 3115.0usft (NA)
Project:	Eddy County, New Mexico (NAD 27)	MD Reference:	WELL @ 3115.0usft (NA)
Site:	Sec 26, T22S, R28E	North Reference:	Grid
Well:	Trojan Horse 35 WXY Fed Com #4H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Design #2		

Project	Eddy County, New Mexico (NAD 27)		
Map System:	US State Plane 1927 (Exact solution)	System Datum:	Mean Sea Level
Geo Datum:	NAD 1927 (NADCON CONUS)		
Map Zone:	New Mexico East 3001		

Site	Sec 26, T22S, R28E					
Site Position:		Northing:	493,701.16 usft	Latitude:	32° 21' 25.232 N	
From:	Map	Easting:	583,671.97 usft	Longitude:	104° 3' 44.512 W	
Position Uncertainty:		0.0 usft	Slot Radius:	13-3/16 "	Grid Convergence:	0.15 °

Well	Trojan Horse 35 WXY Fed Com #4H					
Well Position	+N/-S	0.0 usft	Northing:	493,701.16 usft	Latitude:	32° 21' 25.231 N
	+E/-W	30.0 usft	Easting:	583,701.97 usft	Longitude:	104° 3' 44.162 W
Position Uncertainty		0.0 usft	Wellhead Elevation:		Ground Level:	3,090.0 usft

Wellbore	Wellbore #1				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	HDGM2020	10/8/2020	6.98	60.07	47,785.60000000

Design	Design #2			
Audit Notes:				
Version:	Phase:	PLAN	Tie On Depth:	0.0
Vertical Section:	Depth From (TVD) (usft)	+N/-S (usft)	+E/-W (usft)	Direction (°)
	0.0	0.0	0.0	174.22

Plan Sections										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	TFO (°)	Target
0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.00	0.00	
2,500.0	0.00	0.00	2,500.0	0.0	0.0	0.00	0.00	0.00	0.00	
3,241.5	14.83	107.91	3,233.2	-29.3	90.8	2.00	2.00	0.00	107.91	
6,642.3	14.83	107.91	6,520.8	-297.0	919.1	0.00	0.00	0.00	0.00	
7,383.8	0.00	0.00	7,254.0	-326.3	1,009.8	2.00	-2.00	0.00	180.00	T H 35 WXY FC #4H
9,260.8	0.00	0.00	9,131.0	-326.3	1,009.8	0.00	0.00	0.00	0.00	
10,155.8	89.50	178.29	9,703.9	-894.1	1,026.8	10.00	10.00	19.92	178.29	
14,765.3	89.50	178.29	9,743.8	-5,501.3	1,164.5	0.00	0.00	0.00	0.00	T H 35 WXY FC #4H
14,894.6	89.50	180.87	9,744.9	-5,630.6	1,165.4	2.00	0.00	2.00	90.04	
20,006.0	89.50	180.87	9,789.2	-10,741.2	1,087.5	0.00	0.00	0.00	0.00	T H 35 WXY FC #4H



Well Planning Report



Database:	EDM 5000.1 Single User Db	Local Co-ordinate Reference:	Well Trojan Horse 35 WXY Fed Com #4H
Company:	Marathon Oil Permian LLC	TVD Reference:	WELL @ 3115.0usft (NA)
Project:	Eddy County, New Mexico (NAD 27)	MD Reference:	WELL @ 3115.0usft (NA)
Site:	Sec 26, T22S, R28E	North Reference:	Grid
Well:	Trojan Horse 35 WXY Fed Com #4H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Design #2		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
0.0	0.00	0.00	0.0	0.0	0.0	0.0	0.00	0.00	0.00
100.0	0.00	0.00	100.0	0.0	0.0	0.0	0.00	0.00	0.00
Rustler									
122.0	0.00	0.00	122.0	0.0	0.0	0.0	0.00	0.00	0.00
200.0	0.00	0.00	200.0	0.0	0.0	0.0	0.00	0.00	0.00
300.0	0.00	0.00	300.0	0.0	0.0	0.0	0.00	0.00	0.00
400.0	0.00	0.00	400.0	0.0	0.0	0.0	0.00	0.00	0.00
500.0	0.00	0.00	500.0	0.0	0.0	0.0	0.00	0.00	0.00
Salado									
504.0	0.00	0.00	504.0	0.0	0.0	0.0	0.00	0.00	0.00
600.0	0.00	0.00	600.0	0.0	0.0	0.0	0.00	0.00	0.00
700.0	0.00	0.00	700.0	0.0	0.0	0.0	0.00	0.00	0.00
800.0	0.00	0.00	800.0	0.0	0.0	0.0	0.00	0.00	0.00
900.0	0.00	0.00	900.0	0.0	0.0	0.0	0.00	0.00	0.00
1,000.0	0.00	0.00	1,000.0	0.0	0.0	0.0	0.00	0.00	0.00
Castile									
1,050.0	0.00	0.00	1,050.0	0.0	0.0	0.0	0.00	0.00	0.00
1,100.0	0.00	0.00	1,100.0	0.0	0.0	0.0	0.00	0.00	0.00
1,200.0	0.00	0.00	1,200.0	0.0	0.0	0.0	0.00	0.00	0.00
1,300.0	0.00	0.00	1,300.0	0.0	0.0	0.0	0.00	0.00	0.00
1,400.0	0.00	0.00	1,400.0	0.0	0.0	0.0	0.00	0.00	0.00
1,500.0	0.00	0.00	1,500.0	0.0	0.0	0.0	0.00	0.00	0.00
1,600.0	0.00	0.00	1,600.0	0.0	0.0	0.0	0.00	0.00	0.00
1,700.0	0.00	0.00	1,700.0	0.0	0.0	0.0	0.00	0.00	0.00
1,800.0	0.00	0.00	1,800.0	0.0	0.0	0.0	0.00	0.00	0.00
1,900.0	0.00	0.00	1,900.0	0.0	0.0	0.0	0.00	0.00	0.00
2,000.0	0.00	0.00	2,000.0	0.0	0.0	0.0	0.00	0.00	0.00
2,100.0	0.00	0.00	2,100.0	0.0	0.0	0.0	0.00	0.00	0.00
2,200.0	0.00	0.00	2,200.0	0.0	0.0	0.0	0.00	0.00	0.00
2,300.0	0.00	0.00	2,300.0	0.0	0.0	0.0	0.00	0.00	0.00
2,400.0	0.00	0.00	2,400.0	0.0	0.0	0.0	0.00	0.00	0.00
Build 2°/100'									
2,500.0	0.00	0.00	2,500.0	0.0	0.0	0.0	0.00	0.00	0.00
2,600.0	2.00	107.91	2,600.0	-0.5	1.7	0.7	2.00	2.00	0.00
Lamar/Base of Salt									
2,683.1	3.66	107.91	2,683.0	-1.8	5.6	2.4	2.00	2.00	0.00
2,700.0	4.00	107.91	2,699.8	-2.1	6.6	2.8	2.00	2.00	0.00
Bell Canyon									
2,709.2	4.18	107.91	2,709.0	-2.3	7.3	3.1	2.00	2.00	0.00
2,800.0	6.00	107.91	2,799.5	-4.8	14.9	6.3	2.00	2.00	0.00
2,900.0	8.00	107.91	2,898.7	-8.6	26.5	11.2	2.00	2.00	0.00
3,000.0	10.00	107.91	2,997.5	-13.4	41.4	17.5	2.00	2.00	0.00
3,100.0	12.00	107.91	3,095.6	-19.2	59.6	25.2	2.00	2.00	0.00
3,200.0	14.00	107.91	3,193.1	-26.2	81.0	34.2	2.00	2.00	0.00
EOB @ 14.83° Inc / 107.91° Azm									
3,241.5	14.83	107.91	3,233.2	-29.3	90.8	38.3	2.00	2.00	0.00
3,300.0	14.83	107.91	3,289.8	-33.9	105.1	44.4	0.00	0.00	0.00
3,400.0	14.83	107.91	3,386.5	-41.8	129.4	54.6	0.00	0.00	0.00
3,500.0	14.83	107.91	3,483.1	-49.7	153.8	64.9	0.00	0.00	0.00
Cherry Canyon									
3,583.6	14.83	107.91	3,564.0	-56.3	174.1	73.5	0.00	0.00	0.00
3,600.0	14.83	107.91	3,579.8	-57.6	178.1	75.2	0.00	0.00	0.00
3,700.0	14.83	107.91	3,676.5	-65.4	202.5	85.5	0.00	0.00	0.00



Well Planning Report



Database:	EDM 5000.1 Single User Db	Local Co-ordinate Reference:	Well Trojan Horse 35 WXY Fed Com #4H
Company:	Marathon Oil Permian LLC	TVD Reference:	WELL @ 3115.0usft (NA)
Project:	Eddy County, New Mexico (NAD 27)	MD Reference:	WELL @ 3115.0usft (NA)
Site:	Sec 26, T22S, R28E	North Reference:	Grid
Well:	Trojan Horse 35 WXY Fed Com #4H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Design #2		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
3,800.0	14.83	107.91	3,773.1	-73.3	226.8	95.8	0.00	0.00	0.00
3,900.0	14.83	107.91	3,869.8	-81.2	251.2	106.1	0.00	0.00	0.00
4,000.0	14.83	107.91	3,966.5	-89.0	275.5	116.3	0.00	0.00	0.00
4,100.0	14.83	107.91	4,063.2	-96.9	299.9	126.6	0.00	0.00	0.00
4,200.0	14.83	107.91	4,159.8	-104.8	324.2	136.9	0.00	0.00	0.00
4,300.0	14.83	107.91	4,256.5	-112.6	348.6	147.2	0.00	0.00	0.00
4,400.0	14.83	107.91	4,353.2	-120.5	373.0	157.5	0.00	0.00	0.00
4,500.0	14.83	107.91	4,449.8	-128.4	397.3	167.7	0.00	0.00	0.00
4,600.0	14.83	107.91	4,546.5	-136.2	421.7	178.0	0.00	0.00	0.00
4,700.0	14.83	107.91	4,643.2	-144.1	446.0	188.3	0.00	0.00	0.00
4,800.0	14.83	107.91	4,739.8	-152.0	470.4	198.6	0.00	0.00	0.00
Brushy Canyon									
4,861.2	14.83	107.91	4,799.0	-156.8	485.3	204.9	0.00	0.00	0.00
4,900.0	14.83	107.91	4,836.5	-159.9	494.7	208.9	0.00	0.00	0.00
5,000.0	14.83	107.91	4,933.2	-167.7	519.1	219.2	0.00	0.00	0.00
5,100.0	14.83	107.91	5,029.8	-175.6	543.4	229.4	0.00	0.00	0.00
5,200.0	14.83	107.91	5,126.5	-183.5	567.8	239.7	0.00	0.00	0.00
5,300.0	14.83	107.91	5,223.2	-191.3	592.1	250.0	0.00	0.00	0.00
5,400.0	14.83	107.91	5,319.9	-199.2	616.5	260.3	0.00	0.00	0.00
5,500.0	14.83	107.91	5,416.5	-207.1	640.8	270.6	0.00	0.00	0.00
5,600.0	14.83	107.91	5,513.2	-214.9	665.2	280.9	0.00	0.00	0.00
5,700.0	14.83	107.91	5,609.9	-222.8	689.6	291.1	0.00	0.00	0.00
Enter @ 5778.6' MD / 5685.8' TVD									
5,778.6	14.83	107.91	5,685.8	-229.0	708.7	299.2	0.00	0.00	0.00
5,800.0	14.83	107.91	5,706.5	-230.7	713.9	301.4	0.00	0.00	0.00
5,900.0	14.83	107.91	5,803.2	-238.6	738.3	311.7	0.00	0.00	0.00
6,000.0	14.83	107.91	5,899.9	-246.4	762.6	322.0	0.00	0.00	0.00
6,100.0	14.83	107.91	5,996.5	-254.3	787.0	332.3	0.00	0.00	0.00
6,200.0	14.83	107.91	6,093.2	-262.2	811.3	342.6	0.00	0.00	0.00
6,300.0	14.83	107.91	6,189.9	-270.0	835.7	352.8	0.00	0.00	0.00
Bone Spring									
6,379.8	14.83	107.91	6,267.0	-276.3	855.1	361.0	0.00	0.00	0.00
6,400.0	14.83	107.91	6,286.5	-277.9	860.0	363.1	0.00	0.00	0.00
6,500.0	14.83	107.91	6,383.2	-285.8	884.4	373.4	0.00	0.00	0.00
6,600.0	14.83	107.91	6,479.9	-293.6	908.7	383.7	0.00	0.00	0.00
Drop 2°/100'									
6,642.3	14.83	107.91	6,520.8	-297.0	919.1	388.0	0.00	0.00	0.00
6,700.0	13.68	107.91	6,576.7	-301.3	932.6	393.7	2.00	-2.00	0.00
6,800.0	11.68	107.91	6,674.3	-308.1	953.4	402.6	2.00	-2.00	0.00
6,900.0	9.68	107.91	6,772.5	-313.8	971.1	410.0	2.00	-2.00	0.00
7,000.0	7.68	107.91	6,871.4	-318.4	985.4	416.1	2.00	-2.00	0.00
7,100.0	5.68	107.91	6,970.7	-322.0	996.5	420.7	2.00	-2.00	0.00
7,200.0	3.68	107.91	7,070.3	-324.5	1,004.2	424.0	2.00	-2.00	0.00
7,300.0	1.68	107.91	7,170.2	-325.9	1,008.7	425.9	2.00	-2.00	0.00
EOD @ Vertical - 1st Bone Spring Sand									
7,383.8	0.00	0.00	7,254.0	-326.3	1,009.8	426.4	2.00	-2.00	0.00
7,400.0	0.00	0.00	7,270.2	-326.3	1,009.8	426.4	0.00	0.00	0.00
7,500.0	0.00	0.00	7,370.2	-326.3	1,009.8	426.4	0.00	0.00	0.00
7,600.0	0.00	0.00	7,470.2	-326.3	1,009.8	426.4	0.00	0.00	0.00
7,700.0	0.00	0.00	7,570.2	-326.3	1,009.8	426.4	0.00	0.00	0.00
7,800.0	0.00	0.00	7,670.2	-326.3	1,009.8	426.4	0.00	0.00	0.00
7,900.0	0.00	0.00	7,770.2	-326.3	1,009.8	426.4	0.00	0.00	0.00
8,000.0	0.00	0.00	7,870.2	-326.3	1,009.8	426.4	0.00	0.00	0.00
8,100.0	0.00	0.00	7,970.2	-326.3	1,009.8	426.4	0.00	0.00	0.00



Well Planning Report



Database:	EDM 5000.1 Single User Db	Local Co-ordinate Reference:	Well Trojan Horse 35 WXY Fed Com #4H
Company:	Marathon Oil Permian LLC	TVD Reference:	WELL @ 3115.0usft (NA)
Project:	Eddy County, New Mexico (NAD 27)	MD Reference:	WELL @ 3115.0usft (NA)
Site:	Sec 26, T22S, R28E	North Reference:	Grid
Well:	Trojan Horse 35 WXY Fed Com #4H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Design #2		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
2nd Bone Spring Sand									
8,130.8	0.00	0.00	8,001.0	-326.3	1,009.8	426.4	0.00	0.00	0.00
8,200.0	0.00	0.00	8,070.2	-326.3	1,009.8	426.4	0.00	0.00	0.00
8,300.0	0.00	0.00	8,170.2	-326.3	1,009.8	426.4	0.00	0.00	0.00
8,400.0	0.00	0.00	8,270.2	-326.3	1,009.8	426.4	0.00	0.00	0.00
8,500.0	0.00	0.00	8,370.2	-326.3	1,009.8	426.4	0.00	0.00	0.00
8,600.0	0.00	0.00	8,470.2	-326.3	1,009.8	426.4	0.00	0.00	0.00
8,700.0	0.00	0.00	8,570.2	-326.3	1,009.8	426.4	0.00	0.00	0.00
8,800.0	0.00	0.00	8,670.2	-326.3	1,009.8	426.4	0.00	0.00	0.00
8,900.0	0.00	0.00	8,770.2	-326.3	1,009.8	426.4	0.00	0.00	0.00
9,000.0	0.00	0.00	8,870.2	-326.3	1,009.8	426.4	0.00	0.00	0.00
9,100.0	0.00	0.00	8,970.2	-326.3	1,009.8	426.4	0.00	0.00	0.00
9,200.0	0.00	0.00	9,070.2	-326.3	1,009.8	426.4	0.00	0.00	0.00
KOP @ 9260.8' MD / 9131.0' TVD - Build 10°/100'									
9,260.8	0.00	0.00	9,131.0	-326.3	1,009.8	426.4	0.00	0.00	0.00
9,300.0	3.92	178.29	9,170.2	-327.7	1,009.9	427.7	10.00	10.00	0.00
9,350.0	8.92	178.29	9,219.9	-333.2	1,010.1	433.3	10.00	10.00	0.00
3rd Bone Spring Sand									
9,366.4	10.56	178.29	9,236.0	-336.0	1,010.1	436.1	10.00	10.00	0.00
9,400.0	13.92	178.29	9,268.9	-343.1	1,010.4	443.2	10.00	10.00	0.00
9,450.0	18.92	178.29	9,316.8	-357.3	1,010.8	457.3	10.00	10.00	0.00
9,500.0	23.92	178.29	9,363.3	-375.5	1,011.3	475.5	10.00	10.00	0.00
9,550.0	28.92	178.29	9,408.1	-397.7	1,012.0	497.7	10.00	10.00	0.00
9,600.0	33.92	178.29	9,450.7	-423.8	1,012.8	523.6	10.00	10.00	0.00
9,650.0	38.92	178.29	9,491.0	-453.5	1,013.6	553.2	10.00	10.00	0.00
9,700.0	43.92	178.29	9,528.5	-486.5	1,014.6	586.2	10.00	10.00	0.00
Wolfcamp									
9,712.0	45.12	178.29	9,537.0	-494.9	1,014.9	594.6	10.00	10.00	0.00
9,750.0	48.92	178.29	9,562.9	-522.7	1,015.7	622.4	10.00	10.00	0.00
9,800.0	53.92	178.29	9,594.1	-561.8	1,016.9	661.3	10.00	10.00	0.00
9,850.0	58.92	178.29	9,621.7	-603.4	1,018.1	702.9	10.00	10.00	0.00
9,900.0	63.92	178.29	9,645.6	-647.3	1,019.4	746.7	10.00	10.00	0.00
9,950.0	68.92	178.29	9,665.6	-693.0	1,020.8	792.3	10.00	10.00	0.00
10,000.0	73.92	178.29	9,681.5	-740.4	1,022.2	839.6	10.00	10.00	0.00
10,050.0	78.92	178.29	9,693.3	-789.0	1,023.7	888.1	10.00	10.00	0.00
10,100.0	83.92	178.29	9,700.7	-838.4	1,025.2	937.4	10.00	10.00	0.00
Wolfcamp A									
10,102.5	84.18	178.29	9,701.0	-840.9	1,025.2	939.9	10.00	10.00	0.00
10,150.0	88.92	178.29	9,703.9	-888.2	1,026.6	987.1	10.00	10.00	0.00
EOC @ 89.50° Inc / 178.29° Azm / 9703.9' TVD									
10,155.8	89.50	178.29	9,703.9	-894.1	1,026.8	992.9	10.00	10.00	0.00
10,200.0	89.50	178.29	9,704.3	-938.2	1,028.1	1,037.0	0.00	0.00	0.00
10,300.0	89.50	178.29	9,705.2	-1,038.2	1,031.1	1,136.8	0.00	0.00	0.00
10,400.0	89.50	178.29	9,706.0	-1,138.1	1,034.1	1,236.5	0.00	0.00	0.00
10,500.0	89.50	178.29	9,706.9	-1,238.1	1,037.1	1,336.2	0.00	0.00	0.00
10,600.0	89.50	178.29	9,707.8	-1,338.0	1,040.1	1,436.0	0.00	0.00	0.00
10,700.0	89.50	178.29	9,708.6	-1,438.0	1,043.1	1,535.7	0.00	0.00	0.00
10,800.0	89.50	178.29	9,709.5	-1,537.9	1,046.1	1,635.5	0.00	0.00	0.00
10,900.0	89.50	178.29	9,710.4	-1,637.9	1,049.0	1,735.2	0.00	0.00	0.00
11,000.0	89.50	178.29	9,711.2	-1,737.8	1,052.0	1,835.0	0.00	0.00	0.00
11,100.0	89.50	178.29	9,712.1	-1,837.8	1,055.0	1,934.7	0.00	0.00	0.00
11,200.0	89.50	178.29	9,713.0	-1,937.7	1,058.0	2,034.4	0.00	0.00	0.00
11,300.0	89.50	178.29	9,713.8	-2,037.7	1,061.0	2,134.2	0.00	0.00	0.00



Well Planning Report



Database:	EDM 5000.1 Single User Db	Local Co-ordinate Reference:	Well Trojan Horse 35 WXY Fed Com #4H
Company:	Marathon Oil Permian LLC	TVD Reference:	WELL @ 3115.0usft (NA)
Project:	Eddy County, New Mexico (NAD 27)	MD Reference:	WELL @ 3115.0usft (NA)
Site:	Sec 26, T22S, R28E	North Reference:	Grid
Well:	Trojan Horse 35 WXY Fed Com #4H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Design #2		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
11,400.0	89.50	178.29	9,714.7	-2,137.6	1,064.0	2,233.9	0.00	0.00	0.00
11,500.0	89.50	178.29	9,715.6	-2,237.6	1,067.0	2,333.7	0.00	0.00	0.00
11,600.0	89.50	178.29	9,716.4	-2,337.5	1,070.0	2,433.4	0.00	0.00	0.00
11,700.0	89.50	178.29	9,717.3	-2,437.5	1,072.9	2,533.2	0.00	0.00	0.00
11,800.0	89.50	178.29	9,718.2	-2,537.4	1,075.9	2,632.9	0.00	0.00	0.00
11,900.0	89.50	178.29	9,719.0	-2,637.4	1,078.9	2,732.7	0.00	0.00	0.00
12,000.0	89.50	178.29	9,719.9	-2,737.3	1,081.9	2,832.4	0.00	0.00	0.00
12,100.0	89.50	178.29	9,720.7	-2,837.3	1,084.9	2,932.1	0.00	0.00	0.00
12,200.0	89.50	178.29	9,721.6	-2,937.2	1,087.9	3,031.9	0.00	0.00	0.00
12,300.0	89.50	178.29	9,722.5	-3,037.2	1,090.9	3,131.6	0.00	0.00	0.00
12,400.0	89.50	178.29	9,723.3	-3,137.2	1,093.8	3,231.4	0.00	0.00	0.00
12,500.0	89.50	178.29	9,724.2	-3,237.1	1,096.8	3,331.1	0.00	0.00	0.00
12,600.0	89.50	178.29	9,725.1	-3,337.1	1,099.8	3,430.9	0.00	0.00	0.00
12,700.0	89.50	178.29	9,725.9	-3,437.0	1,102.8	3,530.6	0.00	0.00	0.00
12,800.0	89.50	178.29	9,726.8	-3,537.0	1,105.8	3,630.4	0.00	0.00	0.00
12,900.0	89.50	178.29	9,727.7	-3,636.9	1,108.8	3,730.1	0.00	0.00	0.00
13,000.0	89.50	178.29	9,728.5	-3,736.9	1,111.8	3,829.8	0.00	0.00	0.00
13,100.0	89.50	178.29	9,729.4	-3,836.8	1,114.8	3,929.6	0.00	0.00	0.00
13,200.0	89.50	178.29	9,730.3	-3,936.8	1,117.7	4,029.3	0.00	0.00	0.00
13,300.0	89.50	178.29	9,731.1	-4,036.7	1,120.7	4,129.1	0.00	0.00	0.00
13,400.0	89.50	178.29	9,732.0	-4,136.7	1,123.7	4,228.8	0.00	0.00	0.00
13,500.0	89.50	178.29	9,732.8	-4,236.6	1,126.7	4,328.6	0.00	0.00	0.00
13,600.0	89.50	178.29	9,733.7	-4,336.6	1,129.7	4,428.3	0.00	0.00	0.00
13,700.0	89.50	178.29	9,734.6	-4,436.5	1,132.7	4,528.1	0.00	0.00	0.00
13,800.0	89.50	178.29	9,735.4	-4,536.5	1,135.7	4,627.8	0.00	0.00	0.00
13,900.0	89.50	178.29	9,736.3	-4,636.4	1,138.6	4,727.5	0.00	0.00	0.00
14,000.0	89.50	178.29	9,737.2	-4,736.4	1,141.6	4,827.3	0.00	0.00	0.00
14,100.0	89.50	178.29	9,738.0	-4,836.3	1,144.6	4,927.0	0.00	0.00	0.00
14,200.0	89.50	178.29	9,738.9	-4,936.3	1,147.6	5,026.8	0.00	0.00	0.00
14,300.0	89.50	178.29	9,739.8	-5,036.2	1,150.6	5,126.5	0.00	0.00	0.00
14,400.0	89.50	178.29	9,740.6	-5,136.2	1,153.6	5,226.3	0.00	0.00	0.00
14,500.0	89.50	178.29	9,741.5	-5,236.1	1,156.6	5,326.0	0.00	0.00	0.00
14,600.0	89.50	178.29	9,742.4	-5,336.1	1,159.6	5,425.7	0.00	0.00	0.00
14,700.0	89.50	178.29	9,743.2	-5,436.0	1,162.5	5,525.5	0.00	0.00	0.00
PPP2 @ 14765.3' MD / 9743.8' TVD - Turn 2°/100'									
14,765.3	89.50	178.29	9,743.8	-5,501.3	1,164.5	5,590.7	0.00	0.00	0.00
14,800.0	89.50	178.98	9,744.1	-5,536.0	1,165.3	5,625.2	2.00	0.00	2.00
EOT @ 89.50° Inc / 180.87° Azm									
14,894.6	89.50	180.87	9,744.9	-5,630.6	1,165.4	5,719.4	2.00	0.00	2.00
14,900.0	89.50	180.87	9,745.0	-5,636.0	1,165.4	5,724.7	0.00	0.00	0.00
15,000.0	89.50	180.87	9,745.8	-5,736.0	1,163.8	5,824.0	0.00	0.00	0.00
15,100.0	89.50	180.87	9,746.7	-5,836.0	1,162.3	5,923.4	0.00	0.00	0.00
15,200.0	89.50	180.87	9,747.6	-5,935.9	1,160.8	6,022.7	0.00	0.00	0.00
15,300.0	89.50	180.87	9,748.4	-6,035.9	1,159.3	6,122.0	0.00	0.00	0.00
15,400.0	89.50	180.87	9,749.3	-6,135.9	1,157.7	6,221.3	0.00	0.00	0.00
15,500.0	89.50	180.87	9,750.2	-6,235.9	1,156.2	6,320.6	0.00	0.00	0.00
15,600.0	89.50	180.87	9,751.0	-6,335.9	1,154.7	6,420.0	0.00	0.00	0.00
15,700.0	89.50	180.87	9,751.9	-6,435.9	1,153.2	6,519.3	0.00	0.00	0.00
15,800.0	89.50	180.87	9,752.8	-6,535.8	1,151.6	6,618.6	0.00	0.00	0.00
15,900.0	89.50	180.87	9,753.6	-6,635.8	1,150.1	6,717.9	0.00	0.00	0.00
16,000.0	89.50	180.87	9,754.5	-6,735.8	1,148.6	6,817.3	0.00	0.00	0.00
16,100.0	89.50	180.87	9,755.4	-6,835.8	1,147.1	6,916.6	0.00	0.00	0.00
16,200.0	89.50	180.87	9,756.2	-6,935.8	1,145.5	7,015.9	0.00	0.00	0.00
16,300.0	89.50	180.87	9,757.1	-7,035.8	1,144.0	7,115.2	0.00	0.00	0.00



Well Planning Report



Database:	EDM 5000.1 Single User Db	Local Co-ordinate Reference:	Well Trojan Horse 35 WXY Fed Com #4H
Company:	Marathon Oil Permian LLC	TVD Reference:	WELL @ 3115.0usft (NA)
Project:	Eddy County, New Mexico (NAD 27)	MD Reference:	WELL @ 3115.0usft (NA)
Site:	Sec 26, T22S, R28E	North Reference:	Grid
Well:	Trojan Horse 35 WXY Fed Com #4H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Design #2		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
16,400.0	89.50	180.87	9,758.0	-7,135.8	1,142.5	7,214.5	0.00	0.00	0.00
16,500.0	89.50	180.87	9,758.8	-7,235.7	1,141.0	7,313.9	0.00	0.00	0.00
16,600.0	89.50	180.87	9,759.7	-7,335.7	1,139.4	7,413.2	0.00	0.00	0.00
16,700.0	89.50	180.87	9,760.6	-7,435.7	1,137.9	7,512.5	0.00	0.00	0.00
16,800.0	89.50	180.87	9,761.4	-7,535.7	1,136.4	7,611.8	0.00	0.00	0.00
16,900.0	89.50	180.87	9,762.3	-7,635.7	1,134.9	7,711.2	0.00	0.00	0.00
17,000.0	89.50	180.87	9,763.2	-7,735.7	1,133.3	7,810.5	0.00	0.00	0.00
17,100.0	89.50	180.87	9,764.0	-7,835.6	1,131.8	7,909.8	0.00	0.00	0.00
17,200.0	89.50	180.87	9,764.9	-7,935.6	1,130.3	8,009.1	0.00	0.00	0.00
17,300.0	89.50	180.87	9,765.8	-8,035.6	1,128.8	8,108.4	0.00	0.00	0.00
17,400.0	89.50	180.87	9,766.6	-8,135.6	1,127.2	8,207.8	0.00	0.00	0.00
17,500.0	89.50	180.87	9,767.5	-8,235.6	1,125.7	8,307.1	0.00	0.00	0.00
17,600.0	89.50	180.87	9,768.4	-8,335.6	1,124.2	8,406.4	0.00	0.00	0.00
17,700.0	89.50	180.87	9,769.2	-8,435.6	1,122.7	8,505.7	0.00	0.00	0.00
17,800.0	89.50	180.87	9,770.1	-8,535.5	1,121.1	8,605.1	0.00	0.00	0.00
17,900.0	89.50	180.87	9,771.0	-8,635.5	1,119.6	8,704.4	0.00	0.00	0.00
18,000.0	89.50	180.87	9,771.8	-8,735.5	1,118.1	8,803.7	0.00	0.00	0.00
18,100.0	89.50	180.87	9,772.7	-8,835.5	1,116.6	8,903.0	0.00	0.00	0.00
18,200.0	89.50	180.87	9,773.6	-8,935.5	1,115.0	9,002.3	0.00	0.00	0.00
18,300.0	89.50	180.87	9,774.4	-9,035.5	1,113.5	9,101.7	0.00	0.00	0.00
18,400.0	89.50	180.87	9,775.3	-9,135.4	1,112.0	9,201.0	0.00	0.00	0.00
18,500.0	89.50	180.87	9,776.2	-9,235.4	1,110.4	9,300.3	0.00	0.00	0.00
18,600.0	89.50	180.87	9,777.0	-9,335.4	1,108.9	9,399.6	0.00	0.00	0.00
18,700.0	89.50	180.87	9,777.9	-9,435.4	1,107.4	9,499.0	0.00	0.00	0.00
PPP3 @ 18772.5' MD / 9778.5' TVD									
18,772.5	89.50	180.87	9,778.5	-9,507.9	1,106.3	9,571.0	0.00	0.00	0.00
18,800.0	89.50	180.87	9,778.8	-9,535.4	1,105.9	9,598.3	0.00	0.00	0.00
18,900.0	89.50	180.87	9,779.6	-9,635.4	1,104.3	9,697.6	0.00	0.00	0.00
19,000.0	89.50	180.87	9,780.5	-9,735.4	1,102.8	9,796.9	0.00	0.00	0.00
19,100.0	89.50	180.87	9,781.4	-9,835.3	1,101.3	9,896.3	0.00	0.00	0.00
19,200.0	89.50	180.87	9,782.2	-9,935.3	1,099.8	9,995.6	0.00	0.00	0.00
19,300.0	89.50	180.87	9,783.1	-10,035.3	1,098.2	10,094.9	0.00	0.00	0.00
19,400.0	89.50	180.87	9,784.0	-10,135.3	1,096.7	10,194.2	0.00	0.00	0.00
19,500.0	89.50	180.87	9,784.8	-10,235.3	1,095.2	10,293.5	0.00	0.00	0.00
19,600.0	89.50	180.87	9,785.7	-10,335.3	1,093.7	10,392.9	0.00	0.00	0.00
19,700.0	89.50	180.87	9,786.6	-10,435.2	1,092.1	10,492.2	0.00	0.00	0.00
19,800.0	89.50	180.87	9,787.4	-10,535.2	1,090.6	10,591.5	0.00	0.00	0.00
19,900.0	89.50	180.87	9,788.3	-10,635.2	1,089.1	10,690.8	0.00	0.00	0.00
TD @ 20006.0' MD / 9789.2' TVD									
20,006.0	89.50	180.87	9,789.2	-10,741.2	1,087.5	10,796.1	0.00	0.00	0.00



Well Planning Report



Database:	EDM 5000.1 Single User Db	Local Co-ordinate Reference:	Well Trojan Horse 35 WXY Fed Com #4H
Company:	Marathon Oil Permian LLC	TVD Reference:	WELL @ 3115.0usft (NA)
Project:	Eddy County, New Mexico (NAD 27)	MD Reference:	WELL @ 3115.0usft (NA)
Site:	Sec 26, T22S, R28E	North Reference:	Grid
Well:	Trojan Horse 35 WXY Fed Com #4H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Design #2		

Design Targets									
Target Name									
- hit/miss target	Dip Angle	Dip Dir.	TVD	+N/-S	+E/-W	Northing	Easting	Latitude	Longitude
- Shape	(°)	(°)	(usft)	(usft)	(usft)	(usft)	(usft)		
T H 35 WXY FC #4H - E	0.00	0.00	5,685.8	-228.2	708.7	493,472.97	584,410.71	32° 21' 22.955 N	104° 3' 35.906 W
- plan misses target center by 0.8usft at 5778.5usft MD (5685.7 TVD, -229.0 N, 708.7 E)									
- Point									
T H 35 WXY FC #4H - V	0.00	0.00	7,254.0	-326.3	1,009.8	493,374.85	584,711.82	32° 21' 21.976 N	104° 3' 32.399 W
- plan hits target center									
- Point									
T H 35 WXY FC #4H - P	0.00	0.00	9,743.8	-5,501.3	1,164.5	488,199.81	584,866.47	32° 20' 30.760 N	104° 3' 30.751 W
- plan hits target center									
- Point									
T H 35 WXY FC #4H - P	0.00	0.00	9,778.5	-9,507.8	1,105.6	484,193.32	584,807.55	32° 19' 51.113 N	104° 3' 31.557 W
- plan misses target center by 0.7usft at 18772.5usft MD (9778.5 TVD, -9507.9 N, 1106.3 E)									
- Point									
T H 35 WXY FC #4H - P	0.00	0.00	9,789.2	-10,741.2	1,087.5	482,960.00	584,789.45	32° 19' 38.908 N	104° 3' 31.805 W
- plan hits target center									
- Point									

Formations						
Measured Depth	Vertical Depth	Name	Lithology	Dip	Dip Direction	
(usft)	(usft)			(°)	(°)	
122.0	122.0	Rustler				
504.0	504.0	Salado				
1,050.0	1,050.0	Castile				
2,683.1	2,683.0	Lamar/Base of Salt				
2,709.2	2,709.0	Bell Canyon				
3,583.6	3,564.0	Cherry Canyon				
4,861.2	4,799.0	Brushy Canyon				
6,379.8	6,267.0	Bone Spring				
7,383.8	7,254.0	1st Bone Spring Sand				
8,130.8	8,001.0	2nd Bone Spring Sand				
9,366.4	9,236.0	3rd Bone Spring Sand				
9,712.0	9,537.0	Wolfcamp				
10,102.5	9,701.0	Wolfcamp A				

Plan Annotations					
Measured Depth	Vertical Depth	Local Coordinates		Comment	
(usft)	(usft)	+N/-S	+E/-W		
(usft)	(usft)	(usft)	(usft)		
2,500.0	2,500.0	0.0	0.0	Build 2°/100'	
3,241.5	3,233.2	-29.3	90.8	EOB @ 14.83° Inc / 107.91° Azm	
5,778.6	5,685.8	-229.0	708.7	Enter @ 5778.6' MD / 5685.8' TVD	
6,642.3	6,520.8	-297.0	919.1	Drop 2°/100'	
7,383.8	7,254.0	-326.3	1,009.8	EOD @ Vertical	
9,260.8	9,131.0	-326.3	1,009.8	KOP @ 9260.8' MD / 9131.0' TVD - Build 10°/100'	
10,155.8	9,703.9	-894.1	1,026.8	EOC @ 89.50° Inc / 178.29° Azm / 9703.9' TVD	
14,765.3	9,743.8	-5,501.3	1,164.5	PPP2 @ 14765.3' MD / 9743.8' TVD - Turn 2°/100'	
14,894.6	9,744.9	-5,630.6	1,165.4	EOT @ 89.50° Inc / 180.87° Azm	
18,772.5	9,778.5	-9,507.9	1,106.3	PPP3 @ 18772.5' MD / 9778.5' TVD	
20,006.0	9,789.2	-10,741.2	1,087.5	TD @ 20006.0' MD / 9789.2' TVD	

MARATHON OIL PERMIAN LLC

DRILLING AND OPERATIONS PLAN

WELL NAME / NUMBER: TROJAN HORSE 35 WXY FED COM 4H

STATE: NEW MEXICO

COUNTY: EDDY

Application Data Report

1. WELL LOCATION TABLE

Traverse Segment	Latitude NAD83	Longitude NAD83	Elevation (ft SS)	MD (RKB)	TVD (RKB)	Lease Serial	NS Foot	NS Indicator	EW Foot	EW Indicator	TWSP	Range	Section	Aliquot/Lot	Lease Type
SHL	32.35712921	-104.06276375	3090	0	0	NMNM067979	233	FSL	1302	FWL	22S	28E	26	SWSW	F
ENTER	32.35649703	-104.06047844	-2596	5779	5686	NMNM019601	0	FNL	2010	FWL	22S	28E	35	NENW	F
KOP/ FTP	32.35622838	-104.05949583	-6041	9261	9131	NMNM019601	100	FNL	2310	FWL	22S	28E	35	NENW	F
PPP-2	32.34199886	-104.05903812	-6654	14765	9744	STATE	0	FNL	2311	FWL	23S	28E	2	NENW (3)	S
PPP-3	32.33098551	-104.05926131	-6689	18773	9779	PRIVATE/FEE	1333	FSL	2310	FWL	23S	28E	2	SESW	P
BHL	32.32759537	-104.05933000	-6699	20006	9789	PRIVATE/FEE	100	FSL	2310	FWL	23S	28E	2	SESW	P

Drilling Plan Data Report

1. GEOLOGIC FORMATIONS

Formation	True Vertical Depth (ft)	Measured Depth (ft)	Lithologies	Mineral Resources
Rustler	122	122	Salt/Anhydrite	BRINE
Castile	1050	1050	Salt/Anhydrite	BRINE
Base of Salt	2683	2683	Limy Sands	BRINE
Lamar	2683	2683	Sand/Shales	NONE
Delaware	2709	2710	Sands/Shale	OIL
Bone Spring	6267	6281	Sands/Carbonates	OIL
Wolfcamp	9537	9709	Carbonates/Shales/Sands	OIL

2. BLOWOUT PREVENTION

BOP installed and tested before drilling which hole?	Size?	Min. Required WP	Type	✓	Tested to:
12 1/4"	13 5/8"	5000	Annular	X	100% of working pressure
			BOP Stack	X	5000
8 3/4"	13 5/8"	10000	Annular	X	50% of working pressure
			BOP Stack	X	10000

BOP/BOPE will be tested by an independent service company to 250 psi low and the high pressure indicated above per Onshore Order 2 requirements. The System may be upgraded to a higher pressure but still tested to the working pressure listed in the table above. If the system is upgraded all the components installed will be functional and tested.

Pipe rams will be operationally checked each 24 hour period. Blind rams will be operationally checked on each trip out of the hole. These checks will be noted on the daily tour sheets. Other accessories to the BOP equipment will include a Kelly cock, full opening safety valve / inside BOP and choke lines and choke manifold. See attached schematics.

Y	Formation integrity test will be performed per Onshore Order #2. On Exploratory wells or on that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Will be tested in accordance with Onshore Oil and Gas Order #2 III.B.1.i.	
Y	A variance is requested for the use of a flexible choke line from the BOP to Choke Manifold. See attached for specs and hydrostatic test chart.	
	N	Are anchors required by manufacturer?
Y	A multibowl wellhead is being used. The BOP will be tested per Onshore Order #2 after installation on the surface casing which will cover testing requirements for a maximum of 30 days. If any seal subject to test pressure is broken the system must be tested.	

3. CASING PROGRAM

String Type	Hole Size	Csg Size	Top Set MD	Bottom Set MD	Top Set TVD	Bottom Set TVD	Top Set MSL	Bottom Set MSL	Weight (lbs/ft)	Grade	Conn.	SF Collapse	SF Burst	SF Tension
Surface	17.5	13 3/8	0	400	0	400	2911	2511	54.5	J55	BTC	5.22	1.81	4.52
Intermediate	12.25	9 5/8	0	9160	0	9031	2911	-6120	40	P110HC	BTC	1.2	1.42	2.44
Production	8.75	5 1/2	0	20006	0	9789	2911	-6878	23	P110HC	TLW	2.53	1.26	2.22

All casing strings will be tested in accordance with Onshore Oil and Gas Order #2 III.B.1.h

Is casing new? If used, attach certification as required in Onshore Order #1											Y
Does casing meet API specifications? If no, attach casing specification sheet.											Y
Is premium or uncommon casing planned? If yes attach casing specification sheet.											N
Does the above casing design meet or exceed BLM's minimum standards? If not provide justification (loading assumptions, casing design criteria).											Y
Will the intermediate pipe be kept at a minimum 1/3 fluid filled to avoid approaching the collapse pressure rating of the casing?											Y
Is well located within Capitan Reef?											N
If yes, does production casing cement tie back a minimum of 50' above the Reef?											
Is well within the designated 4 string boundary.											
Is well located in SOPA but not in R-111-P?											N
If yes, are the first 2 strings cemented to surface and 3 rd string cement tied back 500' into previous casing?											
Is well located in R-111-P and SOPA?											N
If yes, are the first three strings cemented to surface?											
Is 2 nd string set 100' to 600' below the base of salt?											
Is well located in high	N										N
If yes, are there two strings cemented to surface?											
(For 2 string wells) If yes, is there a contingency casing if lost circulation occurs?											
Is well located in critical Cave/Karst?											N
If yes, are there three strings cemented to surface?											

4. CEMENT

String Type	Lead/Tail	Top MD	Bottom MD	Quantity (sks)	Yield (ft3/sks)	Density (ppg)	Slurry Volume (ft3)	Excess (%)	Cement Type	Additives
Surface	Lead	0	100	64	2.12	12.5	135	25	Class C	LCM
Surface	Tail	100	400	197	1.32	14.8	260	25	Class C	Accelerator
Intermediate	Lead	0	8660	1567	2.18	12.4	3415	25	Class C	Extender, Accelerator
Intermediate	Tail	8660	9160	147	1.33	14.8	196	25	Class C	Retarder
Production	Tail	8860	20006	2135	1.68	13.0	3588	25	Class H	Extender, Fluid Loss, Dispersant

Stage tool depth(s) will be adjusted based on hole conditions and cement volumes will be adjusted proportionally. Stage tool will be set a minimum of 50 feet below previous casing and a minimum of 200 feet above current shoe. Lab reports with the 500 psi compressive strength time for the cement will be onsite for review.

Pilot hole depth: N/A TVD/MD

KOP: N/A TVD/MD

Plug Top	Plug Bottom	Excess (%)	Quantity (sx)	Density (ppg)	Yield (ft3/sks)	Water gal/sk	Slurry Description and Cement Type

Attach plugging procedure for pilot hole: N/A

5. CIRCULATING MEDIUM

Top Depth	Bottom Depth	Mud Type	Min. Weight (ppg)	Max Weight (ppg)
0	400	Water Based Mud	8.4	8.8
400	9160	Brine/Oil Based	9.2	10.2
9160	20006	Oil Based Mud	10.5	12.5

Losses or gains in the mud system will be monitored visually/manually as well as with an electronic PVT.
The necessary mud products for additional weight and fluid loss control will be on location at all times.

6. TEST, LOGGING, CORING

List of production tests including testing procedures, equipment and safety measures:

GR from TD to surface (horizontal well - vertical portion of hole)

List of open and cased hole logs run in the well:

GR while drilling from Intermediate casing shoe to TD.

Coring operation description for the well:

No coring is planned at this time.

Mud Logger: None.

DST's: None.

Open Hole Logs: GR while drilling from Intermediate casing shoe to TD.

7. PRESSURE

ANTICIPATED BOTTOM HOLE PRESSURE: 6,363 psi

ANTICIPATED BOTTOM HOLE TEMPERATURE: 195 °F

ANTICIPATED ABNORMAL PRESSURE: N

ANTICIPATED ABNORMAL TEMPERATURE: N

POTENTIAL HAZARDS:

A. H2S detection equipment will be in operation after drilling out the surface casing shoe until the production casing has been cemented. Breathing equipment will be on location from drilling out the surface shoe until production casing is cemented. If H2S is encountered the operator will comply with Onshore Order #6.

B. No abnormal temperatures or pressures are anticipated. All personnel will be familiar with all aspects of safe operation of equipment being used to drill this well. Adequate flare lines will be installed off the mud/gas separator where gas may be flared safely.

C. No losses are anticipated at this time.

D. All personnel will be familiar with all aspects of safe operation of equipment being used to drill this well.

E. Adequate flare lines will be installed off the mud/gas separator where gas may be flared safely.

8. OTHER

Other Well Information**AUXILIARY WELL CONTROL AND MONITORING EQUIPMENT**

A Kelly cock will be in the drill string at all times.

A full opening drill pipe stabbing valve having the appropriate connections will be on the rig floor unobstructed and readily accessible at all times.

Hydrogen Sulfide detection equipment will be in operation after drilling out the surface casing shoe until the production casing is cemented. Breathing equipment will be on location upon drilling the surface casing shoe until total depth is reached. If Hydrogen Sulfide is encountered, measured amounts and formations will be reported to the BLM

ANTICIPATED STARTING DATE AND DURATION OF OPERATIONS

Road and location construction will begin after the BLM has approved the APD. Anticipated spud date will be as soon as possible after BLM approval and as soon as a rig will be available. Move in operations and drilling is expected to take 30 days.

Batch Drilling Plan

- Marathon Oil Permian LLC. respectfully requests the option to “batch” drill sections of a well with intentions of returning to the well for later completion.
- When it is determined that the use of a “batch” drilling process to increase overall efficiency and reduce rig time on location, the following steps will be utilized to ensure compliant well control before releasing drilling rig during the batch process.
- Succeeding a successful cement job, fluid levels will be monitored in both the annulus and casing string to be verified static.
- A mandrel hanger packoff will be ran and installed in the multi-bowl wellhead isolating and creating a barrier on the annulus. This packoff will be tested to 5,000 PSI validating the seals.
- At this point the well is secure and the drilling adapter will be removed from the wellhead.
- A 13-5/8” 5M temporary abandonment cap will be installed on the wellhead by stud and nut flange. The seals of the TA cap will then be pressure tested to 5,000 PSI.
- The drilling rig will skid to the next well on the pad to continue the batch drilling process.
- When returning to the well with the TA cap, the TA cap will be removed and the BOP will be nipped up on the wellhead.
- A BOP test will then be conducted according to Onshore Order #2 and drilling operations will resume on the subject well.

Request for Surface Rig

- Marathon Oil Permian LLC. Requests the option to contract a surface rig to drill, set surface casing and cement on the subject well. If the timing between rigs is such that Marathon Oil Permian LLC. would not be able to preset the surface section, the primary drilling rig will drill the well in its entirety per the APD.

PECOS DISTRICT DRILLING CONDITIONS OF APPROVAL

OPERATOR'S NAME:	Marathon Oil
LEASE NO.:	NMNM19601
LOCATION:	Section 26, T.22 S., R.28 E., NMPM
COUNTY:	Eddy County, New Mexico

WELL NAME & NO.:	Trojan Horse 35 WXY Fed Com 4H
SURFACE HOLE FOOTAGE:	233'/S & 1302'/W
BOTTOM HOLE FOOTAGE:	100'/S & 2310'/W

COA

H2S	<input checked="" type="radio"/> Yes	<input type="radio"/> No	
Potash	<input checked="" type="radio"/> None	<input type="radio"/> Secretary	<input type="radio"/> R-111-P
Cave/Karst Potential	<input type="radio"/> Low	<input checked="" type="radio"/> Medium	<input type="radio"/> High
Cave/Karst Potential	<input type="radio"/> Critical		
Variance	<input type="radio"/> None	<input checked="" type="radio"/> Flex Hose	<input type="radio"/> Other
Wellhead	<input type="radio"/> Conventional	<input checked="" type="radio"/> Multibowl	<input type="radio"/> Both
Other	<input type="checkbox"/> 4 String Area	<input type="checkbox"/> Capitan Reef	<input type="checkbox"/> WIPP
Other	<input checked="" type="checkbox"/> Fluid Filled	<input type="checkbox"/> Cement Squeeze	<input type="checkbox"/> Pilot Hole
Special Requirements	<input type="checkbox"/> Water Disposal	<input checked="" type="checkbox"/> COM	<input type="checkbox"/> Unit

A. HYDROGEN SULFIDE

A Hydrogen Sulfide (H2S) Drilling Plan shall be activated 500 feet prior to drilling into the **Delaware and Bone Springs** formations. As a result, the Hydrogen Sulfide area must meet Onshore Order 6 requirements, which includes equipment and personnel/public protection items. If Hydrogen Sulfide is encountered, please provide measured values and formations to the BLM.

B. CASING

1. The **13-3/8** inch surface casing shall be set at approximately **350** feet (a minimum of **70 feet (Eddy County)** into the Rustler Anhydrite and above the salt) and cemented to the surface.
 - a. If cement does not circulate to the surface, the appropriate BLM office shall be notified and a temperature survey utilizing an electronic type temperature survey with surface log readout will be used or a cement bond log shall be run to verify the top of the cement. Temperature survey will be run a minimum of six hours after pumping cement and ideally between 8-10 hours after completing the cement job.

- b. Wait on cement (WOC) time for a primary cement job will be a minimum of **8 hours** or 500 pounds compressive strength, whichever is greater. (This is to include the lead cement)
- c. Wait on cement (WOC) time for a remedial job will be a minimum of 4 hours after bringing cement to surface or 500 pounds compressive strength, whichever is greater.
- d. If cement falls back, remedial cementing will be done prior to drilling out that string.

Intermediate casing must be kept 1/3rd fluid filled to meet BLM minimum collapse requirement.

2. The minimum required fill of cement behind the **9-5/8** inch intermediate casing is:
 - Cement to surface. If cement does not circulate see B.1.a, c-d above.

Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry due to cave/karst or potash.

Option 2:

Operator is approved to use a DV tool, the depth may be adjusted as long as the cement is changed proportionally. The Operator shall contact BLM before proceeding with DV Tool operation.

- ❖ In Medium Cave/Karst Areas if cement does not circulate to surface on the first two casing strings, the cement on the 3rd casing string must come to surface.

3. The minimum required fill of cement behind the **5-1/2** inch production casing is:
 - Cement should tie-back at least **200 feet** into previous casing string. Operator shall provide method of verification.

C. PRESSURE CONTROL

1. **Variance approved to use flex line from BOP to choke manifold. Manufacturer's specification to be readily available. No external damage to flex line. Flex line to be installed as straight as possible (no hard bends).**
2. Operator has proposed a multi-bowl wellhead assembly. This assembly will only be tested when installed on the surface casing. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **5000 (5M)** psi.
 - a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.

- b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
- c. Manufacturer representative shall install the test plug for the initial BOP test.
- d. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
- e. Whenever any seal subject to test pressure is broken, all the tests in OOGO2.III.A.2.i must be followed.

D. SPECIAL REQUIREMENT (S)

Communitization Agreement

- The operator will submit a Communitization Agreement to the Santa Fe Office, 301 Dinosaur Trail Santa Fe, New Mexico 87508, at least 90 days before the anticipated date of first production from a well subject to a spacing order issued by the New Mexico Oil Conservation Division. The Communitization Agreement will include the signatures of all working interest owners in all Federal and Indian leases subject to the Communitization Agreement (i.e., operating rights owners and lessees of record), or certification that the operator has obtained the written signatures of all such owners and will make those signatures available to the BLM immediately upon request.
- If the operator does not comply with this condition of approval, the BLM may take enforcement actions that include, but are not limited to, those specified in 43 CFR 3163.1.
- In addition, the well sign shall include the surface and bottom hole lease numbers. When the Communitization Agreement number is known, it shall also be on the sign.

GENERAL REQUIREMENTS

The BLM is to be notified in advance for a representative to witness:

- a. Spudding well (minimum of 24 hours)
- b. Setting and/or Cementing of all casing strings (minimum of 4 hours)
- c. BOPE tests (minimum of 4 hours)

☒ Eddy County

Call the Carlsbad Field Office, 620 East Greene St., Carlsbad, NM 88220,
(575) 361-2822

☒ Lea County

Call the Hobbs Field Station, 414 West Taylor, Hobbs NM 88240, (575)
689-5981

1. Unless the production casing has been run and cemented or the well has been properly plugged, the drilling rig shall not be removed from over the hole without prior approval.
 - a. **Operator is approved to drill multiple wells utilizing a skid/walking rig. Operator shall secure the wellbore on the current well, after installing and testing the wellhead, by installing a blind flange of like pressure rating to the wellhead and a pressure gauge that can be monitored while drilling is performed on the other well(s).**
 - b. **Operator is approved to set surface casing with Spudder Rig**
 - **Notify the BLM when moving in and removing the Spudder Rig.**
 - **Notify the BLM when moving in the 2nd Rig. Rig to be moved in within 90 days of notification that Spudder Rig has left the location.**
 - **BOP/BOPE test to be conducted per Onshore Oil and Gas Order No. 2 as soon as 2nd Rig is rigged up on well.**
2. Floor controls are required for 3M or Greater systems. These controls will be on the rig floor, unobstructed, readily accessible to the driller and will be operational at all times during drilling and/or completion activities. Rig floor is defined as the area immediately around the rotary table; the area immediately above the substructure on which the draw works are located, this does not include the dog house or stairway area.
3. The record of the drilling rate along with the GR/N well log run from TD to surface (horizontal well – vertical portion of hole) shall be submitted to the BLM office as well as all other logs run on the borehole 30 days from completion. If available, a digital copy of the logs is to be submitted in addition to the paper copies. The Rustler top and top and bottom of Salt are to be recorded on the Completion Report.

A. CASING

1. Changes to the approved APD casing program need prior approval if the items substituted are of lesser grade or different casing size or are Non-API. The Operator can exchange the components of the proposal with that of superior strength (i.e. changing from J-55 to N-80, or from 36# to 40#). Changes to the approved cement program need prior approval if the altered cement plan has less volume or strength or if the changes are substantial (i.e. Multistage tool, ECP, etc.). The initial wellhead installed on the well will remain on the well with spools used as needed.
2. Wait on cement (WOC) for Potash Areas: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi for all cement blends, 2) until cement has been in place at least 24 hours. WOC time will be recorded in the driller's log. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.

3. Wait on cement (WOC) for Water Basin: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi at the shoe, 2) until cement has been in place at least 8 hours. WOC time will be recorded in the driller's log. See individual casing strings for details regarding lead cement slurry requirements. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
4. Provide compressive strengths including hours to reach required 500 pounds compressive strength prior to cementing each casing string. Have well specific cement details onsite prior to pumping the cement for each casing string.
5. No pea gravel permitted for remedial or fall back remedial without prior authorization from the BLM engineer.
6. On that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Formation at the shoe shall be tested to a minimum of the mud weight equivalent anticipated to control the formation pressure to the next casing depth or at total depth of the well. This test shall be performed before drilling more than 20 feet of new hole.
7. If hardband drill pipe is rotated inside casing, returns will be monitored for metal. If metal is found in samples, drill pipe will be pulled and rubber protectors which have a larger diameter than the tool joints of the drill pipe will be installed prior to continuing drilling operations.
8. Whenever a casing string is cemented in the R-111-P potash area, the NMOCD requirements shall be followed.

B. PRESSURE CONTROL

1. All blowout preventer (BOP) and related equipment (BOPE) shall comply with well control requirements as described in Onshore Oil and Gas Order No. 2 and API RP 53 Sec. 17.
2. If a variance is approved for a flexible hose to be installed from the BOP to the choke manifold, the following requirements apply: The flex line must meet the requirements of API 16C. Check condition of flexible line from BOP to choke manifold, replace if exterior is damaged or if line fails test. Line to be as straight as possible with no hard bends and is to be anchored according to Manufacturer's requirements. The flexible hose can be exchanged with a hose of equal size and equal or greater pressure rating. Anchor requirements, specification sheet and hydrostatic pressure test certification matching the hose in service, to be onsite for review. These documents shall be posted in the company man's trailer and on the rig floor.

3. 5M or higher system requires an HCR valve, remote kill line and annular to match. The remote kill line is to be installed prior to testing the system and tested to stack pressure.
4. If the operator has proposed a multi-bowl wellhead assembly in the APD. The following requirements must be met:
 - a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
 - b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
 - c. Manufacturer representative shall install the test plug for the initial BOP test.
 - d. Whenever any seal subject to test pressure is broken, all the tests in OOGO2.III.A.2.i must be followed.
 - e. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
5. The appropriate BLM office shall be notified a minimum of 4 hours in advance for a representative to witness the tests.
 - a. In a water basin, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. The casing cut-off and BOP installation can be initiated four hours after installing the slips, which will be approximately six hours after bumping the plug. For those casing strings not using slips, the minimum wait time before cut-off is eight hours after bumping the plug. BOP/BOPE testing can begin after cut-off or once cement reaches 500 psi compressive strength (including lead when specified), whichever is greater. However, if the float does not hold, cut-off cannot be initiated until cement reaches 500 psi compressive strength (including lead when specified).
 - b. In potash areas, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. For all casing strings, casing cut-off and BOP installation can be initiated at twelve hours after bumping the plug. However, **no tests** shall commence until the cement has had a minimum of 24 hours setup time, except the casing pressure test can be initiated immediately after bumping the plug (only applies to single stage cement jobs).
 - c. The tests shall be done by an independent service company utilizing a test plug not a cup or J-packer. The operator also has the option of utilizing an independent tester to test without a plug (i.e. against the casing) pursuant to Onshore Order 2 with the pressure not to exceed 70% of the burst rating for

the casing. Any test against the casing must meet the WOC time for water basin (8 hours) or potash (24 hours) or 500 pounds compressive strength, whichever is greater, prior to initiating the test (see casing segment as lead cement may be critical item).

- d. The test shall be run on a 5000 psi chart for a 2-3M BOP/BOP, on a 10000 psi chart for a 5M BOP/BOPE and on a 15000 psi chart for a 10M BOP/BOPE. If a linear chart is used, it shall be a one hour chart. A circular chart shall have a maximum 2 hour clock. If a twelve hour or twenty-four hour chart is used, tester shall make a notation that it is run with a two hour clock.
- e. The results of the test shall be reported to the appropriate BLM office.
- f. All tests are required to be recorded on a calibrated test chart. A copy of the BOP/BOPE test chart and a copy of independent service company test will be submitted to the appropriate BLM office.
- g. The BOP/BOPE test shall include a low pressure test from 250 to 300 psi. The test will be held for a minimum of 10 minutes if test is done with a test plug and 30 minutes without a test plug. This test shall be performed prior to the test at full stack pressure.
- h. BOP/BOPE must be tested by an independent service company within 500 feet of the top of the Wolfcamp formation if the time between the setting of the intermediate casing and reaching this depth exceeds 20 days. This test does not exclude the test prior to drilling out the casing shoe as per Onshore Order No. 2.

C. DRILLING MUD

Mud system monitoring equipment, with derrick floor indicators and visual and audio alarms, shall be operating before drilling into the Wolfcamp formation, and shall be used until production casing is run and cemented.

D. WASTE MATERIAL AND FLUIDS

All waste (i.e. drilling fluids, trash, salts, chemicals, sewage, gray water, etc.) created as a result of drilling operations and completion operations shall be safely contained and disposed of properly at a waste disposal facility. No waste material or fluid shall be disposed of on the well location or surrounding area.

Porto-johns and trash containers will be on-location during fracturing operations or any other crew-intensive operations.

ZS 031422

District I

1625 N. French Dr., Hobbs, NM 88240
 Phone:(575) 393-6161 Fax:(575) 393-0720

District II

811 S. First St., Artesia, NM 88210
 Phone:(575) 748-1283 Fax:(575) 748-9720

District III

1000 Rio Brazos Rd., Aztec, NM 87410
 Phone:(505) 334-6178 Fax:(505) 334-6170

District IV

1220 S. St Francis Dr., Santa Fe, NM 87505
 Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 121753

CONDITIONS

Operator: MARATHON OIL PERMIAN LLC 990 Town & Country Blvd. Houston, TX 77024	OGRID: 372098
	Action Number: 121753
	Action Type: [C-101] BLM - Federal/Indian Land Lease (Form 3160-3)

CONDITIONS

Created By	Condition	Condition Date
kpickford	Operator must be in compliance with 5.9 for inactive wells prior to C-104 approval.	7/6/2022
kpickford	Will require a administrative order for non-standard location prior to placing the well on production	7/6/2022
kpickford	Notify OCD 24 hours prior to casing & cement	7/6/2022
kpickford	Will require a File As Drilled C-102 and a Directional Survey with the C-104	7/6/2022
kpickford	Once the well is spud, to prevent ground water contamination through whole or partial conduits from the surface, the operator shall drill without interruption through the fresh water zone or zones and shall immediately set in cement the water protection string	7/6/2022
kpickford	Cement is required to circulate on both surface and intermediate1 strings of casing	7/6/2022
kpickford	Oil base muds are not to be used until fresh water zones are cased and cemented providing isolation from the oil or diesel. This includes synthetic oils. Oil based mud, drilling fluids and solids must be contained in a steel closed loop system	7/6/2022
