

Form 3160-3
(June 2015)FORM APPROVED
OMB No. 1004-0137
Expires: January 31, 2018

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
APPLICATION FOR PERMIT TO DRILL OR REENTER

1a. Type of work: <input type="checkbox"/> DRILL <input type="checkbox"/> REENTER 1b. Type of Well: <input type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input type="checkbox"/> Other 1c. Type of Completion: <input type="checkbox"/> Hydraulic Fracturing <input type="checkbox"/> Single Zone <input type="checkbox"/> Multiple Zone		5. Lease Serial No. 6. If Indian, Allottee or Tribe Name 7. If Unit or CA Agreement, Name and No. 8. Lease Name and Well No.
2. Name of Operator		9. API Well No. 30-015-49821
3a. Address	3b. Phone No. (include area code)	10. Field and Pool, or Exploratory COTTON DRAW; BONE SPRING
4. Location of Well (Report location clearly and in accordance with any State requirements. *) At surface At proposed prod. zone		11. Sec., T. R. M. or Blk. and Survey or Area
14. Distance in miles and direction from nearest town or post office*		12. County or Parish
13. State		
15. Distance from proposed* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any)	16. No of acres in lease	17. Spacing Unit dedicated to this well
18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft.	19. Proposed Depth	20. BLM/BIA Bond No. in file
21. Elevations (Show whether DF, KDB, RT, GL, etc.)	22. Approximate date work will start*	23. Estimated duration
24. Attachments		

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, and the Hydraulic Fracturing rule per 43 CFR 3162.3-3 (as applicable)

- | | |
|---|---|
| 1. Well plat certified by a registered surveyor.
2. A Drilling Plan.
3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office). | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).
5. Operator certification.
6. Such other site specific information and/or plans as may be requested by the BLM. |
|---|---|

25. Signature	Name (Printed/Typed)	Date
Title		
Approved by (Signature)	Name (Printed/Typed)	Date
Title		
Office		

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
 Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.



(Continued on page 2)

*(Instructions on page 2)

District I
1625 N. French Dr., Hobbs, NM 88240
Phone: (575) 393-6161 Fax: (575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone: (575) 748-1283 Fax: (575) 748-9720
District III
1000 Rio Brazos Road, Aztec, NM 87410
Phone: (505) 334-6178 Fax: (505) 334-6170
District IV
1220 S. St. Francis Dr., Santa Fe, NM 87505
Phone: (505) 476-3460 Fax: (505) 476-3462

State of New Mexico
Energy, Minerals & Natural Resources Department
OIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, NM 87505

Form C-102
Revised August 1, 2011
Submit one copy to appropriate
District Office

☐ AMENDED REPORT

WELL LOCATION AND ACREAGE DEDICATION PLAT

¹ API Number 30-015-49821	² Pool Code 53800 13367	³ Pool Name Sand Dunes; Bone Spring COTTON DRAW; BONE SPRING
⁴ Property Code 332905	⁵ Property Name JAVELINA UNIT	
⁷ OGRID No. 4323	⁸ Operator Name CHEVRON U.S.A. INC	⁹ Elevation 3544'

¹⁰ Surface Location

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
C	14	24 SOUTH	31 EAST, N.M.P.M.		524'	NORTH	2365'	WEST	EDDY

¹¹ Bottom Hole Location If Different From Surface

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
C	2	24 SOUTH	31 EAST, N.M.P.M.		25'	NORTH	2310'	WEST	EDDY

¹² Dedicated Acres 640	¹³ Joint or Infill INFILL	¹⁴ Consolidation Code	¹⁵ Order No.
--------------------------------------	---	----------------------------------	-------------------------

No allowable will be assigned to this completion until all interests have been consolidated or a non-standard unit has been approved by the division.

¹⁶ JAVELINA UNIT NO. 420H WELL X= 680,693' Y= 445,363' LAT. 32.223070° N LONG. 103.749028° W NAD 27 X= 721,877' Y= 445,422' LAT. 32.223194° N LONG. 103.749511° W NAD83/2011 ELEV. +3,544' NAVD88	PROPOSED LAST TAKE POINT X= 680,591' Y= 456,349' LAT. 32.253271° N LONG. 103.749166° W NAD 27 X= 721,774' Y= 456,408' LAT. 32.253394° N LONG. 103.749650° W NAD83/2011	<p>2310'</p> <p>25'</p> <p>Proposed Last Take Point 100' FNL, 2310' FWL</p> <p>2</p> <p>Proposed Mid-Point</p> <p>N 00°13'51" W 5,259.52'</p> <p>N 00°14'53" W 5,177.40'</p> <p>11</p> <p>Proposed First Take Point 100' FSL, 2310' FWL</p> <p>N 05°23'44" W 626.84'</p> <p>14</p> <p>2365'</p> <p>524'</p>	¹⁷ OPERATOR CERTIFICATION I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief, and that this organization either owns a working interest or unleased mineral interest in the land including the proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of such a mineral or working interest, or to a voluntary pooling agreement or a compulsory pooling order heretofore entered by the division. <i>Jennifer Van Curen</i> 9/11/21 Signature Date JENNIFER VAN CUREN Printed Name E-mail Address
PROPOSED FIRST TAKE POINT X= 680,634' Y= 445,987' LAT. 32.224787° N LONG. 103.749208° W NAD 27 X= 721,818' Y= 446,046' LAT. 32.224910° N LONG. 103.749691° W NAD83/2011	PROPOSED BOTTOM HOLE LOCATION X= 680,590' Y= 456,424' LAT. 32.253477° N LONG. 103.749165° W NAD 27 X= 721,774' Y= 456,483' LAT. 32.253600° N LONG. 103.749650° W NAD83/2011		JENNIFER VAN CUREN Printed Name E-mail Address
PROPOSED MID-POINT X= 680,612' Y= 451,169' LAT. 32.239031° N LONG. 103.749189° W NAD 27 X= 721,795' Y= 451,228' LAT. 32.239154° N LONG. 103.749673° W NAD83/2011			¹⁸ SURVEYOR CERTIFICATION I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief. 05/21/2021 Date of Survey Signature and Seal of Professional Surveyor: Certificate Number

CORNER COORDINATES TABLE (NAD 27)

A - X=678280.36, Y=456436.48
B - X=679599.47, Y=456443.79
C - X=680918.57, Y=456451.10
D - X=683556.77, Y=456465.72
E - X=678301.64, Y=451154.80
F - X=679622.13, Y=451163.10
G - X=680942.63, Y=451171.39
H - X=683583.61, Y=451187.99
I - X=678324.50, Y=445873.60
J - X=679646.09, Y=445881.52
K - X=680967.68, Y=445889.45
L - X=683610.86, Y=445905.30

Section 2 – Enhanced Plan

EFFECTIVE APRIL 1, 2022

Beginning April 1, 2022, an operator that is not in compliance with its statewide natural gas capture requirement for the applicable reporting area must complete this section.

☐ Operator certifies that it is not required to complete this section because Operator is in compliance with its statewide natural gas capture requirement for the applicable reporting area.

IX. Anticipated Natural Gas Production:

Well	API	Anticipated Average Natural Gas Rate MCF/D	Anticipated Volume of Natural Gas for the First Year MCF

X. Natural Gas Gathering System (NGGS):

Operator	System	ULSTR of Tie-in	Anticipated Gathering Start Date	Available Maximum Daily Capacity of System Segment Tie-in

XI. Map. ☐ Attach an accurate and legible map depicting the location of the well(s), the anticipated pipeline route(s) connecting the production operations to the existing or planned interconnect of the natural gas gathering system(s), and the maximum daily capacity of the segment or portion of the natural gas gathering system(s) to which the well(s) will be connected.

XII. Line Capacity. The natural gas gathering system ☐ will ☐ will not have capacity to gather 100% of the anticipated natural gas production volume from the well prior to the date of first production.

XIII. Line Pressure. Operator ☐ does ☐ does not anticipate that its existing well(s) connected to the same segment, or portion, of the natural gas gathering system(s) described above will continue to meet anticipated increases in line pressure caused by the new well(s).

☐ Attach Operator's plan to manage production in response to the increased line pressure.

XIV. Confidentiality: ☐ Operator asserts confidentiality pursuant to Section 71-2-8 NMSA 1978 for the information provided in Section 2 as provided in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and attaches a full description of the specific information for which confidentiality is asserted and the basis for such assertion.

Section 3 - Certifications

Effective May 25, 2021

Operator certifies that, after reasonable inquiry and based on the available information at the time of submittal:

☒ Operator will be able to connect the well(s) to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system; or

☐ Operator will not be able to connect to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system.

If Operator checks this box, Operator will select one of the following:

Well Shut-In. ☐ Operator will shut-in and not produce the well until it submits the certification required by Paragraph (4) of Subsection D of 19.15.27.9 NMAC; or

Venting and Flaring Plan. ☐ Operator has attached a venting and flaring plan that evaluates and selects one or more of the potential alternative beneficial uses for the natural gas until a natural gas gathering system is available, including:

- (a) power generation on lease;
- (b) power generation for grid;
- (c) compression on lease;
- (d) liquids removal on lease;
- (e) reinjection for underground storage;
- (f) reinjection for temporary storage;
- (g) reinjection for enhanced oil recovery;
- (h) fuel cell production; and
- (i) other alternative beneficial uses approved by the division.

Section 4 - Notices

1. If, at any time after Operator submits this Natural Gas Management Plan and before the well is spud:

(a) Operator becomes aware that the natural gas gathering system it planned to connect the well(s) to has become unavailable or will not have capacity to transport one hundred percent of the production from the well(s), no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised venting and flaring plan containing the information specified in Paragraph (5) of Subsection D of 19.15.27.9 NMAC; or

(b) Operator becomes aware that it has, cumulatively for the year, become out of compliance with its baseline natural gas capture rate or natural gas capture requirement, no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised Natural Gas Management Plan for each well it plans to spud during the next 90 days containing the information specified in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and shall file an update for each Natural Gas Management Plan until Operator is back in compliance with its baseline natural gas capture rate or natural gas capture requirement.

2. OCD may deny or conditionally approve an APD if Operator does not make a certification, fails to submit an adequate venting and flaring plan which includes alternative beneficial uses for the anticipated volume of natural gas produced, or if OCD determines that Operator will not have adequate natural gas takeaway capacity at the time a well will be spud.

I certify that, after reasonable inquiry, the statements in and attached to this Natural Gas Management Plan are true and correct to the best of my knowledge and acknowledge that a false statement may be subject to civil and criminal penalties under the Oil and Gas Act.

Signature:	<i>Cindy Herrera-Murillo</i>
Printed Name:	Cindy Herrera-Murillo
Title:	Sr HSE Regulatory affairs Coordinator
E-mail Address:	eeof@chevron.com
Date:	09/11/2021
Phone:	575-263-0431
OIL CONSERVATION DIVISION (Only applicable when submitted as a standalone form)	
Approved By:	
Title:	
Approval Date:	
Conditions of Approval:	

VI. Separation Equipment:

Separation equipment installed at each Chevron facility is designed for maximum anticipated throughput and pressure to minimize waste. Separation equipment is designed and built according to ASME Sec VIII Div I to ensure gas is separated from liquid streams according to projected production.

VII./VIII. Operational & Best Management Practices:**1. General Requirements for Venting and Flaring of Natural Gas:**

- In all circumstances, Chevron will flare rather than vent unless flaring is technically infeasible and venting of natural gas will avoid a risk of an immediate and substantial adverse impact on safety, public health, or the environment.
- Chevron installs and operates vapor recovery units (VRUs) in new facilities to minimize venting and flaring. If a VRU experiences operating issues, it is quickly assessed so that action can be taken to return the VRU to operation or, if necessary, facilities are shut-in to reduce the venting or flaring of natural gas.

2. During Drilling Operations:

- Flare stacks will be located a minimum of 110 feet from the nearest surface hole location.
- If an emergency or malfunction occurs, gas will be flared or vented to avoid a risk of an immediate and substantial adverse impact on public health, safety or the environment and be properly reported to the NMOCD pursuant to 19.15.27.8.G.
- Natural gas is captured or combusted if technically feasible using best industry practices and control technologies, such as the use of separators (e.g., Sand Commanders) during normal drilling and completions operations.

3. During Completions:

- Chevron typically does not complete traditional flowback, instead Chevron will flow produced oil, water, and gas to a centralized tank battery and continuously recover salable quality gas. If Chevron completes traditional flowback, Chevron conducts reduced emission completions as required by 40 CFR 60.5375a by routing gas to a gas flow line as soon as practicable once there is enough gas to operate a separator. Venting does not occur once there is enough gas to operate a separator
- Normally, during completions a flare is not on-site. A Snubbing Unit will have a flare on-site, and the flare volume will be estimated.
- If natural gas does not meet pipeline quality specification, the gas is sampled twice per week until the gas meets the specifications.

4. During Production:

- An audio, visual and olfactory (AVO) inspection will be performed daily (at minimum) for active wells and facilities to confirm that all production equipment is operating properly and there are no leaks or releases except as allowed in Subsection D of 19.15.27.8 NMAC. Inactive, temporarily abandoned, or shut-in wells and facilities will be inspected weekly. Inspection records will be kept for a minimum of five years and will be available upon request by the division.
- Monitor manual liquid unloading for wells on-site, takes all reasonable actions to achieve a stabilized rate and pressure at the earliest practical time and takes reasonable actions to minimize venting to the maximum extent practicable.
- In all circumstances, Chevron will flare rather than vent unless flaring is technically infeasible and venting of natural gas will avoid a risk of an immediate and substantial adverse impact on safety, public health, or the environment.
- Chevron's design for new facilities utilizes air-activated pneumatic controllers and pumps.
- If natural gas does not meet pipeline quality specification, the gas is sampled twice per week until the gas meets the specifications.
- Chevron does not produce oil or gas until all flowlines, tank batteries, and oil/gas takeaway are installed, tested, and determined operational.

5. Performance Standards

- Equipment installed at each facility is designed for maximum anticipated throughput and pressure to minimize waste. Tank pressure relief systems utilize a soft seated or metal seated PSVs, as appropriate, which are both designed to not leak.
- Flare stack has been designed for proper size and combustion efficiency. New flares will have a continuous pilot and will be located at least 100 feet from the well and storage tanks and will be securely anchored.
- New tanks will be equipped with an automatic gauging system.
- An audio, visual and olfactory (AVO) inspection will be performed daily (at minimum) for active wells and facilities to confirm that all production equipment is operating properly and there are no leaks or releases except as allowed in Subsection D of 19.15.27.8 NMAC. Inactive, temporarily abandoned, or shut-in wells and facilities will be inspected weekly. Inspection records will be kept for a minimum of five years and will be available upon request by the division.

6. Measurement or Estimation of Vented and Flared Natural Gas

- Chevron estimates or measures the volume of natural gas that is vented, flared, or beneficially used during drilling, operations, regardless of the reason or authorization for such venting or flaring.
- Where technically practicable, Chevron will install meters on flares installed after May 25, 2021. Meters will conform to industry standards. Bypassing the meter will only occur for inspecting and servicing of the meter.

Operator Name: CHEVRON USA INCORPORATED**Well Name:** JAVELINA UNIT**Well Number:** 420H

Variance request: - Chevron respectfully request to vary from the Onshore Order 2 where it states: "(A full BOP Test) shall be performed: when initially installed and whenever any seal subject to test pressure is broken." We propose to break test if able to finish the next hole section within 21 days of the previous full BOP test. No BOP components nor any break will ever surpass 21 days between testing. A break test will consist of a 250 psi low / 5,000 psi high for 10 min each test against the connection that was broken when skidding the rig. Upon the first nipple up of the pad a full BOP test will be performed. A full BOP test will be completed prior to drilling the production liner hole sections, unless the BOP connection was not broken prior to drilling that hole section (example: drilling straight from production into production liner hole section). A break test will only be performed on operations where BLM documentation states a 5M or less BOP can be utilized. Break Tests will not be performed on Production hole sections. - Chevron requests a variance to use a FMC Technologies UH-S Multibowl wellhead, which will be run through the rig floor on surface casing. BOPE will be nipped up and tested after cementing surface casing. Subsequent tests will be performed as needed, not to exceed 30 days. The field report from FMC Technologies and BOP test information will be provided in a subsequent report at the end of the well. Please see the attached wellhead schematic. An installation manual has been placed on file with the BLM office and remains unchanged from previous submittal. All tests performed by third party. - Chevron also requests a variance to use a CoFlex hose with a metal protective covering that will be utilized between the BOP and Choke manifold. Please refer to the attached testing and specification documents.

Testing Procedure: Stack will be tested as specified in the attached testing requirements, upon NU and not to exceed 30 days. Test BOP from 250 psi to 5000 psi in Ram and 250 psi to 3500 psi in annular. BOP/BOPE will be tested by an independent service company to 250 psi low and a minimum of the high pressure indicated above. Batch drilling of the surface, intermediate, and production will take place. A full BOP test will be performed each hole section unless approval from the BLM is received otherwise. Flex choke hose will be used for all wells on the pad (see attached specs). BOP test will be conducted by a third party.

Choke Diagram Attachment:

D2.1a_BLM_5M_Choke_Manifold_Diagram_20210823122058.pdf

D2.2a_BLM_Choke_Hose_Test_Specs_and_Pressure_Test_Continental_20210823122144.pdf

BOP Diagram Attachment:

D2.1b_NM_Slim_Hole_Wellhead_6650_psi_UH_S_20210823122152.pdf

D2.3a_BLM_5M_Annular_10M_Rams_Stackup_and_Test_Plan_20210823122216.pdf

D2.2b_Break_Testing_and_WOC_500_psi_SND_Pad_417_20210916085231.pdf

Section 3 - Casing

Casing ID	String Type	Hole Size	Csg Size	Condition	Standard	Tapered String	Top Set MD	Bottom Set MD	Top Set TVD	Bottom Set TVD	Top Set MSL	Bottom Set MSL	Calculated casing length MD	Grade	Weight	Joint Type	Collapse SF	Burst SF	Joint SF Type	Joint SF	Body SF Type	Body SF
1	SURFACE	16	13.375	NEW	API	N	0	977	0	977	3544	2567	977	J-55	54.4	ST&C	2.13	1.43	DRY	4.07	DRY	1.53
2	INTERMEDIATE	12.25	9.625	NEW	API	N	0	4544	0	4494	3544	-950	4544	L-80	40	BUTT	1.24	1.64	DRY	2.78	DRY	1.99
3	PRODUCTION	8.75	7.0	NEW	API	N	0	9478	0	9577	3544	-6033	9478	P-110	29	OTHER - BLUE	1.63	1.15	DRY	2.39	DRY	1.18

Operator Name: CHEVRON USA INCORPORATED**Well Name:** JAVELINA UNIT**Well Number:** 420H

Casing ID	String Type	Hole Size	Csg Size	Condition	Standard	Tapered String	Top Set MD	Bottom Set MD	Top Set TVD	Bottom Set TVD	Top Set MSL	Bottom Set MSL	Calculated casing length MD	Grade	Weight	Joint Type	Collapse SF	Burst SF	Joint SF Type	Joint SF	Body SF Type	Body SF
4	PRODUCTI ON	6.12 5	5.0	NEW	API	N	9278	10078	9278	9518	-5734	-5974	800	P- 110	18	OTHER - W513	1.39	1.1	DRY	1.32	DRY	1.16
5	PRODUCTI ON	6.12 5	4.5	NEW	API	N	10078	21511	9518	10212	-5974	-6668	11433	P- 110	11.6	OTHER - W521	1.39	1.1	DRY	1.32	DRY	1.16

Casing Attachments**Casing ID:** 1 **String** SURFACE**Inspection Document:****Spec Document:****Tapered String Spec:****Casing Design Assumptions and Worksheet(s):**

D3_13.375_54.5ppf_J55_STC_20210823123505.pdf

Casing ID: 2 **String** INTERMEDIATE**Inspection Document:****Spec Document:****Tapered String Spec:****Casing Design Assumptions and Worksheet(s):**

9.625_40.0lb_L80IC_BTC_20210916085344.pdf

Operator Name: CHEVRON USA INCORPORATED**Well Name:** JAVELINA UNIT**Well Number:** 420H**Casing Attachments****Casing ID:** 3 **String** PRODUCTION**Inspection Document:****Spec Document:****Tapered String Spec:****Casing Design Assumptions and Worksheet(s):**

7_29ppf_TN110SS_TSH_Blue_20210916085420.pdf

Casing ID: 4 **String** PRODUCTION**Inspection Document:****Spec Document:****Tapered String Spec:****Casing Design Assumptions and Worksheet(s):**

5_18ppf_P110_Flush_W513_20210916085521.pdf

Casing ID: 5 **String** PRODUCTION**Inspection Document:****Spec Document:****Tapered String Spec:****Casing Design Assumptions and Worksheet(s):**

4.5_11.6ppf_P110_TSH_W521_20210916085646.pdf

Section 4 - Cement

Operator Name: CHEVRON USA INCORPORATED**Well Name:** JAVELINA UNIT**Well Number:** 420H

String Type	Lead/Tail	Stage Tool Depth	Top MD	Bottom MD	Quantity(sx)	Yield	Density	Cu Ft	Excess%	Cement type	Additives
SURFACE	Lead		0	977	0	0	0	0	0	C	NONE
SURFACE	Tail		0	977	457	1.34	14.8	612	100	C	EXTENDER, ANTIFOAM, RETARDER
INTERMEDIATE	Lead		0	3544	1110	2	13.2	2220	100	C	Extender, Antifoam, Retarder
INTERMEDIATE	Tail		3544	4544	336	1.4	13.2	470	50	CLASS C	Extender, Antifoam, Retarder
PRODUCTION	Lead		4044	8578	511	2	13.2	1022	50	CLASS C	Extender, Antifoam, Retarder, Viscosifier
PRODUCTION	Tail		8579	9578	134	1.4	14.8	188	25	C	Extender, Antifoam, Retarder, Viscosifier
PRODUCTION	Lead		9278	2151 1	783	1.84	13.2	1440	25	Class C	Extender, Antifoam, Retarder, Viscosifier

Section 5 - Circulating Medium

Mud System Type: Closed**Will an air or gas system be Used?** NO**Description of the equipment for the circulating system in accordance with Onshore Order #2:****Diagram of the equipment for the circulating system in accordance with Onshore Order #2:**

Describe what will be on location to control well or mitigate other conditions: A closed system will be used consisting of above ground steel tanks. All wastes accumulated during drilling operations will be contained in a portable trash cage and removed from location and deposited in an approved sanitary landfill. Sanitary wastes will be contained in a chemical porta-toilet and then hauled to an approved sanitary landfill. All fluids and cuttings will be disposed of in accordance with New Mexico Oil Conservation Division rules and regulations. And transporting of E&P waste will follow EPA regulations and accompanying manifests.

Describe the mud monitoring system utilized: A mud test shall be performed every 24 hours after muddling up to determine, as applicable: density, viscosity, gel strength, filtration, and pH. Visual mud monitoring equipment shall be in place to detect volume changes indicating loss or gain of circulating fluid volume. When abnormal pressures are anticipated a PVT, stroke counter, flow sensor will be used to detect volume changes indicating loss or gain of circulating fluid volume in compliance with Onshore Order #2. A weighting agent and lost circulating material (LCM) will be onsite to mitigate pressure or lost circulation as hole conditions dictate.

Circulating Medium Table

Operator Name: CHEVRON USA INCORPORATED**Well Name:** JAVELINA UNIT**Well Number:** 420H

Top Depth	Bottom Depth	Mud Type	Min Weight (lbs/gal)	Max Weight (lbs/gal)	Density (lbs/cu ft)	Gel Strength (lbs/100 sqft)	PH	Viscosity (CP)	Salinity (ppm)	Filtration (cc)	Additional Characteristics
9578	2151 1	OIL-BASED MUD	8.7	10.5							Viscosity 50-70 Filtrate 5-10
4544	9578	OTHER : WBM/SALT- SATURATED	8.7	10.6							Viscosity: 26-36 Filtrate: 15-25
0	977	SPUD MUD	8.3	8.9							Viscosity: 26-36 Filtrate: 15-25
977	4544	SALT SATURATED	8.3	10.6							Viscosity: 26-36 Filtrate: 15-25 10# weight will be used through salt zone

Section 6 - Test, Logging, Coring

List of production tests including testing procedures, equipment and safety measures:

Drill stem tests are not planned

The logging program will be as follows:

Type: Mudlogs Logs: 2 man mudlog Interval: Surf csg shoe through Prod hole TD Timing: While drilling or circulating

Type: LWD Logs: MWD gamma Interval: Int. and Prod. Hole Timing: While drilling

List of open and cased hole logs run in the well:

GAMMA RAY LOG, MUD LOG/GEOLOGIC LITHOLOGY LOG, MUD LOG/GEOLOGICAL LITHOLOGY LOG, DIRECTIONAL SURVEY,

Coring operation description for the well:

Conventional whole core samples are not planned; direction survey will be run - will send log(s) when run.

Section 7 - Pressure

Anticipated Bottom Hole Pressure: 5098

Anticipated Surface Pressure: 2851

Anticipated Bottom Hole Temperature(F): 150

Anticipated abnormal pressures, temperatures, or potential geologic hazards? NO

Describe:

Contingency Plans geohazards description:

Contingency Plans geohazards

Hydrogen Sulfide drilling operations plan required? YES

Operator Name: CHEVRON USA INCORPORATED**Well Name:** JAVELINA UNIT**Well Number:** 420H**Hydrogen sulfide drilling operations**

D8.1_H2S_Contingency_Plan_20210823132430.pdf

Section 8 - Other Information**Proposed horizontal/directional/multi-lateral plan submission:**

DefPlan100ft_JavelinaUnit420H_R0_20210916120055.pdf

Other proposed operations facets description:

Chevron formally requests the variances below:

- Authorization to use the spudder rig to spud the well and set surface casing. The drilling rig will move in less than 90 days to continue drilling operations. Rig layouts attached.

- Authorization to batch drill all 4 sections. Surface, Intermediate, Production, and production (liner) sections.

***Drilling plan attached contains a contingency cement program.

Other proposed operations facets attachment:

D8.2_Rig_layout_20210823132532.pdf

Operational_Best_Management_Practices_V2_20210916120237.pdf

Javelina_Unit_Pad_417_Gas_Management_Plan___NMOCD__1__20210916120237.pdf

Javelina_Unit_420H_20210916120258.pdf

CUSA_Spudder_Rig_Data_20210916120314.pdf

Other Variance attachment:



Javelina Unit 420H R0 mdv 26Jul21 Proposal Geodetic Report

(Def Plan)

Report Date: July 27, 2021 - 03:34 PM
Client: Chevron
Field: NM, Eddy County (NAD 27 EZ)
Structure / Slot: Chevron Javelina Unit Pad 417 / Javelina Unit 420H
Well: Javelina Unit 420H
Borehole: Javelina Unit 420H
UWI / API#: Unknown / Unknown
Survey Name: Javelina Unit 420H R0 mdv 26Jul21
Survey Date: July 27, 2021
Tort / AHD / DDI / ERD Ratio: 100.674 ° / 11113.378 ft / 6.361 / 1.088
Coordinate Reference System: NAD27 New Mexico State Plane, Eastern Zone, US Feet
Location Lat / Long: N 32° 13' 23.04987", W 103° 44' 56.50109"
Location Grid N/E Y/X: N 445363.000 ftUS, E 680693.000 ftUS
CRS Grid Convergence Angle: 0.3116 °
Grid Scale Factor: 0.99994649
Version / Patch: 2.10.825.0

Survey / DLS Computation: Minimum Curvature / Lubinski
Vertical Section Azimuth: 359.760 ° (Grid North)
Vertical Section Origin: 0.000 ft, 0.000 ft
TVD Reference Datum: Unknown
TVD Reference Elevation: 3544.000 ft above MSL
Seabed / Ground Elevation: 3544.000 ft above MSL
Magnetic Declination: 6.518 °
Total Gravity Field Strength: 998.4305mgn (9.80665 Based)
Gravity Model: GARM
Total Magnetic Field Strength: 47687.391 nT
Magnetic Dip Angle: 59.861 °
Declination Date: July 27, 2021
Magnetic Declination Model: HDGM 2021
North Reference: Grid North
Grid Convergence Used: -0.8644 °
Total Corr Mag North->Grid North: 7.3824 °
Local Coord Referenced To: Well Head

Comments	MD (ft)	Incl (°)	Azim Grid (°)	TVD (ft)	VSEC (ft)	NS (ft)	EW (ft)	DLS (°/100ft)	Northing (ftUS)	Easting (ftUS)	Latitude (N/S ° ' ")		Longitude (E/W ° ' ")	
Surface	0.00	0.00	0.00	0.00	0.00	0.00	0.00	N/A	445363.00	680693.00	N	32 13 23.05	W	103 44 56.50
	100.00	0.00	275.00	100.00	0.00	0.00	0.00	0.00	445363.00	680693.00	N	32 13 23.05	W	103 44 56.50
	200.00	0.00	275.00	200.00	0.00	0.00	0.00	0.00	445363.00	680693.00	N	32 13 23.05	W	103 44 56.50
	300.00	0.00	275.00	300.00	0.00	0.00	0.00	0.00	445363.00	680693.00	N	32 13 23.05	W	103 44 56.50
	400.00	0.00	275.00	400.00	0.00	0.00	0.00	0.00	445363.00	680693.00	N	32 13 23.05	W	103 44 56.50
	500.00	0.00	275.00	500.00	0.00	0.00	0.00	0.00	445363.00	680693.00	N	32 13 23.05	W	103 44 56.50
	600.00	0.00	275.00	600.00	0.00	0.00	0.00	0.00	445363.00	680693.00	N	32 13 23.05	W	103 44 56.50
Rustler (RSLR)	700.00	0.00	275.00	700.00	0.00	0.00	0.00	0.00	445363.00	680693.00	N	32 13 23.05	W	103 44 56.50
	716.00	0.00	275.00	716.00	0.00	0.00	0.00	0.00	445363.00	680693.00	N	32 13 23.05	W	103 44 56.50
	800.00	0.00	275.00	800.00	0.00	0.00	0.00	0.00	445363.00	680693.00	N	32 13 23.05	W	103 44 56.50
	900.00	0.00	275.00	900.00	0.00	0.00	0.00	0.00	445363.00	680693.00	N	32 13 23.05	W	103 44 56.50
Build 1.5°/100ft Saldo (SLDO)	1000.00	0.00	275.00	1000.00	0.00	0.00	0.00	0.00	445363.00	680693.00	N	32 13 23.05	W	103 44 56.50
	1100.00	0.00	275.00	1100.00	0.00	0.00	0.00	0.00	445363.00	680693.00	N	32 13 23.05	W	103 44 56.50
	1135.00	0.53	275.00	1135.00	0.01	0.01	-0.16	1.50	445363.01	680692.84	N	32 13 23.05	W	103 44 56.50
	1200.00	1.50	275.00	1199.99	0.12	0.11	-1.30	1.50	445363.11	680691.70	N	32 13 23.05	W	103 44 56.52
Hold	1300.00	3.00	275.00	1299.91	0.48	0.46	-5.21	1.50	445363.46	680687.79	N	32 13 23.05	W	103 44 56.56
	1400.00	4.50	275.00	1399.69	1.07	1.03	-11.73	1.50	445364.03	680681.27	N	32 13 23.06	W	103 44 56.64
	1467.00	5.50	275.00	1466.43	1.61	1.53	-17.55	1.50	445364.53	680675.45	N	32 13 23.07	W	103 44 56.71
	1500.00	5.50	275.00	1499.28	1.90	1.81	-20.70	0.00	445364.81	680672.30	N	32 13 23.07	W	103 44 56.74
Drop 0.75°/100ft	1506.03	5.50	275.00	1505.28	1.95	1.86	-21.28	0.00	445364.86	680671.72	N	32 13 23.07	W	103 44 56.75
	1600.00	4.80	275.00	1598.88	2.72	2.60	-29.69	0.75	445365.60	680663.31	N	32 13 23.08	W	103 44 56.85
	1700.00	4.05	275.00	1698.58	3.42	3.27	-37.37	0.75	445366.27	680655.63	N	32 13 23.08	W	103 44 56.94
	1800.00	3.30	275.00	1798.37	4.01	3.83	-43.76	0.75	445366.83	680649.24	N	32 13 23.09	W	103 44 57.01
	1900.00	2.55	275.00	1898.24	4.48	4.27	-48.84	0.75	445367.27	680644.16	N	32 13 23.09	W	103 44 57.07
	2000.00	1.80	275.00	1998.17	4.82	4.60	-52.62	0.75	445367.60	680640.38	N	32 13 23.10	W	103 44 57.11
	2100.00	1.05	275.00	2098.13	5.05	4.82	-55.10	0.75	445367.82	680637.90	N	32 13 23.10	W	103 44 57.14
	2200.00	0.30	275.00	2198.13	5.16	4.92	-56.28	0.75	445367.92	680636.73	N	32 13 23.10	W	103 44 57.16
	2240.02	0.00	275.00	2238.15	5.17	4.93	-56.38	0.75	445367.93	680636.62	N	32 13 23.10	W	103 44 57.16
	2300.00	0.00	275.00	2298.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W	103 44 57.16
Hold	2400.00	0.00	275.00	2398.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W	103 44 57.16
	2500.00	0.00	275.00	2498.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W	103 44 57.16
	2600.00	0.00	275.00	2598.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W	103 44 57.16
	2700.00	0.00	275.00	2698.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W	103 44 57.16
	2800.00	0.00	275.00	2798.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W	103 44 57.16
	2900.00	0.00	275.00	2898.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W	103 44 57.16
	2996.87	0.00	275.00	2995.00	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W	103 44 57.16
	3000.00	0.00	275.00	2998.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W	103 44 57.16
	3100.00	0.00	275.00	3098.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W	103 44 57.16
	3200.00	0.00	275.00	3198.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W	103 44 57.16
Castile (CSTL)	3300.00	0.00	275.00	3298.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W	103 44 57.16
	3400.00	0.00	275.00	3398.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W	103 44 57.16
	3500.00	0.00	275.00	3498.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W	103 44 57.16
	3600.00	0.00	275.00	3598.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W	103 44 57.16
	3700.00	0.00	275.00	3698.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W	103 44 57.16
	3800.00	0.00	275.00	3798.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W	103 44 57.16
	3900.00	0.00	275.00	3898.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W	103 44 57.16
	4000.00	0.00	275.00	3998.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W	103 44 57.16
	4100.00	0.00	275.00	4098.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W	103 44 57.16
	4200.00	0.00	275.00	4198.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W	103 44 57.16
Lamar (LMAR)	4300.00	0.00	275.00	4298.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W	103 44 57.16
	4400.00	0.00	275.00	4398.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W	103 44 57.16
	4500.00	0.00	275.00	4498.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W	103 44 57.16
	4553.87	0.00	275.00	4552.00	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W	103 44 57.16
	4591.87	0.00	275.00	4590.00	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W	103 44 57.16
	4600.00	0.00	275.00	4598.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W	103 44 57.16
	4700.00	0.00	275.00	4698.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W	103 44 57.16
	4800.00	0.00	275.00	4798.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W	103 44 57.16
	4900.00	0.00	275.00	4898.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W	103 44 57.16
	5000.00	0.00	275.00	4998.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W	103 44 57.16
Bell Canyon (BLCN)	5100.00	0.00	275.00	5098.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W	103 44 57.16
	5200.00	0.00	275.00	5198.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W	103 44 57.16
	5300.00	0.00	275.00	5298.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W	103 44 57.16
	5400.00	0.00	275.00	5398.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W	103 44 57.16
	5487.87	0.00	275.00	5486.00	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W	103 44 57.16
	5500.00	0.00	275.00	5498.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W	103 44 57.16
	5600.00	0.00	275.00	5598.13	5.1									

Comments	MD (ft)	Incl (°)	Azim Grid (°)	TVD (ft)	VSEC (ft)	NS (ft)	EW (ft)	DLS (°/100ft)	Northing (ftUS)	Easting (ftUS)		Latitude (N/S ° ' ")	Longitude (E/W ° ' ")	
Brushy Canyon (BCN)	6700.00	0.00	275.00	6698.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W 103 44 57.16	
	6768.87	0.00	275.00	6767.00	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W 103 44 57.16	
	6800.00	0.00	275.00	6798.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W 103 44 57.16	
	6900.00	0.00	275.00	6898.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W 103 44 57.16	
	7000.00	0.00	275.00	6998.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W 103 44 57.16	
	7100.00	0.00	275.00	7098.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W 103 44 57.16	
	7200.00	0.00	275.00	7198.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W 103 44 57.16	
	7300.00	0.00	275.00	7298.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W 103 44 57.16	
	7400.00	0.00	275.00	7398.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W 103 44 57.16	
	7500.00	0.00	275.00	7498.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W 103 44 57.16	
	7600.00	0.00	275.00	7598.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W 103 44 57.16	
	7700.00	0.00	275.00	7698.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W 103 44 57.16	
	7800.00	0.00	275.00	7798.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W 103 44 57.16	
	7900.00	0.00	275.00	7898.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W 103 44 57.16	
	8000.00	0.00	275.00	7998.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W 103 44 57.16	
	8100.00	0.00	275.00	8098.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W 103 44 57.16	
	8200.00	0.00	275.00	8198.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W 103 44 57.16	
	8300.00	0.00	275.00	8298.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W 103 44 57.16	
	8400.00	0.00	275.00	8398.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W 103 44 57.16	
Bone Spring (BSGL)	8492.87	0.00	275.00	8491.00	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W 103 44 57.16	
Upper Avalon (AVN)	8500.00	0.00	275.00	8498.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W 103 44 57.16	
	8561.87	0.00	275.00	8560.00	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W 103 44 57.16	
	8600.00	0.00	275.00	8598.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W 103 44 57.16	
	8700.00	0.00	275.00	8698.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W 103 44 57.16	
	8800.00	0.00	275.00	8798.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W 103 44 57.16	
	8900.00	0.00	275.00	8898.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W 103 44 57.16	
	9000.00	0.00	275.00	8998.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W 103 44 57.16	
	Lower Avalon (AVL)	9042.87	0.00	275.00	9041.00	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W 103 44 57.16
	9100.00	0.00	275.00	9098.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W 103 44 57.16	
	9200.00	0.00	275.00	9198.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W 103 44 57.16	
	9300.00	0.00	275.00	9298.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W 103 44 57.16	
	9400.00	0.00	275.00	9398.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W 103 44 57.16	
	9500.00	0.00	275.00	9498.13	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W 103 44 57.16	
	First Bone Spring Upper (FBS)	9561.87	0.00	275.00	9560.00	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W 103 44 57.16
	Build 10°/100ft	9578.92	0.00	275.00	9577.05	5.17	4.93	-56.38	0.00	445367.93	680636.62	N	32 13 23.10	W 103 44 57.16
		9600.00	2.11	359.76	9598.12	5.55	5.32	-56.38	10.00	445368.32	680636.62	N	32 13 23.11	W 103 44 57.16
		9700.00	12.11	359.76	9697.23	17.91	17.68	-56.43	10.00	445380.67	680636.57	N	32 13 23.23	W 103 44 57.16
		9800.00	22.11	359.76	9792.68	47.29	47.05	-56.56	10.00	445410.05	680636.44	N	32 13 23.52	W 103 44 57.16
	First Bone Spring Lower (FBL)	9844.26	26.53	359.76	9833.00	65.51	65.28	-56.64	10.00	445428.27	680636.37	N	32 13 23.70	W 103 44 57.16
Landing Point	9900.00	32.11	359.76	9881.58	92.80	92.56	-56.75	10.00	445455.56	680636.25	N	32 13 23.97	W 103 44 57.16	
	10000.00	42.11	359.76	9961.23	153.05	152.82	-57.01	10.00	445515.81	680636.00	N	32 13 24.57	W 103 44 57.15	
	10100.00	52.11	359.76	10029.21	226.23	225.99	-57.32	10.00	445588.97	680635.68	N	32 13 25.29	W 103 44 57.15	
	10200.00	62.11	359.76	10083.45	310.09	309.85	-57.67	10.00	445672.83	680635.33	N	32 13 26.12	W 103 44 57.15	
	10300.00	72.11	359.76	10122.30	402.09	401.85	-58.06	10.00	445764.83	680634.94	N	32 13 27.03	W 103 44 57.15	
	10400.00	82.11	359.76	10144.58	499.45	499.21	-58.48	10.00	445862.18	680634.53	N	32 13 27.99	W 103 44 57.15	
	10475.53	89.66	359.76	10150.00	574.73	574.49	-58.80	10.00	445937.46	680634.21	N	32 13 28.74	W 103 44 57.15	
	10500.00	89.66	359.76	10150.14	599.20	598.96	-58.90	0.00	445961.93	680634.10	N	32 13 28.98	W 103 44 57.15	
	FTP Cross	10525.14	89.66	359.76	10150.29	624.34	624.10	-59.01	0.00	445987.07	680634.00	N	32 13 29.23	W 103 44 57.15
	10600.00	89.66	359.76	10150.74	699.20	698.96	-59.33	0.00	446061.92	680633.68	N	32 13 29.97	W 103 44 57.15	
	10700.00	89.66	359.76	10151.33	799.20	798.95	-59.75	0.00	446161.91	680633.25	N	32 13 30.96	W 103 44 57.15	
	10800.00	89.66	359.76	10151.92	899.20	898.95	-60.17	0.00	446261.90	680632.83	N	32 13 31.95	W 103 44 57.14	
	10900.00	89.66	359.76	10152.51	999.19	998.95	-60.60	0.00	446361.89	680632.4				

Comments	MD (ft)	Incl (°)	Azim Grid (°)	TVD (ft)	VSEC (ft)	NS (ft)	EW (ft)	DLS (°/100ft)	Northing (ftUS)	Easting (ftUS)	Latitude (N/S ° ' ")	Longitude (E/W ° ' ")
Hold	15707.69	89.66	359.76	10181.00	5806.79	5806.51	-81.01	2.00	451169.18	680612.00	N 32 14 20.51	W 103 44 57.08
	15800.00	89.66	359.76	10181.55	5899.11	5898.82	-81.39	0.00	451261.49	680611.61	N 32 14 21.42	W 103 44 57.08
	15900.00	89.66	359.76	10182.14	5999.11	5998.82	-81.81	0.00	451361.48	680611.19	N 32 14 22.41	W 103 44 57.07
	16000.00	89.66	359.76	10182.73	6099.10	6098.81	-82.23	0.00	451461.47	680610.78	N 32 14 23.40	W 103 44 57.07
	16100.00	89.66	359.76	10183.32	6199.10	6198.81	-82.65	0.00	451561.47	680610.36	N 32 14 24.39	W 103 44 57.07
	16200.00	89.66	359.76	10183.91	6299.10	6298.81	-83.07	0.00	451661.46	680609.94	N 32 14 25.38	W 103 44 57.07
	16300.00	89.66	359.76	10184.49	6399.10	6398.81	-83.48	0.00	451761.45	680609.52	N 32 14 26.37	W 103 44 57.07
	16400.00	89.66	359.76	10185.08	6499.10	6498.80	-83.90	0.00	451861.44	680609.10	N 32 14 27.36	W 103 44 57.07
	16500.00	89.66	359.76	10185.67	6599.10	6598.80	-84.32	0.00	451961.43	680608.68	N 32 14 28.35	W 103 44 57.06
	16600.00	89.66	359.76	10186.26	6699.09	6698.80	-84.74	0.00	452061.43	680608.26	N 32 14 29.34	W 103 44 57.06
	16700.00	89.66	359.76	10186.85	6799.09	6798.79	-85.16	0.00	452161.42	680607.85	N 32 14 30.33	W 103 44 57.06
	16800.00	89.66	359.76	10187.44	6899.09	6898.79	-85.58	0.00	452261.41	680607.43	N 32 14 31.32	W 103 44 57.06
	16900.00	89.66	359.76	10188.03	6999.09	6998.79	-86.00	0.00	452361.40	680607.01	N 32 14 32.31	W 103 44 57.06
	17000.00	89.66	359.76	10188.62	7099.09	7098.79	-86.42	0.00	452461.39	680606.59	N 32 14 33.30	W 103 44 57.06
	17100.00	89.66	359.76	10189.21	7199.08	7198.78	-86.83	0.00	452561.38	680606.17	N 32 14 34.29	W 103 44 57.06
	17200.00	89.66	359.76	10189.80	7299.08	7298.78	-87.25	0.00	452661.38	680605.75	N 32 14 35.28	W 103 44 57.05
	17300.00	89.66	359.76	10190.39	7399.08	7398.78	-87.67	0.00	452761.37	680605.33	N 32 14 36.27	W 103 44 57.05
	17400.00	89.66	359.76	10190.98	7499.08	7498.78	-88.09	0.00	452861.36	680604.91	N 32 14 37.26	W 103 44 57.05
	17500.00	89.66	359.76	10191.57	7599.08	7598.77	-88.51	0.00	452961.35	680604.50	N 32 14 38.25	W 103 44 57.05
	17600.00	89.66	359.76	10192.16	7699.08	7698.77	-88.93	0.00	453061.34	680604.08	N 32 14 39.24	W 103 44 57.05
	17700.00	89.66	359.76	10192.75	7799.07	7798.77	-89.35	0.00	453161.34	680603.66	N 32 14 40.23	W 103 44 57.05
	17800.00	89.66	359.76	10193.34	7899.07	7898.77	-89.76	0.00	453261.33	680603.24	N 32 14 41.22	W 103 44 57.05
	17900.00	89.66	359.76	10193.93	7999.07	7998.76	-90.18	0.00	453361.32	680602.82	N 32 14 42.20	W 103 44 57.04
	18000.00	89.66	359.76	10194.52	8099.07	8098.76	-90.60	0.00	453461.31	680602.40	N 32 14 43.19	W 103 44 57.04
	18100.00	89.66	359.76	10195.11	8199.07	8198.76	-91.02	0.00	453561.30	680601.98	N 32 14 44.18	W 103 44 57.04
	18200.00	89.66	359.76	10195.70	8299.07	8298.76	-91.44	0.00	453661.29	680601.57	N 32 14 45.17	W 103 44 57.04
	18300.00	89.66	359.76	10196.29	8399.06	8398.75	-91.86	0.00	453761.29	680601.15	N 32 14 46.16	W 103 44 57.04
	18400.00	89.66	359.76	10196.88	8499.06	8498.75	-92.28	0.00	453861.28	680600.73	N 32 14 47.15	W 103 44 57.04
	18500.00	89.66	359.76	10197.47	8599.06	8598.75	-92.69	0.00	453961.27	680600.31	N 32 14 48.14	W 103 44 57.04
	18600.00	89.66	359.76	10198.06	8699.06	8698.74	-93.11	0.00	454061.26	680599.89	N 32 14 49.13	W 103 44 57.03
	18700.00	89.66	359.76	10198.65	8799.06	8798.74	-93.53	0.00	454161.25	680599.47	N 32 14 50.12	W 103 44 57.03
	18800.00	89.66	359.76	10199.24	8899.06	8898.74	-93.95	0.00	454261.25	680599.05	N 32 14 51.11	W 103 44 57.03
	18900.00	89.66	359.76	10199.83	8999.05	8998.74	-94.37	0.00	454361.24	680598.64	N 32 14 52.10	W 103 44 57.03
	19000.00	89.66	359.76	10200.42	9099.05	9098.73	-94.79	0.00	454461.23	680598.22	N 32 14 53.09	W 103 44 57.03
	19100.00	89.66	359.76	10201.01	9199.05	9198.73	-95.21	0.00	454561.22	680597.80	N 32 14 54.08	W 103 44 57.03
	19200.00	89.66	359.76	10201.60	9299.05	9298.73	-95.63	0.00	454661.21	680597.38	N 32 14 55.07	W 103 44 57.03
	19300.00	89.66	359.76	10202.19	9399.05	9398.73	-96.04	0.00	454761.20	680596.96	N 32 14 56.06	W 103 44 57.02
	19400.00	89.66	359.76	10202.78	9499.04	9498.72	-96.46	0.00	454861.20	680596.54	N 32 14 57.05	W 103 44 57.02
	19500.00	89.66	359.76	10203.37	9599.04	9598.72	-96.88	0.00	454961.19	680596.12	N 32 14 58.04	W 103 44 57.02
	19600.00	89.66	359.76	10203.96	9699.04	9698.72	-97.30	0.00	455061.18	680595.71	N 32 14 59.03	W 103 44 57.02
	19700.00	89.66	359.76	10204.55	9799.04	9798.72	-97.72	0.00	455161.17	680595.29	N 32 15 0.02	W 103 44 57.02
	19800.00	89.66	359.76	10205.14	9899.04	9898.71	-98.14	0.00	455261.16	680594.87	N 32 15 1.01	W 103 44 57.02
	19900.00	89.66	359.76	10205.73	9999.04	9998.71	-98.56	0.00	455361.16	680594.45	N 32 15 2.00	W 103 44 57.02
	20000.00	89.66	359.76	10206.32	10099.03	10098.71	-98.97	0.00	455461.15	680594.03	N 32 15 2.98	W 103 44 57.01
	20100.00	89.66	359.76	10206.91	10199.03	10198.71	-99.39	0.00	455561.14	680593.61	N 32 15 3.97	W 103 44 57.01
	20200.00	89.66	359.76	10207.50	10299.03	10298.70	-99.81	0.00	455661.13	680593.19	N 32 15 4.96	W 103 44 57.01
	20300.00	89.66	359.76	10208.09	10399.03	10398.70	-100.23	0.00	455761.12	680592.78	N 32 15 5.95	W 103 44 57.01
	20400.00	89.66	359.76	10208.68	10499.03	10498.70	-100.65	0.00	455861.11	680592.36	N 32 15 6.94	W 103 44 57.01
	20500.00	89.66	359.76	10209.27	10599.03	10598.70	-101.07	0.00	455961.11	680591.94	N 32 15 7.93	W 103 44 57.01
	20600.00	89.66	359.76	10209.86	10699.02	10698.69	-101.49	0.00	456061.10	680591.52	N 32 15 8.92	W 103 44 57.01
	20700.00	89.66	359.76	10210.45	10799.02	10798.69	-101.90	0.00	456161.09	680591.10	N 32 15 9.91	W 103 44 57.00
	20800.00	89.66	359.76	10211.04	10899.02	10898.69	-102.32	0.00	456261.08	680590.68	N 32 15 10.90	W 103 44 57.00
LTP Cross	20888.01	89.66	359.76	10211.56	10987.03	10986.70	-102.69	0.00	456349.09	680590.31	N 32 15 11.77	W 103 44 57.00
	20900.00	89.66	359.76	10211.63	10999.02	10998.68	-102.74	0.00	456361.07	680590.26	N 32 15 11.89	W 103 44 57.00
Javelina Unit 420H BHL	20962.93	89.66	359.76	10212.00	11061.95	11061.61	-103.01	0.00	456424.00	680590.00	N 32 15 12.51	W 103 44 57.00

Survey Type: Def Plan

Survey Error Model: ISCWSA Rev 3 *** 3-D 97.071% Confidence 3.0000 sigma
Survey Program:

Description	Part	MD From (ft)	MD To (ft)	EOU Freq (ft)	Hole Size (in)	Casing Diameter (in)	Expected Max Inclination (deg)	Survey Tool Type	Borehole / Survey
	1	0.000	20962.931	1/100.000	30.000	30.000		B001Mb_MWD+HRGM	Javelina Unit 420H / Javelina Unit 420H R0 mdv 26Jul21

PECOS DISTRICT DRILLING CONDITIONS OF APPROVAL

OPERATOR'S NAME:	CHEVRON USA INCORPORATED
LEASE NO.:	NMNM070805
LOCATION:	Section 10, T.24 S., R.31 E., NMP
COUNTY:	Eddy County, New Mexico

WELL NAME & NO.:	JAVELINA UNIT 420H
SURFACE HOLE FOOTAGE:	524'/N & 2365'/W
BOTTOM HOLE FOOTAGE:	25'/N & 2310'/W

COA

H2S	<input type="radio"/> Yes	<input checked="" type="radio"/> No	
Potash	<input type="radio"/> None	<input type="radio"/> Secretary	<input checked="" type="radio"/> R-111-P
Cave/Karst Potential	<input checked="" type="radio"/> Low	<input type="radio"/> Medium	<input type="radio"/> High
Cave/Karst Potential	<input type="radio"/> Critical		
Variance	<input type="radio"/> None	<input checked="" type="radio"/> Flex Hose	<input type="radio"/> Other
Wellhead	<input type="radio"/> Conventional	<input type="radio"/> Multibowl	<input checked="" type="radio"/> Both
Other	<input type="checkbox"/> 4 String Area	<input type="checkbox"/> Capitan Reef	<input type="checkbox"/> WIPP
Other	<input type="checkbox"/> Fluid Filled	<input checked="" type="checkbox"/> Cement Squeeze	<input type="checkbox"/> Pilot Hole
Special Requirements	<input type="checkbox"/> Water Disposal	<input type="checkbox"/> COM	<input checked="" type="checkbox"/> Unit

A. HYDROGEN SULFIDE

Hydrogen Sulfide (H2S) monitors shall be installed prior to drilling out the surface shoe. If H2S is detected in concentrations greater than 100 ppm, the Hydrogen Sulfide area shall meet Onshore Order 6 requirements, which includes equipment and personnel/public protection items. If Hydrogen Sulfide is encountered, provide measured values and formations to the BLM.

B. CASING

Casing Design:

1. The **13-3/8** inch surface casing shall be set at approximately **977** feet (a minimum of **70 feet (Eddy County)** into the Rustler Anhydrite and above the salt) and cemented to the surface.
 - a. If cement does not circulate to the surface, the appropriate BLM office shall be notified and a temperature survey utilizing an electronic type temperature survey with surface log readout will be used or a cement bond log shall be run to verify the top of the cement. Temperature survey will be run a minimum of

- six hours after pumping cement and ideally between 8-10 hours after completing the cement job.
- b. Wait on cement (WOC) time for a primary cement job will be a minimum of **24 hours in the Potash Area** or 500 pounds compressive strength, whichever is greater. (This is to include the lead cement)
 - c. Wait on cement (WOC) time for a remedial job will be a minimum of 4 hours after bringing cement to surface or 500 pounds compressive strength, whichever is greater.
 - d. If cement falls back, remedial cementing will be done prior to drilling out that string.
2. The **9-5/8** inch intermediate casing shall be set at approximately **4494** feet. The minimum required fill of cement behind the **9-5/8** inch intermediate casing is:

Option 1 (Single Stage):

- Cement to surface. If cement does not circulate see B.1.a, c-d above.
Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry due to cave/karst or potash.

Option 2:

Operator has proposed a DV tool, the depth may be adjusted as long as the cement is changed proportionally. The DV tool may be cancelled if cement circulates to surface on the first stage.

- a. First stage to DV tool: Cement to circulate. If cement does not circulate off the DV tool, contact the appropriate BLM office before proceeding with second stage cement job.
 - b. Second stage above DV tool:
 - Cement to surface. If cement does not circulate, contact the appropriate BLM office.
Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry due to cave/karst or potash.
- ❖ In **R111 Potash Areas** if cement does not circulate to surface on the first two salt protection casing strings, the cement on the 3rd casing string must come to surface.

Operator has proposed to pump down 13-3/8" X 9-5/8" annulus. Operator must run a CBL from TD of the 9-5/8" casing to surface. Submit results to BLM.

3. The minimum required fill of cement behind the **7** inch production casing is:

Option 1 (Single Stage):

- Cement to surface. If cement does not circulate, contact the appropriate BLM office.

Option 2:

Operator has proposed a DV tool, the depth may be adjusted as long as the cement is changed proportionally. The DV tool may be cancelled if cement circulates to surface on the first stage.

- First stage to DV tool: Cement to circulate. If cement does not circulate off the DV tool, contact the appropriate BLM office before proceeding with second stage cement job.
- Second stage above DV tool:
 - Cement to surface. If cement does not circulate, contact the appropriate BLM office.

Operator has proposed to pump down 9-5/8" X 7" annulus. Operator must run a CBL from TD of the 7" casing to surface. Submit results to BLM.

- The minimum required fill of cement behind the 5 X 4-1/2 inch production liner is:
 - Cement should tie-back **100 feet** into the previous casing. Operator shall provide method of verification.

C. PRESSURE CONTROL

- Variance approved to use flex line from BOP to choke manifold. Manufacturer's specification to be readily available. No external damage to flex line. Flex line to be installed as straight as possible (no hard bends).'
-

Option 1:

- Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **3000 (3M)** psi.
- Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the intermediate casing shoe shall be **5000 (5M)** psi.

Option 2:

1. Operator has proposed a multi-bowl wellhead assembly. This assembly will only be tested when installed on the surface casing. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **5000 (5M)** psi.
 - a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
 - b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
 - c. Manufacturer representative shall install the test plug for the initial BOP test.
 - d. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
 - e. Whenever any seal subject to test pressure is broken, all the tests in OOGO2.III.A.2.i must be followed.

D. SPECIAL REQUIREMENT (S)**Unit Wells**

The well sign for a unit well shall include the unit number in addition to the surface and bottom hole lease numbers. This also applies to participating area numbers. If a participating area has not been established, the operator can use the general unit designation, but will replace the unit number with the participating area number when the sign is replaced.

Commercial Well Determination

A commercial well determination shall be submitted after production has been established for at least six months.

BOPE Break Testing Variance (Note: For 5M BOPE or less)

- BOPE Break Testing is ONLY permitted for 5M BOPE or less.
- BOPE Break Testing is NOT permitted to drilling the production hole section.
- While in transfer between wells, the BOPE shall be secured by the hydraulic carrier or cradle.
- Any well control event while drilling require notification to the BLM Petroleum Engineer prior to the commencement of any BOPE Break Testing operations.
- A full BOPE test is required prior to drilling the first deep intermediate hole section. If any subsequent hole interval is deeper than the first, a full BOPE test will be required.
- The BLM is to be contacted (**575-361-2822 Eddy County**) 4 hours prior to BOPE tests.
- As a minimum, a full BOPE test shall be performed at 21-day intervals.

- In the event any repairs or replacement of the BOPE is required, the BOPE shall test as per Onshore Oil and Gas Order No. 2.

ONSHORE ORDER NO. 1
Chevron
SD 24 13 FED P415 13H
Lea County, NM

CONFIDENTIAL -- TIGHT HOLE
DRILLING PLAN
PAGE: 4

6. MUD PROGRAM

From	To	TVD Top	TVD Btm	Type	Weight	F. Vis	Filtrate
0'	850'	0'	850'	Spud Mud	8.3-8.7	32 - 34	NC - NC
850'	4600'	850'	4,587'	Brine	9.4-10.6	28 - 30	25-30
4600'	10,820'	4,587'	10,808'	Cut Brine	8.8-10.0	70 - 75	25-30
10,820'	22,257'	10,808'	11,786'	Oil Based Mud	12.0-14.8	70 - 75	25-30

A closed system will be utilized consisting of above ground steel tanks. All wastes accumulated during drilling operations will be contained in a portable trash cage and removed from location and deposited in an approved sanitary landfill. Sanitary wastes will be contained in a chemical porta-toilet and then hauled to an approved sanitary landfill.

All fluids and cuttings will be disposed of in accordance with New Mexico Oil Conservation Division rules and regulations.

A mud test shall be performed every 24 hours after mudding up to determine, as applicable: density, viscosity, gel strength, filtration, and pH.

Visual mud monitoring equipment shall be in place to detect volume changes indicating loss or gain of circulating fluid volume. When abnormal pressures are anticipated -- a pit volume totalizer (PVT), stroke counter, and flow sensor will be used to detect volume changes indicating loss or gain of circulating fluid volume.

A weighting agent and lost circulating material (LCM) will be onsite to mitigate pressure or lost circulation as hole conditions dictate.

7. TESTING, LOGGING, AND CORING

The anticipated type and amount of testing, logging, and coring are as follows:

- Drill stem tests are not planned.
- The logging program will be as follows:

TYPE	Logs	Interval	Timing	Vendor
Mudlogs	2 man mudlog	Int Csg to TD	Drillout of Int Csg	TBD
LWD	MWD Gamma	Int. and Prod. Hole	While Drilling	TBD

- Conventional whole core samples are not planned.
- A Directional Survey will be run.

8. ABNORMAL PRESSURES AND HYDROGEN SULFIDE

- No abnormal pressures or temperatures are expected. Estimated BHP at intermediate TD is: 5750 psi
No abnormal pressures or temperatures are expected. Estimated BHP at production TD is: 8650 psi
- Hydrogen sulfide gas is not anticipated. An H2S Contingency plan is attached with this APD in the event that H2S is encountered



U.S. Department of the Interior
BUREAU OF LAND MANAGEMENT

Drilling Plan Data Report

06/07/2022

APD ID: 10400080133

Submission Date: 09/16/2021

Highlighted data
reflects the most
recent changes

Operator Name: CHEVRON USA INCORPORATED

Well Name: JAVELINA UNIT

Well Number: 420H

Well Type: OIL WELL

Well Work Type: Drill

[Show Final Text](#)

Section 1 - Geologic Formations

Formation ID	Formation Name	Elevation	True Vertical	Measured Depth	Lithologies	Mineral Resources	Producing Formatio
6950174	RUSTLER	3572	741	741	DOLOMITE	NONE	N
6992890	TOP SALT	2620	952	952	MUDSTONE, SALT, SANDSTONE	NONE	N
6992891	SALADO	2528	1044	1044	HALITE, SALT	NONE	N
6950191	CASTILE	606	2966	3016	ANHYDRITE	NONE	N
6950193	LAMAR	-922	4494	4544	LIMESTONE	NONE	N
6950175	BELL CANYON	-959	4531	4581	SANDSTONE	NONE	N
6950177	CHERRY CANYON	-1839	5411	5711	SANDSTONE	NONE	N
6950178	BRUSHY CANYON	-3095	6667	6867	SANDSTONE	NONE	N
6950179	BONE SPRING	-4787	8359	8559	LIMESTONE	NATURAL GAS, OIL	N
6950189	UPPER AVALON SHALE	-4854	8426	8676	LIMESTONE, SHALE	NATURAL GAS, OIL	N
6950181	BONE SPRING 1ST	-5836	9408	9658	SANDSTONE	NATURAL GAS, OIL	N
6950182	BONE SPRING 2ND	-6438	10010	21511	SANDSTONE	NATURAL GAS, OIL	Y

Section 2 - Blowout Prevention

Pressure Rating (PSI): 5M

Rating Depth: 10604

Equipment: Chevron will have a minimum of a 5,000 psi rig stack for drill out below surface casing. The stack will be tested as specified in the attached testing requirements. Batch drilling of the surface, intermediate, and production will take place. A full BOP test will be performed per hole section, unless approval from BLM is received otherwise. Flex choke hose will be used for all wells on the pad (see attached specs and variance). BOP test will be conducted by a third party.

Requesting Variance? YES

BLOWOUT PREVENTER SCHEMATIC

Operation:

Intermediate & Production Drilling Operations

Minimum System operation pressure

5,000 psi

BOP Stack

Part	Size	Pressure Rating	Description
A	13-5/8"	N/A	Rotating Head/Bell nipple
B	13-5/8"	5,000	Annular
C	13-5/8"	10,000	Blind Ram
D	13-5/8"	10,000	Pipe Ram
E	13-5/8"	10,000	Mud Cross
F	13-5/8"	10,000	Pipe Ram

Kill Line


Part	Size	Pressure Rating	Description
G	2"	10,000	Inside Kill Line Valve (gate valve)
H	2"	10,000	Outside Kill Line Valve (gate valve)
I	2"	10,000	Kill Line Check valve

Choke line

Part	Size	Pressure Rating	Description
J	3"	10,000	HCR (gate valve)
K	3"	10,000	Manual HCR (gate valve)

Wellhead

Part	Size	Pressure Rating	Description
L	13-5/8"	5,000	FMC Multibowl wellhead

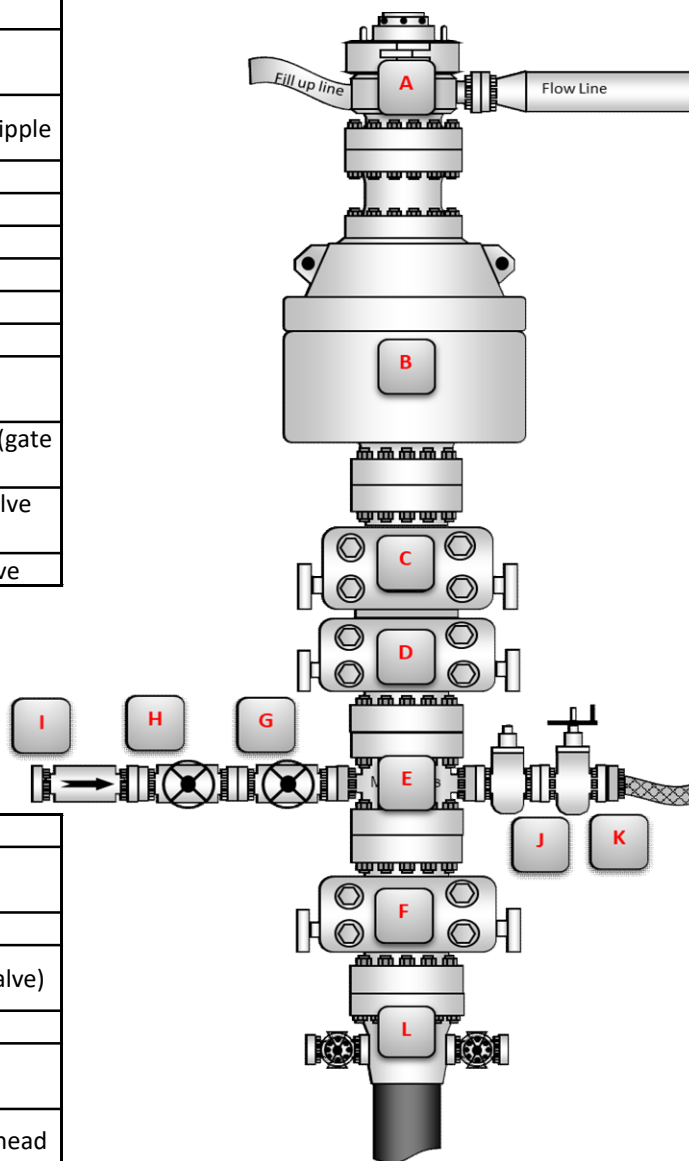

BOP Installation Checklist: The following items must be verified and checked off prior to pressure testing BOP equipment

The installed BOP equipment meets at least the minimum requirements (rating, type, size, configuration) as shown on this schematic. Components may be substituted for equivalent equipment rated to higher pressures. Additional components may be put into place as long as they meet or exceed the minimum pressure rating of the system.

All valves on the kill line and choke line will be full opening and will allow straight flow through.

Manual (hand wheels) or automatic locking devices will be installed on all ram preventers. Hand wheels will also be install on all manual valves on the choke and kill line.

A valve will be installed in the closing line as close as possible to the annular preventer to act as a locking device. This valve will remain open unless accumulator is inoperative.

Upper kelly cock valve with handle will be available on rig floor along with saved valve and subs to fit all drill string connections in use.

District I

1625 N. French Dr., Hobbs, NM 88240
Phone:(575) 393-6161 Fax:(575) 393-0720

District II

811 S. First St., Artesia, NM 88210
Phone:(575) 748-1283 Fax:(575) 748-9720

District III

1000 Rio Brazos Rd., Aztec, NM 87410
Phone:(505) 334-6178 Fax:(505) 334-6170

District IV

1220 S. St Francis Dr., Santa Fe, NM 87505
Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 114497

CONDITIONS

Operator: CHEVRON U S A INC 6301 Deauville Blvd Midland, TX 79706	OGRID:
	4323
	Action Number: 114497
	Action Type: [C-101] BLM - Federal/Indian Land Lease (Form 3160-3)

CONDITIONS

Created By	Condition	Condition Date
kpickford	Will require administrative order for non-standard spacing unit	8/15/2022
kpickford	The pool assignment for this well has been corrected on the C-102. Subsequent sundries must reflect the correct pool.	8/15/2022
kpickford	Notify OCD 24 hours prior to casing & cement	8/15/2022
kpickford	Will require a File As Drilled C-102 and a Directional Survey with the C-104	8/15/2022
kpickford	Once the well is spud, to prevent ground water contamination through whole or partial conduits from the surface, the operator shall drill without interruption through the fresh water zone or zones and shall immediately set in cement the water protection string	8/15/2022
kpickford	Cement is required to circulate on both surface and intermediate1 strings of casing	8/15/2022
kpickford	Oil base muds are not to be used until fresh water zones are cased and cemented providing isolation from the oil or diesel. This includes synthetic oils. Oil based mud, drilling fluids and solids must be contained in a steel closed loop system	8/15/2022
