

Form 3160-3
(June 2015)FORM APPROVED
OMB No. 1004-0137
Expires: January 31, 2018

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
APPLICATION FOR PERMIT TO DRILL OR REENTER

1a. Type of work: <input type="checkbox"/> DRILL <input type="checkbox"/> REENTER 1b. Type of Well: <input type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input type="checkbox"/> Other 1c. Type of Completion: <input type="checkbox"/> Hydraulic Fracturing <input type="checkbox"/> Single Zone <input type="checkbox"/> Multiple Zone		5. Lease Serial No. 6. If Indian, Allottee or Tribe Name 7. If Unit or CA Agreement, Name and No. 8. Lease Name and Well No.
2. Name of Operator		9. API Well No. 30-043-21484
3a. Address	3b. Phone No. (include area code)	10. Field and Pool, or Exploratory
4. Location of Well (Report location clearly and in accordance with any State requirements. *) At surface At proposed prod. zone		11. Sec., T. R. M. or Blk. and Survey or Area
14. Distance in miles and direction from nearest town or post office*		12. County or Parish
13. State		
15. Distance from proposed* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any)	16. No of acres in lease	17. Spacing Unit dedicated to this well
18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft.	19. Proposed Depth	20. BLM/BIA Bond No. in file
21. Elevations (Show whether DF, KDB, RT, GL, etc.)	22. Approximate date work will start*	23. Estimated duration
24. Attachments		

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, and the Hydraulic Fracturing rule per 43 CFR 3162.3-3 (as applicable)

- | | |
|---|---|
| 1. Well plat certified by a registered surveyor.
2. A Drilling Plan.
3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office). | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).
5. Operator certification.
6. Such other site specific information and/or plans as may be requested by the BLM. |
|---|---|

25. Signature	Name (Printed/Typed)	Date
Title		
Approved by (Signature)	Name (Printed/Typed)	Date
Title	Office	

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
 Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Continued on page 2)

*(Instructions on page 2)



DISTRICT I1625 N. French Dr., Hobbs, N.M. 88240
Phone: (575) 393-6161 Fax: (575) 393-9720**DISTRICT II**511 S. First St., Artesia, N.M. 88210
Phone: (575) 748-1263 Fax: (575) 748-9720**DISTRICT III**1000 Rio Brazos Rd., Artesia, N.M. 87410
Phone: (505) 334-6176 Fax: (505) 334-6170**DISTRICT IV**1220 S. St. Francis Dr., Santa Fe, NM 87505
Phone: (505) 476-8460 Fax: (505) 476-8462State of New Mexico
Energy, Minerals & Natural Resources DepartmentForm C-102
Revised August 1, 2011Submit one copy to appropriate
District OfficeOIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, NM 87505☐ AMENDED REPORT

WELL LOCATION AND ACREAGE DEDICATION PLAT

¹ API Number 30-043-21484	² Pool Code 98174	³ Pool Name NORTH ALAMITO UNIT MANCOS OIL POOL
⁴ Property Code 325267	⁵ Property Name NORTH ALAMITO UNIT	⁶ Well Number 534H
⁷ GRID No. 371838	⁸ Operator Name DJR OPERATING, LLC	⁹ Elevation 6875'

¹⁰ Surface Location

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
L	29	23N	7W		1668'	SOUTH	797'	WEST	SANDOVAL

¹¹ Bottom Hole Location If Different From Surface

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
M	19	23N	7W		229'	SOUTH	755'	WEST	SANDOVAL


¹² Dedicated Acres
SEC 29: SW/SW & NW/SW (80 AC.); SEC 30:
NE/SE, NW/SE, SE/NE, SW/NE, NW/NE, SE/NW,
NE/NW & NW/NW (320.70 AC.); SEC 19: SE/SW
& SW/SW (80.74 AC.) = 481.44 ACRES

¹³ Joint or Infill¹⁴ Consolidation Code¹⁵ Order No.

R-14081 R-14081A

NO ALLOWABLE WILL BE ASSIGNED TO THIS COMPLETION UNTIL ALL INTERESTS HAVE BEEN CONSOLIDATED
OR A NON-STANDARD UNIT HAS BEEN APPROVED BY THE DIVISION

16

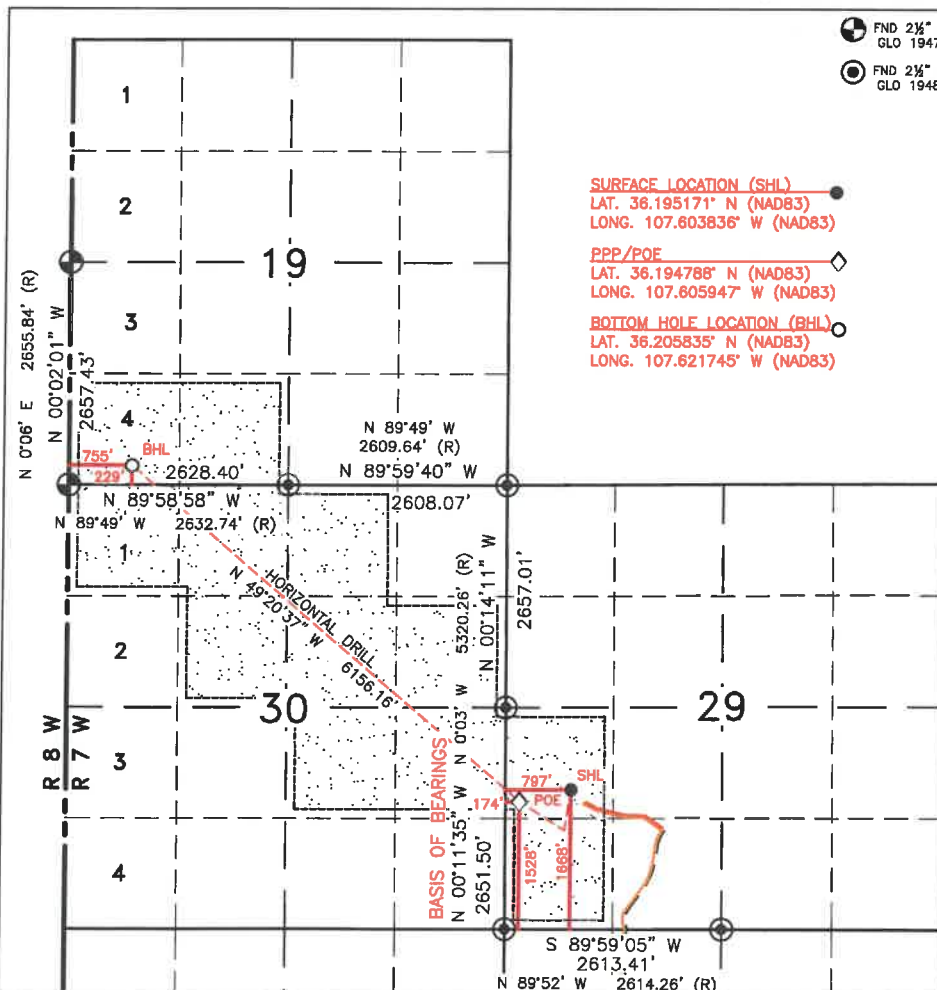

FND 2 1/2" BC
GLO 1947
FND 2 1/2" BC
GLO 1948

17 OPERATOR CERTIFICATION

I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief, and that this organization either owns a working interest or unleased mineral interest in the land including the proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of such a mineral or working interest, or to a voluntary pooling agreement or a compulsory pooling order heretofore entered by the division.

Shaw-Marie Ford 02/02/2021
Signature Date

Shaw-Marie Ford
Printed Name

sford@djrlc.com
E-mail Address

SURVEYOR CERTIFICATION

I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief.

JULY 10, 2020

Date of Survey
Signature and Seal of Professional Surveyor:



Certificate Number 11393

State of New Mexico
Energy, Minerals and Natural Resources Department

Submit Electronically
Via E-permitting

Oil Conservation Division
1220 South St. Francis Dr.
Santa Fe, NM 87505

NATURAL GAS MANAGEMENT PLAN

This Natural Gas Management Plan must be submitted with each Application for Permit to Drill (APD) for a new or recompleted well.

Section 1 – Plan Description

Effective May 25, 2021

I. Operator: DJR Operating, LLC **OGRID:** 371838 **Date:** 09 / 20 / 2022

II. Type: ☒ Original ☐ Amendment due to ☐ 19.15.27.9.D(6)(a) NMAC ☐ 19.15.27.9.D(6)(b) NMAC ☐ Other.

If Other, please describe: _____

III. Well(s): Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	API	ULSTR	Footages	Anticipated Oil BBL/D	Anticipated Gas MCF/D	Anticipated Produced Water BBL/D
N. Alamito Unit 236H	TBD	L-29-23N-07W	1676 FSL x 815 FWL	315	470	110
N. Alamito Unit 534H	TBD	L-29-23N-07W	1668 FSL x 797 FWL	340	510	120

IV. Central Delivery Point Name: Chaco Processing Plant [See 19.15.27.9(D)(1) NMAC]

V. Anticipated Schedule: Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	API	Spud Date	TD Reached Date	Completion Commencement Date	Initial Flow Back Date	First Production Date
N. Alamito Unit 236H	TBD	12/06/2022	12/17/2022	01/12/2023	02/03/2023	02/04/2023
N. Alamito Unit 534H	TBD	12/07/2022	12/18/2022	01/12/2023	02/03/2023	02/04/2023

VI. Separation Equipment: ☒ Attach a complete description of how Operator will size separation equipment to optimize gas capture.

VII. Operational Practices: ☒ Attach a complete description of the actions Operator will take to comply with the requirements of Subsection A through F of 19.15.27.8 NMAC.

VIII. Best Management Practices: ☒ Attach a complete description of Operator's best management practices to minimize venting during active and planned maintenance.

Section 2 – Enhanced Plan**EFFECTIVE APRIL 1, 2022**

Beginning April 1, 2022, an operator that is not in compliance with its statewide natural gas capture requirement for the applicable reporting area must complete this section.

☒ Operator certifies that it is not required to complete this section because Operator is in compliance with its statewide natural gas capture requirement for the applicable reporting area.

IX. Anticipated Natural Gas Production:

Well	API	Anticipated Average Natural Gas Rate MCF/D	Anticipated Volume of Natural Gas for the First Year MCF

X. Natural Gas Gathering System (NGGS):

Operator	System	ULSTR of Tie-in	Anticipated Gathering Start Date	Available Maximum Daily Capacity of System Segment Tie-in

XI. Map. ☐ Attach an accurate and legible map depicting the location of the well(s), the anticipated pipeline route(s) connecting the production operations to the existing or planned interconnect of the natural gas gathering system(s), and the maximum daily capacity of the segment or portion of the natural gas gathering system(s) to which the well(s) will be connected.

XII. Line Capacity. The natural gas gathering system ☐ will ☐ will not have capacity to gather 100% of the anticipated natural gas production volume from the well prior to the date of first production.

XIII. Line Pressure. Operator ☐ does ☐ does not anticipate that its existing well(s) connected to the same segment, or portion, of the natural gas gathering system(s) described above will continue to meet anticipated increases in line pressure caused by the new well(s).

☐ Attach Operator's plan to manage production in response to the increased line pressure.

XIV. Confidentiality: ☐ Operator asserts confidentiality pursuant to Section 71-2-8 NMSA 1978 for the information provided in Section 2 as provided in Paragraph (2) of Subsection D of 19.15.27.9 NMAC and attaches a full description of the specific information for which confidentiality is asserted and the basis for such assertion.

Section 3 - Certifications

Effective May 25, 2021

Operator certifies that, after reasonable inquiry and based on the available information at the time of submittal:

☒ Operator will be able to connect the well(s) to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system; or

☐ Operator will not be able to connect to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system.

If Operator checks this box, Operator will select one of the following:

Well Shut-In. ☐ Operator will shut-in and not produce the well until it submits the certification required by Paragraph (4) of Subsection D of 19.15.27.9 NMAC; or

Venting and Flaring Plan. ☐ Operator has attached a venting and flaring plan that evaluates and selects one or more of the potential alternative beneficial uses for the natural gas until a natural gas gathering system is available, including:

- (a) power generation on lease;
- (b) power generation for grid;
- (c) compression on lease;
- (d) liquids removal on lease;
- (e) reinjection for underground storage;
- (f) reinjection for temporary storage;
- (g) reinjection for enhanced oil recovery;
- (h) fuel cell production; and
- (i) other alternative beneficial uses approved by the division.

Section 4 - Notices

1. If, at any time after Operator submits this Natural Gas Management Plan and before the well is spud:

(a) Operator becomes aware that the natural gas gathering system it planned to connect the well(s) to has become unavailable or will not have capacity to transport one hundred percent of the production from the well(s), no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised venting and flaring plan containing the information specified in Paragraph (5) of Subsection D of 19.15.27.9 NMAC; or

(b) Operator becomes aware that it has, cumulatively for the year, become out of compliance with its baseline natural gas capture rate or natural gas capture requirement, no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised Natural Gas Management Plan for each well it plans to spud during the next 90 days containing the information specified in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and shall file an update for each Natural Gas Management Plan until Operator is back in compliance with its baseline natural gas capture rate or natural gas capture requirement.

2. OCD may deny or conditionally approve an APD if Operator does not make a certification, fails to submit an adequate venting and flaring plan which includes alternative beneficial uses for the anticipated volume of natural gas produced, or if OCD determines that Operator will not have adequate natural gas takeaway capacity at the time a well will be spud.

I certify that, after reasonable inquiry, the statements in and attached to this Natural Gas Management Plan are true and correct to the best of my knowledge and acknowledge that a false statement may be subject to civil and criminal penalties under the Oil and Gas Act.

Signature: <i>Shaw-Marie Ford</i>
Printed Name: Shaw-Marie Ford
Title: Regulatory Specialist
E-mail Address: sford@djrlc.com
Date: 09/20/2022
Phone: 505-716-3297
OIL CONSERVATION DIVISION (Only applicable when submitted as a standalone form)
Approved By:
Title:
Approval Date:
Conditions of Approval:



DJR OPERATING, LLC.
OGRID NO: 371838
NATURAL GAS MANAGEMENT PLAN
North Alamito Unit 236H and 534H
NWSW L-29-23N-07W

SEPARATION EQUIPMENT

DJR Operating, LLC (DJR) has pulled representative pressurized samples from wells in the same producing formation. DJR has utilized these samples in process simulations to determine the amount of gas anticipated in each stage of the process and utilized this information with a safety factor to size the equipment listed below:

Separation equipment will be set as follows:

- Individual 3 phase separator will be set for the individual well.
- The separator will be sized based on the anticipated volume of the well and the pressure of the lines utilized for oil, gas, and water takeaway.
- The 3 phase production separator will be equipped with a 0.75 MMBtu/hr indirect fired heater.

Heater treaters will be set as follows:

- Individual heater treaters will be set for the individual well.
- The heater treaters are sized based on the anticipated combined volume of oil and produced water predicted to come from the initial 3 phase separator.
- Oil will be separated from the produced water and the oil/produced water will be sent to its respective tanks.
- The combined oil and natural gas stream is routed to the Vapor Recovery Tower.

Vapor Recovery Equipment will be set as follows:

- The Vapor Recovery Tower has been sized, based on the anticipated volume of gas from the heater treater and oil and water tanks.
- The Vapor Recovery Unit has been sized, based on the anticipated volume of gas from the heater treater and oil and water tanks. The Vapor Recovery Unit is utilized to push the recovered gas into the sales pipeline.

Production storage tanks will be set as follows:

- The oil and produced water tanks utilize a closed vent capture system to ensure all breathing, working, and flashing losses are routed to the Vapor Recovery Tower and Vapor Recovery Unit.
- Each of the production storage tanks will be equipped with a 0.5 MMBtu/hr indirect heater.



DJR OPERATING, LLC.
OGRID NO: 371838
NATURAL GAS MANAGEMENT PLAN
North Alamito Unit 236H and 534H
NWSW L-29-23N-07W

VENTING and FLARING

DJR Operating, LLC (DJR) has a natural gas system available prior to startup of completion operations. DJR utilizes a Vapor Recovery Unit System and sells all natural gas except during periods of startup, shutdown, maintenance, or malfunction for the gas capturing equipment, including the vapor recovery tower, vapor recovery unit, storage tanks, and pipelines.

Currently, DJR utilizes the following from list A-I of Section 3 for its operations to minimize flaring:

- a) DJR utilizes natural gas-powered generators to power its leases where grid power isn't available.
- b) When electrical grid power is unavailable, natural gas generators will be used for major equipment onsite.
- c) DJR's in service compression will be natural gas powered.
- d) Should liquids removal, such as dehydration be required, units will be powered by natural gas.

DJR will only flare gas during the following times:

- Scheduled maintenance for gas capturing equipment including:
 - Vapor Recovery Tower
 - Vapor Recovery Unit
 - Storage tanks
 - Pipelines
 - Emergency flaring



DJR OPERATING, LLC.
OGRID NO: 371838
NATURAL GAS MANAGEMENT PLAN
North Alamito Unit 236H and 534H
NWSW L-29-23N-07W

OPERATIONAL PRACTICES

19.15.27.8 A. Venting and Flaring of Natural Gas

DJR Operating, LLC (DJR) understands the requirements of NMAC 19.15.27.8 which states that the venting and flaring of natural gas during drilling, completion or production that constitutes waste as defined in 19.15.2 are prohibited.

19.15.27.8 B. Venting and flaring during drilling operations

- DJR shall capture or combust natural gas if technically feasible during drilling operations using best industry practices.
- A flare stack with a 100% capacity for expected volumes will be set on location of the facility at least 100 feet from the nearest surface hole location, well heads, and storage tanks.
- In the event of an emergency, DJR will vent natural gas in order to avoid substantial impact. DJR shall report the vented or flared gas to the NMOCD.

19.15.27.8 E. Venting and flaring during completion or recompletion operations

During Completion Operations, DJR utilizes the following:

- DJR facilities are built and ready from day 1 of Flowback.
- Individual well test separators will be set to properly separate gas and liquids. Temporary test separator will be utilized initially to process volumes. In addition, separators will be tied into flowback tanks which will be tied into the gas processing equipment for sales down a pipeline. See Separation Equipment for details.
- Should the facility not yet be capable of processing gas, or the gas does not meet quality standards, then storage tanks will be set that are tied into gas busters or temporary flare to manage natural gas. This flare would meet the following requirements:
 - 1) An appropriately sized flare stack with an automatic igniter.
 - 2) DJR analyzes the natural gas samples twice per week.
 - 3) DJR routes the natural gas into a gathering pipeline as soon as the pipeline specifications are met.
 - 4) DJR provides the NMOCD with pipeline specifications and natural gas data.



19.15.27.8 D. Venting and flaring during production operations

During Production Operations DJR will not vent or flare natural gas except under the following circumstances:

1. During an emergency or malfunction
2. To unload or clean-up liquid holdup in a well to atmospheric pressure, provided:
 - a. DJR does not vent after the well achieves a stabilized rate and pressure.
 - b. DJR will remain present on-site during liquids unloading by manual purging and take all reasonable actions to achieve a stabilized rate and pressure at the earliest practical time.
 - c. DJR will optimize the system to minimize natural gas venting on any well equipped with a plunger lift or auto control system.
 - d. Best Management Practices will be used during downhole well maintenance.
3. During the first year of production from an exploratory well provided:
 - a. DJR receives approval from the NMOCD.
 - b. DJR remains in compliance with the NM gas capture requirements.
 - c. DJR submits an updated C-129 form to the NMOCD.
4. During the following activities unless prohibited:
 - a. Gauging or sampling a storage tank or low-pressure production vessel.
 - b. Loading out liquids from a storage tank.
 - c. Repair and maintenance.
 - d. Normal operation of gas activated pneumatic controller or pump.
 - e. Normal operation of a storage tank but not including venting from a thief hatch.
 - f. Normal operation of dehydration units.
 - g. Normal operations of compressors, compressor engines, turbines, valves, flanges, and connectors.
 - h. During a bradenhead, packer leakage test, or production test lasting less than 24-hours.
 - i. When natural gas does not meet the gathering pipeline specifications.
 - j. Commissioning of pipelines, equipment, or facilities only for as long as necessary to purge introduced impurities.

19.15.27.8 E. Performance standards

1. DJR has utilized process simulations with a safety factor to design all separation and storage equipment. The equipment is routed to a Vapor Recovery System and utilizes a flare as back up for periods of startup, shutdown, maintenance, or malfunction of the VRU System.
2. DJR will install a flare that designed to handle the full volume of vapors from the facility in case of the VRU failure and it is designed with an auto ignition system.
3. Flare stacks will appropriately sized and designed to ensure proper combustion efficiency.



- a. Flare stacks installed or replaced will be equipped with an automatic ignitor or continuous pilot.
 - b. Previously installed flare stacks will be retrofitted with an automatic ignitor, continuous pilot, or technology that alerts DJR of flare malfunction within 18 months after May 25, 2021.
 - c. Flare stacks replaced after May 25, 2021, will be equipped with an automatic ignitor or continuous pilot if located at a well or facility with average daily production of 60,000 cubic feet of natural gas or less.
 - d. Flare stacks will be located at least 100 feet from the well and storage tanks and securely anchored.
4. DJR will conduct an AVO inspection on all components for leaks and defects on a weekly basis.
 5. DJR will make and keep records of AVO inspections which will be available to the NMOCD for at least 5 years.
 6. DJR may use a remote or automated monitoring technology to detect leaks and releases in lieu of AVO inspections with prior NMOCD approval.
 7. Facilities will be designed to minimize waste.
 8. DJR will resolve emergencies as promptly as possible.

19.15.27.8 F. Measurement or estimation of vented and flared natural gas

1. DJR will have meters on both the low- and high-pressure sides of the flares and the volumes will be recorded in DJR's SCADA system.
2. DJR will install equipment to measure the volume of flared natural gas that has an average daily production of 60,000 cubic feet or greater of natural gas.
3. DJR's measuring equipment will conform to the industry standards.
4. The measurement system is designed such that it cannot be bypassed except for inspections and servicing meters.
5. DJR will estimate the volume of vented or flared natural gas using a methodology that can be independently verified if metering is not practicable due to low flow rate or pressure.
6. DJR will estimate the volume of flared and vented natural gas based on the results of an annual GOR test for wells that do not require measuring equipment reported on Form C-116.
7. DJR will install measuring equipment whenever the NMOCD determines that metering is necessary.



DJR OPERATING, LLC.
OGRID NO: 371838
NATURAL GAS MANAGEMENT PLAN
North Alamito Unit 236H and 534H
NWSW L-29-23N-07W

BEST MANAGEMENT PRACTICES

DJR Operating, LLC (DJR) utilizes the following Best Management Practices to minimize venting during active and planned maintenance.

DJR has a closed vent capture system to route emissions from the heater treater, tanks, and vapor recovery to the vapor recovery unit with an enclosed combustion device (ECD) for backup. The system is designed such that if the vapor recovery unit is taken out of service for any reason, the vapors will be routed to the ECD for combustion.

DJR will isolate and attempt to route all vapors to the vapor recovery unit or ECD prior to opening any lines for maintenance to minimize venting from the equipment.

DJR shall notify the NMOCD of venting or flaring that exceeds 50 MCF but less than 500 MCF in volume that either resulted from an emergency or malfunction, or an event lasting over eight hours or more cumulatively within any 24-hour period from a single event by filing a form C-129 no later than 15 days following the discovery or commencement of venting or flaring.

DJR shall notify the NMOCD verbally or by e-mail within 24-hours following discovery or commencement of venting or flaring that exceeds 500 MCF in volume or otherwise qualifies as a major release as defined in 19.15.29.7 NMAC from a single event and provide the information required in form C-129 to the NMOCD no later than 15 days that verifies, updates, or corrects the verbal or e-mail notification.

DJR will install measuring equipment to conform to industry standards such as American Petroleum Institute (API) Manual of Petroleum Measurement Standards (MPMS) Chapter 14.10 Measurement of Flow to Flares.

DJR's measuring equipment shall not be designed or equipped with a manifold that allows the diversion of natural gas around the metering element except for the sole purpose of inspecting and servicing the measurement equipment.

DJR shall report the volume of vented and flared natural gas for each well or facility at which venting or flaring occurred on a monthly basis.

Rev 0



DRILLING PLAN

North Alamito #534H

Sandoval County, New Mexico

Surface Location

797-ft FWL & 1668-ft FSL
 Sec 29 T23N R07W
 Graded Elevation 6875' MSL
 RKB Elevation 6889' (14' KB)

SHL Geographical Coordinates (NAD-83)

Latitude 36.1951710° N
 Longitude 107.6038360° W

Kick Off Point for Horizontal Build Curve

4449-ft MD
 4416-ft TVD

Local Coordinates (from SHL)

495-ft South
 94-ft West

Heel Location (Pay zone entry)

174-ft FWL & 1528-ft FSL
 Sec 29 T23N R07W

Heel Geographical Coordinates (NAD-83)

Latitude 36.1947882° N
 Longitude 107.60594650° W

Bottom Hole Location (TD)

755-ft FWL & 229-ft FSL
 Sec 19 T23N R07W

BHL Geographical Coordinates (NAD-83)

Latitude 36.2058354° N
 Longitude 107.6217450° W

Well objectives

This well is planned as a 6150-ft lateral in the Gallup C sand.

Bottom Hole temperature and pressure

The temperature in the Gallup C horizontal objective is 139°F. Bottom hole pressure in the Gallup C is forecast to be 1985 psi.

Formation Tops (Sd = Sand; Sh = Shale; Siltstone = Slt, Coal = C; W = water; O = oil; G = gas; NP = no penetration)

Name	MD (ft)	TVD (ft)	Lithology	Pore fluid	Expected Pore Pressure (ppg)	Planned Mud Weight (ppg)
Ojo Alamo	887	885	Sd	W	8.3	8.4 – 8.8
Kirtland	987	984	Sh	-	8.3	8.4 – 8.8
Fruitland	1173	1169	C	G	8.3	9.0 - 9.5
Pictured Cliffs	1469	1462	Sd	W	8.3	9.0 - 9.5
Lewis	1584	1576	Sh	-		9.0 - 9.5
Chacra	2293	2279	Sd	-	8.3	9.0 - 9.5
Menefee	3010	2990	Sd, C	G	8.3	9.0 - 9.5
Point Lookout	3865	3838	Sd	-	8.3	9.0 - 9.5
Mancos	4054	4025	Sh	-		9.0 - 9.5
Mancos Silt	4346	4314	Slt	O/G	6.6	9.0 - 9.5
Gallup A	4858	4803	Slt	O/G	6.6	9.0 - 9.5
Gallup B	4907	4843	Sd	O/G	6.6	8.8 - 9.0
Gallup C	5046	4942	Sd	O/G	6.6	8.8 - 9.0
Target	5487	5090	Sd	O/G	6.6	8.8 - 9.0

Casing Program

Casing OD	Hole Size	Weight (#/ft)	Grade	Coupling	MD Top	MD Bottom	TVD Top	TVD Bottom	Top of Cement
9-5/8"	12-1/4"	36	K-55	STC	surf	350	surf	350	surface
7"	8-3/4"	26	K-55	LTC	surf	5434	surf	5088	surface
4-1/2"	6-1/8"	11.6	P-110	BTC	5154	11643	5004	5120	5154

Note: all casing will be new

Rev 0



Casing Design Load Cases

		Casing String		
Description		9-5/8" Surface	7" Intermediate	4-1/2" Production Liner
Collapse	Full internal evacuation ¹	✓	✓	✓
	Cementing	✓	✓	✓
Burst	Pressure test	✓ ²	✓ ²	✓
	Gas kick		✓ ³	
	Fracture at shoe, 1/3 BHP at surface		✓ ⁴	
	Injection down casing			✓ ⁵
Axial	Dynamic load on casing coupling ⁶	✓	✓	✓
Axial	Overpull ⁷	✓	✓	✓

Note

- 1 Fluid level at shoe, air column to surface, pore pressure outside
- 2 Tested to 80% of minimum internal yield with freshwater inside, pore pressure outside
- 3 50 bbl kick at TD, 0.50 ppg intensity, 4" drill pipe, 9.0 ppg mud, fracture gradient at shoe
- 4 2060 psi BHP, 687 psi surface pressure, 12.5 ppg EMW shoe integrity
- 5 Surface stimulation pressure of 8000 psi on 8.3 ppg fluid column. Stimulation will be down frac string, so load does not apply to 7" intermediate casing.
- 6 Shock load from abrupt pipe deceleration, evaluated against coupling rating
- 7 Overpull values as follows: Surface casing 20,000 lbs, Intermediate & Production 100,000 lbs

Casing Design Factors

		Design Factors			
Casing string	Casing OD	Burst	Collapse	Axial	Triaxial
Surface	9-5/8"	1.25	13.38	8.16	1.56
Intermediate	7"	1.25	1.50	1.68	1.34
Production liner	4-1/2"	1.37	3.68	1.88	1.69

Cement Design

9-5/8" Surface Casing

	Lead
Name	Redi-Mix
Type	I-II
Planned top	Surface
Density (ppg)	14.50
Yield (cf/sx)	1.61
Mix water (gal/sx)	7.41
Volume (sx)	114
Volume (bbls)	33
Volume (cu. ft.)	185
Excess %	50

7" Intermediate Casing

	Lead	Tail
	BJ Services	BJ Services
Type	III	Poz/G
Planned top	Surface	3949-ft
Density (ppg)	12.30	13.50
Yield (cf/sx)	2.34	1.50
Mix water (gal/sx)	13.26	7.20
Volume (sx)	383	238
Volume (bbls)	160	63
Volume (cu.ft.)	897	355
Excess %	55	55



Rev 0

4-1/2" Production Liner

	BJ Services
Type	Poz/G
Planned top	5154-ft
Density (ppg)	13.3
Yield (cf/sx)	1.56
Mix water (gal/sx)	7.71
Volume (sx)	545
Volume (bbls)	152
Volume (cu.ft)	852
Excess %	40

Wellhead & Pressure Control

The well head will be an 11" 5M multi-bowl system. A 3M BOPE conforming to Onshore Order #2 will be installed on the surface casing. The BOP and accumulator will meet API 16D and 16E respectively.

A PVT mud monitoring system and a trip tank will be rigged up and operational for all hole intervals. An electronic geolograph will be employed to monitor and record drilling data (ROP, WOB, SPM, Pressure, RPM and torque).

Mud Program

Surface hole will be drilled with a fresh water, native mud system. In intermediate hole, a low weight 7% KCl LSND drilling fluid will be used, with KCl providing chemical stability for the young shales and clays present in the interval. In production hole a LSND system with polymer and lubricant additives is programmed. Sufficient drill water and mud additives will be on hand to maintain adequate pit volumes and maintain well control.

Hole Section	Fluid type	Interval (MD)	Density (ppg)	Funnel Viscosity	Yield Point	Fluid Loss (cc/30 min)
Surface	Fresh water spud mud	0 – 350	8.4 – 8.8	32 – 44	2 – 12	NC
Intermediate	7% KCl Low solids, non-dispersed	350 – 5434	9.0 – 9.5	38 – 45	8 – 14	<20
Production	Low solids, non-dispersed	5434 – 11643	8.8 – 9.2	34 – 38	6 – 8	6 – 8

Cores, tests and logs

Wellbore surveying: Drift (inclination only) surveys will be obtained in surface hole. MWD directional surveys will be taken in intermediate and production hole.

Logging while drilling: None in surface hole. MWD GR in intermediate and production hole.

Mud logging: a two-person mud logging unit with C1 – C4 gas analysis will be operational in intermediate and production hole.

Electric logging: No open hole electric logs are programmed. A cased hole GR/CCL will be run during completions for perforating depth control.

Cuttings and drilling fluids management

A closed loop, steel tank-based circulating system will be used. In addition to the rig solids control equipment, a dewatering centrifuge and chemical flocculation system will be operational to strip solids from the whole mud. All solids will be collected in 3-sided bins and will then be put into transports with a bucket loader. Drying agents will be used if necessary. The solids will be taken to a licensed commercial disposal facility. Whole mud will be dewatered back to drill water and used as make up for subsequent wells or hauled off for disposal. A diagram of the closed loop system is included.

Completion

It is envisioned that this well will be completed with a multi-stage sand frac, using the plug and perf technique. After drilling out the plugs, the current plan is to install a 2-7/8" plunger-assisted gas lift tubing string. The stimulation and completion plan will be sundried at a later date.



Company: DJR Operating
Project: North Alamito Unit
Site: L29 2307 Pad
Well: # 534H
Wellbore: Original Drilling
Design: APD

WELL DETAILS: # 534H

GL 6875' & RKB 14' @ 6889.00usft		Latitude	Longitude
+N/-S	+E/-W	Northing	Easting
0.00	0.00	1890419.68	2790806.48

DESIGN TARGET DETAILS

Time	TVD	+N/-S	+E/-W	Northing	Easting	Latitude	Longitude
534H Heel	5090.00	-135.34	-622.72	1890278.87	2790184.09	36.19478820	-107.60594650
534H Toe	5120.00	3882.56	-5283.48	1894289.73	2785513.83	36.20583540	-107.62174500




PROJECT DETAILS: North Alamito Unit

Geodetic System: US State Plane 1983
Datum: North American Datum 1983
Ellipsoid: GRS 1980
Zone: New Mexico Western Zone
System Datum: Mean Sea Level
Local North: True

Plan: APD (# 534H/Original Drilling)
Created By: Janie Collins Date: 11:37, July 16 2020

SECTION DETAILS

MD	Inc	Azi	TVD	+N/-S	+E/-W	Dleg	TFace	Vsect	Target
0.00	0.00	0.000	0.00	0.00	0.00	0.00	0.00	0.00	
400.00	0.00	0.000	400.00	0.00	0.00	0.00	0.00	0.00	
774.55	7.49	190.787	773.49	-24.02	-4.58	2.00	190.79	-10.54	
446.52	7.49	190.787	446.52	-135.34	-622.72	0.00	119.92	211.32	534H Heel
548.52	89.72	310.792	509.00	-135.34	-622.72	0.00	119.92	419.26	534H Toe
11643.31	89.72	310.792	5120.00	3882.56	-5283.48	0.00	0.00	6556.63	

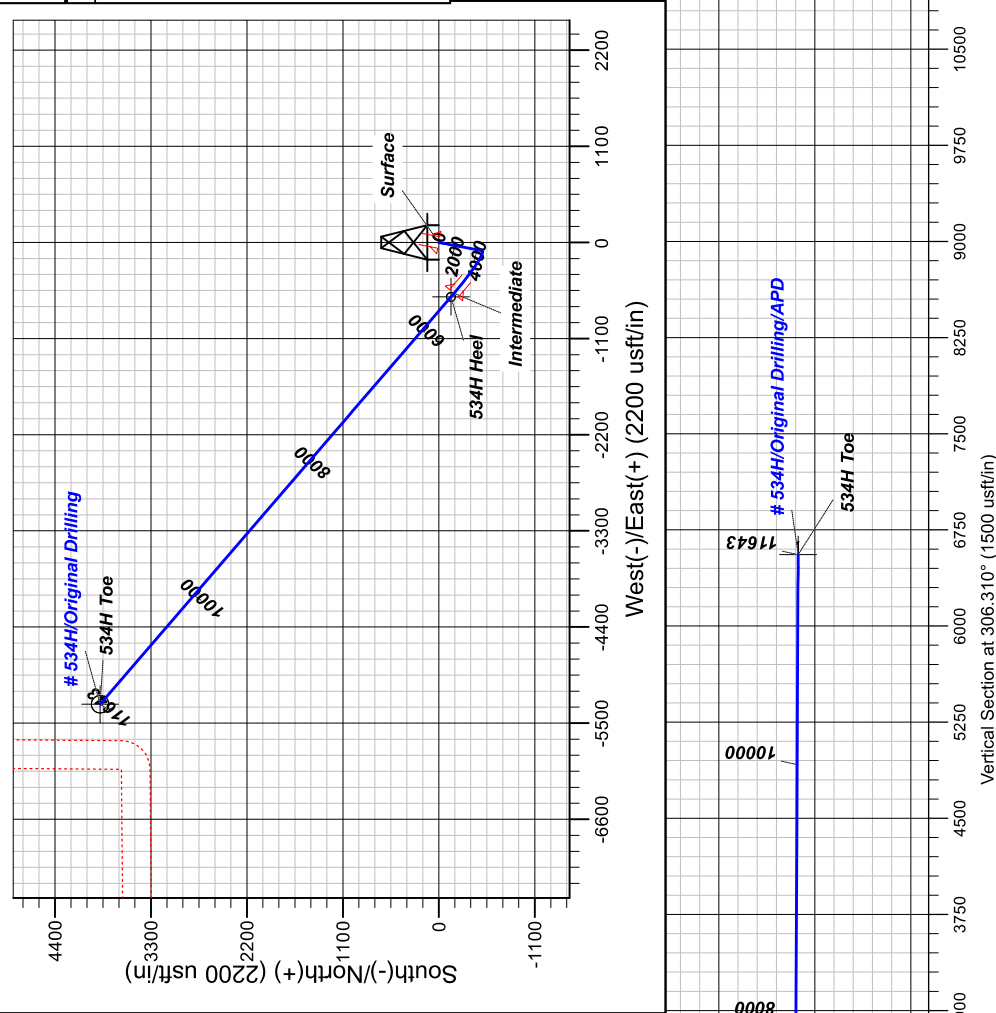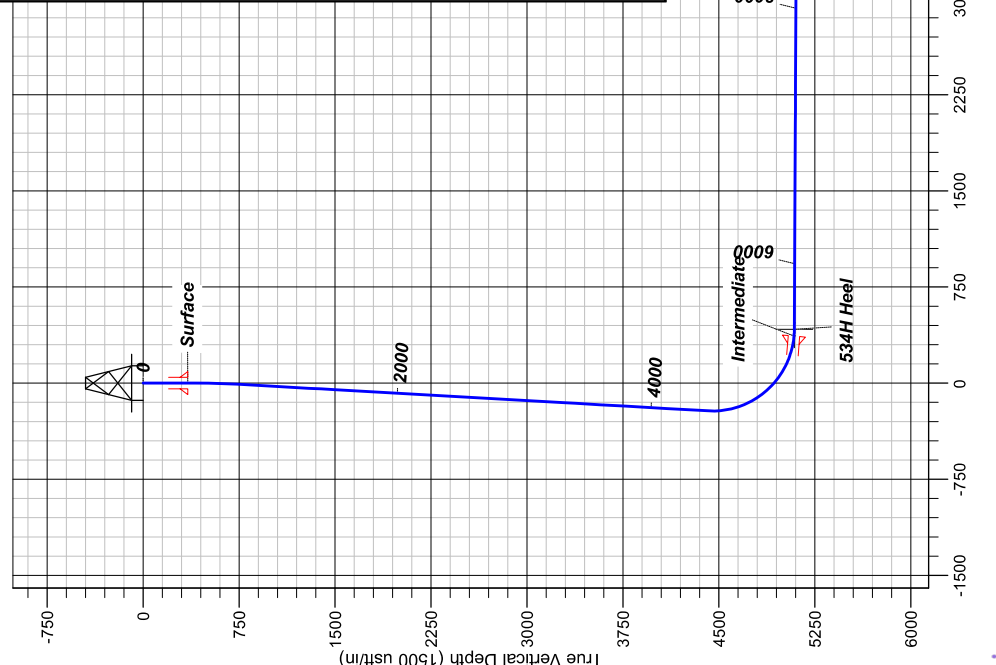

Azimuths to True North
Magnetic North: 81.83°
Magnetic Field
Strength: 49276.62
Dip Angle: 62.22°
Date: 6/26/2020
Model: HDGM_F13E

CASING DETAILS

TVD	MD	Na
350.00	350.00	Surface
5087.57	5434.28	Intermed

FORMATION DETAILS

MDPath	Formation
885.00	Ojo Alamo
984.00	Kirtland
1169.00	Fruitland
1462.00	Pictured Cliffs
1576.00	Lewis
2279.00	Chacra
2293.03	Menefee
3010.15	Point Lookout
3865.45	Mancos
4025.00	Mancos Silt
4314.00	Gallup A
4803.00	Gallup B
4843.00	Gallup C
4907.45	
4942.00	
5045.71	



DJR Operating

North Alamito Unit

L29 2307 Pad

534H - Slot 1

Original Drilling

Plan: APD

Standard Planning Report

16 July, 2020





Lonestar Consulting, LLC
Planning Report



Database:	DJR	Local Co-ordinate Reference:	Well # 534H - Slot 1
Company:	DJR Operating	TVD Reference:	GL 6875' & RKB 14' @ 6889.00usft
Project:	North Alamito Unit	MD Reference:	GL 6875' & RKB 14' @ 6889.00usft
Site:	L29 2307 Pad	North Reference:	True
Well:	# 534H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Original Drilling		
Design:	APD		

Project	North Alamito Unit		
Map System:	US State Plane 1983	System Datum:	Mean Sea Level
Geo Datum:	North American Datum 1983		
Map Zone:	New Mexico Western Zone		

Site	L29 2307 Pad				
Site Position:		Northing:	1,890,427.01 usft	Latitude:	36.19519100
From:	Lat/Long	Easting:	2,790,825.05 usft	Longitude:	-107.60377300
Position Uncertainty:	0.00 usft	Slot Radius:	13.20 in	Grid Convergence:	0.14

Well	# 534H - Slot 1					
Well Position	+N/-S	-7.28 usft	Northing:	1,890,419.68 usft	Latitude:	36.19517100
	+E/-W	-18.59 usft	Easting:	2,790,806.48 usft	Longitude:	-107.60383600
Position Uncertainty		0.00 usft	Wellhead Elevation:		Ground Level:	6,875.00 usft

Wellbore	Original Drilling				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	HDGM_FILE	6/26/2020	8.65	62.75	49,276.30000000

Design	APD			
Audit Notes:				
Version:	Phase:	PLAN	Tie On Depth:	0.00
Vertical Section:	Depth From (TVD) (usft)	+N/-S (usft)	+E/-W (usft)	Direction (°)
	0.00	0.00	0.00	306.310

Plan Survey Tool Program	Date	7/16/2020			
Depth From (usft)	Depth To (usft)	Survey (Wellbore)	Tool Name	Remarks	
1	0.00	11,643.31	APD (Original Drilling)	MWD+HDGM	
			OWSG MWD + HDGM		

Plan Sections										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)	TFO (°)	Target
0.00	0.00	0.000	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
400.00	0.00	0.000	400.00	0.00	0.00	0.00	0.00	0.00	0.00	
774.55	7.49	190.787	773.49	-24.02	-4.58	2.00	2.00	0.00	190.79	
4,448.62	7.49	190.787	4,416.20	-494.55	-94.22	0.00	0.00	0.00	0.00	
5,487.07	89.72	310.792	5,090.00	-139.34	-622.72	9.00	7.92	11.56	119.82	534H Heel
11,643.31	89.72	310.792	5,120.00	3,882.56	-5,283.48	0.00	0.00	0.00	0.00	534H Toe



Lonestar Consulting, LLC

Planning Report



Database:	DJR	Local Co-ordinate Reference:	Well # 534H - Slot 1
Company:	DJR Operating	TVD Reference:	GL 6875' & RKB 14' @ 6889.00usft
Project:	North Alamito Unit	MD Reference:	GL 6875' & RKB 14' @ 6889.00usft
Site:	L29 2307 Pad	North Reference:	True
Well:	# 534H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Original Drilling		
Design:	APD		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
0.00	0.00	0.000	0.00	0.00	0.00	0.00	0.00	0.00	0.00
100.00	0.00	0.000	100.00	0.00	0.00	0.00	0.00	0.00	0.00
200.00	0.00	0.000	200.00	0.00	0.00	0.00	0.00	0.00	0.00
300.00	0.00	0.000	300.00	0.00	0.00	0.00	0.00	0.00	0.00
400.00	0.00	0.000	400.00	0.00	0.00	0.00	0.00	0.00	0.00
500.00	2.00	190.787	499.98	-1.71	-0.33	-0.75	2.00	2.00	0.00
600.00	4.00	190.787	599.84	-6.86	-1.31	-3.01	2.00	2.00	0.00
700.00	6.00	190.787	699.45	-15.42	-2.94	-6.76	2.00	2.00	0.00
774.55	7.49	190.787	773.49	-24.02	-4.58	-10.54	2.00	2.00	0.00
800.00	7.49	190.787	798.72	-27.28	-5.20	-11.96	0.00	0.00	0.00
900.00	7.49	190.787	897.86	-40.08	-7.64	-17.58	0.00	0.00	0.00
1,000.00	7.49	190.787	997.01	-52.89	-10.08	-23.20	0.00	0.00	0.00
1,100.00	7.49	190.787	1,096.16	-65.70	-12.52	-28.82	0.00	0.00	0.00
1,200.00	7.49	190.787	1,195.30	-78.50	-14.96	-34.43	0.00	0.00	0.00
1,300.00	7.49	190.787	1,294.45	-91.31	-17.40	-40.05	0.00	0.00	0.00
1,400.00	7.49	190.787	1,393.60	-104.12	-19.84	-45.67	0.00	0.00	0.00
1,500.00	7.49	190.787	1,492.74	-116.92	-22.28	-51.29	0.00	0.00	0.00
1,600.00	7.49	190.787	1,591.89	-129.73	-24.72	-56.90	0.00	0.00	0.00
1,700.00	7.49	190.787	1,691.04	-142.54	-27.16	-62.52	0.00	0.00	0.00
1,800.00	7.49	190.787	1,790.18	-155.35	-29.60	-68.14	0.00	0.00	0.00
1,900.00	7.49	190.787	1,889.33	-168.15	-32.04	-73.76	0.00	0.00	0.00
2,000.00	7.49	190.787	1,988.47	-180.96	-34.48	-79.37	0.00	0.00	0.00
2,100.00	7.49	190.787	2,087.62	-193.77	-36.92	-84.99	0.00	0.00	0.00
2,200.00	7.49	190.787	2,186.77	-206.57	-39.36	-90.61	0.00	0.00	0.00
2,300.00	7.49	190.787	2,285.91	-219.38	-41.80	-96.23	0.00	0.00	0.00
2,400.00	7.49	190.787	2,385.06	-232.19	-44.24	-101.84	0.00	0.00	0.00
2,500.00	7.49	190.787	2,484.21	-244.99	-46.68	-107.46	0.00	0.00	0.00
2,600.00	7.49	190.787	2,583.35	-257.80	-49.12	-113.08	0.00	0.00	0.00
2,700.00	7.49	190.787	2,682.50	-270.61	-51.56	-118.69	0.00	0.00	0.00
2,800.00	7.49	190.787	2,781.65	-283.41	-54.00	-124.31	0.00	0.00	0.00
2,900.00	7.49	190.787	2,880.79	-296.22	-56.44	-129.93	0.00	0.00	0.00
3,000.00	7.49	190.787	2,979.94	-309.03	-58.88	-135.55	0.00	0.00	0.00
3,100.00	7.49	190.787	3,079.09	-321.83	-61.32	-141.16	0.00	0.00	0.00
3,200.00	7.49	190.787	3,178.23	-334.64	-63.76	-146.78	0.00	0.00	0.00
3,300.00	7.49	190.787	3,277.38	-347.45	-66.20	-152.40	0.00	0.00	0.00
3,400.00	7.49	190.787	3,376.53	-360.25	-68.64	-158.02	0.00	0.00	0.00
3,500.00	7.49	190.787	3,475.67	-373.06	-71.08	-163.63	0.00	0.00	0.00
3,600.00	7.49	190.787	3,574.82	-385.87	-73.52	-169.25	0.00	0.00	0.00
3,700.00	7.49	190.787	3,673.97	-398.67	-75.96	-174.87	0.00	0.00	0.00
3,800.00	7.49	190.787	3,773.11	-411.48	-78.40	-180.49	0.00	0.00	0.00
3,900.00	7.49	190.787	3,872.26	-424.29	-80.84	-186.10	0.00	0.00	0.00
4,000.00	7.49	190.787	3,971.41	-437.09	-83.28	-191.72	0.00	0.00	0.00
4,100.00	7.49	190.787	4,070.55	-449.90	-85.72	-197.34	0.00	0.00	0.00
4,200.00	7.49	190.787	4,169.70	-462.71	-88.16	-202.96	0.00	0.00	0.00
4,300.00	7.49	190.787	4,268.84	-475.51	-90.60	-208.57	0.00	0.00	0.00
4,400.00	7.49	190.787	4,367.99	-488.32	-93.04	-214.19	0.00	0.00	0.00
4,448.62	7.49	190.787	4,416.20	-494.55	-94.22	-216.92	0.00	0.00	0.00
4,500.00	6.55	228.579	4,467.22	-499.78	-97.05	-217.74	9.00	-1.82	73.55
4,600.00	11.81	277.831	4,566.04	-502.17	-111.50	-207.51	9.00	5.25	49.25
4,700.00	19.93	292.526	4,662.18	-494.23	-137.43	-181.92	9.00	8.12	14.69
4,800.00	28.57	298.757	4,753.29	-476.16	-174.21	-141.58	9.00	8.64	6.23
4,900.00	37.37	302.252	4,837.11	-448.40	-220.93	-87.49	9.00	8.80	3.49
5,000.00	46.24	304.565	4,911.58	-411.64	-276.45	-20.99	9.00	8.87	2.31
5,100.00	55.14	306.276	4,974.87	-366.79	-339.39	56.29	9.00	8.90	1.71



Lonestar Consulting, LLC

Planning Report



Database:	DJR	Local Co-ordinate Reference:	Well # 534H - Slot 1
Company:	DJR Operating	TVD Reference:	GL 6875' & RKB 14' @ 6889.00usft
Project:	North Alamito Unit	MD Reference:	GL 6875' & RKB 14' @ 6889.00usft
Site:	L29 2307 Pad	North Reference:	True
Well:	# 534H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Original Drilling		
Design:	APD		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)	
5,200.00	64.06	307.650	5,025.42	-314.94	-408.21	142.45	9.00	8.92	1.37	
5,300.00	73.00	308.829	5,061.99	-257.38	-481.21	235.36	9.00	8.93	1.18	
5,400.00	81.94	309.899	5,083.67	-195.52	-556.59	332.74	9.00	8.94	1.07	
5,487.07	89.72	310.792	5,090.00	-139.34	-622.72	419.29	9.00	8.94	1.02	
5,500.00	89.72	310.792	5,090.06	-130.89	-632.51	432.18	0.00	0.00	0.00	
5,600.00	89.72	310.792	5,090.55	-65.56	-708.22	531.88	0.00	0.00	0.00	
5,700.00	89.72	310.792	5,091.04	-0.23	-783.93	631.57	0.00	0.00	0.00	
5,800.00	89.72	310.792	5,091.53	65.10	-859.64	731.26	0.00	0.00	0.00	
5,900.00	89.72	310.792	5,092.01	130.43	-935.34	830.96	0.00	0.00	0.00	
6,000.00	89.72	310.792	5,092.50	195.76	-1,011.05	930.65	0.00	0.00	0.00	
6,100.00	89.72	310.792	5,092.99	261.09	-1,086.76	1,030.34	0.00	0.00	0.00	
6,200.00	89.72	310.792	5,093.47	326.42	-1,162.47	1,130.04	0.00	0.00	0.00	
6,300.00	89.72	310.792	5,093.96	391.75	-1,238.18	1,229.73	0.00	0.00	0.00	
6,400.00	89.72	310.792	5,094.45	457.08	-1,313.88	1,329.42	0.00	0.00	0.00	
6,500.00	89.72	310.792	5,094.94	522.41	-1,389.59	1,429.11	0.00	0.00	0.00	
6,600.00	89.72	310.792	5,095.42	587.74	-1,465.30	1,528.81	0.00	0.00	0.00	
6,700.00	89.72	310.792	5,095.91	653.07	-1,541.01	1,628.50	0.00	0.00	0.00	
6,800.00	89.72	310.792	5,096.40	718.40	-1,616.72	1,728.19	0.00	0.00	0.00	
6,900.00	89.72	310.792	5,096.89	783.73	-1,692.42	1,827.89	0.00	0.00	0.00	
7,000.00	89.72	310.792	5,097.37	849.06	-1,768.13	1,927.58	0.00	0.00	0.00	
7,100.00	89.72	310.792	5,097.86	914.39	-1,843.84	2,027.27	0.00	0.00	0.00	
7,200.00	89.72	310.792	5,098.35	979.73	-1,919.55	2,126.97	0.00	0.00	0.00	
7,300.00	89.72	310.792	5,098.83	1,045.06	-1,995.26	2,226.66	0.00	0.00	0.00	
7,400.00	89.72	310.792	5,099.32	1,110.39	-2,070.96	2,326.35	0.00	0.00	0.00	
7,500.00	89.72	310.792	5,099.81	1,175.72	-2,146.67	2,426.05	0.00	0.00	0.00	
7,600.00	89.72	310.792	5,100.30	1,241.05	-2,222.38	2,525.74	0.00	0.00	0.00	
7,700.00	89.72	310.792	5,100.78	1,306.38	-2,298.09	2,625.43	0.00	0.00	0.00	
7,800.00	89.72	310.792	5,101.27	1,371.71	-2,373.80	2,725.12	0.00	0.00	0.00	
7,900.00	89.72	310.792	5,101.76	1,437.04	-2,449.50	2,824.82	0.00	0.00	0.00	
8,000.00	89.72	310.792	5,102.25	1,502.37	-2,525.21	2,924.51	0.00	0.00	0.00	
8,100.00	89.72	310.792	5,102.73	1,567.70	-2,600.92	3,024.20	0.00	0.00	0.00	
8,200.00	89.72	310.792	5,103.22	1,633.03	-2,676.63	3,123.90	0.00	0.00	0.00	
8,300.00	89.72	310.792	5,103.71	1,698.36	-2,752.33	3,223.59	0.00	0.00	0.00	
8,400.00	89.72	310.792	5,104.20	1,763.69	-2,828.04	3,323.28	0.00	0.00	0.00	
8,500.00	89.72	310.792	5,104.68	1,829.02	-2,903.75	3,422.98	0.00	0.00	0.00	
8,600.00	89.72	310.792	5,105.17	1,894.35	-2,979.46	3,522.67	0.00	0.00	0.00	
8,700.00	89.72	310.792	5,105.66	1,959.68	-3,055.17	3,622.36	0.00	0.00	0.00	
8,800.00	89.72	310.792	5,106.14	2,025.01	-3,130.87	3,722.06	0.00	0.00	0.00	
8,900.00	89.72	310.792	5,106.63	2,090.34	-3,206.58	3,821.75	0.00	0.00	0.00	
9,000.00	89.72	310.792	5,107.12	2,155.67	-3,282.29	3,921.44	0.00	0.00	0.00	
9,100.00	89.72	310.792	5,107.61	2,221.00	-3,358.00	4,021.13	0.00	0.00	0.00	
9,200.00	89.72	310.792	5,108.09	2,286.34	-3,433.71	4,120.83	0.00	0.00	0.00	
9,300.00	89.72	310.792	5,108.58	2,351.67	-3,509.41	4,220.52	0.00	0.00	0.00	
9,400.00	89.72	310.792	5,109.07	2,417.00	-3,585.12	4,320.21	0.00	0.00	0.00	
9,500.00	89.72	310.792	5,109.56	2,482.33	-3,660.83	4,419.91	0.00	0.00	0.00	
9,600.00	89.72	310.792	5,110.04	2,547.66	-3,736.54	4,519.60	0.00	0.00	0.00	
9,700.00	89.72	310.792	5,110.53	2,612.99	-3,812.25	4,619.29	0.00	0.00	0.00	
9,800.00	89.72	310.792	5,111.02	2,678.32	-3,887.95	4,718.99	0.00	0.00	0.00	
9,900.00	89.72	310.792	5,111.50	2,743.65	-3,963.66	4,818.68	0.00	0.00	0.00	
10,000.00	89.72	310.792	5,111.99	2,808.98	-4,039.37	4,918.37	0.00	0.00	0.00	
10,100.00	89.72	310.792	5,112.48	2,874.31	-4,115.08	5,018.07	0.00	0.00	0.00	
10,200.00	89.72	310.792	5,112.97	2,939.64	-4,190.79	5,117.76	0.00	0.00	0.00	
10,300.00	89.72	310.792	5,113.45	3,004.97	-4,266.49	5,217.45	0.00	0.00	0.00	
10,400.00	89.72	310.792	5,113.94	3,070.30	-4,342.20	5,317.14	0.00	0.00	0.00	



Lonestar Consulting, LLC
Planning Report



Database:	DJR	Local Co-ordinate Reference:	Well # 534H - Slot 1
Company:	DJR Operating	TVD Reference:	GL 6875' & RKB 14' @ 6889.00usft
Project:	North Alamito Unit	MD Reference:	GL 6875' & RKB 14' @ 6889.00usft
Site:	L29 2307 Pad	North Reference:	True
Well:	# 534H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Original Drilling		
Design:	APD		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)	
10,500.00	89.72	310.792	5,114.43	3,135.63	-4,417.91	5,416.84	0.00	0.00	0.00	
10,600.00	89.72	310.792	5,114.92	3,200.96	-4,493.62	5,516.53	0.00	0.00	0.00	
10,700.00	89.72	310.792	5,115.40	3,266.29	-4,569.33	5,616.22	0.00	0.00	0.00	
10,800.00	89.72	310.792	5,115.89	3,331.62	-4,645.03	5,715.92	0.00	0.00	0.00	
10,900.00	89.72	310.792	5,116.38	3,396.95	-4,720.74	5,815.61	0.00	0.00	0.00	
11,000.00	89.72	310.792	5,116.87	3,462.28	-4,796.45	5,915.30	0.00	0.00	0.00	
11,100.00	89.72	310.792	5,117.35	3,527.61	-4,872.16	6,015.00	0.00	0.00	0.00	
11,200.00	89.72	310.792	5,117.84	3,592.95	-4,947.86	6,114.69	0.00	0.00	0.00	
11,300.00	89.72	310.792	5,118.33	3,658.28	-5,023.57	6,214.38	0.00	0.00	0.00	
11,400.00	89.72	310.792	5,118.81	3,723.61	-5,099.28	6,314.07	0.00	0.00	0.00	
11,500.00	89.72	310.792	5,119.30	3,788.94	-5,174.99	6,413.77	0.00	0.00	0.00	
11,600.00	89.72	310.792	5,119.79	3,854.27	-5,250.70	6,513.46	0.00	0.00	0.00	
11,643.31	89.72	310.792	5,120.00	3,882.56	-5,283.48	6,556.63	0.00	0.00	0.00	

Design Targets										
Target Name	Dip Angle (°)	Dip Dir. (°)	TVD (usft)	+N/-S (usft)	+E/-W (usft)	Northing (usft)	Easting (usft)	Latitude	Longitude	
- hit/miss target										
- Shape										
534H Heel	0.00	0.000	5,090.00	-139.34	-622.72	1,890,278.87	2,790,184.09	36.19478820	-107.60594650	
- plan hits target center										
- Circle (radius 50.00)										
534H Toe	0.00	0.000	5,120.00	3,882.56	-5,283.48	1,894,289.73	2,785,513.83	36.20583540	-107.62174500	
- plan hits target center										
- Circle (radius 100.00)										

Casing Points						Casing Diameter (in)	Hole Diameter (in)
Measured Depth (usft)	Vertical Depth (usft)	Name					
350.00	350.00	Surface				9.62	12.25
5,434.28	5,087.57	Intermediate				7.00	8.75



Lonestar Consulting, LLC
Planning Report



Database:	DJR	Local Co-ordinate Reference:	Well # 534H - Slot 1
Company:	DJR Operating	TVD Reference:	GL 6875' & RKB 14' @ 6889.00usft
Project:	North Alamito Unit	MD Reference:	GL 6875' & RKB 14' @ 6889.00usft
Site:	L29 2307 Pad	North Reference:	True
Well:	# 534H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Original Drilling		
Design:	APD		

Formations						
Measured Depth (usft)	Vertical Depth (usft)	Name	Lithology	Dip (°)	Dip Direction (°)	
887.03	885.00	Ojo Alamo		0.00	0.000	
986.88	984.00	Kirtland		0.00	0.000	
1,173.47	1,169.00	Fruitland		0.00	0.000	
1,468.99	1,462.00	Pictured Cliffs		0.00	0.000	
1,583.97	1,576.00	Lewis		0.00	0.000	
2,293.03	2,279.00	Chacra		0.00	0.000	
3,010.15	2,990.00	Menefee		0.00	0.000	
3,865.45	3,838.00	Point Lookout		0.00	0.000	
4,054.06	4,025.00	Mancos		0.00	0.000	
4,345.54	4,314.00	Mancos Silt		0.00	0.000	
4,858.09	4,803.00	Gallup A		0.00	0.000	
4,907.45	4,843.00	Gallup B		0.00	0.000	
5,045.71	4,942.00	Gallup C		0.00	0.000	



DJR Operating

North Alamito Unit

L29 2307 Pad

534H

Original Drilling

APD

Anticollision Report

16 July, 2020





Lonestar Consulting, LLC

Anticollision Report



Company:	DJR Operating	Local Co-ordinate Reference:	Well # 534H - Slot 1
Project:	North Alamito Unit	TVD Reference:	GL 6875' & RKB 14' @ 6889.00usft
Reference Site:	L29 2307 Pad	MD Reference:	GL 6875' & RKB 14' @ 6889.00usft
Site Error:	0.00 usft	North Reference:	True
Reference Well:	# 534H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	Original Drilling	Database:	DJR
Reference Design:	APD	Offset TVD Reference:	Offset Datum

Reference	APD		
Filter type:	NO GLOBAL FILTER: Using user defined selection & filtering criteria		
Interpolation Method:	Stations	Error Model:	ISCWSA
Depth Range:	Unlimited	Scan Method:	Closest Approach 3D
Results Limited by:	Maximum ellipse separation of 1,000.00 usft	Error Surface:	Pedal Curve
Warning Levels Evaluated at:	2.00 Sigma	Casing Method:	Not applied

Survey Tool Program		Date	7/16/2020		
From (usft)	To (usft)	Survey (Wellbore)	Tool Name	Description	
0.00	11,643.31	APD (Original Drilling)	MWD+HDGM	OWSG MWD + HDGM	

Summary						
Site Name	Reference Measured Depth (usft)	Offset Measured Depth (usft)	Distance Between Centres (usft)	Distance Between Ellipses (usft)	Separation Factor	Warning
Offset Well - Wellbore - Design						
L29 2307 Pad						
# 236H - Original Drilling - APD	400.00	400.00	19.96	17.50	8.118	CC, ES
# 236H - Original Drilling - APD	11,643.31	12,617.25	1,294.73	913.34	3.395	SF

Offset Design L29 2307 Pad - # 236H - Original Drilling - APD													Offset Site Error:	0.00 usft
Survey Program: 0-MWD+HDGM													Offset Well Error:	0.00 usft
Reference		Offset		Semi Major Axis			Distance							
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	Warning	
0.00	0.00	0.00	0.00	0.00	0.00	68.61	7.28	18.59	19.96					
100.00	100.00	100.00	100.00	0.15	0.15	68.61	7.28	18.59	19.96	19.66	0.31	64.757		
200.00	200.00	200.00	200.00	0.51	0.51	68.61	7.28	18.59	19.96	18.94	1.03	19.472		
300.00	300.00	300.00	300.00	0.87	0.87	68.61	7.28	18.59	19.96	18.22	1.74	11.459		
400.00	400.00	400.00	400.00	1.23	1.23	68.61	7.28	18.59	19.96	17.50	2.46	8.118	CC, ES	
500.00	499.98	499.52	499.52	1.57	1.58	-124.66	7.10	19.54	21.74	18.59	3.15	6.898		
600.00	599.84	598.60	598.49	1.91	1.92	-128.25	6.29	23.75	28.33	24.50	3.83	7.391		
700.00	699.45	697.02	696.62	2.26	2.27	-130.96	4.86	31.26	39.86	35.33	4.53	8.799		
774.55	773.49	769.77	768.94	2.53	2.54	-132.25	3.39	38.94	51.63	46.57	5.06	10.206		
800.00	798.72	794.47	793.44	2.62	2.63	-132.56	2.81	41.96	56.18	50.94	5.24	10.722		
900.00	897.86	890.94	888.89	3.00	3.00	-132.31	0.18	55.72	75.60	69.66	5.95	12.711		
1,000.00	997.01	986.37	982.78	3.38	3.38	-130.85	-3.02	72.44	97.46	90.80	6.66	14.632		
1,100.00	1,096.16	1,080.55	1,074.84	3.77	3.78	-128.95	-6.75	91.94	121.82	114.44	7.38	16.517		
1,200.00	1,195.30	1,173.31	1,164.83	4.16	4.20	-126.93	-10.98	114.04	148.75	140.67	8.09	18.394		
1,300.00	1,294.45	1,264.49	1,252.53	4.55	4.64	-124.94	-15.67	138.54	178.31	169.52	8.80	20.270		
1,400.00	1,393.60	1,353.96	1,337.76	4.95	5.11	-123.07	-20.77	165.23	210.51	201.01	9.50	22.160		
1,500.00	1,492.74	1,446.28	1,425.07	5.34	5.62	-121.36	-26.41	194.72	244.67	234.42	10.25	23.870		
1,600.00	1,591.89	1,540.01	1,513.67	5.74	6.16	-120.03	-32.16	224.75	279.06	268.03	11.03	25.308		
1,700.00	1,691.04	1,633.74	1,602.27	6.14	6.72	-119.00	-37.90	254.78	313.55	301.74	11.81	26.551		
1,800.00	1,790.18	1,727.46	1,690.87	6.54	7.28	-118.17	-43.65	284.81	348.12	335.52	12.60	27.636		
1,900.00	1,889.33	1,821.19	1,779.47	6.94	7.84	-117.49	-49.39	314.83	382.74	369.35	13.39	28.588		
2,000.00	1,988.47	1,914.92	1,868.07	7.34	8.42	-116.92	-55.14	344.86	417.40	403.22	14.18	29.430		
2,100.00	2,087.62	2,008.64	1,956.67	7.75	9.00	-116.44	-60.88	374.89	452.10	437.12	14.98	30.180		
2,200.00	2,186.77	2,102.37	2,045.27	8.15	9.58	-116.02	-66.63	404.92	486.81	471.03	15.78	30.851		
2,300.00	2,285.91	2,196.10	2,133.87	8.55	10.16	-115.67	-72.37	434.94	521.55	504.97	16.58	31.454		



Lonestar Consulting, LLC

Anticollision Report



Company:	DJR Operating	Local Co-ordinate Reference:	Well # 534H - Slot 1
Project:	North Alamito Unit	TVD Reference:	GL 6875' & RKB 14' @ 6889.00usft
Reference Site:	L29 2307 Pad	MD Reference:	GL 6875' & RKB 14' @ 6889.00usft
Site Error:	0.00 usft	North Reference:	True
Reference Well:	# 534H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	Original Drilling	Database:	DJR
Reference Design:	APD	Offset TVD Reference:	Offset Datum

Offset Design L29 2307 Pad - # 236H - Original Drilling - APD													Offset Site Error:	0.00 usft
Survey Program: 0-MWD+HDGM													Offset Well Error:	0.00 usft
Reference		Offset		Semi Major Axis			Distance						Warning	
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
2,400.00	2,385.06	2,289.83	2,222.47	8.95	10.75	-115.35	-78.11	464.97	556.30	538.91	17.38	32.000		
2,500.00	2,484.21	2,383.55	2,311.08	9.36	11.34	-115.08	-83.86	495.00	591.06	572.87	18.19	32.496		
2,600.00	2,583.35	2,477.28	2,399.68	9.76	11.93	-114.83	-89.60	525.03	625.84	606.84	18.99	32.948		
2,700.00	2,682.50	2,571.01	2,488.28	10.17	12.53	-114.61	-95.35	555.05	660.62	640.82	19.80	33.362		
2,800.00	2,781.65	2,664.73	2,576.88	10.57	13.12	-114.41	-101.09	585.08	695.41	674.80	20.61	33.742		
2,900.00	2,880.79	2,758.46	2,665.48	10.97	13.72	-114.23	-106.84	615.11	730.21	708.79	21.42	34.093		
3,000.00	2,979.94	2,852.19	2,754.08	11.38	14.31	-114.07	-112.58	645.14	765.01	742.78	22.23	34.417		
3,100.00	3,079.09	2,945.91	2,842.68	11.78	14.91	-113.92	-118.32	675.16	799.82	776.78	23.04	34.717		
3,200.00	3,178.23	3,039.64	2,931.28	12.19	15.51	-113.79	-124.07	705.19	834.63	810.78	23.85	34.996		
3,300.00	3,277.38	3,133.37	3,019.88	12.59	16.11	-113.66	-129.81	735.22	869.45	844.79	24.66	35.257		
3,400.00	3,376.53	3,227.10	3,108.48	13.00	16.71	-113.55	-135.56	765.25	904.27	878.80	25.47	35.500		
3,500.00	3,475.67	3,320.82	3,197.08	13.40	17.31	-113.44	-141.30	795.28	939.09	912.81	26.29	35.727		
3,600.00	3,574.82	3,414.55	3,285.68	13.81	17.91	-113.34	-147.05	825.30	973.92	946.82	27.10	35.940		
3,700.00	3,673.97	3,508.28	3,374.29	14.21	18.52	-113.25	-152.79	855.33	1,008.74	980.83	27.91	36.140		
3,800.00	3,773.11	3,602.00	3,462.89	14.62	19.12	-113.16	-158.54	885.36	1,043.57	1,014.85	28.73	36.329		
3,900.00	3,872.26	3,695.73	3,551.49	15.02	19.72	-113.08	-164.28	915.39	1,078.41	1,048.87	29.54	36.507		
4,000.00	3,971.41	3,789.46	3,640.09	15.43	20.32	-113.00	-170.02	945.41	1,113.24	1,082.89	30.35	36.675		
4,100.00	4,070.55	3,883.19	3,728.69	15.83	20.93	-112.93	-175.77	975.44	1,148.08	1,116.91	31.17	36.833		
4,200.00	4,169.70	3,976.91	3,817.29	16.24	21.53	-112.87	-181.51	1,005.47	1,182.91	1,150.93	31.98	36.984		
4,300.00	4,268.84	4,070.64	3,905.89	16.64	22.14	-112.80	-187.26	1,035.50	1,217.75	1,184.95	32.80	37.126		
4,400.00	4,367.99	4,164.37	3,994.49	17.05	22.74	-112.74	-193.00	1,065.52	1,252.59	1,218.97	33.62	37.261		
4,448.62	4,416.20	4,209.94	4,037.57	17.25	23.03	-112.72	-195.79	1,080.12	1,269.53	1,235.52	34.01	37.325		
4,450.00	4,417.56	4,211.23	4,038.79	17.25	23.04	-113.58	-195.87	1,080.54	1,270.01	1,235.99	34.02	37.327		
4,500.00	4,467.22	4,257.58	4,082.61	17.45	23.34	-151.62	-198.71	1,095.39	1,288.59	1,254.18	34.42	37.442		
4,550.00	4,516.81	4,302.77	4,125.32	17.62	23.63	175.18	-201.48	1,109.86	1,309.32	1,274.55	34.77	37.656		
4,600.00	4,566.04	5,834.77	5,107.81	17.79	32.18	127.09	399.98	678.89	1,316.10	1,271.86	44.23	29.754		
4,650.00	4,614.59	5,845.49	5,107.87	17.94	32.35	118.99	407.03	670.81	1,302.04	1,256.87	45.17	28.826		
4,700.00	4,662.18	5,860.01	5,107.94	18.08	32.57	114.24	416.57	659.87	1,289.94	1,243.82	46.12	27.972		
4,750.00	4,708.51	5,878.23	5,108.03	18.20	32.86	111.02	428.55	646.14	1,279.79	1,232.72	47.07	27.189		
4,800.00	4,753.29	5,900.05	5,108.14	18.32	33.20	108.56	442.89	629.70	1,271.55	1,223.51	48.03	26.474		
4,850.00	4,796.24	5,925.33	5,108.26	18.42	33.63	106.47	459.51	610.64	1,265.12	1,216.09	49.02	25.806		
4,900.00	4,837.11	5,953.92	5,108.40	18.51	34.12	104.57	478.30	589.10	1,260.37	1,210.33	50.03	25.191		
4,950.00	4,875.63	5,985.63	5,108.56	18.60	34.66	102.78	499.14	565.20	1,257.12	1,206.06	51.06	24.620		
5,000.00	4,911.58	6,020.28	5,108.73	18.67	35.27	101.05	521.92	539.09	1,255.19	1,203.05	52.14	24.074		
5,050.00	4,944.73	6,057.65	5,108.91	18.73	35.96	99.39	546.48	510.92	1,254.35	1,201.08	53.28	23.545		
5,072.34	4,958.58	6,075.17	5,109.00	18.75	36.28	98.67	558.00	497.72	1,254.27	1,200.46	53.81	23.310		
5,100.00	4,974.87	6,097.51	5,109.11	18.78	36.69	97.81	572.68	480.89	1,254.38	1,199.92	54.47	23.031		
5,150.00	5,001.82	6,139.62	5,109.31	18.82	37.50	96.32	600.35	449.16	1,255.06	1,199.31	55.75	22.512		
5,200.00	5,025.42	6,183.70	5,109.53	19.14	38.36	94.97	629.33	415.93	1,256.16	1,199.05	57.12	21.993		
5,250.00	5,045.52	6,229.50	5,109.76	19.64	39.28	93.77	659.44	381.42	1,257.49	1,198.91	58.58	21.466		
5,300.00	5,061.99	6,276.73	5,109.99	20.20	40.23	92.76	690.48	345.82	1,258.86	1,198.72	60.14	20.932		
5,350.00	5,074.73	6,325.10	5,110.23	20.83	41.24	91.95	722.27	309.37	1,260.12	1,198.33	61.79	20.392		
5,400.00	5,083.67	6,374.31	5,110.47	21.52	42.27	91.37	754.62	272.29	1,261.16	1,197.62	63.54	19.849		
5,450.00	5,088.75	6,424.06	5,110.71	22.26	43.34	91.04	787.32	234.80	1,261.88	1,196.53	65.35	19.309		
5,487.07	5,090.00	6,461.10	5,110.90	22.84	44.14	90.95	811.67	206.88	1,262.18	1,195.44	66.74	18.912		
5,500.00	5,090.06	6,474.03	5,110.96	23.05	44.42	90.95	820.17	197.13	1,262.25	1,195.02	67.23	18.776		
5,600.00	5,090.55	6,574.03	5,111.45	24.76	46.63	90.95	885.90	121.77	1,262.78	1,191.62	71.15	17.747		
5,700.00	5,091.04	6,674.03	5,111.94	26.62	48.89	90.95	951.62	46.41	1,263.30	1,188.02	75.28	16.780		
5,800.00	5,091.53	6,774.03	5,112.44	28.61	51.19	90.95	1,017.35	-28.95	1,263.83	1,184.25	79.59	15.880		
5,900.00	5,092.01	6,874.03	5,112.93	30.70	53.53	90.95	1,083.08	-104.31	1,264.36	1,180.34	84.02	15.047		
6,000.00	5,092.50	6,974.03	5,113.42	32.88	55.90	90.95	1,148.81	-179.67	1,264.89	1,176.31	88.58	14.280		
6,100.00	5,092.99	7,074.02	5,113.91	35.12	58.29	90.95	1,214.54	-255.03	1,265.42	1,172.19	93.23	13.573		



Lonestar Consulting, LLC

Anticollision Report



Company:	DJR Operating	Local Co-ordinate Reference:	Well # 534H - Slot 1
Project:	North Alamito Unit	TVD Reference:	GL 6875' & RKB 14' @ 6889.00usft
Reference Site:	L29 2307 Pad	MD Reference:	GL 6875' & RKB 14' @ 6889.00usft
Site Error:	0.00 usft	North Reference:	True
Reference Well:	# 534H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	Original Drilling	Database:	DJR
Reference Design:	APD	Offset TVD Reference:	Offset Datum

Offset Design L29 2307 Pad - # 236H - Original Drilling - APD													Offset Site Error:	0.00 usft
Survey Program: 0-MWD+HDGM													Offset Well Error:	0.00 usft
Reference		Offset		Semi Major Axis		Highside Toolface (°)	Distance		Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	Warning	
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)		Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)						
6,200.00	5,093.47	7,174.02	5,114.41	37.43	60.71	90.95	1,280.27	-330.39	1,265.95	1,167.99	97.96	12.923		
6,300.00	5,093.96	7,274.02	5,114.90	39.77	63.15	90.95	1,346.00	-405.75	1,266.48	1,163.72	102.75	12.325		
6,400.00	5,094.45	7,374.02	5,115.39	42.16	65.61	90.95	1,411.73	-481.11	1,267.01	1,159.40	107.60	11.775		
6,500.00	5,094.94	7,474.02	5,115.88	44.58	68.08	90.95	1,477.46	-556.47	1,267.53	1,155.03	112.51	11.266		
6,600.00	5,095.42	7,574.02	5,116.37	47.03	70.57	90.95	1,543.19	-631.83	1,268.06	1,150.61	117.45	10.797		
6,700.00	5,095.91	7,674.02	5,116.87	49.50	73.08	90.95	1,608.91	-707.19	1,268.59	1,146.16	122.43	10.362		
6,800.00	5,096.40	7,774.02	5,117.36	51.99	75.59	90.95	1,674.64	-782.55	1,269.12	1,141.68	127.44	9.959		
6,900.00	5,096.89	7,874.01	5,117.85	54.50	78.12	90.95	1,740.37	-857.91	1,269.65	1,137.17	132.48	9.584		
7,000.00	5,097.37	7,974.01	5,118.34	57.03	80.65	90.95	1,806.10	-933.27	1,270.18	1,132.64	137.54	9.235		
7,100.00	5,097.86	8,074.01	5,118.84	59.57	83.19	90.95	1,871.83	-1,008.63	1,270.71	1,128.08	142.62	8.910		
7,200.00	5,098.35	8,174.01	5,119.33	62.12	85.75	90.95	1,937.56	-1,083.99	1,271.24	1,123.51	147.73	8.605		
7,300.00	5,098.83	8,274.01	5,119.82	64.68	88.30	90.95	2,003.29	-1,159.35	1,271.76	1,118.92	152.85	8.320		
7,400.00	5,099.32	8,374.01	5,120.31	67.25	90.87	90.95	2,069.02	-1,234.71	1,272.29	1,114.31	157.98	8.053		
7,500.00	5,099.81	8,474.01	5,120.80	69.82	93.44	90.95	2,134.75	-1,310.07	1,272.82	1,109.69	163.14	7.802		
7,600.00	5,100.30	8,574.00	5,121.30	72.41	96.02	90.95	2,200.48	-1,385.43	1,273.35	1,105.05	168.30	7.566		
7,700.00	5,100.78	8,674.00	5,121.79	75.00	98.60	90.95	2,266.20	-1,460.79	1,273.88	1,100.41	173.47	7.343		
7,800.00	5,101.27	8,774.00	5,122.28	77.60	101.19	90.95	2,331.93	-1,536.15	1,274.41	1,095.75	178.66	7.133		
7,900.00	5,101.76	8,874.00	5,122.77	80.20	103.78	90.95	2,397.66	-1,611.51	1,274.94	1,091.09	183.85	6.935		
8,000.00	5,102.25	8,974.00	5,123.26	82.80	106.37	90.95	2,463.39	-1,686.87	1,275.47	1,086.41	189.06	6.747		
8,100.00	5,102.73	9,074.00	5,123.76	85.42	108.97	90.95	2,529.12	-1,762.23	1,276.00	1,081.73	194.27	6.568		
8,200.00	5,103.22	9,174.00	5,124.25	88.03	111.57	90.95	2,594.85	-1,837.59	1,276.52	1,077.04	199.49	6.399		
8,300.00	5,103.71	9,273.99	5,124.74	90.65	114.18	90.95	2,660.58	-1,912.95	1,277.05	1,072.34	204.71	6.238		
8,400.00	5,104.20	9,373.99	5,125.23	93.27	116.79	90.95	2,726.31	-1,988.32	1,277.58	1,067.64	209.94	6.085		
8,500.00	5,104.68	9,473.99	5,125.73	95.90	119.40	90.94	2,792.04	-2,063.68	1,278.11	1,062.93	215.18	5.940		
8,600.00	5,105.17	9,573.99	5,126.22	98.53	122.01	90.94	2,857.77	-2,139.04	1,278.64	1,058.22	220.42	5.801		
8,700.00	5,105.66	9,673.99	5,126.71	101.16	124.63	90.94	2,923.49	-2,214.40	1,279.17	1,053.50	225.67	5.668		
8,800.00	5,106.14	9,773.99	5,127.20	103.79	127.25	90.94	2,989.22	-2,289.76	1,279.70	1,048.77	230.92	5.542		
8,900.00	5,106.63	9,873.99	5,127.69	106.43	129.87	90.94	3,054.95	-2,365.12	1,280.23	1,044.05	236.18	5.421		
9,000.00	5,107.12	9,973.98	5,128.19	109.06	132.49	90.94	3,120.68	-2,440.48	1,280.75	1,039.31	241.44	5.305		
9,100.00	5,107.61	10,073.98	5,128.68	111.70	135.11	90.94	3,186.41	-2,515.84	1,281.28	1,034.58	246.70	5.194		
9,200.00	5,108.09	10,173.98	5,129.17	114.35	137.74	90.94	3,252.14	-2,591.20	1,281.81	1,029.84	251.97	5.087		
9,300.00	5,108.58	10,273.98	5,129.66	116.99	140.37	90.94	3,317.87	-2,666.56	1,282.34	1,025.10	257.24	4.985		
9,400.00	5,109.07	10,373.98	5,130.16	119.63	143.00	90.94	3,383.60	-2,741.92	1,282.87	1,020.35	262.52	4.887		
9,500.00	5,109.56	10,473.98	5,130.65	122.28	145.63	90.94	3,449.33	-2,817.28	1,283.40	1,015.60	267.80	4.792		
9,600.00	5,110.04	10,573.98	5,131.14	124.93	148.26	90.94	3,515.06	-2,892.64	1,283.93	1,010.85	273.08	4.702		
9,700.00	5,110.53	10,673.97	5,131.63	127.57	150.90	90.94	3,580.78	-2,968.00	1,284.46	1,006.10	278.36	4.614		
9,800.00	5,111.02	10,773.97	5,132.12	130.22	153.53	90.94	3,646.51	-3,043.36	1,284.98	1,001.34	283.65	4.530		
9,900.00	5,111.50	10,873.97	5,132.62	132.88	156.17	90.94	3,712.24	-3,118.72	1,285.51	996.58	288.93	4.449		
10,000.00	5,111.99	10,973.97	5,133.11	135.53	158.81	90.94	3,777.97	-3,194.08	1,286.04	991.82	294.22	4.371		
10,100.00	5,112.48	11,073.97	5,133.60	138.18	161.45	90.94	3,843.70	-3,269.44	1,286.57	987.06	299.51	4.296		
10,200.00	5,112.97	11,173.97	5,134.09	140.83	164.09	90.94	3,909.43	-3,344.80	1,287.10	982.29	304.81	4.223		
10,300.00	5,113.45	11,273.97	5,134.59	143.49	166.73	90.94	3,975.16	-3,420.16	1,287.63	977.52	310.10	4.152		
10,400.00	5,113.94	11,373.96	5,135.08	146.14	169.37	90.94	4,040.89	-3,495.52	1,288.16	972.76	315.40	4.084		
10,500.00	5,114.43	11,473.96	5,135.57	148.80	172.01	90.94	4,106.62	-3,570.88	1,288.69	967.98	320.70	4.018		
10,600.00	5,114.92	11,573.96	5,136.06	151.46	174.66	90.94	4,172.35	-3,646.24	1,289.22	963.21	326.00	3.955		
10,700.00	5,115.40	11,673.96	5,136.55	154.12	177.30	90.94	4,238.07	-3,721.60	1,289.74	958.44	331.31	3.893		
10,800.00	5,115.89	11,773.96	5,137.05	156.78	179.95	90.94	4,303.80	-3,796.96	1,290.27	953.66	336.61	3.833		
10,900.00	5,116.38	11,873.96	5,137.54	159.43	182.59	90.94	4,369.53	-3,872.32	1,290.80	948.89	341.91	3.775		
11,000.00	5,116.87	11,973.96	5,138.03	162.09	185.24	90.94	4,435.26	-3,947.68	1,291.33	944.11	347.22	3.719		
11,100.00	5,117.35	12,073.96	5,138.52	164.75	187.89	90.94	4,500.99	-4,023.04	1,291.86	939.33	352.53	3.665		
11,200.00	5,117.84	12,173.95	5,139.01	167.42	190.54	90.94	4,566.72	-4,098.40	1,292.39	934.55	357.84	3.612		
11,300.00	5,118.33	12,273.95	5,139.51	170.08	193.19	90.94	4,632.45	-4,173.76	1,292.92	929.77	363.15	3.560		



Lonestar Consulting, LLC
Anticollision Report



Company:	DJR Operating	Local Co-ordinate Reference:	Well # 534H - Slot 1
Project:	North Alamito Unit	TVD Reference:	GL 6875' & RKB 14' @ 6889.00usft
Reference Site:	L29 2307 Pad	MD Reference:	GL 6875' & RKB 14' @ 6889.00usft
Site Error:	0.00 usft	North Reference:	True
Reference Well:	# 534H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	Original Drilling	Database:	DJR
Reference Design:	APD	Offset TVD Reference:	Offset Datum

Offset Design													L29 2307 Pad - # 236H - Original Drilling - APD		Offset Site Error:		0.00 usft	
Survey Program:													0-MWD+HDGM		Offset Well Error:		0.00 usft	
Reference		Offset		Semi Major Axis			Distance							Warning				
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor						
11,400.00	5,118.81	12,373.95	5,140.00	172.74	195.84	90.94	4,698.18	-4,249.13	1,293.45	924.99	368.46	3.510						
11,500.00	5,119.30	12,473.95	5,140.49	175.40	198.49	90.94	4,763.91	-4,324.49	1,293.97	920.20	373.77	3.462						
11,600.00	5,119.79	12,573.95	5,140.98	178.07	201.14	90.94	4,829.64	-4,399.85	1,294.50	915.42	379.09	3.415						
11,643.31	5,120.00	12,617.25	5,141.20	179.22	202.29	90.94	4,858.10	-4,432.48	1,294.73	913.34	381.39	3.395 SF						



Lonestar Consulting, LLC
Anticollision Report



Company:	DJR Operating	Local Co-ordinate Reference:	Well # 534H - Slot 1
Project:	North Alamito Unit	TVD Reference:	GL 6875' & RKB 14' @ 6889.00usft
Reference Site:	L29 2307 Pad	MD Reference:	GL 6875' & RKB 14' @ 6889.00usft
Site Error:	0.00 usft	North Reference:	True
Reference Well:	# 534H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	Original Drilling	Database:	DJR
Reference Design:	APD	Offset TVD Reference:	Offset Datum

Reference Depths are relative to GL 6875' & RKB 14' @ 6889.00usft


Offset Depths are relative to Offset Datum

Central Meridian is -107.83333333

Coordinates are relative to: # 534H - Slot 1

Coordinate System is US State Plane 1983, New Mexico Western Zone

Grid Convergence at Surface is: 0.14°

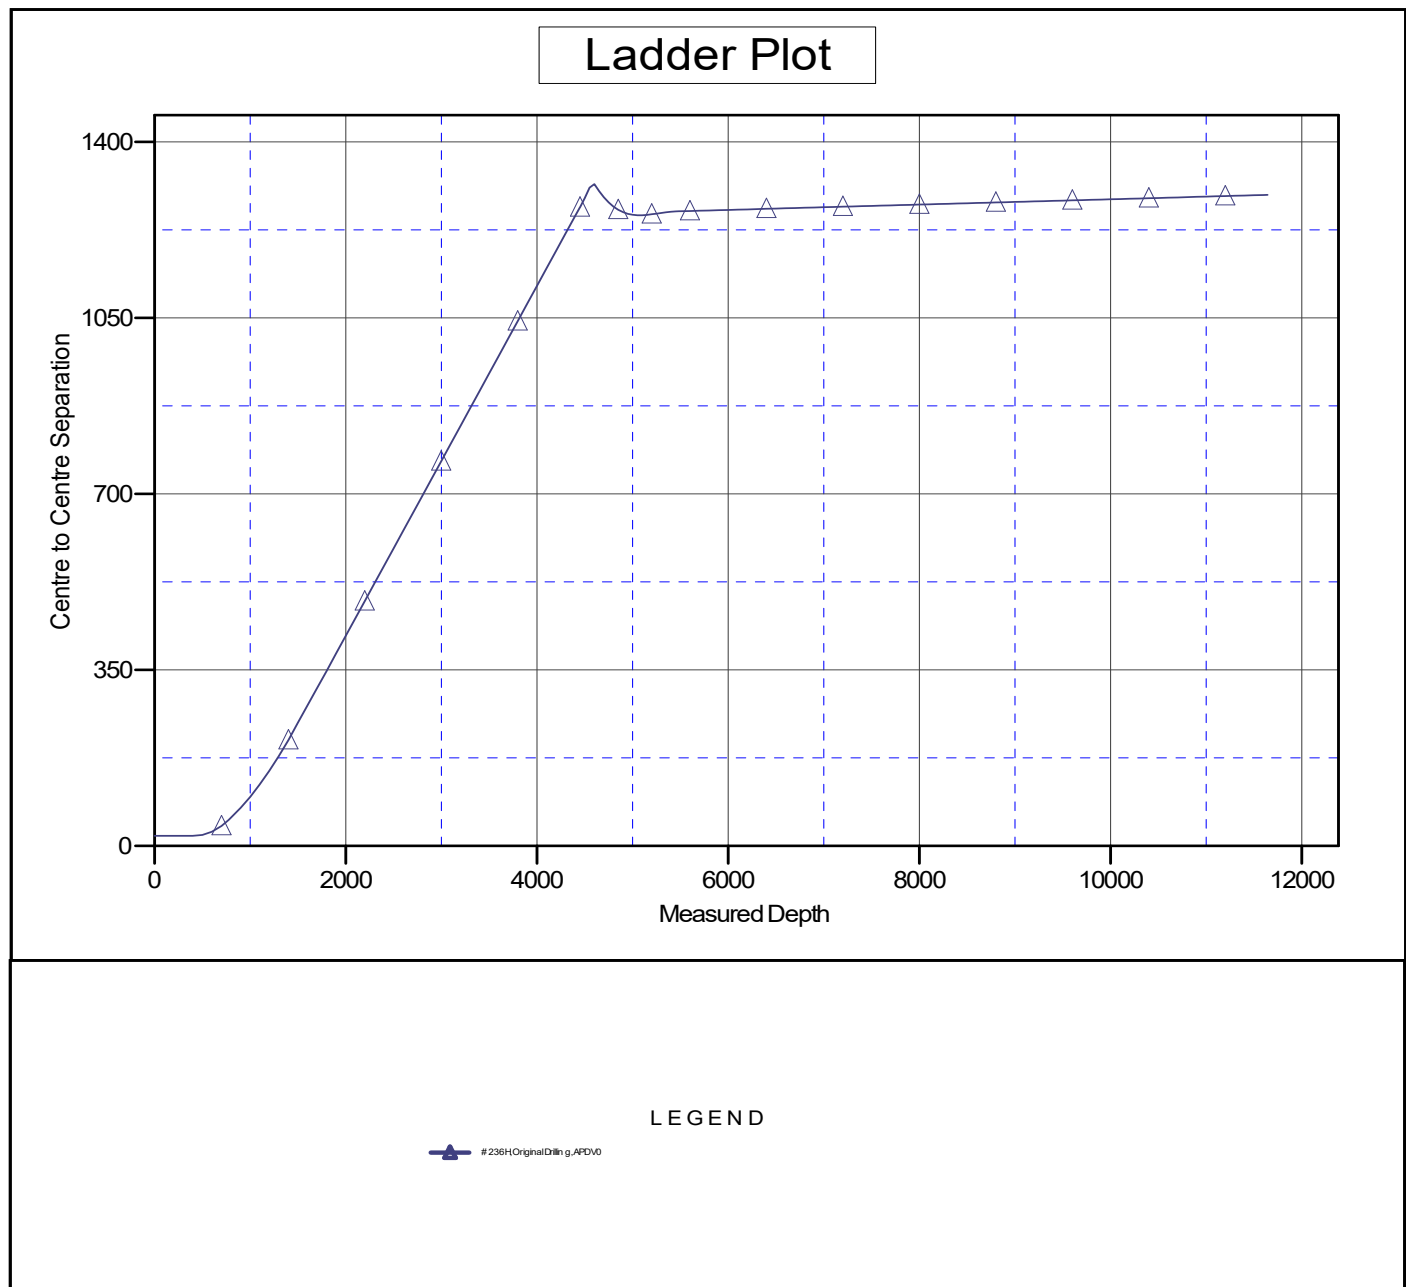



Lonestar Consulting, LLC
Anticollision Report



Company:	DJR Operating	Local Co-ordinate Reference:	Well # 534H - Slot 1
Project:	North Alamito Unit	TVD Reference:	GL 6875' & RKB 14' @ 6889.00usft
Reference Site:	L29 2307 Pad	MD Reference:	GL 6875' & RKB 14' @ 6889.00usft
Site Error:	0.00 usft	North Reference:	True
Reference Well:	# 534H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	Original Drilling	Database:	DJR
Reference Design:	APD	Offset TVD Reference:	Offset Datum

Reference Depths are relative to GL 6875' & RKB 14' @ 6889.00usft

Offset Depths are relative to Offset Datum


Central Meridian is -107.8333333

Coordinates are relative to: # 534H - Slot 1

Coordinate System is US State Plane 1983, New Mexico Western Zone

Grid Convergence at Surface is: 0.14°

Separation Factor Plot

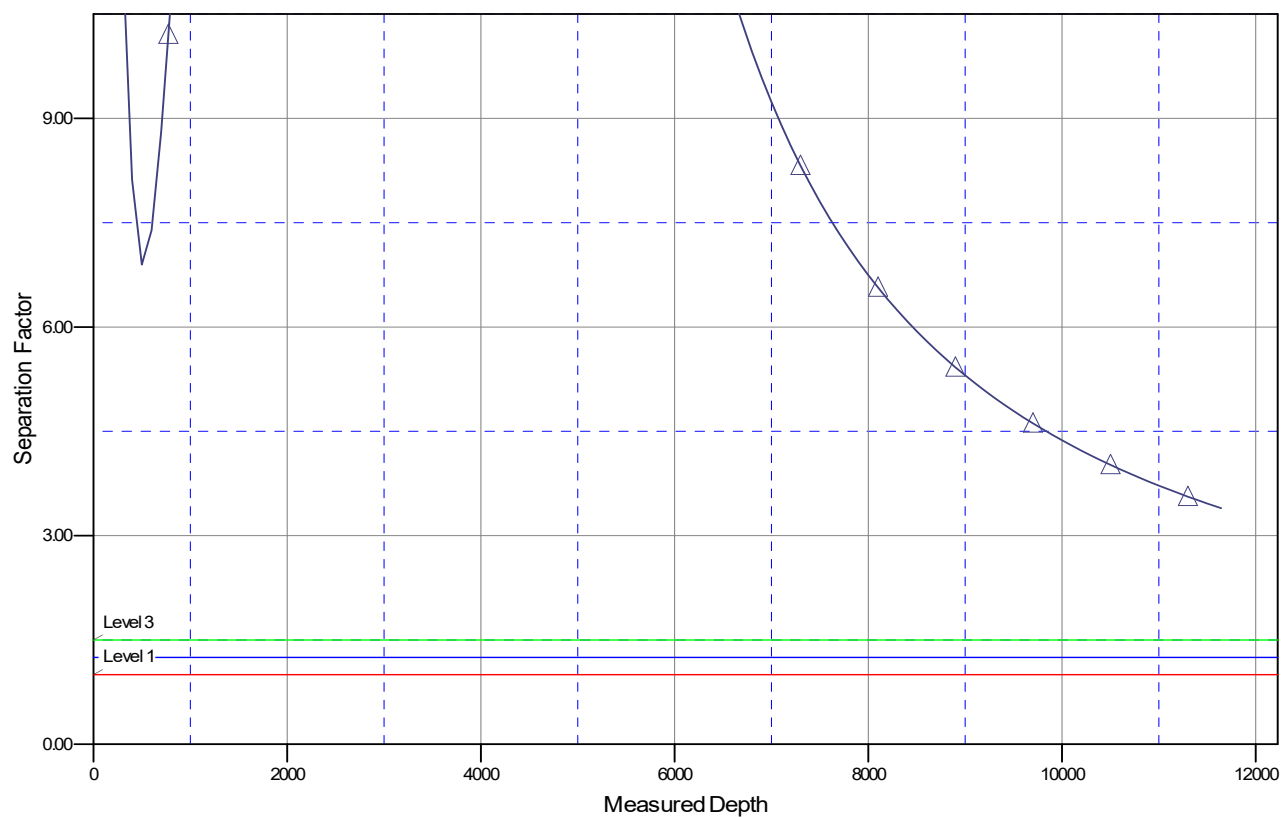

LEGEND

 # 236H Original Drilling APDVO

District I

1625 N. French Dr., Hobbs, NM 88240
Phone:(575) 393-6161 Fax:(575) 393-0720

District II

811 S. First St., Artesia, NM 88210
Phone:(575) 748-1283 Fax:(575) 748-9720

District III

1000 Rio Brazos Rd., Aztec, NM 87410
Phone:(505) 334-6178 Fax:(505) 334-6170

District IV

1220 S. St Francis Dr., Santa Fe, NM 87505
Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 144882

CONDITIONS

Operator: DJR OPERATING, LLC 1 Road 3263 Aztec, NM 87410	OGRID: 371838
	Action Number: 144882
	Action Type: [C-101] BLM - Federal/Indian Land Lease (Form 3160-3)

CONDITIONS

Created By	Condition	Condition Date
kpickford	Notify OCD 24 hours prior to casing & cement	9/21/2022
kpickford	Will require a File As Drilled C-102 and a Directional Survey with the C-104	9/21/2022
kpickford	Once the well is spud, to prevent ground water contamination through whole or partial conduits from the surface, the operator shall drill without interruption through the fresh water zone or zones and shall immediately set in cement the water protection string	9/21/2022
kpickford	Cement is required to circulate on both surface and intermediate1 strings of casing	9/21/2022
kpickford	Oil base muds are not to be used until fresh water zones are cased and cemented providing isolation from the oil or diesel. This includes synthetic oils. Oil based mud, drilling fluids and solids must be contained in a steel closed loop system	9/21/2022
