

Form 3160-5
(June 2019)UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENTFORM APPROVED
OMB No. 1004-0137
Expires: October 31, 2021**SUNDRY NOTICES AND REPORTS ON WELLS**
Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.

5. Lease Serial No. NMNM108503

6. If Indian, Allottee or Tribe Name

SUBMIT IN TRIPLICATE - Other instructions on page 2

1. Type of Well

☒ Oil Well ☐ Gas Well ☐ Other

2. Name of Operator EOG RESOURCES INCORPORATED

3a. Address 1111 BAGBY SKY LOBBY 2, HOUSTON, TX 77030 3b. Phone No. (include area code)
(713) 651-70004. Location of Well (Footage, Sec., T., R., M., or Survey Description)
SEC 23/T25S/R33E/NMP

7. If Unit of CA/Agreement, Name and/or No.

8. Well Name and No. CABALLO 23 FED/406H

9. API Well No. 3002550735

10. Field and Pool or Exploratory Area
RED HILLS; LOWER BONE SPRINGS11. Country or Parish, State
LEA/NM

12. CHECK THE APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, REPORT OR OTHER DATA

| TYPE OF SUBMISSION | TYPE OF ACTION | | | | |
|--|---|---|--|---|--|
| <input checked="" type="checkbox"/> Notice of Intent | <input type="checkbox"/> Acidize | <input type="checkbox"/> Deepen | <input type="checkbox"/> Production (Start/Resume) | <input type="checkbox"/> Water Shut-Off | |
| <input type="checkbox"/> Subsequent Report | <input type="checkbox"/> Alter Casing | <input type="checkbox"/> Hydraulic Fracturing | <input type="checkbox"/> Reclamation | <input type="checkbox"/> Well Integrity | |
| <input type="checkbox"/> Final Abandonment Notice | <input type="checkbox"/> Casing Repair | <input type="checkbox"/> New Construction | <input type="checkbox"/> Recomplete | <input checked="" type="checkbox"/> Other | |
| | <input type="checkbox"/> Change Plans | <input type="checkbox"/> Plug and Abandon | <input type="checkbox"/> Temporarily Abandon | | |
| | <input type="checkbox"/> Convert to Injection | <input type="checkbox"/> Plug Back | <input type="checkbox"/> Water Disposal | | |

13. Describe Proposed or Completed Operation: Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recompleat horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports must be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompleat in a new interval, a Form 3160-4 must be filed once testing has been completed. Final Abandonment Notices must be filed only after all requirements, including reclamation, have been completed and the operator has detennined that the site is ready for final inspection.)

EOG respectfully requests an amendment to our approved APD for this well to reflect the following changes:
API #: 30-025-50735

Change name from Caballo 23 Fed 406H to Caballo 23 Fed 204H.

Change BHL from T-25-S, R-33-E, Sec 14, 2540' FSL, 745' FWL, Lea Co., NM,
to T-25-S, R-33-E, Sec 14, 2541' FSL, 880' FWL, Lea Co., N.M.

Change target formation to Leonard B.

Update casing and cement program to current design.

14. I hereby certify that the foregoing is true and correct. Name (Printed/Typed)
STAR HARRELL / Ph: (432) 848-9161

Title Regulatory Specialist

Signature

Date 12/21/2022

THE SPACE FOR FEDERAL OR STATE OFFICE USE

Approved by

KEITH P IMMATTY / Ph: (575) 988-4722 / Approved

Title ENGINEER

Date 01/30/2023

Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Office CARLSBAD

Title 18 U.S.C Section 1001 and Title 43 U.S.C Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Instructions on page 2)

GENERAL INSTRUCTIONS

This form is designed for submitting proposals to perform certain well operations and reports of such operations when completed as indicated on Federal and Indian lands pursuant to applicable Federal law and regulations. Any necessary special instructions concerning the use of this form and the number of copies to be submitted, particularly with regard to local area or regional procedures and practices, are either shown below, will be issued by or may be obtained from the local Federal office.

SPECIFIC INSTRUCTIONS

Item 4 - Locations on Federal or Indian land should be described in accordance with Federal requirements. Consult the local Federal office for specific instructions.

Item 13: Proposals to abandon a well and subsequent reports of abandonment should include such special information as is required by the local Federal office. In addition, such proposals and reports should include reasons for the abandonment; data on any former or present productive zones or other zones with present significant fluid contents not sealed off by cement or otherwise; depths (top and bottom) and method of placement of cement plugs; mud or other material placed below, between and above plugs; amount, size, method of parting of any casing, liner or tubing pulled and the depth to the top of any tubing left in the hole; method of closing top of well and date well site conditioned for final inspection looking for approval of the abandonment. If the proposal will involve **hydraulic fracturing operations**, you must comply with 43 CFR 3162.3-3, including providing information about the protection of usable water. Operators should provide the best available information about all formations containing water and their depths. This information could include data and interpretation of resistivity logs run on nearby wells. Information may also be obtained from state or tribal regulatory agencies and from local BLM offices.

NOTICES

The privacy Act of 1974 and the regulation in 43 CFR 2.48(d) provide that you be furnished the following information in connection with information required by this application.

AUTHORITY: 30 U.S.C. 181 et seq., 351 et seq., 25 U.S.C. 396; 43 CFR 3160.

PRINCIPAL PURPOSE: The information is used to: (1) Evaluate, when appropriate, approve applications, and report completion of subsequent well operations, on a Federal or Indian lease; and (2) document for administrative use, information for the management, disposal and use of National Resource lands and resources, such as: (a) evaluating the equipment and procedures to be used during a proposed subsequent well operation and reviewing the completed well operations for compliance with the approved plan; (b) requesting and granting approval to perform those actions covered by 43 CFR 3162.3-2, 3162.3-3, and 3162.3-4; (c) reporting the beginning or resumption of production, as required by 43 CFR 3162.4-1(c) and (d) analyzing future applications to drill or modify operations in light of data obtained and methods used.

ROUTINE USES: Information from the record and/or the record will be transferred to appropriate Federal, State, local or foreign agencies, when relevant to civil, criminal or regulatory investigations or prosecutions in connection with congressional inquiries or to consumer reporting agencies to facilitate collection of debts owed the Government.

EFFECT OF NOT PROVIDING THE INFORMATION: Filing of this notice and report and disclosure of the information is mandatory for those subsequent well operations specified in 43 CFR 3162.3-2, 3162.3-3, 3162.3-4.

The Paperwork Reduction Act of 1995 requires us to inform you that:

The BLM collects this information to evaluate proposed and/or completed subsequent well operations on Federal or Indian oil and gas leases.

Response to this request is mandatory.

The BLM would like you to know that you do not have to respond to this or any other Federal agency-sponsored information collection unless it displays a currently valid OMB control number.

BURDEN HOURS STATEMENT: Public reporting burden for this form is estimated to average 8 hours per response, including the time for reviewing instructions, gathering and maintaining data, and completing and reviewing the form. Direct comments regarding the burden estimate or any other aspect of this form to U.S. Department of the Interior, Bureau of Land Management (1004-0137), Bureau Information Collection Clearance Officer (WO-630), 1849 C St., N.W., Mail Stop 401 LS, Washington, D.C. 20240

Additional Information

Location of Well

0. SHL: TR M / 434 FSL / 335 FWL / TWSP: 25S / RANGE: 33E / SECTION: 23 / LAT: 32.1099714 / LONG: -103.5505751 (TVD: 0 feet, MD: 0 feet)

PPP: TR M / 100 FSL / 745 FWL / TWSP: 25S / RANGE: 33E / SECTION: 23 / LAT: 32.1090521 / LONG: -103.5492524 (TVD: 10262 feet, MD: 10295 feet)

BHL: TR L / 2540 FSL / 745 FWL / TWSP: 25S / RANGE: 33E / SECTION: 14 / LAT: 32.1302747 / LONG: -103.5492498 (TVD: 10527 feet, MD: 18117 feet)

District I
1625 N. French Dr., Hobbs, NM 88240
Phone: (575) 393-6161 Fax: (575) 393-0720

District II
811 S. First St., Artesia, NM 88210
Phone: (575) 748-1283 Fax: (575) 748-9720

District III
1000 Rio Brazos Road, Aztec, NM 87410
Phone: (505) 334-6178 Fax: (505) 334-6170

District IV
1220 S. St. Francis Dr., Santa Fe, NM 87505
Phone: (505) 476-3460 Fax: (505) 476-3462

State of New Mexico
Energy, Minerals & Natural Resources
Department
OIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, NM 87505

FORM C-102

Revised August 1, 2011

Submit one copy to appropriate

District Office

☐ **AMENDED REPORT**

WELL LOCATION AND ACREAGE DEDICATION PLAT

| | | |
|--|--|---|
| ¹ API Number 30-025-50735 | ² Pool Code 51020 | ³ Pool Name Red Hills; Lower Bone Spring |
| ⁴ Property Code 38481 | ⁵ Property Name CABALLO 23 FED | |
| ⁷ OGRID No. 7377 | ⁸ Operator Name EOG RESOURCES, INC. | ⁶ Well Number 204H |
| | | ⁹ Elevation 3341' |

¹⁰Surface Location


| | | | | | | | | | |
|---------------|-----------|-------------|-------------|----------|---------------|------------------|---------------|----------------|------------|
| UL or lot no. | Section | Township | Range | Lot Idn | Feet from the | North/South line | Feet from the | East/West line | County |
| M | 23 | 25-S | 33-E | - | 434' | SOUTH | 335' | WEST | LEA |

¹¹Bottom Hole Location If Different From Surface

| UL or lot no. | Section | Township | Range | Lot Idn | Feet from the | North/South line | Feet from the | East/West line | County |
|---------------|---------|----------|-------|---------|---------------|------------------|---------------|----------------|--------|
| L | 14 | 25-S | 33-E | - | 2541' | SOUTH | 880' | WEST | LEA |

| | | | |
|--|-------------------------------|----------------------------------|-------------------------|
| ¹² Dedicated Acres 480.00 | ¹³ Joint or Infill | ¹⁴ Consolidation Code | ¹⁵ Order No. |
|--|-------------------------------|----------------------------------|-------------------------|

No allowable will be assigned to this completion until all interests have been consolidated or a non-standard unit has been approved by the division.

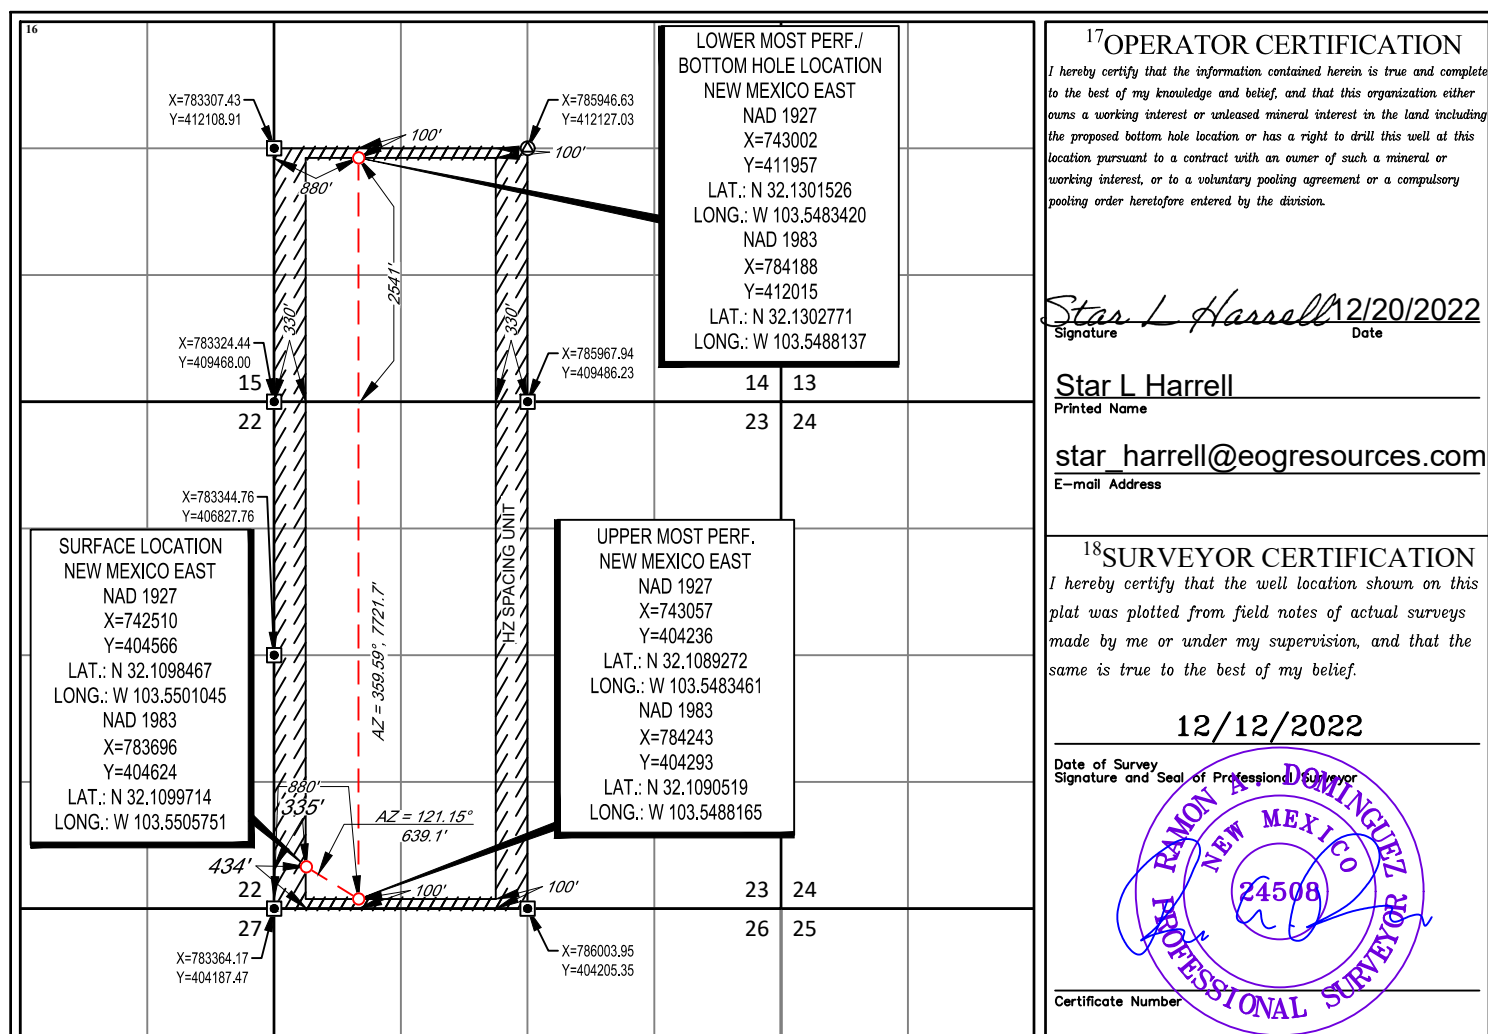



Caballo 23 Fed 204H

Revised Permit Information 11/30/2022:

Well Name: Caballo 23 Fed 204H

Location: SHL: 434' FSL & 335' FWL, Section 23, T-25-S, R-33-E, Lea Co., N.M.

BHL: 2541' FSL & 880' FWL, Section 14, T-25-S, R-33-E, Lea Co., N.M.

Casing Program A:

| Hole Size | Interval MD | | Interval TVD | | Csg OD | Weight | Grade | Conn |
|-----------|-------------|---------|--------------|---------|---------|--------|---------|------|
| | From (ft) | To (ft) | From (ft) | To (ft) | | | | |
| 16" | 0 | 1,070 | 0 | 1,070 | 13-3/8" | 54.5# | J-55 | STC |
| 11" | 0 | 4,037 | 0 | 4,000 | 9-5/8" | 40# | J-55 | LTC |
| 11" | 4,037 | 5,067 | 4,000 | 5,030 | 9-5/8" | 40# | HCK-55 | LTC |
| 6-3/4" | 0 | 17,181 | 0 | 9,578 | 5-1/2" | 17# | HCP-110 | LTC |

Variance is requested to waive the centralizer requirements for the 9-5/8" casing in the 11" hole size. An expansion additive will be utilized, in the cement slurry, for the entire length of the 11" hole interval to maximize cement bond and zonal isolation.

Variance is also requested to waive any centralizer requirements for the 5-1/2" casing in the 6-3/4" hole size. An expansion additive will be utilized, in the cement slurry, for the entire length of the 6-3/4" hole interval to maximize cement bond and zonal isolation.

EOG requests permission to allow deviation from the 0.422" annulus clearance requirement for the intermediate (salt) section from Onshore Order #2 under the following conditions:

- The variance is not applicable within the Potash Boundaries or Capitan Reef areas.
- Operator takes responsibility to get casing to set point in the event that the clearance causes stuck pipe issues.

Cementing Program:

| Depth | No. Sacks | Wt. ppg | Yld Ft3/sk | Slurry Description |
|-------------------|-----------|---------|------------|---|
| 1,070' 13-3/8" | 320 | 13.5 | 1.73 | Lead: Class C + 4.0% Bentonite Gel + 0.5% CaCl ₂ + 0.25 lb/sk Cello-Flake (TOC @ Surface) |
| | 100 | 14.8 | 1.34 | Tail: Class C + 0.6% FL-62 + 0.25 lb/sk Cello-Flake + 0.2% Sodium Metasilicate (TOC @ 870') |
| 5,030' 9-5/8" | 470 | 12.7 | 2.22 | Lead: Class C + 10% NaCl + 6% Bentonite Gel + 3% MagOx (TOC @ Surface) |
| | 170 | 14.8 | 1.32 | Tail: Class C + 10% NaCl + 3% MagOx (TOC @ 4,020') |
| 17,181' 5-1/2" | 330 | 11.0 | 3.21 | Lead: Class H + 0.4% Halad-344 + 0.35% HR-601 + 3% Microbond (TOC @ 4,530') |
| | 570 | 13.2 | 1.52 | Tail: Class H + 5% NEX-020 + 0.2% NAC-102 + 0.15% NAS-725 + 0.5% NFL-549 + 0.2% NFP-703 + 1% NBE-737 + 0.3% NRT-241 (TOC @ 9140') |



Caballo 23 Fed 204H

| Additive | Purpose |
|---------------------|---|
| Bentonite Gel | Lightweight/Lost circulation prevention |
| Calcium Chloride | Accelerator |
| Cello-flake | Lost circulation prevention |
| Sodium Metasilicate | Accelerator |
| MagOx | Expansive agent |
| Pre-Mag-M | Expansive agent |
| Sodium Chloride | Accelerator |
| FL-62 | Fluid loss control |
| Halad-344 | Fluid loss control |
| Halad-9 | Fluid loss control |
| HR-601 | Retarder |
| Microbond | Expansive Agent |

Note: Cement volumes based on bit size plus at least 25% excess in the open hole plus 10% excess in the cased-hole overlap section.

Mud Program:

| Depth (TVD) | Type | Weight (ppg) | Viscosity | Water Loss |
|------------------|-------------|--------------|-----------|------------|
| 0 – 1,070' | Fresh - Gel | 8.6-8.8 | 28-34 | N/c |
| 1,070' – 5,030' | Brine | 8.6-8.8 | 28-34 | N/c |
| 5,030' – 17,181' | Oil Base | 8.8-9.5 | 58-68 | N/c - 6 |

Wellhead & Offline Cementing:

EOG Resources Inc. (EOG) respectfully requests a variance from the minimum standards for well control equipment testing of Onshore Order No. 2 (item III.A.2.a.i) to allow a testing schedule of the blow out preventer (BOP) and blow out prevention equipment (BOPE) along with Batch Drilling & Offline cement operations to include the following:

- Full BOPE test at first installation on the pad.
- Full BOPE test every 21 days per Onshore Order No. 2.
- Function test BOP elements per Onshore Order No. 2.
- Break testing BOP and BOPE coupled with batch drilling operations and option to offline cement and/or remediate (if needed) any surface or intermediate sections, according to attached offline cementing support documentation.
- After the well section is secured, the BOP will be disconnected from the wellhead and walked with the rig to another well on the pad.
- TA cap will also be installed per Wellhead vendor procedure and pressure inside the casing will be monitored via the valve on the TA cap as per standard batch drilling ops.
- See attached "EOG BLM Variance 3a -Offline Cement Intermediate Operational Procedure"




434' FSL
335' FWL
Section 23
T-25-S, R-33-E

Revised Wellbore A:

KB: 3366'
GL: 3341'

API: 30-025-50735

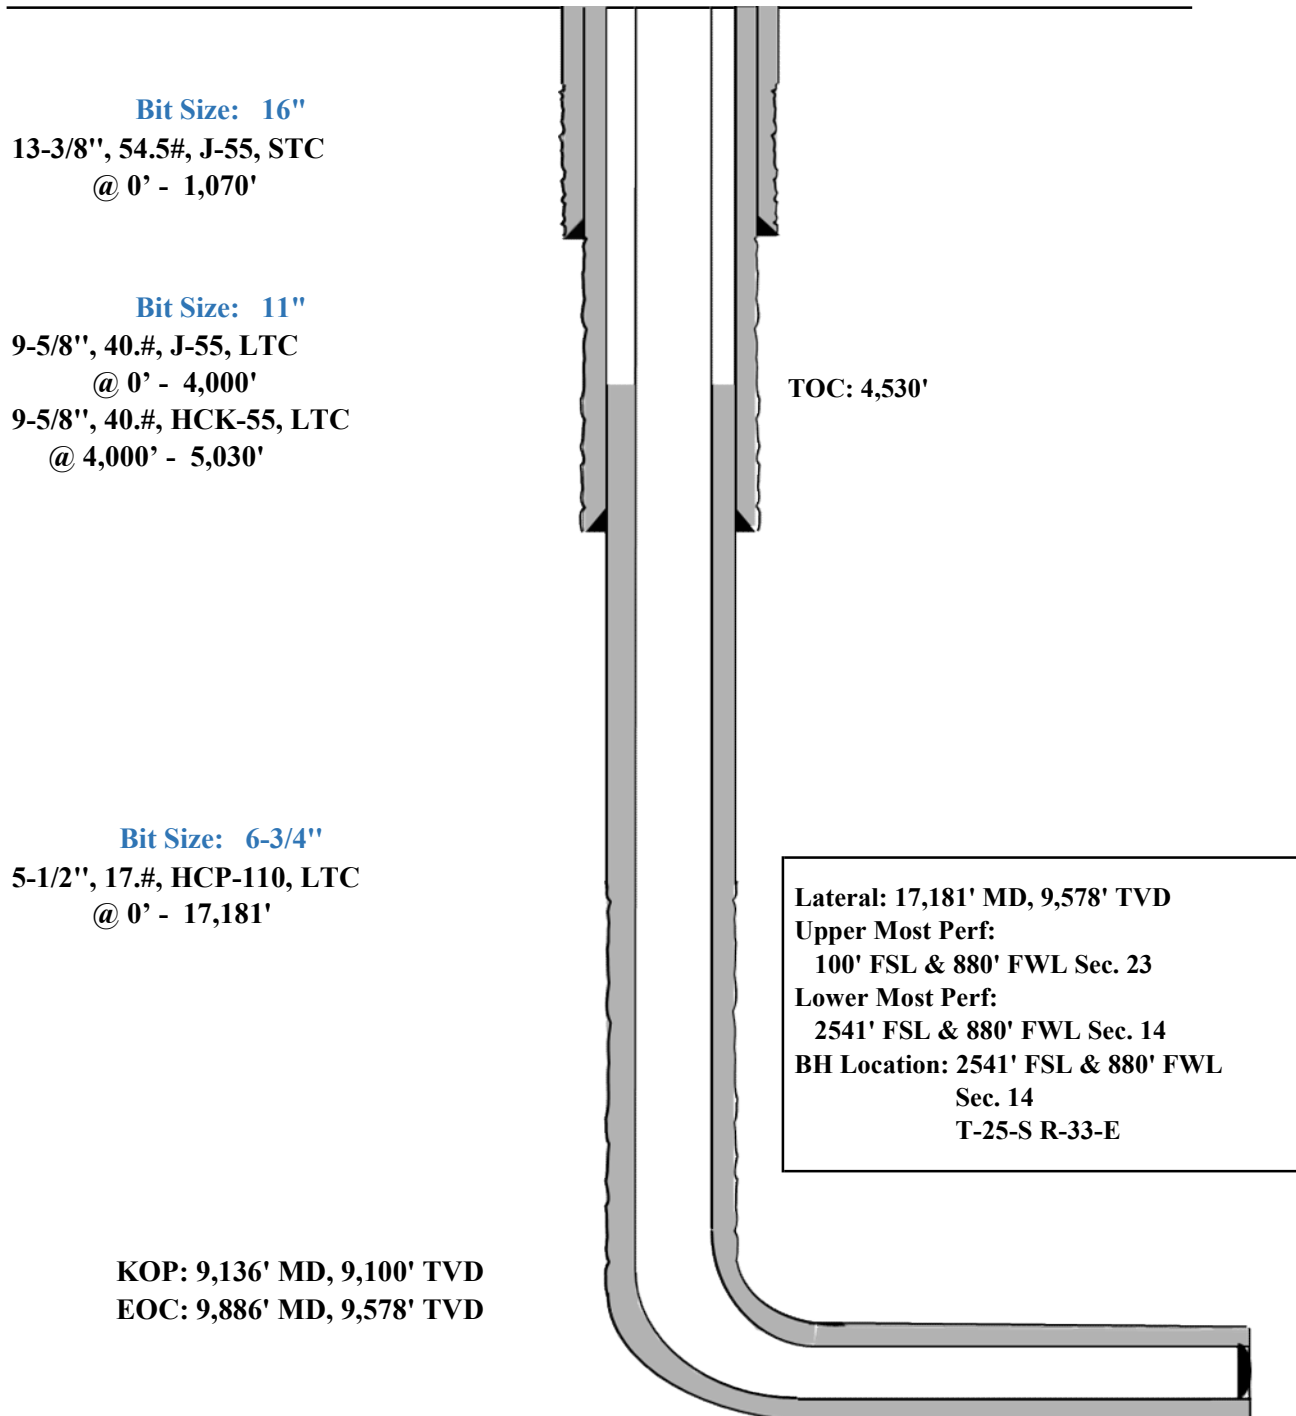



Caballo 23 Fed 204H

Revised Permit Information 11/30/2022:

Well Name: Caballo 23 Fed 204H

Location: SHL: 434' FSL & 335' FWL, Section 23, T-25-S, R-33-E, Lea Co., N.M.

BHL: 2541' FSL & 880' FWL, Section 14, T-25-S, R-33-E, Lea Co., N.M.

Casing Program B:

| Hole Size | Interval MD | | Interval TVD | | Csg OD | Weight | Grade | Conn |
|-----------|-------------|---------|--------------|---------|---------|--------|---------|--------|
| | From (ft) | To (ft) | From (ft) | To (ft) | | | | |
| 13-1/2" | 0 | 1,070 | 0 | 1,070 | 10-3/4" | 40.5# | J-55 | STC |
| 9-7/8" | 0 | 4,037 | 0 | 4,000 | 8-5/8" | 32# | J-55 | BTC-SC |
| 9-7/8" | 4,037 | 5,067 | 4,000 | 5,030 | 8-5/8" | 32# | P110-EC | BTC-SC |
| 6-3/4" | 0 | 17,181 | 0 | 9,578 | 5-1/2" | 17# | HCP-110 | LTC |

Cementing Program:

| Depth | No. Sacks | Wt. ppg | Yld Ft3/sk | Slurry Description |
|-------------------|-----------|---------|------------|---|
| 1,070' 10-3/4" | 360 | 13.5 | 1.73 | Lead: Class C + 4.0% Bentonite Gel + 0.5% CaCl ₂ + 0.25 lb/sk Cello-Flake (TOC @ Surface) |
| | 110 | 14.8 | 1.34 | Tail: Class C + 0.6% FL-62 + 0.25 lb/sk Cello-Flake + 0.2% Sodium Metasilicate (TOC @ 870') |
| 5,030' 8-5/8" | 340 | 12.7 | 2.22 | Lead: Class C + 10% NaCl + 6% Bentonite Gel + 3% MagOx (TOC @ Surface) |
| | 160 | 14.8 | 1.32 | Tail: Class C + 10% NaCl + 3% MagOx (TOC @ 4,020') |
| 17,181' 5-1/2" | 480 | 11.0 | 3.21 | Lead: Class H + 0.4% Halad-344 + 0.35% HR-601 + 3% Microbond (TOC @ 4,530') |
| | 590 | 13.2 | 1.52 | Tail: Class H + 5% NEX-020 + 0.2% NAC-102 + 0.15% NAS-725 + 0.5% NFL-549 + 0.2% NFP-703 + 1% NBE-737 + 0.3% NRT-241 (TOC @ 9140') |



Caballo 23 Fed 204H

| Additive | Purpose |
|---------------------|---|
| Bentonite Gel | Lightweight/Lost circulation prevention |
| Calcium Chloride | Accelerator |
| Cello-flake | Lost circulation prevention |
| Sodium Metasilicate | Accelerator |
| MagOx | Expansive agent |
| Pre-Mag-M | Expansive agent |
| Sodium Chloride | Accelerator |
| FL-62 | Fluid loss control |
| Halad-344 | Fluid loss control |
| Halad-9 | Fluid loss control |
| HR-601 | Retarder |
| Microbond | Expansive Agent |

Wellhead & Offline Cementing:

EOG Resources Inc. (EOG) respectfully requests a variance from the minimum standards for well control equipment testing of Onshore Order No. 2 (item III.A.2.a.i) to allow a testing schedule of the blow out preventer (BOP) and blow out prevention equipment (BOPE) along with Batch Drilling & Offline cement operations to include the following:

- Full BOPE test at first installation on the pad.
- Full BOPE test every 21 days per Onshore Order No. 2.
- Function test BOP elements per Onshore Order No. 2.
- Break testing BOP and BOPE coupled with batch drilling operations and option to offline cement and/or remediate (if needed) any surface or intermediate sections, according to attached offline cementing support documentation.
- After the well section is secured, the BOP will be disconnected from the wellhead and walked with the rig to another well on the pad.
- TA cap will also be installed per Wellhead vendor procedure and pressure inside the casing will be monitored via the valve on the TA cap as per standard batch drilling ops.
- See attached "EOG BLM Variance 3a -Offline Cement Intermediate Operational Procedure"



434'
335'
Section 23
T-25-S, R-33-E

Revised Wellbore B:

API: 30-025-50735

KB: 3366'
GL: 3341'

Bit Size: 13-1/2"
10-3/4", 40.5#, J-55, STC
@ 0' - 1,070'

Bit Size: 9-7/8"
8-5/8", 32.#, J-55, BTC-SC
@ 0' - 4,000'
8-5/8", 32.#, P110-EC, BTC-SC
@ 4,000' - 5,030'

TOC: 4,530'

Bit Size: 6-3/4"
5-1/2", 17.#, HCP-110, LTC
@ 0' - 17,181'

Lateral: 17,181' MD, 9,578' TVD
Upper Most Perf:
100' FSL & 880' FWL Sec. 23
Lower Most Perf:
2541' FSL & 880' FWL Sec. 14
BH Location: 2541' FSL & 880'
FWL

Sec. 14
T-25-S R-33-E

KOP: 9,136' MD, 9,100' TVD
EOC: 9,886' MD, 9,578' TVD

**GEOLOGIC NAME OF SURFACE FORMATION:**

Permian

ESTIMATED TOPS OF IMPORTANT GEOLOGICAL MARKERS:

| | |
|------------------------|---------|
| Rustler | 954' |
| Tamarisk Anhydrite | 1,045' |
| Top of Salt | 1,342' |
| Base of Salt | 4,934' |
| Lamar | 5,041' |
| Bell Canyon | 5,079' |
| Cherry Canyon | 6,117' |
| Brushy Canyon | 7,702' |
| Bone Spring Lime | 9,235' |
| Leonard (Avalon) Shale | 9,261' |
| 1st Bone Spring Sand | 10,195' |
| 2nd Bone Spring Shale | 10,392' |
| 2nd Bone Spring Sand | 10,741' |
| 3rd Bone Spring Carb | 11,220' |
| 3rd Bone Spring Sand | 11,813' |
| TD | 9,578' |

ESTIMATED DEPTHS OF ANTICIPATED FRESH WATER, OIL OR GAS:

| | | |
|------------------------|---------|-------------|
| Upper Permian Sands | 0- 400' | Fresh Water |
| Bell Canyon | 5,079' | Oil |
| Cherry Canyon | 6,117' | Oil |
| Brushy Canyon | 7,702' | Oil |
| Leonard (Avalon) Shale | 9,261' | Oil |
| 1st Bone Spring Sand | 10,195' | Oil |
| 2nd Bone Spring Shale | 10,392' | Oil |
| 2nd Bone Spring Sand | 10,741' | Oil |



Midland

Lea County, NM (NAD 83 NME)

Caballo 23 Fed

#204H

OH

Plan: Plan #0.2

Standard Planning Report

21 December, 2022



Planning Report

| | | | |
|------------------|-----------------------------|-------------------------------------|-----------------------|
| Database: | PEDM | Local Co-ordinate Reference: | Well #204H |
| Company: | Midland | TVD Reference: | kb = 25' @ 3367.0usft |
| Project: | Lea County, NM (NAD 83 NME) | MD Reference: | kb = 25' @ 3367.0usft |
| Site: | Caballo 23 Fed | North Reference: | Grid |
| Well: | #204H | Survey Calculation Method: | Minimum Curvature |
| Wellbore: | OH | | |
| Design: | Plan #0.2 | | |

| | | | |
|--------------------|-----------------------------|----------------------|----------------|
| Project | Lea County, NM (NAD 83 NME) | | |
| Map System: | US State Plane 1983 | System Datum: | Mean Sea Level |
| Geo Datum: | North American Datum 1983 | | |
| Map Zone: | New Mexico Eastern Zone | | |

| | | | | | |
|-----------------------|----------------|--------------|-----------------|------------|-------------------|
| Site | Caballo 23 Fed | | | | |
| Site Position: | | Northing: | 404,499.00 usft | Latitude: | 32° 6' 34.558 N |
| From: | Map | Easting: | 785,117.00 usft | Longitude: | 103° 32' 45.566 W |
| Position Uncertainty: | 0.0 usft | Slot Radius: | 13-3/16 " | | |

| | | | | | | |
|----------------------|-------|----------|---------------------|-----------------|---------------|------------------|
| Well | #204H | | | | | |
| Well Position | +N/-S | 0.0 usft | Northing: | 404,624.00 usft | Latitude: | 32° 6' 35.897 N |
| | +E/-W | 0.0 usft | Easting: | 783,696.00 usft | Longitude: | 103° 33' 2.076 W |
| Position Uncertainty | | 0.0 usft | Wellhead Elevation: | usft | Ground Level: | 3,342.0 usft |
| Grid Convergence: | | 0.42 ° | | | | |

| | | | | | |
|------------------|-------------------|--------------------|------------------------|----------------------|----------------------------|
| Wellbore | OH | | | | |
| Magnetics | Model Name | Sample Date | Declination (°) | Dip Angle (°) | Field Strength (nT) |
| | IGRF2020 | 9/9/2021 | 6.50 | 59.79 | 47,404.77761372 |

| | | | | | |
|--------------------------|--------------------------------|---------------------|----------------------|----------------------|--|
| Design | Plan #0.2 | | | | |
| Audit Notes: | | | | | |
| Version: | Phase: | PLAN | Tie On Depth: | 0.0 | |
| Vertical Section: | Depth From (TVD) (usft) | +N/-S (usft) | +E/-W (usft) | Direction (°) | |
| | 0.0 | 0.0 | 0.0 | 3.81 | |

| | | | | | |
|---------------------------------|------------------------|--------------------------|------------------|----------------|--|
| Plan Survey Tool Program | Date | 12/21/2022 | | | |
| Depth From (usft) | Depth To (usft) | Survey (Wellbore) | Tool Name | Remarks | |
| 1 | 0.0 | 17,181.2 Plan #0.2 (OH) | EOG MWD+IFR1 | | |
| | | | MWD + IFR1 | | |



Planning Report

| | | | |
|------------------|-----------------------------|-------------------------------------|-----------------------|
| Database: | PEDM | Local Co-ordinate Reference: | Well #204H |
| Company: | Midland | TVD Reference: | kb = 25' @ 3367.0usft |
| Project: | Lea County, NM (NAD 83 NME) | MD Reference: | kb = 25' @ 3367.0usft |
| Site: | Caballo 23 Fed | North Reference: | Grid |
| Well: | #204H | Survey Calculation Method: | Minimum Curvature |
| Wellbore: | OH | | |
| Design: | Plan #0.2 | | |

| Plan Sections | | | | | | | | | | |
|-----------------------|-----------------|-------------|-----------------------|--------------|--------------|-------------------------|------------------------|-----------------------|---------|----------------------|
| Measured Depth (usft) | Inclination (°) | Azimuth (°) | Vertical Depth (usft) | +N/-S (usft) | +E/-W (usft) | Dogleg Rate (°/100usft) | Build Rate (°/100usft) | Turn Rate (°/100usft) | TFO (°) | Target |
| 0.0 | 0.00 | 0.00 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 | 0.00 | |
| 1,300.0 | 0.00 | 0.00 | 1,300.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 | 0.00 | |
| 1,614.5 | 6.29 | 124.86 | 1,613.9 | -9.9 | 14.2 | 2.00 | 2.00 | 0.00 | 124.86 | |
| 7,383.5 | 6.29 | 124.86 | 7,348.1 | -371.1 | 532.8 | 0.00 | 0.00 | 0.00 | 0.00 | |
| 7,698.0 | 0.00 | 0.00 | 7,662.0 | -381.0 | 547.0 | 2.00 | -2.00 | 0.00 | 180.00 | |
| 9,136.5 | 0.00 | 0.00 | 9,100.5 | -381.0 | 547.0 | 0.00 | 0.00 | 0.00 | 0.00 | KOP(Caballo 23 Fed : |
| 9,356.9 | 26.46 | 0.00 | 9,313.2 | -331.0 | 547.0 | 12.00 | 12.00 | 0.00 | 0.00 | FTP(Caballo 23 Fed # |
| 9,886.5 | 90.00 | 359.58 | 9,577.9 | 96.5 | 544.9 | 12.00 | 12.00 | -0.08 | -0.46 | |
| 17,181.2 | 90.00 | 359.58 | 9,578.0 | 7,391.0 | 492.0 | 0.00 | 0.00 | 0.00 | 0.00 | PBHL(Caballo 23 Fed |



Planning Report

| | | | |
|------------------|-----------------------------|-------------------------------------|-----------------------|
| Database: | PEDM | Local Co-ordinate Reference: | Well #204H |
| Company: | Midland | TVD Reference: | kb = 25' @ 3367.0usft |
| Project: | Lea County, NM (NAD 83 NME) | MD Reference: | kb = 25' @ 3367.0usft |
| Site: | Caballo 23 Fed | North Reference: | Grid |
| Well: | #204H | Survey Calculation Method: | Minimum Curvature |
| Wellbore: | OH | | |
| Design: | Plan #0.2 | | |

| Planned Survey | | | | | | | | | |
|-----------------------|-----------------|-------------|-----------------------|--------------|--------------|-------------------------|-------------------------|------------------------|-----------------------|
| Measured Depth (usft) | Inclination (°) | Azimuth (°) | Vertical Depth (usft) | +N/-S (usft) | +E/-W (usft) | Vertical Section (usft) | Dogleg Rate (°/100usft) | Build Rate (°/100usft) | Turn Rate (°/100usft) |
| 0.0 | 0.00 | 0.00 | 0.0 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 |
| 100.0 | 0.00 | 0.00 | 100.0 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 |
| 200.0 | 0.00 | 0.00 | 200.0 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 |
| 300.0 | 0.00 | 0.00 | 300.0 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 |
| 400.0 | 0.00 | 0.00 | 400.0 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 |
| 500.0 | 0.00 | 0.00 | 500.0 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 |
| 600.0 | 0.00 | 0.00 | 600.0 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 |
| 700.0 | 0.00 | 0.00 | 700.0 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 |
| 800.0 | 0.00 | 0.00 | 800.0 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 |
| 900.0 | 0.00 | 0.00 | 900.0 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 |
| 1,000.0 | 0.00 | 0.00 | 1,000.0 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 |
| 1,100.0 | 0.00 | 0.00 | 1,100.0 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 |
| 1,200.0 | 0.00 | 0.00 | 1,200.0 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 |
| 1,300.0 | 0.00 | 0.00 | 1,300.0 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 |
| 1,400.0 | 2.00 | 124.86 | 1,400.0 | -1.0 | 1.4 | -0.9 | 2.00 | 2.00 | 0.00 |
| 1,500.0 | 4.00 | 124.86 | 1,499.8 | -4.0 | 5.7 | -3.6 | 2.00 | 2.00 | 0.00 |
| 1,600.0 | 6.00 | 124.86 | 1,599.5 | -9.0 | 12.9 | -8.1 | 2.00 | 2.00 | 0.00 |
| 1,614.5 | 6.29 | 124.86 | 1,613.9 | -9.9 | 14.2 | -8.9 | 2.00 | 2.00 | 0.00 |
| 1,700.0 | 6.29 | 124.86 | 1,698.9 | -15.2 | 21.8 | -13.7 | 0.00 | 0.00 | 0.00 |
| 1,800.0 | 6.29 | 124.86 | 1,798.3 | -21.5 | 30.8 | -19.4 | 0.00 | 0.00 | 0.00 |
| 1,900.0 | 6.29 | 124.86 | 1,897.6 | -27.7 | 39.8 | -25.0 | 0.00 | 0.00 | 0.00 |
| 2,000.0 | 6.29 | 124.86 | 1,997.0 | -34.0 | 48.8 | -30.7 | 0.00 | 0.00 | 0.00 |
| 2,100.0 | 6.29 | 124.86 | 2,096.4 | -40.3 | 57.8 | -36.3 | 0.00 | 0.00 | 0.00 |
| 2,200.0 | 6.29 | 124.86 | 2,195.8 | -46.5 | 66.8 | -42.0 | 0.00 | 0.00 | 0.00 |
| 2,300.0 | 6.29 | 124.86 | 2,295.2 | -52.8 | 75.8 | -47.6 | 0.00 | 0.00 | 0.00 |
| 2,400.0 | 6.29 | 124.86 | 2,394.6 | -59.0 | 84.8 | -53.3 | 0.00 | 0.00 | 0.00 |
| 2,500.0 | 6.29 | 124.86 | 2,494.0 | -65.3 | 93.8 | -58.9 | 0.00 | 0.00 | 0.00 |
| 2,600.0 | 6.29 | 124.86 | 2,593.4 | -71.6 | 102.8 | -64.6 | 0.00 | 0.00 | 0.00 |
| 2,700.0 | 6.29 | 124.86 | 2,692.8 | -77.8 | 111.7 | -70.2 | 0.00 | 0.00 | 0.00 |
| 2,800.0 | 6.29 | 124.86 | 2,792.2 | -84.1 | 120.7 | -75.9 | 0.00 | 0.00 | 0.00 |
| 2,900.0 | 6.29 | 124.86 | 2,891.6 | -90.4 | 129.7 | -81.5 | 0.00 | 0.00 | 0.00 |
| 3,000.0 | 6.29 | 124.86 | 2,991.0 | -96.6 | 138.7 | -87.2 | 0.00 | 0.00 | 0.00 |
| 3,100.0 | 6.29 | 124.86 | 3,090.4 | -102.9 | 147.7 | -92.8 | 0.00 | 0.00 | 0.00 |
| 3,200.0 | 6.29 | 124.86 | 3,189.8 | -109.1 | 156.7 | -98.5 | 0.00 | 0.00 | 0.00 |
| 3,300.0 | 6.29 | 124.86 | 3,289.2 | -115.4 | 165.7 | -104.2 | 0.00 | 0.00 | 0.00 |
| 3,400.0 | 6.29 | 124.86 | 3,388.6 | -121.7 | 174.7 | -109.8 | 0.00 | 0.00 | 0.00 |
| 3,500.0 | 6.29 | 124.86 | 3,488.0 | -127.9 | 183.7 | -115.5 | 0.00 | 0.00 | 0.00 |
| 3,600.0 | 6.29 | 124.86 | 3,587.4 | -134.2 | 192.7 | -121.1 | 0.00 | 0.00 | 0.00 |
| 3,700.0 | 6.29 | 124.86 | 3,686.8 | -140.5 | 201.7 | -126.8 | 0.00 | 0.00 | 0.00 |
| 3,800.0 | 6.29 | 124.86 | 3,786.2 | -146.7 | 210.7 | -132.4 | 0.00 | 0.00 | 0.00 |
| 3,900.0 | 6.29 | 124.86 | 3,885.6 | -153.0 | 219.6 | -138.1 | 0.00 | 0.00 | 0.00 |
| 4,000.0 | 6.29 | 124.86 | 3,985.0 | -159.2 | 228.6 | -143.7 | 0.00 | 0.00 | 0.00 |
| 4,100.0 | 6.29 | 124.86 | 4,084.4 | -165.5 | 237.6 | -149.4 | 0.00 | 0.00 | 0.00 |
| 4,200.0 | 6.29 | 124.86 | 4,183.8 | -171.8 | 246.6 | -155.0 | 0.00 | 0.00 | 0.00 |
| 4,300.0 | 6.29 | 124.86 | 4,283.2 | -178.0 | 255.6 | -160.7 | 0.00 | 0.00 | 0.00 |
| 4,400.0 | 6.29 | 124.86 | 4,382.6 | -184.3 | 264.6 | -166.3 | 0.00 | 0.00 | 0.00 |
| 4,500.0 | 6.29 | 124.86 | 4,482.0 | -190.6 | 273.6 | -172.0 | 0.00 | 0.00 | 0.00 |
| 4,600.0 | 6.29 | 124.86 | 4,581.4 | -196.8 | 282.6 | -177.6 | 0.00 | 0.00 | 0.00 |
| 4,700.0 | 6.29 | 124.86 | 4,680.8 | -203.1 | 291.6 | -183.3 | 0.00 | 0.00 | 0.00 |
| 4,800.0 | 6.29 | 124.86 | 4,780.2 | -209.4 | 300.6 | -188.9 | 0.00 | 0.00 | 0.00 |
| 4,900.0 | 6.29 | 124.86 | 4,879.6 | -215.6 | 309.6 | -194.6 | 0.00 | 0.00 | 0.00 |
| 5,000.0 | 6.29 | 124.86 | 4,979.0 | -221.9 | 318.5 | -200.2 | 0.00 | 0.00 | 0.00 |
| 5,100.0 | 6.29 | 124.86 | 5,078.4 | -228.1 | 327.5 | -205.9 | 0.00 | 0.00 | 0.00 |
| 5,200.0 | 6.29 | 124.86 | 5,177.8 | -234.4 | 336.5 | -211.5 | 0.00 | 0.00 | 0.00 |



Planning Report

| | | | |
|------------------|-----------------------------|-------------------------------------|-----------------------|
| Database: | PEDM | Local Co-ordinate Reference: | Well #204H |
| Company: | Midland | TVD Reference: | kb = 25' @ 3367.0usft |
| Project: | Lea County, NM (NAD 83 NME) | MD Reference: | kb = 25' @ 3367.0usft |
| Site: | Caballo 23 Fed | North Reference: | Grid |
| Well: | #204H | Survey Calculation Method: | Minimum Curvature |
| Wellbore: | OH | | |
| Design: | Plan #0.2 | | |

| Planned Survey | | | | | | | | | |
|-----------------------|-----------------|-------------|-----------------------|--------------|--------------|-------------------------|-------------------------|------------------------|-----------------------|
| Measured Depth (usft) | Inclination (°) | Azimuth (°) | Vertical Depth (usft) | +N/-S (usft) | +E/-W (usft) | Vertical Section (usft) | Dogleg Rate (°/100usft) | Build Rate (°/100usft) | Turn Rate (°/100usft) |
| 5,300.0 | 6.29 | 124.86 | 5,277.2 | -240.7 | 345.5 | -217.2 | 0.00 | 0.00 | 0.00 |
| 5,400.0 | 6.29 | 124.86 | 5,376.6 | -246.9 | 354.5 | -222.8 | 0.00 | 0.00 | 0.00 |
| 5,500.0 | 6.29 | 124.86 | 5,476.0 | -253.2 | 363.5 | -228.5 | 0.00 | 0.00 | 0.00 |
| 5,600.0 | 6.29 | 124.86 | 5,575.4 | -259.5 | 372.5 | -234.1 | 0.00 | 0.00 | 0.00 |
| 5,700.0 | 6.29 | 124.86 | 5,674.8 | -265.7 | 381.5 | -239.8 | 0.00 | 0.00 | 0.00 |
| 5,800.0 | 6.29 | 124.86 | 5,774.2 | -272.0 | 390.5 | -245.4 | 0.00 | 0.00 | 0.00 |
| 5,900.0 | 6.29 | 124.86 | 5,873.6 | -278.2 | 399.5 | -251.1 | 0.00 | 0.00 | 0.00 |
| 6,000.0 | 6.29 | 124.86 | 5,973.0 | -284.5 | 408.5 | -256.7 | 0.00 | 0.00 | 0.00 |
| 6,100.0 | 6.29 | 124.86 | 6,072.4 | -290.8 | 417.4 | -262.4 | 0.00 | 0.00 | 0.00 |
| 6,200.0 | 6.29 | 124.86 | 6,171.8 | -297.0 | 426.4 | -268.0 | 0.00 | 0.00 | 0.00 |
| 6,300.0 | 6.29 | 124.86 | 6,271.2 | -303.3 | 435.4 | -273.7 | 0.00 | 0.00 | 0.00 |
| 6,400.0 | 6.29 | 124.86 | 6,370.6 | -309.6 | 444.4 | -279.3 | 0.00 | 0.00 | 0.00 |
| 6,500.0 | 6.29 | 124.86 | 6,470.0 | -315.8 | 453.4 | -285.0 | 0.00 | 0.00 | 0.00 |
| 6,600.0 | 6.29 | 124.86 | 6,569.4 | -322.1 | 462.4 | -290.7 | 0.00 | 0.00 | 0.00 |
| 6,700.0 | 6.29 | 124.86 | 6,668.7 | -328.3 | 471.4 | -296.3 | 0.00 | 0.00 | 0.00 |
| 6,800.0 | 6.29 | 124.86 | 6,768.1 | -334.6 | 480.4 | -302.0 | 0.00 | 0.00 | 0.00 |
| 6,900.0 | 6.29 | 124.86 | 6,867.5 | -340.9 | 489.4 | -307.6 | 0.00 | 0.00 | 0.00 |
| 7,000.0 | 6.29 | 124.86 | 6,966.9 | -347.1 | 498.4 | -313.3 | 0.00 | 0.00 | 0.00 |
| 7,100.0 | 6.29 | 124.86 | 7,066.3 | -353.4 | 507.4 | -318.9 | 0.00 | 0.00 | 0.00 |
| 7,200.0 | 6.29 | 124.86 | 7,165.7 | -359.7 | 516.4 | -324.6 | 0.00 | 0.00 | 0.00 |
| 7,300.0 | 6.29 | 124.86 | 7,265.1 | -365.9 | 525.3 | -330.2 | 0.00 | 0.00 | 0.00 |
| 7,383.5 | 6.29 | 124.86 | 7,348.1 | -371.1 | 532.8 | -334.9 | 0.00 | 0.00 | 0.00 |
| 7,400.0 | 5.96 | 124.86 | 7,364.5 | -372.1 | 534.3 | -335.8 | 2.00 | -2.00 | 0.00 |
| 7,500.0 | 3.96 | 124.86 | 7,464.2 | -377.1 | 541.4 | -340.3 | 2.00 | -2.00 | 0.00 |
| 7,600.0 | 1.96 | 124.86 | 7,564.0 | -380.0 | 545.6 | -343.0 | 2.00 | -2.00 | 0.00 |
| 7,698.0 | 0.00 | 0.00 | 7,662.0 | -381.0 | 547.0 | -343.8 | 2.00 | -2.00 | 0.00 |
| 7,700.0 | 0.00 | 0.00 | 7,664.0 | -381.0 | 547.0 | -343.8 | 0.00 | 0.00 | 0.00 |
| 7,800.0 | 0.00 | 0.00 | 7,764.0 | -381.0 | 547.0 | -343.8 | 0.00 | 0.00 | 0.00 |
| 7,900.0 | 0.00 | 0.00 | 7,864.0 | -381.0 | 547.0 | -343.8 | 0.00 | 0.00 | 0.00 |
| 8,000.0 | 0.00 | 0.00 | 7,964.0 | -381.0 | 547.0 | -343.8 | 0.00 | 0.00 | 0.00 |
| 8,100.0 | 0.00 | 0.00 | 8,064.0 | -381.0 | 547.0 | -343.8 | 0.00 | 0.00 | 0.00 |
| 8,200.0 | 0.00 | 0.00 | 8,164.0 | -381.0 | 547.0 | -343.8 | 0.00 | 0.00 | 0.00 |
| 8,300.0 | 0.00 | 0.00 | 8,264.0 | -381.0 | 547.0 | -343.8 | 0.00 | 0.00 | 0.00 |
| 8,400.0 | 0.00 | 0.00 | 8,364.0 | -381.0 | 547.0 | -343.8 | 0.00 | 0.00 | 0.00 |
| 8,500.0 | 0.00 | 0.00 | 8,464.0 | -381.0 | 547.0 | -343.8 | 0.00 | 0.00 | 0.00 |
| 8,600.0 | 0.00 | 0.00 | 8,564.0 | -381.0 | 547.0 | -343.8 | 0.00 | 0.00 | 0.00 |
| 8,700.0 | 0.00 | 0.00 | 8,664.0 | -381.0 | 547.0 | -343.8 | 0.00 | 0.00 | 0.00 |
| 8,800.0 | 0.00 | 0.00 | 8,764.0 | -381.0 | 547.0 | -343.8 | 0.00 | 0.00 | 0.00 |
| 8,900.0 | 0.00 | 0.00 | 8,864.0 | -381.0 | 547.0 | -343.8 | 0.00 | 0.00 | 0.00 |
| 9,000.0 | 0.00 | 0.00 | 8,964.0 | -381.0 | 547.0 | -343.8 | 0.00 | 0.00 | 0.00 |
| 9,100.0 | 0.00 | 0.00 | 9,064.0 | -381.0 | 547.0 | -343.8 | 0.00 | 0.00 | 0.00 |
| 9,136.5 | 0.00 | 0.00 | 9,100.5 | -381.0 | 547.0 | -343.8 | 0.00 | 0.00 | 0.00 |
| 9,150.0 | 1.62 | 0.00 | 9,114.0 | -380.8 | 547.0 | -343.6 | 12.00 | 12.00 | 0.00 |
| 9,175.0 | 4.62 | 0.00 | 9,139.0 | -379.4 | 547.0 | -342.3 | 12.00 | 12.00 | 0.00 |
| 9,200.0 | 7.62 | 0.00 | 9,163.8 | -376.8 | 547.0 | -339.6 | 12.00 | 12.00 | 0.00 |
| 9,225.0 | 10.62 | 0.00 | 9,188.5 | -372.8 | 547.0 | -335.7 | 12.00 | 12.00 | 0.00 |
| 9,250.0 | 13.62 | 0.00 | 9,212.9 | -367.6 | 547.0 | -330.4 | 12.00 | 12.00 | 0.00 |
| 9,275.0 | 16.62 | 0.00 | 9,237.1 | -361.1 | 547.0 | -323.9 | 12.00 | 12.00 | 0.00 |
| 9,300.0 | 19.62 | 0.00 | 9,260.8 | -353.3 | 547.0 | -316.2 | 12.00 | 12.00 | 0.00 |
| 9,325.0 | 22.62 | 0.00 | 9,284.1 | -344.3 | 547.0 | -307.2 | 12.00 | 12.00 | 0.00 |
| 9,350.0 | 25.62 | 0.00 | 9,307.0 | -334.1 | 547.0 | -297.0 | 12.00 | 12.00 | 0.00 |
| 9,356.9 | 26.46 | 0.00 | 9,313.2 | -331.0 | 547.0 | -293.9 | 12.00 | 12.00 | 0.00 |
| 9,375.0 | 28.62 | 359.96 | 9,329.2 | -322.7 | 547.0 | -285.6 | 12.00 | 12.00 | -0.20 |
| 9,400.0 | 31.62 | 359.92 | 9,350.8 | -310.1 | 547.0 | -273.1 | 12.00 | 12.00 | -0.17 |



Planning Report

| | | | |
|------------------|-----------------------------|-------------------------------------|-----------------------|
| Database: | PEDM | Local Co-ordinate Reference: | Well #204H |
| Company: | Midland | TVD Reference: | kb = 25' @ 3367.0usft |
| Project: | Lea County, NM (NAD 83 NME) | MD Reference: | kb = 25' @ 3367.0usft |
| Site: | Caballo 23 Fed | North Reference: | Grid |
| Well: | #204H | Survey Calculation Method: | Minimum Curvature |
| Wellbore: | OH | | |
| Design: | Plan #0.2 | | |

| Planned Survey | | | | | | | | | |
|-----------------------|-----------------|-------------|-----------------------|--------------|--------------|-------------------------|-------------------------|------------------------|-----------------------|
| Measured Depth (usft) | Inclination (°) | Azimuth (°) | Vertical Depth (usft) | +N/-S (usft) | +E/-W (usft) | Vertical Section (usft) | Dogleg Rate (°/100usft) | Build Rate (°/100usft) | Turn Rate (°/100usft) |
| 9,425.0 | 34.62 | 359.88 | 9,371.8 | -296.5 | 547.0 | -259.5 | 12.00 | 12.00 | -0.15 |
| 9,450.0 | 37.62 | 359.85 | 9,392.0 | -281.7 | 546.9 | -244.8 | 12.00 | 12.00 | -0.12 |
| 9,475.0 | 40.62 | 359.83 | 9,411.3 | -265.9 | 546.9 | -229.0 | 12.00 | 12.00 | -0.11 |
| 9,500.0 | 43.62 | 359.80 | 9,429.9 | -249.2 | 546.8 | -212.3 | 12.00 | 12.00 | -0.10 |
| 9,525.0 | 46.62 | 359.78 | 9,447.5 | -231.5 | 546.8 | -194.6 | 12.00 | 12.00 | -0.09 |
| 9,550.0 | 49.62 | 359.76 | 9,464.2 | -212.8 | 546.7 | -176.1 | 12.00 | 12.00 | -0.08 |
| 9,575.0 | 52.62 | 359.74 | 9,479.9 | -193.4 | 546.6 | -156.7 | 12.00 | 12.00 | -0.07 |
| 9,600.0 | 55.62 | 359.73 | 9,494.5 | -173.1 | 546.5 | -136.5 | 12.00 | 12.00 | -0.07 |
| 9,625.0 | 58.62 | 359.71 | 9,508.1 | -152.1 | 546.4 | -115.5 | 12.00 | 12.00 | -0.06 |
| 9,650.0 | 61.62 | 359.70 | 9,520.6 | -130.5 | 546.3 | -93.9 | 12.00 | 12.00 | -0.06 |
| 9,675.0 | 64.62 | 359.68 | 9,531.9 | -108.2 | 546.2 | -71.7 | 12.00 | 12.00 | -0.05 |
| 9,700.0 | 67.62 | 359.67 | 9,542.0 | -85.3 | 546.0 | -48.9 | 12.00 | 12.00 | -0.05 |
| 9,725.0 | 70.62 | 359.66 | 9,550.9 | -62.0 | 545.9 | -25.6 | 12.00 | 12.00 | -0.05 |
| 9,750.0 | 73.62 | 359.65 | 9,558.6 | -38.2 | 545.8 | -1.8 | 12.00 | 12.00 | -0.05 |
| 9,775.0 | 76.62 | 359.63 | 9,565.0 | -14.0 | 545.6 | 22.3 | 12.00 | 12.00 | -0.05 |
| 9,800.0 | 79.62 | 359.62 | 9,570.1 | 10.5 | 545.5 | 46.7 | 12.00 | 12.00 | -0.05 |
| 9,825.0 | 82.62 | 359.61 | 9,574.0 | 35.1 | 545.3 | 71.3 | 12.00 | 12.00 | -0.04 |
| 9,850.0 | 85.62 | 359.60 | 9,576.6 | 60.0 | 545.1 | 96.1 | 12.00 | 12.00 | -0.04 |
| 9,875.0 | 88.62 | 359.59 | 9,577.8 | 85.0 | 544.9 | 121.0 | 12.00 | 12.00 | -0.04 |
| 9,886.5 | 90.00 | 359.58 | 9,577.9 | 96.5 | 544.9 | 132.4 | 12.00 | 12.00 | -0.04 |
| 9,900.0 | 90.00 | 359.58 | 9,577.9 | 110.0 | 544.8 | 145.9 | 0.00 | 0.00 | 0.00 |
| 10,000.0 | 90.00 | 359.58 | 9,577.9 | 210.0 | 544.0 | 245.6 | 0.00 | 0.00 | 0.00 |
| 10,100.0 | 90.00 | 359.58 | 9,577.9 | 310.0 | 543.3 | 345.4 | 0.00 | 0.00 | 0.00 |
| 10,200.0 | 90.00 | 359.58 | 9,577.9 | 410.0 | 542.6 | 445.1 | 0.00 | 0.00 | 0.00 |
| 10,300.0 | 90.00 | 359.58 | 9,577.9 | 510.0 | 541.9 | 544.8 | 0.00 | 0.00 | 0.00 |
| 10,400.0 | 90.00 | 359.58 | 9,577.9 | 610.0 | 541.1 | 644.6 | 0.00 | 0.00 | 0.00 |
| 10,500.0 | 90.00 | 359.58 | 9,577.9 | 710.0 | 540.4 | 744.3 | 0.00 | 0.00 | 0.00 |
| 10,600.0 | 90.00 | 359.58 | 9,578.0 | 810.0 | 539.7 | 844.0 | 0.00 | 0.00 | 0.00 |
| 10,700.0 | 90.00 | 359.58 | 9,578.0 | 910.0 | 539.0 | 943.7 | 0.00 | 0.00 | 0.00 |
| 10,800.0 | 90.00 | 359.58 | 9,578.0 | 1,010.0 | 538.2 | 1,043.5 | 0.00 | 0.00 | 0.00 |
| 10,900.0 | 90.00 | 359.58 | 9,578.0 | 1,110.0 | 537.5 | 1,143.2 | 0.00 | 0.00 | 0.00 |
| 11,000.0 | 90.00 | 359.58 | 9,578.0 | 1,209.9 | 536.8 | 1,242.9 | 0.00 | 0.00 | 0.00 |
| 11,100.0 | 90.00 | 359.58 | 9,578.0 | 1,309.9 | 536.1 | 1,342.7 | 0.00 | 0.00 | 0.00 |
| 11,200.0 | 90.00 | 359.58 | 9,578.0 | 1,409.9 | 535.3 | 1,442.4 | 0.00 | 0.00 | 0.00 |
| 11,300.0 | 90.00 | 359.58 | 9,578.0 | 1,509.9 | 534.6 | 1,542.1 | 0.00 | 0.00 | 0.00 |
| 11,400.0 | 90.00 | 359.58 | 9,578.0 | 1,609.9 | 533.9 | 1,641.8 | 0.00 | 0.00 | 0.00 |
| 11,500.0 | 90.00 | 359.58 | 9,578.0 | 1,709.9 | 533.2 | 1,741.6 | 0.00 | 0.00 | 0.00 |
| 11,600.0 | 90.00 | 359.58 | 9,578.0 | 1,809.9 | 532.4 | 1,841.3 | 0.00 | 0.00 | 0.00 |
| 11,700.0 | 90.00 | 359.58 | 9,578.0 | 1,909.9 | 531.7 | 1,941.0 | 0.00 | 0.00 | 0.00 |
| 11,800.0 | 90.00 | 359.58 | 9,578.0 | 2,009.9 | 531.0 | 2,040.8 | 0.00 | 0.00 | 0.00 |
| 11,900.0 | 90.00 | 359.58 | 9,578.0 | 2,109.9 | 530.3 | 2,140.5 | 0.00 | 0.00 | 0.00 |
| 12,000.0 | 90.00 | 359.58 | 9,578.0 | 2,209.9 | 529.5 | 2,240.2 | 0.00 | 0.00 | 0.00 |
| 12,100.0 | 90.00 | 359.58 | 9,578.0 | 2,309.9 | 528.8 | 2,339.9 | 0.00 | 0.00 | 0.00 |
| 12,200.0 | 90.00 | 359.58 | 9,578.0 | 2,409.9 | 528.1 | 2,439.7 | 0.00 | 0.00 | 0.00 |
| 12,300.0 | 90.00 | 359.58 | 9,578.0 | 2,509.9 | 527.4 | 2,539.4 | 0.00 | 0.00 | 0.00 |
| 12,400.0 | 90.00 | 359.58 | 9,578.0 | 2,609.9 | 526.6 | 2,639.1 | 0.00 | 0.00 | 0.00 |
| 12,500.0 | 90.00 | 359.58 | 9,578.0 | 2,709.9 | 525.9 | 2,738.9 | 0.00 | 0.00 | 0.00 |
| 12,600.0 | 90.00 | 359.58 | 9,578.0 | 2,809.9 | 525.2 | 2,838.6 | 0.00 | 0.00 | 0.00 |
| 12,700.0 | 90.00 | 359.58 | 9,578.0 | 2,909.9 | 524.5 | 2,938.3 | 0.00 | 0.00 | 0.00 |
| 12,800.0 | 90.00 | 359.58 | 9,578.0 | 3,009.9 | 523.7 | 3,038.0 | 0.00 | 0.00 | 0.00 |
| 12,900.0 | 90.00 | 359.58 | 9,578.0 | 3,109.9 | 523.0 | 3,137.8 | 0.00 | 0.00 | 0.00 |
| 13,000.0 | 90.00 | 359.58 | 9,578.0 | 3,209.9 | 522.3 | 3,237.5 | 0.00 | 0.00 | 0.00 |
| 13,100.0 | 90.00 | 359.58 | 9,578.0 | 3,309.9 | 521.6 | 3,337.2 | 0.00 | 0.00 | 0.00 |
| 13,200.0 | 90.00 | 359.58 | 9,578.0 | 3,409.9 | 520.8 | 3,437.0 | 0.00 | 0.00 | 0.00 |



Planning Report

| | | | |
|------------------|-----------------------------|-------------------------------------|-----------------------|
| Database: | PEDM | Local Co-ordinate Reference: | Well #204H |
| Company: | Midland | TVD Reference: | kb = 25' @ 3367.0usft |
| Project: | Lea County, NM (NAD 83 NME) | MD Reference: | kb = 25' @ 3367.0usft |
| Site: | Caballo 23 Fed | North Reference: | Grid |
| Well: | #204H | Survey Calculation Method: | Minimum Curvature |
| Wellbore: | OH | | |
| Design: | Plan #0.2 | | |



| Planned Survey | | | | | | | | | | |
|-----------------------|-----------------|-------------|-----------------------|--------------|--------------|-------------------------|-------------------------|------------------------|-----------------------|--|
| Measured Depth (usft) | Inclination (°) | Azimuth (°) | Vertical Depth (usft) | +N/-S (usft) | +E/-W (usft) | Vertical Section (usft) | Dogleg Rate (°/100usft) | Build Rate (°/100usft) | Turn Rate (°/100usft) | |
| 13,300.0 | 90.00 | 359.58 | 9,578.0 | 3,509.9 | 520.1 | 3,536.7 | 0.00 | 0.00 | 0.00 | |
| 13,400.0 | 90.00 | 359.58 | 9,578.0 | 3,609.9 | 519.4 | 3,636.4 | 0.00 | 0.00 | 0.00 | |
| 13,500.0 | 90.00 | 359.58 | 9,578.0 | 3,709.9 | 518.7 | 3,736.1 | 0.00 | 0.00 | 0.00 | |
| 13,600.0 | 90.00 | 359.58 | 9,578.0 | 3,809.9 | 517.9 | 3,835.9 | 0.00 | 0.00 | 0.00 | |
| 13,700.0 | 90.00 | 359.58 | 9,578.0 | 3,909.9 | 517.2 | 3,935.6 | 0.00 | 0.00 | 0.00 | |
| 13,800.0 | 90.00 | 359.58 | 9,578.0 | 4,009.9 | 516.5 | 4,035.3 | 0.00 | 0.00 | 0.00 | |
| 13,900.0 | 90.00 | 359.58 | 9,578.0 | 4,109.9 | 515.8 | 4,135.1 | 0.00 | 0.00 | 0.00 | |
| 14,000.0 | 90.00 | 359.58 | 9,578.0 | 4,209.9 | 515.1 | 4,234.8 | 0.00 | 0.00 | 0.00 | |
| 14,100.0 | 90.00 | 359.58 | 9,578.0 | 4,309.9 | 514.3 | 4,334.5 | 0.00 | 0.00 | 0.00 | |
| 14,200.0 | 90.00 | 359.58 | 9,578.0 | 4,409.9 | 513.6 | 4,434.2 | 0.00 | 0.00 | 0.00 | |
| 14,300.0 | 90.00 | 359.58 | 9,578.0 | 4,509.9 | 512.9 | 4,534.0 | 0.00 | 0.00 | 0.00 | |
| 14,400.0 | 90.00 | 359.58 | 9,578.0 | 4,609.9 | 512.2 | 4,633.7 | 0.00 | 0.00 | 0.00 | |
| 14,500.0 | 90.00 | 359.58 | 9,578.0 | 4,709.9 | 511.4 | 4,733.4 | 0.00 | 0.00 | 0.00 | |
| 14,600.0 | 90.00 | 359.58 | 9,578.0 | 4,809.9 | 510.7 | 4,833.2 | 0.00 | 0.00 | 0.00 | |
| 14,700.0 | 90.00 | 359.58 | 9,578.0 | 4,909.9 | 510.0 | 4,932.9 | 0.00 | 0.00 | 0.00 | |
| 14,800.0 | 90.00 | 359.58 | 9,578.0 | 5,009.8 | 509.3 | 5,032.6 | 0.00 | 0.00 | 0.00 | |
| 14,900.0 | 90.00 | 359.58 | 9,578.0 | 5,109.8 | 508.5 | 5,132.3 | 0.00 | 0.00 | 0.00 | |
| 15,000.0 | 90.00 | 359.58 | 9,578.0 | 5,209.8 | 507.8 | 5,232.1 | 0.00 | 0.00 | 0.00 | |
| 15,100.0 | 90.00 | 359.58 | 9,578.0 | 5,309.8 | 507.1 | 5,331.8 | 0.00 | 0.00 | 0.00 | |
| 15,200.0 | 90.00 | 359.58 | 9,578.0 | 5,409.8 | 506.4 | 5,431.5 | 0.00 | 0.00 | 0.00 | |
| 15,300.0 | 90.00 | 359.58 | 9,578.0 | 5,509.8 | 505.6 | 5,531.3 | 0.00 | 0.00 | 0.00 | |
| 15,400.0 | 90.00 | 359.58 | 9,578.0 | 5,609.8 | 504.9 | 5,631.0 | 0.00 | 0.00 | 0.00 | |
| 15,500.0 | 90.00 | 359.58 | 9,578.0 | 5,709.8 | 504.2 | 5,730.7 | 0.00 | 0.00 | 0.00 | |
| 15,600.0 | 90.00 | 359.58 | 9,578.0 | 5,809.8 | 503.5 | 5,830.4 | 0.00 | 0.00 | 0.00 | |
| 15,700.0 | 90.00 | 359.58 | 9,578.0 | 5,909.8 | 502.7 | 5,930.2 | 0.00 | 0.00 | 0.00 | |
| 15,800.0 | 90.00 | 359.58 | 9,578.0 | 6,009.8 | 502.0 | 6,029.9 | 0.00 | 0.00 | 0.00 | |
| 15,900.0 | 90.00 | 359.58 | 9,578.0 | 6,109.8 | 501.3 | 6,129.6 | 0.00 | 0.00 | 0.00 | |
| 16,000.0 | 90.00 | 359.58 | 9,578.0 | 6,209.8 | 500.6 | 6,229.4 | 0.00 | 0.00 | 0.00 | |
| 16,100.0 | 90.00 | 359.58 | 9,578.0 | 6,309.8 | 499.8 | 6,329.1 | 0.00 | 0.00 | 0.00 | |
| 16,200.0 | 90.00 | 359.58 | 9,578.0 | 6,409.8 | 499.1 | 6,428.8 | 0.00 | 0.00 | 0.00 | |
| 16,300.0 | 90.00 | 359.58 | 9,578.0 | 6,509.8 | 498.4 | 6,528.5 | 0.00 | 0.00 | 0.00 | |
| 16,400.0 | 90.00 | 359.58 | 9,578.0 | 6,609.8 | 497.7 | 6,628.3 | 0.00 | 0.00 | 0.00 | |
| 16,500.0 | 90.00 | 359.58 | 9,578.0 | 6,709.8 | 496.9 | 6,728.0 | 0.00 | 0.00 | 0.00 | |
| 16,600.0 | 90.00 | 359.58 | 9,578.0 | 6,809.8 | 496.2 | 6,827.7 | 0.00 | 0.00 | 0.00 | |
| 16,700.0 | 90.00 | 359.58 | 9,578.0 | 6,909.8 | 495.5 | 6,927.4 | 0.00 | 0.00 | 0.00 | |
| 16,800.0 | 90.00 | 359.58 | 9,578.0 | 7,009.8 | 494.8 | 7,027.2 | 0.00 | 0.00 | 0.00 | |
| 16,900.0 | 90.00 | 359.58 | 9,578.0 | 7,109.8 | 494.0 | 7,126.9 | 0.00 | 0.00 | 0.00 | |
| 17,000.0 | 90.00 | 359.58 | 9,578.0 | 7,209.8 | 493.3 | 7,226.6 | 0.00 | 0.00 | 0.00 | |
| 17,100.0 | 90.00 | 359.58 | 9,578.0 | 7,309.8 | 492.6 | 7,326.4 | 0.00 | 0.00 | 0.00 | |
| 17,181.2 | 90.00 | 359.58 | 9,578.0 | 7,391.0 | 492.0 | 7,407.4 | 0.00 | 0.00 | 0.00 | |



Planning Report

| | | | |
|------------------|-----------------------------|-------------------------------------|-----------------------|
| Database: | PEDM | Local Co-ordinate Reference: | Well #204H |
| Company: | Midland | TVD Reference: | kb = 25' @ 3367.0usft |
| Project: | Lea County, NM (NAD 83 NME) | MD Reference: | kb = 25' @ 3367.0usft |
| Site: | Caballo 23 Fed | North Reference: | Grid |
| Well: | #204H | Survey Calculation Method: | Minimum Curvature |
| Wellbore: | OH | | |
| Design: | Plan #0.2 | | |

| Design Targets | | | | | | | | | |
|--|------------------|-----------------|---------------|-----------------|-----------------|--------------------|-------------------|-----------------|-------------------|
| Target Name - hit/miss target - Shape | Dip Angle (°) | Dip Dir. (°) | TVD (usft) | +N/-S (usft) | +E/-W (usft) | Northing (usft) | Easting (usft) | Latitude | Longitude |
| KOP(Caballo 23 Fed #4I - plan hits target center - Point | 0.00 | 0.00 | 9,100.5 | -381.0 | 547.0 | 404,243.00 | 784,243.00 | 32° 6' 32.088 N | 103° 32' 55.748 W |
| FTP(Caballo 23 Fed #4C - plan hits target center - Point | 0.00 | 0.00 | 9,313.2 | -331.0 | 547.0 | 404,293.00 | 784,243.00 | 32° 6' 32.583 N | 103° 32' 55.744 W |
| PBHL(Caballo 23 Fed #4 - plan hits target center - Point | 0.00 | 0.00 | 9,578.0 | 7,391.0 | 492.0 | 412,015.00 | 784,188.00 | 32° 7' 48.998 N | 103° 32' 55.730 W |

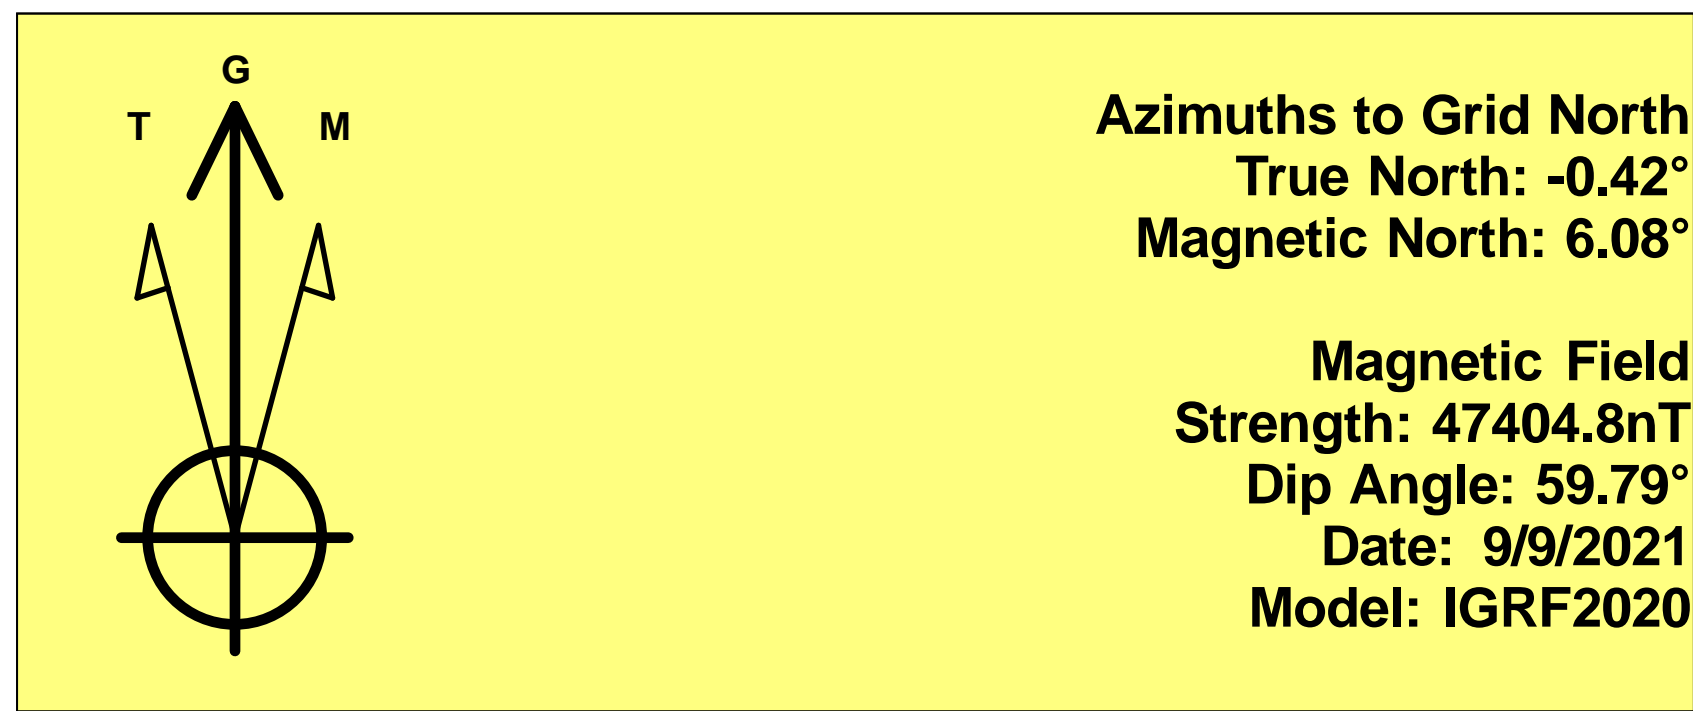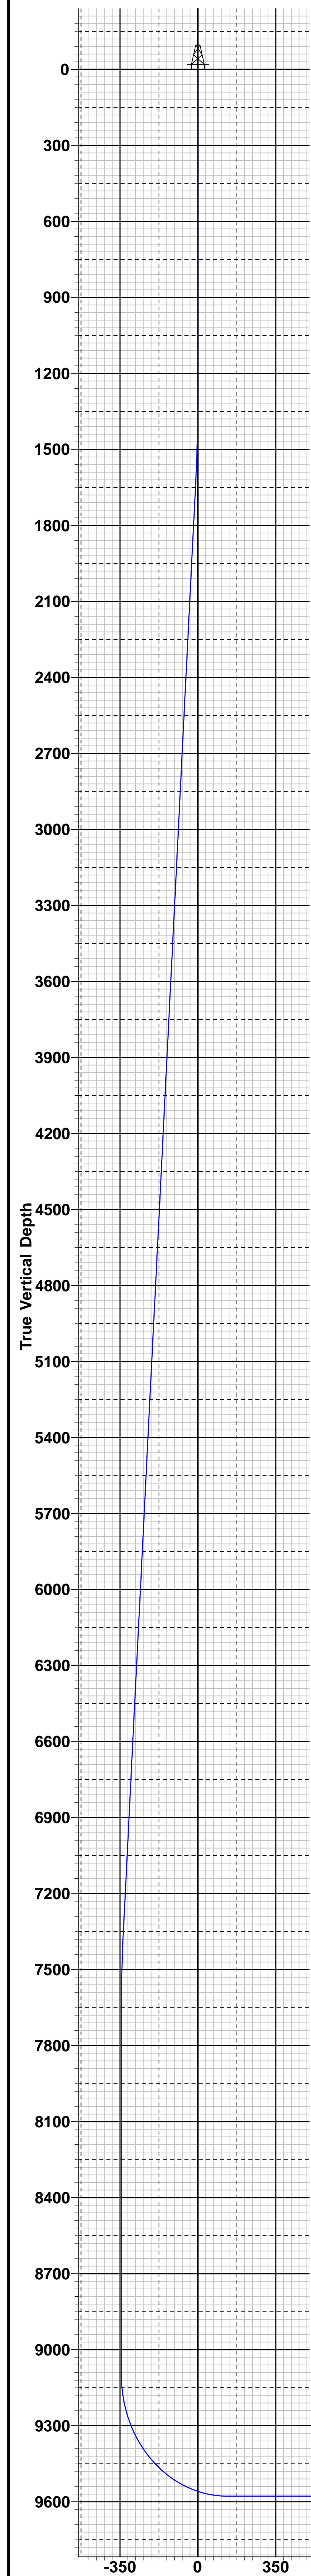

Azimuths to Grid North
True North: -0.42°
Magnetic North: 6.08°

Magnetic Field
Strength: 47404.8nT
Dip Angle: 59.79°
Date: 9/9/2021
Model: IGRF2020

To convert a Magnetic Direction to a Grid Direction, Add 6.08°
To convert a Magnetic Direction to a True Direction, Add 6.50° East
To convert a True Direction to a Grid Direction, Subtract 0.42°

| WELL DETAILS: #204H | | | | |
|-----------------------|-----------|-----------------|------------------|--|
| kb = 25' @ 3367.0usft | | | | |
| 3342.0 | | | | |
| Northings | Easting | Latitude | Longitude | |
| 404624.00 | 783696.00 | 32° 6' 35.897 N | 103° 33' 2.076 W | |

| SECTION DETAILS | | | | | | | | | | |
|-----------------|---------|-------|--------|--------|--------|-------|-------|--------|--------|----------------------------|
| Sec | MD | Inc | Azi | TVD | +N/-S | +E/-W | Dleg | TFace | VSect | Target |
| 1 | 0.0 | 0.00 | 0.00 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.0 | |
| 2 | 1300.0 | 0.00 | 0.00 | 1300.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.0 | |
| 3 | 1614.5 | 6.29 | 124.86 | 1613.9 | -9.9 | 14.2 | 2.00 | 124.86 | -8.9 | |
| 4 | 7383.5 | 6.29 | 124.86 | 7348.1 | -371.1 | 532.8 | 0.00 | 0.00 | -334.9 | |
| 5 | 7698.0 | 0.00 | 0.00 | 7662.0 | -381.0 | 547.0 | 2.00 | 180.00 | -343.8 | |
| 6 | 9136.5 | 0.00 | 0.00 | 9100.5 | -381.0 | 547.0 | 0.00 | 0.00 | -343.8 | KOP(Caballo 23 Fed #406H) |
| 7 | 9356.9 | 26.46 | 0.00 | 9313.2 | -331.0 | 547.0 | 12.00 | 0.00 | -293.9 | FTP(Caballo 23 Fed #406H) |
| 8 | 9886.5 | 90.00 | 359.58 | 9577.9 | 96.5 | 544.9 | 12.00 | -0.46 | 132.4 | |
| 9 | 17181.2 | 90.00 | 359.58 | 9578.0 | 7391.0 | 492.0 | 0.00 | 0.00 | 7407.4 | PBHL(Caballo 23 Fed #406H) |

| CASING DETAILS |
|-----------------------------|
| No casing data is available |

| WELLBORE TARGET DETAILS (MAP CO-ORDINATES) | | | | | |
|--|--------|--------|-------|-----------|-----------|
| Name | TVD | +N/-S | +E/-W | Northings | Easting |
| KOP(Caballo 23 Fed #406H) | 9100.5 | -381.0 | 547.0 | 404243.00 | 784243.00 |
| FTP(Caballo 23 Fed #406H) | 9313.2 | -331.0 | 547.0 | 404293.00 | 784243.00 |
| PBHL(Caballo 23 Fed #406H) | 9578.0 | 7391.0 | 492.0 | 412015.00 | 784188.00 |


Lea County, NM (NAD 83 NME)

Caballo 23 Fed #204H

Plan #0.2

PROJECT DETAILS: Lea County, NM (NAD 83 NME)

Geodetic System: US State Plane 1983
Datum: North American Datum 1983
Ellipsoid: GRS 1980
Zone: New Mexico Eastern Zone
System Datum: Mean Sea Level

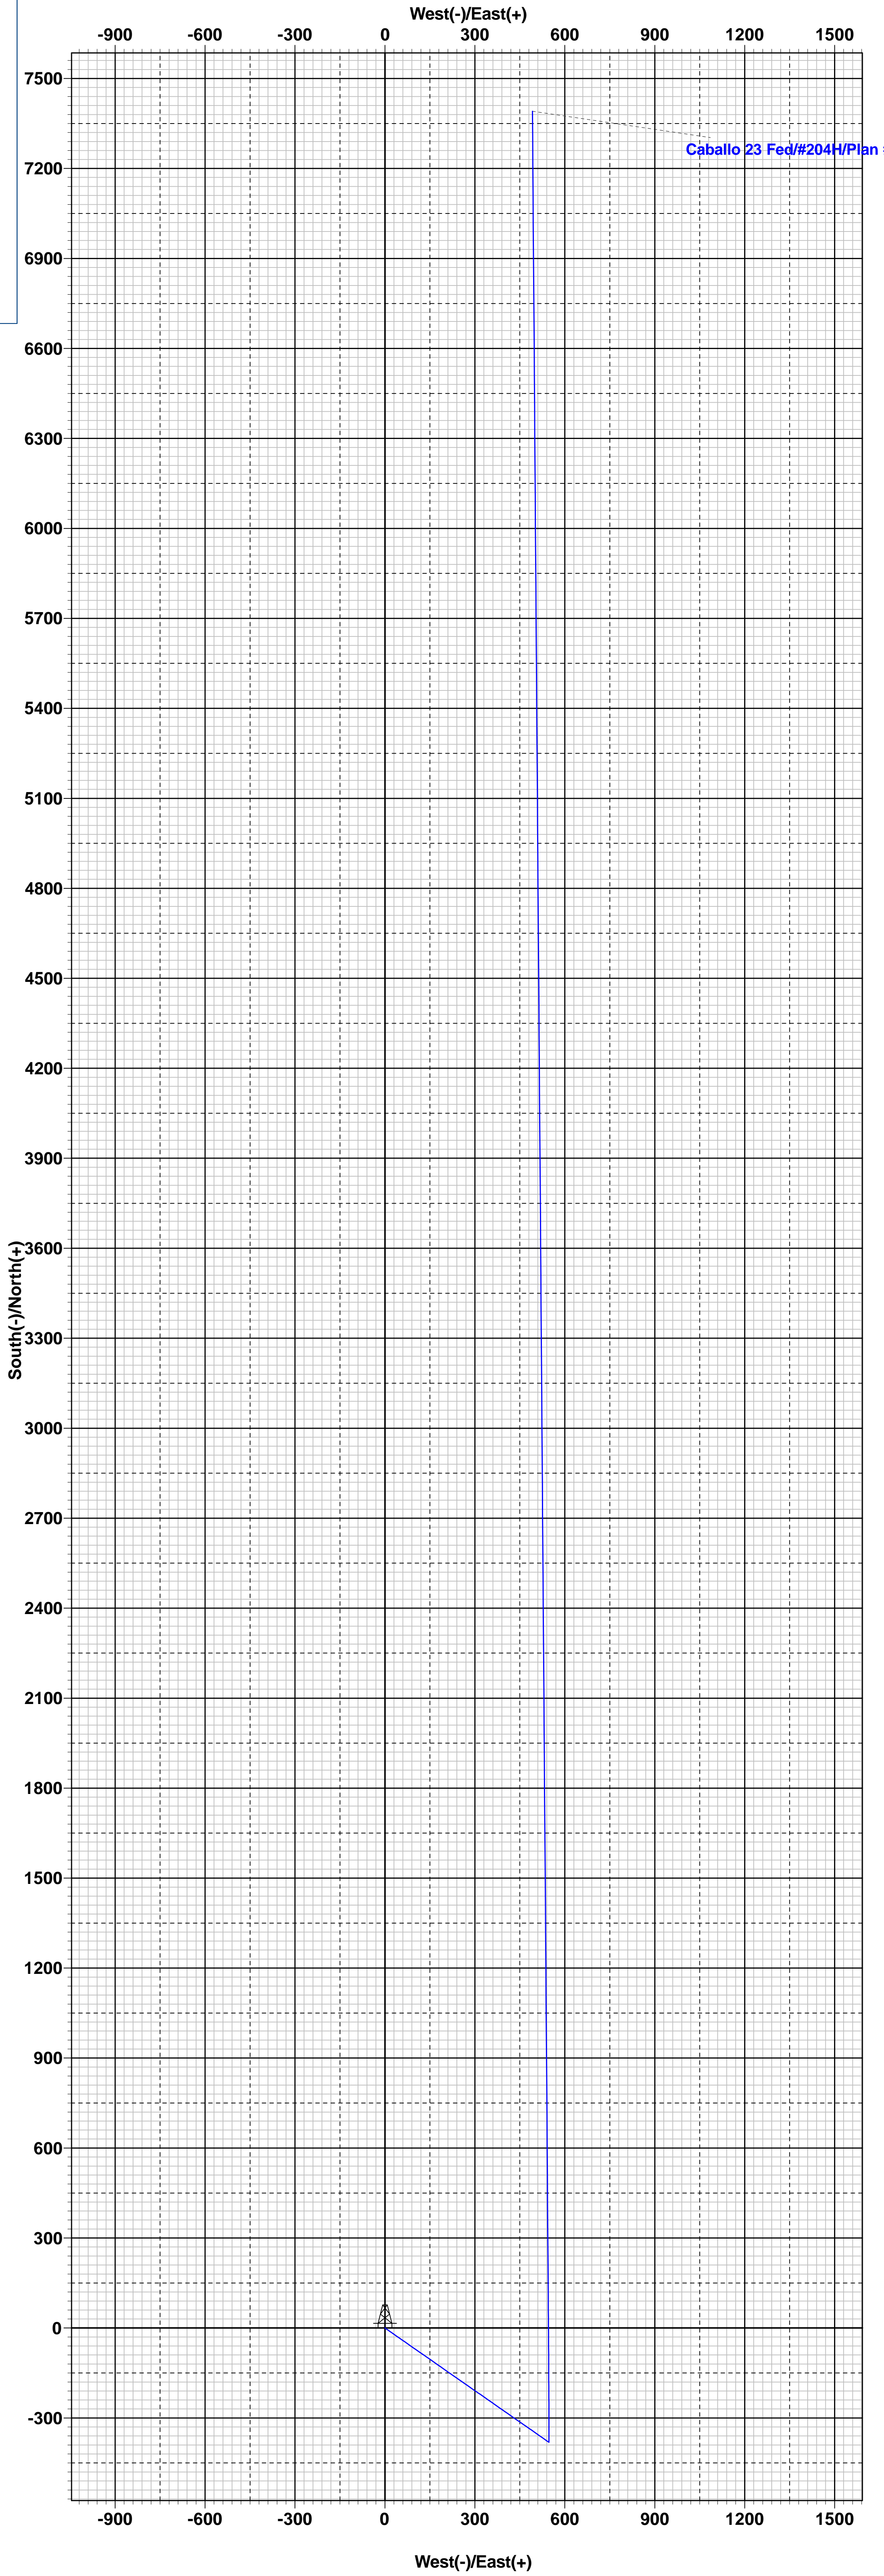



Salt Section Annular Clearance Variance Request

Daniel Moose

Current Design (Salt Strings)

0.422" Annular clearance requirement

- Casing collars shall have a minimum clearance of 0.422 inches on all sides in the hole/casing annulus, with recognition that variances can be granted for justified exceptions.

- 12.25" Hole x 9.625" 40# J55/HCK55 LTC Casing
 - 1.3125" Clearance to casing OD
 - 0.8125" Clearance to coupling OD
- 9.875" Hole x 8.75" 38.5# P110 Sprint-SF Casing
 - 0.5625" Clearance to casing OD
 - 0.433" Clearance to coupling OD

Annular Clearance Variance Request

EOG request permission to allow deviation from the 0.422" annulus clearance requirement for the intermediate (salt) section from Onshore Order #2 under the following conditions:

- The variance is not applicable within the Potash Boundaries or Capitan Reef areas.
- Operator takes responsibility to get casing to set point in the event that the clearance causes stuck pipe issues


Volumetric Hole Size Calculation

Hole Size Calculations Off Cement Volumes

- Known volume of cement pumped
- Known volume of cement returned to surface
- Must not have had any losses
- Must have bumped plug

Average Hole Size


- 12.25" Hole
 - 12.88" Hole
 - 5.13% diameter increase
 - 10.52% area increase
 - 0.63" Average enlargement
 - 0.58" Median enlargement
 - 179 Well Count
- 9.875" Hole
 - 10.30" Hole
 - 4.24% diameter increase
 - 9.64% area increase
 - 0.42" Average enlargement
 - 0.46" Median enlargement
 - 11 Well Count

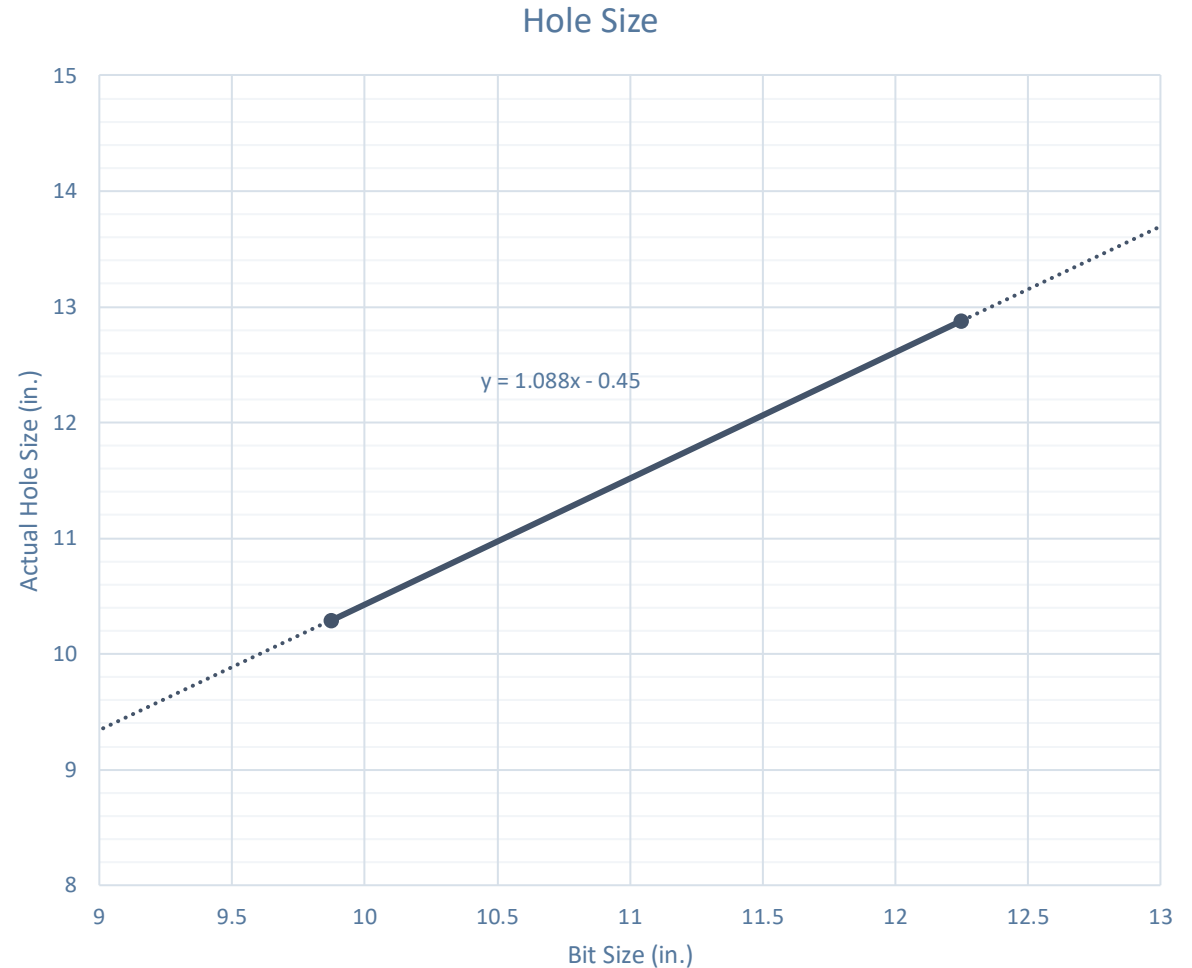

Caliper Hole Size (12.25")

Average Hole Size

- 12.25" Bit
 - 12.76" Hole
 - 4.14% diameter increase
 - 8.44% area increase
 - 0.51" Average enlargement
 - 0.52" Median enlargement
 - Brine

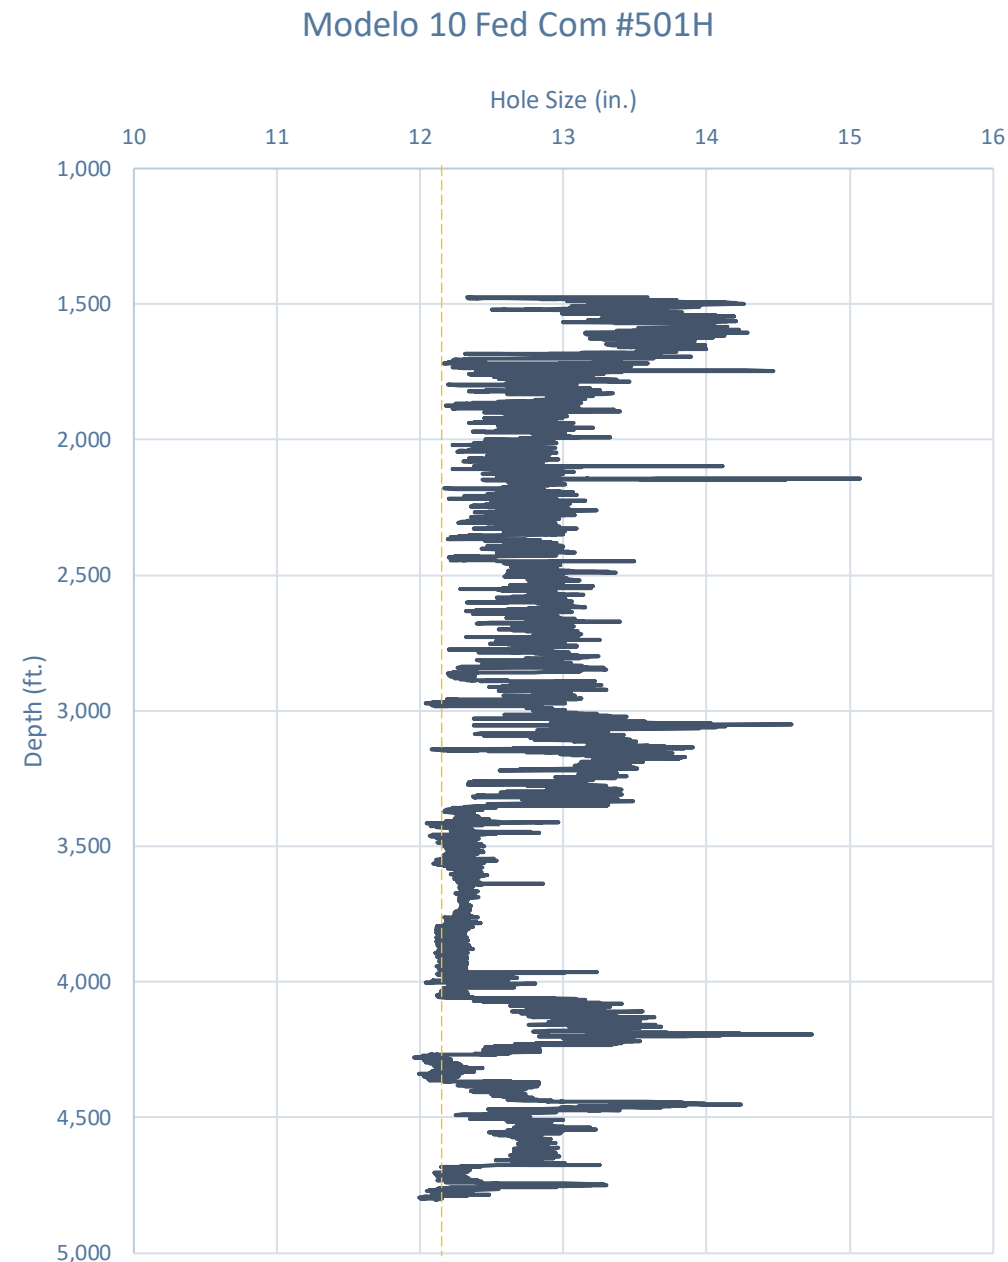


Caliper Hole Size (9.875")

Average Hole Size

- 9.875" Hole
 - 11.21" Hole
 - 13.54% diameter increase
 - 28.92% area increase
 - 1.33" Average enlargement
 - 1.30" Median enlargement
 - EnerLite

Whirling Wind 11 Fed Com #744H

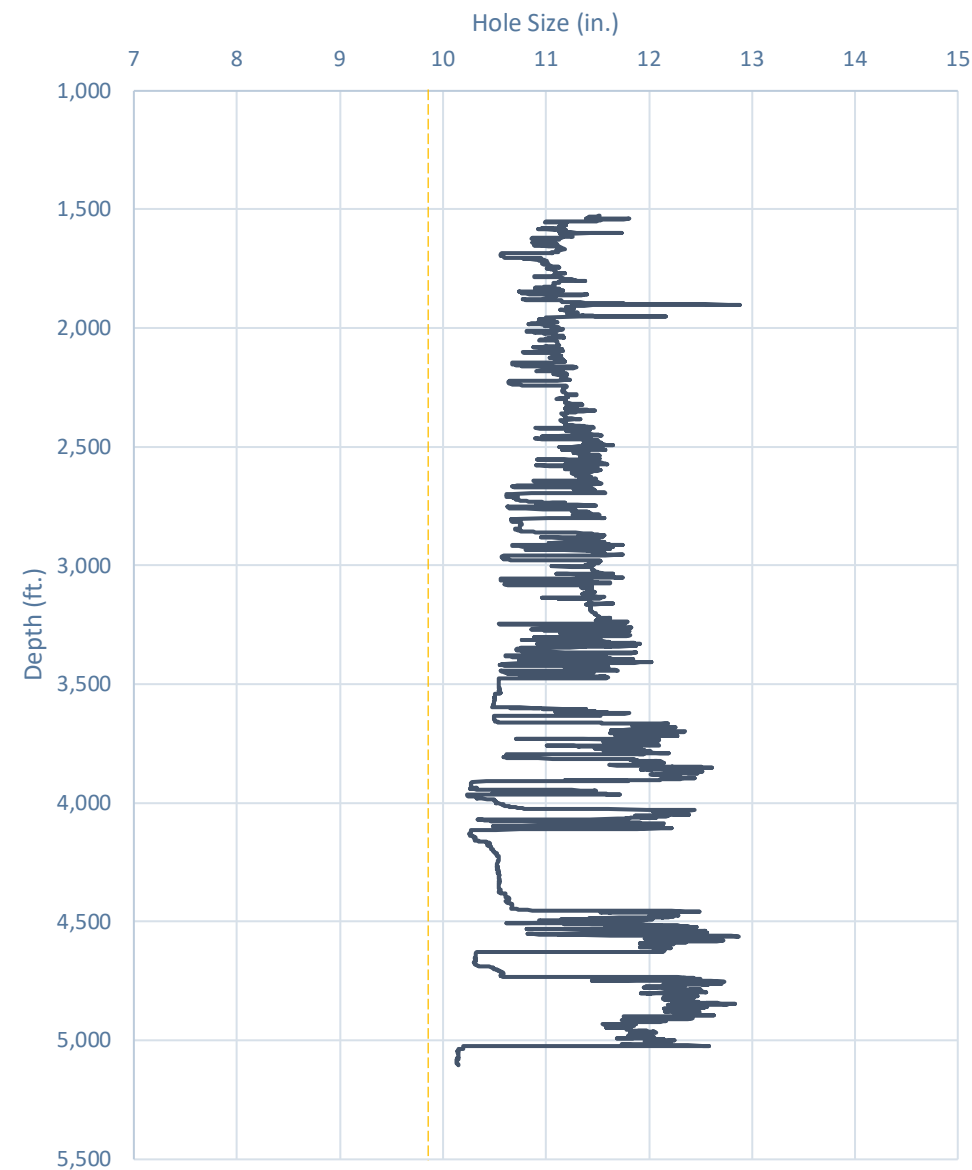

Design A


Proposed 11" Hole with 9.625" 40# J55/HCK55 LTC Casing

- 11" Bit + 0.52" Average hole enlargement = 11.52" Hole Size
 - 0.9475" Clearance to casing OD

$$= \frac{11.52 - 9.625}{2}$$
 - 0.4475" Clearance to coupling OD

$$= \frac{11.52 - 10.625}{2}$$
- Previous Shoe – 13.375" 54.5# J55 STC
 - 0.995" Clearance to coupling OD (~1,200' overlap)

$$= \frac{12.615 - 10.625}{2}$$

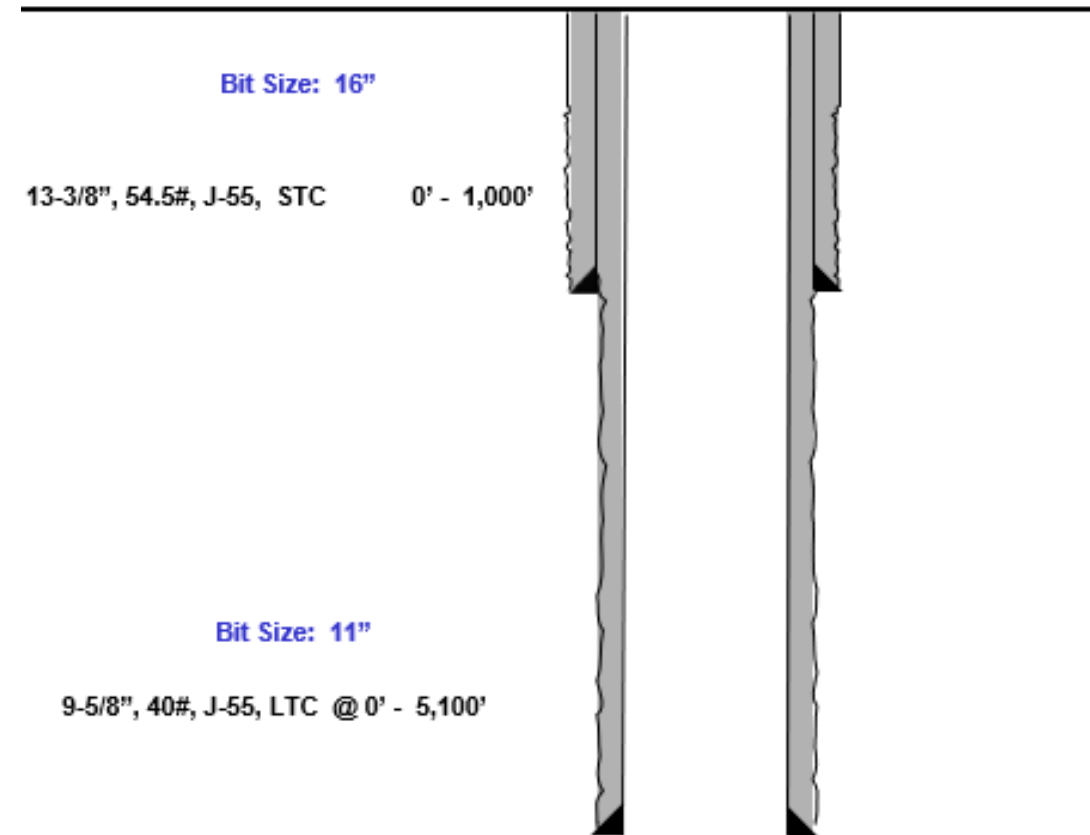

Design B


Proposed 9.875" Hole with 8.625" 32# J55/P110 BTC-SC Casing

- 9.875" Bit + 0.42" Average hole enlargement = 10.295" Hole Size
 - 0.835" Clearance to casing OD

$$= \frac{10.295 - 8.625}{2}$$
 - 0.585" Clearance to coupling OD

$$= \frac{10.295 - 9.125}{2}$$
- Previous Shoe – 10.75" 40.5# J55 STC
 - 0.4625" Clearance to coupling OD (~1,200' overlap)

$$= \frac{10.05 - 9.125}{2}$$

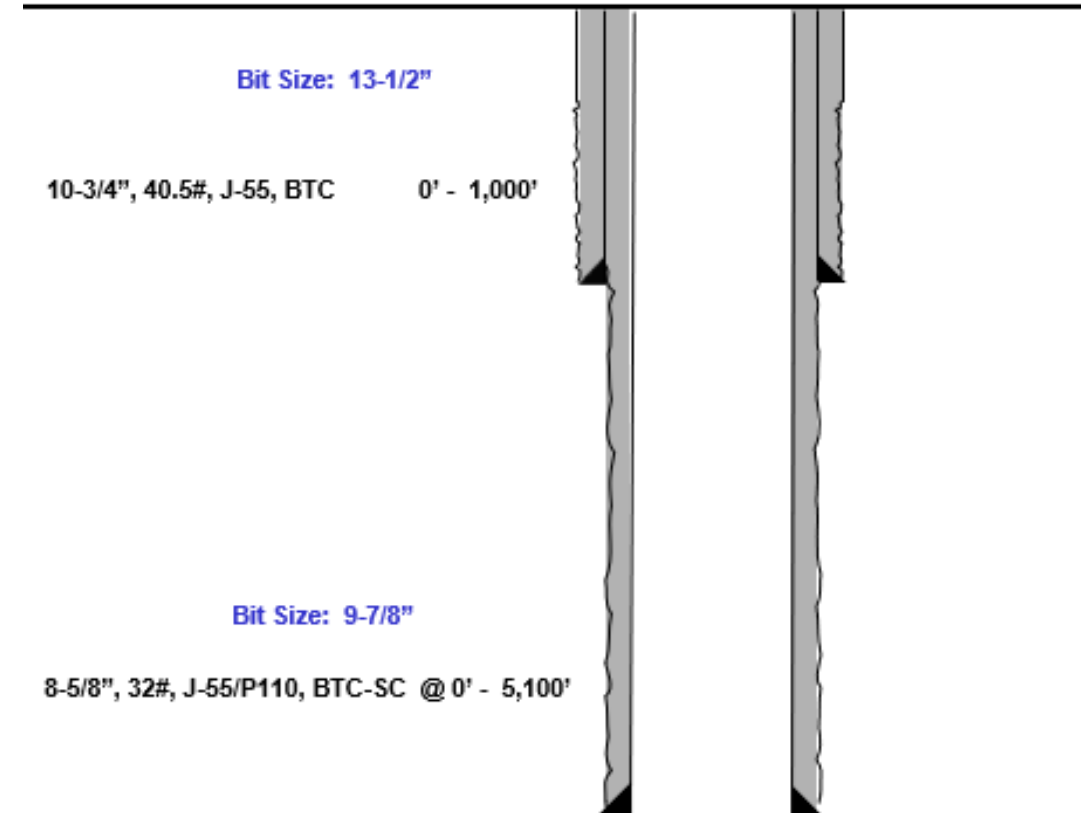



Index

Casing Spec Sheets

PERFORMANCE DATA

API LTC

Technical Data Sheet

9.625 in

40.00 lbs/ft

K55 HC

Tubular Parameters

| | | | | | |
|---------------------|--------|--------|------------------------------|-------|------|
| Size | 9.625 | in | Minimum Yield | 55 | ksi |
| Nominal Weight | 40.00 | lbs/ft | Minimum Tensile | 95 | ksi |
| Grade | K55 HC | | Yield Load | 629 | kips |
| PE Weight | 38.94 | lbs/ft | Tensile Load | 1088 | kips |
| Wall Thickness | 0.395 | in | Min. Internal Yield Pressure | 3,950 | psi |
| Nominal ID | 8.835 | in | Collapse Pressure | 3600 | psi |
| Drift Diameter | 8.750 | in | | | |
| Nom. Pipe Body Area | 11.454 | in² | | | |

Connection Parameters

| | | |
|------------------------------|--------|-------|
| Connection OD | 10.625 | in |
| Coupling Length | 10.500 | in |
| Threads Per Inch | 8 | tpi |
| Standoff Thread Turns | 3.50 | turns |
| Make-Up Loss | 4.750 | in |
| Min. Internal Yield Pressure | 3,950 | psi |

Pipe Body and API Connections Performance Data

13.375 54.50/0.380 J55

PDF

New Search »

« Back to Previous List

USC ☒ Metric

6/8/2015 10:04:37 AM

| Mechanical Properties | Pipe | BTC | LTC | STC | |
|----------------------------------|--------|--------|-----|--------|----------|
| Minimum Yield Strength | 55,000 | -- | -- | -- | psi |
| Maximum Yield Strength | 80,000 | -- | -- | -- | psi |
| Minimum Tensile Strength | 75,000 | -- | -- | -- | psi |
| Dimensions | Pipe | BTC | LTC | STC | |
| Outside Diameter | 13.375 | 14.375 | -- | 14.375 | in. |
| Wall Thickness | 0.380 | -- | -- | -- | in. |
| Inside Diameter | 12.615 | 12.615 | -- | 12.615 | in. |
| Standard Drift | 12.459 | 12.459 | -- | 12.459 | in. |
| Alternate Drift | -- | -- | -- | -- | in. |
| Nominal Linear Weight, T&C | 54.50 | -- | -- | -- | lbs/ft |
| Plain End Weight | 52.79 | -- | -- | -- | lbs/ft |
| Performance | Pipe | BTC | LTC | STC | |
| Minimum Collapse Pressure | 1,130 | 1,130 | -- | 1,130 | psi |
| Minimum Internal Yield Pressure | 2,740 | 2,740 | -- | 2,740 | psi |
| Minimum Pipe Body Yield Strength | 853.00 | -- | -- | -- | 1000 lbs |
| Joint Strength | -- | 909 | -- | 514 | 1000 lbs |
| Reference Length | -- | 11,125 | -- | 6,290 | ft |
| Make-Up Data | Pipe | BTC | LTC | STC | |
| Make-Up Loss | -- | 4.81 | -- | 3.50 | in. |
| Minimum Make-Up Torque | -- | -- | -- | 3,860 | ft-lbs |
| Maximum Make-Up Torque | -- | -- | -- | 6,430 | ft-lbs |

Casing Spec Sheets

Pipe Body and API Connections Performance Data

10.750 40.50/0.350 J55

PDF

New Search »

« Back to Previous List

USC ☒ Metric

6/8/2015 10:14:05 AM

| Mechanical Properties | Pipe | BTC | LTC | STC | |
|----------------------------------|--------|--------|-----|--------|----------|
| Minimum Yield Strength | 55,000 | -- | -- | -- | psi |
| Maximum Yield Strength | 80,000 | -- | -- | -- | psi |
| Minimum Tensile Strength | 75,000 | -- | -- | -- | psi |
| Dimensions | Pipe | BTC | LTC | STC | |
| Outside Diameter | 10.750 | 11.750 | -- | 11.750 | in. |
| Wall Thickness | 0.350 | -- | -- | -- | in. |
| Inside Diameter | 10.050 | 10.050 | -- | 10.050 | in. |
| Standard Drift | 9.894 | 9.894 | -- | 9.894 | in. |
| Alternate Drift | -- | -- | -- | -- | in. |
| Nominal Linear Weight, T&C | 40.50 | -- | -- | -- | lbs/ft |
| Plain End Weight | 38.91 | -- | -- | -- | lbs/ft |
| Performance | Pipe | BTC | LTC | STC | |
| Minimum Collapse Pressure | 1,580 | 1,580 | -- | 1,580 | psi |
| Minimum Internal Yield Pressure | 3,130 | 3,130 | -- | 3,130 | psi |
| Minimum Pipe Body Yield Strength | 629.00 | -- | -- | -- | 1000 lbs |
| Joint Strength | -- | 700 | -- | 420 | 1000 lbs |
| Reference Length | -- | 11,522 | -- | 6,915 | ft |
| Make-Up Data | Pipe | BTC | LTC | STC | |
| Make-Up Loss | -- | 4.81 | -- | 3.50 | in. |
| Minimum Make-Up Torque | -- | -- | -- | 3,150 | ft-lbs |
| Maximum Make-Up Torque | -- | -- | -- | 5,250 | ft-lbs |



API 5CT, 10th Ed. Connection Data Sheet

| O.D. (in) | WEIGHT (lb/ft) | WALL (in) | GRADE | *API DRIFT (in) | RBW % |
|-----------|------------------------------------|-----------|-------|-----------------|-------|
| 8.625 | Nominal: 32.00 Plain End: 31.13 | 0.352 | J55 | 7.796 | 87.5 |

| Material Properties (PE) | | Pipe Body Data (PE) | |
|---------------------------|--------|--|-----------------------|
| Pipe | | Geometry | |
| Minimum Yield Strength: | 55 ksi | Nominal ID: | 7.92 inch |
| Maximum Yield Strength: | 80 ksi | Nominal Area: | 9.149 in ² |
| Minimum Tensile Strength: | 75 ksi | *Special/Alt. Drift: | 7.875 inch |
| Coupling | | Performance | |
| Minimum Yield Strength: | 55 ksi | Pipe Body Yield Strength: | 503 kips |
| Maximum Yield Strength: | 80 ksi | Collapse Resistance: | 2,530 psi |
| Minimum Tensile Strength: | 75 ksi | Internal Yield Pressure: (API Historical) | 3,930 psi |

| API Connection Data | | API Connection Torque | |
|---------------------------------------|--|--|--|
| Coupling OD: 9.625" | | STC Torque (ft-lbs) | |
| STC Performance | | Min: 2,793 Opti: 3,724 Max: 4,655 | |
| STC Internal Pressure: | | LTC Torque (ft-lbs) | |
| STC Joint Strength: | | Min: 3,130 Opti: 4,174 Max: 5,217 | |
| LTC Performance | | BTC Torque (ft-lbs) | |
| LTC Internal Pressure: | | follow API guidelines regarding positional make up | |
| LTC Joint Strength: | | | |
| SC-BTC Performance - Cplg OD = 9.125" | | | |
| BTC Internal Pressure: | | | |
| BTC Joint Strength: | | | |

*Alt. Drift will be used unless API Drift is specified on order.

**If above API connections do not suit your needs, VAM® premium connections are available up to 100% of pipe body ratings.

ALL INFORMATION IS PROVIDED BY VALLOUREC OR ITS AFFILIATES AT USER'S SOLE RISK, WITHOUT LIABILITY FOR LOSS, DAMAGE OR INJURY RESULTING FROM THE USE THEREOF, AND ON AN "AS IS" BASIS WITHOUT WARRANTY OR REPRESENTATION OF ANY KIND, WHETHER EXPRESS OR IMPLIED, INCLUDING WITHOUT LIMITATION ANY WARRANTY OF MERCHANTABILITY, FITNESS FOR PURPOSE, ACCURACY OR COMPLETENESS. THE INFORMATION CONTAINED IN THIS DOCUMENT IS PROVIDED FOR INFORMATIONAL PURPOSES ONLY AND IS BASED ON ESTIMATES THAT HAVE NOT BEEN VERIFIED OR TESTED. IN NO EVENT SHALL VALLOUREC OR ITS AFFILIATES BE RESPONSIBLE FOR ANY INDIRECT, SPECIAL, INCIDENTAL, PUNITIVE, EXEMPLARY OR CONSEQUENTIAL LOSS OR DAMAGE (INCLUDING WITHOUT LIMITATION, LOSS OF USE, LOSS OF BARGAIN, LOSS OF REVENUE, PROFIT OR ANTICIPATED PROFIT) HOWEVER CAUSED OR ARISING, AND WHETHER SUCH LOSSES OR DAMAGES WERE FORESEEABLE OR VALLOUREC OR ITS AFFILIATES WERE ADVISED OF THE POSSIBILITY OF SUCH DAMAGES.

Rev 3, 7/30/2021

10/21/2022 15:24



Annular Clearance Variance



Offline Intermediate Cementing Procedure

2/24/2022

Cement Program

1. No changes to the cement program will take place for offline cementing.

Summarized Operational Procedure for Intermediate Casing

1. Run casing as per normal operations. While running casing, conduct negative pressure test and confirm integrity of the float equipment back pressure valves.
 - a. Float equipment is equipped with two back pressure valves rated to a minimum of 5,000 psi.
2. Land production casing on mandrel hanger through BOP.
 - a. If casing is unable to be landed with a mandrel hanger, then the **casing will be cemented online**.
3. Break circulation and confirm no restrictions.
 - a. Ensure no blockage of float equipment and appropriate annular returns.
 - b. Perform flow check to confirm well is static.
4. Set pack-off
 - a. If utilizing a fluted/ported mandrel hanger, ensure well is static on the annulus and inside the casing by filling the pipe with kill weight fluid, remove landing joint, and set annular packoff through BOP. Pressure test to 5,000 psi for 10 min.
 - b. If utilizing a solid mandrel hanger, ensure well is static on the annulus and inside the casing by filling the pipe with kill weight fluid. Pressure test seals to 5,000 psi for 10 min. Remove landing joint through BOP.
5. After confirmation of both annular barriers and the two casing barriers, install TA plug and pressure test to 5,000 psi for 10 min. Notify the BLM with intent to proceed with nipple down and offline cementing.
 - a. Minimum 4 hrs notice.
6. With the well secured and BLM notified, nipple down BOP and secure on hydraulic carrier or cradle.
 - a. **Note, if any of the barriers fail to test, the BOP stack will not be nipped down until after the cement job has concluded and both lead and tail slurry have reached 500 psi.**
7. Skid/Walk rig off current well.
8. Confirm well is static before removing TA Plug.
 - a. Cementing operations will not proceed until well is under control. (If well is not static, notify BLM and proceed to kill)
 - b. Casing outlet valves will provide access to both the casing ID and annulus. Rig or third party pump truck will kill well prior to cementing.
 - c. Well control plan can be seen in Section B, Well Control Procedures.
 - d. If need be, rig can be moved back over well and BOP nipped back up for any further remediation.



Offline Intermediate Cementing Procedure

2/24/2022

- e. Diagram for rig positioning relative to offline cementing can be seen in Figure 4.
9. Rig up return lines to take returns from wellhead to pits and rig choke.
 - a. Test all connections and lines from wellhead to choke manifold to 5,000 psi high for 10 min.
 - b. If either test fails, perform corrections and retest before proceeding.
 - c. Return line schematics can be seen in Figure 3.
10. Remove TA Plug from the casing.
11. Install offline cement tool.
 - a. Current offline cement tool schematics can be seen in Figure 1 (Cameron) and Figure 2 (Cactus).
12. Rig up cement head and cementing lines.
 - a. Pressure test cement lines against cement head to 80% of casing burst for 10 min.
13. Break circulation on well to confirm no restrictions.
 - a. If gas is present on circulation, well will be shut in and returns rerouted through gas buster.
 - b. Max anticipated time before circulating with cement truck is 6 hrs.
14. Pump cement job as per plan.
 - a. At plug bump, test casing to 0.22 psi/ft or 1500 psi, whichever is greater.
 - b. If plug does not bump on calculated, shut down and wait 8 hrs or 500 psi compressive strength, whichever is greater before testing casing.
15. Confirm well is static and floats are holding after cement job.
 - a. With floats holding and backside static:
 - i. Remove cement head.
 - b. If floats are leaking:
 - i. Shut-in well and WOC (Wait on Cement) until tail slurry reaches 500 psi compressive strength and the casing is static prior to removing cement head.
 - c. If there is flow on the backside:
 - i. Shut in well and WOC until tail slurry reaches 500 psi compressive strength. Ensure that the casing is static prior to removing cement head.
16. Remove offline cement tool.
17. Install night cap with pressure gauge for monitoring.
18. Test night cap to 5,000 psi for 10 min.



Offline Intermediate Cementing Procedure

2/24/2022

Example Well Control Plan Content

A. Well Control Component Table

The table below, which covers the cementing of the **5M MASP (Maximum Allowable Surface Pressure) portion of the well**, outlines the well control component rating in use. This table, combined with the mud program, documents that two barriers to flow can be maintained at all times, independent of the BOP nipped up to the wellhead.

Intermediate hole section, 5M requirement

| Component | RWP |
|--------------------------|-----|
| Pack-off | 10M |
| Casing Wellhead Valves | 10M |
| Annular Wellhead Valves | 5M |
| TA Plug | 10M |
| Float Valves | 5M |
| 2" 1502 Lo-Torque Valves | 15M |

B. Well Control Procedures

Well control procedures are specific to the rig equipment and the operation at the time the kick occurs. Below are the minimal high-level tasks prescribed to assure a proper shut-in while circulating and cementing through the Offline Cement Adapter.

General Procedure While Circulating

1. Sound alarm (alert crew).
2. Shut down pumps.
3. Shut-in Well (close valves to rig pits and open valve to rig choke line. Rig choke will already be in the closed position).
4. Confirm shut-in.
5. Notify tool pusher/company representative.



Offline Intermediate Cementing Procedure

2/24/2022

6. Read and record the following:
 - a. SICP (Shut in Casing Pressure) and AP (Annular Pressure)
 - b. Pit gain
 - c. Time
 - d. Regroup and identify forward plan to continue circulating out kick via rig choke and mud/gas separator. Circulate and adjust mud density as needed to control well.

General Procedure While Cementing

1. Sound alarm (alert crew).
2. Shut down pumps.
3. Shut-in Well (close valves to rig pits and open valve to rig choke line. Rig choke will already be in the closed position).
4. Confirm shut-in.
5. Notify tool pusher/company representative.
6. Open rig choke and begin pumping again taking returns through choke manifold and mud/gas separator.
7. Continue to place cement until plug bumps.
8. At plug bump close rig choke and cement head.
9. Read and record the following
 - a. SICP and AP
 - b. Pit gain
 - c. Time
 - d. Shut-in annulus valves on wellhead

General Procedure After Cementing


1. Sound alarm (alert crew).
2. Shut-in Well (close valves to rig pits and open valve to rig choke line. Rig choke will already be in the closed position).
3. Confirm shut-in.
4. Notify tool pusher/company representative.
5. Read and record the following:
 - a. SICP and AP
 - b. Pit gain
 - c. Time
 - d. Shut-in annulus valves on wellhead



Offline Intermediate Cementing Procedure

2/24/2022

Figure 1: Cameron TA Plug and Offline Adapter Schematic

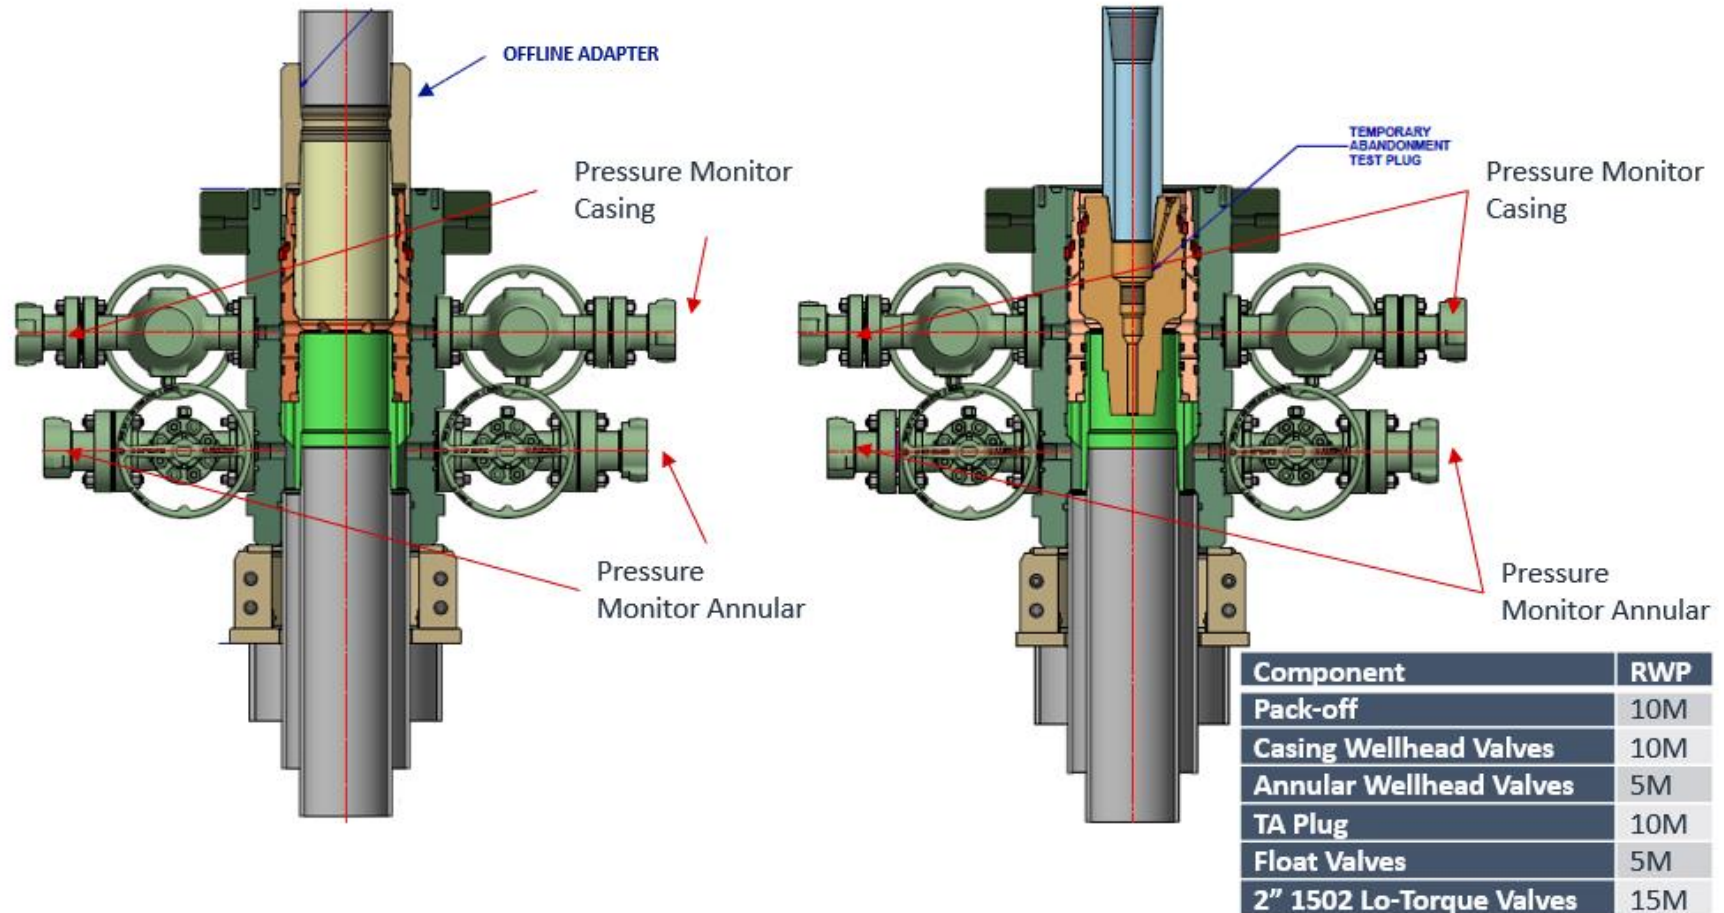




Offline Intermediate Cementing Procedure

2/24/2022

Figure 2: Cactus TA Plug and Offline Adapter Schematic

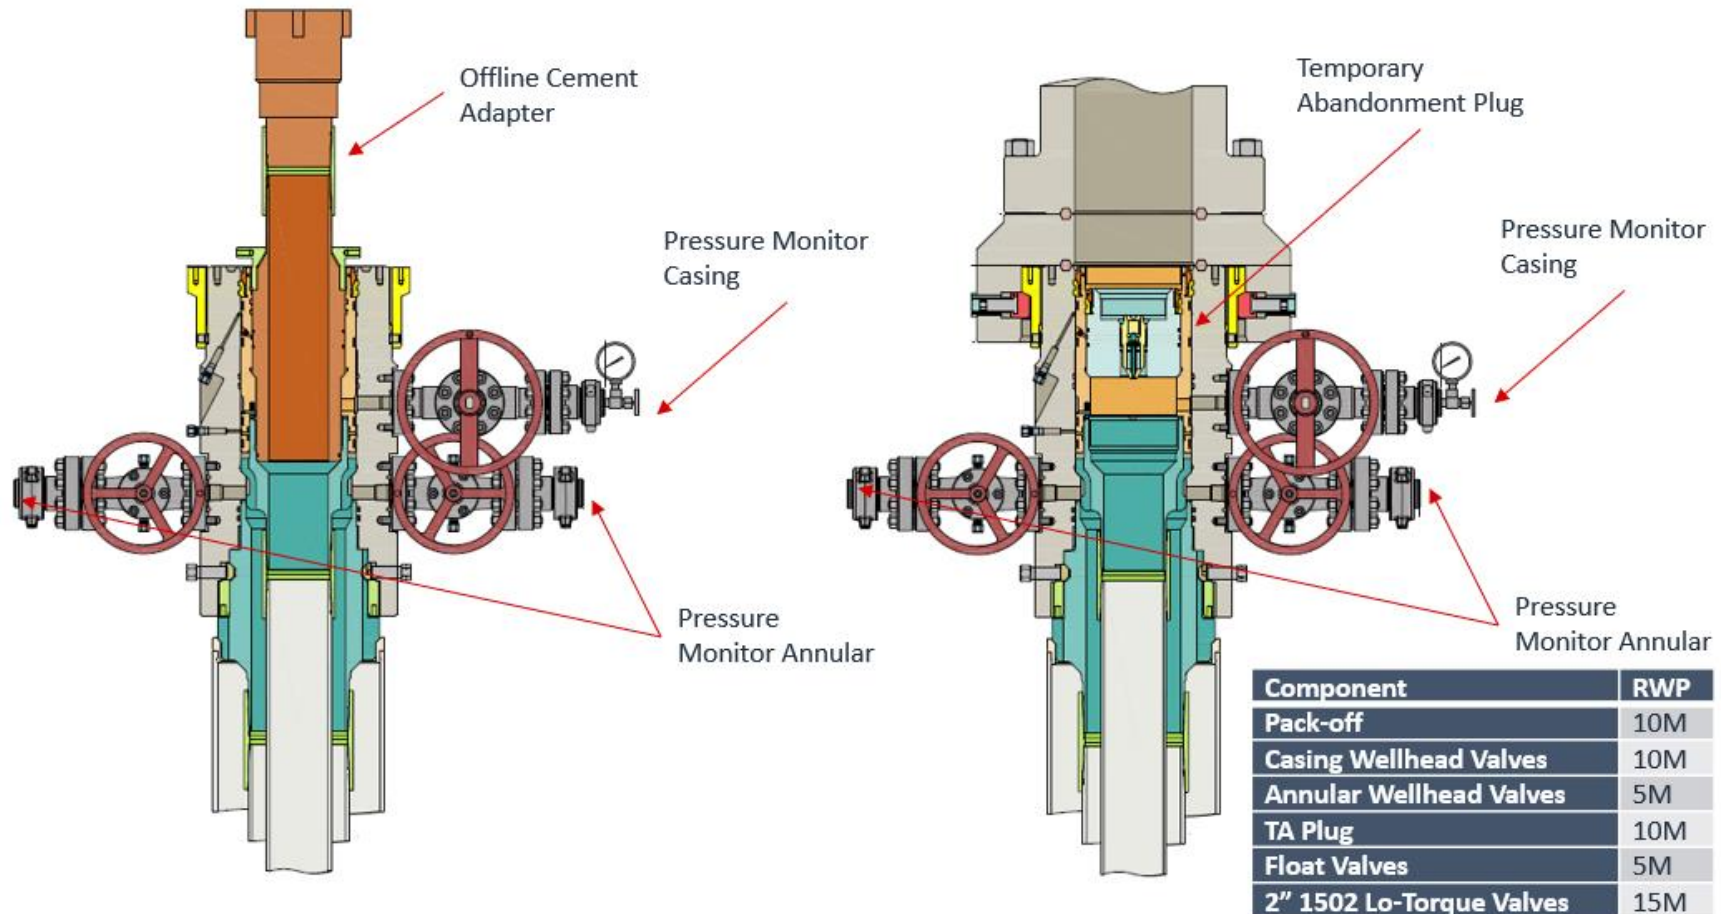




Offline Intermediate Cementing Procedure

2/24/2022

Figure 3: Back Yard Rig Up

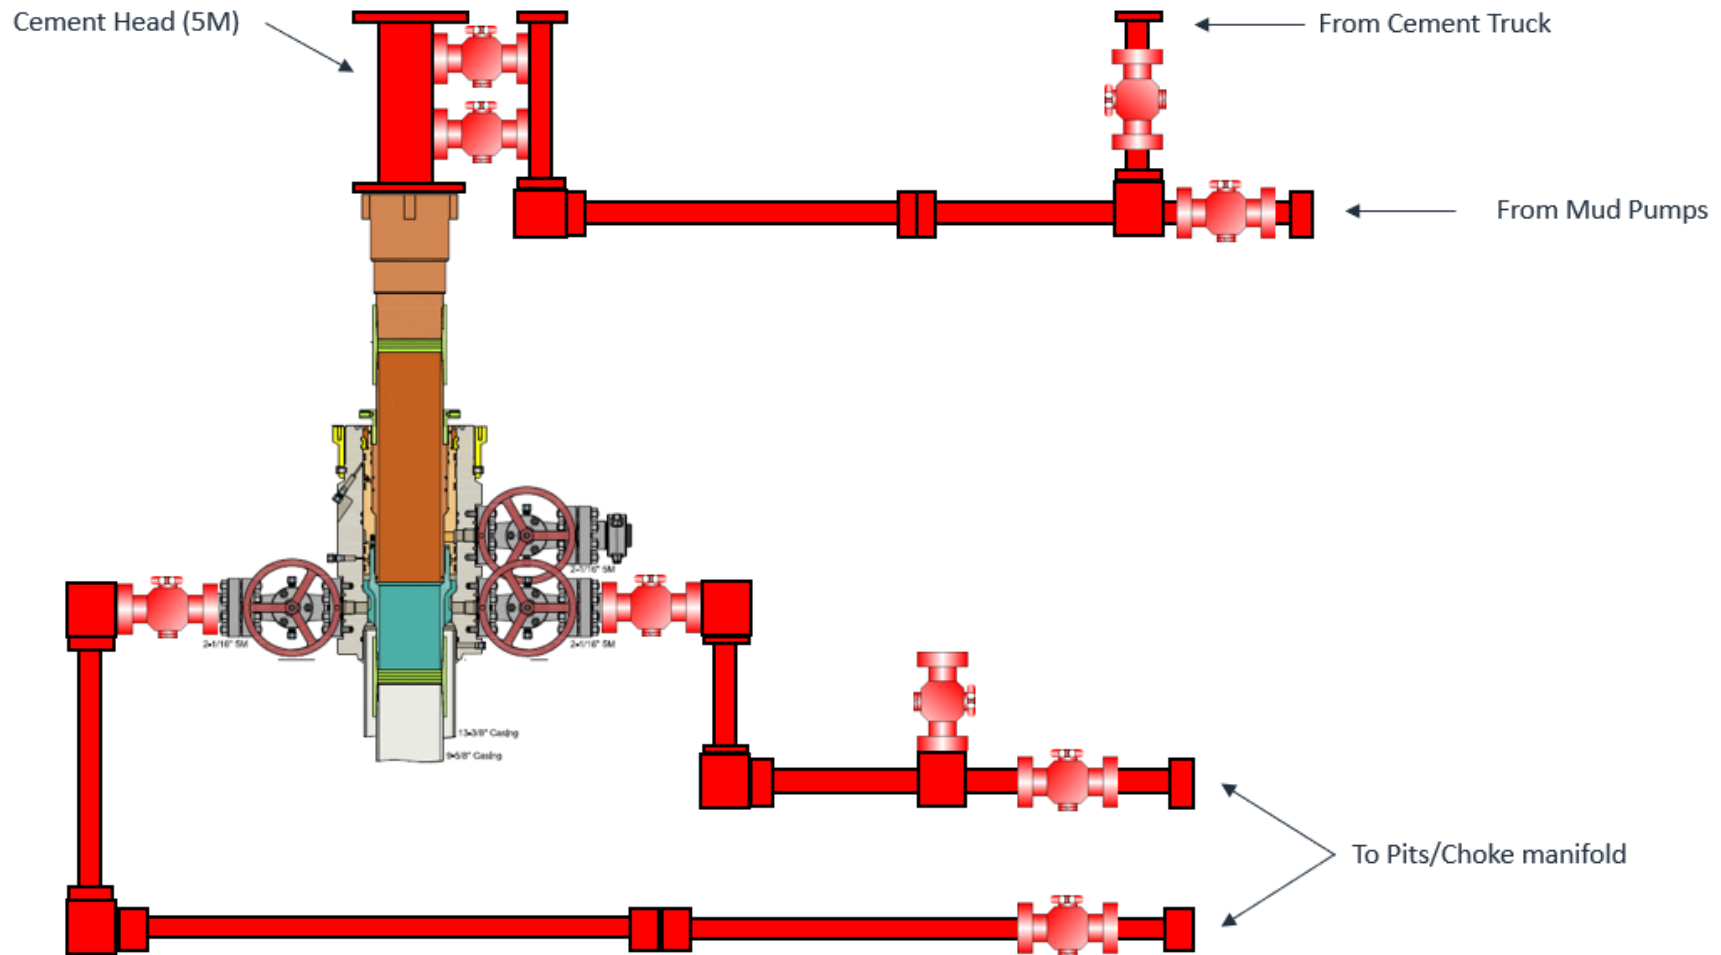


*** All Lines 10M rated working pressure



Offline Intermediate Cementing Procedure

2/24/2022

Figure 4: Rig Placement Diagram

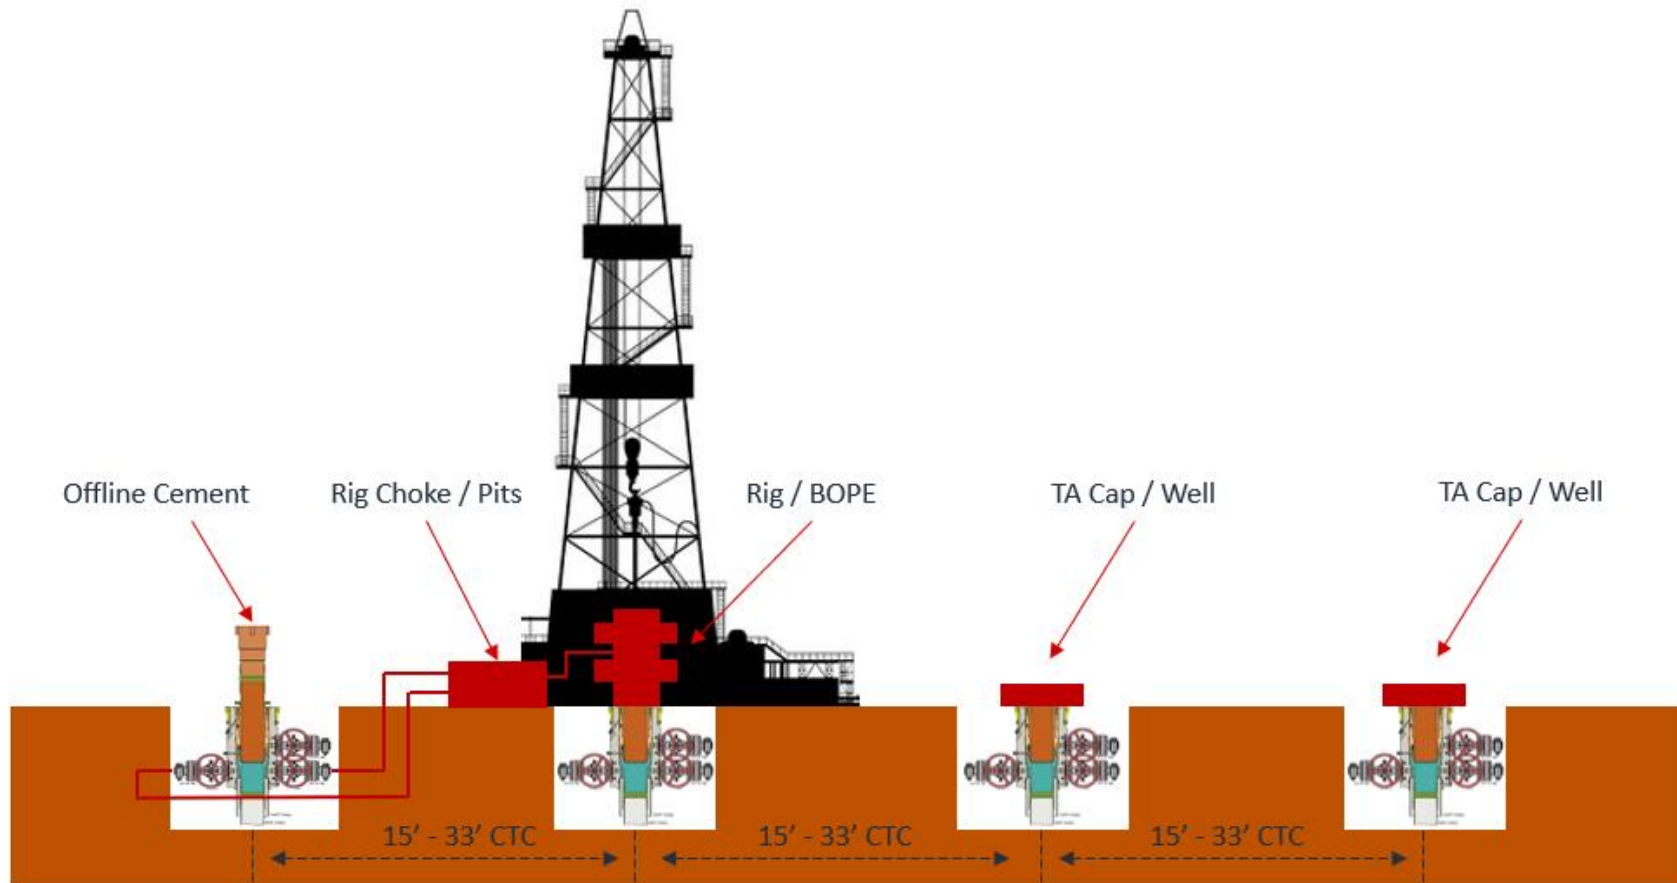

District I
1625 N. French Dr., Hobbs, NM 88240
Phone:(575) 393-6161 Fax:(575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone:(575) 748-1283 Fax:(575) 748-9720
District III
1000 Rio Brazos Rd., Aztec, NM 87410
Phone:(505) 334-6178 Fax:(505) 334-6170
District IV
1220 S. St Francis Dr., Santa Fe, NM 87505
Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 180876

CONDITIONS

| | |
|--|--|
| Operator: EOG RESOURCES INC P.O. Box 2267 Midland, TX 79702 | OGRID: 7377 |
| | Action Number: 180876 |
| | Action Type: [C-103] NOI Change of Plans (C-103A) |

CONDITIONS

| | | |
|------------|-----------|----------------|
| Created By | Condition | Condition Date |
| pkautz | None | 2/2/2023 |
