

Sundry Print Report

U.S. Department of the Interior BUREAU OF LAND MANAGEMENT

Well Name: BENNETT RANCH UNIT Well Location: T26S / R12E / SEC 25 / County or Parish/State: OTERO

SWNE / / NM

Well Number: 25-1 Type of Well: CONVENTIONAL GAS Allottee or Tribe Name:

WELL

Unit or CA Name: BENNETT RANCH - Unit or CA Number:

Lease Number: NMNM95620 Unit or CA Name: BENNETT RANCH - Unit or CA Nur CANYON PA Unit or CA Nur NMNM94469B

US Well Number: 3003520031 Well Status: Gas Well Shut In Operator: HEYCO

DEVELOPMENT CORPORATION

Subsequent Report

Sundry ID: 2728353

Type of Submission: Subsequent Report

Type of Action: Plug and Abandonment

Date Sundry Submitted: 05/01/2023 Time Sundry Submitted: 07:32

Date Operation Actually Began: 02/27/2023

Actual Procedure: See attached daily report and well bore diagram.

SR Attachments

Actual Procedure

BRU_25_1_Daily_Report_20230501073100.pdf

HEYCO_25_1_P_A_WBD_corrected_20230501073100.pdf

Accepted for record – NMOCD

JRH <u>05/08/2023</u>

Well Name: BENNETT RANCH UNIT

25

Well Location: T26S / R12E / SEC 25 /

SWNE /

County or Parish/State: Ofero

/ NM

Well Number: 25-1 Type of Well: CONVENTIONAL GAS

WĖLL

Allottee or Tribe Name:

Lease Number: NMNM95620 Unit or CA Name: BENNETT RANCH - Unit or

CANYON PA

Unit or CA Number:

NMNM94469B

US Well Number: 3003520031 Well Status: Gas Well Shut In Operator: HEYCO

DEVELOPMENT CORPORATION

Zip:

Operator

I certify that the foregoing is true and correct. Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction. Electronic submission of Sundry Notices through this system satisfies regulations requiring a

Operator Electronic Signature: BRIAN WOOD Signed on: MAY 01, 2023 07:31 AM

Name: HEYCO DEVELOPMENT CORPORATION

Title: President

Street Address: 37 VERANO LOOP

City: SANTA FE State: NM

Phone: (505) 466-8120

Email address: AFMSS@PERMITSWEST.COM

Field

Representative Name:

Street Address:

City:

Phone:

Email address:

BLM Point of Contact

BLM POC Name: JENNIFER SANCHEZ BLM POC Title: Petroleum Engineer

BLM POC Phone: 5756270237 BLM POC Email Address: j1sanchez@blm.gov

Disposition: Accepted **Disposition Date:** 05/03/2023

State:

Signature: Jennifer Sanchez

Page 2 of 2

O DEVELOPMENT CORPORA

Daily Report of Operations

Well Name:

BENNETT RANCH 25-1

Field Name:

API# 300 35-20031 Current Zone of Interest: Date: Supervisor: 2/27/23 Jack Gustamantes

Producing Zone

PLUGG NG

	. Dodg No
2/27/22	Detailed Description of Day's Operation
2/27/23	Moved rest of equipment to location, rigged up plugging rig, hooked up pump to kill well. Shut down
2/28/23	Killed well and unset packer, pulled packer, then ran CIBP set it, mixed 32 bbls MLF, pumped it,
	mixed 40sx cement, pumped it on top of CIBP, pulled tubing out of hole.
3/1/23	Tagged cement on top of CIBP @ 1760', perforated @ 542', then pumped through perfs, mixed 45sx cement
	and started pumping down 5 1/2 casing, got down about 215" and started pressuring up, went to 500PSI
	then hooked up and pumped rest of cement down 9 5/8 and 13 3/8. Will check tomorrow for depths.
3/2/23	Took off top flange and checked cement in 5 1/2 casing, cement was down 6' from surface, will do cutoff
	on Monday 3/6/23 and check cement on surface casings.
3/6/23	Decided to drill out cement.
37 07 23	seduce to drill out cerrent.
3/7/23	Moved in drillout equipment and started drilling out top plug.
	, ,
3/8/23	Finished drilling out top plug and tested perfs again, pressured up. Ran 600' of tubing and then
1	mixed 25 sx cement and pumped it.
3/9/23	Tagged at 356', will perforate Monday at 100' and attempt to squeeze.
3/15/23	Perforated at 100', tried to pump into perfs, pressured up to 500 psi, ran 152' of tubing, circulated to
5	surface, pulled tubing and then filled hole.
3/16/23	Did cutoff, will have to do 1" on 13 3/8 and 9 5/8 on Monday.
3/20/23	Did 1' job between 9 5/8 and 5 1/2, then did 1' job between 9 5/8 and 13 3/8, laid down 1' tubing and
t	hen topped off both casings. Went down 60' between 9 5/8 and 5 1/2 and 55' between 9 5/8 and 13 3/8.
3/21/23	Checked cement in all casings, topped off and then welded top plate and dry hole plate.

Service Rig: Prepared by: Prepared for:

3G Well Service Co, LLP

Jack JOHN

3G UNDERWOOD 575 420 8547 214-725-2334

0

WELLBORE DIAGRAM

Bennet Ranch Unit 25-1 API 30-035-20031

PLUGS

NOT TO SCALE

Depth

210


1720

1735

1900

2405

2840

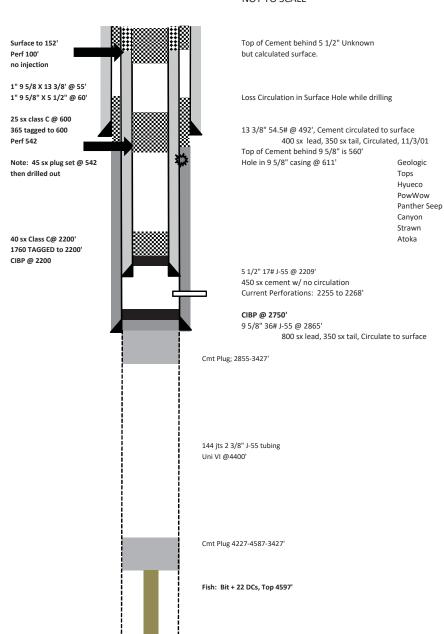

PBTD '

TD 5671

District III

District I
1625 N. French Dr., Hobbs, NM 88240
Phone: (575) 393-6161 Fax: (575) 393-0720

District II 811 S. First St., Artesia, NM 88210 Phone:(575) 748-1283 Fax:(575) 748-9720

1000 Rio Brazos Rd., Aztec, NM 87410 Phone:(505) 334-6178 Fax:(505) 334-6170

1220 S. St Francis Dr., Santa Fe, NM 87505 Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico Energy, Minerals and Natural Resources Oil Conservation Division 1220 S. St Francis Dr. **Santa Fe, NM 87505**

CONDITIONS

Action 214279

CONDITIONS

Operator:	OGRID:
HEYCO DEVELOPMENT CORPORATION	370234
P.O. Box 1933	Action Number:
Roswell, NM 88202	214279
	Action Type:
	[C-103] Sub. Plugging (C-103P)

CONDITIONS

Created By		Condition Date
john.harrison	None	5/8/2023
