

Form 3160-3
(June 2015)FORM APPROVED
OMB No. 1004-0137
Expires: January 31, 2018

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
APPLICATION FOR PERMIT TO DRILL OR REENTER

1a. Type of work: <input type="checkbox"/> DRILL <input type="checkbox"/> REENTER 1b. Type of Well: <input type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input type="checkbox"/> Other 1c. Type of Completion: <input type="checkbox"/> Hydraulic Fracturing <input type="checkbox"/> Single Zone <input type="checkbox"/> Multiple Zone		5. Lease Serial No. 6. If Indian, Allottee or Tribe Name 7. If Unit or CA Agreement, Name and No. 8. Lease Name and Well No.
2. Name of Operator		9. API Well No. 30-039-31439
3a. Address	3b. Phone No. (include area code)	10. Field and Pool, or Exploratory
4. Location of Well (Report location clearly and in accordance with any State requirements. *) At surface At proposed prod. zone		11. Sec., T. R. M. or Blk. and Survey or Area
14. Distance in miles and direction from nearest town or post office*		12. County or Parish
13. State		
15. Distance from proposed* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any)	16. No of acres in lease	17. Spacing Unit dedicated to this well
18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft.	19. Proposed Depth	20. BLM/BIA Bond No. in file
21. Elevations (Show whether DF, KDB, RT, GL, etc.)	22. Approximate date work will start*	23. Estimated duration
24. Attachments		

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, and the Hydraulic Fracturing rule per 43 CFR 3162.3-3 (as applicable)

- | | |
|---|---|
| 1. Well plat certified by a registered surveyor.
2. A Drilling Plan.
3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office). | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).
5. Operator certification.
6. Such other site specific information and/or plans as may be requested by the BLM. |
|---|---|

25. Signature	Name (Printed/Typed)	Date
Title		
Approved by (Signature)	Name (Printed/Typed)	Date
Title		
Office		

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
 Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Continued on page 2)

*(Instructions on page 2)



INSTRUCTIONS

GENERAL: This form is designed for submitting proposals to perform certain well operations, as indicated on Federal and Indian lands and leases for action by appropriate Federal agencies, pursuant to applicable Federal laws and regulations. Any necessary special instructions concerning the use of this form and the number of copies to be submitted, particularly with regard to local, area, or regional procedures and practices, either are shown below or will be issued by, or may be obtained from local Federal offices.

ITEM I: If the proposal is to redrill to the same reservoir at a different subsurface location or to a new reservoir, use this form with appropriate notations. Consult applicable Federal regulations concerning subsequent work proposals or reports on the well.

ITEM 4: Locations on Federal or Indian land should be described in accordance with Federal requirements. Consult local Federal offices for specific instructions.

ITEM 14: Needed only when location of well cannot readily be found by road from the land or lease description. A plat, or plats, separate or on the reverse side, showing the roads to, and the surveyed location of, the well, and any other required information, should be furnished when required by Federal agency offices.

ITEMS 15 AND 18: If well is to be, or has been directionally drilled, give distances for subsurface location of hole in any present or objective productive zone.

ITEM 22: Consult applicable Federal regulations, or appropriate officials, concerning approval of the proposal before operations are started.

ITEM 24: If the proposal will involve hydraulic fracturing operations, you must comply with 43 CFR 3162.3-3, including providing information about the protection of usable water. Operators should provide the best available information about all formations containing water and their depths. This information could include data and interpretation of resistivity logs run on nearby wells. Information may also be obtained from state or tribal regulatory agencies and from local BLM offices.

NOTICES

The Privacy Act of 1974 and regulation in 43 CFR 2.48(d) provide that you be furnished the following information in connection with information required by this application.

AUTHORITY: 30 U.S.C. 181 et seq., 25 U.S.C. 396; 43 CFR 3160

PRINCIPAL PURPOSES: The information will be used to: (1) process and evaluate your application for a permit to drill a new oil, gas, or service well or to reenter a plugged and abandoned well; and (2) document, for administrative use, information for the management, disposal and use of National Resource Lands and resources including (a) analyzing your proposal to discover and extract the Federal or Indian resources encountered; (b) reviewing procedures and equipment and the projected impact on the land involved; and (c) evaluating the effects of the proposed operation on the surface and subsurface water and other environmental impacts.

ROUTINE USE: Information from the record and/or the record will be transferred to appropriate Federal, State, and local or foreign agencies, when relevant to civil, criminal or regulatory investigations or prosecution, in connection with congressional inquiries and for regulatory responsibilities.

EFFECT OF NOT PROVIDING INFORMATION: Filing of this application and disclosure of the information is mandatory only if you elect to initiate a drilling or reentry operation on an oil and gas lease.

The Paperwork Reduction Act of 1995 requires us to inform you that:

The BLM connects this information to an evaluation of the technical, safety, and environmental factors involved with drilling for oil and/or gas on Federal and Indian oil and gas leases. This information will be used to analyze and approve applications. Response to this request is mandatory only if the operator elects to initiate drilling or reentry operations on an oil and gas lease. The BLM would like you to know that you do not have to respond to this or any other Federal agency-sponsored information collection unless it displays a currently valid OMB control number.

BURDEN HOURS STATEMENT: Public reporting burden for this form is estimated to average 8 hours per response, including the time for reviewing instructions, gathering and maintaining data, and completing and reviewing the form. Direct comments regarding the burden estimate or any other aspect of this form to U.S. Department of the Interior, Bureau of Land Management (1004-0137), Bureau Information Connection Clearance Officer (WO-630), 1849 C Street, N.W., Mail Stop 401 LS, Washington, D.C. 20240.

Additional Operator Remarks

Location of Well

0. SHL: NESE / 2592 FSL / 1308 FEL / TWSP: 31N / RANGE: 5W / SECTION: 7 / LAT: 36.913904 / LONG: -107.399208 (TVD: 0 feet, MD: 0 feet)

PPP: LOT 4 / 0 FSL / 0 FEL / TWSP: 31N / RANGE: 5W / SECTION: 12 / LAT: 0.0 / LONG: 0.0 (TVD: 0 feet, MD: 0 feet)

PPP: SESE / 0 FSL / 0 FEL / TWSP: 31N / RANGE: 5W / SECTION: 11 / LAT: 0.0 / LONG: 0.0 (TVD: 0 feet, MD: 0 feet)

PPP: SWSE / 1151 FSL / 1957 FEL / TWSP: 31N / RANGE: 5W / SECTION: 7 / LAT: 36.909948 / LONG: -107.401424 (TVD: 6930 feet, MD: 7461 feet)

BHL: SWSW / 1174 FSL / 1136 FWL / TWSP: 31N / RANGE: 6W / SECTION: 11 / LAT: 36.910114 / LONG: -107.437343 (TVD: 6897 feet, MD: 17962 feet)

CONFIDENTIAL

Review and Appeal Rights

A person contesting a decision shall request a State Director review. This request must be filed within 20 working days of receipt of the Notice with the appropriate State Director (see 43 CFR 3165.3). The State Director review decision may be appealed to the Interior Board of Land Appeals, 801 North Quincy Street, Suite 300, Arlington, VA 22203 (see 43 CFR 3165.4). Contact the above listed Bureau of Land Management office for further information.

CONFIDENTIAL



United States Department of the Interior

BUREAU OF LAND MANAGEMENT
Farmington District Office
6251 College Blvd, Suite A
Farmington, New Mexico 87402



In Reply Refer To:
3162.3-1(NMF0110)

* LOGOS OPERATING LLC

#702H ROSA UNIT

Lease: NMSF078767 Unit: NMNM78407E
SH: NE $\frac{1}{4}$ SE $\frac{1}{4}$ Section 7, T.31 N., R.5 W.
Rio Arriba County, New Mexico
BH: SW $\frac{1}{4}$ SW $\frac{1}{4}$ Section 11, T.31 N., R.6 W.
Rio Arriba County, New Mexico

***Above Data Required on Well Sign**

GENERAL REQUIREMENTS FOR OIL AND GAS OPERATIONS ON FEDERAL AND INDIAN LEASES

The following special requirements apply and are effective when **checked**:

- A. ☒ Note all surface/drilling conditions of approval attached.
- B. ☒ The required wait on cement (WOC) time will be a minimum of 500 psi compressive strength at 60 degrees. Blowout preventor (BOP) nipple-up operations may then be initiated
- C. ☒ Test all casing strings below the conductor casing to .22 psi/ft. of casing string length or 1500 psi, whichever is greater, but not to exceed 70% of the minimum internal yield (burst) for a minimum of 30 minutes. If pressure declines more than 10 percent in 30 minutes, corrective action shall be taken.
- D. ☐ Communitization Agreement covering the acreage dedicated to this well must be filed for approval with the Bureau of Land Management, New Mexico State Office, Reservoir Management Group, 301 Dinosaur Trail, Santa Fe, New Mexico 87508.
The effective date of the agreement must be **prior** to any sales.
- E. ☐ The use of co-flex hose is authorized contingent upon the following:
 1. From the BOP to the choke manifold: the co-flex hose must be hobbled on both ends and saddle to prevent whip.
 2. From the choke manifold to the discharge tank: the co-flex hoses must be as straight as practical, hobbled on both ends and anchored to prevent whip.
 3. The co-flex hose pressure rating must be at least commensurate with approved BOPE.

INTERIOR REGION 7 • UPPER COLORADO BASIN

COLORADO, NEW MEXICO, UTAH, WYOMING

I. GENERAL

- A. Full compliance with all applicable laws and regulations, with the approved Permit to drill, and with the approved Surface Use and Operations Plan is required. Lessees and/or operators are fully accountable for the actions of their contractors and subcontractors. Failure to comply with these requirements and the filing of required reports will result in strict enforcement pursuant to 43 CFR 3163.1 or 3163.2.
- B. Each well shall have a well sign in legible condition from spud date to final abandonment. The sign should show the operator's name, lease serial number, or unit name, well number, location of the well, and whether lease is Tribal or Allotted, (See 43 CFR 3162.6(b)).
- C. A complete copy of the approved Application for Permit to Drill, along with any conditions of approval, shall be available to authorized personnel at the drill site whenever active drilling operations are under way.
- D. For Wildcat wells only, a drilling operations progress report is to be submitted, to the BLM-Field Office, weekly from the spud date until the well is completed and the Well Completion Report is filed. The report should be on 8-1/2 x 11 inch paper, and each page should identify the well by; operator's name, well number, location and lease number.
- E. As soon as practical, notice is required of all blowouts, fires and accidents involving life-threatening injuries or loss of life. (See NTL-3A).
- F. BOP equipment (except the annular preventer) shall be tested utilizing a test plug to full working pressure for 10 minutes. No bleed-off of pressure is acceptable.
- G. The operator shall have sufficient weighting materials and lost circulation materials on location in the event of a pressure kick or in the event of lost circulation
- H. The flare line(s) discharge shall be located not less than 100 feet from the well head, having straight lines unless turns are targeted with running tees, and shall be positioned downwind of the prevailing wind direction and shall be anchored. The flare system shall have an effective method for ignition. Where noncombustible gas is likely or expected to be vented, the system shall be provided supplemental fuel for ignition and to maintain a continuous flare.
- I. Prior approval by the BLM-Authorized Office (Drilling and Production Section) is required for variance from the approved drilling program and before commencing plugging operations, plug back work, casing repair work, corrective cementing operations, or suspending drilling operations indefinitely. Emergency approval may be obtained orally, but such approval is contingent upon filing of a Notice of Intent sundry within three business days. **Any changes to the approved plan or any questions regarding drilling operations should be directed to BLM during regular business hours at 505-564-7600. Emergency program changes after hours should be directed to Virgil Lucero at 505-793-1836.**
- J. The Inspection and Enforcement Section (I&E), phone number (505-564-7750) is to be notified at least 24 hours in advance of BOP test, spudding, cementing, or plugging operations so that a BLM representative may witness the operations.

- K. Unless drilling operations are commenced within two years, approval of the Application for Permit to Drill will expire. A written request for a two-year extension may be granted if submitted prior to expiration.
- L. From the time drilling operations are initiated and until drilling operations are completed, a member of the drilling crew or the tool pusher shall always maintain rig surveillance, unless the well is secured with blowout preventers or cement plugs.
- M. If for any reason, drilling operations are suspended for more than 90 days, a written notice must be provided to this office outlining your plans for this well.
- N. **Commingling:** No production (oil, gas, and water) from the subject well should start until Sundry Notices (if necessary) granting variances from applicable regulations as related to commingling and off-lease measurement are approved by this office.

II. REPORTING REQUIREMENTS

- A. For reporting purposes, all well Sundry notices, well completion and other well actions shall be referenced by the appropriate lease, communitization agreement and/or unit agreement numbers.
- B. The following reports shall be filed with the BLM-Authorized Officer within 30 days after the work is completed.
 - 1. Provide complete information concerning.
 - a. Setting of each string of casing. Show size and depth of hole, grade and weight of casing, depth set, depth of all cementing tools that are used, amount (in cubic feet) and types of cement used, whether cement circulated to surface and all cement tops in the casing annulus, casing test method and results, and the date work was done. Show spud date on first report submitted.
 - b. Intervals tested, perforated (include size, number and location of perforations), acidized, or fractured; and results obtained. Provide date work was done on well completion report and completion sundry notice.
 - c. Subsequent Report of Abandonment, show the way the well was plugged, including depths where casing was cut and pulled, intervals (by depths) where cement plugs were replaced, and dates of the operations.
 - 2. Well Completion Report will be submitted with 30 days after well has been completed.
 - a. Initial Bottom Hole Pressure (BHP) for the producing formations. Show the BHP on the completion report. The pressure may be: 1) measured with a bottom hole bomb, or; 2) calculated based on shut in surface pressures (minimum seven day buildup) and fluid level shot.
 - 3. Submit a cement evaluation log if cement is not circulated to surface.

- C. Production Startup Notification is required no later than the 5th business day after any well begins production on which royalty is due anywhere on a lease site or allocated to a lease site or resumes production in the case of a well which has been off production for more than 90 days. The operator shall notify the Authorized Officer by letter or Sundry Notice, Form 3160-5, or orally to be followed by a letter or Sundry Notice, of the date on which such production has begun or resumed. CFR 43 3162.4-1(c).

III. DRILLER'S LOG

The following shall be entered in the daily driller's log: 1) Blowout preventer pressures tests, including test pressures and results, 2) Blowout preventer tests for proper functioning, 3) Blowout prevention drills conducted, 4) Casing run, including size, grade, weight, and depth set, 5) How pipe was cemented, including amount of cement, type, whether cement circulated to surface, location of cementing tools, etc., 6) Waiting on cement time for each casing string, 7) Casing pressure tests after cementing, including test pressure and results, and 8) Estimated amounts of oil and gas recovered and/or produced during drill stem test.

IV. GAS FLARING

Gas produced from this well may not be vented or flared beyond an initial, authorized test period of * Days or 50 MMCF following its (completion)(recompletion), whichever first occurs, without the prior, written approval of the authorized officer. Should gas be vented or flared without approval beyond the test period authorized above, you may be directed to shut-in the well until the gas can be captured or approval to continue venting or flaring as uneconomic is granted. You shall be required to compensate the lessor for the portion of the gas vented or flared without approval which is determined to have been avoidably lost.

*30 days, unless a longer test period is specifically approved by the authorized officer. The 30-day period will commence upon the first gas to surface.

V. SAFETY

- A. All rig heating stoves are to be of the explosion-proof type.
- B. Rig safety lines are to be installed.
- C. Hard hats and other Personal Protective Equipment (PPE) must be utilized.

VI. CHANGE OF PLANS OR ABANDONMENT

- A. Any changes of plans required to mitigate unanticipated conditions encountered during drilling operations, will require approval as set forth in Section 1.F.
- B. If the well is dry, it is to be plugged in accordance with 43 CFR 3162.3-4, approval of the proposed plugging program is required as set forth in Section 1.F. The report should show the total depth reached, the reason for plugging, and the proposed intervals, by depths, where cement plugs are to be placed, type of plugging mud, etc. A Subsequent Report of Abandonment is required as set forth in Section II.B.1c.
- C. Unless a well has been properly cased and cemented, or properly plugged, the drilling rig must not be moved from the drill site without prior approval from the BLM-Authorized Officer.

Conditions of Approval

Operator: Logos Operating, LLC
Well Names: Rosa Unit Pad 24 (700H, 701H, 702H, 704H, 705H, 706H + 8 futures)
Legal Location: Sec7, TwN 31N, R 5W, Rio Arriba County, NM
NEPA Log Number: DOI-BLM-NM-F010-2022-0060-EA
Inspection Date: February 1, 2022
Lease Number: NMNM78407E

The following conditions of approval will apply to Logos Operating's Rosa Unit Pad 24 Project, and other associated facilities, unless a particular Surface Managing Agency or private surface owner has supplied to Bureau of Land Management and the operator a contradictory environmental stipulation. The failure of the operator to comply with these requirements may result in an assessment or civil penalties pursuant to 43 CFR 3163.1 or 3163.2.

Disclaimers: BLM's approval of the APD does not relieve the lessee and operator from obtaining any other authorizations that may be required by the BIA, Navajo Tribe, State, or other jurisdictional entities.

Copy of Plans: A complete copy of the APD package, including Surface Use Plan of Operations, Bare Soil Reclamation Plan, Plan of Development (if required), Conditions of Approval, Cultural Resource Record of Review, Cultural Resources Compliance Form (if required), and Project Stipulations (if required) shall be at the project area at all times and available to all persons.

Review of NEPA documents: It is the responsibility of the operator to follow all the design features, best management practices, and mitigation measures as contained in the Environmental Assessment DOI-BLM-NM-F010-2022-0060-EA, which contains additional design features and best management practices that must be followed. Copies of the EA, Decision Record, and Finding of No Significant Impact may be obtained from the BLM FFO public room, or online at: [EplanningUi \(blm.gov\)](https://eplanningui.blm.gov).

Best Management Practices (BMPs): Farmington Field Office established environmental Best Management Practices (BMP's) will be followed during construction and reclamation of well site pads, access roads, pipeline ties, facility placement or any other surface disturbing activity associated with this project. Bureau wide standard BMP's are found in the Gold Book, Fourth Edition-Revised 2007 and at http://www.blm.gov/wo/st/en/prog/energy/oil_and_gas/best_management_practices.html. Farmington Field Office BMPs are integrated into the Environmental Assessment, Surface Use Plan of Operations, Bare Soil Reclamation Plan, and COAs.

Construction, Production, Facilities, Reclamation & Maintenance

Construction & Reclamation Notification: The operator or their contractor will contact the Bureau of Land Management, Farmington Field Office Environmental Protection Staff (505) 564-7600 or by email, at least 48 hours prior to any construction or reclamation on this project.

Production Facilities: design and layout of facilities will be deferred until an onsite with BLM-FFO surface protection staff is conducted to determine the best location. Logos or their contractor will contact the Bureau of Land Management, Farmington Field Office, Surface, and Environmental Protection Staff (505) 564-7600 to schedule a facility layout onsite.

Staking: The holder shall place slope stakes, culvert location and grade stakes, and other construction control stakes as deemed necessary by the authorized officer to ensure construction in accordance with the plan of development. If stakes are disturbed, they shall be replaced before proceeding with construction.

Weather: No construction or routine maintenance activities shall be performed during periods when the soil is too wet to adequately support construction equipment. If such equipment creates ruts more than 6 inches deep, the soil shall be deemed too wet.

Stockpile of Soil: The top 6 inches of soil material will be stripped and stockpiled in the construction zones around the pad [construction zones may be restricted or deleted to provide resource avoidance]. The stockpiled soil will be free of brush and tree limbs, trunks, and roots. The stockpiled soil material will be spread on the reclaimed portions of the pad [including the reserve pit, cut and fill slopes] prior to re-seeding. Spreading shall not be done when the ground or topsoil is frozen or wet.

Storage Tanks: All open top permanent production or storage tanks regardless of diameter made of fiberglass, steel, or other material used for the containment of oil, condensate, produced water and or other production waste shall be screened, netted, or otherwise covered to protect migratory birds and other wildlife from access.

Compressors: Compressor units on this well location not equipped with a drip pan for containment of fluids shall be lined with an impervious material at least 8 mils thick and a 12-inch berm. The compressor will be painted to match the well facilities. Any variance to this will be approved by the Authorized Officer (AO). Noise mitigation may be required at the time of compressor installation.

Culverts: Silt Traps/Bell Holes will be built upstream of all culvert locations.

Driving Surface Area: All activities associated within the construction, operation, maintenance, and abandonment of the well location is limited to areas approved in the APD or ROW permit. During the production of the well, vehicular traffic is limited to the daily driving surface area established during interim reclamation construction operations. This area typically forms a keyhole or teardrop driving surface from which all production facilities may be serviced or

inspected. A v-type ditch will be constructed on the outside of the driving surface to further define the driving surface and to deter vehicular traffic from entering onto the interim reclamation areas.

Contouring of Cut and Fill Slopes: The interim cut and fill slope grade shall be as close to the original contour as possible. To obtain this ratio, pits and slopes shall be back sloped into the pad during interim reclamation. Only subsurface soil and material shall be utilized in the contouring of the cut and fill slopes. Under no circumstances shall topsoil be utilized as substrate material for contouring of cut and fill slopes.

Maintenance: In order to perform subsequent well operations, right-of-way (ROW) operations, or install new/additional equipment, it may be necessary to drive, park, and operate on restored, interim vegetation within the previously disturbed area. This is generally acceptable provided damage is promptly repaired and reclaimed following use. Where vehicular travel has occurred as a “convenience” and interim reclamation/vegetation has been compromised, immediate remediation of the affected areas is required. Additionally, where erosion has occurred and compromised the reclamation of the well location, the affected area must be promptly remediated so that future erosion is prevented, and the landform is stabilized.

Layflat Lines: Layflat lines used for development of the wells may be on the ground for a maximum of 6 months and shall be retrieved immediately following completion operations. If the layflat lines are needed for longer than 6 months a Sundry NOI shall be submitted to the BLM FFO for review and decision that includes a rationale for the time extension.

Noxious Weeds

Inventory the proposed site for the presence of noxious and invasive weeds. Noxious weeds are those listed on the New Mexico Noxious Weed List and USDA’s Federal Noxious Weed List. The New Mexico Noxious Weed List or USDA’s Noxious Weed List can be updated at any time and should be regularly check for any changes. Invasive species may or may not be listed as a noxious weed but have been identified to likely cause economic or environmental harm or harm to human health. The following noxious weeds have been identified as occurring on lands within the boundaries of the Farmington Field Office (FFO). There are numerous invasive species on the FFO such as Russian thistle (*Salsola spp.*) and field bindweed (*Convolvulus arvensis*).

Russian Knapweed (<i>Centaurea repens</i>)	Musk Thistle (<i>Carduss nutans</i>)
Bull Thistle (<i>Cirsium vulgare</i>)	Canada Thistle (<i>Cirsium arvense</i>)
Scotch Thistle (<i>Onopordum acanthium</i>)	Hoary Cress (<i>Cardaria draba</i>)
Perennial Pepperweed (<i>Lepidium latifolium</i>)	Halogeton (<i>Halogeton glomeratus</i>)
Spotted Knapweed (<i>Centaurea maculosa</i>)	Dalmation Toadflax (<i>Linaria genistifolia</i>)
Yellow Toadflax (<i>Linaria vulgaris</i>)	Camelthorn (<i>Alhagi pseudalhagi</i>)
African Rue (<i>Penganum harmala</i>)	Salt Cedar (<i>Tamarix spp.</i>)
Diffuse Knapweed (<i>Centaurea diffusa</i>)	Leafy Spurge (<i>Euphorbia esula</i>)

- a. Identified weeds will be treated prior to new surface disturbance if determined by the FFO Noxious Weed Coordinator. A Pesticide Use Proposal (PUP) must be submitted to and approved by the FFO Noxious Weed Coordinator prior to application of pesticide. The FFO Noxious Weeds Coordinator (505-564-7600) can provide assistance in the development of the PUP.
- b. Vehicles and equipment should be inspected and cleaned prior to coming onto the work site. This is especially important on vehicles from out of state or if coming from a weed-infested site.
- c. Fill dirt or gravel may be needed for excavation, road construction/repair, or for spill remediation. If fill dirt or gravel will be required, the source shall be noxious weed free and approved by the FFO Noxious Weed Coordinator.
- d. The site shall be monitored for the life of the project for the presence of noxious weeds (includes maintenance and construction activities). If weeds are found the FFO Coordinator shall be notified at (505) 564-7600 and provided with a Weed Management Plan and if necessary, a Pesticide Use Proposal (PUP). The FFO Coordinator can provide assistance developing the Weed Management Plan and/or the Pesticide Use Proposal.
- e. Only pesticides authorized for use on BLM lands would be used and applied by a licensed pesticide applicator. The use of pesticides would comply with federal and state laws and used only in accordance with their registered use and limitations. Logos's weed-control contractor would contact the BLM-FFO prior to using these chemicals.
- f. Noxious/invasive weed treatments must be reported to the FFO Noxious Weed Coordinator. A Pesticide Use Report (PUR) is required to report any mechanical, chemical, biological, or cultural treatments used to eradicate, and/or control noxious or invasive species. Reporting will be required quarterly and annually or per request from the FFO Noxious Weed Coordinator.

Bare ground vegetation trim-out: If bare ground vegetation treatment (trim-out) is desired around facility structures, the operator will submit a bare ground/trim-out design included in their Surface Use Plan of Operations (SUPO). The design will address vegetation safety concerns of the operator and BLM while minimizing impacts to interim reclamation efforts. The design must include what structures to be treated and buffer distances of trim-out. Pesticide use for vegetation control around anchor structures is not approved. If pesticides are used for bare ground trim-out, the trim-out will not exceed three feet from the edge of any eligible permanent structure (i.e., well heads, fences, tanks). Additional distance/areas may be requested and must be approved by the FFO authorized officer. The additional information below must also be provided to the FFO:

- a. Pesticide use for trim out will require a Pesticide Use Proposal (PUP). A PUP is required **prior** to any treatment and must be approved by the FFO Noxious Weed Coordinator. Only pesticides authorized for use on BLM lands would be used and applied by a licensed pesticide applicator. The use of pesticides would comply with federal and state laws and used only in accordance with their registered use and limitations. Logos's weed-control contractor would contact the BLM-FFO prior to using these chemicals and provide Pesticide Use Reports (PURs) post treatment.
- b. A Pesticide Use Report (PUR) or a Biological Use Report (BUR) is required to report any chemical, or biological treatments used to eradicate, or control vegetation on site. Reporting will be required quarterly and annually or per request from the FFO Noxious Weed Coordinator.

Paleontology

Any paleontological resource discovered by the Operator, or any person working on his behalf, on public or Federal land shall be immediately reported to the Authorized Officer. Holder shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the Authorized Officer. An evaluation of the discovery will be made by the Authorized Officer to determine appropriate actions to prevent the loss of significant scientific values. The Holder will be responsible for the cost of evaluation and any decision as to proper mitigation measures will be made by the Authorized Officer after consulting with the Holder.

Visual Resources

Dark Sky COAs need to be applied to existing lighting, which is not dark sky friendly and to any additional lights added as part of pad expansion. All permanent lighting will use full cutoff luminaires, which are fully shielded (i.e., not emitting direct or indirect light above an imaginary horizontal plane passing through the lowest part of the light source). All permanent lighting will be pointed straight down at the ground in order to prevent light spill to the sides. All permanent lighting will be 4000° Kelvin or less with 3000° Kelvin preferred. Warmer light colors are less noticeable by humans and cause less impact to wildlife. All permanent lighting will be controlled by a switch and/or timer which allows the lights to be turned on when workers are on location during dark periods but will keep the lights off the majority of the time.

Wildlife Resources

Wildlife: F-4 Timing Limitation Stipulation-Important Seasonal Wildlife Habitat Rosa Mesa Wildlife SDA. No surface use is allowed during the following time period: December 1 - March 31.

Hazards: Wildlife hazards associated with the proposed project would be fenced, covered, and/or contained in storage tanks, as necessary.

Migratory Bird: Migratory nest survey stipulations. Once drilling and completion activities are complete, any open water that could be harmful to birds and wildlife. must be covered, screened, or netted to prevent entry.

Threatened, Endangered or Sensitive Species: If, in operations the operator/holder discovers any Threatened, Endangered, or Sensitive species, work in the vicinity of the discovery will be suspended and the discovery promptly reported to the BLM-FFO T&E specialist at (505) 564-7600. The BLM-FFO will then specify what action is to be taken. Failure to notify the BLM-FFO about a discovery may result in civil or criminal penalties in accordance with The Endangered Species Act (as amended).

Noise: This well is located within a designated Noise Sensitive Area (NSA). Once proposed project activities are complete, noise from pumpjack, compressor or other facilities cannot exceed 48.6 db at edge of Bald eagle ACEC core area. Any compressor that emits noise > 48.6db may require a 'noise wall' to deflect sound away from ACEC...

Nesting: If a bird nest containing eggs or young is encountered in the path of construction the operator will cease construction and consult with BLM to determine appropriate actions.

Livestock Grazing: Cattle are in allotment between 5/1 and 10/31. Industry may need to coordinate with permittee if concerns of livestock in area during construction.

Soil, Air, Water

Land Farming: No excavation, remediation or closure activities will be authorized without prior approval, on any federal or Indian mineral estate, federal surface, or federal ROW. A Sundry Notice (DOI, BLM Form 3160-5) must be submitted with an explanation of the remediation or closure plan for on-lease actions.

Emission Control Standard: Compressor engines 300 horsepower or less used during well production must be rated by the manufacturer as emitting NOx at 2 grams per horsepower hour or less to comply with the New Mexico Environmental Department, Air Quality Bureau's guidance.

Waste Disposal: All fluids (i.e., scrubber cleaners) used during washing of production equipment, including compressors, will be properly disposed of to avoid ground contamination, or hazard to livestock or wildlife.

Cultural Resources

Non-Permitted Disturbance: Construction, construction maintenance or any other activity outside the areas permitted by the APD will require additional approval and may require a new cultural survey and clearance.

Employee Education: All employees of the project, including the Project Sponsor and its contractors and sub-contractors will be informed that cultural sites are to be avoided by all personnel, personal vehicles, and company equipment. They will also be notified that it is illegal to collect, damage, or disturb cultural resources, and that such activities are punishable by criminal and or administrative penalties under the provisions of the Archaeological Resources Protection Act (16 U.S.C. 470aa-mm) when on federal land and the New Mexico Cultural Properties Act NMSA 1978 when on state land.

Discovery of Cultural Resources in the Absence of Monitoring: Discovery of Cultural Resources in the Absence of Monitoring: If, in its operations, operator/holder discovers any previously unidentified historic or prehistoric cultural resources, then work in the vicinity of the discovery will be suspended and the discovery promptly reported to BLM Field Manager. BLM will then specify what action is to be taken. If there is an approved "discovery plan" in place for the project, then the plan will be executed. In the absence of an approved plan, the BLM will evaluate the significance of the discovery in accordance with 36 CFR Section 800.13, in consultation with the appropriate State or Tribal Historic Preservation Officer(s) and Indian tribe(s) that might attach religious and cultural significance to the affected property, **or in accordance with an approved program alternative.** Minor recordation, stabilization, or data recovery may be performed by BLM or a third party acting on its behalf, such as a permitted cultural resources consultant. If warranted, more extensive **archaeological or alternative mitigation**, likely implemented by a permitted cultural resources consultant, may be required of the operator/holder prior to allowing the project to proceed. Further damage to significant cultural resources will not be allowed until any **mitigations determined appropriate through the agency's Section 106 consultation are completed.** Failure to notify the BLM about a discovery may result in civil or criminal penalties in accordance with the Archeological Resources Protection Act (ARPA) of 1979, as amended, **the Native American Graves Protection and Repatriation Act (NAGRPA) of 1990, as amended, and other applicable laws.**

Discovery of Cultural Resources during Monitoring: If monitoring confirms the presence of previously unidentified historic or prehistoric cultural resources, then work in the vicinity of the discovery will be suspended and the monitor will promptly report the discovery to the BLM Field Manager. BLM will then specify what action is to be taken. **If there is an approved "discovery plan" in place for the project, then the plan will be executed. In the absence of an approved plan, the BLM will evaluate the significance of the discovery in accordance with 36 CFR Section 800.13, in consultation with the appropriate State or Tribal Historic Preservation Officer(s) and Indian tribe(s) that might attach religious and cultural significance to the affected property, or in accordance with an approved program alternative.** Minor recordation, stabilization, or data recovery may be performed by BLM or a third party acting on its behalf, such as a permitted cultural resources consultant. If warranted, more extensive archaeological or alternative mitigation, likely implemented by a permitted cultural resources consultant, may be required of the operator/holder prior to allowing the project to proceed. Further damage to significant cultural resources will not

be allowed until any mitigations determined appropriate through the agency's Section 106 consultation are completed.

Damage to Sites: If, in its operations, operator/holder damages, or is found to have damaged any previously documented or undocumented historic or prehistoric cultural resources, excluding "discoveries" as noted above, the operator/holder agrees at his/her expense to have a permitted cultural resources consultant prepare a BLM approved damage assessment and/or data recovery plan. The operator/holder agrees at his/her expense to implement a **mitigation** that the agency finds appropriate given the significance of the site, which the agency determines in consultation with the appropriate State or Tribal Historic Preservation Officer(s) and Indian tribe(s) that might attach religious and cultural significance to the affected property. **This mitigation may entail execution of the data recovery plan by a permitted cultural resources consultant and/or alternative mitigations.** Damage to cultural resources may result in **civil or criminal penalties in accordance with the Archeological Resources Protection Act (ARPA) of 1979, as amended, the Native American Graves Protection and Repatriation Act (NAGRPA) of 1990, as amended, and other applicable laws.**

See below additional cultural stipulations.

District I
1625 N. French Drive, Hobbs, NM 88240
Phone: (575) 393-6161 Fax: (575) 393-0720

District II
811 S. First Street, Artesia, NM 88210
Phone: (575) 748-1283 Fax: (575) 748-9720

District III
1000 Rio Brazos Road, Aztec, NM 87410
Phone: (505) 334-6178 Fax: (505) 334-6170

District IV
1220 S. St. Francis Drive, Santa Fe, NM 87505
Phone: (505) 476-3460 Fax: (505) 476-3462

State of New Mexico
Energy, Minerals & Natural Resources Department

Form C-102
Revised August 1, 2011

Submit one copy to
Appropriate District Office

OIL CONSERVATION DIVISION
1220 South St. Francis Drive
Santa Fe, NM 87505

☐ AMENDED REPORT

WELL LOCATION AND ACREAGE DEDICATION PLAT

¹ API Number 30-039-31439	² Pool Code 97232	³ Pool Name BASIN MANCOS
⁴ Property Code 320608	⁵ Property Name ROSA UNIT	⁶ Well Number 702H
⁷ OGRID No. 289408	⁸ Operator Name LOGOS OPERATING, LLC	⁹ Elevation 6295'

¹⁰ Surface Location

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
I	7	31N	5W		2592	SOUTH	1308	EAST	RIO ARriba

¹¹ Bottom Hole Location If Different From Surface

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
M	11	31N	6W		1174	SOUTH	1136	WEST	RIO ARriba
¹² Dedicated Acres 823.25	S/2 - Sections 11, 12, T31N, R6W S/2 - Section 7, T31N, R5W					¹³ Joint or Infill	¹⁴ Consolidation Code	¹⁵ Order No. R-13457	

NO ALLOWABLE WILL BE ASSIGNED TO THIS COMPLETION UNTIL ALL INTERESTS HAVE BEEN CONSOLIDATED OR A NON-STANDARD UNIT HAS BEEN APPROVED BY THE DIVISION

LAST TAKE POINT
1174' FSL 1136' FWL
SECTION 11, T31N, R6W
LAT: 36.910108°N
LONG: 107.436739°W
DATUM: NAD1927

FIRST TAKE POINT
1151' FSL 1957' FEL
SECTION 7, T31N, R5W
LAT: 36.909942°N
LONG: 107.400821°W
DATUM: NAD1927

SURFACE LOCATION
2592' FSL 1308' FEL
SECTION 7, T31N, R5W
LAT: 36.913899°N
LONG: 107.398605°W
DATUM: NAD1927

LAT: 36.910114°N
LONG: 107.437343°W
DATUM: NAD1983

LAT: 36.909948°N
LONG: 107.401424°W
DATUM: NAD1983

LAT: 36.913904°N
LONG: 107.399208°W
DATUM: NAD1983

T31N R6W (RECORD)
NORTH 2640.00'
N0 *12 *07 *W 2636.49'
(MEASURED)

T31N R5W (RECORD)
N0 *02 *W 2642.64'
N0 *12 *05 *W 2632.33'
(MEASURED)

(RECORD)
N89 *57 *W 1832.82'
S89 *53 *00 *W
1832.26'
(MEASURED)

(RECORD)
S89 *50 *E 1185.36'
N89 *57 *49 *E
1178.25'
(MEASURED)


(RECORD)
N0 *03 *E 2640.00'
N0 *10 *08 *W 2659.33'
(MEASURED)

(RECORD)
S89 *54 *E 2644.62'
N89 *51 *49 *E 2646.13'
(MEASURED)

(RECORD)
S89 *54 *E 2644.62'
N89 *57 *35 *E 2646.27'
(MEASURED)

(RECORD)
N89 *57 *W 2640.00'
S89 *47 *35 *W 2651.82'
(MEASURED)

(RECORD)
S89 *50 *E 2640.00'
N89 *51 *20 *E 2630.31'
(MEASURED)

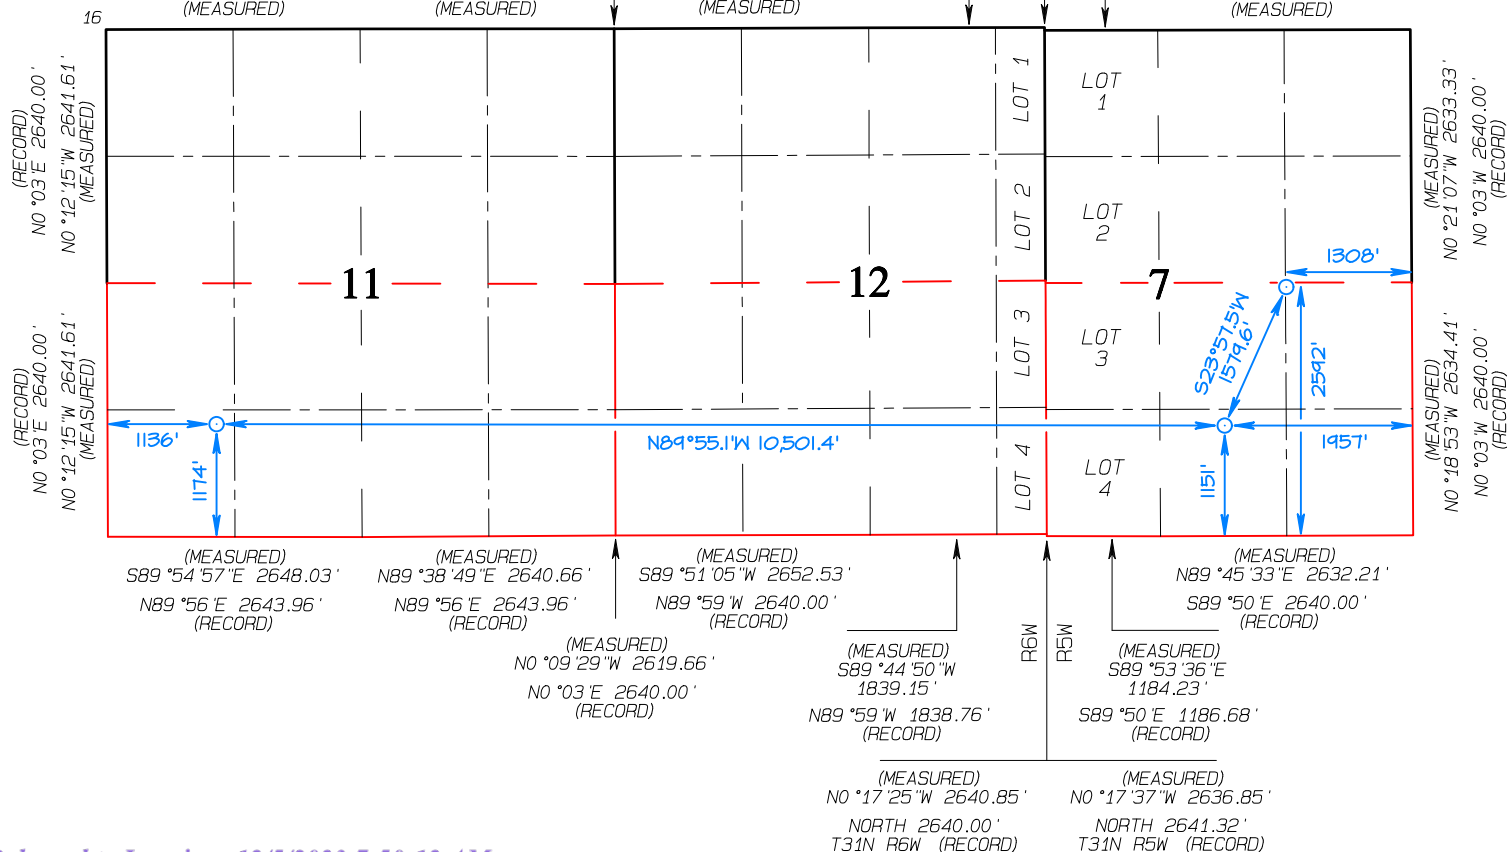

¹⁷ OPERATOR CERTIFICATION

I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief, and that this organization either owns a working interest or unleased mineral interest in the land including the proposed bottom-hole location or has a right to drill this well at this location pursuant to a contract with an owner of such a mineral or working interest, or to a voluntary pooling agreement or a compulsory pooling order heretofore entered by the division.

Marie E. Florez
Signature

1/22/2022
Date

Marie E. Florez

Printed Name

mfflorez@logosresourcesll.com

E-mail Address

¹⁸ SURVEYOR CERTIFICATION

I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief.

Date Revised: JANUARY 22, 2022
Survey Date: NOVEMBER 15, 2021

Signature and Seal of Professional Surveyor



JASON C. EDWARDS

Certificate Number 15269

State of New Mexico
Energy, Minerals and Natural Resources Department
Oil Conservation Division
1220 South St. Francis Dr.
Santa Fe, NM 87505

Submit Electronically
Via E-permitting

NATURAL GAS MANAGEMENT PLAN

This Natural Gas Management Plan must be submitted with each Application for Permit to Drill (APD) for a new or recompleted well.

Section 1 – Plan Description

Effective May 25, 2021

I. Operator: LOGOS Operating, LLC **OGRID:** 289408 **Date:** 8/15/2023

II. Type: ☒ Original ☐ Amendment due to ☐ 19.15.27.9.D(6)(a) NMAC ☐ 19.15.27.9.D(6)(b) NMAC ☐ Other.

If Other, please describe: _____

III. Well(s): Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	API	ULSTR	Footages	Anticipated Oil BBL/D	Anticipated Gas MCF/D	Anticipated Produced Water BBL/D
Rosa Unit 700H	30-039-pending	J-07-T31N-R5W	2612FSL, 1322FEL	N/A	13,671	516
Rosa Unit 701H	30-039-pending	G-07-T31N-R5W	2617FNL, 1351FEL	N/A	19,444	482
Rosa Unit 702H	30-039-pending	I-07-T31N-R5W	2592FSL, 1308FEL	N/A	13,671	520
Rosa Unit 704H	30-039-pending	I-07-T31N-R5W	2571FSL, 1293FEL	N/A	12,413	478
Rosa Unit 705H	30-039-pending	I-07-T31N-R5W	2551FSL, 1279FEL	N/A	16,504	486
Rosa Unit 706H	30-039-pending	I-07-T31N-R5W	2571FSL, 1293FEL	N/A	12,702	481

IV. Central Delivery Point Name: Harvest Gathering System [See 19.15.27.9(D)(1) NMAC]

V. Anticipated Schedule: Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	API	Spud Date	TD Reached Date	Completion Commencement Date	Initial Flow Back Date	First Production Date
Rosa Unit 700H	30-039-pending	Pending	Pending	Pending	Pending	Pending
Rosa Unit 701H	30-039-pending	Pending	Pending	Pending	Pending	Pending
Rosa Unit 702H	30-039-pending	Pending	Pending	Pending	Pending	Pending
Rosa Unit 704H	30-039-pending	Pending	Pending	Pending	Pending	Pending
Rosa Unit 705H	30-039-pending	Pending	Pending	Pending	Pending	Pending
Rosa Unit 706H	30-039-pending	Pending	Pending	Pending	Pending	Pending

VI. Separation Equipment: ☒ Attach a complete description of how Operator will size separation equipment to optimize gas capture.

VII. Operational Practices: ☒ Attach a complete description of the actions Operator will take to comply with the requirements of Subsection A through F of 19.15.27.8 NMAC.

VIII. Best Management Practices: ☒ Attach a complete description of Operator's best management practices to minimize venting during active and planned maintenance.

Section 2 – Enhanced Plan

EFFECTIVE APRIL 1, 2022

Beginning April 1, 2022, an operator that is not in compliance with its statewide natural gas capture requirement for the applicable reporting area must complete this section.

☒ Operator certifies that it is not required to complete this section because Operator is in compliance with its statewide natural gas capture requirement for the applicable reporting area.

IX. Anticipated Natural Gas Production:

Well	API	Anticipated Average Natural Gas Rate MCF/D	Anticipated Volume of Natural Gas for the First Year MCF

X. Natural Gas Gathering System (NGGS):

Operator	System	ULSTR of Tie-in	Anticipated Gathering Start Date	Available Maximum Daily Capacity of System Segment Tie-in

XI. Map. ☐ Attach an accurate and legible map depicting the location of the well(s), the anticipated pipeline route(s) connecting the production operations to the existing or planned interconnect of the natural gas gathering system(s), and the maximum daily capacity of the segment or portion of the natural gas gathering system(s) to which the well(s) will be connected.

XII. Line Capacity. The natural gas gathering system ☐ will ☐ will not have capacity to gather 100% of the anticipated natural gas production volume from the well prior to the date of first production.

XIII. Line Pressure. Operator ☐ does ☐ does not anticipate that its existing well(s) connected to the same segment, or portion, of the natural gas gathering system(s) described above will continue to meet anticipated increases in line pressure caused by the new well(s).

☐ Attach Operator's plan to manage production in response to the increased line pressure.

XIV. Confidentiality: ☐ Operator asserts confidentiality pursuant to Section 71-2-8 NMSA 1978 for the information provided in Section 2 as provided in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and attaches a full description of the specific information for which confidentiality is asserted and the basis for such assertion.

Section 3 - Certifications

Effective May 25, 2021

Operator certifies that, after reasonable inquiry and based on the available information at the time of submittal:

☒ Operator will be able to connect the well(s) to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system; or

☐ Operator will not be able to connect to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system.

If Operator checks this box, Operator will select one of the following:

Well Shut-In. ☐ Operator will shut-in and not produce the well until it submits the certification required by Paragraph (4) of Subsection D of 19.15.27.9 NMAC; or

Venting and Flaring Plan. ☐ Operator has attached a venting and flaring plan that evaluates and selects one or more of the potential alternative beneficial uses for the natural gas until a natural gas gathering system is available, including:

- (a) power generation on lease;
- (b) power generation for grid;
- (c) compression on lease;
- (d) liquids removal on lease;
- (e) reinjection for underground storage;
- (f) reinjection for temporary storage;
- (g) reinjection for enhanced oil recovery;
- (h) fuel cell production; and
- (i) other alternative beneficial uses approved by the division.

Section 4 - Notices


1. If, at any time after Operator submits this Natural Gas Management Plan and before the well is spud:

(a) Operator becomes aware that the natural gas gathering system it planned to connect the well(s) to has become unavailable or will not have capacity to transport one hundred percent of the production from the well(s), no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised venting and flaring plan containing the information specified in Paragraph (5) of Subsection D of 19.15.27.9 NMAC; or

(b) Operator becomes aware that it has, cumulatively for the year, become out of compliance with its baseline natural gas capture rate or natural gas capture requirement, no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised Natural Gas Management Plan for each well it plans to spud during the next 90 days containing the information specified in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and shall file an update for each Natural Gas Management Plan until Operator is back in compliance with its baseline natural gas capture rate or natural gas capture requirement.

2. OCD may deny or conditionally approve an APD if Operator does not make a certification, fails to submit an adequate venting and flaring plan which includes alternative beneficial uses for the anticipated volume of natural gas produced, or if OCD determines that Operator will not have adequate natural gas takeaway capacity at the time a well will be spud.

I certify that, after reasonable inquiry, the statements in and attached to this Natural Gas Management Plan are true and correct to the best of my knowledge and acknowledge that a false statement may be subject to civil and criminal penalties under the Oil and Gas Act.

Signature: 
Printed Name: Etta Trujillo
Title: Regulatory Specialist
E-mail Address: etrujillo@logosresourcesllc.com
Date: 8/15/2023
Phone: 505-324-4154
OIL CONSERVATION DIVISION (Only applicable when submitted as a standalone form)
Approved By:
Title:
Approval Date:
Conditions of Approval:

VI. Separation Equipment

The operator will select separation equipment for the maximum anticipated throughput and pressure to optimize gas capture. Separation equipment is sized according to manufacturer's design specifications. Separation vessels are built following the A.S.M.E. section VII division 1 codes for pressure vessel design, fabrication, inspection, testing and certification. Anticipated well pressures and production rates are evaluated to select separation equipment according to the equipment's designed operating pressure and throughput.

After completion, the operator utilizes flowback equipment, including separators, to manage wellbore fluids and solids during the initial separation period. After the initial flowback period is complete the operator utilizes iterative facility separation equipment to ensure that optimal separation is achieved.

VII. Operational Practices 19.15.27.8 NMAC A through F

- A. The operator will maximize the recovery of natural gas and minimize the amount of gas vented or flared when technically and safely feasible as further described and detailed within the following subsections (B-F of 19.15.27.8). In all cases where natural gas venting and flaring requires regulatory reporting, reporting will be submitted accurately and within the required time frames.
- B. Venting and flaring during drilling operations:
 - a. New Drill HZ Oil Wells: The operator drills wells in the area by utilizing a balanced mud to safely drill the wellbore. This technique prevents gas from coming to surface during the drilling process. If there is an emergency or malfunction and natural gas does come to surface the natural gas will be captured or combusted, with an appropriately sized and located flare stack, if technically and safely feasible.
 - b. New Drill HZ Gas Wells: The operator drills wells in the area by balancing the mud weight to safely drill the wellbore with as minimal flaring as possible. When gas kicks enter the wellbore, sometimes it is necessary to circulate it out of the wellbore to an appropriately sized and located flare stack. The operator will estimate the volume flared and appropriately report.
- C. Venting and flaring during completion or recompletion operations:
 - a. New Drill HZ Oil Wells: The operator's facilities are designed to handle the maximum throughput and pressures from the newly drilled and completed wellbores. The amount of gas vented and flared will be minimized when technically and safely feasible. During initial flowback and initial separation flowback the operator will utilize contracted flowback equipment, including separators, to manage wellbore fluids and solids. The initial flowback period will be minimized and flow will be sent to separation equipment as soon as possible to reduce the amount of gas that is vented to atmosphere. During the separation flowback period natural gas will be routed to a properly sized and located flare until the natural gas is of pipeline quality (less than 60 days). The natural gas will also be utilized on site as needed for fuel gas or injection gas.
 - b. New Drill HZ Gas Wells: The operator's facilities are designed to handle the maximum throughput and pressures from the newly drilled and completed wellbores. The amount of gas vented and flared will be minimized when technically and safely feasible. During initial flowback and initial separation flowback the operator will utilize contracted flowback equipment, including separators, to manage wellbore fluids and solids. The initial flowback period will be minimized and flow will be sent to separation equipment as soon as possible to reduce the amount of gas that is vented to atmosphere. The natural gas will be utilized on site as needed for fuel gas and natural gas will be sold.
- D. Venting and flaring during production operations:

- a. New Drill HZ Oil Wells: The operator's facilities are designed to handle the maximum throughput and pressures from producing wellbores. The amount of gas vented and flared will be minimized when technically and safely feasible. This facility will operate under a notice of intent (NOI) from the New Mexico Environment Department (NMED).

Operations will effectively manage the following scenarios to minimize the quantity of natural gas that is vented or flared:

- (a) If there is an emergency or malfunction, vented or flared natural gas will be reported, if required, and the emergency or malfunction will be resolved as soon as technically and safely feasible.
- (b) If the wellbore requires liquids to be unloaded to atmosphere, the operator will not vent the well after the well has achieved a stabilized rate and pressure. The operator will remain on site during unloading. Plunger lift systems will be optimized to reduce the amount of natural gas venting. Downhole maintenance, such as workovers, swabbing, etc. will only be conducted as needed and best management practices will be utilized to reduce venting of natural gas.
- (c) The operator will minimize the amount of time that natural gas is vented to atmosphere from gauging and sampling a storage tank or low-pressure vessel, automatic tank gauges will be the primary means of gauging with minor exceptions.
- (d) The operator will reduce the amount of time needed for loading out liquids from a storage tanks or other low-pressure vessels whenever feasible. Operations will utilize a LACT system when available to minimize gas vented during oil tank loading.
- (e) Equipment will be repaired and maintained routinely to minimize the venting or flaring of natural gas. Repairs and maintenance will be conducted in a manner that minimizes the amount of natural gas vented to atmosphere through the isolation of the equipment that is being repaired or maintained.
- (f) Electric controllers and pumps will be installed to replace pneumatic controllers whenever feasible. Pneumatic controllers and pumps will be inspected frequently to ensure that no excess gas is vented to atmosphere.
- (g) Storage tanks and other low-pressure vessel normal operational venting will be minimized during the early life of the well with the installation of a vapor recovery unit to limit the flash and working and breathing emissions to atmosphere.
- (h) No dehydration or amine units are anticipated to be set on location.
- (i) Compressors, compressor engines, turbines, flanges, connectors, valves, and flanges will be routinely inspected to ensure that no excess venting occurs outside of normal operation.
- (j) Regulatory required testing, such as bradenhead and packer testing will be performed in a manner that minimizes the amount of natural gas vented to atmosphere.
- (k) When natural gas does not meet gathering pipeline specifications, for example high nitrogen content after a nearby frac, gas samples will be collected twice per week to determine when pipeline specification gas content has been achieved. During this time frame gas will be flared and not vented to atmosphere. Natural gas that meets pipeline specifications will be sold via pipeline and natural gas that can be utilized for fuel gas will be used during this time.
- (l) If pipeline, equipment, or facilities need purged of impurities gas losses will be minimized as much as technically and safely feasible.

- b. New Drill HZ Gas Wells: The operator's facilities are designed to handle the maximum throughput and pressures from producing wellbores. The amount of gas vented and flared will be minimized when technically and safely feasible.

Operations will effectively manage the following scenarios to minimize the quantity of natural gas that is vented or flared:

- (a) If there is an emergency or malfunction vented or flared natural gas will be reported, if required, and the emergency or malfunction will be resolved as soon as technically and safely feasible.
- (b) If the wellbore needs to be unloaded to atmosphere the operator will not vent the well after the well has achieved a stabilized rate and pressure. The operator will remain on site during unloading. Plunger lift systems will be optimized to reduce the amount of natural gas venting. Downhole maintenance, such as workovers, swabbing, etc. will only be conducted as needed and best management practices will be utilized to reduce venting of natural gas.
- (c) The operator will minimize the amount of time that natural gas is vented to atmosphere from gauging and sampling a storage tank or low-pressure vessel, automatic tank gauges will be the primary means of gauging. The formation is only anticipated to produce water and therefore tank emissions are anticipated to be negligible.
- (d) The operator will reduce the amount of time needed for loading out liquids from a storage tanks or other low-pressure vessels whenever feasible. Operations will always utilize the water transfer systems when available. Water loading emissions are anticipated to be negligible.
- (e) Equipment will be repaired and maintained routinely to minimize the venting or flaring of natural gas. Repairs and maintenance will be conducted in a manner that minimizes the amount of natural gas vented to atmosphere through the isolation of the equipment that is being repaired or maintained.
- (f) Electric controllers and pumps, or instrument air, will be installed to replace pneumatic controllers whenever feasible. Pneumatic controllers and pumps will be inspected frequently to ensure that no excess gas is vented to atmosphere.
- (g) No dehydration or amine units are anticipated to be set on location.
- (h) Compressors, compressor engines, turbines, flanges, connectors, valves, storage tanks, and other low-pressure vessels and flanges will be routinely inspected to ensure that no excess venting occurs outside of normal operations.
- (i) Regulatory required testing, such as bradenhead and packer testing will be performed in a manner that minimizes the amount of natural gas vented to atmosphere.
- (j) If natural gas does not meet gathering pipeline specifications gas samples will be collected twice per week to determine when pipeline specification gas content has been achieved. During this time frame gas will be flared and not vented to atmosphere. Natural gas that meets pipeline specifications will be sold via pipeline and natural gas that can be utilized for fuel gas will be used during this time.
- (k) If pipeline, equipment, or facilities need purged of impurities gas losses will be minimized as much as technically and safely feasible.

E. Performance standards:

- a. The production facilities are designed to handle the maximum throughput and pressures from producing wellbores and will be designed to minimize waste. The amount of gas vented and flared will be minimized when technically and safely feasible.

- b. All tanks that are routed to a control device that is installed after 5/25/2021 will have an automatic gauging system to minimize the amount of vented natural gas.
 - c. If a flare stack is installed or replaced after 5/25/2021 it will be equipped with an automatic ignitor or continuous pilot. The flare stack will be properly sized and designed to ensure proper combustion efficiency. The flare stack will be located 100 feet away from the nearest wellhead or storage tank.
 - d. AVO inspections will be conducted weekly for the year after completion and for all wells producing greater than 60,000 cubic feet of natural gas daily. The AVO inspection will include all components, including flare stacks, thief hatches, closed vent systems, pumps, compressors, pressure relief devices, valves, lines, flanges, connectors, and associated pipeline to identify any leaks and releases by comprehensive auditory, visual, and olfactory inspection. The AVO inspection records will be maintained for 5 years which will be available at the department's request. Identified leaks will be repaired as soon as feasible to minimize the amount of vented natural gas.
- F. Measurement or estimation of vented and flared natural gas.
- a. The volume of natural gas that is vented, flared or consumed for beneficial use will be measured when possible, or estimated, during drilling, completions, or production operations.
 - b. Equipment will be installed to measure the volume of natural gas flared for all APD's issued after 5/25/2021 on facilities that will have an average daily gas rate greater than 60,000 cubic feet of natural gas. Measurement equipment will conform to API MPMS Chapter 14.10 regulations. The measurement equipment will not have a manifold that allows the diversion of natural gas around the metering element except for the sole purpose of inspecting and servicing the measurement equipment. If metering is not practical, then the volume of gas will be estimated.



LOGOS Operating, LLC Operations Plan

Note: This procedure will be adjusted onsite based upon actual conditions

Date:	January 25, 2022	Pool:	Basin Mancos
Well Name:	Rosa Unit 702H	GL Elevation:	6,295'
Surface Location:	Sec 7, T31N, R5W 2592 FSL, 1308 FEL (36.913904° N, 107.399208° W – NAD83)	Measured Depth:	17,962' (KB)
Bottom Hole Location:	Sec 11, T31N, R6W 1174 FSL, 1136 FWL (36.910114° N, 107.437343° W – NAD83)	County:	Rio Arriba

Lease Serial #NMSF078767, CA Serial #NMNM078707E

I. GEOLOGY

A. Formation Tops (Based on GL Elevation): Estimated top of important geological markers:
SURFACE FORMATION – NACIMIENTO

NAME	MD	TVD	NAME	MD	TVD
OJO ALAMO	2,437'	2,397'	*POINT LOOKOUT	5,725'	5,596'
KIRTLAND	2,550'	2,507'	*MANCOS	6,277'	6,133'
*FRUITLAND	3,053'	2,996'	KICKOFF POINT	6,459'	6,311'
*PICTURED CLIFFS	3,385'	3,319'	POINT OF ENTRY	7,461'	6,930'
LEWIS	3,493'	3,424'			
CHACRA	4,649'	4,549'			
*CLIFF HOUSE	5,434'	5,313'			
MENEFEE	5,489'	5,367'	TD	17,962'	6,897'

* indicates the depth at which anticipated water, oil, gas, or other mineral-bearing formations are expected to be encountered.

B. MUD LOGGING PROGRAM: Mudlogger on location from KOP to TD.

C. LOGGING PROGRAM: LWD GR from surface casing to TD.

D. NATURAL GAUGES: Gauge any noticeable increases in gas flow. Record all gauges in the Tour book and on morning reports.

II. DRILLING

A. MUD PROGRAM: LSND mud (WBM) will be used to drill the 17-1/2" surface hole as well as the 12-1/4" directional vertical hole. A LSND (WBM) or (OBM) will be used to drill the 8-1/2" curve and lateral portion of the wellbore. Treat for lost circulation as necessary. Obtain 100% returns prior to cementing. Notify Engineering of any mud losses.

Above ground steel pits will be used for fluid and cuttings while drilling. In the unlikely event that a tank develops a leak, upon immediate visual discovery, the fluid would be transferred to another tank and contaminated soil would be removed and disposed of. Any leaks, spills, or other undesirable events will be reported in accordance with BLM NTL 3A. Rig crews will monitor the tanks at all times.

ROSA UNIT 702H



- B. **BOP TESTING:** The BOPE will be tested to **250 psi (Low) for 5 minutes** and **1500 psi (High) for 10 minutes**. Pressure test surface casing to **600 psi for 30 minutes** and intermediate casing to **1500 psi for 30 minutes**. Utilize a BOPE Testing Unit with a recording chart and appropriate test plug for testing. The drum brakes will be inspected and tested each tour. BOP equipment will be tested every 30 days, after any repairs are made to the BOP equipment, and after the BOP equipment is subjected to pressure. Annular preventers will be functionally operated at least once per week. Pipe and blind rams shall be activated each trip but not more than once a day. The New Mexico Oil & Gas Conservation Commission and the BLM will be notified 24 hours in advance of testing of BOPE. **All tests and inspections will be recorded and logged with time and results.** A full BOP test will be conducted when initially installed for the first well on the pad or if seals subject to test pressure are broken, following related repairs and at a minimum of 30-day intervals. A BOPE Shell Test only will be conducted for subsequent wells on the pad when seals subject to pressure have not been broken or repaired and fall within the 30-day interval of the first full test.
- C. **GeoHazards:** There are no Geohazards
- D. **Maximum Anticipated Pressure:** $6930' \text{ TVD} \times 0.43 = 2980 \text{ psi}$
- E. **H2S Concerns:** There is no record of any naturally occurring H2S in any formation in the Rosa Unit. No H2S is anticipated in this formation or this well.

III. **MATERIALS**

A. **CASING EQUIPMENT:**

CASING TYPE	OH SIZE (IN)	DEPTH (MD)	CSG SIZE	WEIGHT	GRADE	CONN
SURFACE	17.5"	320' or greater	13.375"	54.5 LBS	J-55 or equiv	LTC/BTC
INTERMEDIATE	12.25"	6,352'	9.625"	43.5 LBS	N-80 or equiv	LTC/BTC
PRODUCTION	8.5"	17,962'	5.5"	20 LBS	P-110 or equiv	LTC/BTC

NOTE: All casing depths are approximate, based on GL elevation, and will be based on drilling conditions +/- 50'. Weights, grades, and connections will be based on availability and may vary but will be equivalent or greater.

B. **FLOAT EQUIPMENT:**

1. **SURFACE CASING:** 13-3/8" notched regular pattern guide shoe. Run (1) standard centralizer on each of the bottom (3) joints of Surface Casing.
2. **INTERMEDIATE CASING:** 9-5/8" cement nose guide shoe with a self-fill insert float. Place float collar one joint above the shoe. Install (1) centralizer on each of the bottom (3) joints and one standard centralizer every (3) joints to 2,500 ft. Run (1) centralizer at 2,500 ft., 2,300ft., 2,000ft., 1,500 ft., and 1,000 ft. Optional use of DV Tools (2) will be strategically placed above loss circulation zones anticipated in the Mesaverde and Fruitland Coal. Optional use of cancellation plugs for DV tools may be used if losses while cementing are not encountered.
3. **PRODUCTION CASING:** Run 5-1/2" casing with cement nose guide Float Shoe, 5-1/2" full or pup joints as necessary, Landing Collar, 5-1/2" full or pup joints as necessary, at least (1) one Toe Sleeve (Sliding Sleeve) positioned inside the applicable production area. The centralizer program will be determined by wellbore conditions. Production casing to be pressure tested during completion operations with frac stack installed.



C. CEMENTING:

(Note: Cement type and volumes may be adjusted onsite due to actual conditions and availability)

1. SURFACE: Casing shall be set at ~ 320' and cemented to surface. TOC at Surface.
263 sks of 15.8 ppg Type Neat G, 1.18 cuft/sk yield or equivalent 223 sks of 14.6 ppg Type III with 1.39 cuft/sk yield, 30% excess.
2. INTERMEDIATE: Intermediate casing shall be kept fluid-filled while running into the hole to meet BLM minimum collapse requirements. The intermediate casing will be cemented in 2 or 3 stages using DV/STAGE tools in order to reduce cement losses and maximize cement coverage. Operator proposes optional DV tools above anticipated loss circulation zones in the Mesaverde and in the Fruitland coal. If losses are not observed during the second stage a cancelation plug will be pumped and the remaining cement will be pumped during stage 2. If cement does not circulate to the DV tool(s) or to the surface, a CBL will be run to determine TOC.

	Top (ft)	Footage (ft)	Cement (ft3/ft) Annular Capacity	Excess (30%)	Total (ft3)	Total (bbl)	Slurry Yield (ft3/sk)	Sacks Cement	Density (PPG)
Stage 1 Tail	5,825	527	0.31318	1.3	232	41	1.15	202	15.8
Stage 1 Lead	4,700	1,125	0.31318	1.3	458	82	2.30	199	12.3
					690	123		401	
Stage 2 Tail	3,585	1,115	0.31318	1.3	454	81	1.50	303	13.5
Stage 2 Lead	3,104	481	0.31318	1.3	196	35	2.30	85	12.3
					650	116		388	
Stage 3 Tail	2,354	750	0.31318	1.3	305	54	1.99	153	12.8
Stage 3 Lead	320	2,034	0.31318	1.3	828	147	2.53	327	12
Stage 3 Lead	-	320	0.36268	1	116	21	2.53	46	12
					1,250	223		527	
All Stage Totals					2,589	461		1,315	

Calculations based on 30% excess for open hole and cement to the surface. Actual excess pumped will be determined by well conditions.

3. PRODUCTION: Production casing will be cemented in 1 stage with 100' of cement overlap above the intermediate shoe. A CBL, or alternatively, a Temperature Survey will be used to determine TOC.

	Top (ft)	Footage (ft)	Cement (ft3/ft) Annular Capacity	Excess (15%)	Total (ft3)	Total (bbl)	Slurry Yield (ft3/sk)	Sacks Cement	Density (PPG)
Cased Lead	6,252	100	0.2531	1	25	5	1.56	16	13
Open Hole Lead	6,352	11,610	0.2291	1.15	3,069	547	1.56	1,967	13
					3,095	551		1,984	

Calculations based on 15% excess for the open hole and 100' overlap into the intermediate casing. Actual volumes will vary.

Cement calculations are used for volume estimation. Well conditions will dictate the final cement job design. Actual volumes will be calculated and determined by conditions onsite. All cement slurries will meet or exceed minimum BLM and New Mexico Oil Conservation Division requirements. Slurries used will be the slurries listed above or equivalent slurries depending on the service provider selected. Cement yields may change depending on the slurries selected. All waiting on cement times shall be a minimum of 8 hours or adequate to achieve a minimum of 500 psi compressive strength at the casing shoe prior to drilling out.

IV. COMPLETION

A. CBL

ROSA UNIT 702H



CBLs and/or Temperature Surveys will be performed as needed or required to determine cement top if cement is not circulated.

B. PRESSURE TEST

- C. Pressure test 5-1/2" casing to 0.22 psi/ft * 6,930' TVD=1525 psi for 30 minutes. Increase pressure to Open toe sleeves.

D. STIMULATION

Stimulate with sand and water. Isolate stages with flow-through or dissolvable frac plugs. Drill out frac plugs and flow back lateral.



E. PRODUCTION TUBING

2-7/8", 6.5#, J-55 or L-80, EUE tubing will be run once volumes and pressures dictate. Due to the extremely high initial flow rates and pressures seen in offset wells, the tubing will be installed once it is safe to do so, typically 12-18 months after completion.

*NOTE: Although this horizontal well may be drilled past the applicable setbacks, an unorthodox location application is not required because the completed interval in this well, as defined by 19.15.16.7 8(1) NMAC, will be entirely within the applicable setbacks. This approach complies with all applicable rules, including 19.15.16.14 A(3) NMAC, 19.15.16.14 8(2) NMAC, 19.15.16.15 8(2)NMAC, and 19.15.16.15. 8(4) NMAC.



3M 11" B.O.P.E Diagram

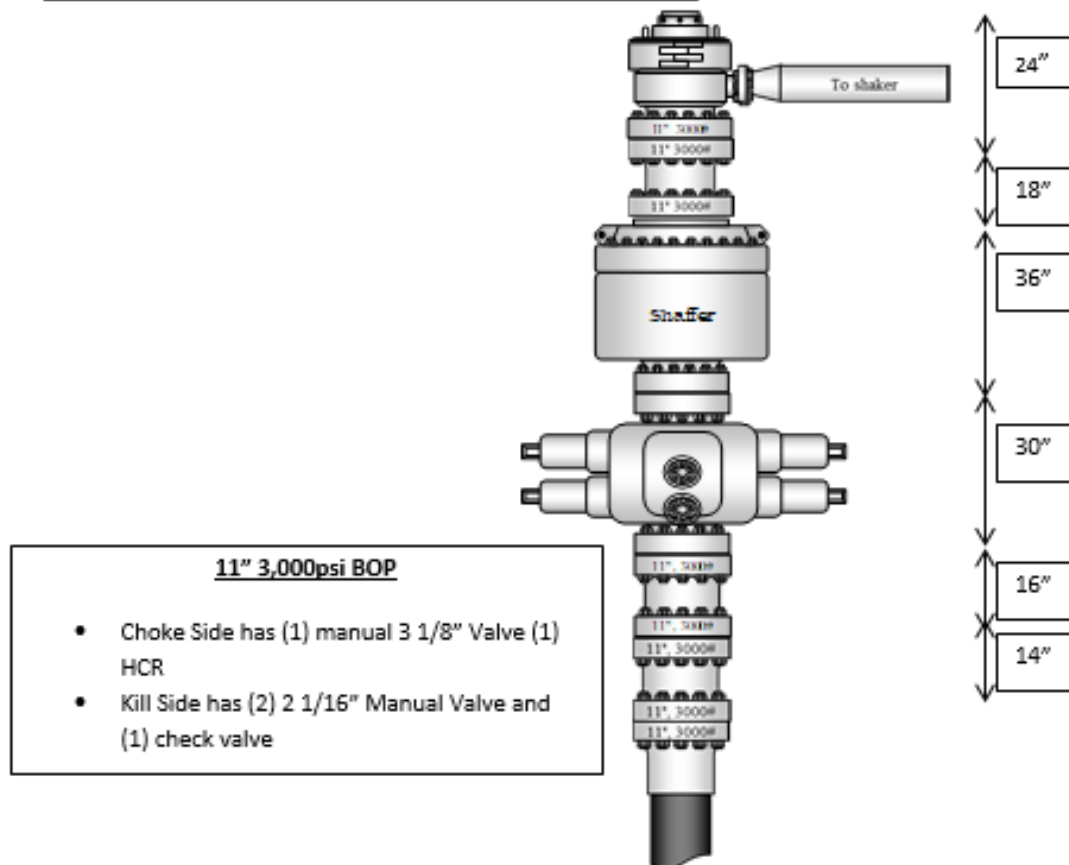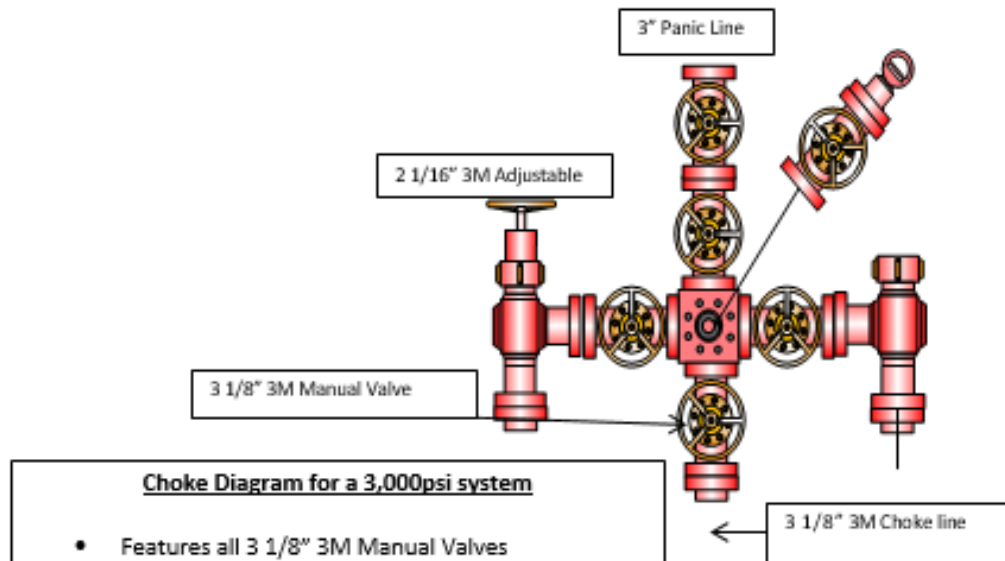

ROSA UNIT 702H

					1.125	1.000		1.400
Surface	Size	Weight	Grade	Conn	Collapse	Burst	70% Burst	Tension (Body)
	13.375	54.5	J-55	BTC	1,130	2,730	1,911	853,000

Burst							
54.5 J-55 BTC	320	15.80	0.00	1763	0	1.55	1500 psi casing test

Tension						
54.5 J-55 BTC		Mud Wt	Air Wt	Bouy Wt	BW +100k	SF
Tension (Body)	320	15.80	17,440	13,233	113,233	7.53
Tension (Conn)	320	15.80	17,440	13,233	113,233	8.03
BF						BF= 1- (MW)/65.5
						0.7588

Intermediate Casing Design - Evacuated/Max SICP (collapse & burst), 100k overpull (tension)

					1.125	1.000		1.400
	Size	Weight	Grade	Conn	Collapse	Burst	80% Burst	Tension (Body)
Intermediate	9.625	43.5	N-80 or L-80 LTC		3,810	6,330	5,064	1,005,000
	9.625	43.5	N-80 or L-80 BTC		3,810	6,330	5,064	1,005,000
	9.625	43.5	P-110	BTC	4,420	8,700	6,960	1,381,000

Collapse

Casing Depth TVD	MW in	MW out	Pres in	Pres out	SF	
43.5 N-80 or L-80 L 6,207	0.00	9.40	0	3034	1.26	full evacuation with 9.4 ppg mu
43.5 N-80 or L-80 E 6,207	0.00	9.40	0	3034	1.26	full evacuation with 9.4 ppg mu

Burst

43.5 N-80 or L-80 L 6,207	9.40	0.00	4534	0	1.40	Casing full with 9.4 ppg mud , al
43.5 N-80 or L-80 E 6,207	9.40	0.00	4534	0	1.40	Casing full with 9.4 ppg mud , al

Tension

		Mud Wt	Air Wt	Bouy Wt	BW +100k	SF	
43.5 N-80 or L-80 LTC							
Tension (Body)	6,207	9.40	270,005	231,256	331,256	3.03	100k over pull
Tension (Conn)	6,207	9.40	270,005	231,256	331,256	2.49	100k over pull
		BF					BF= 1- (MW)/65.5
		0.8565					
43.5 N-80 or L-80 BTC							
Tension (Body)	6,207	9.40	270,005	231,256	331,256	3.03	100k over pull
Tension (Conn)	6,207	9.40	270,005	231,256	331,256	3.24	100k over pull
		BF					BF= 1- (MW)/65.5
		0.8565					

Production Casing Design - Evacuated/Max SICP (collapse & burst), 100k overpull (tension)

					1.125	1.000		1.400
	Size	Weight	Grade	Conn	Collapse	Burst	80% Burst	Tension (Body)
Production	5.5	20	P110	LTC	11,080	12,630	10,104	641,000
	5.5	20	P110	BTC	11,080	12,360	9,888	641,000

Collapse

	Casing Depth TVD	MW in	MW out	Pres in	Pres out	SF	
20 P110 LTC	6,897	0.00	13.30	0	4770	2.32	full evacuation with 13.3 ppg m
20 P110 BTC	6,897	0.00	13.30	0	4770	2.32	full evacuation with 13.3 ppg m

Burst

20 P110 LTC	6,897	13.30	0.00	6270	0	2.01	1500 psi casing test
20 P110 BTC	6,897	13.30	0.00	6270	0	1.97	1500 psi casing test

Tension

		Mud Wt	Air Wt	Bouy Wt	BW +100k	SF	
20 P110 LTC							
Tension (Body)	6,897	13.30	137,940	109,931	209,931	3.05	100k over pull
Tension (Conn)	6,897	13.30	137,940	109,931	209,931	2.61	100k over pull
		BF					BF= 1- (MW)/65.5
		0.7969					
20 P110 BTC							
Tension (Body)	6,897	13.30	137,940	109,931	209,931	3.05	100k over pull
Tension (Conn)	6,897	13.30	137,940	109,931	209,931	3.18	100k over pull
		BF					BF= 1- (MW)/65.5

Released to Imaging: 12/5/2023 7:50:12 AM



Company: Logos Operating LLC
Project: Rio Arriba, NM NAD83
Site: Rosa Unit 24
Well: Rosa Unit 702H
Wellbore: OH
Design: Plan #2

PROJECT DETAILS: Rio Arriba, NM NAD83

Geodetic System: US State Plane 1983
Datum: North American Datum 1983
Ellipsoid: GRS 1980
Zone: New Mexico Western Zone
System Datum: Mean Sea Level
Local North: True



WELL DETAILS: Rosa Unit 702H

GL 6295' @ 6295.00usft							
+N/-S	+E/-W	Northing	Easting	Latitude	Longitude		
0.00	0.00	2152277.01	2850002.92	36.9139040	-107.3992080	A5 (702H)	

Plan: Plan #2 (Rosa Unit 702H/OH)


Created By: Janie Collins Date: 12:04, January 31 2022

DESIGN TARGET DETAILS

Name	TVD	+N/-S	+E/-W	Northing	Easting	Latitude	Longitude
Rosa 702H POE	6930.00	-1440.36	-647.89	2150833.71	2849361.59	36.9099477	-107.4014241
Rosa 702H BHL	6897.00	-1377.59	-11149.07	2150848.69	2838860.23	36.9101140	-107.4373432

SECTION DETAILS

MD	Inc	Azi	TVD	+N/-S	+E/-W	Dleg	TFace	VSect
0.00	0.00	0.000	0.00	0.00	0.00	0.00	0.00	0.00
500.00	0.00	0.000	500.00	0.00	0.00	0.00	0.00	0.00
1166.27	13.33	180.374	1160.28	-77.13	-0.50	2.00	180.37	9.96
6459.20	13.33	180.374	6310.71	-1297.02	-3.46	0.00	0.00	167.45
7461.07	90.18	270.343	6930.00	-1440.36	-647.89	9.00	89.93	819.63
17962.48	90.18	270.343	6897.00	-1377.59	-11149.07	0.00	0.00	11233.86



Azimuths to True North
Magnetic North: 81.1°


Magnetic Field
Strength: 49663.71
Dip Angle: 63.63°
Date: 10/11/2021
Model: HDGM2021_FLE

CASING DETAILS

No casing data is available

FORMATION DETAILS

TVDPath	MDPath	Formation
2397.00	2437.21	Ojo Alamo
2507.00	2550.25	Kirtland
2996.00	3052.78	Fruitland
3319.00	3384.72	Pictured Cliffs
3424.00	3492.62	Lewis
4549.00	4648.75	Chacra
5313.00	5433.89	Cliff House
5367.00	5489.38	Menefee
5596.00	5724.72	Point Lookout
6133.00	6276.58	Mancos

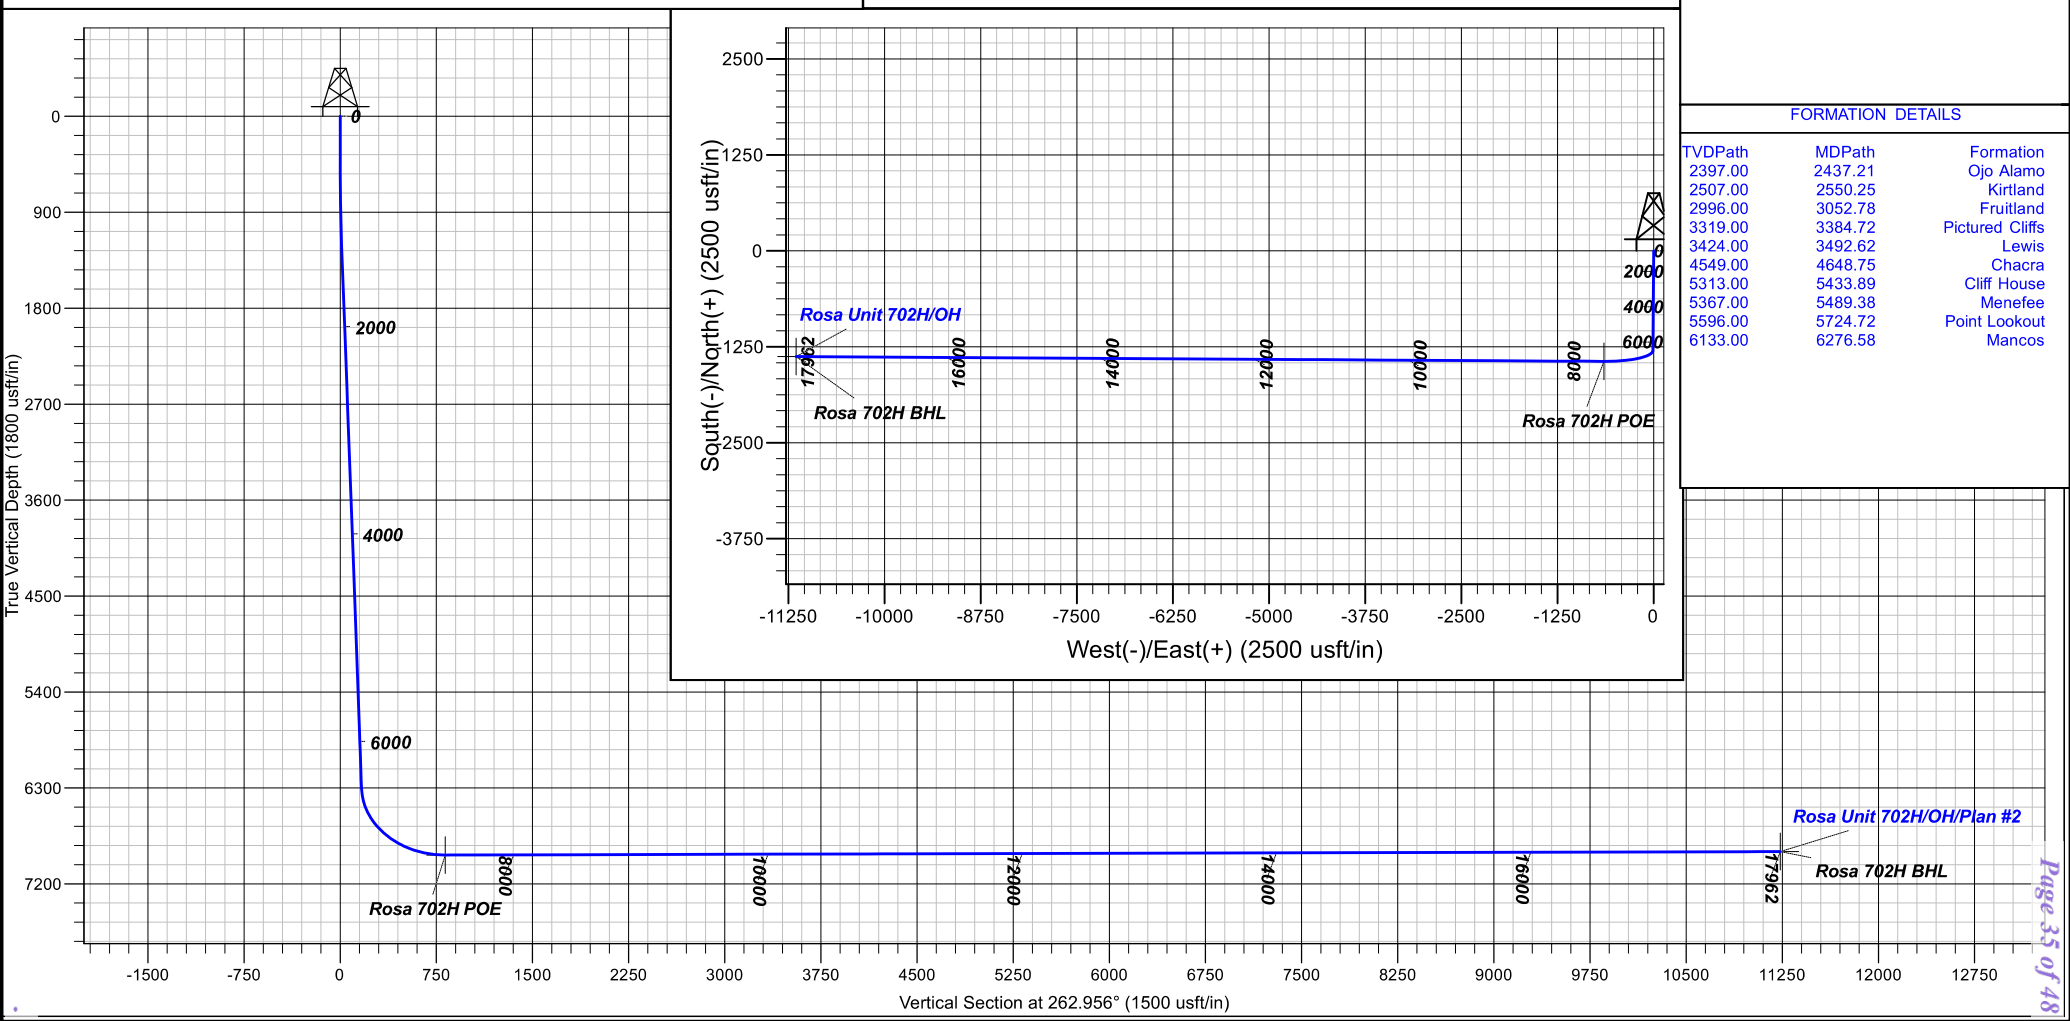

Received by OCB: 12/5/2023 7:13:19 PM



Logos Operating LLC

Rio Arriba, NM NAD83

Rosa Unit 24

Rosa Unit 702H - Slot A5 (702H)

OH

Plan: Plan #2

Standard Planning Report

31 January, 2022





Lonestar Consulting, LLC

Planning Report



Database:	Grand Junction	Local Co-ordinate Reference	Well Rosa Unit 702H - Slot A5 (702H)
Company:	Logos Operating LLC	TVD Reference:	GL 6295' @ 6295.00usft
Project:	Rio Arriba, NM NAD83	MD Reference:	GL 6295' @ 6295.00usft
Site:	Rosa Unit 24	North Reference:	True
Well:	Rosa Unit 702H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan #2		

Project	Rio Arriba, NM NAD83		
Map System:	US State Plane 1983	System Datum:	Mean Sea Level
Geo Datum:	North American Datum 1983		
Map Zone:	New Mexico Western Zone		

Site	Rosa Unit 24		
Site Position:		Northing:	2,152,358.66 usft
From:	Map	Easting:	2,849,944.67 usft
Position Uncertainty:	0.00 usft	Slot Radius:	13.20 in
		Latitude:	36.9141290
		Longitude:	-107.3994060
		Grid Convergence:	0.26 °

Well	Rosa Unit 702H - Slot A5 (702H)					
Well Position	+N/-S	-81.92 usft	Northing:	2,152,277.01 usft	Latitude:	36.9139040
	+E/-W	57.88 usft	Easting:	2,850,002.92 usft	Longitude:	-107.3992080
Position Uncertainty		0.00 usft	Wellhead Elevation:		Ground Level:	6,295.00 usft

Wellbore	OH				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	HDGM2021_FILE	10/11/2021	8.65	63.38	49,663.70000000

Design	Plan #2				
Audit Notes:					
Version:		Phase:	PLAN	Tie On Depth:	0.00
Vertical Section:	Depth From (TVD) (usft)	+N/-S (usft)	+E/-W (usft)	Direction (°)	
	0.00	0.00	0.00	262.956	

Plan Survey Tool Program	Date	1/31/2022			
Depth From (usft)	Depth To (usft)	Survey (Wellbore)	Tool Name	Remarks	
1	0.00	17,962.48 Plan #2 (OH)	MWD+HDGM		
			OWSG MWD + HDGM		

Plan Sections										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	TFO (°)	Target
0.00	0.00	0.000	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
500.00	0.00	0.000	500.00	0.00	0.00	0.00	0.00	0.00	0.00	
1,166.27	13.33	180.374	1,160.28	-77.13	-0.50	2.00	2.00	0.00	180.37	
6,459.20	13.33	180.374	6,310.71	-1,297.02	-8.46	0.00	0.00	0.00	0.00	
7,461.07	90.18	270.343	6,930.00	-1,440.36	-647.89	9.00	7.67	8.98	89.93	Rosa 702H POE
17,962.48	90.18	270.343	6,897.00	-1,377.59	-11,149.07	0.00	0.00	0.00	0.00	Rosa 702H BHL



Lonestar Consulting, LLC

Planning Report



Database:	Grand Junction	Local Co-ordinate Reference	Well Rosa Unit 702H - Slot A5 (702H)
Company:	Logos Operating LLC	TVD Reference:	GL 6295' @ 6295.00usft
Project:	Rio Arriba, NM NAD83	MD Reference:	GL 6295' @ 6295.00usft
Site:	Rosa Unit 24	North Reference:	True
Well:	Rosa Unit 702H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan #2		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
0.00	0.00	0.000	0.00	0.00	0.00	0.00	0.00	0.00	0.00
100.00	0.00	0.000	100.00	0.00	0.00	0.00	0.00	0.00	0.00
200.00	0.00	0.000	200.00	0.00	0.00	0.00	0.00	0.00	0.00
300.00	0.00	0.000	300.00	0.00	0.00	0.00	0.00	0.00	0.00
400.00	0.00	0.000	400.00	0.00	0.00	0.00	0.00	0.00	0.00
500.00	0.00	0.000	500.00	0.00	0.00	0.00	0.00	0.00	0.00
600.00	2.00	180.374	599.98	-1.75	-0.01	0.23	2.00	2.00	0.00
700.00	4.00	180.374	699.84	-6.98	-0.05	0.90	2.00	2.00	0.00
800.00	6.00	180.374	799.45	-15.69	-0.10	2.03	2.00	2.00	0.00
900.00	8.00	180.374	898.70	-27.88	-0.18	3.60	2.00	2.00	0.00
1,000.00	10.00	180.374	997.47	-43.52	-0.28	5.62	2.00	2.00	0.00
1,100.00	12.00	180.374	1,095.62	-62.60	-0.41	8.08	2.00	2.00	0.00
1,166.27	13.33	180.374	1,160.28	-77.13	-0.50	9.96	2.00	2.00	0.00
1,200.00	13.33	180.374	1,193.10	-84.90	-0.55	10.96	0.00	0.00	0.00
1,300.00	13.33	180.374	1,290.41	-107.95	-0.70	13.94	0.00	0.00	0.00
1,400.00	13.33	180.374	1,387.72	-131.00	-0.85	16.91	0.00	0.00	0.00
1,500.00	13.33	180.374	1,485.02	-154.04	-1.00	19.89	0.00	0.00	0.00
1,600.00	13.33	180.374	1,582.33	-177.09	-1.15	22.86	0.00	0.00	0.00
1,700.00	13.33	180.374	1,679.64	-200.14	-1.31	25.84	0.00	0.00	0.00
1,800.00	13.33	180.374	1,776.95	-223.19	-1.46	28.81	0.00	0.00	0.00
1,900.00	13.33	180.374	1,874.26	-246.24	-1.61	31.79	0.00	0.00	0.00
2,000.00	13.33	180.374	1,971.56	-269.28	-1.76	34.76	0.00	0.00	0.00
2,100.00	13.33	180.374	2,068.87	-292.33	-1.91	37.74	0.00	0.00	0.00
2,200.00	13.33	180.374	2,166.18	-315.38	-2.06	40.72	0.00	0.00	0.00
2,300.00	13.33	180.374	2,263.49	-338.43	-2.21	43.69	0.00	0.00	0.00
2,400.00	13.33	180.374	2,360.79	-361.47	-2.36	46.67	0.00	0.00	0.00
2,500.00	13.33	180.374	2,458.10	-384.52	-2.51	49.64	0.00	0.00	0.00
2,600.00	13.33	180.374	2,555.41	-407.57	-2.66	52.62	0.00	0.00	0.00
2,700.00	13.33	180.374	2,652.72	-430.62	-2.81	55.59	0.00	0.00	0.00
2,800.00	13.33	180.374	2,750.02	-453.66	-2.96	58.57	0.00	0.00	0.00
2,900.00	13.33	180.374	2,847.33	-476.71	-3.11	61.54	0.00	0.00	0.00
3,000.00	13.33	180.374	2,944.64	-499.76	-3.26	64.52	0.00	0.00	0.00
3,100.00	13.33	180.374	3,041.95	-522.81	-3.41	67.49	0.00	0.00	0.00
3,200.00	13.33	180.374	3,139.26	-545.86	-3.56	70.47	0.00	0.00	0.00
3,300.00	13.33	180.374	3,236.56	-568.90	-3.71	73.45	0.00	0.00	0.00
3,400.00	13.33	180.374	3,333.87	-591.95	-3.86	76.42	0.00	0.00	0.00
3,500.00	13.33	180.374	3,431.18	-615.00	-4.01	79.40	0.00	0.00	0.00
3,600.00	13.33	180.374	3,528.49	-638.05	-4.16	82.37	0.00	0.00	0.00
3,700.00	13.33	180.374	3,625.79	-661.09	-4.31	85.35	0.00	0.00	0.00
3,800.00	13.33	180.374	3,723.10	-684.14	-4.46	88.32	0.00	0.00	0.00
3,900.00	13.33	180.374	3,820.41	-707.19	-4.61	91.30	0.00	0.00	0.00
4,000.00	13.33	180.374	3,917.72	-730.24	-4.76	94.27	0.00	0.00	0.00
4,100.00	13.33	180.374	4,015.02	-753.28	-4.91	97.25	0.00	0.00	0.00
4,200.00	13.33	180.374	4,112.33	-776.33	-5.06	100.23	0.00	0.00	0.00
4,300.00	13.33	180.374	4,209.64	-799.38	-5.21	103.20	0.00	0.00	0.00
4,400.00	13.33	180.374	4,306.95	-822.43	-5.36	106.18	0.00	0.00	0.00
4,500.00	13.33	180.374	4,404.25	-845.47	-5.51	109.15	0.00	0.00	0.00
4,600.00	13.33	180.374	4,501.56	-868.52	-5.66	112.13	0.00	0.00	0.00
4,700.00	13.33	180.374	4,598.87	-891.57	-5.81	115.10	0.00	0.00	0.00
4,800.00	13.33	180.374	4,696.18	-914.62	-5.96	118.08	0.00	0.00	0.00
4,900.00	13.33	180.374	4,793.49	-937.67	-6.12	121.05	0.00	0.00	0.00
5,000.00	13.33	180.374	4,890.79	-960.71	-6.27	124.03	0.00	0.00	0.00
5,100.00	13.33	180.374	4,988.10	-983.76	-6.42	127.00	0.00	0.00	0.00



Lonestar Consulting, LLC

Planning Report



Database:	Grand Junction	Local Co-ordinate Reference	Well Rosa Unit 702H - Slot A5 (702H)
Company:	Logos Operating LLC	TVD Reference:	GL 6295' @ 6295.00usft
Project:	Rio Arriba, NM NAD83	MD Reference:	GL 6295' @ 6295.00usft
Site:	Rosa Unit 24	North Reference:	True
Well:	Rosa Unit 702H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan #2		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
5,200.00	13.33	180.374	5,085.41	-1,006.81	-6.57	129.98	0.00	0.00	0.00	
5,300.00	13.33	180.374	5,182.72	-1,029.86	-6.72	132.96	0.00	0.00	0.00	
5,400.00	13.33	180.374	5,280.02	-1,052.90	-6.87	135.93	0.00	0.00	0.00	
5,500.00	13.33	180.374	5,377.33	-1,075.95	-7.02	138.91	0.00	0.00	0.00	
5,600.00	13.33	180.374	5,474.64	-1,099.00	-7.17	141.88	0.00	0.00	0.00	
5,700.00	13.33	180.374	5,571.95	-1,122.05	-7.32	144.86	0.00	0.00	0.00	
5,800.00	13.33	180.374	5,669.25	-1,145.09	-7.47	147.83	0.00	0.00	0.00	
5,900.00	13.33	180.374	5,766.56	-1,168.14	-7.62	150.81	0.00	0.00	0.00	
6,000.00	13.33	180.374	5,863.87	-1,191.19	-7.77	153.78	0.00	0.00	0.00	
6,100.00	13.33	180.374	5,961.18	-1,214.24	-7.92	156.76	0.00	0.00	0.00	
6,200.00	13.33	180.374	6,058.49	-1,237.29	-8.07	159.73	0.00	0.00	0.00	
6,300.00	13.33	180.374	6,155.79	-1,260.33	-8.22	162.71	0.00	0.00	0.00	
6,400.00	13.33	180.374	6,253.10	-1,283.38	-8.37	165.69	0.00	0.00	0.00	
6,459.20	13.33	180.374	6,310.71	-1,297.02	-8.46	167.45	0.00	0.00	0.00	
6,500.00	13.82	195.928	6,350.38	-1,306.41	-9.83	169.96	9.00	1.21	38.12	
6,600.00	18.32	224.631	6,446.60	-1,329.13	-24.18	186.98	9.00	4.50	28.70	
6,700.00	25.29	240.208	6,539.46	-1,350.97	-53.81	219.07	9.00	6.97	15.58	
6,800.00	33.20	249.077	6,626.69	-1,371.40	-98.01	265.44	9.00	7.91	8.87	
6,900.00	41.51	254.779	6,706.14	-1,389.92	-155.67	324.94	9.00	8.32	5.70	
7,000.00	50.03	258.849	6,775.84	-1,406.06	-225.39	396.11	9.00	8.52	4.07	
7,100.00	58.66	262.007	6,834.08	-1,419.44	-305.44	477.20	9.00	8.63	3.16	
7,200.00	67.35	264.628	6,879.44	-1,429.72	-393.85	566.21	9.00	8.69	2.62	
7,300.00	76.08	266.935	6,910.78	-1,436.65	-488.45	660.94	9.00	8.73	2.31	
7,400.00	84.83	269.073	6,927.34	-1,440.05	-586.91	759.07	9.00	8.75	2.14	
7,461.07	90.18	270.343	6,930.00	-1,440.36	-647.89	819.63	9.00	8.76	2.08	
7,500.00	90.18	270.343	6,929.88	-1,440.13	-686.83	858.24	0.00	0.00	0.00	
7,600.00	90.18	270.343	6,929.56	-1,439.53	-786.82	957.41	0.00	0.00	0.00	
7,700.00	90.18	270.343	6,929.25	-1,438.93	-886.82	1,056.58	0.00	0.00	0.00	
7,800.00	90.18	270.343	6,928.94	-1,438.34	-986.82	1,155.75	0.00	0.00	0.00	
7,900.00	90.18	270.343	6,928.62	-1,437.74	-1,086.82	1,254.92	0.00	0.00	0.00	
8,000.00	90.18	270.343	6,928.31	-1,437.14	-1,186.81	1,354.09	0.00	0.00	0.00	
8,100.00	90.18	270.343	6,927.99	-1,436.54	-1,286.81	1,453.26	0.00	0.00	0.00	
8,200.00	90.18	270.343	6,927.68	-1,435.94	-1,386.81	1,552.43	0.00	0.00	0.00	
8,300.00	90.18	270.343	6,927.36	-1,435.34	-1,486.81	1,651.60	0.00	0.00	0.00	
8,400.00	90.18	270.343	6,927.05	-1,434.75	-1,586.81	1,750.77	0.00	0.00	0.00	
8,500.00	90.18	270.343	6,926.74	-1,434.15	-1,686.80	1,849.94	0.00	0.00	0.00	
8,600.00	90.18	270.343	6,926.42	-1,433.55	-1,786.80	1,949.11	0.00	0.00	0.00	
8,700.00	90.18	270.343	6,926.11	-1,432.95	-1,886.80	2,048.28	0.00	0.00	0.00	
8,800.00	90.18	270.343	6,925.79	-1,432.35	-1,986.80	2,147.45	0.00	0.00	0.00	
8,900.00	90.18	270.343	6,925.48	-1,431.76	-2,086.79	2,246.62	0.00	0.00	0.00	
9,000.00	90.18	270.343	6,925.16	-1,431.16	-2,186.79	2,345.79	0.00	0.00	0.00	
9,100.00	90.18	270.343	6,924.85	-1,430.56	-2,286.79	2,444.96	0.00	0.00	0.00	
9,200.00	90.18	270.343	6,924.54	-1,429.96	-2,386.79	2,544.13	0.00	0.00	0.00	
9,300.00	90.18	270.343	6,924.22	-1,429.36	-2,486.78	2,643.30	0.00	0.00	0.00	
9,400.00	90.18	270.343	6,923.91	-1,428.77	-2,586.78	2,742.47	0.00	0.00	0.00	
9,500.00	90.18	270.343	6,923.59	-1,428.17	-2,686.78	2,841.64	0.00	0.00	0.00	
9,600.00	90.18	270.343	6,923.28	-1,427.57	-2,786.78	2,940.81	0.00	0.00	0.00	
9,700.00	90.18	270.343	6,922.96	-1,426.97	-2,886.78	3,039.98	0.00	0.00	0.00	
9,800.00	90.18	270.343	6,922.65	-1,426.37	-2,986.77	3,139.14	0.00	0.00	0.00	
9,900.00	90.18	270.343	6,922.34	-1,425.77	-3,086.77	3,238.31	0.00	0.00	0.00	
10,000.00	90.18	270.343	6,922.02	-1,425.18	-3,186.77	3,337.48	0.00	0.00	0.00	
10,100.00	90.18	270.343	6,921.71	-1,424.58	-3,286.77	3,436.65	0.00	0.00	0.00	
10,200.00	90.18	270.343	6,921.39	-1,423.98	-3,386.76	3,535.82	0.00	0.00	0.00	



Lonestar Consulting, LLC

Planning Report



Database:	Grand Junction	Local Co-ordinate Reference	Well Rosa Unit 702H - Slot A5 (702H)
Company:	Logos Operating LLC	TVD Reference:	GL 6295' @ 6295.00usft
Project:	Rio Arriba, NM NAD83	MD Reference:	GL 6295' @ 6295.00usft
Site:	Rosa Unit 24	North Reference:	True
Well:	Rosa Unit 702H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan #2		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
10,300.00	90.18	270.343	6,921.08	-1,423.38	-3,486.76	3,634.99	0.00	0.00	0.00	
10,400.00	90.18	270.343	6,920.76	-1,422.78	-3,586.76	3,734.16	0.00	0.00	0.00	
10,500.00	90.18	270.343	6,920.45	-1,422.19	-3,686.76	3,833.33	0.00	0.00	0.00	
10,600.00	90.18	270.343	6,920.14	-1,421.59	-3,786.75	3,932.50	0.00	0.00	0.00	
10,700.00	90.18	270.343	6,919.82	-1,420.99	-3,886.75	4,031.67	0.00	0.00	0.00	
10,800.00	90.18	270.343	6,919.51	-1,420.39	-3,986.75	4,130.84	0.00	0.00	0.00	
10,900.00	90.18	270.343	6,919.19	-1,419.79	-4,086.75	4,230.01	0.00	0.00	0.00	
11,000.00	90.18	270.343	6,918.88	-1,419.20	-4,186.75	4,329.18	0.00	0.00	0.00	
11,100.00	90.18	270.343	6,918.57	-1,418.60	-4,286.74	4,428.35	0.00	0.00	0.00	
11,200.00	90.18	270.343	6,918.25	-1,418.00	-4,386.74	4,527.52	0.00	0.00	0.00	
11,300.00	90.18	270.343	6,917.94	-1,417.40	-4,486.74	4,626.69	0.00	0.00	0.00	
11,400.00	90.18	270.343	6,917.62	-1,416.80	-4,586.74	4,725.86	0.00	0.00	0.00	
11,500.00	90.18	270.343	6,917.31	-1,416.20	-4,686.73	4,825.03	0.00	0.00	0.00	
11,600.00	90.18	270.343	6,916.99	-1,415.61	-4,786.73	4,924.20	0.00	0.00	0.00	
11,700.00	90.18	270.343	6,916.68	-1,415.01	-4,886.73	5,023.37	0.00	0.00	0.00	
11,800.00	90.18	270.343	6,916.37	-1,414.41	-4,986.73	5,122.54	0.00	0.00	0.00	
11,900.00	90.18	270.343	6,916.05	-1,413.81	-5,086.73	5,221.71	0.00	0.00	0.00	
12,000.00	90.18	270.343	6,915.74	-1,413.21	-5,186.72	5,320.88	0.00	0.00	0.00	
12,100.00	90.18	270.343	6,915.42	-1,412.62	-5,286.72	5,420.05	0.00	0.00	0.00	
12,200.00	90.18	270.343	6,915.11	-1,412.02	-5,386.72	5,519.22	0.00	0.00	0.00	
12,300.00	90.18	270.343	6,914.79	-1,411.42	-5,486.72	5,618.39	0.00	0.00	0.00	
12,400.00	90.18	270.343	6,914.48	-1,410.82	-5,586.71	5,717.56	0.00	0.00	0.00	
12,500.00	90.18	270.343	6,914.17	-1,410.22	-5,686.71	5,816.73	0.00	0.00	0.00	
12,600.00	90.18	270.343	6,913.85	-1,409.62	-5,786.71	5,915.90	0.00	0.00	0.00	
12,700.00	90.18	270.343	6,913.54	-1,409.03	-5,886.71	6,015.06	0.00	0.00	0.00	
12,800.00	90.18	270.343	6,913.22	-1,408.43	-5,986.70	6,114.23	0.00	0.00	0.00	
12,900.00	90.18	270.343	6,912.91	-1,407.83	-6,086.70	6,213.40	0.00	0.00	0.00	
13,000.00	90.18	270.343	6,912.59	-1,407.23	-6,186.70	6,312.57	0.00	0.00	0.00	
13,100.00	90.18	270.343	6,912.28	-1,406.63	-6,286.70	6,411.74	0.00	0.00	0.00	
13,200.00	90.18	270.343	6,911.97	-1,406.04	-6,386.70	6,510.91	0.00	0.00	0.00	
13,300.00	90.18	270.343	6,911.65	-1,405.44	-6,486.69	6,610.08	0.00	0.00	0.00	
13,400.00	90.18	270.343	6,911.34	-1,404.84	-6,586.69	6,709.25	0.00	0.00	0.00	
13,500.00	90.18	270.343	6,911.02	-1,404.24	-6,686.69	6,808.42	0.00	0.00	0.00	
13,600.00	90.18	270.343	6,910.71	-1,403.64	-6,786.69	6,907.59	0.00	0.00	0.00	
13,700.00	90.18	270.343	6,910.39	-1,403.05	-6,886.68	7,006.76	0.00	0.00	0.00	
13,800.00	90.18	270.343	6,910.08	-1,402.45	-6,986.68	7,105.93	0.00	0.00	0.00	
13,900.00	90.18	270.343	6,909.77	-1,401.85	-7,086.68	7,205.10	0.00	0.00	0.00	
14,000.00	90.18	270.343	6,909.45	-1,401.25	-7,186.68	7,304.27	0.00	0.00	0.00	
14,100.00	90.18	270.343	6,909.14	-1,400.65	-7,286.68	7,403.44	0.00	0.00	0.00	
14,200.00	90.18	270.343	6,908.82	-1,400.05	-7,386.67	7,502.61	0.00	0.00	0.00	
14,300.00	90.18	270.343	6,908.51	-1,399.46	-7,486.67	7,601.78	0.00	0.00	0.00	
14,400.00	90.18	270.343	6,908.20	-1,398.86	-7,586.67	7,700.95	0.00	0.00	0.00	
14,500.00	90.18	270.343	6,907.88	-1,398.26	-7,686.67	7,800.12	0.00	0.00	0.00	
14,600.00	90.18	270.343	6,907.57	-1,397.66	-7,786.66	7,899.29	0.00	0.00	0.00	
14,700.00	90.18	270.343	6,907.25	-1,397.06	-7,886.66	7,998.46	0.00	0.00	0.00	
14,800.00	90.18	270.343	6,906.94	-1,396.47	-7,986.66	8,097.63	0.00	0.00	0.00	
14,900.00	90.18	270.343	6,906.62	-1,395.87	-8,086.66	8,196.80	0.00	0.00	0.00	
15,000.00	90.18	270.343	6,906.31	-1,395.27	-8,186.65	8,295.97	0.00	0.00	0.00	
15,100.00	90.18	270.343	6,906.00	-1,394.67	-8,286.65	8,395.14	0.00	0.00	0.00	
15,200.00	90.18	270.343	6,905.68	-1,394.07	-8,386.65	8,494.31	0.00	0.00	0.00	
15,300.00	90.18	270.343	6,905.37	-1,393.48	-8,486.65	8,593.48	0.00	0.00	0.00	
15,400.00	90.18	270.343	6,905.05	-1,392.88	-8,586.65	8,692.65	0.00	0.00	0.00	
15,500.00	90.18	270.343	6,904.74	-1,392.28	-8,686.64	8,791.81	0.00	0.00	0.00	



Lonestar Consulting, LLC

Planning Report



Database:	Grand Junction	Local Co-ordinate Reference	Well Rosa Unit 702H - Slot A5 (702H)
Company:	Logos Operating LLC	TVD Reference:	GL 6295' @ 6295.00usft
Project:	Rio Arriba, NM NAD83	MD Reference:	GL 6295' @ 6295.00usft
Site:	Rosa Unit 24	North Reference:	True
Well:	Rosa Unit 702H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan #2		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
15,600.00	90.18	270.343	6,904.42	-1,391.68	-8,786.64	8,890.98	0.00	0.00	0.00	
15,700.00	90.18	270.343	6,904.11	-1,391.08	-8,886.64	8,990.15	0.00	0.00	0.00	
15,800.00	90.18	270.343	6,903.80	-1,390.48	-8,986.64	9,089.32	0.00	0.00	0.00	
15,900.00	90.18	270.343	6,903.48	-1,389.89	-9,086.63	9,188.49	0.00	0.00	0.00	
16,000.00	90.18	270.343	6,903.17	-1,389.29	-9,186.63	9,287.66	0.00	0.00	0.00	
16,100.00	90.18	270.343	6,902.85	-1,388.69	-9,286.63	9,386.83	0.00	0.00	0.00	
16,200.00	90.18	270.343	6,902.54	-1,388.09	-9,386.63	9,486.00	0.00	0.00	0.00	
16,300.00	90.18	270.343	6,902.22	-1,387.49	-9,486.62	9,585.17	0.00	0.00	0.00	
16,400.00	90.18	270.343	6,901.91	-1,386.90	-9,586.62	9,684.34	0.00	0.00	0.00	
16,500.00	90.18	270.343	6,901.60	-1,386.30	-9,686.62	9,783.51	0.00	0.00	0.00	
16,600.00	90.18	270.343	6,901.28	-1,385.70	-9,786.62	9,882.68	0.00	0.00	0.00	
16,700.00	90.18	270.343	6,900.97	-1,385.10	-9,886.62	9,981.85	0.00	0.00	0.00	
16,800.00	90.18	270.343	6,900.65	-1,384.50	-9,986.61	10,081.02	0.00	0.00	0.00	
16,900.00	90.18	270.343	6,900.34	-1,383.90	-10,086.61	10,180.19	0.00	0.00	0.00	
17,000.00	90.18	270.343	6,900.02	-1,383.31	-10,186.61	10,279.36	0.00	0.00	0.00	
17,100.00	90.18	270.343	6,899.71	-1,382.71	-10,286.61	10,378.53	0.00	0.00	0.00	
17,200.00	90.18	270.343	6,899.40	-1,382.11	-10,386.60	10,477.70	0.00	0.00	0.00	
17,300.00	90.18	270.343	6,899.08	-1,381.51	-10,486.60	10,576.87	0.00	0.00	0.00	
17,400.00	90.18	270.343	6,898.77	-1,380.91	-10,586.60	10,676.04	0.00	0.00	0.00	
17,500.00	90.18	270.343	6,898.45	-1,380.32	-10,686.60	10,775.21	0.00	0.00	0.00	
17,600.00	90.18	270.343	6,898.14	-1,379.72	-10,786.60	10,874.38	0.00	0.00	0.00	
17,700.00	90.18	270.343	6,897.82	-1,379.12	-10,886.59	10,973.55	0.00	0.00	0.00	
17,800.00	90.18	270.343	6,897.51	-1,378.52	-10,986.59	11,072.72	0.00	0.00	0.00	
17,900.00	90.18	270.343	6,897.20	-1,377.92	-11,086.59	11,171.89	0.00	0.00	0.00	
17,962.48	90.18	270.343	6,897.00	-1,377.59	-11,149.07	11,233.86	0.00	0.00	0.00	

Design Targets									
Target Name	Dip Angle (°)	Dip Dir. (°)	TVD (usft)	+N/-S (usft)	+E/-W (usft)	Northing (usft)	Easting (usft)	Latitude	Longitude
- hit/miss target									
- Shape									
Rosa 702H BHL	0.00	0.000	6,897.00	-1,377.59	-11,149.07	2,150,848.69	2,838,860.24	36.9101140	-107.4373432
- plan hits target center									
- Point									
Rosa 702H POE	0.00	0.000	6,930.00	-1,440.36	-647.89	2,150,833.71	2,849,361.59	36.9099477	-107.4014241
- plan hits target center									
- Point									



Lonestar Consulting, LLC
Planning Report



Database:	Grand Junction	Local Co-ordinate Reference	Well Rosa Unit 702H - Slot A5 (702H)
Company:	Logos Operating LLC	TVD Reference:	GL 6295' @ 6295.00usft
Project:	Rio Arriba, NM NAD83	MD Reference:	GL 6295' @ 6295.00usft
Site:	Rosa Unit 24	North Reference:	True
Well:	Rosa Unit 702H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan #2		

Formations						
	Measured Depth (usft)	Vertical Depth (usft)	Name	Lithology	Dip (°)	Dip Direction (°)
	2,437.21	2,397.00	Ojo Alamo		0.00	0.000
	2,550.25	2,507.00	Kirtland		0.00	0.000
	3,052.78	2,996.00	Fruitland		0.00	0.000
	3,384.72	3,319.00	Pictured Cliffs		0.00	0.000
	3,492.62	3,424.00	Lewis		0.00	0.000
	4,648.75	4,549.00	Chacra		0.00	0.000
	5,433.89	5,313.00	Cliff House		0.00	0.000
	5,489.38	5,367.00	Menefee		0.00	0.000
	5,724.72	5,596.00	Point Lookout		0.00	0.000
	6,276.58	6,133.00	Mancos		0.00	0.000



Logos Operating LLC

Rio Arriba, NM NAD83

Rosa Unit 24

Rosa Unit 702H

OH

Plan #2

Anticollision Summary Report

31 January, 2022





Lonestar Consulting, LLC

Anticollision Summary Report



Company:	Logos Operating LLC	Local Co-ordinate Reference	Well Rosa Unit 702H - Slot A5 (702H)
Project:	Rio Arriba, NM NAD83	TVD Reference:	GL 6295' @ 6295.00usft
Reference Site:	Rosa Unit 24	MD Reference:	GL 6295' @ 6295.00usft
Site Error:	0.00 usft	North Reference:	True
Reference Well:	Rosa Unit 702H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	OH	Database:	Grand Junction
Reference Design:	Plan #2	Offset TVD Reference:	Reference Datum

Reference	Plan #2
Filter type:	NO GLOBAL FILTER: Using user defined selection & filtering criteria
Interpolation Method	MD Interval 100.00usft
Depth Range:	Unlimited
Results Limited by:	Maximum centre distance of 9,999.98usft
Warning Levels Evaluated at:	2.00 Sigma
Error Model:	ISCWSA
Scan Method:	Closest Approach 3D
Error Surface:	Pedal Curve
Casing Method:	Not applied

Survey Tool Program		Date	1/31/2022		
From (usft)	To (usft)	Survey (Wellbore)	Tool Name	Description	
0.00	17,962.48	Plan #2 (OH)	MWD+HDGM	OWSG MWD + HDGM	

Summary						
Site Name	Reference Measure	Offset Measure	Distance Between Centres (usft)	Distance Between Ellipses (usft)	Separation	Warning
Offset Well - Wellbore - Design						
Rosa Unit 24						
Rosa Unit #001E - OH - OH	14,631.75	6,957.48	310.32	-133.85	0.699	Level 3, CC, ES, SF
Rosa Unit #030 - OH - OH	10,237.75	7,119.83	268.24	-49.42	0.844	Level 3, CC, ES, SF
Rosa Unit #036B - OH - OH	16,051.77	6,100.00	891.16	738.67	5.844	CC, ES
Rosa Unit #036B - OH - OH	16,500.00	6,100.00	997.54	811.42	5.360	SF
Rosa Unit #154 - OH - OH	8,263.23	6,320.00	887.03	772.81	7.766	CC
Rosa Unit #154 - OH - OH	8,300.00	6,320.00	887.79	772.60	7.707	ES
Rosa Unit #154 - OH - OH	8,900.00	6,320.00	1,091.93	922.52	6.446	SF
Rosa Unit #216 - OH - OH	17,400.14	2,995.00	3,897.30	3,799.59	39.883	CC, ES
Rosa Unit #216 - OH - OH	17,962.48	2,995.00	3,937.67	3,829.70	36.470	SF
Rosa Unit #217A - OH - OH	16,079.98	2,980.00	3,993.26	3,907.06	46.327	CC
Rosa Unit #217A - OH - OH	16,100.00	2,980.00	3,993.31	3,906.94	46.237	ES
Rosa Unit #217A - OH - OH	17,962.48	2,980.00	4,414.75	4,293.13	36.300	SF
Rosa Unit #217A - ST - ST	13,700.00	5,153.00	3,985.23	3,892.57	43.006	SF
Rosa Unit #217A - ST - ST	15,268.88	3,896.39	3,862.81	3,784.54	49.351	CC
Rosa Unit #217A - ST - ST	15,300.00	3,886.55	3,862.90	3,784.51	49.277	ES
Rosa Unit #225 - OH - OH	12,825.82	2,854.00	4,165.95	4,110.81	75.560	CC
Rosa Unit #225 - OH - OH	12,900.00	2,854.00	4,166.61	4,110.60	74.400	ES
Rosa Unit #225 - OH - OH	15,700.00	2,854.00	5,061.23	4,950.49	45.704	SF
Rosa Unit #225A - OH - OH	10,851.25	3,385.00	3,965.09	3,921.89	91.800	CC
Rosa Unit #225A - OH - OH	10,900.00	3,385.00	3,965.39	3,921.86	91.104	ES
Rosa Unit #225A - OH - OH	12,900.00	3,385.00	4,463.10	4,405.06	76.889	SF
Rosa Unit 700H - OH - Plan #2	500.00	500.00	25.22	21.63	7.034	CC
Rosa Unit 700H - OH - Plan #2	600.00	600.68	25.29	21.02	5.924	ES
Rosa Unit 700H - OH - Plan #2	17,962.48	17,750.26	1,254.28	585.58	1.876	SF
Rosa Unit 701H - OH - Plan #1	895.82	904.33	26.00	19.73	4.146	CC
Rosa Unit 701H - OH - Plan #1	900.00	908.51	26.01	19.71	4.127	ES
Rosa Unit 701H - OH - Plan #1	17,962.48	18,035.91	660.59	21.30	1.033	Level 3, SF
Rosa Unit 704H - OH - Plan #2	1,092.34	1,091.70	49.96	42.42	6.620	CC
Rosa Unit 704H - OH - Plan #2	1,100.00	1,099.28	49.97	42.37	6.570	ES
Rosa Unit 704H - OH - Plan #2	1,200.00	1,198.05	52.20	43.80	6.215	SF
Rosa Unit 705H - OH - Plan #1	414.91	419.91	26.53	23.53	8.864	CC
Rosa Unit 705H - OH - Plan #1	600.00	604.29	26.95	22.67	6.296	ES
Rosa Unit 705H - OH - Plan #1	1,300.00	1,300.72	44.05	34.55	4.635	SF
Rosa Unit 706H - OH - Plan #2	414.91	419.91	25.09	22.09	8.383	CC
Rosa Unit 706H - OH - Plan #2	700.00	703.40	25.92	20.99	5.250	ES
Rosa Unit 706H - OH - Plan #2	1,200.00	1,199.22	34.30	25.77	4.024	SF

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Lonestar Consulting, LLC

Anticollision Summary Report



Company:	Logos Operating LLC	Local Co-ordinate Reference	Well Rosa Unit 702H - Slot A5 (702H)
Project:	Rio Arriba, NM NAD83	TVD Reference:	GL 6295' @ 6295.00usft
Reference Site:	Rosa Unit 24	MD Reference:	GL 6295' @ 6295.00usft
Site Error:	0.00 usft	North Reference:	True
Reference Well:	Rosa Unit 702H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	OH	Database:	Grand Junction
Reference Design:	Plan #2	Offset TVD Reference:	Reference Datum

Summary						
Site Name	Reference Measure	Offset Measure	Distance Between Centres (usft)	Distance Between Ellipses (usft)	Separation	Warning
Offset Well - Wellbore - Design						



Lonestar Consulting, LLC


Anticollision Summary Report



Company:	Logos Operating LLC	Local Co-ordinate Reference	Well Rosa Unit 702H - Slot A5 (702H)
Project:	Rio Arriba, NM NAD83	TVD Reference:	GL 6295' @ 6295.00usft
Reference Site:	Rosa Unit 24	MD Reference:	GL 6295' @ 6295.00usft
Site Error:	0.00 usft	North Reference:	True
Reference Well:	Rosa Unit 702H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	OH	Database:	Grand Junction
Reference Design:	Plan #2	Offset TVD Reference:	Reference Datum

Reference Depths are relative to GL 6295' @ 6295.00usft
 Offset Depths are relative to Offset Datum
 Central Meridian is -107.8333334

Coordinates are relative to: Rosa Unit 702H - Slot A5 (702H)
 Coordinate System is US State Plane 1983, New Mexico Western Zone
 Grid Convergence at Surface is: 0.26°

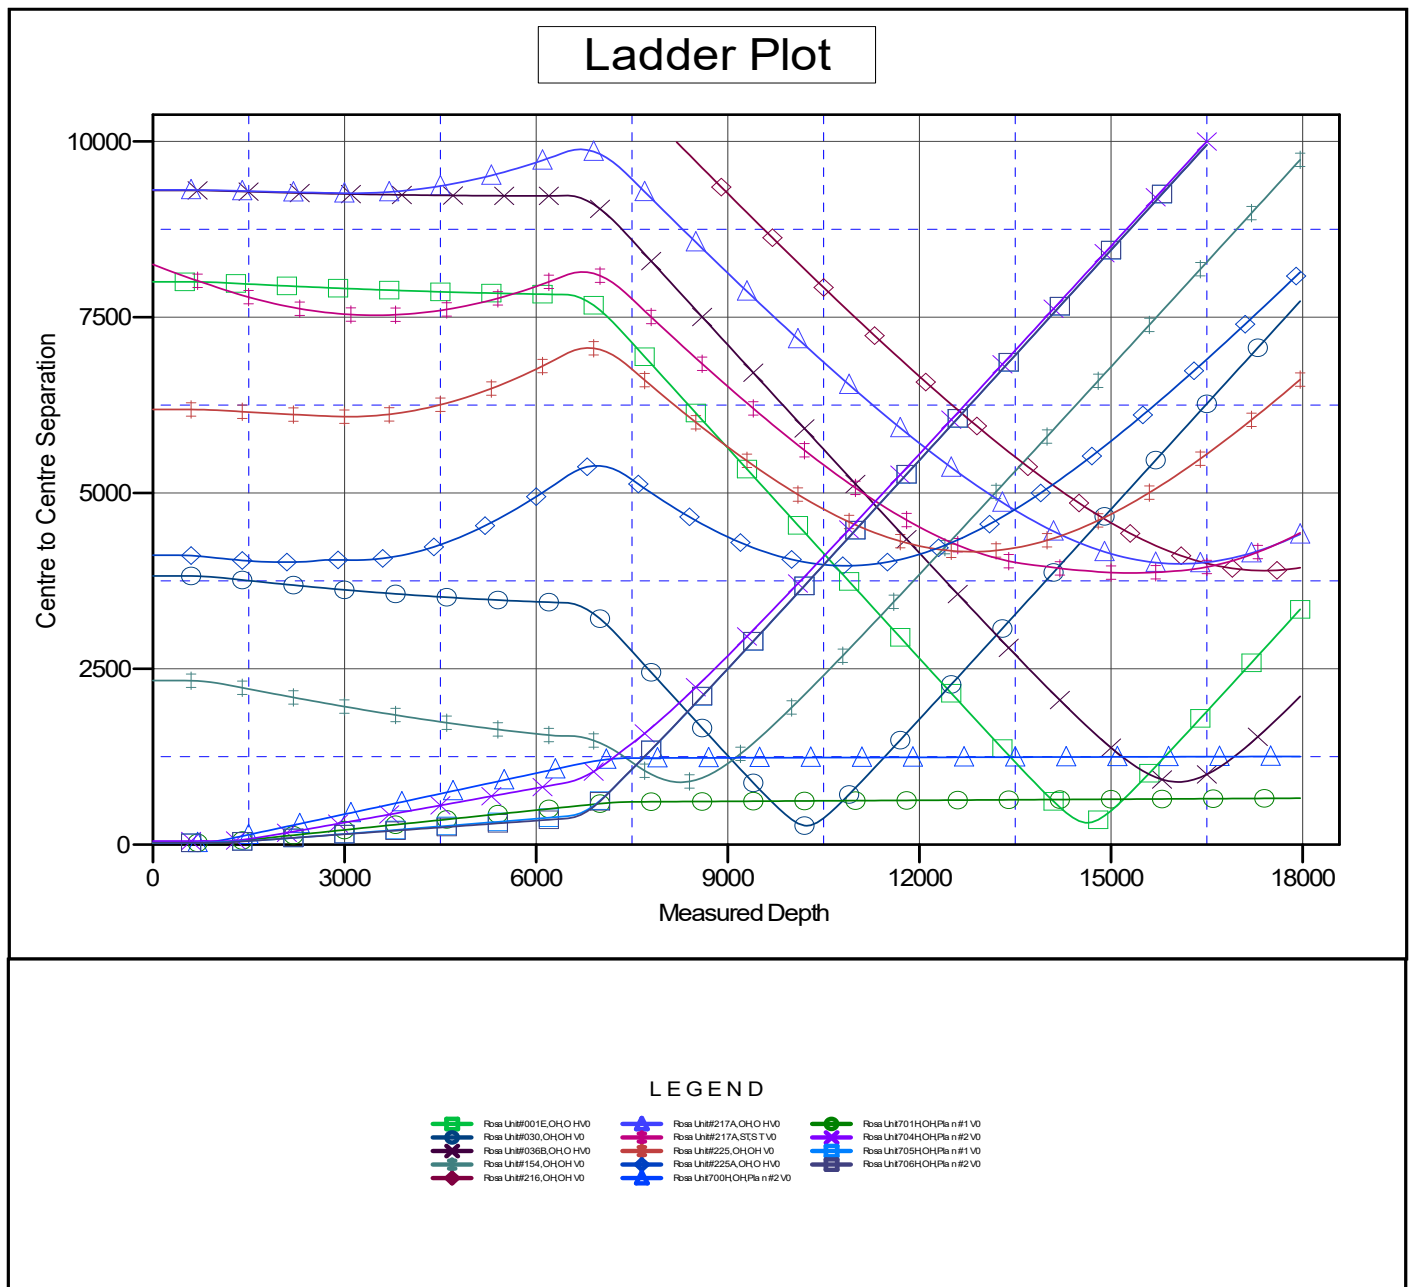

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Lonestar Consulting, LLC

Anticollision Summary Report




Company:	Logos Operating LLC	Local Co-ordinate Reference	Well Rosa Unit 702H - Slot A5 (702H)
Project:	Rio Arriba, NM NAD83	TVD Reference:	GL 6295' @ 6295.00usft
Reference Site:	Rosa Unit 24	MD Reference:	GL 6295' @ 6295.00usft
Site Error:	0.00 usft	North Reference:	True
Reference Well:	Rosa Unit 702H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	OH	Database:	Grand Junction
Reference Design:	Plan #2	Offset TVD Reference:	Reference Datum

Reference Depths are relative to GL 6295' @ 6295.00usft
 Offset Depths are relative to Offset Datum
 Central Meridian is -107.8333334

Coordinates are relative to: Rosa Unit 702H - Slot A5 (702H)
 Coordinate System is US State Plane 1983, New Mexico Western Zone
 Grid Convergence at Surface is: 0.26°

Separation Factor Plot

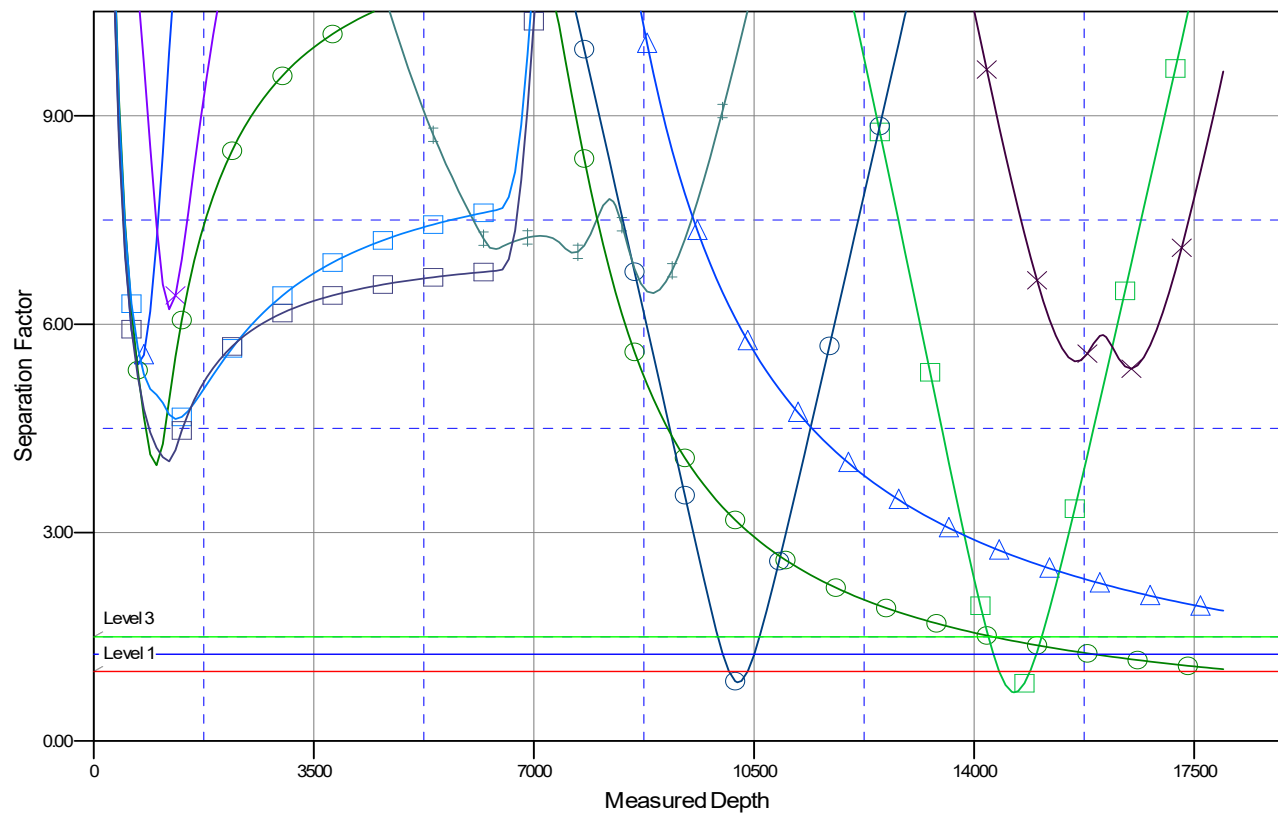

LEGEND

Rosa Unit#001E, OH/O HVO	Rosa Unit#217A, OH/O HVO	Rosa Unit#701H, OH/Pa n#1 V0
Rosa Unit#030, OH/O HVO	Rosa Unit#217A, STS TVO	Rosa Unit#704H, OH/Pa n#2 V0
Rosa Unit#036B, OH/O HVO	Rosa Unit#225, OH/O HVO	Rosa Unit#705H, OH/Pa n#1 V0
Rosa Unit#154, OH/O HVO	Rosa Unit#225A, OH/O HVO	Rosa Unit#706H, OH/Pa n#2 V0
Rosa Unit#216, OH/O HVO	Rosa Unit#700H, OH/Pa n#2 V0	

District I

1625 N. French Dr., Hobbs, NM 88240
 Phone:(575) 393-6161 Fax:(575) 393-0720

District II

811 S. First St., Artesia, NM 88210
 Phone:(575) 748-1283 Fax:(575) 748-9720

District III

1000 Rio Brazos Rd., Aztec, NM 87410
 Phone:(505) 334-6178 Fax:(505) 334-6170

District IV

1220 S. St Francis Dr., Santa Fe, NM 87505
 Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 286826

CONDITIONS

Operator: LOGOS OPERATING, LLC 2010 Afton Place Farmington, NM 87401	OGRID: 289408
	Action Number: 286826
	Action Type: [C-101] BLM - Federal/Indian Land Lease (Form 3160-3)

CONDITIONS

Created By	Condition	Condition Date
ward.rikala	Notify OCD 24 hours prior to casing & cement	12/5/2023
ward.rikala	Will require a File As Drilled C-102 and a Directional Survey with the C-104	12/5/2023
ward.rikala	Once the well is spud, to prevent ground water contamination through whole or partial conduits from the surface, the operator shall drill without interruption through the fresh water zone or zones and shall immediately set in cement the water protection string	12/5/2023
ward.rikala	Cement is required to circulate on both surface and intermediate1 strings of casing	12/5/2023
ward.rikala	If cement does not circulate on any string, a CBL is required for that string of casing	12/5/2023
ward.rikala	Oil base muds are not to be used until fresh water zones are cased and cemented providing isolation from the oil or diesel. This includes synthetic oils. Oil based mud, drilling fluids and solids must be contained in a steel closed loop system	12/5/2023
