

District I
1625 N. French Dr., Hobbs, NM 88240
District II
811 S. First St., Artesia, NM 88210
District III
1000 Rio Brazos Rd., Aztec, NM 87410
District IV
1220 S. St. Francis Dr., Santa Fe, NM 87505

State of New Mexico
Energy, Minerals & Natural
Resources

Form C-104
Revised August 1, 2011

Submit one copy to appropriate District Office

Oil Conservation Division
1220 South St. Francis Dr.

☐ AMENDED REPORT

I. REQUEST FOR ALLOWABLE MINERAL AUTHORIZATION TO TRANSPORT

¹ Operator name and Address EOG RESOURCES INC PO BOX 2267 MIDLAND, TEXAS 79702		² OGRID Number 7377
		³ Reason for Filing Code/ Effective Date NW 7/8/2022
⁴ API Number 30 - 015-48315	⁵ Pool Name Purple Sage; Wolfcamp	⁶ Pool Code 98220
⁷ Property Code 322721	⁸ Property Name GOLDEN GRAHAM 1 STATE COM	⁹ Well Number 723H

II. ¹⁰ Surface Location

UL or lot no. N	Section 1	Township 26S	Range 28E	Lot Idn	Feet from the 215'	North/South Line SOUTH	Feet from the 1799'	East/West line WEST	County LEA
--------------------	--------------	-----------------	--------------	---------	-----------------------	---------------------------	------------------------	------------------------	---------------

¹¹ Bottom Hole Location

UL or lot no. C	Section 36	Township 25S	Range 28E	Lot Idn	Feet from the 341'	North/South line NORTH	Feet from the 1792'	East/West line WEST	County LEA
¹² Lse Code	¹³ Producing Method Code FLOWING	¹⁴ Gas Connection Date	¹⁵ C-129 Permit Number		¹⁶ C-129 Effective Date		¹⁷ C-129 Expiration Date		

III. Oil and Gas Transporters

¹⁸ Transporter OGRID	¹⁹ Transporter Name and Address	²⁰ O/G/W
372812	EOGRM	OIL
151618	ENTERPRISE FIELD SERVICES	GAS
298751	REGENCY FIELD SERVICES	GAS
36785	DCP MIDSTREAM	GAS

IV. Well Completion Data

²¹ Spud Date 07/14/2021	²² Ready Date 07/8/2022	²³ TD 19,945'	²⁴ PBTD 19,922'	²⁵ Perforations 10,002'-19,922'	²⁶ DHC, MC
²⁷ Hole Size		²⁸ Casing & Tubing Size		²⁹ Depth Set	³⁰ Sacks Cement
16"		9 5/8"		791'	425 SXS CL C/CIRC
8 3/4"		7 5/8"		9,058'	1415 SXS CL C/CIRC
8 1/2"		5 1/2"		19,930'	975 SXS CL H/CIRC TOC @9358' PRESSURE TEST ATTACHED

V. Well Test Data

³¹ Date New Oil 7/8/2022	³² Gas Delivery Date 7/8/2022	³³ Test Date 7/13/2022	³⁴ Test Length 24 HRS	³⁵ Tbg. Pressure	³⁶ Csg. Pressure 958
³⁷ Choke Size 100	³⁸ Oil 2441	³⁹ Water 7629	⁴⁰ Gas 8673		⁴¹ Test Method
⁴² I hereby certify that the rules of the Oil Conservation Division have been complied with and that the information given above is true and complete to the best of my knowledge and belief. Signature: <i>Kristina Agee</i>			OIL CONSERVATION DIVISION Approved by: Title: Approval Date:		
Printed name: Kristina Agee					
Title: REGULATORY SPECIALIST					
E-mail Address: kristina_agee@eogresources.com					
Date: 4/10/2024		Phone: 432-686-6996			

DISTRICT I
1625 N. French Dr., Hobbs, NM 88240
Phone: (575) 393-6161 Fax: (575) 393-0720

DISTRICT II
811 S. First St., Artesia, NM 88210
Phone: (575) 748-1283 Fax: (575) 748-9720

DISTRICT III
1000 Rio Brazos Rd., Aztec, NM 87410
Phone: (505) 334-6178 Fax: (505) 334-6170

DISTRICT IV
1220 S. St. Francis Dr., Santa Fe, NM 87505
Phone: (505) 476-3460 Fax: (505) 476-3462

State of New Mexico
Energy, Minerals & Natural Resources Department
OIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, New Mexico 87505

As-Completed Plat
Revised August 1, 2011
Submit one copy to appropriate
District Office
☐ AMENDED REPORT

AS-COMPLETED PLAT

API Number 30-015-48315	Pool Code 98220	Pool Name Purple Sage; Wolfcamp
Property Code 322721	Property Name GOLDEN GRAHAM 1 STATE COM	Well Number 723H
OGRID No. 7377	Operator Name EOG RESOURCES, INC.	Elevation 2933'


Surface Location

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
N	1	26 S	28 E		215	SOUTH	1799	WEST	EDDY

Bottom Hole Location If Different From Surface

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
C	36	25 S	28 E		341	NORTH	1792	WEST	EDDY
Dedicated Acres 640.00	Joint or Infill	Consolidated Code	Order No.						

No allowable will be assigned to this completion until all interests have been consolidated or a non-standard unit has been approved by the division.

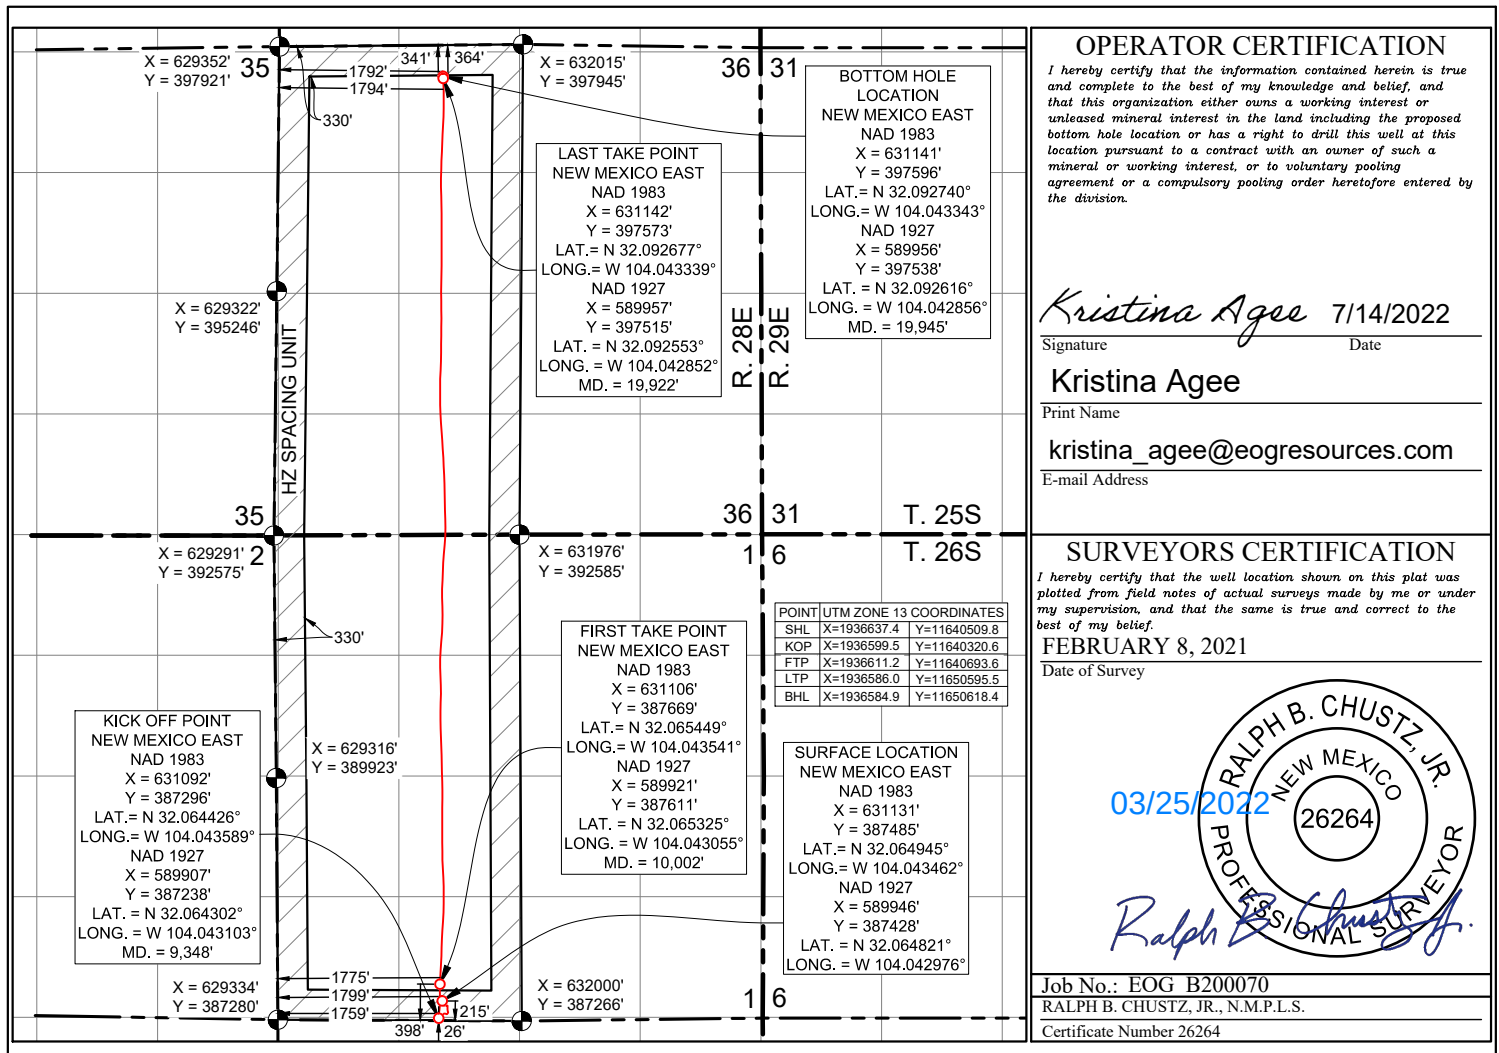




Eddy County, NM (NAD 83 NME)

Golden Graham 1 State Com #723H

H&P 249

OH

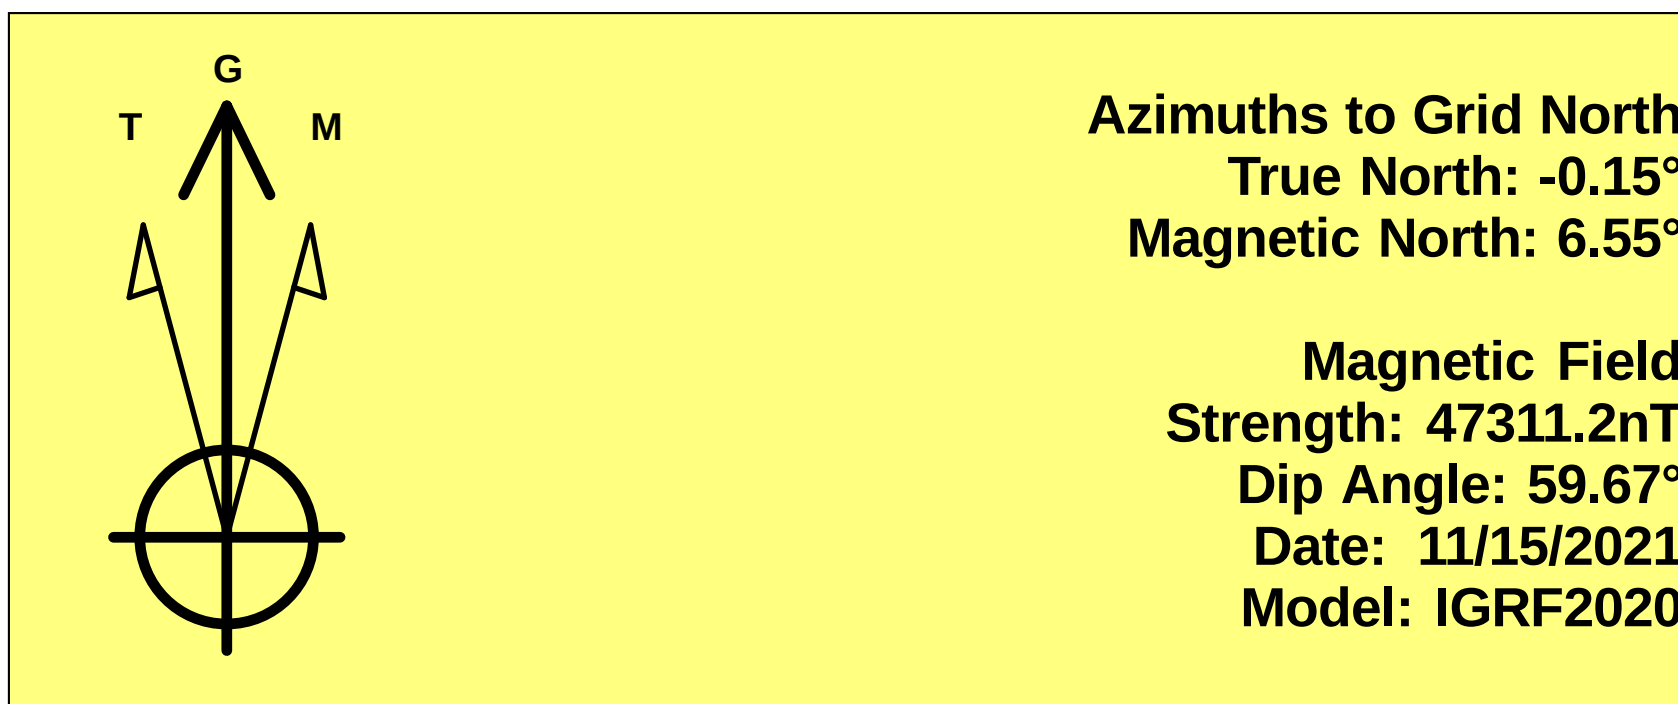

To convert a Magnetic Direction to a Grid Direction, Add 6.55°
To convert a Magnetic Direction to a True Direction, Add 6.70° East
To convert a True Direction to a Grid Direction, Subtract 0.15°










PROJECT DETAILS: Eddy County, NM (NAD 83 NME)

Geodetic System: US State Plane 1983
Datum: North American Datum 1983
Ellipsoid: GRS 1980
Zone: New Mexico Eastern Zone
System Datum: Mean Sea Level

WELL DETAILS: #723H

KB = 25' @ 2958.0usft (H&P 249) 2933.0

Northings	Easting	Latitude	Longitude
387485.00	631131.00	32° 3' 53.800 N	104° 2' 36.462 W

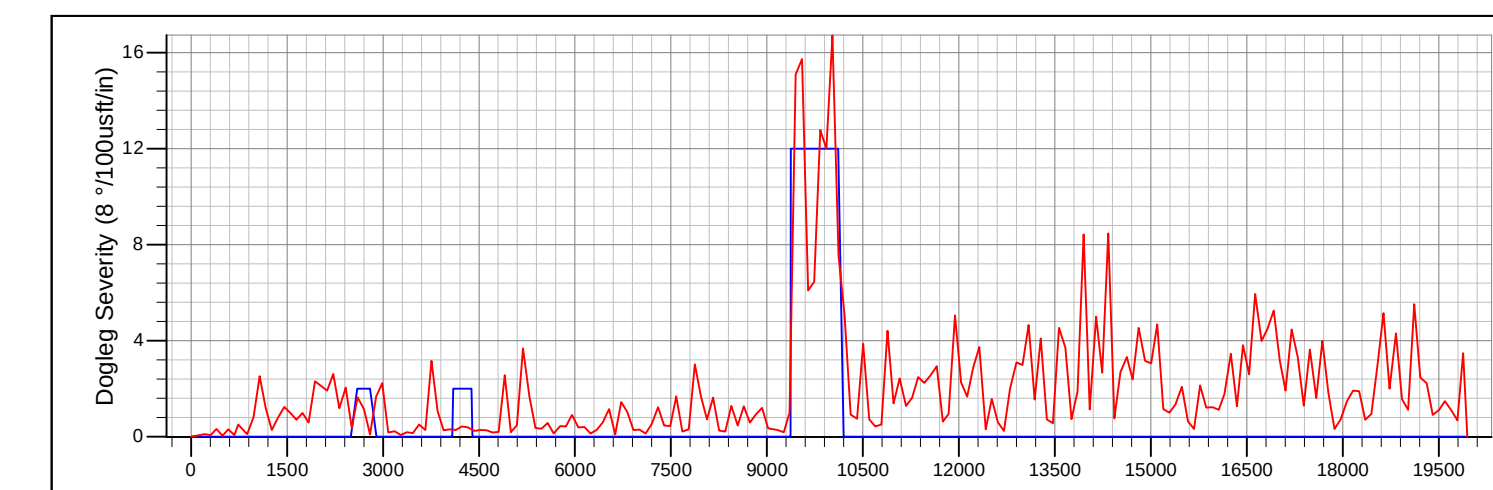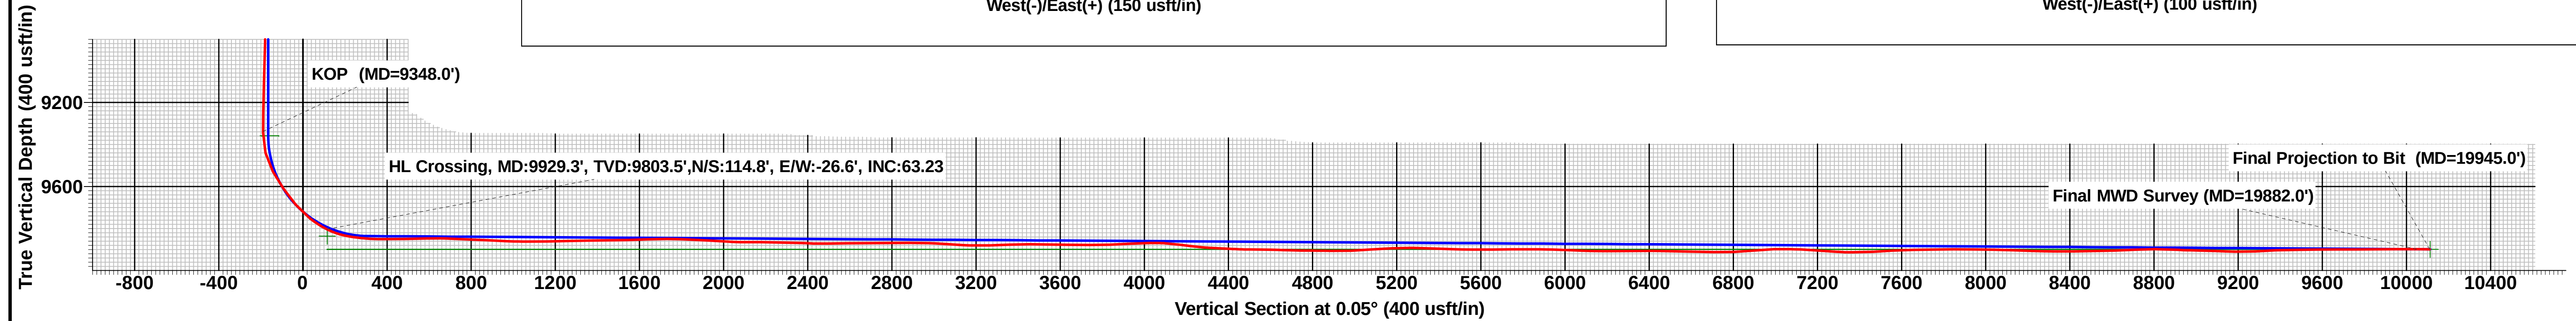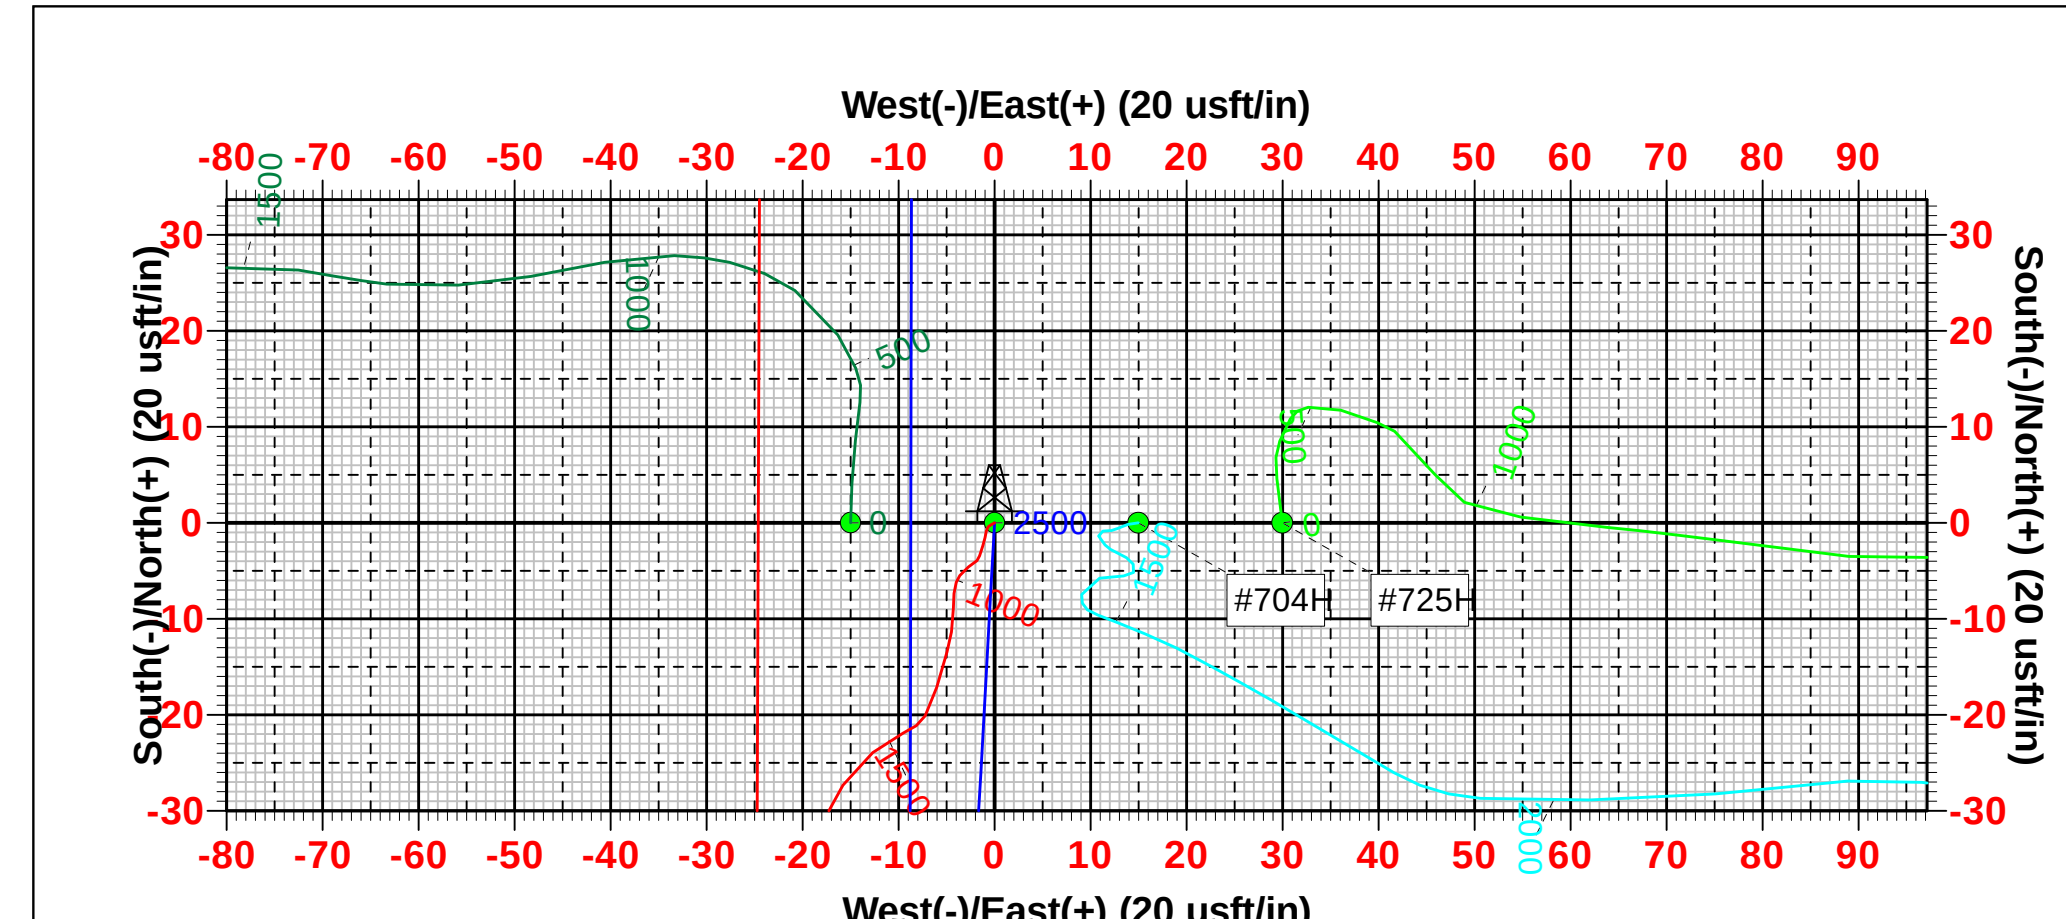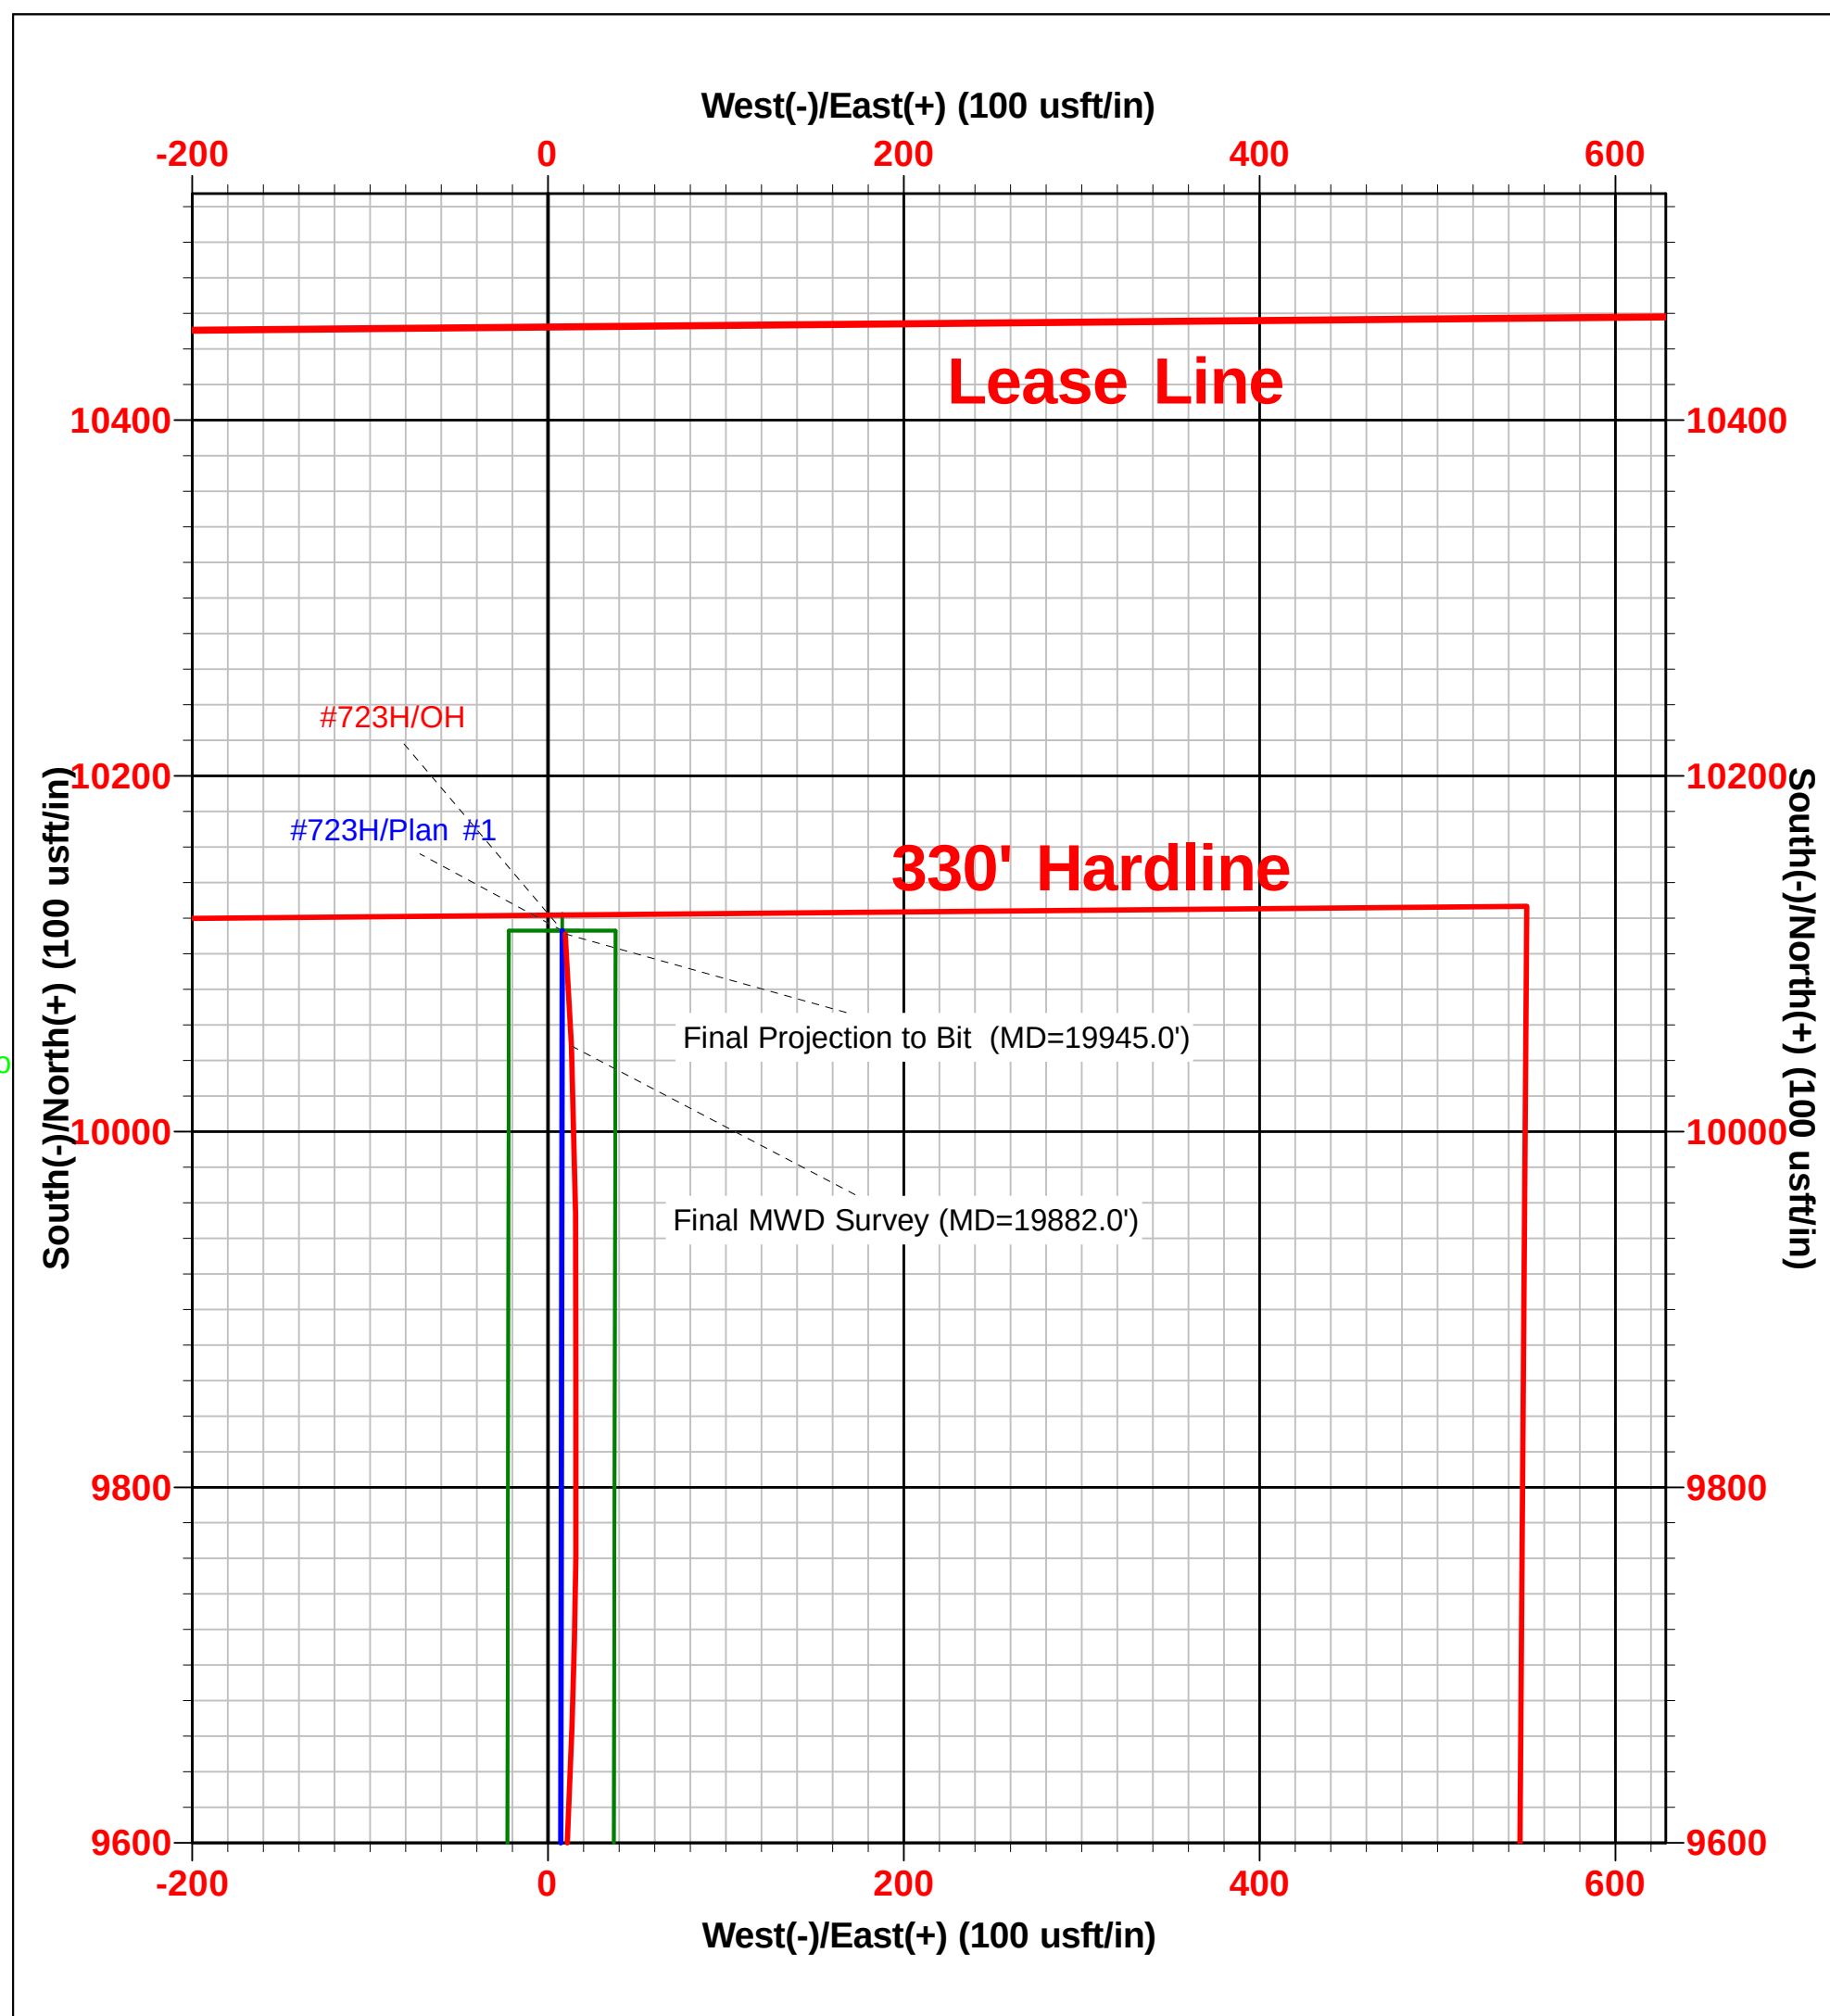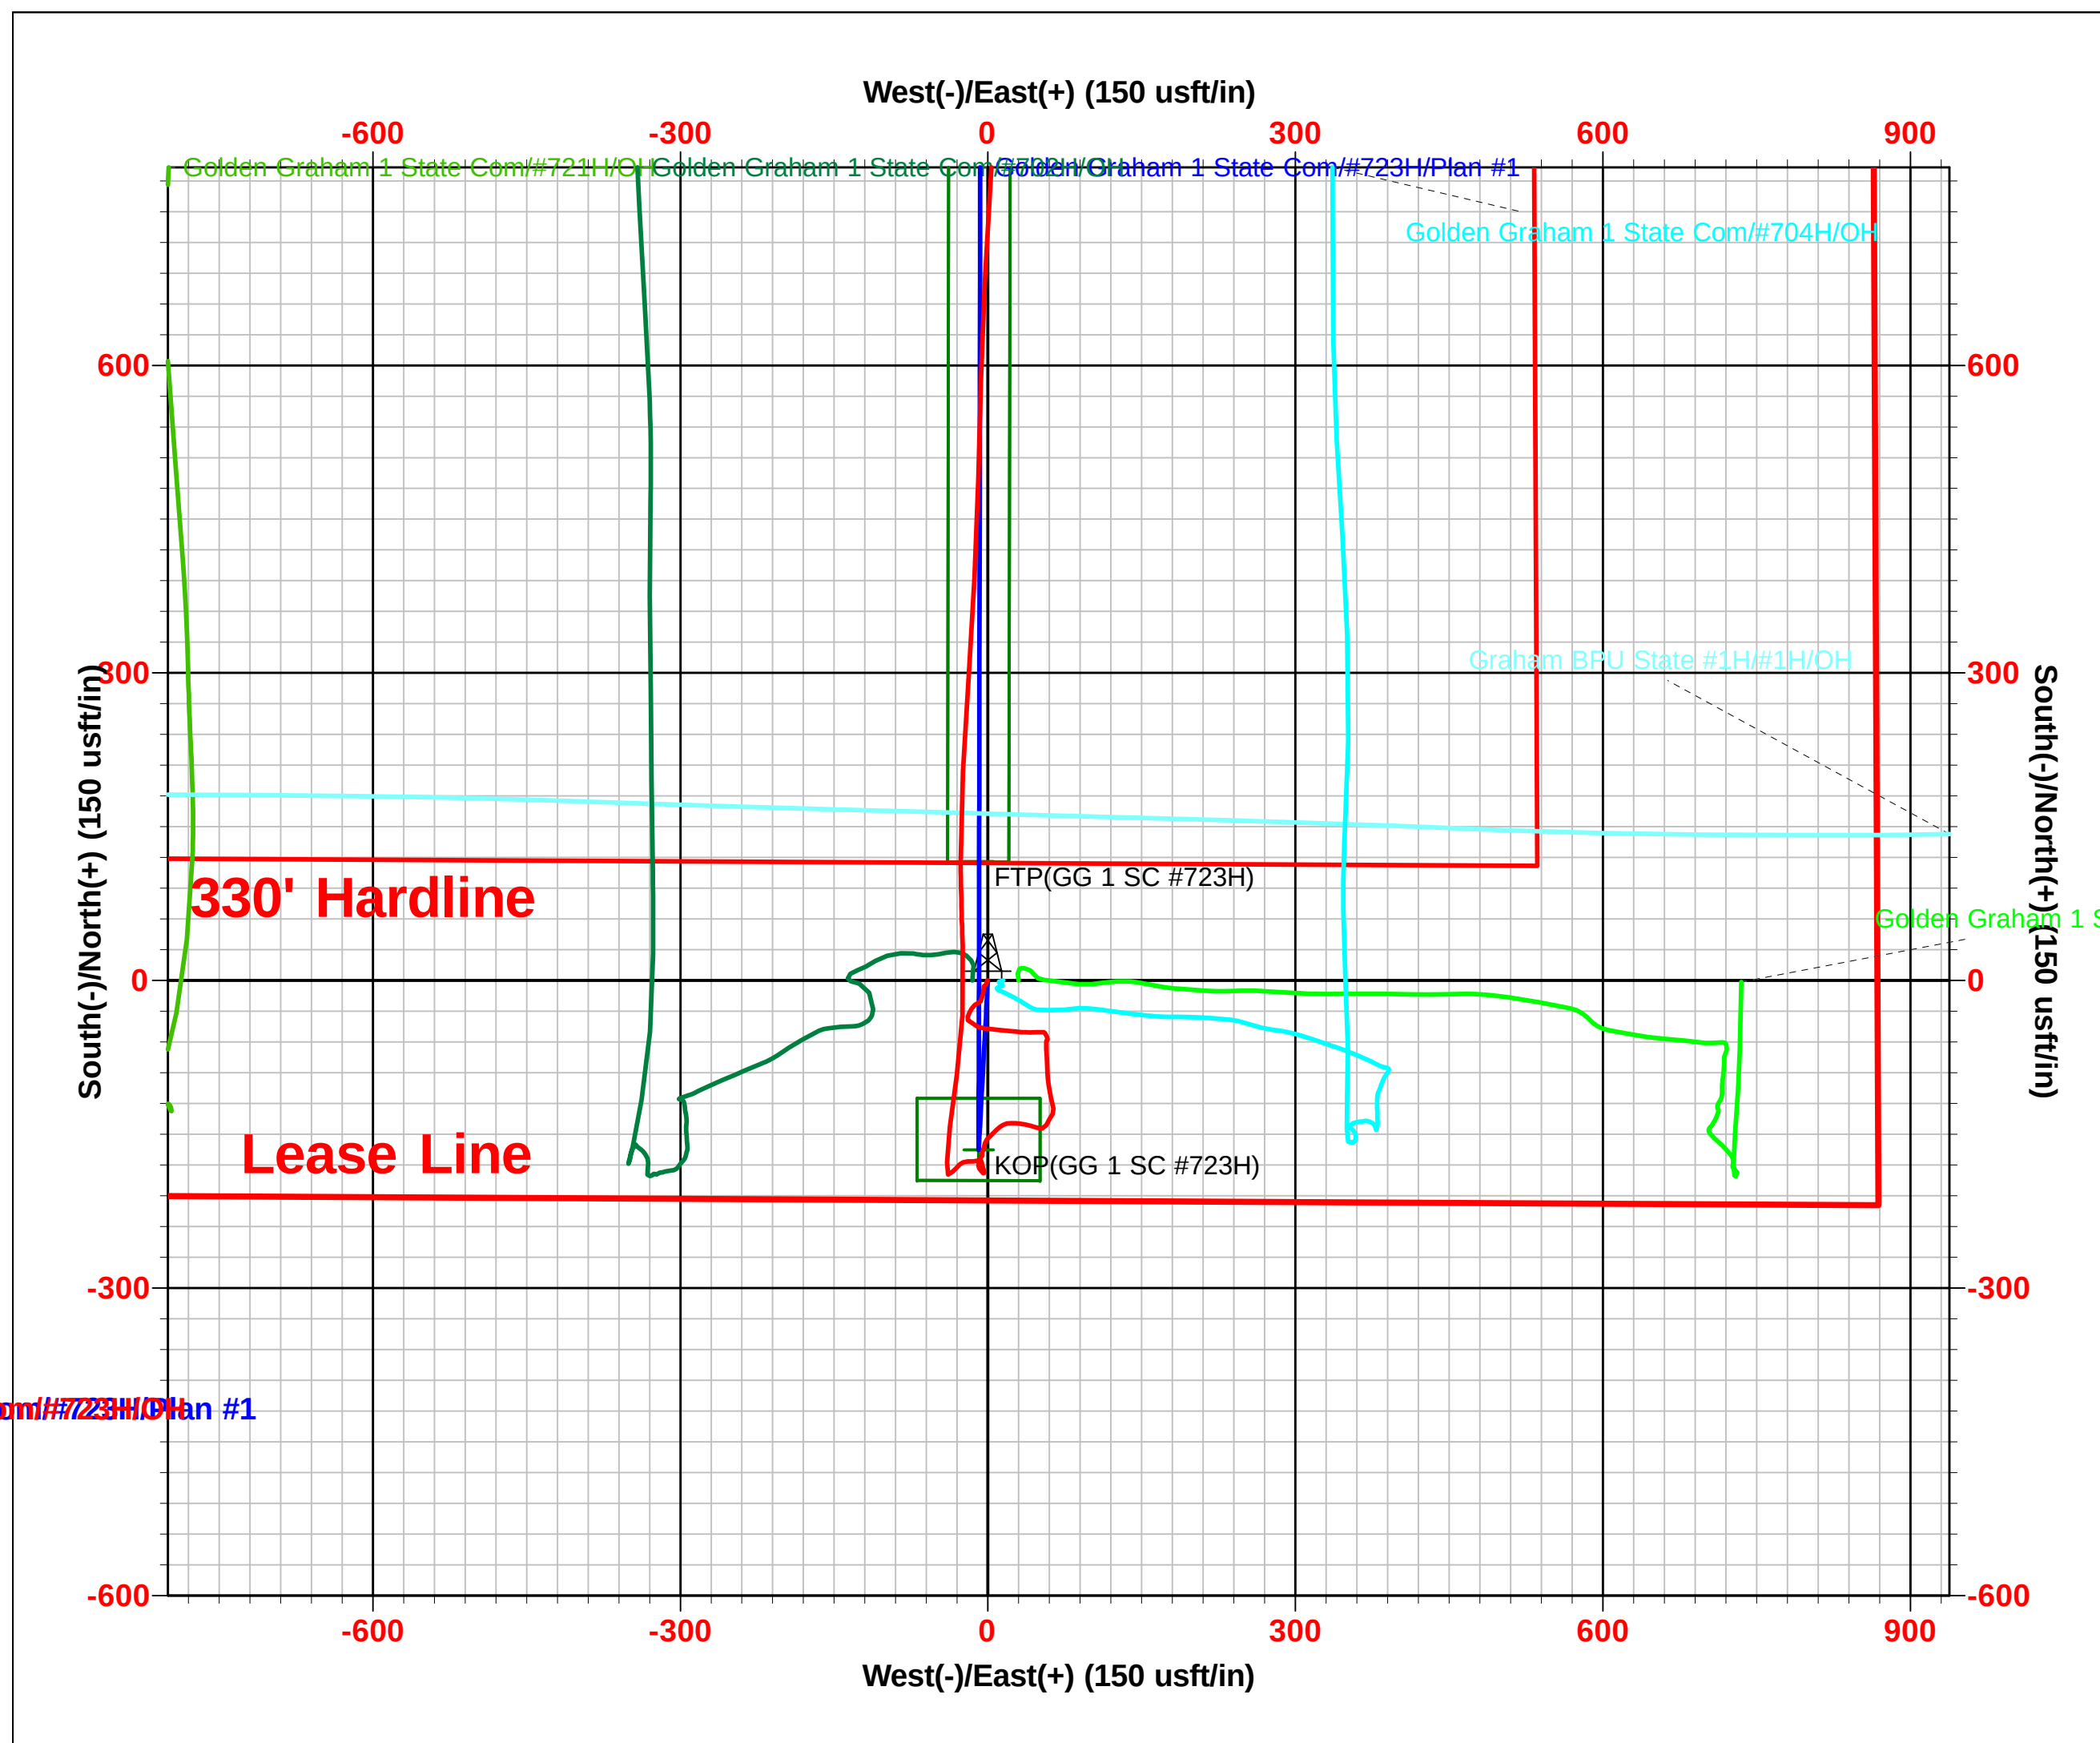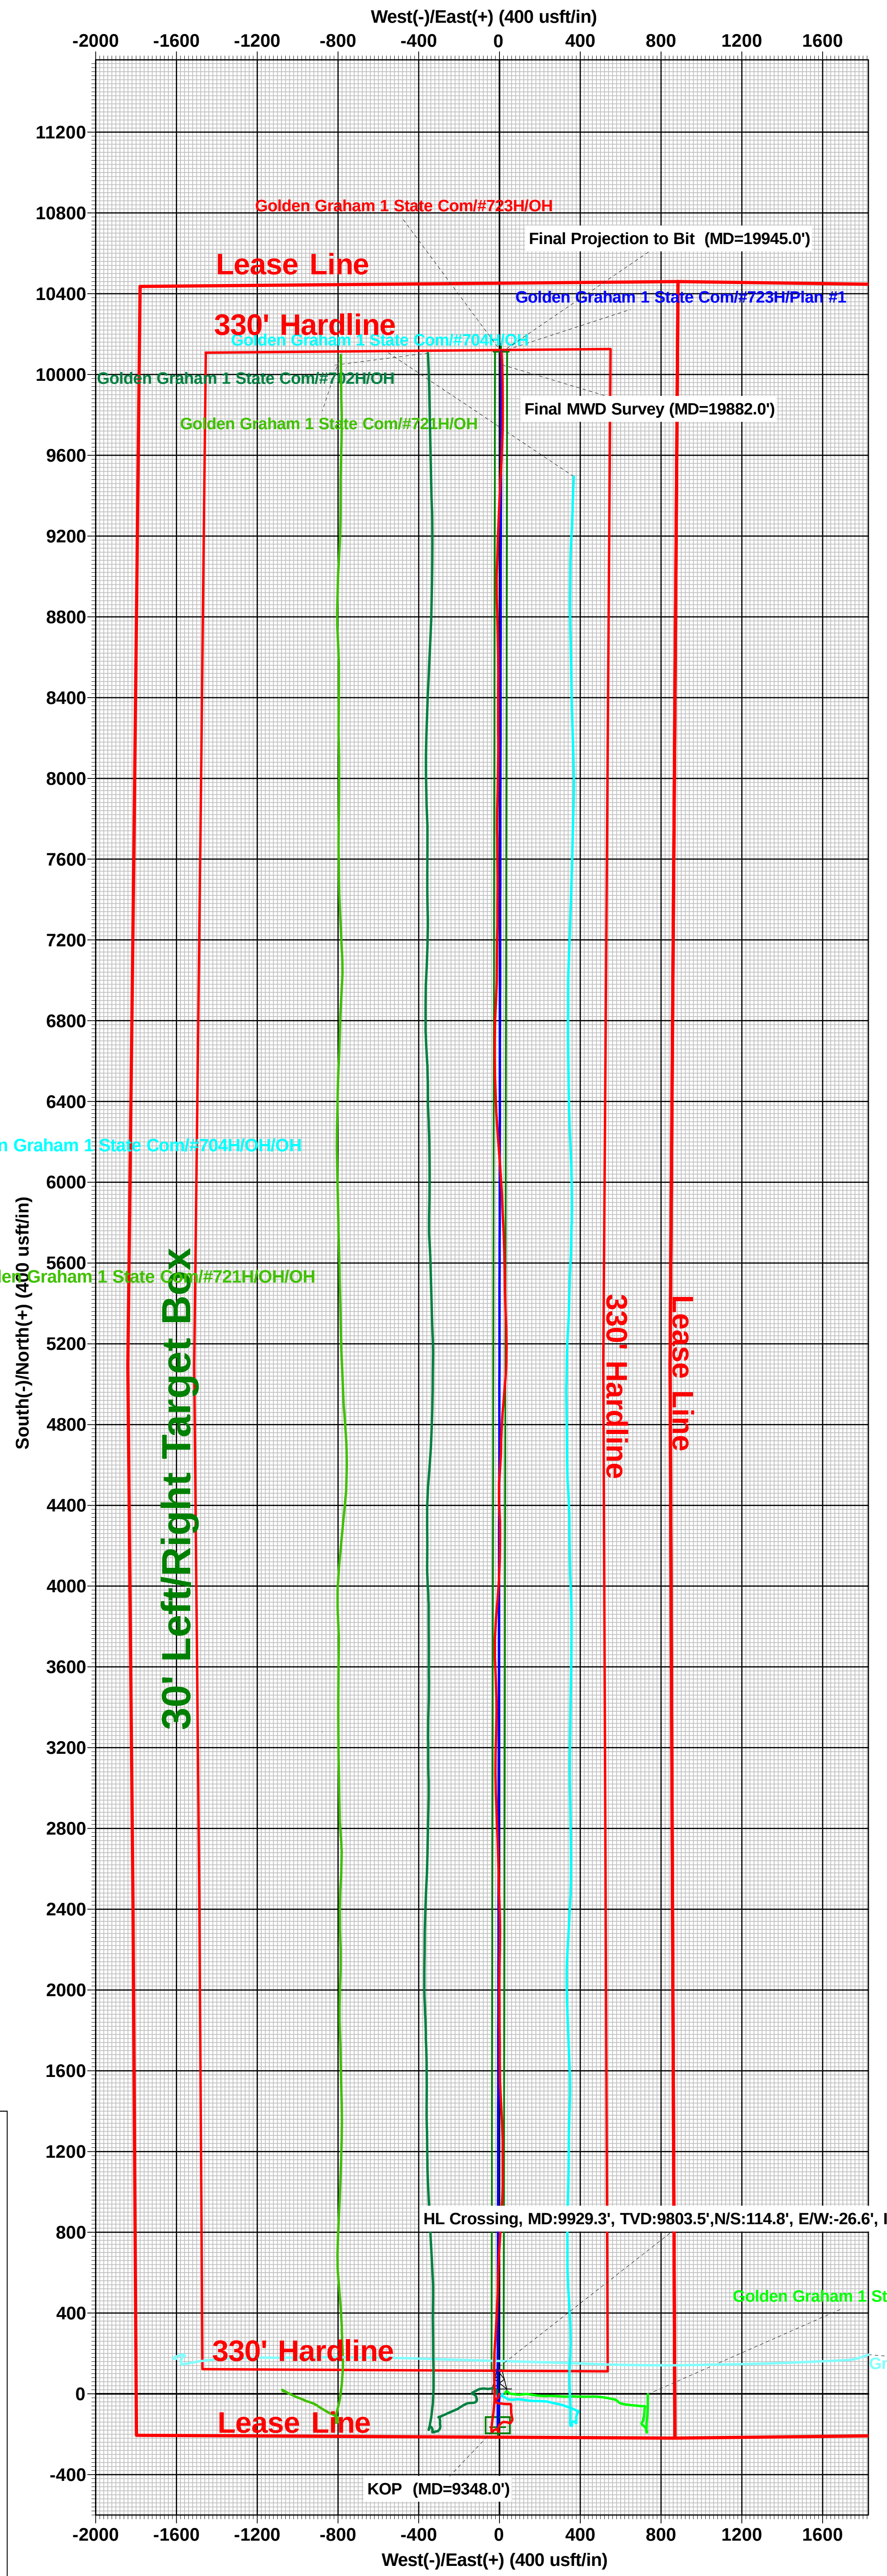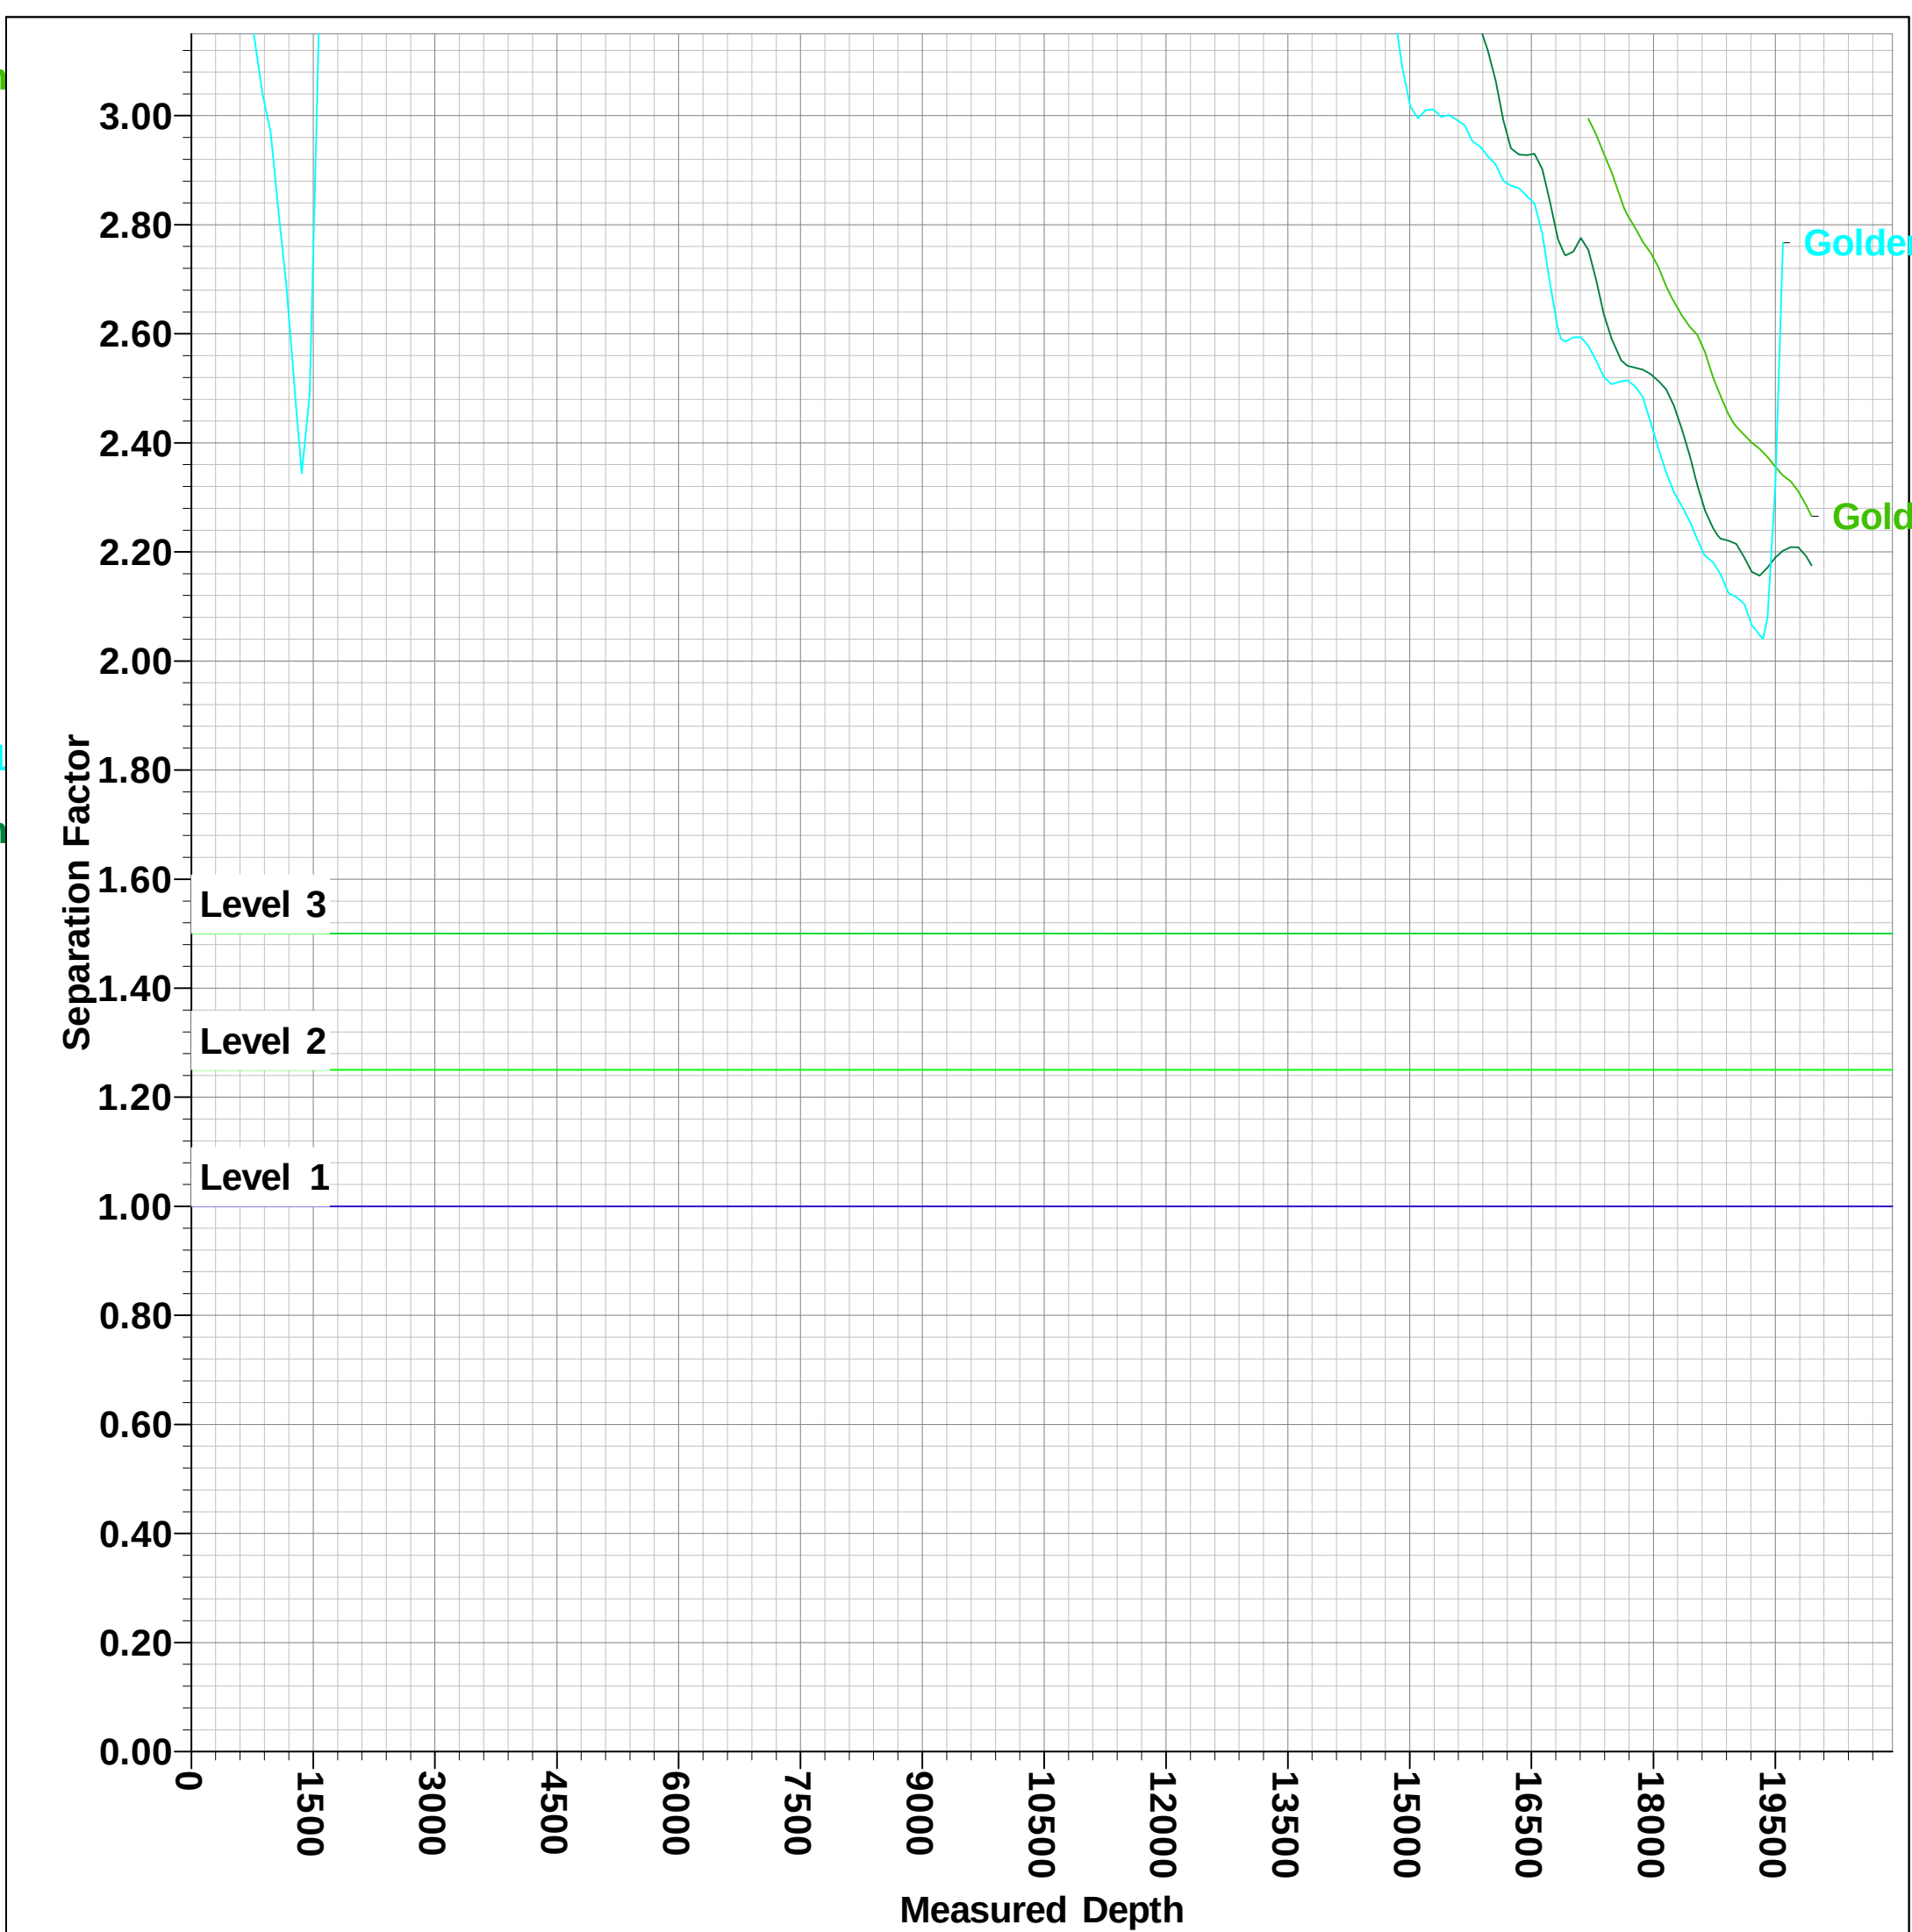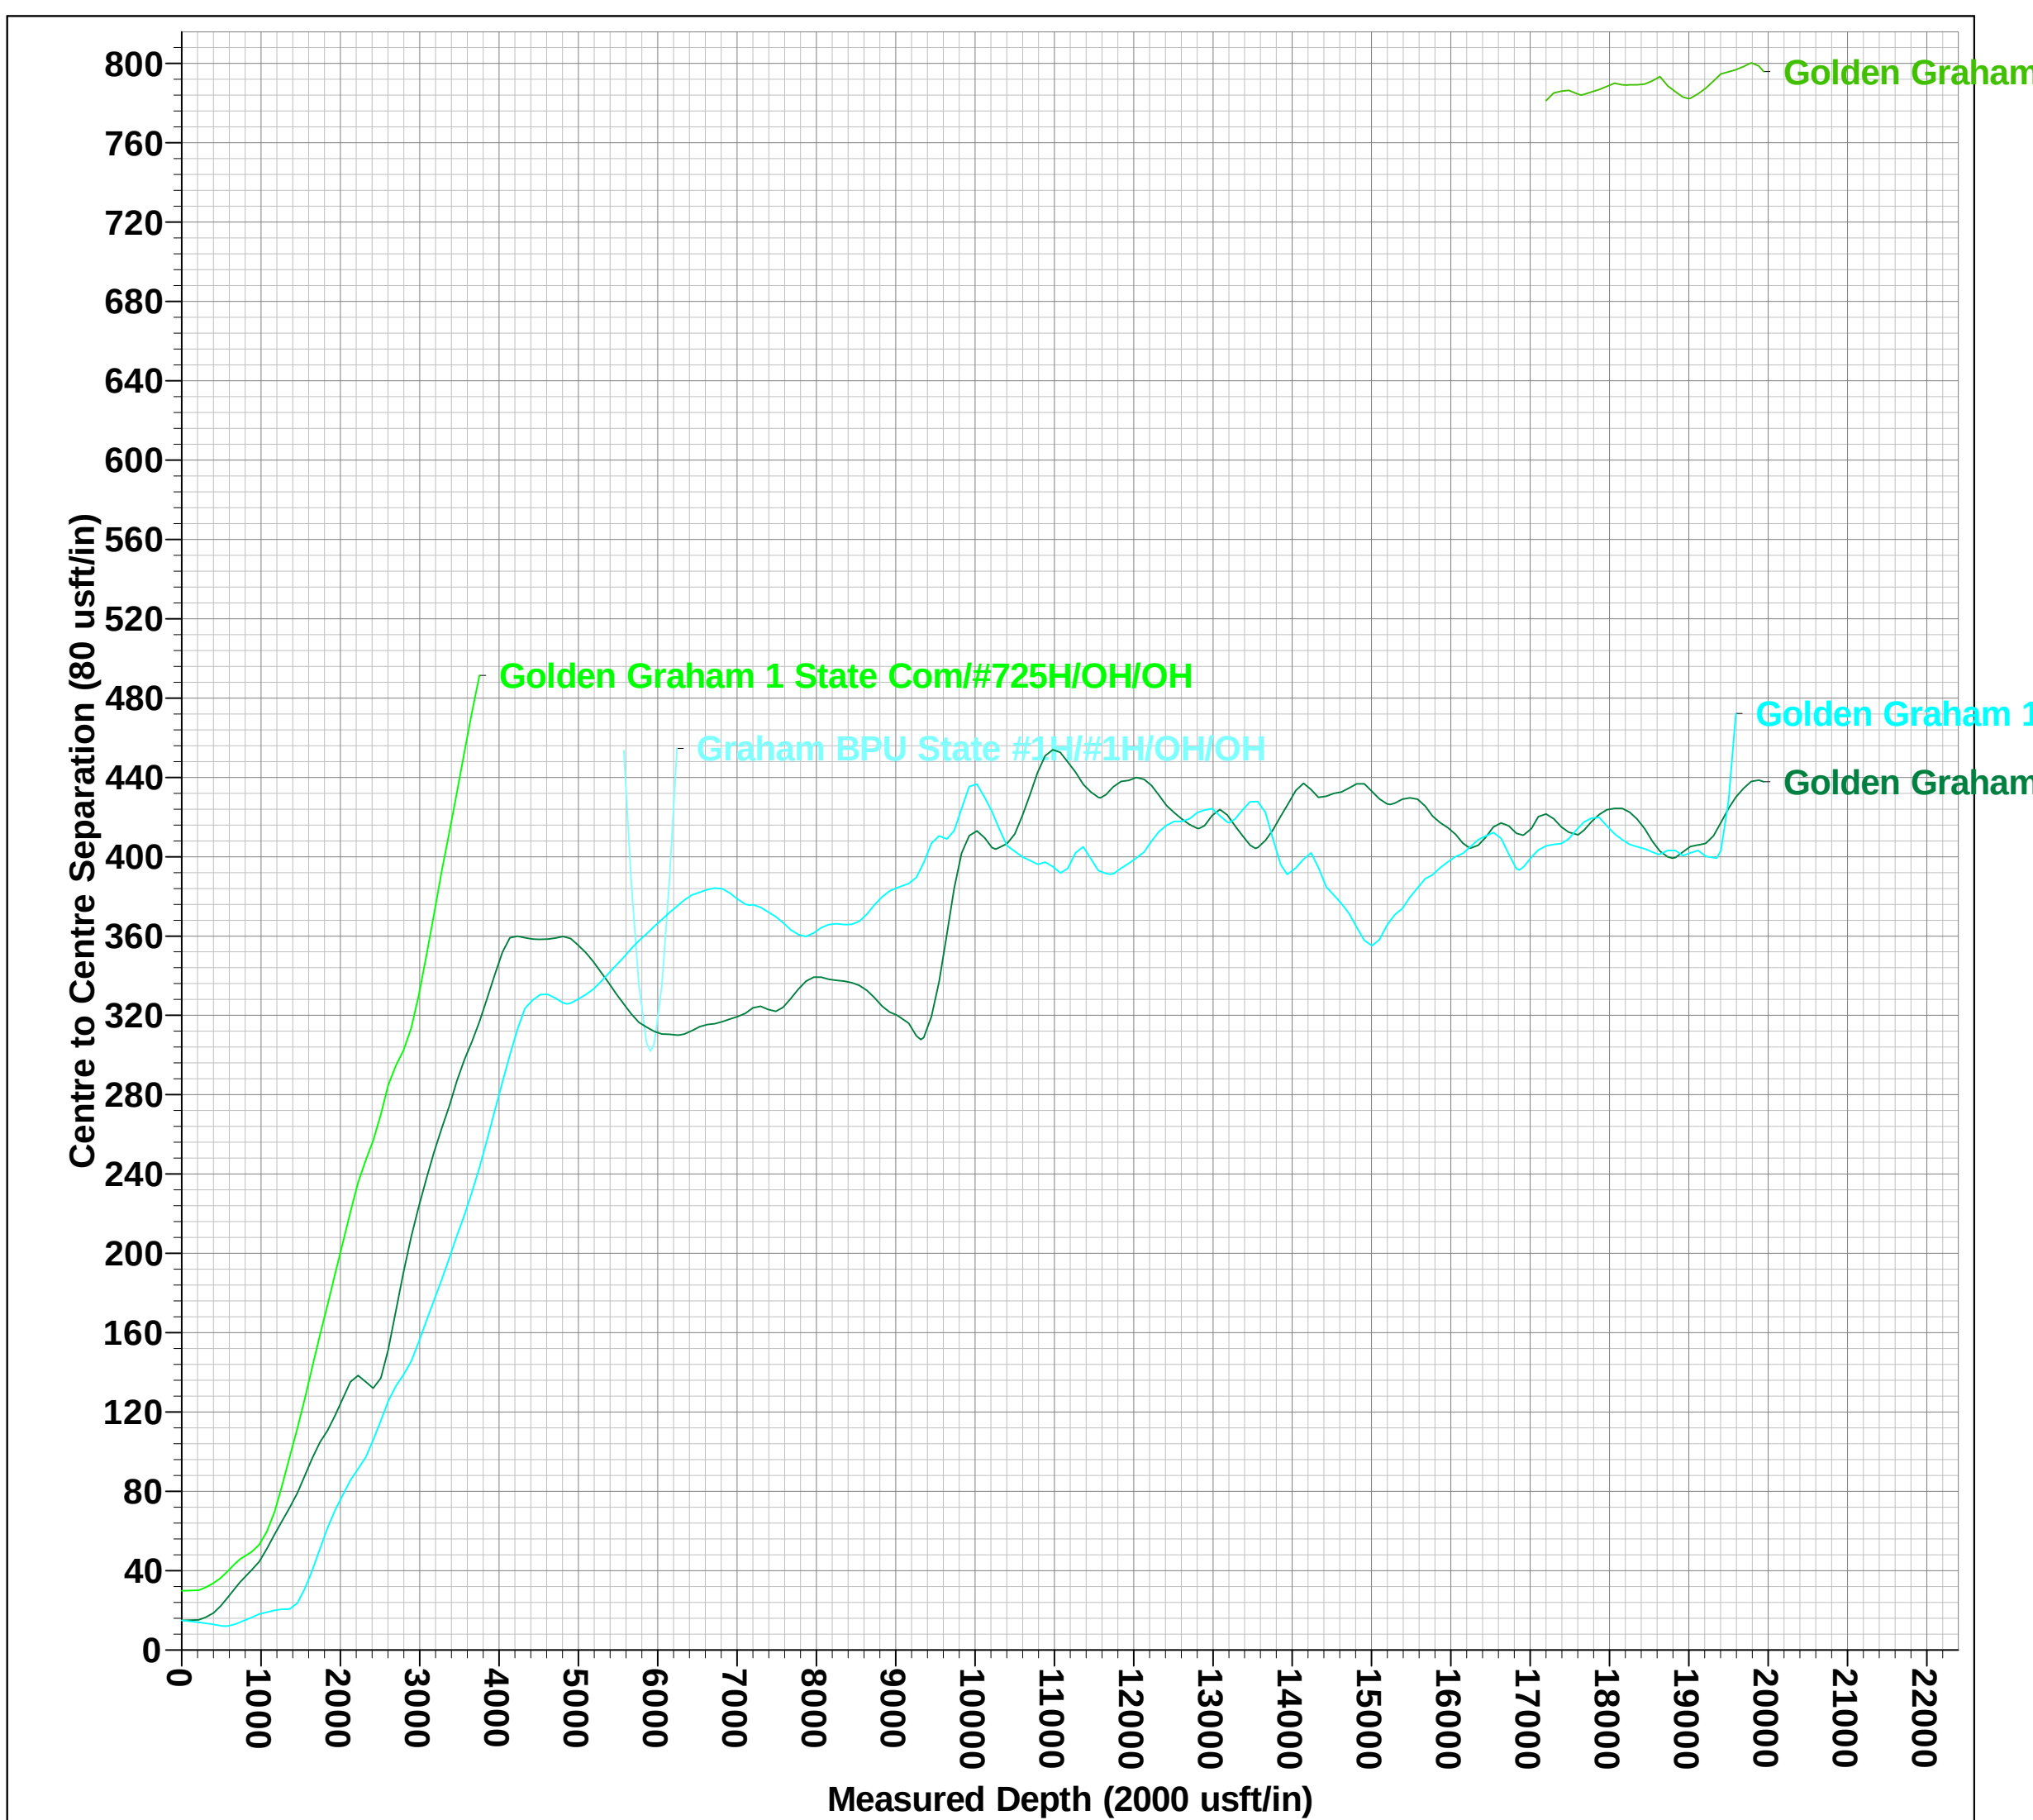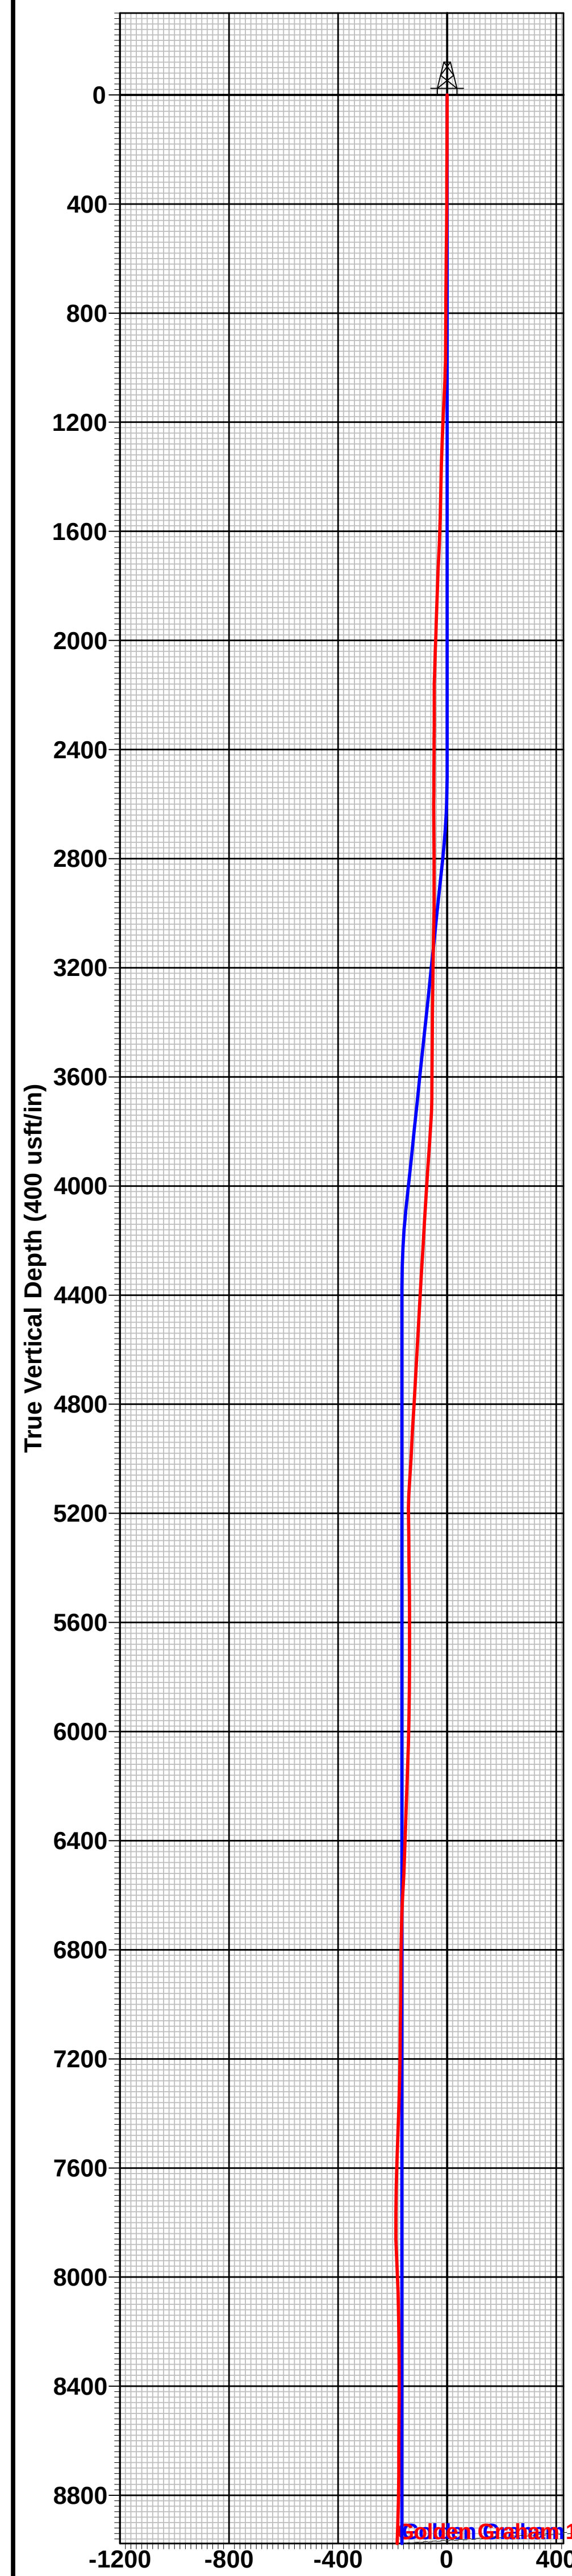



Midland

Eddy County, NM (NAD 83 NME)
Golden Graham 1 State Com
#723H
OH

Design: OH

Final PVA

03 January, 2022



Final PVA

Company:	Midland	Local Co-ordinate Reference:	Well #723H
Project:	Eddy County, NM (NAD 83 NME)	TVD Reference:	KB = 25' @ 2958.0usft (H&P 249)
Site:	Golden Graham 1 State Com	MD Reference:	KB = 25' @ 2958.0usft (H&P 249)
Well:	#723H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Project		Eddy County, NM (NAD 83 NME)	
Map System:	US State Plane 1983	System Datum:	Mean Sea Level
Geo Datum:	North American Datum 1983		
Map Zone:	New Mexico Eastern Zone		

Site		Golden Graham 1 State Com			
Site Position:		Northing:		387,494.00 usft	
From:	Map	Easting:		630,031.00 usft	
Position Uncertainty:		Slot Radius:		13-3/16 "	
				Latitude: 32° 3' 53.919 N	
				Longitude: 104° 2' 49.246 W	
				Grid Convergence: 0.15 °	

Well		#723H				
Well Position	+N/-S	0.0 usft	Northing:	387,485.00 usft	Latitude:	32° 3' 53.800 N
	+E/-W	0.0 usft	Easting:	631,131.00 usft	Longitude:	104° 2' 36.462 W
Position Uncertainty		0.0 usft	Wellhead Elevation:	usft	Ground Level:	2,933.0 usft

Wellbore	OH				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	IGRF2020	11/15/2021	6.70	59.67	47,311.15474245

Design		OH			
Audit Notes:					
Version:	1.0	Phase:	ACTUAL	Tie On Depth:	0.0
Vertical Section:	Depth From (TVD) (usft)		+N/-S (usft)	+E/-W (usft)	Direction (°)
	0.0		0.0	0.0	0.05

Survey Program		Date	1/3/2022		
From (usft)	To (usft)	Survey (Wellbore)	Tool Name	Description	
213.0	19,945.0	Gordon MWD #1 (OH)	EOG MWD+IFR1	MWD + IFR1	



Final PVA

Company:	Midland	Local Co-ordinate Reference:	Well #723H
Project:	Eddy County, NM (NAD 83 NME)	TVD Reference:	KB = 25' @ 2958.0usft (H&P 249)
Site:	Golden Graham 1 State Com	MD Reference:	KB = 25' @ 2958.0usft (H&P 249)
Well:	#723H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Survey										
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.00	0.0	0.0
213.0	0.22	242.54	213.0	-0.2	-0.4	0.10	0.10	0.00	-0.4	0.0
305.0	0.22	227.92	305.0	-0.4	-0.7	0.06	0.00	-15.89	-0.7	-0.1
398.0	0.43	189.95	398.0	-0.9	-0.8	0.31	0.23	-40.83	-1.0	-0.7
491.0	0.42	195.00	491.0	-1.5	-1.0	0.04	-0.01	5.43	-1.7	-0.6
584.0	0.70	196.33	584.0	-2.4	-1.2	0.30	0.30	1.43	-2.7	-0.5
676.0	0.64	197.40	676.0	-3.4	-1.6	0.07	-0.07	1.16	-3.7	-0.5
736.0	0.47	223.95	736.0	-3.9	-1.8	0.51	-0.28	44.25	-4.1	1.4
881.0	0.42	241.65	881.0	-4.6	-2.7	0.10	-0.03	12.21	-4.6	2.8
977.0	1.15	220.25	977.0	-5.5	-3.6	0.81	0.76	-22.29	-6.6	0.8
1,073.0	3.19	180.86	1,072.9	-8.9	-4.3	2.51	2.12	-41.03	-9.0	-4.2
1,168.0	2.42	197.73	1,167.8	-13.5	-4.9	1.18	-0.81	17.76	-14.3	-0.6
1,264.0	2.17	195.08	1,263.7	-17.2	-6.0	0.28	-0.26	-2.76	-18.1	-1.4
1,360.0	1.66	211.60	1,359.7	-20.1	-7.2	0.78	-0.53	17.21	-20.9	4.4
1,456.0	2.01	247.67	1,455.6	-21.9	-9.5	1.23	0.36	37.57	-17.1	16.7
1,551.0	2.59	229.09	1,550.5	-24.0	-12.7	0.99	0.61	-19.56	-25.3	9.8
1,647.0	2.94	217.08	1,646.4	-27.3	-15.8	0.70	0.36	-12.51	-31.3	3.9
1,743.0	2.73	198.52	1,742.3	-31.5	-18.0	0.98	-0.22	-19.33	-35.6	-7.1
1,839.0	2.34	207.36	1,838.2	-35.4	-19.7	0.57	-0.41	9.21	-40.5	-1.2
1,935.0	2.17	148.98	1,934.1	-38.7	-19.6	2.30	-0.18	-60.81	-23.0	-36.7
2,127.0	5.23	113.10	2,125.7	-45.2	-9.7	1.93	1.59	-18.69	-8.8	-45.4
2,223.0	3.41	89.54	2,221.5	-46.9	-2.8	2.61	-1.90	-24.54	3.2	-46.9
2,318.0	4.39	97.51	2,316.3	-47.4	3.6	1.18	1.03	8.39	-9.8	-46.5
2,414.0	6.33	95.37	2,411.8	-48.4	12.5	2.03	2.02	-2.23	-16.9	-47.0
2,510.0	6.66	96.23	2,507.2	-49.5	23.3	0.36	0.34	0.90	-28.4	-46.7
2,605.0	5.13	93.70	2,601.7	-50.3	33.1	1.63	-1.61	-2.66	-36.2	-46.2
2,701.0	4.09	89.30	2,697.4	-50.6	40.8	1.14	-1.08	-4.58	-40.7	-44.1



Final PVA

Company:	Midland	Local Co-ordinate Reference:	Well #723H
Project:	Eddy County, NM (NAD 83 NME)	TVD Reference:	KB = 25' @ 2958.0usft (H&P 249)
Site:	Golden Graham 1 State Com	MD Reference:	KB = 25' @ 2958.0usft (H&P 249)
Well:	#723H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Survey											
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)	
2,797.0	4.05	88.24	2,793.2	-50.4	47.6	0.09	-0.04	-1.10	-47.4	-36.5	
2,893.0	2.45	89.11	2,889.0	-50.3	53.0	1.67	-1.67	0.91	-54.0	-25.8	
2,989.0	1.17	149.96	2,985.0	-51.1	55.6	2.23	-1.33	63.39	-42.5	41.8	
3,085.0	1.01	149.96	3,080.9	-52.7	56.5	0.17	-0.17	0.00	-35.9	47.3	
3,180.0	0.81	153.85	3,175.9	-54.0	57.2	0.22	-0.21	4.09	-25.5	54.5	
3,276.0	0.80	158.14	3,271.9	-55.2	57.7	0.06	-0.01	4.47	-13.7	60.6	
3,372.0	0.73	169.75	3,367.9	-56.5	58.1	0.18	-0.07	12.09	7.3	64.5	
3,468.0	0.60	174.38	3,463.9	-57.6	58.2	0.15	-0.14	4.82	21.2	65.3	
3,563.0	0.39	227.80	3,558.9	-58.3	58.1	0.51	-0.22	56.23	71.6	15.4	
3,659.0	0.52	257.99	3,654.9	-58.6	57.4	0.28	0.14	31.45	71.5	-32.2	
3,755.0	3.12	182.20	3,750.8	-61.3	56.9	3.16	2.71	-78.95	56.2	61.1	
3,851.0	4.04	175.40	3,846.7	-67.3	57.0	1.05	0.96	-7.08	52.6	68.3	
3,946.0	3.84	177.42	3,941.4	-73.8	57.4	0.26	-0.21	2.13	58.4	67.5	
4,042.0	3.55	176.92	4,037.2	-80.0	57.8	0.30	-0.30	-0.52	61.6	69.1	
4,138.0	3.33	179.31	4,133.1	-85.7	57.9	0.27	-0.23	2.49	68.2	67.2	
4,233.0	3.69	176.58	4,227.9	-91.5	58.2	0.42	0.38	-2.87	65.6	71.0	
4,329.0	3.35	174.35	4,323.7	-97.4	58.6	0.38	-0.35	-2.32	60.2	73.9	
4,425.0	3.39	170.66	4,419.5	-103.0	59.4	0.23	0.04	-3.84	50.0	77.6	
4,521.0	3.23	166.93	4,515.4	-108.4	60.4	0.28	-0.17	-3.89	39.4	80.4	
4,617.0	3.44	169.15	4,611.2	-113.9	61.6	0.26	0.22	2.31	36.9	79.0	
4,712.0	3.41	166.45	4,706.0	-119.4	62.8	0.17	-0.03	-2.84	27.4	80.5	
4,808.0	3.24	168.04	4,801.9	-124.9	64.0	0.20	-0.18	1.66	24.1	79.8	
4,903.0	3.57	209.47	4,896.7	-130.1	63.1	2.56	0.35	43.61	65.8	45.7	
4,999.0	3.72	210.64	4,992.5	-135.3	60.1	0.17	0.16	1.22	60.7	44.4	
5,094.0	4.12	207.41	5,087.3	-141.0	56.9	0.48	0.42	-3.40	51.6	47.5	
5,190.0	2.94	264.60	5,183.2	-144.3	52.9	3.68	-1.23	59.57	63.5	-14.8	
5,286.0	3.70	289.45	5,279.0	-143.5	47.5	1.68	0.79	25.89	46.1	-39.1	



Final PVA

Company:	Midland	Local Co-ordinate Reference:	Well #723H
Project:	Eddy County, NM (NAD 83 NME)	TVD Reference:	KB = 25' @ 2958.0usft (H&P 249)
Site:	Golden Graham 1 State Com	MD Reference:	KB = 25' @ 2958.0usft (H&P 249)
Well:	#723H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Survey										
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
5,382.0	3.45	285.59	5,374.8	-141.7	41.8	0.36	-0.26	-4.02	42.6	-36.1
5,477.0	3.17	283.31	5,469.7	-140.3	36.5	0.33	-0.29	-2.40	38.6	-34.5
5,573.0	2.85	274.82	5,565.5	-139.5	31.5	0.57	-0.33	-8.84	38.2	-28.8
5,669.0	2.77	272.88	5,661.4	-139.2	26.8	0.13	-0.08	-2.02	34.5	-27.6
5,765.0	2.39	268.75	5,757.3	-139.1	22.5	0.44	-0.40	-4.30	32.1	-25.2
5,860.0	2.07	262.68	5,852.2	-139.4	18.8	0.42	-0.34	-6.39	30.9	-21.9
5,956.0	2.42	242.11	5,948.2	-140.6	15.3	0.91	0.36	-21.43	32.9	-10.2
6,052.0	2.50	233.63	6,044.1	-142.8	11.8	0.39	0.08	-8.83	30.0	-5.6
6,148.0	2.69	226.47	6,140.0	-145.6	8.5	0.39	0.20	-7.46	26.1	-2.0
6,244.0	2.60	224.67	6,235.9	-148.7	5.4	0.13	-0.09	-1.87	21.7	-1.3
6,339.0	2.84	226.57	6,330.8	-151.8	2.1	0.27	0.25	2.00	17.2	-1.9
6,435.0	2.41	218.91	6,426.7	-155.0	-0.9	0.58	-0.45	-7.98	12.9	0.1
6,530.0	2.88	197.36	6,521.6	-158.8	-2.8	1.15	0.49	-22.68	7.7	4.1
6,626.0	2.94	196.07	6,617.4	-163.5	-4.2	0.09	0.06	-1.34	2.7	4.2
6,722.0	1.56	195.08	6,713.4	-167.1	-5.2	1.44	-1.44	-1.03	-1.1	4.2
6,818.0	0.58	187.62	6,809.4	-168.9	-5.7	1.03	-1.02	-7.77	-3.4	3.8
6,914.0	0.48	160.02	6,905.3	-169.7	-5.6	0.28	-0.10	-28.75	-5.6	1.6
7,009.0	0.53	191.55	7,000.3	-170.5	-5.5	0.29	0.05	33.19	-4.7	4.5
7,105.0	0.57	203.60	7,096.3	-171.4	-5.8	0.13	0.04	12.55	-4.6	5.5
7,201.0	0.83	240.05	7,192.3	-172.2	-6.6	0.52	0.27	37.97	-1.5	7.4
7,296.0	1.70	202.09	7,287.3	-173.9	-7.7	1.22	0.92	-39.96	-7.7	4.5
7,392.0	2.05	193.48	7,383.3	-176.8	-8.7	0.47	0.36	-8.97	-11.4	3.1
7,488.0	2.31	184.98	7,479.2	-180.4	-9.2	0.43	0.27	-8.85	-15.4	1.1
7,583.0	1.90	141.82	7,574.1	-183.6	-8.4	1.68	-0.43	-45.43	-15.0	-11.0
7,679.0	1.80	136.43	7,670.1	-185.9	-6.4	0.21	-0.10	-5.61	-16.9	-12.5
7,775.0	1.52	137.88	7,766.0	-188.0	-4.5	0.29	-0.29	1.51	-20.0	-12.1
7,871.0	1.63	5.19	7,862.0	-187.5	-3.5	3.01	0.11	-138.22	22.0	-7.5



Final PVA

Company:	Midland	Local Co-ordinate Reference:	Well #723H
Project:	Eddy County, NM (NAD 83 NME)	TVD Reference:	KB = 25' @ 2958.0usft (H&P 249)
Site:	Golden Graham 1 State Com	MD Reference:	KB = 25' @ 2958.0usft (H&P 249)
Well:	#723H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Survey											
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)	
7,967.0	2.91	339.30	7,957.9	-183.9	-4.3	1.68	1.33	-26.97	19.4		2.3
8,063.0	2.27	345.06	8,053.9	-179.8	-5.6	0.72	-0.67	6.00	15.2		0.6
8,158.0	0.75	354.80	8,148.8	-177.4	-6.2	1.62	-1.60	10.25	12.6		-1.7
8,254.0	0.60	338.76	8,244.8	-176.3	-6.4	0.25	-0.16	-16.71	11.4		1.7
8,350.0	0.56	319.17	8,340.8	-175.4	-6.9	0.21	-0.04	-20.41	9.3		5.2
8,446.0	1.39	257.58	8,436.8	-175.3	-8.3	1.28	0.86	-64.16	-1.6		10.2
8,543.0	1.83	253.64	8,533.8	-176.0	-11.0	0.47	0.45	-4.06	-5.0		10.0
8,638.0	2.73	274.01	8,628.7	-176.3	-14.7	1.26	0.95	21.44	-4.9		11.7
8,734.0	3.04	264.63	8,724.6	-176.4	-19.5	0.59	0.32	-9.77	-11.5		10.3
8,830.0	2.81	247.61	8,820.4	-177.5	-24.2	0.93	-0.24	-17.73	-18.8		5.8
8,925.0	2.43	223.87	8,915.3	-179.8	-27.8	1.20	-0.40	-24.99	-23.7		-3.2
9,017.0	2.12	222.32	9,007.3	-182.5	-30.3	0.34	-0.34	-1.68	-27.3		-3.9
9,164.0	2.02	233.57	9,154.2	-186.1	-34.2	0.28	-0.07	7.65	-32.8		2.0
9,260.0	1.85	233.88	9,250.1	-188.0	-36.8	0.18	-0.18	0.32	-36.0		2.2
9,348.0	1.13	253.58	9,338.1	-189.1	-38.8	0.99	-0.82	22.38	-35.3		14.7
KOP (MD=9348.0')											
9,355.0	1.08	256.21	9,345.1	-189.1	-38.9	0.99	-0.68	37.60	-34.8		16.3
9,451.0	14.20	0.10	9,440.1	-177.5	-39.8	15.10	13.67	108.22	19.2		30.8
9,546.0	28.97	6.82	9,528.2	-142.8	-37.0	15.74	15.55	7.07	11.2		27.0
9,642.0	34.79	8.07	9,609.7	-92.5	-30.4	6.10	6.06	1.30	1.6		21.5
9,738.0	40.27	3.31	9,685.8	-34.4	-24.7	6.45	5.71	-4.96	0.2		16.0
9,833.0	51.71	357.63	9,751.7	33.8	-24.5	12.78	12.04	-5.98	4.1		15.9
9,928.0	63.02	359.26	9,802.9	113.6	-26.6	11.99	11.91	1.72	9.3		18.1
9,929.3	63.23	359.32	9,803.5	114.8	-26.6	16.71	16.19	4.68	9.4		18.1
HL Crossing, MD:9929.3', TVD:9803.5',N/S:114.8', E/W:-26.6', INC:63.23											
10,024.0	78.61	3.30	9,834.4	204.0	-24.4	16.71	16.24	4.20	10.8		15.9
10,120.0	85.84	3.80	9,847.3	298.8	-18.5	7.55	7.53	0.52	11.6		10.3



Final PVA

Company: Midland
Project: Eddy County, NM (NAD 83 NME)
Site: Golden Graham 1 State Com
Well: #723H
Wellbore: OH
Design: OH

Local Co-ordinate Reference: Well #723H
TVD Reference: KB = 25' @ 2958.0usft (H&P 249)
MD Reference: KB = 25' @ 2958.0usft (H&P 249)
North Reference: Grid
Survey Calculation Method: Minimum Curvature
Database: PEDM

Survey											
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)	
10,215.0	90.49	2.62	9,850.4	393.6	-13.2	5.05	4.89	-1.24	13.9	5.1	
10,311.0	90.91	1.85	9,849.2	489.5	-9.5	0.91	0.44	-0.80	12.1	1.6	
10,406.0	91.41	1.35	9,847.3	584.5	-6.8	0.74	0.53	-0.53	9.6	-0.9	
10,502.0	88.14	3.11	9,847.7	680.4	-3.1	3.87	-3.41	1.83	9.3	-4.5	
10,598.0	87.58	3.52	9,851.2	776.1	2.5	0.72	-0.58	0.43	12.3	-9.9	
10,694.0	87.18	3.44	9,855.6	871.9	8.3	0.42	-0.42	-0.08	16.0	-15.6	
10,789.0	87.41	3.02	9,860.1	966.6	13.6	0.50	0.24	-0.44	19.9	-20.8	
10,885.0	90.07	359.73	9,862.2	1,062.5	15.9	4.41	2.77	-3.43	21.4	-22.9	
10,981.0	90.86	0.80	9,861.4	1,158.5	16.4	1.39	0.82	1.11	20.0	-23.2	
11,076.0	91.56	358.61	9,859.4	1,253.5	15.9	2.42	0.74	-2.31	17.4	-22.5	
11,172.0	90.97	357.53	9,857.3	1,349.4	12.6	1.28	-0.61	-1.12	14.7	-19.1	
11,268.0	90.41	356.08	9,856.2	1,445.3	7.3	1.62	-0.58	-1.51	12.9	-13.6	
11,364.0	91.11	358.35	9,854.9	1,541.1	2.6	2.47	0.73	2.36	11.0	-8.8	
11,460.0	92.37	0.09	9,852.0	1,637.1	1.3	2.24	1.31	1.81	7.5	-7.4	
11,555.0	90.10	359.28	9,849.9	1,732.0	0.8	2.54	-2.39	-0.85	4.8	-6.7	
11,651.0	87.43	0.16	9,852.0	1,828.0	0.3	2.93	-2.78	0.92	6.3	-6.0	
11,747.0	87.01	359.74	9,856.7	1,923.9	0.3	0.62	-0.44	-0.44	10.3	-5.8	
11,842.0	86.29	359.20	9,862.2	2,018.7	-0.6	0.95	-0.76	-0.57	15.3	-4.8	
11,938.0	90.52	1.57	9,864.9	2,114.7	0.0	5.05	4.41	2.47	17.3	-5.3	
12,034.0	88.44	0.97	9,865.8	2,210.6	2.1	2.25	-2.17	-0.62	17.6	-7.2	
12,130.0	89.34	359.65	9,867.6	2,306.6	2.7	1.66	0.94	-1.37	18.8	-7.6	
12,226.0	87.38	357.69	9,870.4	2,402.5	0.4	2.89	-2.04	-2.04	20.9	-5.2	
12,322.0	90.83	358.65	9,871.9	2,498.5	-2.6	3.73	3.59	1.00	21.8	-2.0	
12,417.0	90.99	358.89	9,870.3	2,593.4	-4.7	0.30	0.17	0.25	19.7	0.2	
12,513.0	90.15	357.64	9,869.4	2,689.4	-7.6	1.57	-0.87	-1.30	18.1	3.3	
12,609.0	90.43	358.14	9,868.9	2,785.3	-11.1	0.60	0.29	0.52	17.0	7.0	
12,705.0	90.21	358.10	9,868.4	2,881.2	-14.3	0.23	-0.23	-0.04	15.9	10.3	



Final PVA

Company:	Midland	Local Co-ordinate Reference:	Well #723H
Project:	Eddy County, NM (NAD 83 NME)	TVD Reference:	KB = 25' @ 2958.0usft (H&P 249)
Site:	Golden Graham 1 State Com	MD Reference:	KB = 25' @ 2958.0usft (H&P 249)
Well:	#723H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Survey										
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
12,801.0	88.31	357.86	9,869.6	2,977.2	-17.6	1.99	-1.98	-0.25	16.5	13.8
12,897.0	85.73	359.33	9,874.6	3,073.0	-20.0	3.09	-2.69	1.53	20.8	16.4
12,992.0	87.66	1.40	9,880.1	3,167.8	-19.4	2.98	2.03	2.18	25.7	15.9
13,088.0	92.09	1.94	9,880.3	3,263.8	-16.6	4.65	4.61	0.56	25.3	13.3
13,183.0	92.59	0.57	9,876.4	3,358.7	-14.5	1.53	0.53	-1.44	20.8	11.3
13,279.0	89.45	358.21	9,874.7	3,454.6	-15.5	4.09	-3.27	-2.46	18.5	12.5
13,374.0	88.95	357.75	9,876.0	3,549.6	-18.9	0.72	-0.53	-0.48	19.2	16.0
13,470.0	89.48	357.80	9,877.3	3,645.5	-22.6	0.55	0.55	0.05	19.9	19.9
13,566.0	89.53	2.15	9,878.2	3,741.5	-22.6	4.53	0.05	4.53	20.2	20.1
13,662.0	92.34	4.33	9,876.6	3,837.3	-17.2	3.70	2.93	2.27	18.0	14.8
13,758.0	92.87	4.79	9,872.2	3,932.9	-9.6	0.73	0.55	0.48	13.0	7.4
13,854.0	91.39	3.77	9,868.7	4,028.5	-2.4	1.87	-1.54	-1.06	8.8	0.4
13,950.0	83.90	0.71	9,872.6	4,124.3	1.3	8.43	-7.80	-3.19	12.1	-3.2
14,046.0	82.87	1.06	9,883.7	4,219.6	2.8	1.13	-1.07	0.36	22.6	-4.6
14,142.0	87.06	358.70	9,892.1	4,315.2	2.6	5.00	4.36	-2.46	30.4	-4.2
14,238.0	87.18	356.14	9,896.9	4,411.0	-1.7	2.67	0.12	-2.67	34.6	0.3
14,333.0	89.23	3.92	9,899.9	4,505.9	-1.7	8.46	2.16	8.19	37.0	0.4
14,429.0	89.27	3.19	9,901.2	4,601.7	4.3	0.76	0.04	-0.76	37.6	-5.4
14,525.0	87.85	1.03	9,903.6	4,697.6	7.8	2.69	-1.48	-2.25	39.4	-8.8
14,621.0	90.21	3.16	9,905.2	4,793.5	11.3	3.31	2.46	2.22	40.4	-12.1
14,716.0	88.36	4.45	9,906.4	4,888.3	17.6	2.37	-1.95	1.36	41.0	-18.2
14,812.0	92.62	5.32	9,905.6	4,983.9	25.8	4.53	4.44	0.91	39.6	-26.2
14,908.0	94.05	2.65	9,900.0	5,079.5	32.4	3.15	1.49	-2.78	33.4	-32.8
15,004.0	93.04	359.90	9,894.0	5,175.3	34.6	3.05	-1.05	-2.86	26.8	-34.8
15,100.0	88.95	358.03	9,892.4	5,271.2	32.8	4.68	-4.26	-1.95	24.5	-32.8
15,196.0	87.86	358.18	9,895.0	5,367.1	29.7	1.15	-1.14	0.16	26.6	-29.5
15,292.0	88.28	359.04	9,898.3	5,463.1	27.3	1.00	0.44	0.90	29.2	-27.0



Final PVA

Company:	Midland	Local Co-ordinate Reference:	Well #723H
Project:	Eddy County, NM (NAD 83 NME)	TVD Reference:	KB = 25' @ 2958.0usft (H&P 249)
Site:	Golden Graham 1 State Com	MD Reference:	KB = 25' @ 2958.0usft (H&P 249)
Well:	#723H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Survey										
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
15,388.0	89.45	359.58	9,900.2	5,559.0	26.2	1.34	1.22	0.56	30.5	-25.7
15,483.0	90.69	358.04	9,900.1	5,654.0	24.2	2.08	1.31	-1.62	29.7	-23.6
15,579.0	90.43	357.48	9,899.1	5,749.9	20.5	0.64	-0.27	-0.58	28.2	-19.7
15,675.0	90.15	357.61	9,898.6	5,845.8	16.4	0.32	-0.29	0.14	27.1	-15.4
15,771.0	88.19	357.03	9,900.0	5,941.7	11.9	2.13	-2.04	-0.60	27.9	-10.7
15,866.0	87.63	356.03	9,903.5	6,036.5	6.1	1.21	-0.59	-1.05	30.7	-4.8
15,962.0	88.78	355.77	9,906.5	6,132.2	-0.7	1.23	1.20	-0.27	33.1	2.2
16,058.0	89.82	356.01	9,907.7	6,227.9	-7.6	1.11	1.08	0.25	33.7	9.2
16,153.0	91.50	356.11	9,906.6	6,322.7	-14.1	1.77	1.77	0.11	32.0	15.9
16,249.0	89.15	358.44	9,906.0	6,418.6	-18.7	3.45	-2.45	2.43	30.8	20.6
16,345.0	88.39	357.49	9,908.1	6,514.5	-22.1	1.27	-0.79	-0.99	32.2	24.2
16,441.0	89.31	1.03	9,910.0	6,610.4	-23.4	3.81	0.96	3.69	33.6	25.6
16,536.0	88.08	358.89	9,912.2	6,705.4	-23.4	2.60	-1.29	-2.25	35.1	25.8
16,632.0	92.28	2.76	9,911.9	6,801.4	-22.0	5.95	4.37	4.03	34.2	24.6
16,728.0	96.10	2.78	9,904.9	6,897.0	-17.4	3.98	3.98	0.02	26.5	20.2
16,825.0	91.81	1.98	9,898.2	6,993.6	-13.4	4.50	-4.42	-0.82	19.2	16.2
16,921.0	87.74	359.01	9,898.6	7,089.6	-12.6	5.25	-4.24	-3.09	19.0	15.6
17,016.0	86.56	1.77	9,903.3	7,184.5	-11.9	3.16	-1.24	2.91	23.1	15.1
17,105.0	85.59	0.36	9,909.4	7,273.2	-10.3	1.92	-1.09	-1.58	28.6	13.6
17,200.0	89.82	0.22	9,913.2	7,368.1	-9.8	4.46	4.45	-0.15	31.8	13.3
17,296.0	93.01	0.29	9,910.8	7,464.1	-9.4	3.32	3.32	0.07	28.8	13.0
17,392.0	93.80	359.34	9,905.1	7,559.9	-9.7	1.29	0.82	-0.99	22.5	13.5
17,487.0	90.38	359.71	9,901.6	7,654.8	-10.5	3.62	-3.60	0.39	18.5	14.4
17,583.0	91.47	358.62	9,900.1	7,750.8	-11.9	1.61	1.14	-1.14	16.3	16.0
17,679.0	90.07	2.17	9,898.8	7,846.8	-11.2	3.97	-1.46	3.70	14.4	15.4
17,775.0	89.15	0.70	9,899.5	7,942.8	-8.8	1.81	-0.96	-1.53	14.4	13.2
17,871.0	88.89	0.87	9,901.1	8,038.7	-7.5	0.32	-0.27	0.18	15.4	12.0



Final PVA

Company:	Midland	Local Co-ordinate Reference:	Well #723H
Project:	Eddy County, NM (NAD 83 NME)	TVD Reference:	KB = 25' @ 2958.0usft (H&P 249)
Site:	Golden Graham 1 State Com	MD Reference:	KB = 25' @ 2958.0usft (H&P 249)
Well:	#723H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Survey										
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
17,967.0	88.33	0.47	9,903.4	8,134.7	-6.4	0.72	-0.58	-0.42	17.2	11.1
18,063.0	87.83	359.14	9,906.6	8,230.6	-6.7	1.48	-0.52	-1.39	19.7	11.6
18,158.0	89.26	0.26	9,909.1	8,325.6	-7.2	1.91	1.51	1.18	21.6	12.2
18,254.0	91.05	0.56	9,908.8	8,421.6	-6.5	1.89	1.86	0.31	20.7	11.7
18,349.0	91.33	359.95	9,906.8	8,516.6	-6.1	0.71	0.29	-0.64	18.1	11.4
18,446.0	91.16	359.06	9,904.7	8,613.5	-6.9	0.93	-0.18	-0.92	15.4	12.4
18,541.0	93.94	358.71	9,900.5	8,708.4	-8.8	2.95	2.93	-0.37	10.5	14.4
18,637.0	89.01	358.81	9,898.0	8,804.3	-10.8	5.14	-5.14	0.10	7.4	16.7
18,733.0	87.30	357.95	9,901.1	8,900.2	-13.5	1.99	-1.78	-0.90	9.9	19.6
18,829.0	89.01	1.71	9,904.2	8,996.2	-13.8	4.30	1.78	3.92	12.4	20.0
18,925.0	87.52	1.76	9,907.1	9,092.1	-10.9	1.55	-1.55	0.05	14.7	17.2
19,021.0	88.59	1.85	9,910.4	9,188.0	-7.9	1.12	1.11	0.09	17.3	14.4
19,117.0	93.74	3.08	9,908.4	9,283.8	-3.8	5.52	5.36	1.28	14.7	10.4
19,212.0	91.92	1.60	9,903.7	9,378.6	0.1	2.47	-1.92	-1.56	9.4	6.7
19,308.0	90.94	3.49	9,901.3	9,474.5	4.4	2.22	-1.02	1.97	6.4	2.6
19,404.0	90.38	2.84	9,900.2	9,570.4	9.7	0.89	-0.58	-0.68	4.7	-2.6
19,500.0	89.99	1.85	9,899.9	9,666.3	13.6	1.11	-0.41	-1.03	3.8	-6.3
19,595.0	90.60	0.58	9,899.4	9,761.2	15.6	1.48	0.64	-1.34	2.7	-8.2
19,691.0	90.07	359.65	9,898.9	9,857.2	15.8	1.12	-0.55	-0.97	1.5	-8.2
19,787.0	90.55	0.08	9,898.3	9,953.2	15.6	0.67	0.50	0.45	0.4	-7.8
19,882.0	89.51	356.95	9,898.3	10,048.2	13.1	3.47	-1.09	-3.29	-0.3	-5.2
Final MWD Survey (MD=19882.0')										
19,945.0	89.51	356.95	9,898.8	10,111.1	9.8	0.00	0.00	0.00	-0.2	-1.8
Final Projection to Bit (MD=19945.0')										



Final PVA

Company: Midland
Project: Eddy County, NM (NAD 83 NME)
Site: Golden Graham 1 State Com
Well: #723H
Wellbore: OH
Design: OH

Local Co-ordinate Reference: Well #723H
TVD Reference: KB = 25' @ 2958.0usft (H&P 249)
MD Reference: KB = 25' @ 2958.0usft (H&P 249)
North Reference: Grid
Survey Calculation Method: Minimum Curvature
Database: PEDM

Design Annotations

Measured Depth (usft)	Vertical Depth (usft)	Local Coordinates		Comment
		+N/-S (usft)	+E/-W (usft)	
9,348.0	9,338.1	-189.1	-38.8	KOP (MD=9348.0')
9,929.3	9,803.5	114.8	-26.6	HL Crossing, MD:9929.3', TVD:9803.5',N/S:114.8', E/W:-26.6', INC:63.23
19,882.0	9,898.3	10,048.2	13.1	Final MWD Survey (MD=19882.0')
19,945.0	9,898.8	10,111.1	9.8	Final Projection to Bit (MD=19945.0')

Checked By: _____ Approved By: _____ Date: _____

Intent ☐ As Drilled ☐

API #		
Operator Name:	Property Name:	Well Number

Kick Off Point (KOP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

First Take Point (FTP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

Last Take Point (LTP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

Is this well the defining well for the Horizontal Spacing Unit? ☐Is this well an infill well? ☐

If infill is yes please provide API if available, Operator Name and well number for Defining well for Horizontal Spacing Unit.

API #		
Operator Name:	Property Name:	Well Number

KZ 06/29/2018

Submit To Appropriate District Office Two Copies <u>District I</u> 1625 N. French Dr., Hobbs, NM 88240 <u>District II</u> 811 S. First St., Artesia, NM 88210 <u>District III</u> 1000 Rio Brazos Rd., Aztec, NM 87410 <u>District IV</u> 1220 S. St. Francis Dr., Santa Fe, NM 87505		State of New Mexico Energy, Minerals and Natural Resources Oil Conservation Division 1220 South St. Francis Dr. Santa Fe, NM 87505			Form C-105 Revised August 1, 2011					
WELL COMPLETION OR RECOMPLETION REPORT AND LOG										
4. Reason for filing: ☒ COMPLETION REPORT (Fill in boxes #1 through #31 for State and Fee wells only) ☐ C-144 CLOSURE ATTACHMENT (Fill in boxes #1 through #9, #15 Date Rig Released and #32 and/or #33; attach this and the plat to the C-144 closure report in accordance with 19.15.17.13.K NMAC)					5. Lease Name or Unit Agreement Name GOLDEN GRAHAM 1 STATE COM			6. Well Number: 723H		
7. Type of Completion: ☒ NEW WELL ☐ WORKOVER ☐ DEEPENING ☐ PLUGBACK ☐ DIFFERENT RESERVOIR ☐ OTHER										
8. Name of Operator EOG RESOURCES INC					9. OGRID 7377			11. Pool name or Wildcat Purple Sage; Wolfcamp		
10. Address of Operator PO BOX 2267 MIDLAND, TEXAS 79702										
12. Location	Unit Ltr	Section	Township	Range	Lot	Feet from the	N/S Line	Feet from the	E/W Line	County
Surface:	N	1	26S	28E		215'	SOUTH	1799'	WEST	EDDY
BH:	C	36	25S	28E		341'	NORTH	1792'	WEST	EDDY
13. Date Spudded 07/14/2021		14. Date T.D. Reached 12/30/2021		15. Date Rig Released 1/1/2022		16. Date Completed (Ready to Produce) 7/8/2022		17. Elevations (DF and RKB, RT, GR, etc.) 2933GL		
18. Total Measured Depth of Well MD 19,945' TVD 9,898'				19. Plug Back Measured Depth MD 19,922' TVD 9,898'		20. Was Directional Survey Made? YES		21. Type Electric and Other Logs Run None		
22. Producing Interval(s), of this completion - Top, Bottom, Name WOLFCAMP - 10,002'-19,922'										
23. CASING RECORD (Report all strings set in well)										
CASING SIZE		WEIGHT LB./FT.		DEPTH SET		HOLE SIZE		CEMENTING RECORD		AMOUNT PULLED
9 5/8"		36# J-55		791'		16"		425 CL C/CIRC		
7 5/8"		29.7# ICP 110		9,058'		8 3/4"		1415 C/CIRC		
5 1/2"		20# HCP 110		19,930'		8 1/2"		975 CL H/CIRC TOC @935'		PRESSURE TEST ATTACHED
24. LINER RECORD										
SIZE	TOP	BOTTOM	SACKS CEMENT	SCREEN	25. TUBING RECORD					
					SIZE	DEPTH SET	PACKER SET			
26. Perforation record (interval, size, and number) 10,002'-19,922' 3 1/8", 1995 holes					27. ACID, SHOT, FRACTURE, CEMENT, SQUEEZE, ETC.					
					DEPTH INTERVAL		AMOUNT AND KIND MATERIAL USED			
					10,002'-19,922'		FRAC W/23,799,217 lbs proppant, 389,984 bbls load fld			
28. PRODUCTION										
Date First Production 7/8/2022		Production Method (<i>Flowing, gas lift, pumping - Size and type pump</i>) Flowing				Well Status (<i>Prod. or Shut-in</i>) Producing				
Date of Test 7/13/2022	Hours Tested 24	Choke Size 100	Prod'n For Test Period	Oil - Bbl 2441	Gas - MCF 8673	Water - Bbl. 7629	Gas - Oil Ratio 3553			
Flow Tubing Press.	Casing Pressure 958	Calculated 24-Hour Rate	Oil - Bbl.	Gas - MCF	Water - Bbl.	Oil Gravity - API - (<i>Corr.</i>) 44				
29. Disposition of Gas (<i>Sold, used for fuel, vented, etc.</i>) SOLD							30. Test Witnessed By			
31. List Attachments C-102, C-104, C-103, Directional Survey, H spacing,										
32. If a temporary pit was used at the well, attach a plat with the location of the temporary pit.										
33. If an on-site burial was used at the well, report the exact location of the on-site burial: Latitude _____Longitude _____NAD 1927 1983 _____										
I hereby certify that the information shown on both sides of this form is true and complete to the best of my knowledge and belief										
Signature <i>Kristina Agee</i>			Printed Name Kristina Agee		Title REGULATORY SPECIALIST			Date 4/10/2024		
E-mail Address kristina_agee@eogresources.com										

This form is to be filed with the appropriate District Office of the Division not later than 20 days after the completion of any newly-drilled or deepened well and not later than 60 days after completion of closure. When submitted as a completion report, this shall be accompanied by one copy of all electrical and radio-activity logs run on the well and a summary of all special tests conducted, including drill stem tests. All depths reported shall be measured depths. In the case of directionally drilled wells, true vertical depths shall also be reported. For multiple completions, items 11, 12 and 26-31 shall be reported for each zone.

Southeastern New Mexico			Northwestern New Mexico				
T. Anhy	Rustler	480'	T. Canyon	Brushy	4,768'	T. Ojo Alamo	T. Penn A"
T. Salt		850'	T. Strawn			T. Kirtland	T. Penn. "B"
B. Salt			T. Atoka			T. Fruitland	T. Penn. "C"
T. Yates			T. Miss			T. Pictured Cliffs	T. Penn. "D"
T. 7 Rivers			T. Devonian			T. Cliff House	T. Leadville
T. Queen			T. Silurian			T. Menefee	T. Madison
T. Grayburg			T. Montoya			T. Point Lookout	T. Elbert
T. San Andres			T. Simpson			T. Mancos	T. McCracken
T. Glorieta			T. McKee			T. Gallup	T. Ignacio Otzte
T. Paddock			T. Ellenburger			Base Greenhorn	T. Granite
T. Blinebry			T. Gr. Wash			T. Dakota	
T. Tubb			T. Delaware Sand			T. Morrison	
T. Drinkard			T. Bone Springs			T. Todilto	
T. Abo			T. 1st BS Sand	7,285'		T. Entrada	
T. Wolfcamp	9,496'		T. 2nd BS Sand	8,048'		T. Wingate	
T. Penn			T.			T. Chinle	
T. Cisco (Bough C)			T.			T. Permian	

No. 1, from.....to.....
No. 2, from.....to.....
No. 3, from.....to.....
No. 4, from.....to.....

Include data on rate of water inflow and elevation to which water rose in hole.

No. 1, from.....to.....feet.....
 No. 2, from.....to.....feet.....
 No. 3, from.....to.....feet.....

From	To	Thickness In Feet	Lithology

Submit a Copy To Appropriate District Office
 District I – (575) 393-6161
 1625 N. French Dr., Hobbs, NM 88240
 District II – (575) 748-1283
 811 S. First St., Artesia, NM 88210
 District III – (505) 334-6178
 1000 Rio Brazos Rd., Aztec, NM 87410
 District IV – (505) 476-3460
 1220 S. St. Francis Dr., Santa Fe, NM 87505

State of New Mexico
 Energy, Minerals and Natural Resources

Form C-103
 Revised July 18, 2013

OIL CONSERVATION DIVISION
 1220 South St. Francis Dr.
 Santa Fe, NM 87505

WELL API NO. 30-015-48315	
5. Indicate Type of Lease STATE ☒ FEE ☐	
6. State Oil & Gas Lease No.	
7. Lease Name or Unit Agreement Name GOLDEN GRAHAM 1 STATE COM	
8. Well Number	723H
9. OGRID Number	7377
10. Pool name or Wildcat Purple Sage; Wolfcamp	
4. Well Location Unit Letter N : 215' feet from the SOUTH line and 1799' feet from the WEST line Section 1 Township 26S Range 28E NMPM County EDDY	
11. Elevation (Show whether DR, RKB, RT, GR, etc.) 2933'	

12. Check Appropriate Box to Indicate Nature of Notice, Report or Other Data

NOTICE OF INTENTION TO:		SUBSEQUENT REPORT OF:	
PERFORM REMEDIAL WORK ☐	PLUG AND ABANDON ☐	REMEDIAL WORK ☐	ALTERING CASING ☐
TEMPORARILY ABANDON ☐	CHANGE PLANS ☐	COMMENCE DRILLING OPNS. ☐	P AND A ☐
PULL OR ALTER CASING ☐	MULTIPLE COMPL ☐	CASING/CEMENT JOB ☐	
DOWNHOLE COMMINGLE ☐			
CLOSED-LOOP SYSTEM ☐			
OTHER: ☐		OTHER: COMPLETION ☒	

13. Describe proposed or completed operations. (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work). SEE RULE 19.15.7.14 NMAC. For Multiple Completions: Attach wellbore diagram of proposed completion or recompletion.

TOC IS BELOW THE CASING SHOE, ON 5/15/2023 A SUBSEQUENT PRESSURE TEST HELD
 EOG IS REQUESTING NO REMEDIAL CEMENT AT THIS TIME.

Spud Date:

07/14/2021

Rig Release Date:

01/01/2022

I hereby certify that the information above is true and complete to the best of my knowledge and belief.

SIGNATURE Kristina Agee TITLE REGULATORY SPECIALIST DATE 5/24/2023

Type or print name Kristina Agee E-mail address: kristina_agee@eogresources.com PHONE: (432)686-6996

For State Use Only

APPROVED BY: _____ TITLE _____ DATE _____

Conditions of Approval (if any):



Detailed Job Breakdown



JOB REPORT

COMPANY DETAILS

Company: EOG
Contact: MARK POPE
PHONE:


Email: Mark_pope@eogresources.com

JOB DETAILS

DATE 5/15/2023 11:44:15AM
START TIME 5/15/2023 11:44:15AM
END TIME 5/15/2023 12:19:46PM
Ticket#:
Other:
Other:

Operator:
WELL: GOLDEN GRAHAM 1
Licence #: STATE COM 723
Contractor:
AFE:

Comments:

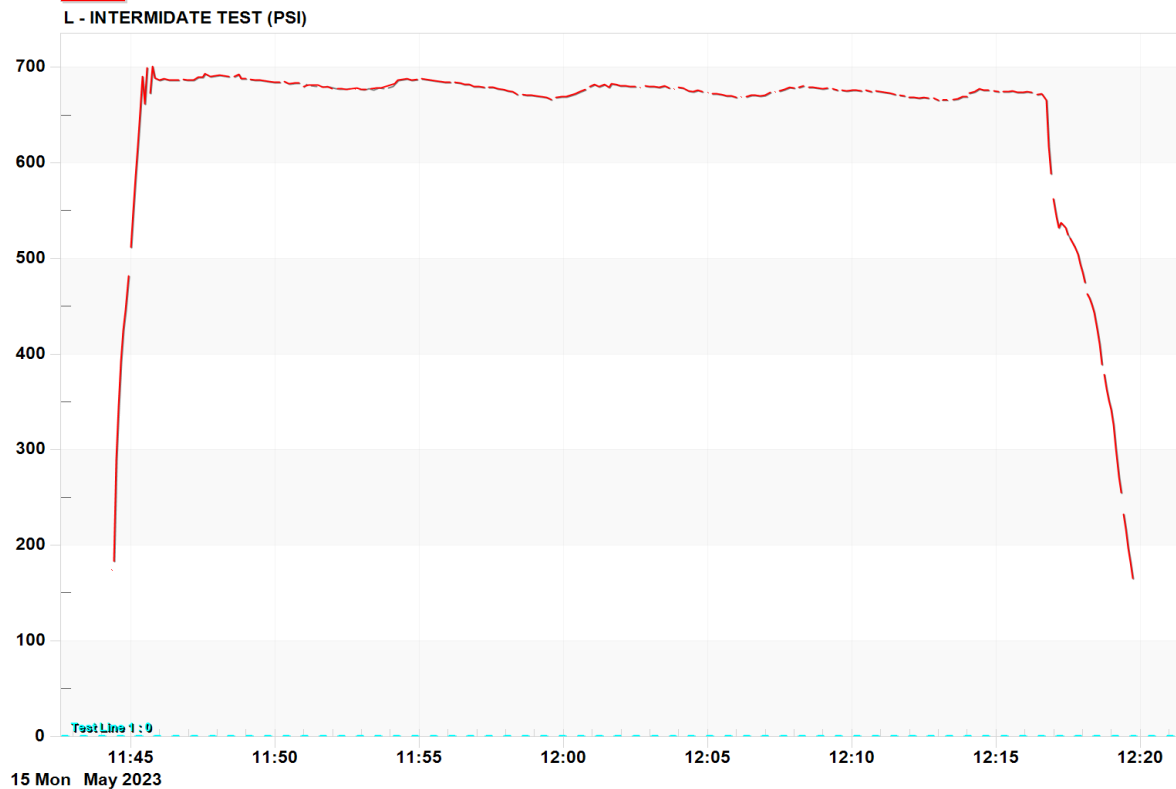

11:44:14

Detailed Job Breakdown

May/15/2023

INTERMEDIATE TEST (PSI)								
Time								
11:44	14.879	177						
11:44	19.879	175						
11:44	24.879	183						
11:44	29.879	290						
11:44	34.879	346						
11:44	39.879	392						
11:44	44.879	425						
11:44	49.879	447						
11:44	54.879	482						
11:44	59.879	512						
11:45	4.879	550						
11:45	9.879	585						
11:45	14.879	619						
11:45	19.879	655						
11:45	24.879	690						
11:45	29.879	662						
11:45	34.879	700						
11:45	39.879	673						
11:45	44.879	701						
11:45	49.879	689						
11:45	54.879	686						
11:45	59.879	687						
11:46	4.879	687						
11:46	9.879	688						
11:46	14.879	687						
11:46	19.879	687						
11:46	24.879	688						
11:46	29.879	687						
11:46	34.879	686						
11:46	39.879	686						
11:46	44.879	687						
11:46	49.879	688						
11:46	54.879	687						
11:46	59.879	687						
11:47	4.879	688						
11:47	9.879	687						
11:47	14.879	688						
11:47	19.879	690						
11:47	24.879	690						
11:47	29.879	690						
11:47	34.879	693						
11:47	39.879	693						
11:47	44.879	690						
11:47	49.879	692						
11:47	54.879	691						
11:47	59.879	692						
11:48	4.879	692						
11:48	9.879	691						

INTERMEDIATE TEST (PSI)								
Time								
11:48	14.879	692						
11:48	19.879	690						
11:48	24.879	690						
11:48	29.879	691						
11:48	34.879	690						
11:48	39.879	690						
11:48	44.879	692						
11:48	49.879	688						
11:48	54.879	690						
11:48	59.879	688						
11:49	4.879	688						
11:49	9.879	688						
11:49	14.879	688						
11:49	19.879	687						
11:49	24.879	688						
11:49	29.879	687						
11:49	34.879	686						
11:49	39.879	686						
11:49	44.879	685						
11:49	49.879	685						
11:49	54.879	685						
11:49	59.879	685						
11:50	4.879	685						
11:50	9.879	684						
11:50	14.879	683						
11:50	19.879	685						
11:50	24.879	684						
11:50	29.879	683						
11:50	34.879	683						
11:50	39.879	684						
11:50	44.879	684						
11:50	49.879	684						
11:50	54.879	682						
11:50	59.879	680						
11:51	4.879	683						
11:51	9.879	681						
11:51	14.880	682						
11:51	19.879	682						
11:51	24.879	681						
11:51	29.879	681						
11:51	34.879	681						
11:51	39.879	679						
11:51	44.879	680						
11:51	49.879	680						
11:51	54.879	680						
11:51	59.879	678						
11:52	4.879	678						
11:52	9.879	678						

INTERMEDIATE TEST (PSI)								
Time								
11:52	14.879	678						
11:52	19.879	678						
11:52	24.879	678						
11:52	29.879	677						
11:52	34.879	678						
11:52	39.879	678						
11:52	44.879	678						
11:52	49.879	678						
11:52	54.880	678						
11:52	59.879	677						
11:53	4.879	677						
11:53	9.879	677						
11:53	14.879	678						
11:53	19.879	678						
11:53	24.879	677						
11:53	29.879	678						
11:53	34.879	679						
11:53	39.879	678						
11:53	44.879	678						
11:53	49.879	680						
11:53	54.879	680						
11:53	59.879	682						
11:54	4.879	681						
11:54	9.879	683						
11:54	14.879	686						
11:54	19.879	686						
11:54	24.879	687						
11:54	29.879	687						
11:54	34.879	688						
11:54	39.879	688						
11:54	44.879	686						
11:54	49.879	685						
11:54	54.879	688						
11:54	59.879	686						
11:55	4.879	688						
11:55	9.879	687						
11:55	14.879	687						
11:55	19.879	687						
11:55	24.879	686						
11:55	29.879	686						
11:55	34.879	686						
11:55	39.879	686						
11:55	44.879	685						
11:55	49.879	686						
11:55	54.879	685						
11:55	59.879	686						
11:56	4.879	685						
11:56	9.879	685						

INTERMEDIATE TEST (PSI)								
Time								
11:56	14.880	684						
11:56	19.879	684						
11:56	24.879	684						
11:56	29.879	684						
11:56	34.879	682						
11:56	39.879	683						
11:56	44.879	682						
11:56	49.880	681						
11:56	54.879	680						
11:56	59.879	681						
11:57	4.879	680						
11:57	9.879	679						
11:57	14.879	679						
11:57	19.879	680						
11:57	24.880	679						
11:57	29.879	679						
11:57	34.879	679						
11:57	39.879	678						
11:57	44.879	678						
11:57	49.880	678						
11:57	54.879	677						
11:57	59.880	677						
11:58	4.879	675						
11:58	9.879	674						
11:58	14.879	675						
11:58	19.879	674						
11:58	24.879	672						
11:58	29.879	673						
11:58	34.880	672						
11:58	39.879	672						
11:58	44.879	671						
11:58	49.879	671						
11:58	54.879	671						
11:58	59.879	669						
11:59	4.879	670						
11:59	9.880	669						
11:59	14.879	669						
11:59	19.879	669						
11:59	24.879	668						
11:59	29.879	668						
11:59	34.879	667						
11:59	39.879	669						
11:59	44.880	669						
11:59	49.879	669						
11:59	54.879	669						
11:59	59.879	668						
12:00	4.879	669						
12:00	9.879	670						

INTERMIDAT E TEST (PSI)								
Time								
12:00	14.879	671						
12:00	19.880	671						
12:00	24.879	672						
12:00	29.879	672						
12:00	34.879	675						
12:00	39.879	676						
12:00	44.879	677						
12:00	49.879	678						
12:00	54.880	680						
12:00	59.879	681						
12:01	4.879	682						
12:01	9.879	682						
12:01	14.879	680						
12:01	19.879	682						
12:01	24.879	682						
12:01	29.880	683						
12:01	34.879	679						
12:01	39.879	683						
12:01	44.879	681						
12:01	49.879	682						
12:01	54.879	682						
12:01	59.879	681						
12:02	4.880	681						
12:02	9.879	681						
12:02	14.879	682						
12:02	19.879	680						
12:02	24.879	680						
12:02	29.879	680						
12:02	34.879	680						
12:02	39.880	679						
12:02	44.879	680						
12:02	49.879	681						
12:02	54.879	680						
12:02	59.879	680						
12:03	4.879	680						
12:03	9.879	680						
12:03	14.880	680						
12:03	19.879	679						
12:03	24.879	679						
12:03	29.879	681						
12:03	34.879	679						
12:03	39.879	679						
12:03	44.879	679						
12:03	49.880	678						
12:03	54.879	678						
12:03	59.879	680						
12:04	4.879	678						
12:04	9.879	678						

12:04:14

Detailed Job Breakdown

May/15/2023

INTERMIDAT E TEST (PSI)								
Time								
12:04	14.879	677						
12:04	19.879	675						
12:04	24.880	676						
12:04	29.879	675						
12:04	34.879	674						
12:04	39.879	676						
12:04	44.879	675						
12:04	49.879	674						
12:04	54.879	675						
12:04	59.880	674						
12:05	4.879	672						
12:05	9.879	672						
12:05	14.879	672						
12:05	19.879	672						
12:05	24.879	670						
12:05	29.879	671						
12:05	34.880	670						
12:05	39.879	670						
12:05	44.879	669						
12:05	49.879	670						
12:05	54.879	669						
12:05	59.879	668						
12:06	4.879	670						
12:06	9.880	669						
12:06	14.879	670						
12:06	19.879	669						
12:06	24.879	669						
12:06	29.879	671						
12:06	34.879	669						
12:06	39.879	671						
12:06	44.880	670						
12:06	49.879	670						
12:06	54.879	670						
12:06	59.879	671						
12:07	4.879	672						
12:07	9.879	673						
12:07	14.879	673						
12:07	19.880	675						
12:07	24.879	675						
12:07	29.879	675						
12:07	34.879	676						
12:07	39.879	677						
12:07	44.879	678						
12:07	49.879	679						
12:07	54.880	678						
12:07	59.879	679						
12:08	4.879	679						
12:08	9.879	680						

12:08:14

Detailed Job Breakdown

May/15/2023

INTERMIDATE TEST (PSI)								
Time								
12:08	14.879	680						
12:08	19.879	681						
12:08	24.879	680						
12:08	29.880	679						
12:08	34.879	680						
12:08	39.879	679						
12:08	44.879	679						
12:08	49.879	679						
12:08	54.879	679						
12:08	59.879	678						
12:09	4.880	677						
12:09	9.879	679						
12:09	14.879	677						
12:09	19.879	678						
12:09	24.879	677						
12:09	29.879	676						
12:09	34.879	675						
12:09	39.880	676						
12:09	44.879	675						
12:09	49.879	675						
12:09	54.879	675						
12:09	59.879	676						
12:10	4.879	676						
12:10	9.879	676						
12:10	14.880	676						
12:10	19.879	675						
12:10	24.879	675						
12:10	29.879	676						
12:10	34.879	676						
12:10	39.879	675						
12:10	44.879	675						
12:10	49.880	675						
12:10	54.879	674						
12:10	59.879	675						
12:11	4.879	672						
12:11	9.879	673						
12:11	14.879	672						
12:11	19.879	673						
12:11	24.880	671						
12:11	29.879	671						
12:11	34.879	671						
12:11	39.879	671						
12:11	44.879	670						
12:11	49.879	670						
12:11	54.879	670						
12:11	59.880	669						
12:12	4.879	668						
12:12	9.879	669						

12:12:14

Detailed Job Breakdown

May/15/2023

INTERMEDIATE TEST (PSI)								
Time								
12:12	14.879	668						
12:12	19.879	668						
12:12	24.879	669						
12:12	29.879	669						
12:12	34.880	668						
12:12	39.879	668						
12:12	44.879	668						
12:12	49.879	667						
12:12	54.879	666						
12:12	59.879	665						
12:13	4.879	667						
12:13	9.880	665						
12:13	14.879	666						
12:13	19.879	665						
12:13	24.879	667						
12:13	29.879	666						
12:13	34.879	667						
12:13	39.879	667						
12:13	44.880	668						
12:13	49.879	669						
12:13	54.879	670						
12:13	59.879	669						
12:14	4.879	673						
12:14	9.879	673						
12:14	14.879	675						
12:14	19.880	674						
12:14	24.879	678						
12:14	29.879	678						
12:14	34.879	676						
12:14	39.879	676						
12:14	44.879	676						
12:14	49.879	675						
12:14	54.880	675						
12:14	59.879	674						
12:15	4.879	675						
12:15	9.879	674						
12:15	14.879	675						
12:15	19.879	675						
12:15	24.879	674						
12:15	29.880	674						
12:15	34.879	675						
12:15	39.879	673						
12:15	44.879	674						
12:15	49.879	673						
12:15	54.879	674						
12:15	59.879	675						
12:16	4.879	675						
12:16	9.879	675						

INTERMEDIATE TEST (PSI)								
Time								
12:16	14.879	674						
12:16	19.879	672						
12:16	24.879	671						
12:16	29.879	673						
12:16	34.879	672						
12:16	39.879	671						
12:16	44.879	665						
12:16	49.879	617						
12:16	54.879	589						
12:16	59.879	562						
12:17	4.879	544						
12:17	9.879	532						
12:17	14.879	538						
12:17	19.879	534						
12:17	24.879	532						
12:17	29.879	525						
12:17	34.879	521						
12:17	39.879	517						
12:17	44.879	512						
12:17	49.879	504						
12:17	54.879	494						
12:17	59.879	486						
12:18	4.879	475						
12:18	9.879	463						
12:18	14.879	458						
12:18	19.879	451						
12:18	24.879	443						
12:18	29.879	425						
12:18	34.879	410						
12:18	39.879	389						
12:18	44.879	378						
12:18	49.879	363						
12:18	54.879	351						
12:18	59.879	342						
12:19	4.879	326						
12:19	9.879	301						
12:19	14.879	272						
12:19	19.879	255						
12:19	24.879	232						
12:19	29.879	216						
12:19	34.879	197						
12:19	39.879	182						
12:19	44.879	166						

Well Name:	Golden Gram 1 State Com #723H
Property Number:	76166
API Number:	30015483150000
Opening Intermediate PSI:	175 psi
Bled Intermediate PSI down to:	N/A
Fluid back to surface:	Yes / OBM
Bbls pumped to load casing:	N/A
Bbls pumped to reach 500 psi:	1 bbls
Bbls bled back after test:	.75 bbls
Start	687 psi
30 min	674 psi
Bleed down, SICP:	165 psi

District I
1625 N. French Dr., Hobbs, NM 88240
Phone:(575) 393-6161 Fax:(575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone:(575) 748-1283 Fax:(575) 748-9720
District III
1000 Rio Brazos Rd., Aztec, NM 87410
Phone:(505) 334-6178 Fax:(505) 334-6170
District IV
1220 S. St Francis Dr., Santa Fe, NM 87505
Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

ACKNOWLEDGMENTS

Action 331992

ACKNOWLEDGMENTS

Operator: EOG RESOURCES INC 5509 Champions Drive Midland, TX 79706	OGRID: 7377
	Action Number: 331992
	Action Type: [C-104] Completion Packet (C-104C)

ACKNOWLEDGMENTS

☒	I hereby certify that the required Water Use Report has been, or will be, submitted for this wells completion.
☒	I hereby certify that the required FracFocus disclosure has been, or will be, submitted for this wells completion.

District I
1625 N. French Dr., Hobbs, NM 88240
Phone:(575) 393-6161 Fax:(575) 393-0720

District II
811 S. First St., Artesia, NM 88210
Phone:(575) 748-1283 Fax:(575) 748-9720

District III
1000 Rio Brazos Rd., Aztec, NM 87410
Phone:(505) 334-6178 Fax:(505) 334-6170

District IV
1220 S. St Francis Dr., Santa Fe, NM 87505
Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 331992

CONDITIONS

Operator: EOG RESOURCES INC 5509 Champions Drive Midland, TX 79706	OGRID: 7377
	Action Number: 331992
	Action Type: [C-104] Completion Packet (C-104C)

CONDITIONS

Created By	Condition	Condition Date
smcgrath	None	4/12/2024
