

Well Name: MR POTATO HEAD 11-14  
FED COM

Well Location: T24S / R29E / SEC 11 /  
NENW / 32.2380497 / -103.9572629

County or Parish/State: EDDY /  
NM

Well Number: 233H

Type of Well: OIL WELL

Allottee or Tribe Name:

Lease Number: NMNM088134

Unit or CA Name:

Unit or CA Number:

US Well Number: 3001548147

Operator: DEVON ENERGY  
PRODUCTION COMPANY LP

Notice of Intent

Sundry ID: 2788345

Type of Submission: Notice of Intent

Date Sundry Submitted: 05/03/2024

Date proposed operation will begin: 05/03/2024

Type of Action: APD Change

Time Sundry Submitted: 11:49

**Procedure Description:** Devon Energy Production Co., L.P. (Devon) respectfully requests to move the SHL, BHL, and dedicated spacing on the subject well. Please see attached revised C102, drill plan (break test and offline cement variance included), and directional plan. Permitted SHL: NENW 500 FNL, 2016 FWL, 11-24S-29E Proposed SHL: NENW 520 FNL, 1756 FWL, 11-24S-29E Permitted BHL: SESW 20 FSL, 2250 FWL, 14-24S-29E Proposed BHL: SESW 20 FSL, 2570 FEL, 14-24S-29E No new leases have been added since approved APD.

NOI Attachments

Procedure Description

- WA018178400\_MR\_POTATO\_HEAD\_11\_14\_FED\_COM\_233H\_WL\_R2\_20240514055514.pdf
- MR\_POTATO\_HEAD\_11\_14\_FED\_COM\_233H\_Directional\_Plan\_05\_03\_24\_20240503114701.pdf
- MR\_POTATO\_HEAD\_11\_14\_FED\_COM\_233H\_20240503114703.pdf
- Mr\_Potato\_Head\_11\_Wellpad\_3\_plat\_NEW\_SHL\_20240503114653.pdf
- Mr\_Potato\_Head\_11\_Wellpad\_3\_plat\_OLD\_SHL\_20240503114652.pdf
- break\_test\_variance\_BOP\_1\_15\_24\_20240503114652.pdf
- 5.5\_20\_\_P110ICY\_TXP\_20240503114651.pdf
- 9.625\_40lb\_J55\_SeAH\_20240503114651.pdf

Received by OCD: 6/6/2024 7:35:43 AM

Page 2 of 37

|  |   |   |                                      |
|--|---|---|--------------------------------------|
| Well Name: MR POTATO HEAD 11-14<br>FED COM |   | Well Location: T24S / R29E / SEC 11 /<br>NENW / 32.2380497 / -103.9572629 | County or Parish/State: EDDY /<br>NM |
| Well Number: 233H                          | Type of Well: OIL WELL                          |   | Allottee or Tribe Name:              |
| Lease Number: NMNM088134                   | Unit or CA Name:                                | Unit or CA Number:  |                                      |
| US Well Number: 3001548147                 | Operator: DEVON ENERGY<br>PRODUCTION COMPANY LP |   |                                      |

13.375\_54.50\_J55\_20240503114651.pdf

Conditions of Approval

Additional

11\_24\_29\_C\_Sundry\_ID\_2788345\_Mr\_Potato\_Head\_11\_14\_Fed\_Com\_233H\_20240515083804.pdf  
Mr\_Potato\_Head\_11\_14\_Fed\_Com\_233H\_Dr\_COA\_20240515083804.pdf

Operator

I certify that the foregoing is true and correct. Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction. Electronic submission of Sundry Notices through this system satisfies regulations requiring a

|  |                                  |
|--|----------------------------------|
| Operator Electronic Signature: SHAYDA OMOUMI | Signed on: MAY 14, 2024 05:55 AM |
| Name: DEVON ENERGY PRODUCTION COMPANY LP     |                                  |
| Title: Regulatory Compliance Associate 3     |                                  |
| Street Address: 333 W SHERIDAN AVE           |                                  |
| City: OKLAHOMA CITY                          | State: OK                        |
| Phone: (405) 235-3611                        |                                  |
| Email address: SHAYDA.OMOUMI@DVN.COM         |                                  |

Field

|                      |        |      |
|----------------------|--------|------|
| Representative Name: |        |      |
| Street Address:      |        |      |
| City:                | State: | Zip: |
| Phone:               |        |      |
| Email address:       |        |      |

BLM Point of Contact

|                                 |                                       |
|---------------------------------|---------------------------------------|
| BLM POC Name: CHRISTOPHER WALLS | BLM POC Title: Petroleum Engineer     |
| BLM POC Phone: 5752342234       | BLM POC Email Address: cwalls@blm.gov |
| Disposition: Approved           | Disposition Date: 05/29/2024          |
| Signature: Chris Walls          |                                       |

Form 3160-5  
(June 2019)

UNITED STATES  
DEPARTMENT OF THE INTERIOR  
BUREAU OF LAND MANAGEMENT

FORM APPROVED  
OMB No. 1004-0137  
Expires: October 31, 2021

**SUNDRY NOTICES AND REPORTS ON WELLS**  
**Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.**

|   |  |
|---|--|
| 5. Lease Serial No.                         |  |
| 6. If Indian, Allottee or Tribe Name        |  |
| 7. If Unit of CA/Agreement, Name and/or No. |  |
| 8. Well Name and No.                        |  |
| 9. API Well No.                             |  |
| 10. Field and Pool or Exploratory Area      |  |
| 11. Country or Parish, State                |  |

12. CHECK THE APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, REPORT OR OTHER DATA

| TYPE OF SUBMISSION                                | TYPE OF ACTION                                |   |  |   |  |
|---|---|---|--|---|--|
| <input type="checkbox"/> Notice of Intent         | <input type="checkbox"/> Acidize              | <input type="checkbox"/> Deepen               | <input type="checkbox"/> Production (Start/Resume) | <input type="checkbox"/> Water Shut-Off |  |
| <input type="checkbox"/> Subsequent Report        | <input type="checkbox"/> Alter Casing         | <input type="checkbox"/> Hydraulic Fracturing | <input type="checkbox"/> Reclamation               | <input type="checkbox"/> Well Integrity |  |
| <input type="checkbox"/> Final Abandonment Notice | <input type="checkbox"/> Casing Repair        | <input type="checkbox"/> New Construction     | <input type="checkbox"/> Recomplete                | <input type="checkbox"/> Other          |  |
|   | <input type="checkbox"/> Change Plans         | <input type="checkbox"/> Plug and Abandon     | <input type="checkbox"/> Temporarily Abandon       |   |  |
|   | <input type="checkbox"/> Convert to Injection | <input type="checkbox"/> Plug Back            | <input type="checkbox"/> Water Disposal            |   |  |

13. Describe Proposed or Completed Operation: Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recompleate horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be perfonned or provide the Bond No. on file with BLM/BIA. Required subsequent reports must be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompletion in a new interval, a Form 3160-4 must be filed once testing has been completed. Final Abandonment Notices must be filed only after all requirements, including reclamation, have been completed and the operator has detennined that the site is ready for final inspection.)

|   |       |
|---|-------|
| 14. I hereby certify that the foregoing is true and correct. Name (Printed/Typed) | Title |
| Signature   | Date  |

THE SPACE FOR FEDERAL OR STATE OFFICE USE

|   |        |      |
|---|--------|------|
| Approved by   | Title  | Date |
| Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon. | Office |      |

Title 18 U.S.C Section 1001 and Title 43 U.S.C Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Instructions on page 2)

## GENERAL INSTRUCTIONS

This form is designed for submitting proposals to perform certain well operations and reports of such operations when completed as indicated on Federal and Indian lands pursuant to applicable Federal law and regulations. Any necessary special instructions concerning the use of this form and the number of copies to be submitted, particularly with regard to local area or regional procedures and practices, are either shown below, will be issued by or may be obtained from the local Federal office.

## SPECIFIC INSTRUCTIONS

*Item 4* - Locations on Federal or Indian land should be described in accordance with Federal requirements. Consult the local Federal office for specific instructions.

*Item 13*: Proposals to abandon a well and subsequent reports of abandonment should include such special information as is required by the local Federal office. In addition, such proposals and reports should include reasons for the abandonment; data on any former or present productive zones or other zones with present significant fluid contents not sealed off by cement or otherwise; depths (top and bottom) and method of placement of cement plugs; mud or other material placed below, between and above plugs; amount, size, method of parting of any casing, liner or tubing pulled and the depth to the top of any tubing left in the hole; method of closing top of well and date well site conditioned for final inspection looking for approval of the abandonment. If the proposal will involve **hydraulic fracturing operations**, you must comply with 43 CFR 3162.3-3, including providing information about the protection of usable water. Operators should provide the best available information about all formations containing water and their depths. This information could include data and interpretation of resistivity logs run on nearby wells. Information may also be obtained from state or tribal regulatory agencies and from local BLM offices.

## NOTICES

The privacy Act of 1974 and the regulation in 43 CFR 2.48(d) provide that you be furnished the following information in connection with information required by this application.

AUTHORITY: 30 U.S.C. 181 et seq., 351 et seq., 25 U.S.C. 396; 43 CFR 3160.

PRINCIPAL PURPOSE: The information is used to: (1) Evaluate, when appropriate, approve applications, and report completion of subsequent well operations, on a Federal or Indian lease; and (2) document for administrative use, information for the management, disposal and use of National Resource lands and resources, such as: (a) evaluating the equipment and procedures to be used during a proposed subsequent well operation and reviewing the completed well operations for compliance with the approved plan; (b) requesting and granting approval to perform those actions covered by 43 CFR 3162.3-2, 3162.3-3, and 3162.3-4; (c) reporting the beginning or resumption of production, as required by 43 CFR 3162.4-1(c) and (d) analyzing future applications to drill or modify operations in light of data obtained and methods used.

ROUTINE USES: Information from the record and/or the record will be transferred to appropriate Federal, State, local or foreign agencies, when relevant to civil, criminal or regulatory investigations or prosecutions in connection with congressional inquiries or to consumer reporting agencies to facilitate collection of debts owed the Government.

EFFECT OF NOT PROVIDING THE INFORMATION: Filing of this notice and report and disclosure of the information is mandatory for those subsequent well operations specified in 43 CFR 3162.3-2, 3162.3-3, 3162.3-4.

The Paperwork Reduction Act of 1995 requires us to inform you that:

The BLM collects this information to evaluate proposed and/or completed subsequent well operations on Federal or Indian oil and gas leases.

Response to this request is mandatory.

The BLM would like you to know that you do not have to respond to this or any other Federal agency-sponsored information collection unless it displays a currently valid OMB control number.

**BURDEN HOURS STATEMENT:** Public reporting burden for this form is estimated to average 8 hours per response, including the time for reviewing instructions, gathering and maintaining data, and completing and reviewing the form. Direct comments regarding the burden estimate or any other aspect of this form to U.S. Department of the Interior, Bureau of Land Management (1004-0137), Bureau Information Collection Clearance Officer (WO-630), 1849 C St., N.W., Mail Stop 401 LS, Washington, D.C. 20240

## Additional Information

### Location of Well

0. SHL: NENW / 500 FNL / 2016 FWL / TWSP: 24S / RANGE: 29E / SECTION: 11 / LAT: 32.2380497 / LONG: -103.9572629 ( TVD: 0 feet, MD: 0 feet )

PPP: NENW / 100 FNL / 2250 FWL / TWSP: 24S / RANGE: 29E / SECTION: 11 / LAT: 32.2391499 / LONG: -103.9565081 ( TVD: 8762 feet, MD: 8843 feet )

PPP: SESW / 100 FSL / 2271 FWL / TWSP: 24S / RANGE: 29E / SECTION: 11 / LAT: 32.225 / LONG: -103.9565 ( TVD: 8977 feet, MD: 13988 feet )

BHL: SESW / 20 FSL / 2250 FWL / TWSP: 24S / RANGE: 29E / SECTION: 14 / LAT: 32.2103062 / LONG: -103.9564755 ( TVD: 8930 feet, MD: 19373 feet )

CONFIDENTIAL

11-24-29-C Sundry ID 2788345 Mr Potato Head 11-14 Fed Com 233H

## Mr Potato Head 11-14 Fed Com 233H

| 13 3/8  |         | surface csg in a |  | 17 1/2   |  | inch hole. |          | Design Factors |              |         |           | Surface |       |        |  |
|---|---------|------------------|--|----------|--|------------|----------|----------------|--------------|---------|-----------|---------|-------|--------|--|
| Segment   | #/ft    | Grade            |  |          |  | Coupling   | Body     | Collapse       | Burst        | Length  | B@s       | a-B     | a-C   | Weight |  |
| "A"   | 54.50   |                  |  | j 55     |  | btc        | 39.14    | 6.04           | 1.57         | 400     | 15        | 2.63    | 11.41 | 21,800 |  |
| "B"   |         |                  |  |          |  | btc        |          |                |              | 0       |           |         |       | 0      |  |
| w/8.4#/g mud, 30min Sfc Csg Test psig: 1,500                  |         |                  |  |          |  |            | Tail Cmt | does not       | circ to sfc. | Totals: | 400       |         |       | 21,800 |  |
| Comparison of Proposed to Minimum Required Cement Volumes     |         |                  |  |          |  |            |          |                |              |         |           |         |       |        |  |
| Hole  | Annular | 1 Stage          |  | 1 Stage  |  | Min        | 1 Stage  | Drilling       | Calc         | Req'd   |           |         |       |        |  |
| Size  | Volume  | Cmt Sx           |  | CuFt Cmt |  | Cu Ft      | % Excess | Mud Wt         | MASP         | BOPE    | Hole-Cplg |         |       |        |  |
| 17 1/2  | 0.6946  | 225              |  | 315      |  | 278        | 13       | 9.00           | 1039         | 2M      | 1.56      |         |       |        |  |
| Site plot (pipe racks 5 or 6) as per O.O.I. (O.D.) not found. |         |                  |  |          |  |            |          |                |              |         |           |         |       |        |  |

| 9 5/8   |         | casing inside the |  | 13 3/8   |       | Design Factors |                      |       |         | Int 1 |          |      |         |
|---|---------|-------------------|--|----------|-------|----------------|----------------------|-------|---------|-------|----------|------|---------|
| Segment   | #/ft    | Grade             |  | Coupling |       | Body           | Collapse             | Burst | Length  | B@s   | a-B      | a-C  | Weight  |
| "A"   | 40.00   |                   |  | j 55     | btc   | 4.93           | 1.48                 | 0.95  | 3,193   | 2     | 1.79     | 2.47 | 127,720 |
| "B"   |         |                   |  |          |       |                |                      |       |         |       |          |      |         |
| w/8.4#/g mud, 30min Sfc Csg Test psig:  |         |                   |  |          |       |                |                      |       | Totals: | 3,193 |          |      |         |
| The cement volume(s) are intended to achieve a top of                             |         |                   |  |          |       | 0              | ft from surface or a |       |         | 400   | overlap. |      |         |
| Hole  | Annular | 1 Stage           |  | 1 Stage  | Min   | 1 Stage        | Drilling             | Calc  | Req'd   |       |          |      |         |
| Size  | Volume  | Cmt Sx            |  | CuFt Cmt | Cu Ft | % Excess       | Mud Wt               | MASP  | BOPE    |       |          |      |         |
| 12 1/4  | 0.3132  | 468               |  | 1252     | 1020  | 23             | 10.50                | 2210  | 3M      |       |          |      |         |
| Class 'C' tail cmt yld > 1.35   |         |                   |  |          |       |                |                      |       |         |       |          |      |         |
| Burst Frac Gradient(s) for Segment(s): A, B, C, D = 1.24, b, c, d All > 0.70, OK. |         |                   |  |          |       |                |                      |       |         |       |          |      |         |

| 5 1/2   |         | casing inside the |  | 9 5/8    |  | Design Factors |          |          |         |        | Prod 1 |      |        |           |                      |  |     |          |  |
|---|---------|-------------------|--|----------|--|----------------|----------|----------|---------|--------|--------|------|--------|-----------|----------------------|--|-----|----------|--|
| Segment   | #/ft    | Grade             |  | Coupling |  | Joint          | Collapse | Burst    | Length  | B@s    | a-B    | a-C  | Weight |           |                      |  |     |          |  |
| "A"   | 20.00   |                   |  | p 110    |  | txp            | 4.08     | 2.9      | 3.44    | 19,433 | 3      | 6.50 | 5.47   | 388,660   |                      |  |     |          |  |
| "B"   |         |                   |  |          |  |                |          |          |         | 0      |        |      |        | 0         |                      |  |     |          |  |
| w/8.4#/g mud, 30min Sfc Csg Test psig: 1,965          |         |                   |  |          |  |                |          |          | Totals: | 19,433 |        |      |        | 388,660   |                      |  |     |          |  |
| The cement volume(s) are intended to achieve a top of |         |                   |  |          |  |                |          |          |         |        |        |      |        | 2993      | ft from surface or a |  | 200 | overlap. |  |
| Hole  | Annular | 1 Stage           |  | 1 Stage  |  | Min            | 1 Stage  | Drilling | Calc    | Req'd  |        |      |        | Min Dist  |                      |  |     |          |  |
| Size  | Volume  | Cmt Sx            |  | CuFt Cmt |  | Cu Ft          | % Excess | Mud Wt   | MASP    | BOPE   |        |      |        | Hole-Cplg |                      |  |     |          |  |
| 8 3/4   | 0.2526  | 2609              |  | 4625     |  | 4154           | 11       | 9.00     |         |        |        |      |        | 1.33      |                      |  |     |          |  |
| Class 'C' tail cmt yld > 1.35                         |         |                   |  |          |  |                |          |          |         |        |        |      |        |           |                      |  |     |          |  |

| #N/A   |         |         |          |       |          |          |         |                 |           |     |        |  |
|--|---------|---------|----------|-------|----------|----------|---------|-----------------|-----------|-----|--------|--|
| 0  | 5 1/2   |         |          |       |          |          |         |                 |           |     |        |  |
| Design Factors                                     |         |         |          |       |          |          |         |                 |           |     |        |  |
| Segment  | #/ft    | Grade   | Coupling | #N/A  | Collapse | Burst    | Length  | <Choose Casing> |           |     | Weight |  |
| "A"  |         |         | 0.00     |       |          |          | 0       | B@s             | a-B       | a-C | 0      |  |
| "B"  |         |         | 0.00     |       |          |          | 0       |                 |           |     | 0      |  |
| w/8.4#/g mud, 30min Sfc Csg Test psig:             |         |         |          |       |          |          | Totals: | 0               | 0         |     |        |  |
| Cmt vol calc below includes this csg, TOC intended |         |         |          |       |          |          |         |                 |           |     |        |  |
| Hole   | Annular | 1 Stage | 1 Stage  | Min   | 1 Stage  | Drilling | Calc    | #N/A            | overlap.  |     |        |  |
| Size   | Volume  | Cmt Sx  | CuFt Cmt | Cu Ft | % Excess | Mud Wt   | MASP    | Req'd           | Min Dist  |     |        |  |
| 0  |         | #N/A    | #N/A     | 0     | #N/A     |          |         | BOPE            | Hole-Cplg |     |        |  |
| #N/A   |         |         |          |       |          |          |         |                 |           |     |        |  |
| Capitan Reef est top XXXX.                         |         |         |          |       |          |          |         |                 |           |     |        |  |

## PECOS DISTRICT DRILLING CONDITIONS OF APPROVAL

|                         |   |
|-------------------------|---|
| <b>OPERATOR'S NAME:</b> | <b>Devon Energy Production Company LP</b> |
| <b>LEASE NO.:</b>       | <b>NMNM088134</b>                         |
| <b>LOCATION:</b>        | Section 11, T.24 S., R.29 E., NMPM        |
| <b>COUNTY:</b>          | Eddy County, New Mexico ▼                 |

|                              |  |
|------------------------------|--|
| <b>WELL NAME &amp; NO.:</b>  | <b>Mr Potato Head 11-14 Fed Com 233H</b> |
| <b>SURFACE HOLE FOOTAGE:</b> | 520'/N & 1756'/W                         |
| <b>BOTTOM HOLE FOOTAGE:</b>  | 20'/S & 2570'/E                          |
| <b>ATS/API ID:</b>           | <b>3001548147</b>                        |
| <b>APD ID:</b>               | <b>10400062542</b>                       |
| <b>Sundry ID:</b>            | <b>2788345</b>                           |

COA

|                               |   |   |   |
|-------------------------------|---|---|---|
| H2S                           | Yes ▼   |   |   |
| Potash                        | None ▼  |   |   |
| Cave/Karst Potential          | Medium ▼  |   |   |
| Cave/Karst Potential          | <input type="checkbox"/> Critical                 |   |   |
| Variance                      | <input type="radio"/> None                        | <input checked="" type="radio"/> Flex Hose            | <input type="radio"/> Other               |
| Wellhead                      | Conventional and Multibowl ▼                      |   |   |
| Other                         | <input type="checkbox"/> 4 String                 | Capitan Reef<br>None ▼                                | <input type="checkbox"/> WIPP             |
| Other                         | Pilot Hole<br>None ▼                              | <input type="checkbox"/> Open Annulus                 |   |
| Cementing                     | Contingency Squeeze<br>Int 1 ▼                    | Echo-Meter<br>None ▼                                  | Primary Cement Squeeze<br>None ▼          |
| Special Requirements          | <input type="checkbox"/> Water Disposal/Injection | <input checked="" type="checkbox"/> COM               | <input type="checkbox"/> Unit             |
| Special Requirements          | <input type="checkbox"/> Batch Sundry             |   |   |
| Special Requirements Variance | <input checked="" type="checkbox"/> Break Testing | <input checked="" type="checkbox"/> Offline Cementing | <input type="checkbox"/> Casing Clearance |

## A. HYDROGEN SULFIDE

A Hydrogen Sulfide (H<sub>2</sub>S) Drilling Plan shall be activated 500 feet prior to drilling into the **Cedar Canyon** formation. As a result, the Hydrogen Sulfide area must meet **43 CFR part 3170 Subpart 3176** requirements, which includes equipment and personnel/public protection items. If Hydrogen Sulfide is encountered, please provide measured values and formations to the BLM.

## B. CASING

1. The **13-3/8** inch surface casing shall be set at approximately **400 feet** (a minimum of **70 feet (Eddy County)** into the Rustler Anhydrite and above the salt when present, and below usable fresh water) and cemented to the surface. The surface hole shall be **17 1/2** inch in diameter.
  - a. If cement does not circulate to the surface, the appropriate BLM office shall be notified and a temperature survey utilizing an electronic type temperature survey with surface log readout will be used or a cement bond log shall be run to verify the top of the cement. Temperature survey will be run a minimum of six hours after pumping cement and ideally between 8-10 hours after completing the cement job.
  - b. Wait on cement (WOC) time for a primary cement job will be a minimum of **8 hours** or 500 pounds compressive strength, whichever is greater. (This is to include the lead cement)
  - c. Wait on cement (WOC) time for a remedial job will be a minimum of 4 hours after bringing cement to surface or 500 pounds compressive strength, whichever is greater.
  - d. If cement falls back, remedial cementing will be done prior to drilling out that string.

**Cement excess is less than 25%, more cement is required if washout occurs. Adjust cement volume and excess based on a fluid caliper or similar method that reflects the as-drilled size of the wellbore.**

2. The minimum required fill of cement behind the **9-5/8** inch intermediate casing shall be set at approximately **3193 feet** is:

### Option 1 (Single Stage):

- Cement to surface. If cement does not circulate see B.1.a, c-d above.  
**Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry due to cave/karst or potash.**  
**Cement excess is less than 25%, more cement is required if washout occurs. Adjust cement volume and excess based on a fluid caliper or similar method that reflects the as-drilled size of the wellbore.**



**Option 2:**

Operator has proposed a DV tool(s), the depth may be adjusted as long as the cement is changed proportionally. The DV tool(s) may be cancelled if cement circulates to surface on the first stage.

DV tool(s) shall be set a minimum of 50' below previous shoe and a minimum of 200' above current shoe. Operator shall contact the BLM if DV tool(s) depth cannot be set in this range. If an ECP is used, it is to be set a minimum of 50' below the shoe to provide cement across the shoe. If it cannot be set below the shoe, a CBL shall be run to verify cement coverage.

- a. First stage to DV tool(s): Cement to circulate. If cement does not circulate off the DV tool(s), contact the appropriate BLM office before proceeding with second stage cement job.
- b. Second stage above DV tool(s):
  - Cement to surface. If cement does not circulate, contact the appropriate BLM office.  
**Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry due to cave/karst or potash.**  
**Cement excess is less than 25%, more cement is required if washout occurs. Adjust cement volume and excess based on a fluid caliper or similar method that reflects the as-drilled size of the wellbore.**

**Operator has proposed to pump down 13-3/8" X 9-5/8" annulus after primary cementing stage. Operator must run a CBL from TD of the 9-5/8" casing to surface. Submit results to the BLM.**

**If cement does not tie-back into the previous casing shoe, a third stage remediation BH may be performed. The appropriate BLM office shall be notified.**

- ❖ In Medium Cave/Karst Areas if cement does not circulate to surface on the first two casing strings, the cement on the 3rd casing string must come to surface.
3. The minimum required fill of cement behind the 5-1/2 inch production casing is:
    - Cement should tie-back at least **200 feet** into previous casing string. Operator shall provide method of verification.  
**Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry due to cave/karst or potash.**  
**Cement excess is less than 25%, more cement is required if washout occurs. Adjust cement volume and excess based on a fluid caliper or similar method that reflects the as-drilled size of the wellbore.**

## C. PRESSURE CONTROL

1. Variance approved to use flex line from BOP to choke manifold. Manufacturer's specification to be readily available. No external damage to flex line. Flex line to be installed as straight as possible (no hard bends).'
- 2.

### Option 1:

- a. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **3000 (3M) psi. Annular which shall be tested to 2100 (70% Working Pressure) psi.**
- b. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the **9-5/8** inch intermediate casing shoe shall be **5000 (5M) psi.**

### Option 2:

Operator has proposed a multi-bowl wellhead assembly. This assembly will only be tested when installed on the **13-3/8** inch surface casing. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **5000 (5M) psi.**

- a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
- b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
- c. Manufacturer representative shall install the test plug for the initial BOP test.
- d. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
- e. Whenever any seal subject to test pressure is broken, all the tests in 43 CFR 3172.6(b)(9) must be followed.

## D. SPECIAL REQUIREMENT (S)

### Communitization Agreement

- The operator will submit a Communitization Agreement to the Santa Fe Office, 301 Dinosaur Trail Santa Fe, New Mexico 87508, at least 90 days before the anticipated date of first production from a well subject to a spacing order issued by the New Mexico Oil Conservation Division. The Communitization Agreement will include the signatures of all working interest owners in all Federal and Indian leases subject to

the Communitization Agreement (i.e., operating rights owners and lessees of record), or certification that the operator has obtained the written signatures of all such owners and will make those signatures available to the BLM immediately upon request.

- The operator will submit an as-drilled survey well plat of the well completion, but are not limited to, those specified in **43 CFR part 3170 Subpart 3171**
- If the operator does not comply with this condition of approval, the BLM may take enforcement actions that include, but are not limited to, those specified in 43 CFR 3163.1.
- In addition, the well sign shall include the surface and bottom hole lease numbers. When the Communitization Agreement number is known, it shall also be on the sign.

### **BOPE Break Testing Variance (Approved)**

- BOPE Break Testing is ONLY permitted for 5M BOPE or less. **(Annular preventer must be tested to a minimum of 70% of BOPE working pressure and shall be higher than the MASP)**
- BOPE Break Testing is NOT permitted to drilling the production hole section.
- Variance only pertains to the intermediate hole-sections and no deeper than the Bone Springs formation.
- While in transfer between wells, the BOPE shall be secured by the hydraulic carrier or cradle.
- Any well control event while drilling require notification to the BLM Petroleum Engineer **(575-706-2779)** prior to the commencement of any BOPE Break Testing operations.
- A full BOPE test is required prior to drilling the first deep intermediate hole section. If any subsequent hole interval is deeper than the first, a full BOPE test will be required. (200' TVD tolerance between intermediate shoes is allowable).
- The BLM is to be contacted **(575-361-2822 Eddy County)** 4 hours prior to BOPE tests.
- As a minimum, a full BOPE test shall be performed at **21-day** intervals.
- In the event any repairs or replacement of the BOPE is required, the BOPE shall test as per **43 CFR part 3170 Subpart 3172**.
- If in the event break testing is not utilized, then a full BOPE test would be conducted.

### **Offline Cementing**

Operator has been **(Approved)** to pump the proposed cement program offline in the **Intermediate(s) interval**.

Offline cementing should commence within 24 hours of landing the casing for the interval.

Notify the BLM 4hrs prior to cementing offline at **Eddy County: 575-361-2822**.

## GENERAL REQUIREMENTS

The BLM is to be notified in advance for a representative to witness:

- a. Spudding well (minimum of 24 hours)
- b. Setting and/or Cementing of all casing strings (minimum of 4 hours)
- c. BOPE tests (minimum of 4 hours)

☒ Eddy County

**EMAIL** or call the Carlsbad Field Office, 620 East Greene St., Carlsbad, NM 88220,

**[BLM\\_NM\\_CFO\\_DrillingNotifications@BLM.GOV](mailto:BLM_NM_CFO_DrillingNotifications@BLM.GOV)**

(575) 361-2822

1. Unless the production casing has been run and cemented or the well has been properly plugged, the drilling rig shall not be removed from over the hole without prior approval.
  - a. In the event the operator has proposed to drill multiple wells utilizing a skid/walking rig. Operator shall secure the wellbore on the current well, after installing and testing the wellhead, by installing a blind flange of like pressure rating to the wellhead and a pressure gauge that can be monitored while drilling is performed on the other well(s).
  - b. When the operator proposes to set surface casing with Spudder Rig
    - Notify the BLM when moving in and removing the Spudder Rig.
    - Notify the BLM when moving in the 2<sup>nd</sup> Rig. Rig to be moved in within 90 days of notification that Spudder Rig has left the location.
    - BOP/BOPE test to be conducted per **43 CFR part 3170 Subpart 3172** as soon as 2nd Rig is rigged up on well.
2. Floor controls are required for 3M or Greater systems. These controls will be on the rig floor, unobstructed, readily accessible to the driller and will be operational at all times during drilling and/or completion activities. Rig floor is defined as the area immediately around the rotary table; the area immediately above the substructure on which the draw works are located, this does not include the dog house or stairway area.
3. The record of the drilling rate along with the GR/N well log run from TD to surface (horizontal well – vertical portion of hole) shall be submitted to the BLM office as well as all other logs run on the borehole 30 days from completion. If available, a digital copy of the logs is to be submitted in addition to the paper copies. The Rustler top and top and bottom of Salt are to be recorded on the Completion Report when present.

A. CASING

1. Changes to the approved APD casing program need prior approval if the items substituted are of lesser grade or different casing size or are Non-API. The Operator can exchange the components of the proposal with that of superior strength (i.e. changing from J-55 to N-80, or from 36# to 40#). Changes to the approved cement program need prior approval if the altered cement plan has less volume or strength or if the changes are substantial (i.e. Multistage tool, ECP, etc.). The initial wellhead installed on the well will remain on the well with spools used as needed.
2. Wait on cement (WOC) for Potash Areas: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi for all cement blends, 2) until cement has been in place at least 24 hours. WOC time will be recorded in the driller's log. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
3. Wait on cement (WOC) for Water Basin: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi at the shoe, 2) until cement has been in place at least 8 hours. WOC time will be recorded in the driller's log. See individual casing strings for details regarding lead cement slurry requirements. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
4. Provide compressive strengths including hours to reach required 500 pounds compressive strength prior to cementing each casing string. Have well specific cement details onsite prior to pumping the cement for each casing string.
5. No pea gravel permitted for remedial or fall back remedial without prior authorization from the BLM engineer.
6. On that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Formation at the shoe shall be tested to a minimum of the mud weight equivalent anticipated to control the formation pressure to the next casing depth or at total depth of the well. This test shall be performed before drilling more than 20 feet of new hole.
7. If hardband drill pipe is rotated inside casing, returns will be monitored for metal. If metal is found in samples, drill pipe will be pulled and rubber protectors which have a larger diameter than the tool joints of the drill pipe will be installed prior to continuing drilling operations.
8. Whenever a casing string is cemented in the R-111-P potash area, the NMOCD requirements shall be followed.

## B. PRESSURE CONTROL

1. All blowout preventer (BOP) and related equipment (BOPE) shall comply with well control requirements as described in **43 CFR part 3170 Subpart 3172** and **API STD 53 Sec. 5.3**.
2. If a variance is approved for a flexible hose to be installed from the BOP to the choke manifold, the following requirements apply: The flex line must meet the requirements of API 16C. Check condition of flexible line from BOP to choke manifold, replace if exterior is damaged or if line fails test. Line to be as straight as possible with no hard bends and is to be anchored according to Manufacturer's requirements. The flexible hose can be exchanged with a hose of equal size and equal or greater pressure rating. Anchor requirements, specification sheet and hydrostatic pressure test certification matching the hose in service, to be onsite for review. These documents shall be posted in the company man's trailer and on the rig floor.
3. 5M or higher system requires an HCR valve, remote kill line and annular to match. The remote kill line is to be installed prior to testing the system and tested to stack pressure.
4. If the operator has proposed a multi-bowl wellhead assembly in the APD. The following requirements must be met:
  - a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
  - b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
  - c. Manufacturer representative shall install the test plug for the initial BOP test.
  - d. Whenever any seal subject to test pressure is broken, all the tests in 43 CFR 3172.6(b)(9) must be followed.
  - e. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
5. The appropriate BLM office shall be notified a minimum of 4 hours in advance for a representative to witness the tests.
  - a. In a water basin, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. The casing cut-off and BOP installation can be initiated four hours after installing the slips, which will be approximately six hours after bumping the plug. For those casing strings not using slips, the minimum wait time before cut-off is eight hours after bumping the plug. BOP/BOPE testing can begin after cut-off or once cement reaches 500 psi compressive strength (including

lead cement), whichever is greater. However, if the float does not hold, cut-off cannot be initiated until cement reaches 500 psi compressive strength (including lead when specified).

- b. In potash areas, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. For all casing strings, casing cut-off and BOP installation can be initiated at twelve hours after bumping the cement plug. The BOPE test can be initiated after bumping the cement plug with the casing valve open. (only applies to single stage cement jobs, prior to the cement setting up.)
- c. The tests shall be done by an independent service company utilizing a test plug not a cup or J-packer and can be initiated immediately with the casing valve open. The operator also has the option of utilizing an independent tester to test without a plug (i.e. against the casing) pursuant to **43 CFR part 3170 Subpart 3172** with the pressure not to exceed 70% of the burst rating for the casing. Any test against the casing must meet the WOC time for water basin (8 hours) or potash (24 hours) or 500 pounds compressive strength, whichever is greater, prior to initiating the test (see casing segment as lead cement may be critical item).
- d. The test shall be run on a 5000 psi chart for a 2-3M BOP/BOP, on a 10000 psi chart for a 5M BOP/BOPE and on a 15000 psi chart for a 10M BOP/BOPE. If a linear chart is used, it shall be a one hour chart. A circular chart shall have a maximum 2 hour clock. If a twelve hour or twenty-four hour chart is used, tester shall make a notation that it is run with a two hour clock.
- e. The results of the test shall be reported to the appropriate BLM office.
- f. All tests are required to be recorded on a calibrated test chart. A copy of the BOP/BOPE test chart and a copy of independent service company test will be submitted to the appropriate BLM office.
- g. The BOP/BOPE test shall include a low pressure test from 250 to 300 psi. The test will be held for a minimum of 10 minutes if test is done with a test plug and 30 minutes without a test plug. This test shall be performed prior to the test at full stack pressure.
- h. BOP/BOPE must be tested by an independent service company within 500 feet of the top of the Wolfcamp formation if the time between the setting of the intermediate casing and reaching this depth exceeds 20 days. This test does not exclude the test prior to drilling out the casing shoe as per **43 CFR part 3170 Subpart 3172**.

C. DRILLING MUD

Mud system monitoring equipment, with derrick floor indicators and visual and audio alarms, shall be operating before drilling into the Wolfcamp formation, and shall be used until production casing is run and cemented.

D. WASTE MATERIAL AND FLUIDS

All waste (i.e. drilling fluids, trash, salts, chemicals, sewage, gray water, etc.) created as a result of drilling operations and completion operations shall be safely contained and disposed of properly at a waste disposal facility. No waste material or fluid shall be disposed of on the well location or surrounding area.

Porto-johns and trash containers will be on-location during fracturing operations or any other crew-intensive operations.

Long Vo (LVO) 5/15/2024



District I  
1625 N. French Dr., Hobbs, NM 88240  
Phone: (575) 393-6161 Fax: (575) 393-0720  
District II  
811 S. First St., Artesia, NM 88210  
Phone: (575) 748-1283 Fax: (575) 748-9720  
District III  
1000 Rio Brazos Road, Aztec, NM 87410  
Phone: (505) 334-6178 Fax: (505) 334-6170  
District IV  
1220 S. St. Francis Dr., Santa Fe, NM 87505  
Phone: (505) 476-3460 Fax: (505) 476-3462

State of New Mexico  
Energy, Minerals & Natural Resources Department  
OIL CONSERVATION DIVISION  
1220 South St. Francis Dr.  
Santa Fe, NM 87505

Form C-102  
Revised August 1, 2011  
Submit one copy to appropriate  
District Office

☐ AMENDED REPORT

WELL LOCATION AND ACREAGE DEDICATION PLAT

|   |   |  |
|---|---|--|
| <sup>1</sup> API Number<br>30-015-48147 | <sup>2</sup> Pool Code<br>96473                                     | <sup>3</sup> Pool Name<br>PIERCE CROSSING; BONE SPRING, EAST |
| <sup>4</sup> Property Code<br>326251    | <sup>5</sup> Property Name<br>MR POTATO HEAD 11 14 FED COM          | <sup>6</sup> Well Number<br>233H                             |
| <sup>7</sup> OGRID No.<br>6137          | <sup>8</sup> Operator Name<br>DEVON ENERGY PRODUCTION COMPANY, L.P. | <sup>9</sup> Elevation<br>3070.8                             |

<sup>10</sup> Surface Location

| UL or lot no. | Section | Township | Range | Lot Idn | Feet from the | North/South line | Feet from the | East/West line | County |
|---------------|---------|----------|-------|---------|---------------|------------------|---------------|----------------|--------|
| C             | 11      | 24 S     | 29 E  |         | 520           | NORTH            | 1756          | WEST           | EDDY   |

<sup>11</sup> Bottom Hole Location If Different From Surface

| UL or lot no. | Section | Township | Range | Lot Idn | Feet from the | North/South line | Feet from the | East/West line | County |
|---------------|---------|----------|-------|---------|---------------|------------------|---------------|----------------|--------|
| O             | 14      | 24 S     | 29 E  |         | 20            | SOUTH            | 2570          | EAST           | EDDY   |

|                                      |                               |                                  |  |
|--------------------------------------|-------------------------------|----------------------------------|--|
| <sup>12</sup> Dedicated Acres<br>320 | <sup>13</sup> Joint or Infill | <sup>14</sup> Consolidation Code | <sup>15</sup> Order No.<br>NSL Pending |
|--------------------------------------|-------------------------------|----------------------------------|--|

No allowable will be assigned to this completion until all interests have been consolidated or a non-standard unit has been approved by the division.

|                    |  |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |   |
|--------------------|--|--------------------|----------------|--------------------|----------------|--------------------|----------------|--------------------|----------------|--------------------|----------------|--------------------|----------------|--------------------|----------------|--------------------|----------------|--------------------|----------------|--------------------|----------------|--------------------|----------------|--------------------|----------------|--------------------|----------------|---|
|                    | <p>MR POTATO HEAD 11 14 FED COM 233H<br/>EL. = 3070.8</p> <p>GEODETTIC COORDINATES<br/>NAD 83 NMSP EAST<br/>SURFACE LOCATION<br/>N. = 450518.44<br/>E. = 657353.16<br/>LAT. = 32.2379940°N<br/>LONG. = 103.9581036°W</p> <p>KICK OFF POINT<br/>CALLS 54' FNL 2570' FEL<br/>N. = 450989<br/>E. = 658363<br/>LAT. = 32.23918545<br/>LONG. = 103.95493050</p> <p>FIRST TAKE POINT (PPP 1)<br/>100' FNL, 2570' FEL<br/>N. = 450943.09<br/>E. = 658332.73<br/>LAT. = 32.2391519°N<br/>LONG. = 103.9549305°W</p> <p>LAST TAKE POINT<br/>100' FSL, 2570' FEL<br/>N. = 440530.99<br/>E. = 658363.10<br/>LAT. = 32.2105303°N<br/>LONG. = 103.9549509°W</p> <p>BOTTOM OF HOLE<br/>20' FSL, 2570' FEL<br/>N. = 440451.01<br/>E. = 658363.26<br/>LAT. = 32.2103105°N<br/>LONG. = 103.9549513°W</p> <p>PPP 2<br/>0' FSL, 2576' FEL<br/>N. = 445735.55<br/>E. = 658347.92<br/>LAT. = 32.2248370°N<br/>LONG. = 103.9549407°W</p> <p>CORNER COORDINATES TABLE<br/>NAD 83 NMSP EAST</p> <table border="1"> <tr> <td>A - N. = 451030.14</td> <td>E. = 655595.01</td> </tr> <tr> <td>B - N. = 451042.47</td> <td>E. = 658249.35</td> </tr> <tr> <td>C - N. = 451059.78</td> <td>E. = 660901.66</td> </tr> <tr> <td>D - N. = 448402.62</td> <td>E. = 660913.47</td> </tr> <tr> <td>E - N. = 445749.34</td> <td>E. = 660923.11</td> </tr> <tr> <td>F - N. = 443099.57</td> <td>E. = 660927.38</td> </tr> <tr> <td>G - N. = 440449.43</td> <td>E. = 660932.70</td> </tr> <tr> <td>H - N. = 440430.47</td> <td>E. = 658288.01</td> </tr> <tr> <td>I - N. = 440412.71</td> <td>E. = 655642.49</td> </tr> <tr> <td>J - N. = 443066.77</td> <td>E. = 655632.22</td> </tr> <tr> <td>K - N. = 445720.12</td> <td>E. = 655621.49</td> </tr> <tr> <td>L - N. = 448375.07</td> <td>E. = 655608.09</td> </tr> <tr> <td>M - N. = 445735.13</td> <td>E. = 658270.76</td> </tr> </table> <p>LEGEND<br/>--- SECTION LINE<br/>--- QUARTER LINE<br/>--- LEASE LINE<br/>--- WELL PATH</p> | A - N. = 451030.14 | E. = 655595.01 | B - N. = 451042.47 | E. = 658249.35 | C - N. = 451059.78 | E. = 660901.66 | D - N. = 448402.62 | E. = 660913.47 | E - N. = 445749.34 | E. = 660923.11 | F - N. = 443099.57 | E. = 660927.38 | G - N. = 440449.43 | E. = 660932.70 | H - N. = 440430.47 | E. = 658288.01 | I - N. = 440412.71 | E. = 655642.49 | J - N. = 443066.77 | E. = 655632.22 | K - N. = 445720.12 | E. = 655621.49 | L - N. = 448375.07 | E. = 655608.09 | M - N. = 445735.13 | E. = 658270.76 | <p><b>17 OPERATOR CERTIFICATION</b></p> <p>I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief, and that this organization either owns a working interest or unleased mineral interest in the land including the proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of such a mineral or working interest, or to a voluntary pooling agreement or a compulsory pooling order heretofore entered by the division.</p> <p><i>Shayda Omoumi</i> 4/23/2024<br/>Signature Date</p> <p>Shayda Omoumi<br/>Printed Name</p> <p>shayda.omoumi@divn.com<br/>E-mail Address</p> <p><b>18 SURVEYOR CERTIFICATION</b></p> <p>I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief.</p> <p>APRIL 22, 2024<br/>Date of Survey</p> <p><i>Shayda Omoumi</i><br/>Signature and Seal of Professional Surveyor</p> <p>Certificate Number: 12797<br/>SURV. NO. 8414B</p> |
| A - N. = 451030.14 | E. = 655595.01   |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |   |
| B - N. = 451042.47 | E. = 658249.35   |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |   |
| C - N. = 451059.78 | E. = 660901.66   |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |   |
| D - N. = 448402.62 | E. = 660913.47   |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |   |
| E - N. = 445749.34 | E. = 660923.11   |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |   |
| F - N. = 443099.57 | E. = 660927.38   |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |   |
| G - N. = 440449.43 | E. = 660932.70   |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |   |
| H - N. = 440430.47 | E. = 658288.01   |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |   |
| I - N. = 440412.71 | E. = 655642.49   |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |   |
| J - N. = 443066.77 | E. = 655632.22   |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |   |
| K - N. = 445720.12 | E. = 655621.49   |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |   |
| L - N. = 448375.07 | E. = 655608.09   |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |   |
| M - N. = 445735.13 | E. = 658270.76   |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |                    |                |   |

Intent ☒ As Drilled ☐

|  |  |                     |
|--|--|---------------------|
| API #  |  |                     |
| Operator Name:<br>DEVON ENERGY PRODUCTION<br>COMPANY, L.P. | Property Name:<br>MR POTATO HEAD 11 14 FED COM | Well Number<br>233H |

## Kick Off Point (KOP)

| UL<br>B                 | Section<br>11 | Township<br>24S | Range<br>29E | Lot | Feet<br>54                 | From N/S<br>NORTH | Feet<br>2570 | From E/W<br>EAST | County<br>EDDY |
|-------------------------|---------------|-----------------|--------------|-----|----------------------------|-------------------|--------------|------------------|----------------|
| Latitude<br>32.23918545 |               |                 |              |     | Longitude<br>-103.95493050 |                   |              |                  | NAD<br>83      |

## First Take Point (FTP)

| UL<br>B                | Section<br>11 | Township<br>24S | Range<br>29E | Lot | Feet<br>100              | From N/S<br>NORTH | Feet<br>2570 | From E/W<br>EAST | County<br>EDDY |
|------------------------|---------------|-----------------|--------------|-----|--------------------------|-------------------|--------------|------------------|----------------|
| Latitude<br>32.2391519 |               |                 |              |     | Longitude<br>103.9549305 |                   |              |                  | NAD<br>83      |

## Last Take Point (LTP)

| UL<br>O                | Section<br>14 | Township<br>24S | Range<br>29E | Lot | Feet<br>100              | From N/S<br>SOUTH | Feet<br>2570 | From E/W<br>EAST | County<br>EDDY |
|------------------------|---------------|-----------------|--------------|-----|--------------------------|-------------------|--------------|------------------|----------------|
| Latitude<br>32.2105303 |               |                 |              |     | Longitude<br>103.9549509 |                   |              |                  | NAD<br>83      |

Is this well the defining well for the Horizontal Spacing Unit?

☐ N

Is this well an infill well?

☐ Y

If infill is yes please provide API if available, Operator Name and well number for Defining well for Horizontal Spacing Unit.

|  |  |                     |
|--|--|---------------------|
| API #<br>30-015-46703                                      |  |                     |
| Operator Name:<br>DEVON ENERGY PRODUCTION<br>COMPANY, L.P. | Property Name:<br>MR POTATO HEAD 11-14 FED COM | Well Number<br>332H |

KZ 06/29/2018



**Well:** MR POTATO HEAD 11-14 FED COM 233H

**County:** Eddy

**Wellbore:** Permit Plan

**Design:** Permit Plan #1


**Geodetic System:** US State Plane 1983

**Datum:** North American Datum 1927

**Ellipsoid:** Clarke 1866

**Zone:** 3001 - NM East (NAD83)

| MD       | INC   | AZI    | TVD     | NS        | EW      | VS       | DLS       | Comment          |
|----------|-------|--------|---------|-----------|---------|----------|-----------|------------------|
| (ft)     | (°)   | (°)    | (ft)    | (ft)      | (ft)    | (ft)     | (°/100ft) |                  |
| 0.00     | 0.00  | 0.00   | 0.00    | 0.00      | 0.00    | 0.00     | 0.00      | SHL              |
| 2000.00  | 0.00  | 65.00  | 2000.00 | 0.00      | 0.00    | 0.00     | 0.00      | Start Tangent    |
| 2500.00  | 13.00 | 65.00  | 2495.72 | 23.87     | 51.19   | -18.64   | 1.00      | Hold Tangent     |
| 6877.03  | 13.00 | 65.00  | 6760.57 | 439.99    | 943.55  | -343.59  | 0.00      | Drop to Vertical |
| 7527.03  | 0.00  | 65.00  | 7405.00 | 471.02    | 1010.10 | -367.82  | 2.00      | Hold Vertical    |
| 8567.09  | 0.00  | 180.00 | 8445.06 | 471.02    | 1010.10 | -367.82  | 0.00      | KOP              |
| 9472.15  | 90.51 | 180.00 | 9018.00 | -107.00   | 1010.10 | 207.30   | 10.00     | Landing Point    |
| 19432.97 | 90.51 | 180.00 | 8930.00 | -10067.43 | 1010.10 | 10117.98 | 0.00      | BHL              |

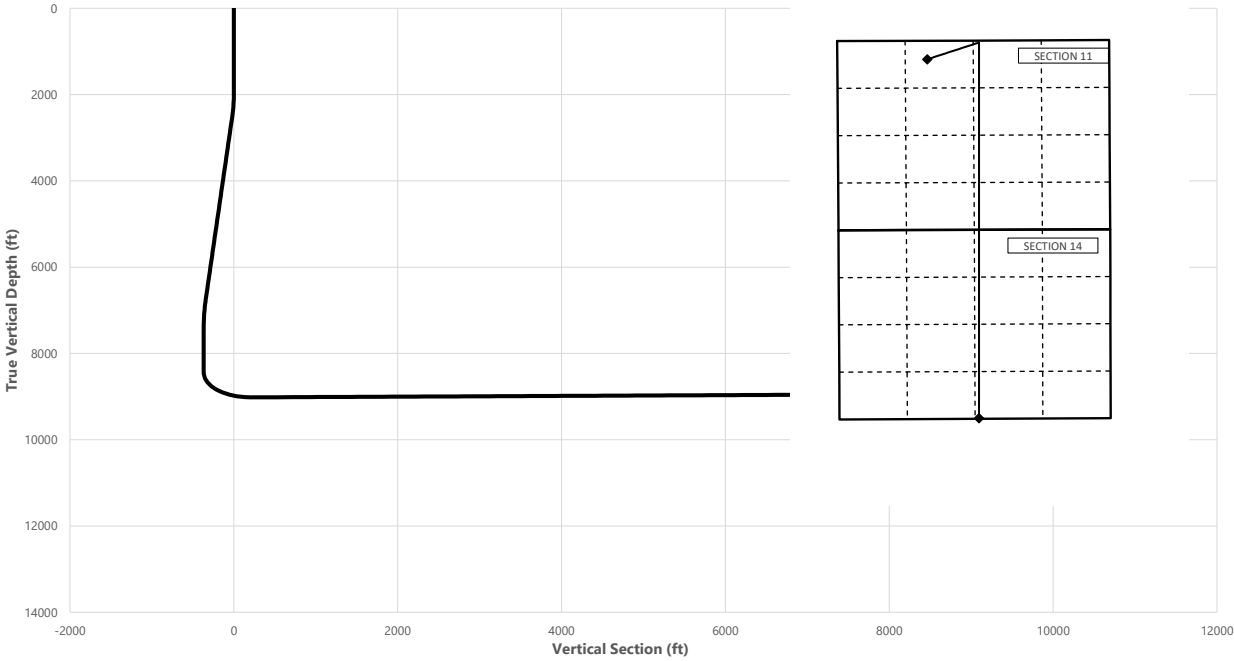

| Key Depths                        | MD       | TVD     |
|-----------------------------------|----------|---------|
|                                   | (ft)     | (ft)    |
| Rustler                           | 234.00   | 234.00  |
| Top of Salt                       | 523.00   | 523.00  |
| Base of Salt                      | 2970.33  | 2954.00 |
| Lamar                             | 3214.59  | 3192.00 |
| Bell Canyon                       | 3243.33  | 3220.00 |
| Cherry Canyon                     | 4090.03  | 4045.00 |
| Brushy Canyon                     | 5750.59  | 5663.00 |
| 1st Bone Spring Lime              | 7035.62  | 6916.00 |
| 1st Bone Spring Sand              | 8069.02  | 7947.00 |
| BONE SPRING 2ND / Point of Penetr | 8902.93  | 8762.00 |
| Exit                              | 19352.97 | 8930.72 |

|                      | MD       | TVD     | Lat     | Long      | Section Footages                            |
|----------------------|----------|---------|---------|-----------|---|
|                      | (ft)     | (ft)    | (°)     | (°)       |   |
| SHL                  | 0.00     | 0.00    | 32.2379 | -103.9582 | 520' FNL, 1756' FWL of Sec 11 in T24S, R29E |
| KOP                  | 8567.09  | 8445.06 | 32.2392 | -103.9549 | 54' FNL, 2570' FEL of Sec 11 in T24S, R29E  |
| Point of Penetration | 8902.93  | 8762.00 | 32.2392 | -103.9549 | 100' FNL, 2570' FEL of Sec 11 in T24S, R29S |
| Exit                 | 19352.97 | 8930.72 | 32.2105 | -103.9550 | 100' FSL, 2570' FEL of Sec 14 in T24S, R29E |
| BHL                  | 19432.97 | 8930.00 | 32.2102 | -103.9550 | 19' FSL, 2569' FEL of Sec 14 in T24S, R29E  |

|     | Y      | X         | MD      |
|-----|--------|-----------|---------|
| KOP | 450989 | 658363.26 | 8567.09 |

MR POTATO HEAD 11-14 FED COM 233H



**Well:** MR POTATO HEAD 11-14 FED COM 233H

**County:** Eddy

**Wellbore:** Permit Plan

**Design:** Permit Plan #1

**Geodetic System:** US State Plane 1983

**Datum:** North American Datum 1927

**Ellipsoid:** Clarke 1866

**Zone:** 3001 - NM East (NAD83)

| MD      | INC   | AZI   | TVD     | NS     | EW     | VS      | DLS       | Comment       |
|---------|-------|-------|---------|--------|--------|---------|-----------|---------------|
| (ft)    | (°)   | (°)   | (ft)    | (ft)   | (ft)   | (ft)    | (°/100ft) |               |
| 0.00    | 0.00  | 0.00  | 0.00    | 0.00   | 0.00   | 0.00    | 0.00      | SHL           |
| 100.00  | 0.00  | 65.00 | 100.00  | 0.00   | 0.00   | 0.00    | 0.00      |               |
| 200.00  | 0.00  | 65.00 | 200.00  | 0.00   | 0.00   | 0.00    | 0.00      |               |
| 234.00  | 0.00  | 65.00 | 234.00  | 0.00   | 0.00   | 0.00    | 0.00      | Rustler       |
| 300.00  | 0.00  | 65.00 | 300.00  | 0.00   | 0.00   | 0.00    | 0.00      |               |
| 400.00  | 0.00  | 65.00 | 400.00  | 0.00   | 0.00   | 0.00    | 0.00      |               |
| 500.00  | 0.00  | 65.00 | 500.00  | 0.00   | 0.00   | 0.00    | 0.00      |               |
| 523.00  | 0.00  | 65.00 | 523.00  | 0.00   | 0.00   | 0.00    | 0.00      | Top of Salt   |
| 600.00  | 0.00  | 65.00 | 600.00  | 0.00   | 0.00   | 0.00    | 0.00      |               |
| 700.00  | 0.00  | 65.00 | 700.00  | 0.00   | 0.00   | 0.00    | 0.00      |               |
| 800.00  | 0.00  | 65.00 | 800.00  | 0.00   | 0.00   | 0.00    | 0.00      |               |
| 900.00  | 0.00  | 65.00 | 900.00  | 0.00   | 0.00   | 0.00    | 0.00      |               |
| 1000.00 | 0.00  | 65.00 | 1000.00 | 0.00   | 0.00   | 0.00    | 0.00      |               |
| 1100.00 | 0.00  | 65.00 | 1100.00 | 0.00   | 0.00   | 0.00    | 0.00      |               |
| 1200.00 | 0.00  | 65.00 | 1200.00 | 0.00   | 0.00   | 0.00    | 0.00      |               |
| 1300.00 | 0.00  | 65.00 | 1300.00 | 0.00   | 0.00   | 0.00    | 0.00      |               |
| 1400.00 | 0.00  | 65.00 | 1400.00 | 0.00   | 0.00   | 0.00    | 0.00      |               |
| 1500.00 | 0.00  | 65.00 | 1500.00 | 0.00   | 0.00   | 0.00    | 0.00      |               |
| 1600.00 | 0.00  | 65.00 | 1600.00 | 0.00   | 0.00   | 0.00    | 0.00      |               |
| 1700.00 | 0.00  | 65.00 | 1700.00 | 0.00   | 0.00   | 0.00    | 0.00      |               |
| 1800.00 | 0.00  | 65.00 | 1800.00 | 0.00   | 0.00   | 0.00    | 0.00      |               |
| 1900.00 | 0.00  | 65.00 | 1900.00 | 0.00   | 0.00   | 0.00    | 0.00      |               |
| 2000.00 | 0.00  | 65.00 | 2000.00 | 0.00   | 0.00   | 0.00    | 0.00      | Start Tangent |
| 2100.00 | 2.60  | 65.00 | 2099.97 | 0.96   | 2.06   | -0.75   | 2.60      |               |
| 2200.00 | 5.20  | 65.00 | 2199.73 | 3.83   | 8.22   | -2.99   | 2.60      |               |
| 2300.00 | 7.80  | 65.00 | 2299.07 | 8.62   | 18.48  | -6.73   | 2.60      |               |
| 2400.00 | 10.40 | 65.00 | 2397.81 | 15.30  | 32.81  | -11.95  | 2.60      |               |
| 2500.00 | 13.00 | 65.00 | 2495.72 | 23.87  | 51.19  | -18.64  | 1.00      | Hold Tangent  |
| 2600.00 | 13.00 | 65.00 | 2593.16 | 33.38  | 71.58  | -26.06  | 0.00      |               |
| 2700.00 | 13.00 | 65.00 | 2690.60 | 42.88  | 91.96  | -33.49  | 0.00      |               |
| 2800.00 | 13.00 | 65.00 | 2788.03 | 52.39  | 112.35 | -40.91  | 0.00      |               |
| 2900.00 | 13.00 | 65.00 | 2885.47 | 61.90  | 132.74 | -48.34  | 0.00      |               |
| 2970.33 | 13.00 | 65.00 | 2954.00 | 68.58  | 147.08 | -53.56  | 0.00      | Base of Salt  |
| 3000.00 | 13.00 | 65.00 | 2982.91 | 71.40  | 153.13 | -55.76  | 0.00      |               |
| 3100.00 | 13.00 | 65.00 | 3080.34 | 80.91  | 173.51 | -63.18  | 0.00      |               |
| 3200.00 | 13.00 | 65.00 | 3177.78 | 90.42  | 193.90 | -70.61  | 0.00      |               |
| 3214.59 | 13.00 | 65.00 | 3192.00 | 91.81  | 196.88 | -71.69  | 0.00      | Lamar         |
| 3243.33 | 13.00 | 65.00 | 3220.00 | 94.54  | 202.73 | -73.82  | 0.00      | Bell Canyon   |
| 3300.00 | 13.00 | 65.00 | 3275.22 | 99.92  | 214.29 | -78.03  | 0.00      |               |
| 3400.00 | 13.00 | 65.00 | 3372.65 | 109.43 | 234.68 | -85.46  | 0.00      |               |
| 3500.00 | 13.00 | 65.00 | 3470.09 | 118.94 | 255.06 | -92.88  | 0.00      |               |
| 3600.00 | 13.00 | 65.00 | 3567.53 | 128.44 | 275.45 | -100.30 | 0.00      |               |
| 3700.00 | 13.00 | 65.00 | 3664.97 | 137.95 | 295.84 | -107.73 | 0.00      |               |
| 3800.00 | 13.00 | 65.00 | 3762.40 | 147.46 | 316.23 | -115.15 | 0.00      |               |
| 3900.00 | 13.00 | 65.00 | 3859.84 | 156.97 | 336.61 | -122.58 | 0.00      |               |
| 4000.00 | 13.00 | 65.00 | 3957.28 | 166.47 | 357.00 | -130.00 | 0.00      |               |
| 4090.03 | 13.00 | 65.00 | 4045.00 | 175.03 | 375.36 | -136.68 | 0.00      | Cherry Canyon |
| 4100.00 | 13.00 | 65.00 | 4054.71 | 175.98 | 377.39 | -137.42 | 0.00      |               |
| 4200.00 | 13.00 | 65.00 | 4152.15 | 185.49 | 397.78 | -144.85 | 0.00      |               |
| 4300.00 | 13.00 | 65.00 | 4249.59 | 194.99 | 418.16 | -152.27 | 0.00      |               |
| 4400.00 | 13.00 | 65.00 | 4347.02 | 204.50 | 438.55 | -159.70 | 0.00      |               |
| 4500.00 | 13.00 | 65.00 | 4444.46 | 214.01 | 458.94 | -167.12 | 0.00      |               |
| 4600.00 | 13.00 | 65.00 | 4541.90 | 223.51 | 479.33 | -174.54 | 0.00      |               |
| 4700.00 | 13.00 | 65.00 | 4639.34 | 233.02 | 499.71 | -181.97 | 0.00      |               |
| 4800.00 | 13.00 | 65.00 | 4736.77 | 242.53 | 520.10 | -189.39 | 0.00      |               |
| 4900.00 | 13.00 | 65.00 | 4834.21 | 252.03 | 540.49 | -196.82 | 0.00      |               |
| 5000.00 | 13.00 | 65.00 | 4931.65 | 261.54 | 560.88 | -204.24 | 0.00      |               |
| 5100.00 | 13.00 | 65.00 | 5029.08 | 271.05 | 581.26 | -211.66 | 0.00      |               |
| 5200.00 | 13.00 | 65.00 | 5126.52 | 280.55 | 601.65 | -219.09 | 0.00      |               |
| 5300.00 | 13.00 | 65.00 | 5223.96 | 290.06 | 622.04 | -226.51 | 0.00      |               |
| 5400.00 | 13.00 | 65.00 | 5321.39 | 299.57 | 642.42 | -233.94 | 0.00      |               |
| 5500.00 | 13.00 | 65.00 | 5418.83 | 309.08 | 662.81 | -241.36 | 0.00      |               |
| 5600.00 | 13.00 | 65.00 | 5516.27 | 318.58 | 683.20 | -248.78 | 0.00      |               |
| 5700.00 | 13.00 | 65.00 | 5613.71 | 328.09 | 703.59 | -256.21 | 0.00      |               |
| 5750.59 | 13.00 | 65.00 | 5663.00 | 332.90 | 713.90 | -259.96 | 0.00      | Brushy Canyon |
| 5800.00 | 13.00 | 65.00 | 5711.14 | 337.60 | 723.97 | -263.63 | 0.00      |               |
| 5900.00 | 13.00 | 65.00 | 5808.58 | 347.10 | 744.36 | -271.06 | 0.00      |               |
| 6000.00 | 13.00 | 65.00 | 5906.02 | 356.61 | 764.75 | -278.48 | 0.00      |               |
| 6100.00 | 13.00 | 65.00 | 6003.45 | 366.12 | 785.14 | -285.90 | 0.00      |               |
| 6200.00 | 13.00 | 65.00 | 6100.89 | 375.62 | 805.52 | -293.33 | 0.00      |               |

MR POTATO HEAD 11-14 FED COM 233H



Well: MR POTATO HEAD 11-14 FED COM 233H

County: Eddy

Wellbore: Permit Plan

Design: Permit Plan #1

Geodetic System: US State Plane 1983

Datum: North American Datum 1927

Ellipsoid: Clarke 1866

Zone: 3001 - NM East (NAD83)

| MD<br>(ft) | INC<br>(°) | AZI<br>(°) | TVD<br>(ft) | NS<br>(ft) | EW<br>(ft) | VS<br>(ft) | DLS<br>(°/100ft) | Comment                                |
|------------|------------|------------|-------------|------------|------------|------------|------------------|--|
| 6300.00    | 13.00      | 65.00      | 6198.33     | 385.13     | 825.91     | -300.75    | 0.00             |  |
| 6400.00    | 13.00      | 65.00      | 6295.76     | 394.64     | 846.30     | -308.18    | 0.00             |  |
| 6500.00    | 13.00      | 65.00      | 6393.20     | 404.14     | 866.69     | -315.60    | 0.00             |  |
| 6600.00    | 13.00      | 65.00      | 6490.64     | 413.65     | 887.07     | -323.02    | 0.00             |  |
| 6700.00    | 13.00      | 65.00      | 6588.08     | 423.16     | 907.46     | -330.45    | 0.00             |  |
| 6800.00    | 13.00      | 65.00      | 6685.51     | 432.66     | 927.85     | -337.87    | 0.00             |  |
| 6877.03    | 13.00      | 65.00      | 6760.57     | 439.99     | 943.55     | -343.59    | 0.00             | Drop to Vertical                       |
| 6900.00    | 12.54      | 65.00      | 6782.97     | 442.13     | 948.16     | -345.27    | 2.00             |  |
| 7000.00    | 10.54      | 65.00      | 6880.94     | 450.59     | 966.29     | -351.87    | 2.00             |  |
| 7035.62    | 9.83       | 65.00      | 6916.00     | 453.25     | 972.00     | -353.95    | 2.00             | 1st Bone Spring Lime                   |
| 7100.00    | 8.54       | 65.00      | 6979.55     | 457.59     | 981.31     | -357.34    | 2.00             |  |
| 7200.00    | 6.54       | 65.00      | 7078.69     | 463.14     | 993.20     | -361.67    | 2.00             |  |
| 7300.00    | 4.54       | 65.00      | 7178.21     | 467.22     | 1001.95    | -364.86    | 2.00             |  |
| 7400.00    | 2.54       | 65.00      | 7278.02     | 469.83     | 1007.55    | -366.89    | 2.00             |  |
| 7500.00    | 0.54       | 65.00      | 7377.98     | 470.96     | 1009.98    | -367.78    | 2.00             |  |
| 7527.03    | 0.00       | 65.00      | 7405.00     | 471.02     | 1010.10    | -367.82    | 2.00             | Hold Vertical                          |
| 7600.00    | 0.00       | 180.00     | 7477.98     | 471.02     | 1010.10    | -367.82    | 0.00             |  |
| 7700.00    | 0.00       | 180.00     | 7577.98     | 471.02     | 1010.10    | -367.82    | 0.00             |  |
| 7800.00    | 0.00       | 180.00     | 7677.98     | 471.02     | 1010.10    | -367.82    | 0.00             |  |
| 7900.00    | 0.00       | 180.00     | 7777.98     | 471.02     | 1010.10    | -367.82    | 0.00             |  |
| 8000.00    | 0.00       | 180.00     | 7877.98     | 471.02     | 1010.10    | -367.82    | 0.00             |  |
| 8069.02    | 0.00       | 180.00     | 7947.00     | 471.02     | 1010.10    | -367.82    | 0.00             | 1st Bone Spring Sand                   |
| 8100.00    | 0.00       | 180.00     | 7977.98     | 471.02     | 1010.10    | -367.82    | 0.00             |  |
| 8200.00    | 0.00       | 180.00     | 8077.98     | 471.02     | 1010.10    | -367.82    | 0.00             |  |
| 8300.00    | 0.00       | 180.00     | 8177.98     | 471.02     | 1010.10    | -367.82    | 0.00             |  |
| 8400.00    | 0.00       | 180.00     | 8277.98     | 471.02     | 1010.10    | -367.82    | 0.00             |  |
| 8500.00    | 0.00       | 180.00     | 8377.98     | 471.02     | 1010.10    | -367.82    | 0.00             |  |
| 8567.09    | 0.00       | 180.00     | 8445.06     | 471.02     | 1010.10    | -367.82    | 0.00             | KOP                                    |
| 8600.00    | 3.29       | 180.00     | 8477.96     | 470.07     | 1010.10    | -366.88    | 10.00            |  |
| 8700.00    | 13.29      | 180.00     | 8576.79     | 455.67     | 1010.10    | -352.55    | 10.00            |  |
| 8800.00    | 23.29      | 180.00     | 8671.61     | 424.33     | 1010.10    | -321.36    | 10.00            |  |
| 8900.00    | 33.29      | 180.00     | 8759.56     | 376.99     | 1010.10    | -274.27    | 10.00            |  |
| 8902.93    | 33.58      | 180.00     | 8762.00     | 375.38     | 1010.10    | -272.66    | 10.00            | BONE SPRING 2ND / Point of Penetration |
| 9000.00    | 43.29      | 180.00     | 8837.94     | 315.10     | 1010.10    | -212.69    | 10.00            |  |
| 9100.00    | 53.29      | 180.00     | 8904.39     | 240.54     | 1010.10    | -138.50    | 10.00            |  |
| 9200.00    | 63.29      | 180.00     | 8956.89     | 155.58     | 1010.10    | -53.96     | 10.00            |  |
| 9300.00    | 73.29      | 180.00     | 8993.83     | 62.79      | 1010.10    | 38.37      | 10.00            |  |
| 9400.00    | 83.29      | 180.00     | 9014.10     | -35.00     | 1010.10    | 135.67     | 10.00            |  |
| 9472.15    | 90.51      | 180.00     | 9018.00     | -107.00    | 1010.10    | 207.30     | 10.00            | Landing Point                          |
| 9500.00    | 90.51      | 180.00     | 9017.75     | -134.85    | 1010.10    | 235.02     | 0.00             |  |
| 9600.00    | 90.51      | 180.00     | 9016.87     | -234.85    | 1010.10    | 334.52     | 0.00             |  |
| 9700.00    | 90.51      | 180.00     | 9015.99     | -334.84    | 1010.10    | 434.01     | 0.00             |  |
| 9800.00    | 90.51      | 180.00     | 9015.10     | -434.84    | 1010.10    | 533.51     | 0.00             |  |
| 9900.00    | 90.51      | 180.00     | 9014.22     | -534.83    | 1010.10    | 633.00     | 0.00             |  |
| 10000.00   | 90.51      | 180.00     | 9013.34     | -634.83    | 1010.10    | 732.50     | 0.00             |  |
| 10100.00   | 90.51      | 180.00     | 9012.45     | -734.83    | 1010.10    | 832.00     | 0.00             |  |
| 10200.00   | 90.51      | 180.00     | 9011.57     | -834.82    | 1010.10    | 931.49     | 0.00             |  |
| 10300.00   | 90.51      | 180.00     | 9010.69     | -934.82    | 1010.10    | 1030.99    | 0.00             |  |
| 10400.00   | 90.51      | 180.00     | 9009.80     | -1034.82   | 1010.10    | 1130.49    | 0.00             |  |
| 10500.00   | 90.51      | 180.00     | 9008.92     | -1134.81   | 1010.10    | 1229.98    | 0.00             |  |
| 10600.00   | 90.51      | 180.00     | 9008.04     | -1234.81   | 1010.10    | 1329.48    | 0.00             |  |
| 10700.00   | 90.51      | 180.00     | 9007.15     | -1334.80   | 1010.10    | 1428.98    | 0.00             |  |
| 10800.00   | 90.51      | 180.00     | 9006.27     | -1434.80   | 1010.10    | 1528.47    | 0.00             |  |
| 10900.00   | 90.51      | 180.00     | 9005.39     | -1534.80   | 1010.10    | 1627.97    | 0.00             |  |
| 11000.00   | 90.51      | 180.00     | 9004.50     | -1634.79   | 1010.10    | 1727.47    | 0.00             |  |
| 11100.00   | 90.51      | 180.00     | 9003.62     | -1734.79   | 1010.10    | 1826.96    | 0.00             |  |
| 11200.00   | 90.51      | 180.00     | 9002.74     | -1834.78   | 1010.10    | 1926.46    | 0.00             |  |
| 11300.00   | 90.51      | 180.00     | 9001.85     | -1934.78   | 1010.10    | 2025.96    | 0.00             |  |
| 11400.00   | 90.51      | 180.00     | 9000.97     | -2034.78   | 1010.11    | 2125.45    | 0.00             |  |
| 11500.00   | 90.51      | 180.00     | 9000.09     | -2134.77   | 1010.11    | 2224.95    | 0.00             |  |
| 11600.00   | 90.51      | 180.00     | 8999.20     | -2234.77   | 1010.11    | 2324.45    | 0.00             |  |
| 11700.00   | 90.51      | 180.00     | 8998.32     | -2334.76   | 1010.11    | 2423.94    | 0.00             |  |
| 11800.00   | 90.51      | 180.00     | 8997.44     | -2434.76   | 1010.11    | 2523.44    | 0.00             |  |
| 11900.00   | 90.51      | 180.00     | 8996.55     | -2534.76   | 1010.11    | 2622.94    | 0.00             |  |
| 12000.00   | 90.51      | 180.00     | 8995.67     | -2634.75   | 1010.11    | 2722.43    | 0.00             |  |
| 12100.00   | 90.51      | 180.00     | 8994.79     | -2734.75   | 1010.11    | 2821.93    | 0.00             |  |
| 12200.00   | 90.51      | 180.00     | 8993.90     | -2834.75   | 1010.11    | 2921.43    | 0.00             |  |
| 12300.00   | 90.51      | 180.00     | 8993.02     | -2934.74   | 1010.11    | 3020.92    | 0.00             |  |
| 12400.00   | 90.51      | 180.00     | 8992.14     | -3034.74   | 1010.11    | 3120.42    | 0.00             |  |
| 12500.00   | 90.51      | 180.00     | 8991.25     | -3134.73   | 1010.11    | 3219.92    | 0.00             |  |

MR POTATO HEAD 11-14 FED COM 233H



Well: MR POTATO HEAD 11-14 FED COM 233H  
County: Eddy  
Wellbore: Permit Plan  
Design: Permit Plan #1

Geodetic System: US State Plane 1983  
Datum: North American Datum 1927  
Ellipsoid: Clarke 1866  
Zone: 3001 - NM East (NAD83)

| MD       | INC   | AZI    | TVD     | NS       | EW      | VS       | DLS       | Comment    |
|----------|-------|--------|---------|----------|---------|----------|-----------|------------|
| (ft)     | (°)   | (°)    | (ft)    | (ft)     | (ft)    | (ft)     | (°/100ft) |            |
| 12600.00 | 90.51 | 180.00 | 8990.37 | -3234.73 | 1010.11 | 3319.41  | 0.00      |            |
| 12700.00 | 90.51 | 180.00 | 8989.49 | -3334.73 | 1010.11 | 3418.91  | 0.00      |            |
| 12800.00 | 90.51 | 180.00 | 8988.60 | -3434.72 | 1010.11 | 3518.41  | 0.00      |            |
| 12900.00 | 90.51 | 180.00 | 8987.72 | -3534.72 | 1010.11 | 3617.90  | 0.00      |            |
| 13000.00 | 90.51 | 180.00 | 8986.84 | -3634.71 | 1010.11 | 3717.40  | 0.00      |            |
| 13100.00 | 90.51 | 180.00 | 8985.95 | -3734.71 | 1010.11 | 3816.89  | 0.00      |            |
| 13200.00 | 90.51 | 180.00 | 8985.07 | -3834.71 | 1010.11 | 3916.39  | 0.00      |            |
| 13300.00 | 90.51 | 180.00 | 8984.19 | -3934.70 | 1010.11 | 4015.89  | 0.00      |            |
| 13400.00 | 90.51 | 180.00 | 8983.30 | -4034.70 | 1010.11 | 4115.38  | 0.00      |            |
| 13500.00 | 90.51 | 180.00 | 8982.42 | -4134.69 | 1010.11 | 4214.88  | 0.00      |            |
| 13600.00 | 90.51 | 180.00 | 8981.54 | -4234.69 | 1010.11 | 4314.38  | 0.00      |            |
| 13700.00 | 90.51 | 180.00 | 8980.65 | -4334.69 | 1010.11 | 4413.87  | 0.00      |            |
| 13800.00 | 90.51 | 180.00 | 8979.77 | -4434.68 | 1010.11 | 4513.37  | 0.00      |            |
| 13900.00 | 90.51 | 180.00 | 8978.89 | -4534.68 | 1010.11 | 4612.87  | 0.00      |            |
| 13988.00 | 90.51 | 180.00 | 8978.11 | -4622.68 | 1010.11 | 4700.42  | 0.00      | NMNM085892 |
| 14000.00 | 90.51 | 180.00 | 8978.00 | -4634.68 | 1010.11 | 4712.36  | 0.00      |            |
| 14100.00 | 90.51 | 180.00 | 8977.12 | -4734.67 | 1010.11 | 4811.86  | 0.00      |            |
| 14200.00 | 90.51 | 180.00 | 8976.24 | -4834.67 | 1010.11 | 4911.36  | 0.00      |            |
| 14300.00 | 90.51 | 180.00 | 8975.35 | -4934.66 | 1010.11 | 5010.85  | 0.00      |            |
| 14400.00 | 90.51 | 180.00 | 8974.47 | -5034.66 | 1010.11 | 5110.35  | 0.00      |            |
| 14500.00 | 90.51 | 180.00 | 8973.59 | -5134.66 | 1010.11 | 5209.85  | 0.00      |            |
| 14600.00 | 90.51 | 180.00 | 8972.70 | -5234.65 | 1010.11 | 5309.34  | 0.00      |            |
| 14700.00 | 90.51 | 180.00 | 8971.82 | -5334.65 | 1010.11 | 5408.84  | 0.00      |            |
| 14800.00 | 90.51 | 180.00 | 8970.94 | -5434.64 | 1010.11 | 5508.34  | 0.00      |            |
| 14900.00 | 90.51 | 180.00 | 8970.05 | -5534.64 | 1010.11 | 5607.83  | 0.00      |            |
| 15000.00 | 90.51 | 180.00 | 8969.17 | -5634.64 | 1010.11 | 5707.33  | 0.00      |            |
| 15100.00 | 90.51 | 180.00 | 8968.29 | -5734.63 | 1010.11 | 5806.83  | 0.00      |            |
| 15200.00 | 90.51 | 180.00 | 8967.40 | -5834.63 | 1010.12 | 5906.32  | 0.00      |            |
| 15300.00 | 90.51 | 180.00 | 8966.52 | -5934.62 | 1010.12 | 6005.82  | 0.00      |            |
| 15400.00 | 90.51 | 180.00 | 8965.64 | -6034.62 | 1010.12 | 6105.32  | 0.00      |            |
| 15500.00 | 90.51 | 180.00 | 8964.75 | -6134.62 | 1010.12 | 6204.81  | 0.00      |            |
| 15600.00 | 90.51 | 180.00 | 8963.87 | -6234.61 | 1010.12 | 6304.31  | 0.00      |            |
| 15700.00 | 90.51 | 180.00 | 8962.99 | -6334.61 | 1010.12 | 6403.81  | 0.00      |            |
| 15800.00 | 90.51 | 180.00 | 8962.10 | -6434.60 | 1010.12 | 6503.30  | 0.00      |            |
| 15900.00 | 90.51 | 180.00 | 8961.22 | -6534.60 | 1010.12 | 6602.80  | 0.00      |            |
| 16000.00 | 90.51 | 180.00 | 8960.34 | -6634.60 | 1010.12 | 6702.30  | 0.00      |            |
| 16100.00 | 90.51 | 180.00 | 8959.45 | -6734.59 | 1010.12 | 6801.79  | 0.00      |            |
| 16200.00 | 90.51 | 180.00 | 8958.57 | -6834.59 | 1010.12 | 6901.29  | 0.00      |            |
| 16300.00 | 90.51 | 180.00 | 8957.69 | -6934.59 | 1010.12 | 7000.78  | 0.00      |            |
| 16400.00 | 90.51 | 180.00 | 8956.80 | -7034.58 | 1010.12 | 7100.28  | 0.00      |            |
| 16500.00 | 90.51 | 180.00 | 8955.92 | -7134.58 | 1010.12 | 7199.78  | 0.00      |            |
| 16600.00 | 90.51 | 180.00 | 8955.04 | -7234.57 | 1010.12 | 7299.27  | 0.00      |            |
| 16700.00 | 90.51 | 180.00 | 8954.15 | -7334.57 | 1010.12 | 7398.77  | 0.00      |            |
| 16800.00 | 90.51 | 180.00 | 8953.27 | -7434.57 | 1010.12 | 7498.27  | 0.00      |            |
| 16900.00 | 90.51 | 180.00 | 8952.39 | -7534.56 | 1010.12 | 7597.76  | 0.00      |            |
| 17000.00 | 90.51 | 180.00 | 8951.50 | -7634.56 | 1010.12 | 7697.26  | 0.00      |            |
| 17100.00 | 90.51 | 180.00 | 8950.62 | -7734.55 | 1010.12 | 7796.76  | 0.00      |            |
| 17200.00 | 90.51 | 180.00 | 8949.74 | -7834.55 | 1010.12 | 7896.25  | 0.00      |            |
| 17300.00 | 90.51 | 180.00 | 8948.85 | -7934.55 | 1010.12 | 7995.75  | 0.00      |            |
| 17400.00 | 90.51 | 180.00 | 8947.97 | -8034.54 | 1010.12 | 8095.25  | 0.00      |            |
| 17500.00 | 90.51 | 180.00 | 8947.09 | -8134.54 | 1010.12 | 8194.74  | 0.00      |            |
| 17600.00 | 90.51 | 180.00 | 8946.20 | -8234.53 | 1010.12 | 8294.24  | 0.00      |            |
| 17700.00 | 90.51 | 180.00 | 8945.32 | -8334.53 | 1010.12 | 8393.74  | 0.00      |            |
| 17800.00 | 90.51 | 180.00 | 8944.44 | -8434.53 | 1010.12 | 8493.23  | 0.00      |            |
| 17900.00 | 90.51 | 180.00 | 8943.55 | -8534.52 | 1010.12 | 8592.73  | 0.00      |            |
| 18000.00 | 90.51 | 180.00 | 8942.67 | -8634.52 | 1010.12 | 8692.23  | 0.00      |            |
| 18100.00 | 90.51 | 180.00 | 8941.79 | -8734.52 | 1010.12 | 8791.72  | 0.00      |            |
| 18200.00 | 90.51 | 180.00 | 8940.90 | -8834.51 | 1010.12 | 8891.22  | 0.00      |            |
| 18300.00 | 90.51 | 180.00 | 8940.02 | -8934.51 | 1010.12 | 8990.72  | 0.00      |            |
| 18400.00 | 90.51 | 180.00 | 8939.14 | -9034.50 | 1010.12 | 9090.21  | 0.00      |            |
| 18500.00 | 90.51 | 180.00 | 8938.25 | -9134.50 | 1010.12 | 9189.71  | 0.00      |            |
| 18600.00 | 90.51 | 180.00 | 8937.37 | -9234.50 | 1010.12 | 9289.21  | 0.00      |            |
| 18700.00 | 90.51 | 180.00 | 8936.49 | -9334.49 | 1010.12 | 9388.70  | 0.00      |            |
| 18800.00 | 90.51 | 180.00 | 8935.60 | -9434.49 | 1010.12 | 9488.20  | 0.00      |            |
| 18900.00 | 90.51 | 180.00 | 8934.72 | -9534.48 | 1010.13 | 9587.70  | 0.00      |            |
| 19000.00 | 90.51 | 180.00 | 8933.84 | -9634.48 | 1010.13 | 9687.19  | 0.00      |            |
| 19100.00 | 90.51 | 180.00 | 8932.95 | -9734.48 | 1010.13 | 9786.69  | 0.00      |            |
| 19200.00 | 90.51 | 180.00 | 8932.07 | -9834.47 | 1010.13 | 9886.19  | 0.00      |            |
| 19300.00 | 90.51 | 180.00 | 8931.19 | -9934.47 | 1010.13 | 9985.68  | 0.00      |            |
| 19352.97 | 90.51 | 180.00 | 8930.72 | -9987.43 | 1010.13 | 10038.38 | 0.00      | Exit       |

devon

Well: MR POTATO HEAD 11-14 FED COM 233H

County: Eddy

Wellbore: Permit Plan

Design: Permit Plan #1

Geodetic System: US State Plane 1983

Datum: North American Datum 1927

Ellipsoid: Clarke 1866

Zone: 3001 - NM East (NAD83)

| MD       | INC   | AZI    | TVD     | NS        | EW      | VS       | DLS       | Comment |
|----------|-------|--------|---------|-----------|---------|----------|-----------|---------|
| (ft)     | (°)   | (°)    | (ft)    | (ft)      | (ft)    | (ft)     | (°/100ft) |         |
| 19400.00 | 90.51 | 180.00 | 8930.30 | -10034.46 | 1010.13 | 10085.18 | 0.00      |         |
| 19432.97 | 90.51 | 180.00 | 8930.00 | -10067.43 | 1010.10 | 10117.98 | 0.00      | BHL     |

MR POTATO HEAD 11-14 FED COM 233H

1. Geologic Formations

|               |       |                              |     |
|---------------|-------|------------------------------|-----|
| TVD of target | 8930  | Pilot hole depth             | N/A |
| MD at TD:     | 19433 | Deepest expected fresh water |     |

Basin

| Formation            | Depth (TVD) from KB | Water/Mineral Bearing/Target Zone? | Hazards* |
|----------------------|---------------------|------------------------------------|----------|
| Rustler              | 234                 |                                    |          |
| Top of Salt          | 523                 |                                    |          |
| Base of Salt         | 2954                |                                    |          |
| Lamar                | 3192                |                                    |          |
| Bell Canyon          | 3220                |                                    |          |
| Cherry Canyon        | 4045                |                                    |          |
| Brushy Canyon        | 5663                |                                    |          |
| 1st Bone Spring Lime | 6916                |                                    |          |
| 1st Bone Spring Sand | 7947                |                                    |          |
| BONE SPRING 2ND      | 8762                |                                    |          |
|                      |                     |                                    |          |
|                      |                     |                                    |          |
|                      |                     |                                    |          |
|                      |                     |                                    |          |
|                      |                     |                                    |          |
|                      |                     |                                    |          |
|                      |                     |                                    |          |
|                      |                     |                                    |          |

\*H2S, water flows, loss of circulation, abnormal pressures, etc.



MR POTATO HEAD 11-14 FED COM 233H

2. Casing Program

| Hole Size | Csg. Size | Wt (PPF) | Grade   | Conn | Casing Interval |         | Casing Interval |          |
|-----------|-----------|----------|---------|------|-----------------|---------|-----------------|----------|
|           |           |          |         |      | From (MD)       | To (MD) | From (TVD)      | To (TVD) |
| 17 1/2    | 13 3/8    | 54 1/2   | J-55    | BTC  | 0               | 259     | 0               | 259      |
| 12 1/4    | 9 5/8     | 40       | J-55    | BTC  | 0               | 3054    | 0               | 3054     |
| 8 3/4     | 5 1/2     | 20       | P110ICY | TXP  | 0               | 19433   | 0               | 8930     |

- All casing strings will be tested in accordance with Onshore Oil and Gas Order #2 IILB.1.h Must have table for contingency casing.

## MR POTATO HEAD 11-14 FED COM 233H

**3. Cementing Program (3-String Primary Design)**

| Casing                           | # Sks | TOC  | Wt.<br>(lb/gal) | Yld<br>(ft <sup>3</sup> /sack) | Slurry Description                       |
|----------------------------------|-------|------|-----------------|--------------------------------|--|
| Surface                          | 225   | Surf | 13.2            | 1.4                            | Lead: Class C Cement + additives         |
| Int 1                            | 314   | Surf | 9.0             | 3.3                            | Lead: Class C Cement + additives         |
|                                  | 154   | 2554 | 13.2            | 1.4                            | Tail: Class H / C + additives            |
| Int 1<br>Intermediate<br>Squeeze | 408   | Surf | 9.0             | 3.3                            | Squeeze Lead: Class C Cement + additives |
|                                  | 314   | Surf | 9.0             | 3.3                            | Lead: Class C Cement + additives         |
|                                  | 154   | 2554 | 13.2            | 1.4                            | Tail: Class H / C + additives            |
| Production                       | 512   | 2554 | 9.0             | 3.3                            | Lead: Class H / C + additives            |
|                                  | 2097  | 8567 | 13.2            | 1.4                            | Tail: Class H / C + additives            |

If a DV tool is ran the depth(s) will be adjusted based on hole conditions and cement volumes will be adjusted proportionally. Slurry weights will be adjusted based on estimated fracture gradient of the formation. DV tool will be set a minimum of 50 feet below previous casing and a minimum of 200 feet above current shoe. If cement is not returned to surface during the primary cement job on the surface casing string, a planned top job will be conducted immediately after completion of the primary job.

| Casing String | % Excess |
|---------------|----------|
| Surface       | 50%      |
| Intermediate  | 30%      |
| Production    | 10%      |

Devon Energy requests to offline cement on intermediate strings that are set in formations shallower than the Wolfcamp. Prior to commencing offline cementing operations, the well will be monitored for any abnormal pressures and confirmed to be static. A dual manifold system (equipped with chokes) for the returns will also be utilized as a redundancy. All equipment used for offline cementing will have a minimum 5M rating to match intermediate sections' 5M BOPE requirements.

4. Pressure Control Equipment (Three String Design)

| BOP installed and tested before drilling which hole? | Size?   | Min. Required WP | Type               | ✓ | Tested to:                    |
|--|---------|------------------|--------------------|---|-------------------------------|
| Int 1  | 13-58"  | 5M               | Annular            | X | 50% of rated working pressure |
|  |         |                  | Blind Ram          | X | 5M                            |
|  |         |                  | Pipe Ram           |   |                               |
|  |         |                  | Double Ram         | X |                               |
|  |         |                  | Other* <div></div> |   |                               |
| Production   | 13-5/8" | 5M               | Annular            | X | 50% of rated working pressure |
|  |         |                  | Blind Ram          | X | 5M                            |
|  |         |                  | Pipe Ram           |   |                               |
|  |         |                  | Double Ram         | X |                               |
|  |         |                  | Other* <div></div> |   |                               |
|  |         |                  | Annular (5M)       |   |                               |
|  |         |                  | Blind Ram          |   |                               |
|  |         |                  | Pipe Ram           |   |                               |
|  |         |                  | Double Ram         |   |                               |
|  |         |                  | Other* <div></div> |   |                               |

## MR POTATO HEAD 11-14 FED COM 233H

**5. Mud Program (Three String Design)**

| Section      | Type   | Weight (ppg) |
|--------------|--------|--------------|
| Surface      | FW Gel | 8.5-9        |
| Intermediate | Brine  | 10-10.5      |
| Production   | WBM    | 8.5-9        |

Sufficient mud materials to maintain mud properties and meet minimum lost circulation and weight increase requirements will be kept on location at all times.

|   |                             |
|---|-----------------------------|
| What will be used to monitor the loss or gain of fluid? | PVT/Pason/Visual Monitoring |
|---|-----------------------------|

**6. Logging and Testing Procedures**

| Logging, Coring and Testing |   |
|-----------------------------|---|
| X                           | Will run GR/CNL from TD to surface (horizontal well - vertical portion of hole). Stated logs run will be in the Completion Report and submitted to the BLM. |
|                             | No logs are planned based on well control or offset log information.  |
|                             | Drill stem test? If yes, explain.   |
|                             | Coring? If yes, explain.  |

| Additional logs planned |             | Interval          |
|-------------------------|-------------|-------------------|
|                         | Resistivity |                   |
|                         | Density     |                   |
| X                       | CBL         | Production casing |
| X                       | Mud log     | KOP to TD         |
|                         | PEX         |                   |

**7. Drilling Conditions**

| Condition                  | Specify what type and where? |
|----------------------------|------------------------------|
| BH pressure at deepest TVD | 4179                         |
| Abnormal temperature       | No                           |

Mitigation measure for abnormal conditions. Describe. Lost circulation material/sweeps/mud scavengers.

Hydrogen Sulfide (H<sub>2</sub>S) monitors will be installed prior to drilling out the surface shoe. If H<sub>2</sub>S is detected in concentrations greater than 100 ppm, the operator will comply with the provisions of Onshore Oil and Gas Order #6. If Hydrogen Sulfide is encountered measured values and formations will be provided to the BLM.

|   |                                 |
|---|---------------------------------|
| N | H <sub>2</sub> S is present     |
| Y | H <sub>2</sub> S plan attached. |

## MR POTATO HEAD 11-14 FED COM 233H

**8. Other facets of operation**

Is this a walking operation? Potentially

- 1 If operator elects, drilling rig will batch drill the surface holes and run/cement surface casing; walking the rig to next wells on the pad.
- 2 The drilling rig will then batch drill the intermediate sections and run/cement intermediate casing; the wellbore will be isolated with a blind flange and pressure gauge installed for monitoring the well before walking to the next well.
- 3 The drilling rig will then batch drill the production hole sections on the wells with OBM, run/cement production casing, and install TA caps or tubing heads for completions.

NOTE: During batch operations the drilling rig will be moved from well to well however, it will not be removed from the pad until all wells have production casing run/cemented.

Will be pre-setting casing? Potentially

- 1 Spudder rig will move in and batch drill surface hole.
  - a. Rig will utilize fresh water based mud to drill surface hole to TD. Solids control will be handled entirely on a closed loop basis.
- 2 After drilling the surface hole section, the spudder rig will run casing and cement following all of the applicable rules and regulations (OnShore Order 2, all COAs and NMOCD regulations).
- 3 The wellhead will be installed and tested once the surface casing is cut off and the WOC time has been reached.
- 4 A blind flange with the same pressure rating as the wellhead will be installed to seal the wellbore. Pressure will be monitored with a pressure gauge installed on the wellhead.
- 5 Spudder rig operations is expected to take 4-5 days per well on a multi-well pad.
- 6 The NMOCD will be contacted and notified 24 hours prior to commencing spudder rig operations.
- 7 Drilling operations will be performed with drilling rig. At that time an approved BOP stack will be nipped up and tested on the wellhead before drilling operations commences on each well.
  - a. The NMOCD will be contacted / notified 24 hours before the drilling rig moves back on to the pad with the pre-set surface casing.

Attachments


X Directional Plan  
           Other, describe

**MR POTATO HEAD 11 WELLPAD 3 (AA000152498)  
DEVON ENERGY PRODUCTION COMPANY, L.P.**

**IN THE N/2 NE/4 NW/4 OF  
SECTION 11, TOWNSHIP 24 SOUTH, RANGE 29 EAST, N.M.P.M.  
EDDY COUNTY, STATE OF NEW MEXICO  
MARCH 25, 2024**

**SITE MAP**

- |  |  |
|--|--|
| Ⓐ EXISTING<br>MR POTATO HEAD<br>11-14 FED COM 833H | Ⓓ EXISTING<br>MR POTATO HEAD<br>11-14 FED COM 712H |
| Ⓑ EXISTING<br>MR POTATO HEAD<br>11-14 FED COM 834H | Ⓔ EXISTING<br>MR POTATO HEAD<br>11-14 FED COM 623H |
| Ⓒ EXISTING<br>MR POTATO HEAD<br>11-14 FED COM 739H | Ⓕ EXISTING<br>MR POTATO HEAD<br>11-14 FED COM 332H |
| Ⓖ EXISTING<br>MR POTATO HEAD<br>11 14 FED COM 232H |  |
| Ⓗ EXISTING<br>MR POTATO HEAD<br>11 14 FED COM 233H | <b>New well location</b>                           |

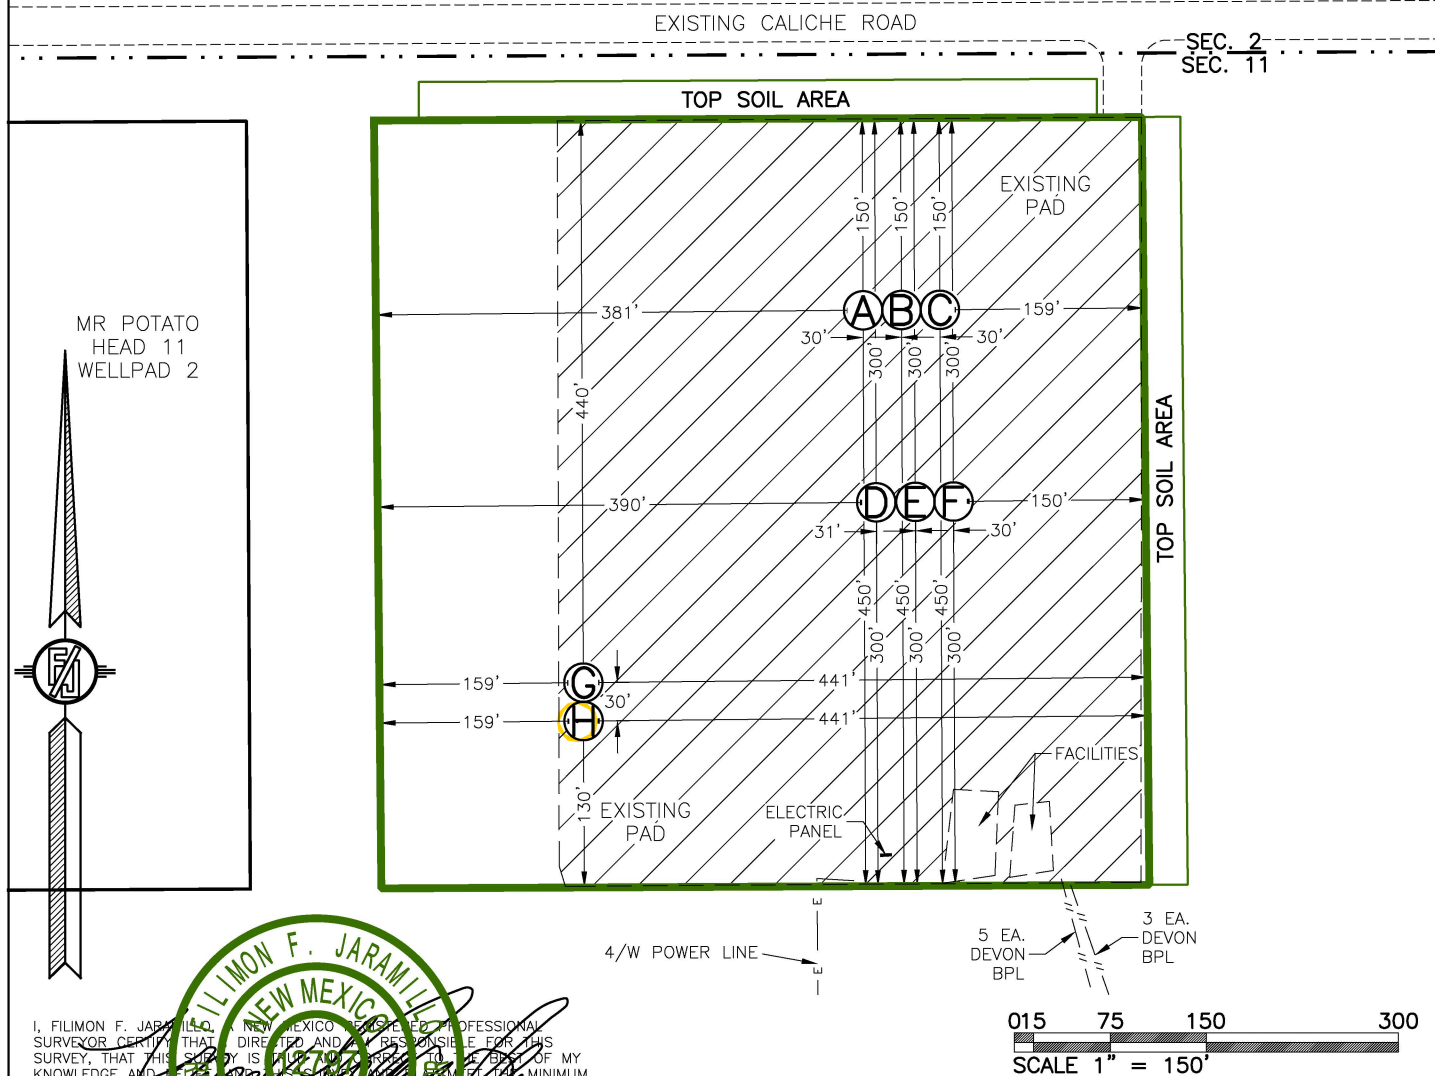

I, FILIMON F. JARAMILLO, NEW MEXICO REGISTERED PROFESSIONAL SURVEYOR, CERTIFY THAT I DIRECTED AND AM RESPONSIBLE FOR THIS SURVEY, THAT THIS SURVEY IS IN ACCORDANCE WITH THE STANDARDS OF MY KNOWLEDGE AND SKILL, AND THAT I HAVE COMPLIED WITH THE MINIMUM STANDARDS FOR SURVEYING IN THE STATE OF NEW MEXICO.

FILIMON F. JARAMILLO, P.S. 17989


**SHEET: 3**

**MADRON SURVEYING, INC.**

301 SOUTH CANAL  
(575) 234-3327

**SURVEY NO. 5623B  
CARLSBAD, NEW MEXICO**

# SECTION 11, TOWNSHIP 24 SOUTH, RANGE 29 EAST, N.M.P.M. EDDY COUNTY, STATE OF NEW MEXICO SITE MAP

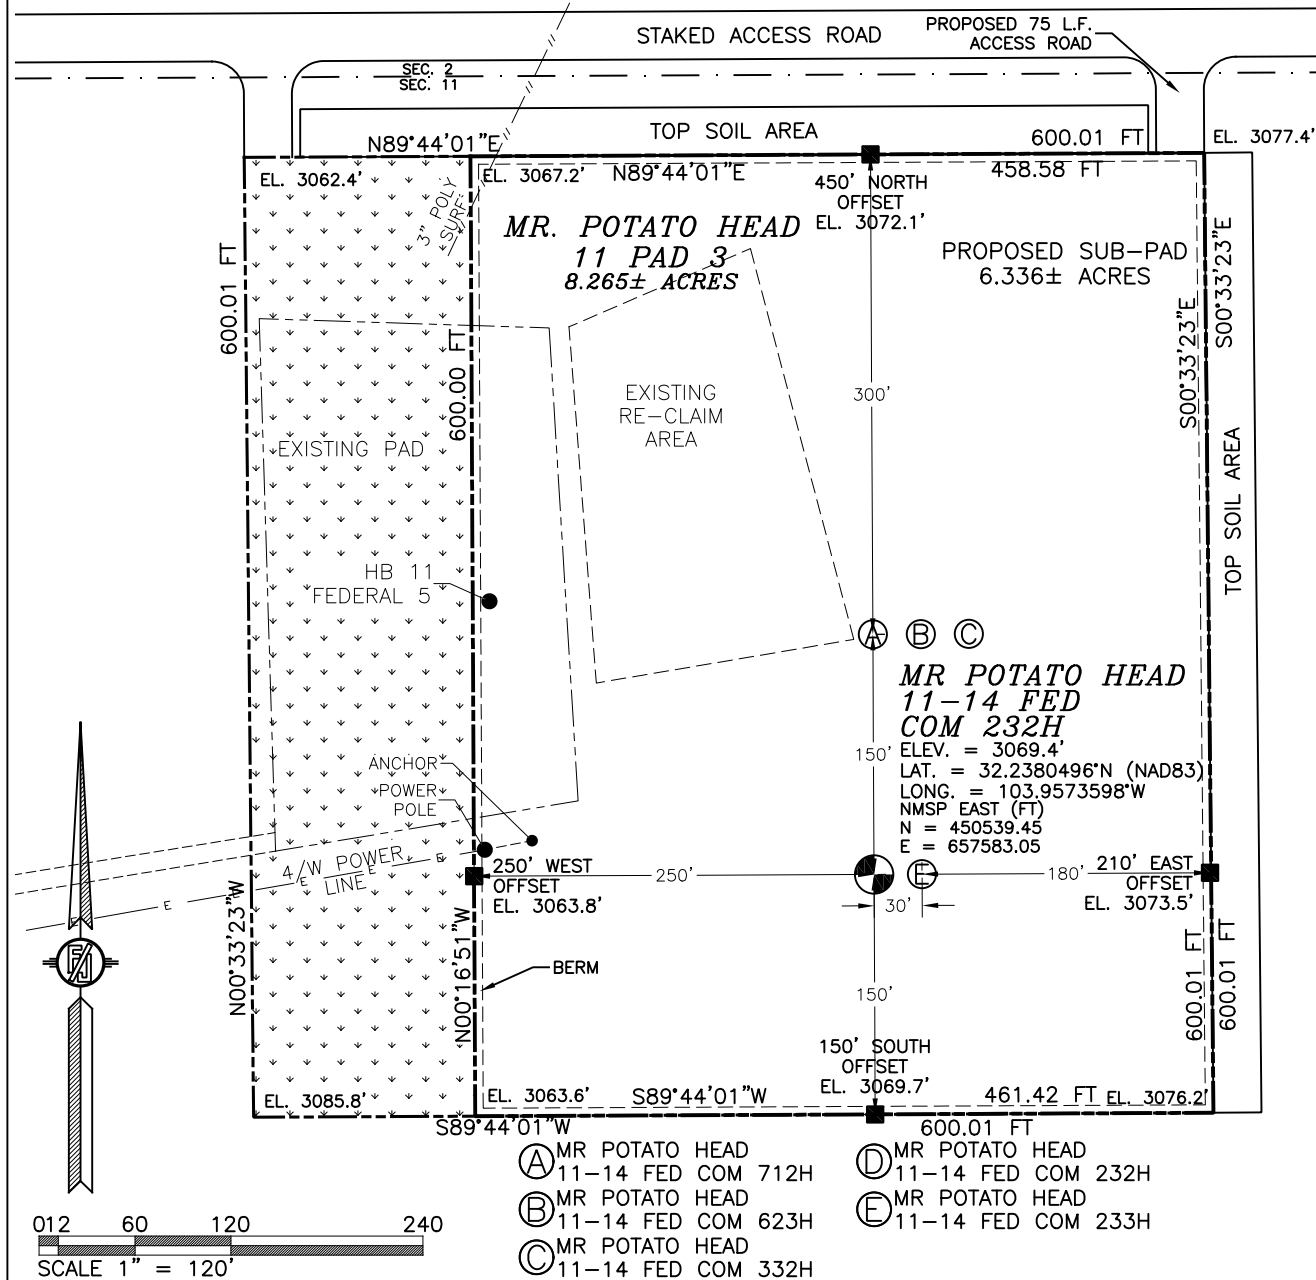

SCALE 1" = 120'

DIRECTIONS TO LOCATION

FROM STATE HWY. 128 & CR. 793 (RAWHIDE) GO SOUTH ON CR. 793 4.1 MILES WHERE PAVEMENT ENDS, CONTINUE SOUTH ON CALICHE ROAD 0.37 MILE, BEND LEFT AND GO EAST 0.22 MILE, TURN RIGHT AND GO SOUTH 0.95 MILE, BEND LEFT AND GO EAST 0.3 MILE, TURN RIGHT AND GO SOUTH 1.0 MILE, BEND RIGHT AND GO SOUTHWEST 0.7 MILE, BEND LEFT AND GO SOUTH 1.0 MILE, TURN RIGHT AND GO WEST 2.00 MILES, TURN RIGHT AND GO NORTHWEST 0.5 MILE TO A ROAD SURVEY, FOLLOW ROAD SURVEY WEST APPROX. 710 FEET THEN SOUTH 75' TO THE NORTHEAST PAD CORNER FOR THIS LOCATION.

I, FILIMON F. JARAMILLO, A NEW MEXICO LICENSED PROFESSIONAL SURVEYOR CERTIFY THAT I DIRECTED AND AM RESPONSIBLE FOR THIS SURVEY, THAT THIS SURVEY IS TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF, AND THAT I HAVE COMPLIED WITH THE MINIMUM STANDARDS FOR SURVEYING IN THE STATE OF NEW MEXICO.

FILIMON F. JARAMILLO, LICENSE NO. 7081

MADRON SURVEYING, INC.

301 SOUTH CANAL  
(575) 234-3341

CARLSBAD, NEW MEXICO

DEVON ENERGY PRODUCTION COMPANY, L.P.  
**MR POTATO HEAD 11-14 FED COM 232H**  
LOCATED 500 FT. FROM THE NORTH LINE  
AND 1986 FT. FROM THE WEST LINE OF  
SECTION 11, TOWNSHIP 24 SOUTH,  
RANGE 29 EAST, N.M.P.M.  
EDDY COUNTY, STATE OF NEW MEXICO

AUGUST 18, 2020

SURVEY NO. 8413

## Section 2 - Blowout Preventer Testing Procedure

### Variance Request

Devon Energy requests to only test BOP connection breaks after drilling out of surface casing and while skidding between wells which conforms to API Standard 53 and industry standards. This test will include the Top Pipe Rams, HCR, Kill Line Check Valve, QDC (quick disconnect to wellhead) and Shell of the 10M BOPE to 5M for 10 minutes. If a break to the flex hose that runs to the choke manifold is required due to repositioning from a skid, the HCR will remain open during the shell test to include that additional break. The variance only pertains to intermediate hole-sections and no deeper than the Bone Springs Formation where 5M BOP tests are required. The initial BOP test will follow 43 CFR 3172, and subsequent tests following a skid will only test connections that are broken. The annular preventer will be tested to 100% working pressure. This variance will meet or exceed 43 CFR 3172 per the following: Devon Energy will perform a full BOP test per 43 CFR 3172 before drilling out of the intermediate casing string(s) and starting the production hole, before starting any hole section that requires a 10M test, before the expiration of the allotted 14-days for 5M intermediate batch drilling or when the drilling rig is fully mobilized to a new well pad, whichever is sooner. We will utilize a 200' TVD tolerance between intermediate shoes as the cutoff for a full BOP test. The BLM will be contacted 4hrs prior to a BOPE test. The BLM will be notified if and when a well control event is encountered. Break test will be a 14 day interval and not a 30 day full BOPE test interval. If in the event break testing is not utilized, then a full BOPE test would be conducted.

1. Well Control Response:
  1. Primary barrier remains fluid
  2. In the event of an influx due to being underbalanced and after a realized gain or flow, the order of closing BOPE is as follows:
    - a) Annular first
    - b) If annular were to not hold, Upper pipe rams second (which were tested on the skid BOP test)
    - c) If the Upper Pipe Rams were to not hold, Lower Pipe Rams would be third




**Cactus**  
Wellhead

2-9-17  
E Bell

80.7 °F

15:49



50

Date 02-09-17

Tested By E.BELL

Transducer bay2

Transducer Serial 181504

Calibration Date 9/6/15

|   | Job#            | Part#  | Serial#     | Description                           | Test Pressure |
|---|-----------------|--------|-------------|---------------------------------------|---------------|
| 1 | TRJ0006341-0007 | 116966 | TRJ6341-7-1 | ADPT,DRLG,CW,MBU-3T,13-5/8 10M        | 15000         |
| 2 |                 |        |             |                                       |               |
| 3 |                 |        |             |                                       |               |
| 4 |                 |        |             |                                       |               |
| 5 |                 |        |             | TRANSDUCER CALIBRATION DUE 03/13/2017 |               |
| 6 |                 |        |             |                                       |               |
| 7 |                 |        |             |                                       |               |
| 8 |                 |        |             |                                       |               |



Start



Stop



Zero



Config



Save



Print

EXIT



TXP® BTC



| Coupling             | Pipe Body            |
|----------------------|----------------------|
| Grade: P110-ICY      | Grade: P110-ICY      |
| Body: White          | 1st Band: White      |
| 1st Band: Pale Green | 2nd Band: Pale Green |
| 2nd Band: -          | 3rd Band: Pale Green |
| 3rd Band: -          | 4th Band: -          |
|                      | 5th Band: -          |
|                      | 6th Band: -          |

|                      |           |                 |              |       |          |
|----------------------|-----------|-----------------|--------------|-------|----------|
| Outside Diameter     | 5.500 in. | Wall Thickness  | 0.361 in.    | Grade | P110-ICY |
| Min. Wall Thickness  | 87.50 %   | Pipe Body Drift | API Standard | Type  | Casing   |
| Connection OD Option | REGULAR   |                 |              |       |          |

Pipe Body Data

| Geometry       |             |                  |             | Performance                  |              |
|----------------|-------------|------------------|-------------|------------------------------|--------------|
| Nominal OD     | 5.500 in.   | Wall Thickness   | 0.361 in.   | Body Yield Strength          | 729 x1000 lb |
| Nominal Weight | 20.00 lb/ft | Plain End Weight | 19.83 lb/ft | Min. Internal Yield Pressure | 14,360 psi   |
| Drift          | 4.653 in.   | OD Tolerance     | API         | SMYS                         | 125,000 psi  |
| Nominal ID     | 4.778 in.   |                  |             | Collapse Pressure            | 12,300 psi   |

Connection Data

| Geometry             |           | Performance                |              | Make-Up Torques         |              |
|----------------------|-----------|----------------------------|--------------|-------------------------|--------------|
| Connection OD        | 6.100 in. | Tension Efficiency         | 100 %        | Minimum                 | 11,540 ft-lb |
| Coupling Length      | 9.450 in. | Joint Yield Strength       | 729 x1000 lb | Optimum                 | 12,820 ft-lb |
| Connection ID        | 4.766 in. | Internal Pressure Capacity | 14,360 psi   | Maximum                 | 14,100 ft-lb |
| Make-up Loss         | 4.204 in. | Compression Efficiency     | 100 %        | Operation Limit Torques |              |
| Threads per inch     | 5         | Compression Strength       | 729 x1000 lb | Operating Torque        | 22,700 ft-lb |
| Connection OD Option | Regular   | Max. Allowable Bending     | 104 °/100 ft | Yield Torque            | 25,250 ft-lb |
|                      |           | External Pressure Capacity | 12,300 psi   |                         |              |

Notes

This connection is fully interchangeable with:  
TXP® BTC - 5.5 in. - 0.275 (15.50) / 0.304 (17.00) / 0.415 (23.00) / 0.476 (26.00) in. (lb/ft)  
Connections with Dopeless® Technology are fully compatible with the same connection in its doped version  
Datasheet is also valid for Special Bevel option when applicable - except for Coupling Face Load, which will be reduced. Please contact a local Tenaris technical sales representative.  
Standard coupling design comes with optimized 20° bevel.

For the latest performance data, always visit our website: [www.tenaris.com](http://www.tenaris.com)  
For further information on concepts indicated in this datasheet, download the Datasheet Manual from [www.tenaris.com](http://www.tenaris.com)

Tenaris has issued this document for general information only, and the information in this document, including, without limitation, any pictures, drawings or designs ("Information") is not intended to constitute professional or any other type of advice or recommendation and is provided on an "as is" basis. No warranty is given. Tenaris has not independently verified any information –if any- provided by the user in connection with, or for the purpose of, the Information contained hereunder. The use of the Information is at user's own risk and Tenaris does not assume any responsibility or liability of any kind for any loss, damage or injury resulting from, or in connection with any Information contained hereunder or any use thereof. The Information in this document is subject to change or modification without notice. Tenaris's products and services are subject to Tenaris's standard terms and conditions or otherwise to the terms resulting from the respective contracts of sale or services, as the case may be, between petitioner and Tenaris. For more complete information please contact a Tenaris's representative or visit our website at [www.tenaris.com](http://www.tenaris.com) . ©Tenaris 2024. All rights reserved.



9.625"    40#    .395"    J-55

**Dimensions (Nominal)**

|                  |        |          |
|------------------|--------|----------|
| Outside Diameter | 9.625  | in.      |
| Wall             | 0.395  | in.      |
| Inside Diameter  | 8.835  | in.      |
| Drift            | 8.750  | in.      |
| Weight, T&C      | 40.000 | lbs./ft. |
| Weight, PE       | 38.970 | lbs./ft. |

**Performance Properties**

|  |      |           |
|--|------|-----------|
| Collapse, PE                             | 2570 | psi       |
| Internal Yield Pressure at Minimum Yield |      |           |
| PE                                       | 3950 | psi       |
| LTC                                      | 3950 | psi       |
| BTC                                      | 3950 | psi       |
| Yield Strength, Pipe Body                | 630  | 1000 lbs. |
| Joint Strength                           |      |           |
| STC                                      | 452  | 1000 lbs. |
| LTC                                      | 520  | 1000 lbs. |
| BTC                                      | 714  | 1000 lbs. |

Note: SeAH Steel has produced this specification sheet for general information only. SeAH does not assume liability or responsibility for any loss or injury resulting from the use of information or data contained herein. All applications for the material described are at the customer's own risk and responsibility.



13-3/8"   54.50#   .380   J-55

**Dimensions (Nominal)**

|                  |        |        |
|------------------|--------|--------|
| Outside Diameter | 13.375 | in.    |
| Wall             | 0.380  | in.    |
| Inside Diameter  | 12.615 | in.    |
| Drift            | 12.459 | in.    |
|                  |        |        |
| Weight, T&C      | 54.500 | lbs/ft |
| Weight, PE       | 52.790 | lbs/ft |

**Performance Ratings, Minimum**

|                           |      |          |
|---------------------------|------|----------|
| Collapse, PE              | 1130 | psi      |
|                           |      |          |
| Internal Yields Pressure  |      |          |
| PE                        | 2730 | psi      |
| STC                       | 2730 | PSI      |
| BTC                       | 2730 | psi      |
|                           |      |          |
| Yield Strength, Pipe Body | 853  | 1000 lbs |
|                           |      |          |
| Joint Strength, STC       | 514  | 1000 lbs |
| Joint Strength, BTC       | 909  | 1000 lbs |

Note: SeAH Steel has produced this specification sheet for general information only. SeAH does not assume liability or responsibility for any loss or injury resulting from the use of information or data contained herein. All applications for the material described are at the customer's own risk and responsibility.

**District I**  
1625 N. French Dr., Hobbs, NM 88240  
Phone:(575) 393-6161 Fax:(575) 393-0720  
**District II**  
811 S. First St., Artesia, NM 88210  
Phone:(575) 748-1283 Fax:(575) 748-9720  
**District III**  
1000 Rio Brazos Rd., Aztec, NM 87410  
Phone:(505) 334-6178 Fax:(505) 334-6170  
**District IV**  
1220 S. St Francis Dr., Santa Fe, NM 87505  
Phone:(505) 476-3470 Fax:(505) 476-3462

**State of New Mexico**  
**Energy, Minerals and Natural Resources**  
**Oil Conservation Division**  
**1220 S. St Francis Dr.**  
**Santa Fe, NM 87505**

CONDITIONS  
  
Action 351271

CONDITIONS

|   |  |
|---|--|
| Operator:<br>DEVON ENERGY PRODUCTION COMPANY, LP<br>333 West Sheridan Ave.<br>Oklahoma City, OK 73102 | OGRID:<br>6137                                       |
|   | Action Number:<br>351271                             |
|   | Action Type:<br>[C-103] NOI Change of Plans (C-103A) |

CONDITIONS

| Created By  | Condition   | Condition Date |
|-------------|---|----------------|
| ward.rikala | All original COA's still apply. Additionally, if cement is not circulated to surface during cementing operations, then a CBL is required. | 6/10/2024      |
| ward.rikala | NSP may be required.  | 6/10/2024      |
