

Form 3160-3
(June 2015)FORM APPROVED
OMB No. 1004-0137
Expires: January 31, 2018UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
APPLICATION FOR PERMIT TO DRILL OR REENTER

1a. Type of work: <input type="checkbox"/> DRILL <input type="checkbox"/> REENTER		5. Lease Serial No.
1b. Type of Well: <input type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input type="checkbox"/> Other		6. If Indian, Allottee or Tribe Name
1c. Type of Completion: <input type="checkbox"/> Hydraulic Fracturing <input type="checkbox"/> Single Zone <input type="checkbox"/> Multiple Zone		7. If Unit or CA Agreement, Name and No.
2. Name of Operator		8. Lease Name and Well No.
3a. Address		9. API Well No. 30-015-55186
3b. Phone No. (include area code)		10. Field and Pool, or Exploratory
4. Location of Well (Report location clearly and in accordance with any State requirements. *) At surface At proposed prod. zone		11. Sec., T. R. M. or Blk. and Survey or Area
14. Distance in miles and direction from nearest town or post office*		12. County or Parish
		13. State
15. Distance from proposed* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any)	16. No of acres in lease	17. Spacing Unit dedicated to this well
18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft.	19. Proposed Depth	20. BLM/BIA Bond No. in file
21. Elevations (Show whether DF, KDB, RT, GL, etc.)	22. Approximate date work will start*	23. Estimated duration
24. Attachments		

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, and the Hydraulic Fracturing rule per 43 CFR 3162.3-3 (as applicable)

- | | |
|--|---|
| 1. Well plat certified by a registered surveyor. | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above). |
| 2. A Drilling Plan. | 5. Operator certification. |
| 3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office). | 6. Such other site specific information and/or plans as may be requested by the BLM. |

25. Signature	Name (Printed/Typed)	Date
Title		
Approved by (Signature)	Name (Printed/Typed)	Date
Title		
Office		

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Continued on page 2)

*(Instructions on page 2)



Approval Date: 05/23/2024

District I
1625 N. French Dr., Hobbs, NM 88240
Phone: (575) 393-6161 Fax: (575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone: (575) 748-1283 Fax: (575) 748-9720
District III
1000 Rio Brazos Road, Aztec, NM 87410
Phone: (505) 334-6178 Fax: (505) 334-6170
District IV
1220 S. St. Francis Dr., Santa Fe, NM 87505
Phone: (505) 476-3460 Fax: (505) 476-3462

State of New Mexico
Energy, Minerals & Natural Resources Department
OIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, NM 87505

Form C-102
Revised August 1, 2011
Submit one copy to appropriate
District Office

☐ AMENDED REPORT

WELL LOCATION AND ACREAGE DEDICATION PLAT

¹ API Number 30-015- 55186	² Pool Code 96473	³ Pool Name PIERCE CROSSING; BONE SPRING, EAST
⁴ Property Code 328290	⁵ Property Name HEADS CC 9 4 FED COM	⁶ Well Number 14H
⁷ OGRID No. 16696	⁸ Operator Name OXY USA INC.	⁹ Elevation 2934.5'

¹⁰ Surface Location

UL or lot no. O	Section 9	Township 24S	Range 29E	Lot Idn	Feet from the 909	North/South line SOUTH	Feet from the 1426	East/West line EAST	County EDDY
--------------------	--------------	-----------------	--------------	---------	----------------------	---------------------------	-----------------------	------------------------	----------------

¹¹ Bottom Hole Location If Different From Surface

UL or lot no. 1	Section 4	Township 24S	Range 29E	Lot Idn	Feet from the 20	North/South line NORTH	Feet from the 940	East/West line EAST	County EDDY
¹² Dedicated Acres 1280	¹³ Joint or Infill	¹⁴ Consolidation Code	¹⁵ Order No.						

No allowable will be assigned to this completion until all interests have been consolidated or a non-standard unit has been approved by the division.

¹⁶ NAD 83 (SURFACE HOLE LOCATION) LATITUDE = 32°13'38.56" (32.227377°) LONGITUDE = -103°59'07.95" (-103.985542°) NAD 27 (SURFACE HOLE LOCATION) LATITUDE = 32°13'38.11" (32.227254°) LONGITUDE = -103°59'06.19" (-103.985054°) STATE PLANE NAD 83 (N.M. EAST) N: 446627.46' E: 648881.89' STATE PLANE NAD 27 (N.M. EAST) N: 446568.49' E: 607698.05'	NAD 83 (KICK OFF POINT) LATITUDE = 32°13'26.60" (32.224056°) LONGITUDE = -103°59'02.27" (-103.983963°) NAD 27 (KICK OFF POINT) LATITUDE = 32°13'26.16" (32.223933°) LONGITUDE = -103°59'00.51" (-103.983474°) STATE PLANE NAD 83 (N.M. EAST) N: 445421.03' E: 649374.19' STATE PLANE NAD 27 (N.M. EAST) N: 445362.08' E: 608190.32'	NAD 83 (FIRST TAKE POINT) LATITUDE = 32°13'30.56" (32.225155°) LONGITUDE = -103°59'02.28" (-103.983967°) NAD 27 (FIRST TAKE POINT) LATITUDE = 32°13'30.12" (32.225033°) LONGITUDE = -103°59'00.52" (-103.983478°) STATE PLANE NAD 83 (N.M. EAST) N: 445820.94' E: 649371.65' STATE PLANE NAD 27 (N.M. EAST) N: 445761.98' E: 608187.79'
NAD 83 (LEASE CROSSING 1) LATITUDE = 32°13'55.85" (32.232180°) LONGITUDE = -103°59'02.32" (-103.983979°) NAD 27 (LEASE CROSSING 1) LATITUDE = 32°13'55.41" (32.232058°) LONGITUDE = -103°59'00.56" (-103.983490°) STATE PLANE NAD 83 (N.M. EAST) N: 448376.56' E: 649359.79' STATE PLANE NAD 27 (N.M. EAST) N: 448317.55' E: 608176.00'	NAD 83 (LEASE CROSSING 2) LATITUDE = 32°14'48.37" (32.246768°) LONGITUDE = -103°59'02.41" (-103.984002°) NAD 27 (LEASE CROSSING 2) LATITUDE = 32°14'47.93" (32.246646°) LONGITUDE = -103°59'00.65" (-103.983513°) STATE PLANE NAD 83 (N.M. EAST) N: 453683.39' E: 649335.15' STATE PLANE NAD 27 (N.M. EAST) N: 453624.28' E: 608151.50'	NAD 83 (LEASE CROSSING 3) LATITUDE = 32°15'01.50" (32.250418°) LONGITUDE = -103°59'02.43" (-103.984008°) NAD 27 (LEASE CROSSING 3) LATITUDE = 32°15'01.06" (32.250295°) LONGITUDE = -103°59'00.67" (-103.983519°) STATE PLANE NAD 83 (N.M. EAST) N: 455011.03' E: 649328.99' STATE PLANE NAD 27 (N.M. EAST) N: 454951.88' E: 608145.37'
NAD 83 (LAST TAKE POINT) LATITUDE = 32°15'13.54" (32.253761°) LONGITUDE = -103°59'02.45" (-103.984014°) NAD 27 (LAST TAKE POINT) LATITUDE = 32°15'13.10" (32.253638°) LONGITUDE = -103°59'00.69" (-103.983524°) STATE PLANE NAD 83 (N.M. EAST) N: 456227.05' E: 649323.34' STATE PLANE NAD 27 (N.M. EAST) N: 456167.88' E: 608139.75'	NAD 83 (BOTTOM HOLE LOCATION) LATITUDE = 32°15'14.33" (32.253980°) LONGITUDE = -103°59'02.45" (-103.984014°) NAD 27 (BOTTOM HOLE LOCATION) LATITUDE = 32°15'13.89" (32.253858°) LONGITUDE = -103°59'00.69" (-103.983524°) STATE PLANE NAD 83 (N.M. EAST) N: 456307.04' E: 649323.02' STATE PLANE NAD 27 (N.M. EAST) N: 456247.86' E: 608139.43'	

¹⁷ OPERATOR
CERTIFICATION

I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief, and that this organization either owns a working interest or unleased mineral interest in the land including the proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of such a mineral or working interest, or to a voluntary pooling agreement or a compulsory pooling order heretofore entered by the division.

Leslie T. Reeves9/20/2023

Signature Date

LESLIE REEVES

Printed Name

LESLIE_REEVES@OXY.COM

E-mail Address

¹⁸ SURVEYOR
CERTIFICATION

I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief.

June 2, 2023

Date of Survey
Signature and Seal of Professional Surveyor:




Certificate Number:

- = SURFACE HOLE LOCATION
- ◆ = KICK OFF POINT/TAKE POINTS
- ◇ = LEASE CROSSING
- = BOTTOM HOLE LOCATION
- ▲ = SECTION CORNER LOCATED
- = LEASE LINE
- = HORIZONTAL SPACING UNIT
- N.O.W. = NORTH OF WELL.
- E.O.W. = EAST OF WELL.


HSU COORDINATES				
	NAD 27 N.M. STATE PLANE, EAST ZONE		NAD 83 N.M. STATE PLANE, EAST ZONE	
POINT	NORTHING	EASTING	NORTHING	EASTING
A	456251.93'	603786.25'	456311.10'	644969.83'
B	456261.68'	606432.26'	456320.85'	647615.84'
C	456271.26'	609079.15'	456330.43'	650262.74'
D	453629.22'	609089.75'	453688.34'	650273.41'
E	450974.81'	609100.88'	451033.87'	650284.61'
F	448322.87'	609114.24'	448381.88'	650298.04'
G	445667.28'	609128.10'	445726.23'	650311.96'
H	445637.62'	603837.40'	445696.58'	645021.24'
I	448292.86'	603824.90'	448351.88'	645008.68'
J	450947.86'	603813.62'	451006.92'	644997.33'
K	453601.34'	603799.71'	453660.46'	644983.36'

Detail "A"
No Scale

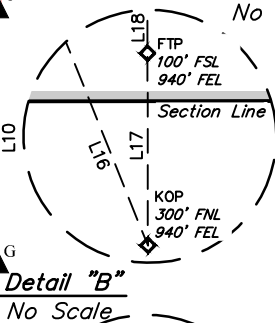

Detail "B"
No Scale

LINE TABLE			LINE TABLE		
LINE	DIRECTION	LENGTH	LINE	DIRECTION	LENGTH
L1	N89°58'16"W	2646.59'	L12	N00°01'52"W	2655.89'
L2	N89°58'02"W	2647.47'	L13	N00°00'17"W	2655.63'
L3	N00°00'31"E	2642.67'	L14	N00°08'44"W	2654.77'
L4	N00°00'06"W	2655.05'	L15	N00°09'55"E	5303.34'
L5	S89°57'15"W	2644.28'	L16	S21°57'31"E	1303.28'
L6	S89°56'31"W	2644.18'	L17	N00°07'27"W	400.00'
L7	N00°03'42"W	2654.14'	L18	N00°01'33"W	2556.18'
L8	N00°03'08"W	2651.24'	L19	N00°01'33"W	5308.01'
L9	N00°03'00"W	2652.59'	L20	N00°01'33"W	1327.93'
L10	N00°03'37"W	2656.24'	L21	N00°01'33"W	1216.30'
L11	S89°55'08"W	5291.92'	L22	N00°00'31"E	80.00'

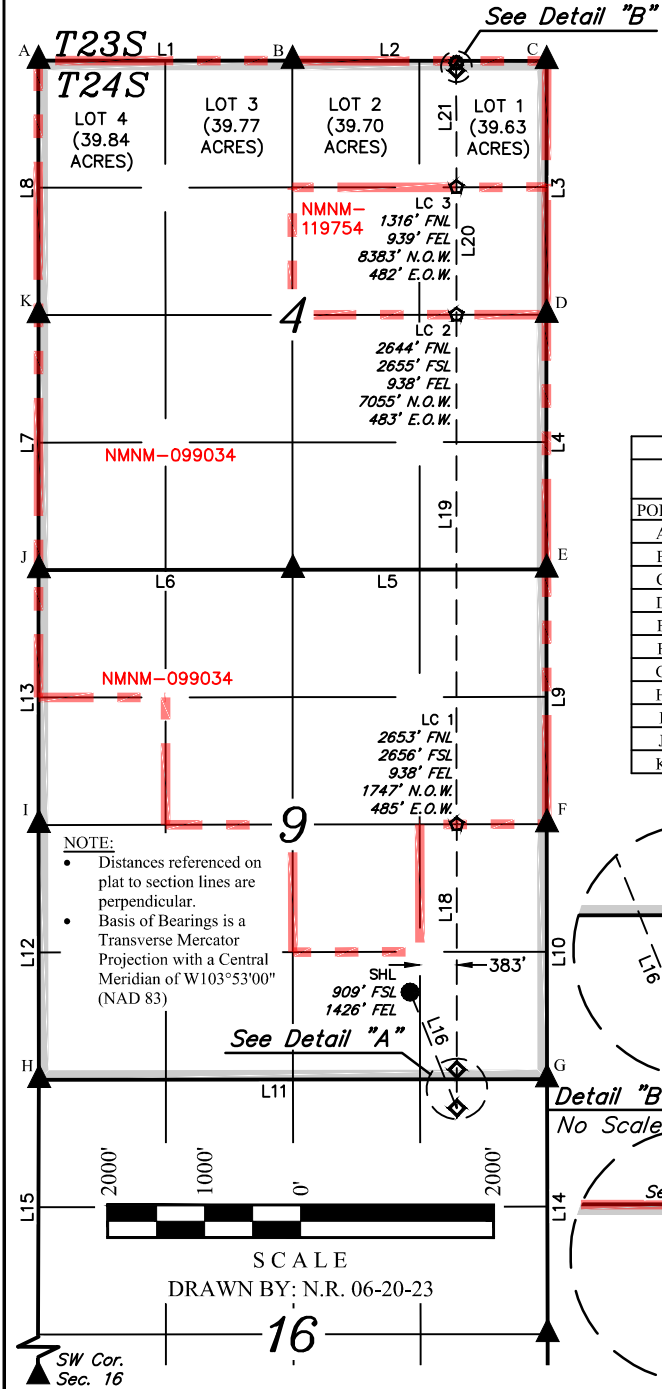

PECOS DISTRICT DRILLING CONDITIONS OF APPROVAL

OPERATOR'S NAME:	OXY USA INCORPORATED
WELL NAME & NO.:	HEADS CC 9-7 FEDERAL COM 14H
SURFACE HOLE FOOTAGE:	909'/S & 1426'/E
BOTTOM HOLE FOOTAGE:	20'/N & 9400'/E
LOCATION:	Section 9, T.24 S., R.29 E.
COUNTY:	Eddy County, New Mexico

COA

H2S	<input checked="" type="radio"/> Yes	<input type="radio"/> No	
Potash	<input checked="" type="radio"/> None	<input type="radio"/> Secretary	<input type="radio"/> R-111-P
Cave/Karst Potential	<input type="radio"/> Low	<input checked="" type="radio"/> Medium	<input type="radio"/> High
Cave/Karst Potential	<input type="radio"/> Critical		
Variance	<input type="radio"/> None	<input checked="" type="radio"/> Flex Hose	<input type="radio"/> Other
Wellhead	<input type="radio"/> Conventional	<input checked="" type="radio"/> Multibowl	<input type="radio"/> Both
Wellhead Variance	<input type="radio"/> Diverter		
Other	<input type="checkbox"/> 4 String	<input type="checkbox"/> Capitan Reef	<input type="checkbox"/> WIPP
Other	<input type="checkbox"/> Fluid Filled	<input type="checkbox"/> Pilot Hole	<input type="checkbox"/> Open Annulus
Cementing	<input type="checkbox"/> Contingency Cement Squeeze	<input type="checkbox"/> EchoMeter	<input checked="" type="checkbox"/> Primary Cement Squeeze
Special Requirements	<input type="checkbox"/> Water Disposal	<input checked="" type="checkbox"/> COM	<input type="checkbox"/> Unit
Special Requirements	<input type="checkbox"/> Batch Sundry		
Special Requirements Variance	<input checked="" type="checkbox"/> Break Testing	<input checked="" type="checkbox"/> Offline Cementing	<input checked="" type="checkbox"/> Casing Clearance

A. HYDROGEN SULFIDE

A Hydrogen Sulfide (H2S) Drilling Plan shall be activated AT SPUD. As a result, the Hydrogen Sulfide area must meet Onshore Order 6 requirements, which includes equipment and personnel/public protection items. If Hydrogen Sulfide is encountered, please provide measured values and formations to the BLM.

B. CASING

Primary Casing Design:

- The **10-3/4** inch surface casing shall be set at approximately **588** feet (a minimum of 70 feet (Eddy County) into the Rustler Anhydrite, above the salt, and below usable fresh water) and cemented to the surface.

- a. If cement does not circulate to the surface, the appropriate BLM office shall be notified and a temperature survey utilizing an electronic type temperature survey with surface log readout will be used or a cement bond log shall be run to verify the top of the cement. Temperature survey will be run a minimum of six hours after pumping cement and ideally between 8-10 hours after completing the cement job.
 - b. Wait on cement (WOC) time for a primary cement job will be a minimum of **8 hours** or 500 pounds compressive strength, whichever is greater. (This is to include the lead cement)
 - c. Wait on cement (WOC) time for a remedial job will be a minimum of 4 hours after bringing cement to surface or 500 pounds compressive strength, whichever is greater.
 - d. If cement falls back, remedial cementing will be done prior to drilling out that string.
2. The **7.827** inch intermediate casing shall be set at approximately **7209** feet. The minimum required fill of cement behind the **7.827** inch intermediate casing is:

Option 1 (Single Stage):

- Cement to surface. If cement does not circulate see B.1.a, c-d above.

Option 2:

Operator has proposed to cement in two stages by conventionally cementing the first stage and performing a bradenhead squeeze on the second stage, contingent upon no returns to surface.

- a. First stage: Operator will cement with intent to reach the top of the **Brushy Canyon**
 - b. Second stage:
 - Operator will perform bradenhead squeeze and top-out. Cement to surface. If cement does not reach surface, the appropriate BLM office shall be notified
- ❖ In Medium Cave/Karst Areas if cement does not circulate to surface on the first two casing strings, the cement on the 3rd casing string must come to surface.

Operator has proposed to pump down 10-3/4" 7.827" annulus. Operator must top out cement after the bradenhead squeeze and verify cement to surface. Operator can also check TOC with Echo-meter. CBL must be run from TD of the 7.827" casing to surface if confidence is lacking on the quality of the bradenhead squeeze cement job. Submit results to BLM.

If cement does not tie-back into the previous casing shoe, a third stage remediation BH may be performed. The appropriate BLM office shall be notified.

Bradenhead squeeze in the production interval is only as an edge case remediation measure and is NOT approved in this COA. If production cement job experiences losses and a bradenhead squeeze is needed for tie-back, BLM Engineering should be notified prior to job with volumes and planned wellbore schematic. CBL will be needed when this occurs.

3. The 5-1/2 inch production liner shall be set at approximately 18,671 feet. Liner to tie back minimum 200'. The minimum required fill of cement behind the 5-1/2 inch production casing is:

Option 1 (Single Stage):

- Cement should tie-back at least **200 feet** into previous casing string. Operator shall provide method of verification.

Falcon Design Requirements (applicable if second intermediate exposed to frac pressures):

- Tie Back of the liner should be a minimum of 200' into the previous casing
- Surface and Intermediate cement to surface should be verified visually. If cement fallback is suspected, an Echo-meter can be run to verify cement top in the intermediate and a temp log may be run in the surface interval. CBL should be run if confidence is lacking in the surface or intermediate cement job. The proposed falcon design (when intermediate string is exposed to frac pressures) is only approved when surface and intermediate sections are cemented to surface. Operator to revert to pre-frac tie-in design when surface or intermediate cementing is of poor quality or not verified to surface
- Region 2 NACE certified intermediate casing must be used
- A third-party verification (such as thread rep or torque turn) must be conducted to ensure the connection makeups are to spec for the intermediate casing string exposed to frac pressures
- Corrosion inhibitors must be used in areas with corrosive production fluids
- Operator should actively monitor annulus during the completion phase. Wells should be monitored in a manner capable of identifying a casing leak or liner top packer leak, within an acceptable time frame while on production. Remedial work may be required to restore intermediate casing integrity or liner top packer integrity in a failure event
- BLM should be notified if cement is not verified to the liner top
- 4-String Falcon Design meets the minimum requirement for the R111P area with the salt interval intermediate casing and an additional intermediate string cemented to surface

C. PRESSURE CONTROL

1. Variance approved to use flex line from BOP to choke manifold. Manufacturer's specification to be readily available. No external damage to flex line. Flex line to be installed as straight as possible (no hard bends).'
2. Operator has proposed a multi-bowl wellhead assembly. This assembly will only be tested when installed on the **10-3/4** inch surface casing. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **5000 (5M) psi. Variance is approved to use a 5000 (5M) Annular which shall be tested to 3500 (70% Working Pressure) psi.**
 - a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
 - b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
 - c. Manufacturer representative shall install the test plug for the initial BOP test.
 - d. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
 - e. Whenever any seal subject to test pressure is broken, all the tests in OOGO2.III.A.2.i must be followed.

D. SPECIAL REQUIREMENT (S)

Communitization Agreement

- The operator will submit a Communitization Agreement to the Santa Fe Office, 301 Dinosaur Trail Santa Fe, New Mexico 87508, at least 90 days before the anticipated date of first production from a well subject to a spacing order issued by the New Mexico Oil Conservation Division. The Communitization Agreement will include the signatures of all working interest owners in all Federal and Indian leases subject to the Communitization Agreement (i.e., operating rights owners and lessees of record), or certification that the operator has obtained the written signatures of all such owners and will make those signatures available to the BLM immediately upon request.
- The operator will submit an as-drilled survey well plat of the well completion, but are not limited to, those specified in Onshore Order 1 and 43 CFR part 3170 Subpart 3172.
- If the operator does not comply with this condition of approval, the BLM may take enforcement actions that include, but are not limited to, those specified in 43 CFR 3163.1.
- In addition, the well sign shall include the surface and bottom hole lease numbers. When the Communitization Agreement number is known, it shall also be on the sign.

**(Note: For a minimum 5M BOPE or less (Utilizing a 10M BOPE system)
BOPE Break Testing Variance**

- BOPE Break Testing is ONLY permitted for 5M BOPE or less. (**Annular preventer must be tested to a minimum of 70% of BOPE working pressure and shall be higher than the MASP**)
- BOPE Break Testing is NOT permitted to drilling the production hole section.
- Variance only pertains to the intermediate hole-sections and no deeper than the Bone Springs formation.
- While in transfer between wells, the BOPE shall be secured by the hydraulic carrier or cradle.
- Any well control event while drilling require notification to the BLM Petroleum Engineer (**575-706-2779**) prior to the commencement of any BOPE Break Testing operations.
- A full BOPE test is required prior to drilling the first deep intermediate hole section. If any subsequent hole interval is deeper than the first, a full BOPE test will be required. (200' TVD tolerance between intermediate shoes is allowable).
- The BLM is to be contacted (575-361-2822 Eddy County) 4 hours prior to BOPE tests.
- As a minimum, a full BOPE test shall be performed at 21-day intervals.
- In the event any repairs or replacement of the BOPE is required, the BOPE shall test as per 43 CFR part 3170 Subpart 3172.
- If in the event break testing is not utilized, then a full BOPE test would be conducted.

Offline Cementing

Operator has been (**Approved**) to pump the proposed cement program offline in the **Surface and intermediate(s) intervals**.

Offline cementing should commence within 24 hours of landing the casing for the interval.

Notify the BLM 4hrs prior to cementing offline at **Eddy County: 575-361-2822**.

Casing Clearance:

*If Production Casing Connection OD does not meet 0.422" annular clearance inside casing:

- Cement excess will be circulated from Top of Liner to surface (Cement Confirmation)
- Liner Top will be tested to confirm seal
- If ICP in Bone Spring Pool and lateral landed in Wolfcamp Pool, a CBL will be ran.

Operator shall clean up cycles until wellbore is clear of cuttings and any large debris, ensure cutting sizes are adequate "coffee ground or less" before cementing.

GENERAL REQUIREMENTS

The BLM is to be notified in advance for a representative to witness:

- a. Spudding well (minimum of 24 hours)

- b. Setting and/or Cementing of all casing strings (minimum of 4 hours)
 - c. BOPE tests (minimum of 4 hours)
 - If well located in Eddy County
EMAIL or call the Carlsbad Field Office, 620 East Greene St., Carlsbad, NM 88220,
BLM_NM_CFO_DrillingNotifications@BLM.GOV
 (575) 361-2822
 - If well located in Lea County
 Call the Hobbs Field Station, 414 West Taylor, Hobbs NM 88240,
 (575) 689-5981
1. Unless the production casing has been run and cemented or the well has been properly plugged, the drilling rig shall not be removed from over the hole without prior approval.
 - a. In the event the operator has proposed to drill multiple wells utilizing a skid/walking rig. Operator shall secure the wellbore on the current well, after installing and testing the wellhead, by installing a blind flange of like pressure rating to the wellhead and a pressure gauge that can be monitored while drilling is performed on the other well(s).
 - b. When the operator proposes to set surface casing with Spudder Rig
 - Notify the BLM when moving in and removing the Spudder Rig.
 - Notify the BLM when moving in the 2nd Rig. Rig to be moved in within 90 days of notification that Spudder Rig has left the location.
 - BOP/BOPE test to be conducted per **43 CFR part 3170 Subpart 3172** as soon as 2nd Rig is rigged up on well.
 2. Floor controls are required for 3M or Greater systems. These controls will be on the rig floor, unobstructed, readily accessible to the driller and will be operational at all times during drilling and/or completion activities. Rig floor is defined as the area immediately around the rotary table; the area immediately above the substructure on which the draw works are located, this does not include the dog house or stairway area.
 3. The record of the drilling rate along with the GR/N well log run from TD to surface (horizontal well – vertical portion of hole) shall be submitted to the BLM office as well as all other logs run on the borehole 30 days from completion. If available, a digital copy of the logs is to be submitted in addition to the paper copies. The Rustler top and top and bottom of Salt are to be recorded on the Completion Report.
- A. CASING
1. Changes to the approved APD casing program need prior approval if the items substituted are of lesser grade or different casing size or are Non-API. The Operator

can exchange the components of the proposal with that of superior strength (i.e. changing from J-55 to N-80, or from 36# to 40#). Changes to the approved cement program need prior approval if the altered cement plan has less volume or strength or if the changes are substantial (i.e. Multistage tool, ECP, etc.). The initial wellhead installed on the well will remain on the well with spools used as needed.

2. Wait on cement (WOC) for Potash Areas: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi for all cement blends, 2) until cement has been in place at least 24 hours. WOC time will be recorded in the driller's log. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
3. Wait on cement (WOC) for Water Basin: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi at the shoe, 2) until cement has been in place at least 8 hours. WOC time will be recorded in the driller's log. See individual casing strings for details regarding lead cement slurry requirements. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
4. Provide compressive strengths including hours to reach required 500 pounds compressive strength prior to cementing each casing string. Have well specific cement details onsite prior to pumping the cement for each casing string.
5. No pea gravel permitted for remedial or fall back remedial without prior authorization from the BLM engineer.
6. On that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Formation at the shoe shall be tested to a minimum of the mud weight equivalent anticipated to control the formation pressure to the next casing depth or at total depth of the well. This test shall be performed before drilling more than 20 feet of new hole.
7. If hardband drill pipe is rotated inside casing, returns will be monitored for metal. If metal is found in samples, drill pipe will be pulled and rubber protectors which have a larger diameter than the tool joints of the drill pipe will be installed prior to continuing drilling operations.
8. Whenever a casing string is cemented in the R-111-P potash area, the NMOCD requirements shall be followed.

B. PRESSURE CONTROL

1. All blowout preventer (BOP) and related equipment (BOPE) shall comply with well control requirements as described in **43 CFR part 3170 Subpart 3172** and **API STD 53 Sec. 5.3**.
2. If a variance is approved for a flexible hose to be installed from the BOP to the choke manifold, the following requirements apply: The flex line must meet the requirements of API 16C. Check condition of flexible line from BOP to choke manifold, replace if exterior is damaged or if line fails test. Line to be as straight as possible with no hard bends and is to be anchored according to Manufacturer's requirements. The flexible hose can be exchanged with a hose of equal size and equal or greater pressure rating. Anchor requirements, specification sheet and hydrostatic pressure test certification matching the hose in service, to be onsite for review. These documents shall be posted in the company man's trailer and on the rig floor.
3. 5M or higher system requires an HCR valve, remote kill line and annular to match. The remote kill line is to be installed prior to testing the system and tested to stack pressure.
4. If the operator has proposed a multi-bowl wellhead assembly in the APD. The following requirements must be met:
 - a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
 - b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
 - c. Manufacturer representative shall install the test plug for the initial BOP test.
 - d. Whenever any seal subject to test pressure is broken, all the tests in **43 CFR part 3170 Subpart 3172** must be followed.
 - e. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
5. The appropriate BLM office shall be notified a minimum of 4 hours in advance for a representative to witness the tests.
 - a. In a water basin, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. The casing cut-off and BOP installation can be initiated four hours after installing the slips, which will be approximately six hours after bumping the plug. For those casing strings not using slips, the minimum wait time before cut-off is eight hours after bumping the plug. BOP/BOPE testing can begin after cut-off or once cement reaches 500 psi compressive strength (including lead cement), whichever is greater. However, if the float does not hold, cut-

off cannot be initiated until cement reaches 500 psi compressive strength (including lead when specified).

- b. In potash areas, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. For all casing strings, casing cut-off and BOP installation can be initiated at twelve hours after bumping the cement plug. The BOPE test can be initiated after bumping the cement plug with the casing valve open. (only applies to single stage cement jobs, prior to the cement setting up.)
- c. The tests shall be done by an independent service company utilizing a test plug not a cup or J-packer and can be initiated immediately with the casing valve open. The operator also has the option of utilizing an independent tester to test without a plug (i.e. against the casing) pursuant to **43 CFR part 3170 Subpart 3172** with the pressure not to exceed 70% of the burst rating for the casing. Any test against the casing must meet the WOC time for water basin (8 hours) or potash (24 hours) or 500 pounds compressive strength, whichever is greater, prior to initiating the test (see casing segment as lead cement may be critical item).
- d. The test shall be run on a 5000 psi chart for a 2-3M BOP/BOP, on a 10000 psi chart for a 5M BOP/BOPE and on a 15000 psi chart for a 10M BOP/BOPE. If a linear chart is used, it shall be a one hour chart. A circular chart shall have a maximum 2 hour clock. If a twelve hour or twenty-four hour chart is used, tester shall make a notation that it is run with a two hour clock.
- e. The results of the test shall be reported to the appropriate BLM office.
- f. All tests are required to be recorded on a calibrated test chart. A copy of the BOP/BOPE test chart and a copy of independent service company test will be submitted to the appropriate BLM office.
- g. The BOP/BOPE test shall include a low pressure test from 250 to 300 psi. The test will be held for a minimum of 10 minutes if test is done with a test plug and 30 minutes without a test plug. This test shall be performed prior to the test at full stack pressure.
- h. BOP/BOPE must be tested by an independent service company within 500 feet of the top of the Wolfcamp formation if the time between the setting of the intermediate casing and reaching this depth exceeds 20 days. This test does not exclude the test prior to drilling out the casing shoe as per **43 CFR part 3170 Subpart 3172**.

C. DRILLING MUD

Mud system monitoring equipment, with derrick floor indicators and visual and audio alarms, shall be operating before drilling into the Wolfcamp formation, and shall be used until production casing is run and cemented.

D. WASTE MATERIAL AND FLUIDS

All waste (i.e. drilling fluids, trash, salts, chemicals, sewage, gray water, etc.) created as a result of drilling operations and completion operations shall be safely contained and disposed of properly at a waste disposal facility. No waste material or fluid shall be disposed of on the well location or surrounding area.

Porto-johns and trash containers will be on-location during fracturing operations or any other crew-intensive operations.

KPI 5/20/2024

OXY

PRD NM DIRECTIONAL PLANS (NAD 1983)

Heads CC 9_4

Heads CC 9_4 Federal Com 14H

Wellbore #1

Plan: Permitting Plan

Standard Planning Report

21 August, 2023

OXY
Planning Report

Database:	HOPSPP	Local Co-ordinate Reference:	Well Heads CC 9_4 Federal Com 14H
Company:	ENGINEERING DESIGNS	TVD Reference:	25' RKB @ 2959.50ft
Project:	PRD NM DIRECTIONAL PLANS (NAD 1983)	MD Reference:	25' RKB @ 2959.50ft
Site:	Heads CC 9_4	North Reference:	Grid
Well:	Heads CC 9_4 Federal Com 14H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Permitting Plan		

Project	PRD NM DIRECTIONAL PLANS (NAD 1983)		
Map System:	US State Plane 1983	System Datum:	Mean Sea Level
Geo Datum:	North American Datum 1983		
Map Zone:	New Mexico Eastern Zone		Using geodetic scale factor

Site	Heads CC 9_4		
Site Position:		Northing:	446,198.60 usft
From:	Map	Easting:	648,677.50 usft
Position Uncertainty:	2.00 ft	Slot Radius:	13.200 in
		Latitude:	32.226200
		Longitude:	-103.986208

Well	Heads CC 9_4 Federal Com 14H		
Well Position	+N/-S	0.00 ft	Northing:
	+E/-W	0.00 ft	Easting:
Position Uncertainty	1.00 ft	Wellhead Elevation:	0.00 ft
Grid Convergence:	0.19 °		
		Latitude:	32.227377
		Longitude:	-103.985543
		Ground Level:	2,934.50 ft

Wellbore	Wellbore #1				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	HDGM_FILE	12/31/2019	6.90	59.93	47,854.70000000

Design	Permitting Plan			
Audit Notes:				
Version:	Phase:	PROTOTYPE	Tie On Depth:	0.00
Vertical Section:	Depth From (TVD) (ft)	+N/-S (ft)	+E/-W (ft)	Direction (°)
	0.00	0.00	0.00	2.61

Plan Survey Tool Program	Date	8/21/2023		
Depth From (ft)	Depth To (ft)	Survey (Wellbore)	Tool Name	Remarks
1	0.00	18,677.57	Permitting Plan (Wellbore #1)	B001Mb_MWD+HRGM
				OWSG MWD + HRGM

Plan Sections										
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)	TFO (°)	Target
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
2,408.00	0.00	0.00	2,408.00	0.00	0.00	0.00	0.00	0.00	0.00	
4,208.00	18.00	160.53	4,178.54	-264.39	93.48	1.00	1.00	0.00	160.53	
7,308.32	18.00	160.53	7,127.12	-1,167.64	412.84	0.00	0.00	0.00	0.00	
8,377.72	89.97	359.73	7,863.09	-619.54	488.93	10.00	6.73	-15.04	-159.89	
18,677.72	89.97	359.73	7,868.00	9,680.35	441.17	0.00	0.00	0.00	0.00	PBHL (Heads CC

OXY

Planning Report

Database:	HOPSPP	Local Co-ordinate Reference:	Well Heads CC 9_4 Federal Com 14H
Company:	ENGINEERING DESIGNS	TVD Reference:	25' RKB @ 2959.50ft
Project:	PRD NM DIRECTIONAL PLANS (NAD 1983)	MD Reference:	25' RKB @ 2959.50ft
Site:	Heads CC 9_4	North Reference:	Grid
Well:	Heads CC 9_4 Federal Com 14H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Permitting Plan		

Planned Survey									
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
100.00	0.00	0.00	100.00	0.00	0.00	0.00	0.00	0.00	0.00
200.00	0.00	0.00	200.00	0.00	0.00	0.00	0.00	0.00	0.00
300.00	0.00	0.00	300.00	0.00	0.00	0.00	0.00	0.00	0.00
400.00	0.00	0.00	400.00	0.00	0.00	0.00	0.00	0.00	0.00
500.00	0.00	0.00	500.00	0.00	0.00	0.00	0.00	0.00	0.00
600.00	0.00	0.00	600.00	0.00	0.00	0.00	0.00	0.00	0.00
700.00	0.00	0.00	700.00	0.00	0.00	0.00	0.00	0.00	0.00
800.00	0.00	0.00	800.00	0.00	0.00	0.00	0.00	0.00	0.00
900.00	0.00	0.00	900.00	0.00	0.00	0.00	0.00	0.00	0.00
1,000.00	0.00	0.00	1,000.00	0.00	0.00	0.00	0.00	0.00	0.00
1,100.00	0.00	0.00	1,100.00	0.00	0.00	0.00	0.00	0.00	0.00
1,200.00	0.00	0.00	1,200.00	0.00	0.00	0.00	0.00	0.00	0.00
1,300.00	0.00	0.00	1,300.00	0.00	0.00	0.00	0.00	0.00	0.00
1,400.00	0.00	0.00	1,400.00	0.00	0.00	0.00	0.00	0.00	0.00
1,500.00	0.00	0.00	1,500.00	0.00	0.00	0.00	0.00	0.00	0.00
1,600.00	0.00	0.00	1,600.00	0.00	0.00	0.00	0.00	0.00	0.00
1,700.00	0.00	0.00	1,700.00	0.00	0.00	0.00	0.00	0.00	0.00
1,800.00	0.00	0.00	1,800.00	0.00	0.00	0.00	0.00	0.00	0.00
1,900.00	0.00	0.00	1,900.00	0.00	0.00	0.00	0.00	0.00	0.00
2,000.00	0.00	0.00	2,000.00	0.00	0.00	0.00	0.00	0.00	0.00
2,100.00	0.00	0.00	2,100.00	0.00	0.00	0.00	0.00	0.00	0.00
2,200.00	0.00	0.00	2,200.00	0.00	0.00	0.00	0.00	0.00	0.00
2,300.00	0.00	0.00	2,300.00	0.00	0.00	0.00	0.00	0.00	0.00
2,408.00	0.00	0.00	2,408.00	0.00	0.00	0.00	0.00	0.00	0.00
2,500.00	0.92	160.53	2,500.00	-0.70	0.25	-0.68	1.00	1.00	0.00
2,600.00	1.92	160.53	2,599.96	-3.03	1.07	-2.98	1.00	1.00	0.00
2,700.00	2.92	160.53	2,699.87	-7.01	2.48	-6.89	1.00	1.00	0.00
2,800.00	3.92	160.53	2,799.69	-12.64	4.47	-12.42	1.00	1.00	0.00
2,900.00	4.92	160.53	2,899.40	-19.90	7.04	-19.56	1.00	1.00	0.00
3,000.00	5.92	160.53	2,998.95	-28.81	10.19	-28.32	1.00	1.00	0.00
3,100.00	6.92	160.53	3,098.32	-39.35	13.91	-38.68	1.00	1.00	0.00
3,200.00	7.92	160.53	3,197.48	-51.53	18.22	-50.64	1.00	1.00	0.00
3,300.00	8.92	160.53	3,296.40	-65.33	23.10	-64.21	1.00	1.00	0.00
3,400.00	9.92	160.53	3,395.05	-80.76	28.56	-79.38	1.00	1.00	0.00
3,500.00	10.92	160.53	3,493.40	-97.81	34.58	-96.14	1.00	1.00	0.00
3,600.00	11.92	160.53	3,591.42	-116.48	41.18	-114.49	1.00	1.00	0.00
3,700.00	12.92	160.53	3,689.08	-136.76	48.35	-134.42	1.00	1.00	0.00
3,800.00	13.92	160.53	3,786.35	-158.64	56.09	-155.92	1.00	1.00	0.00
3,900.00	14.92	160.53	3,883.20	-182.12	64.39	-179.00	1.00	1.00	0.00
4,000.00	15.92	160.53	3,979.59	-207.19	73.25	-203.64	1.00	1.00	0.00
4,100.00	16.92	160.53	4,075.51	-233.84	82.68	-229.83	1.00	1.00	0.00
4,208.00	18.00	160.53	4,178.54	-264.39	93.48	-259.86	1.00	1.00	0.00
4,300.00	18.00	160.53	4,266.03	-291.19	102.96	-286.20	0.00	0.00	0.00
4,400.00	18.00	160.53	4,361.14	-320.32	113.26	-314.84	0.00	0.00	0.00
4,500.00	18.00	160.53	4,456.25	-349.46	123.56	-343.47	0.00	0.00	0.00
4,600.00	18.00	160.53	4,551.35	-378.59	133.86	-372.11	0.00	0.00	0.00
4,700.00	18.00	160.53	4,646.46	-407.73	144.16	-400.74	0.00	0.00	0.00
4,800.00	18.00	160.53	4,741.56	-436.86	154.46	-429.38	0.00	0.00	0.00
4,900.00	18.00	160.53	4,836.67	-466.00	164.76	-458.01	0.00	0.00	0.00
5,000.00	18.00	160.53	4,931.77	-495.13	175.06	-486.65	0.00	0.00	0.00
5,100.00	18.00	160.53	5,026.88	-524.26	185.36	-515.28	0.00	0.00	0.00
5,200.00	18.00	160.53	5,121.99	-553.40	195.67	-543.92	0.00	0.00	0.00
5,300.00	18.00	160.53	5,217.09	-582.53	205.97	-572.55	0.00	0.00	0.00
5,400.00	18.00	160.53	5,312.20	-611.67	216.27	-601.19	0.00	0.00	0.00

OXY

Planning Report

Database:	HOPSPP	Local Co-ordinate Reference:	Well Heads CC 9_4 Federal Com 14H
Company:	ENGINEERING DESIGNS	TVD Reference:	25' RKB @ 2959.50ft
Project:	PRD NM DIRECTIONAL PLANS (NAD 1983)	MD Reference:	25' RKB @ 2959.50ft
Site:	Heads CC 9_4	North Reference:	Grid
Well:	Heads CC 9_4 Federal Com 14H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Permitting Plan		

Planned Survey									
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
5,500.00	18.00	160.53	5,407.30	-640.80	226.57	-629.82	0.00	0.00	0.00
5,600.00	18.00	160.53	5,502.41	-669.94	236.87	-658.46	0.00	0.00	0.00
5,700.00	18.00	160.53	5,597.51	-699.07	247.17	-687.09	0.00	0.00	0.00
5,800.00	18.00	160.53	5,692.62	-728.20	257.47	-715.73	0.00	0.00	0.00
5,900.00	18.00	160.53	5,787.72	-757.34	267.77	-744.36	0.00	0.00	0.00
6,000.00	18.00	160.53	5,882.83	-786.47	278.07	-773.00	0.00	0.00	0.00
6,100.00	18.00	160.53	5,977.94	-815.61	288.37	-801.63	0.00	0.00	0.00
6,200.00	18.00	160.53	6,073.04	-844.74	298.68	-830.27	0.00	0.00	0.00
6,300.00	18.00	160.53	6,168.15	-873.88	308.98	-858.90	0.00	0.00	0.00
6,400.00	18.00	160.53	6,263.25	-903.01	319.28	-887.54	0.00	0.00	0.00
6,500.00	18.00	160.53	6,358.36	-932.14	329.58	-916.17	0.00	0.00	0.00
6,600.00	18.00	160.53	6,453.46	-961.28	339.88	-944.81	0.00	0.00	0.00
6,700.00	18.00	160.53	6,548.57	-990.41	350.18	-973.44	0.00	0.00	0.00
6,800.00	18.00	160.53	6,643.68	-1,019.55	360.48	-1,002.08	0.00	0.00	0.00
6,900.00	18.00	160.53	6,738.78	-1,048.68	370.78	-1,030.71	0.00	0.00	0.00
7,000.00	18.00	160.53	6,833.89	-1,077.82	381.08	-1,059.35	0.00	0.00	0.00
7,100.00	18.00	160.53	6,928.99	-1,106.95	391.39	-1,087.98	0.00	0.00	0.00
7,200.00	18.00	160.53	7,024.10	-1,136.08	401.69	-1,116.62	0.00	0.00	0.00
7,308.32	18.00	160.53	7,127.12	-1,167.64	412.84	-1,147.64	0.00	0.00	0.00
7,350.00	14.16	154.66	7,167.16	-1,178.33	417.17	-1,158.11	10.00	-9.22	-14.07
7,400.00	9.89	141.93	7,216.06	-1,187.24	422.44	-1,166.78	10.00	-8.53	-25.47
7,450.00	6.71	114.44	7,265.55	-1,191.83	427.75	-1,171.12	10.00	-6.36	-54.97
7,500.00	6.48	69.85	7,315.25	-1,192.07	433.07	-1,171.12	10.00	-0.45	-89.18
7,550.00	9.43	39.80	7,364.78	-1,187.94	438.34	-1,166.76	10.00	5.89	-60.11
7,600.00	13.62	25.91	7,413.77	-1,179.50	443.54	-1,158.08	10.00	8.39	-27.79
7,650.00	18.22	18.68	7,461.85	-1,166.79	448.61	-1,145.16	10.00	9.20	-14.45
7,700.00	22.98	14.33	7,508.64	-1,149.92	453.54	-1,128.08	10.00	9.53	-8.70
7,750.00	27.83	11.41	7,553.79	-1,129.01	458.26	-1,106.98	10.00	9.69	-5.83
7,800.00	32.71	9.31	7,596.97	-1,104.22	462.76	-1,082.01	10.00	9.77	-4.21
7,850.00	37.63	7.70	7,637.83	-1,075.75	467.00	-1,053.37	10.00	9.83	-3.22
7,900.00	42.56	6.42	7,676.07	-1,043.80	470.93	-1,021.28	10.00	9.86	-2.57
7,950.00	47.50	5.35	7,711.39	-1,008.62	474.54	-985.97	10.00	9.89	-2.13
8,000.00	52.45	4.44	7,743.54	-970.48	477.80	-947.73	10.00	9.90	-1.82
8,050.00	57.41	3.65	7,772.26	-929.68	480.68	-906.83	10.00	9.92	-1.59
8,100.00	62.37	2.94	7,797.34	-886.51	483.16	-863.59	10.00	9.92	-1.42
8,150.00	67.34	2.29	7,818.58	-841.31	485.21	-818.35	10.00	9.93	-1.30
8,200.00	72.30	1.69	7,835.82	-794.42	486.84	-771.43	10.00	9.94	-1.21
8,250.00	77.27	1.11	7,848.93	-746.20	488.01	-723.21	10.00	9.94	-1.14
8,300.00	82.24	0.57	7,857.82	-697.02	488.73	-674.05	10.00	9.94	-1.10
8,350.00	87.22	0.03	7,862.41	-647.25	488.99	-624.32	10.00	9.94	-1.07
8,377.72	89.97	359.73	7,863.09	-619.54	488.93	-596.64	10.00	9.94	-1.06
8,400.00	89.97	359.73	7,863.10	-597.26	488.83	-574.39	0.00	0.00	0.00
8,500.00	89.97	359.73	7,863.15	-497.26	488.36	-474.51	0.00	0.00	0.00
8,600.00	89.97	359.73	7,863.20	-397.26	487.90	-374.64	0.00	0.00	0.00
8,700.00	89.97	359.73	7,863.24	-297.26	487.44	-274.76	0.00	0.00	0.00
8,800.00	89.97	359.73	7,863.29	-197.26	486.97	-174.89	0.00	0.00	0.00
8,900.00	89.97	359.73	7,863.34	-97.26	486.51	-75.02	0.00	0.00	0.00
9,000.00	89.97	359.73	7,863.39	2.74	486.05	24.86	0.00	0.00	0.00
9,100.00	89.97	359.73	7,863.43	102.73	485.58	124.73	0.00	0.00	0.00
9,200.00	89.97	359.73	7,863.48	202.73	485.12	224.61	0.00	0.00	0.00
9,300.00	89.97	359.73	7,863.53	302.73	484.65	324.48	0.00	0.00	0.00
9,400.00	89.97	359.73	7,863.58	402.73	484.19	424.36	0.00	0.00	0.00
9,500.00	89.97	359.73	7,863.62	502.73	483.73	524.23	0.00	0.00	0.00
9,600.00	89.97	359.73	7,863.67	602.73	483.26	624.10	0.00	0.00	0.00
9,700.00	89.97	359.73	7,863.72	702.73	482.80	723.98	0.00	0.00	0.00

OXY

Planning Report

Database:	HOPSPP	Local Co-ordinate Reference:	Well Heads CC 9_4 Federal Com 14H
Company:	ENGINEERING DESIGNS	TVD Reference:	25' RKB @ 2959.50ft
Project:	PRD NM DIRECTIONAL PLANS (NAD 1983)	MD Reference:	25' RKB @ 2959.50ft
Site:	Heads CC 9_4	North Reference:	Grid
Well:	Heads CC 9_4 Federal Com 14H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Permitting Plan		

Planned Survey									
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
9,800.00	89.97	359.73	7,863.77	802.73	482.34	823.85	0.00	0.00	0.00
9,900.00	89.97	359.73	7,863.82	902.73	481.87	923.73	0.00	0.00	0.00
10,000.00	89.97	359.73	7,863.86	1,002.72	481.41	1,023.60	0.00	0.00	0.00
10,100.00	89.97	359.73	7,863.91	1,102.72	480.94	1,123.47	0.00	0.00	0.00
10,200.00	89.97	359.73	7,863.96	1,202.72	480.48	1,223.35	0.00	0.00	0.00
10,300.00	89.97	359.73	7,864.01	1,302.72	480.02	1,323.22	0.00	0.00	0.00
10,400.00	89.97	359.73	7,864.05	1,402.72	479.55	1,423.10	0.00	0.00	0.00
10,500.00	89.97	359.73	7,864.10	1,502.72	479.09	1,522.97	0.00	0.00	0.00
10,600.00	89.97	359.73	7,864.15	1,602.72	478.63	1,622.84	0.00	0.00	0.00
10,700.00	89.97	359.73	7,864.20	1,702.72	478.16	1,722.72	0.00	0.00	0.00
10,800.00	89.97	359.73	7,864.24	1,802.72	477.70	1,822.59	0.00	0.00	0.00
10,900.00	89.97	359.73	7,864.29	1,902.71	477.23	1,922.47	0.00	0.00	0.00
11,000.00	89.97	359.73	7,864.34	2,002.71	476.77	2,022.34	0.00	0.00	0.00
11,100.00	89.97	359.73	7,864.39	2,102.71	476.31	2,122.22	0.00	0.00	0.00
11,200.00	89.97	359.73	7,864.43	2,202.71	475.84	2,222.09	0.00	0.00	0.00
11,300.00	89.97	359.73	7,864.48	2,302.71	475.38	2,321.96	0.00	0.00	0.00
11,400.00	89.97	359.73	7,864.53	2,402.71	474.92	2,421.84	0.00	0.00	0.00
11,500.00	89.97	359.73	7,864.58	2,502.71	474.45	2,521.71	0.00	0.00	0.00
11,600.00	89.97	359.73	7,864.63	2,602.71	473.99	2,621.59	0.00	0.00	0.00
11,700.00	89.97	359.73	7,864.67	2,702.71	473.52	2,721.46	0.00	0.00	0.00
11,800.00	89.97	359.73	7,864.72	2,802.70	473.06	2,821.33	0.00	0.00	0.00
11,900.00	89.97	359.73	7,864.77	2,902.70	472.60	2,921.21	0.00	0.00	0.00
12,000.00	89.97	359.73	7,864.82	3,002.70	472.13	3,021.08	0.00	0.00	0.00
12,100.00	89.97	359.73	7,864.86	3,102.70	471.67	3,120.96	0.00	0.00	0.00
12,200.00	89.97	359.73	7,864.91	3,202.70	471.21	3,220.83	0.00	0.00	0.00
12,300.00	89.97	359.73	7,864.96	3,302.70	470.74	3,320.71	0.00	0.00	0.00
12,400.00	89.97	359.73	7,865.01	3,402.70	470.28	3,420.58	0.00	0.00	0.00
12,500.00	89.97	359.73	7,865.05	3,502.70	469.81	3,520.45	0.00	0.00	0.00
12,600.00	89.97	359.73	7,865.10	3,602.70	469.35	3,620.33	0.00	0.00	0.00
12,700.00	89.97	359.73	7,865.15	3,702.70	468.89	3,720.20	0.00	0.00	0.00
12,800.00	89.97	359.73	7,865.20	3,802.69	468.42	3,820.08	0.00	0.00	0.00
12,900.00	89.97	359.73	7,865.25	3,902.69	467.96	3,919.95	0.00	0.00	0.00
13,000.00	89.97	359.73	7,865.29	4,002.69	467.50	4,019.82	0.00	0.00	0.00
13,100.00	89.97	359.73	7,865.34	4,102.69	467.03	4,119.70	0.00	0.00	0.00
13,200.00	89.97	359.73	7,865.39	4,202.69	466.57	4,219.57	0.00	0.00	0.00
13,300.00	89.97	359.73	7,865.44	4,302.69	466.10	4,319.45	0.00	0.00	0.00
13,400.00	89.97	359.73	7,865.48	4,402.69	465.64	4,419.32	0.00	0.00	0.00
13,500.00	89.97	359.73	7,865.53	4,502.69	465.18	4,519.19	0.00	0.00	0.00
13,600.00	89.97	359.73	7,865.58	4,602.69	464.71	4,619.07	0.00	0.00	0.00
13,700.00	89.97	359.73	7,865.63	4,702.68	464.25	4,718.94	0.00	0.00	0.00
13,800.00	89.97	359.73	7,865.67	4,802.68	463.79	4,818.82	0.00	0.00	0.00
13,900.00	89.97	359.73	7,865.72	4,902.68	463.32	4,918.69	0.00	0.00	0.00
14,000.00	89.97	359.73	7,865.77	5,002.68	462.86	5,018.57	0.00	0.00	0.00
14,100.00	89.97	359.73	7,865.82	5,102.68	462.39	5,118.44	0.00	0.00	0.00
14,200.00	89.97	359.73	7,865.87	5,202.68	461.93	5,218.31	0.00	0.00	0.00
14,300.00	89.97	359.73	7,865.91	5,302.68	461.47	5,318.19	0.00	0.00	0.00
14,400.00	89.97	359.73	7,865.96	5,402.68	461.00	5,418.06	0.00	0.00	0.00
14,500.00	89.97	359.73	7,866.01	5,502.68	460.54	5,517.94	0.00	0.00	0.00
14,600.00	89.97	359.73	7,866.06	5,602.67	460.08	5,617.81	0.00	0.00	0.00
14,700.00	89.97	359.73	7,866.10	5,702.67	459.61	5,717.68	0.00	0.00	0.00
14,800.00	89.97	359.73	7,866.15	5,802.67	459.15	5,817.56	0.00	0.00	0.00
14,900.00	89.97	359.73	7,866.20	5,902.67	458.68	5,917.43	0.00	0.00	0.00
15,000.00	89.97	359.73	7,866.25	6,002.67	458.22	6,017.31	0.00	0.00	0.00
15,100.00	89.97	359.73	7,866.29	6,102.67	457.76	6,117.18	0.00	0.00	0.00
15,200.00	89.97	359.73	7,866.34	6,202.67	457.29	6,217.06	0.00	0.00	0.00

OXY

Planning Report

Database:	HOPSPP	Local Co-ordinate Reference:	Well Heads CC 9_4 Federal Com 14H
Company:	ENGINEERING DESIGNS	TVD Reference:	25' RKB @ 2959.50ft
Project:	PRD NM DIRECTIONAL PLANS (NAD 1983)	MD Reference:	25' RKB @ 2959.50ft
Site:	Heads CC 9_4	North Reference:	Grid
Well:	Heads CC 9_4 Federal Com 14H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Permitting Plan		

Planned Survey									
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
15,300.00	89.97	359.73	7,866.39	6,302.67	456.83	6,316.93	0.00	0.00	0.00
15,400.00	89.97	359.73	7,866.44	6,402.67	456.37	6,416.80	0.00	0.00	0.00
15,500.00	89.97	359.73	7,866.49	6,502.66	455.90	6,516.68	0.00	0.00	0.00
15,600.00	89.97	359.73	7,866.53	6,602.66	455.44	6,616.55	0.00	0.00	0.00
15,700.00	89.97	359.73	7,866.58	6,702.66	454.97	6,716.43	0.00	0.00	0.00
15,800.00	89.97	359.73	7,866.63	6,802.66	454.51	6,816.30	0.00	0.00	0.00
15,900.00	89.97	359.73	7,866.68	6,902.66	454.05	6,916.17	0.00	0.00	0.00
16,000.00	89.97	359.73	7,866.72	7,002.66	453.58	7,016.05	0.00	0.00	0.00
16,100.00	89.97	359.73	7,866.77	7,102.66	453.12	7,115.92	0.00	0.00	0.00
16,200.00	89.97	359.73	7,866.82	7,202.66	452.66	7,215.80	0.00	0.00	0.00
16,300.00	89.97	359.73	7,866.87	7,302.66	452.19	7,315.67	0.00	0.00	0.00
16,400.00	89.97	359.73	7,866.91	7,402.66	451.73	7,415.54	0.00	0.00	0.00
16,500.00	89.97	359.73	7,866.96	7,502.65	451.26	7,515.42	0.00	0.00	0.00
16,600.00	89.97	359.73	7,867.01	7,602.65	450.80	7,615.29	0.00	0.00	0.00
16,700.00	89.97	359.73	7,867.06	7,702.65	450.34	7,715.17	0.00	0.00	0.00
16,800.00	89.97	359.73	7,867.10	7,802.65	449.87	7,815.04	0.00	0.00	0.00
16,900.00	89.97	359.73	7,867.15	7,902.65	449.41	7,914.92	0.00	0.00	0.00
17,000.00	89.97	359.73	7,867.20	8,002.65	448.95	8,014.79	0.00	0.00	0.00
17,100.00	89.97	359.73	7,867.25	8,102.65	448.48	8,114.66	0.00	0.00	0.00
17,200.00	89.97	359.73	7,867.30	8,202.65	448.02	8,214.54	0.00	0.00	0.00
17,300.00	89.97	359.73	7,867.34	8,302.65	447.55	8,314.41	0.00	0.00	0.00
17,400.00	89.97	359.73	7,867.39	8,402.64	447.09	8,414.29	0.00	0.00	0.00
17,500.00	89.97	359.73	7,867.44	8,502.64	446.63	8,514.16	0.00	0.00	0.00
17,600.00	89.97	359.73	7,867.49	8,602.64	446.16	8,614.03	0.00	0.00	0.00
17,700.00	89.97	359.73	7,867.53	8,702.64	445.70	8,713.91	0.00	0.00	0.00
17,800.00	89.97	359.73	7,867.58	8,802.64	445.24	8,813.78	0.00	0.00	0.00
17,900.00	89.97	359.73	7,867.63	8,902.64	444.77	8,913.66	0.00	0.00	0.00
18,000.00	89.97	359.73	7,867.68	9,002.64	444.31	9,013.53	0.00	0.00	0.00
18,100.00	89.97	359.73	7,867.72	9,102.64	443.84	9,113.40	0.00	0.00	0.00
18,200.00	89.97	359.73	7,867.77	9,202.64	443.38	9,213.28	0.00	0.00	0.00
18,300.00	89.97	359.73	7,867.82	9,302.63	442.92	9,313.15	0.00	0.00	0.00
18,400.00	89.97	359.73	7,867.87	9,402.63	442.45	9,413.03	0.00	0.00	0.00
18,500.00	89.97	359.73	7,867.92	9,502.63	441.99	9,512.90	0.00	0.00	0.00
18,600.00	89.97	359.73	7,867.96	9,602.63	441.53	9,612.78	0.00	0.00	0.00
18,677.72	89.97	359.73	7,868.00	9,680.35	441.17	9,690.40	0.00	0.00	0.00

Design Targets									
Target Name	Dip Angle (°)	Dip Dir. (°)	TVD (ft)	+N/-S (ft)	+E/-W (ft)	Northing (usft)	Easting (usft)	Latitude	Longitude
- hit/miss target - Shape									
FTP (Heads CC 9_4 - plan misses target center by 29.78ft at 8198.06ft MD (7835.23 TVD, -796.26 N, 486.78 E) - Point	0.00	0.00	7,863.00	-806.58	489.80	445,820.94	649,371.65	32.225155	-103.983967
PBHL (Heads CC 9_4 - plan hits target center - Point	0.00	0.00	7,868.00	9,680.35	441.17	456,307.04	649,323.02	32.253981	-103.984014

OXY
Planning Report

Database:	HOPSPP	Local Co-ordinate Reference:	Well Heads CC 9_4 Federal Com 14H
Company:	ENGINEERING DESIGNS	TVD Reference:	25' RKB @ 2959.50ft
Project:	PRD NM DIRECTIONAL PLANS (NAD 1983)	MD Reference:	25' RKB @ 2959.50ft
Site:	Heads CC 9_4	North Reference:	Grid
Well:	Heads CC 9_4 Federal Com 14H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Permitting Plan		

Formations					
Measured Depth (ft)	Vertical Depth (ft)	Name	Lithology	Dip (°)	Dip Direction (°)
178.50	178.50	RUSTLER			
647.50	647.50	SALADO			
1,381.50	1,381.50	CASTILE			
2,932.23	2,931.50	LAMAR			
2,967.39	2,966.50	BELL CANYON			
3,821.80	3,807.50	CHERRY CANYON			
5,135.35	5,060.50	BRUSHY CANYON			
6,829.26	6,671.50	BONE SPRING			
7,881.84	7,662.50	BONE SPRING 1ST			

Plan Annotations				
Measured Depth (ft)	Vertical Depth (ft)	Local Coordinates		Comment
		+N/-S (ft)	+E/-W (ft)	
2,408.00	2,408.00	0.00	0.00	Build 1°/100'
4,208.00	4,178.54	-264.39	93.48	Hold 18° Tangent
7,308.32	7,127.12	-1,167.64	412.84	KOP, Build & Turn 10°/100'
8,377.72	7,863.09	-619.54	488.93	Landing Point
18,677.71	7,868.00	9,680.34	441.17	TD at 18677.72' MD



Project: PRD NM DIRECTIONAL PLANS (NAD 1983)
 Site: Heads CC 9_4
 Well: Heads CC 9_4 Federal Com 14H
 Wellbore: Wellbore #1
 Design: Permitting Plan

PROJECT DETAILS: NM DIRECTIONAL PLANS (NAD 1983)

Geodetic System: US State Plane 1983
 Datum: North American Datum 1983
 Ellipsoid: GRS 1980
 Zone: New Mexico Eastern Zone

System Datum: Mean Sea Level

WELL DETAILS: Heads CC 9_4 Federal Com 14H

+N/-S	+E/-W	Northing	Ground Level: Easting	2934.50	Latitude	Longitude
0.00	0.00	446627.46	648881.89		32.227377	-103.985542



SECTION DETAILS

MD	Inc	Azi	TVD	+N/-S	+E/-W	Dleg	TFace	VSec	Annotation
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
2408.00	0.00	0.00	2408.00	0.00	0.00	0.00	0.00	0.00	Build 1°/100'
4208.00	18.00	160.53	4178.54	-264.39	93.48	1.00	160.53	-259.86	Hold 18° Tangent
7308.32	18.00	160.53	7127.12	-1167.64	412.84	0.00	0.00	-1147.64	KOP, Build & Turn 10°/100'
8377.72	89.97	359.73	7863.09	-619.54	488.93	10.00	-159.89	-596.64	Landing Point
18677.72	89.97	359.73	7868.00	9680.35	441.17	0.00	0.00	9690.40	TD at 18677.72' MD



Azimuths to Grid North
 True North: -0.19°
 Magnetic North: 6.71°

Magnetic Field
 Strength: 47854.7nT
 Dip Angle: 59.93°
 Date: 12/31/2019
 Model: HDGM_FILE

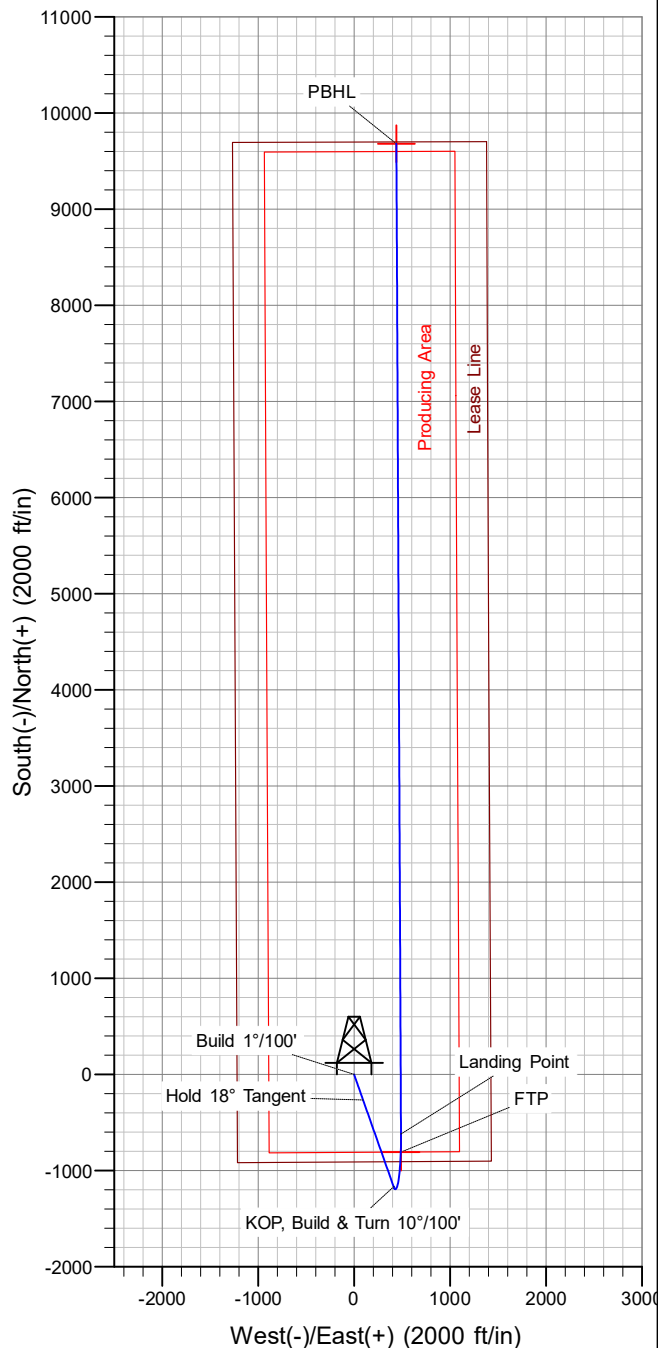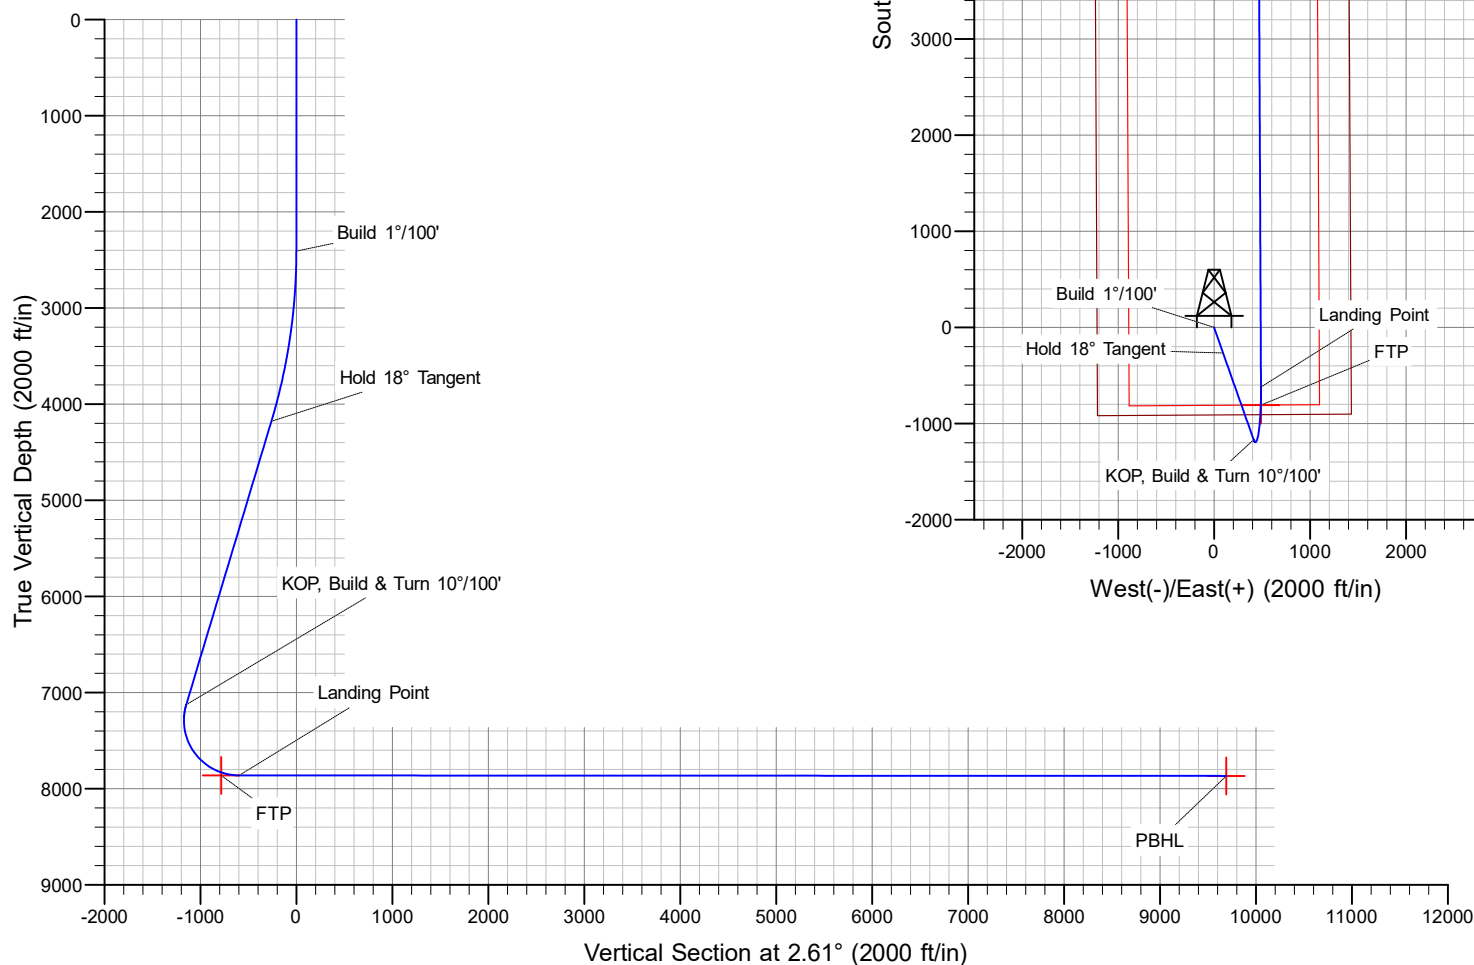

Oxy USA Inc. - Heads CC 9_4 Federal Com 14H Drill Plan

1. Geologic Formations

TVD of Target (ft):	7861	Pilot Hole Depth (ft):	
Total Measured Depth (ft):	18671	Deepest Expected Fresh Water (ft):	179

Delaware Basin

Formation	MD-RKB (ft)	TVD-RKB (ft)	Expected Fluids
Rustler	179	179	
Salado	648	648	Salt
Castile	1382	1382	Salt
Delaware	2926	2925	Oil/Gas/Brine
Bell Canyon	2967	2967	Oil/Gas/Brine
Cherry Canyon	3822	3808	Oil/Gas/Brine
Brushy Canyon	5135	5061	Losses
Bone Spring	6823	6665	Oil/Gas
Bone Spring 1st	7882	7663	Oil/Gas
Bone Spring 2nd			Oil/Gas
Bone Spring 3rd			Oil/Gas
Wolfcamp			Oil/Gas
Penn			Oil/Gas
Strawn			Oil/Gas

*H2S, water flows, loss of circulation, abnormal pressures, etc.

2. Casing Program

Section	Hole Size (in)	MD		TVD		Csg. OD (in)	Csg Wt. (ppf)	Grade	Conn.
		From (ft)	To (ft)	From (ft)	To (ft)				
Surface	14.75	0	588	0	588	10.75	45.5	J-55	BTC
Intermediate	9.875	0	7202	0	7021	7.827	39.3	P110S	Wedge 463
Production	6.75	7002	18671	6821	7861	5.5	20	P-110	Wedge 461

All casing strings will be tested in accordance with 43 CFR part 3170 Subpart 3172

All Casing SF Values will meet or exceed those below			
SF Collapse	SF Burst	Body SF Tension	Joint SF Tension
1.00	1.100	1.4	1.4

- *If Production Casing Connection OD does not meet 0.422" annular clearance inside casing:
- Cement excess will be circulated from Top of Liner to surface (Cement Confirmation)
 - Liner Top will be tested to confirm seal
 - If ICP in Bone Spring Pool and lateral landed in Wolfcamp Pool, a CBL will be ran.

	Y or N
Is casing new? If used, attach certification as required in 43 CFR 3160	Y
Does casing meet API specifications? If no, attach casing specification sheet.	Y
Is premium or uncommon casing planned? If yes attach casing specification sheet.	Y
Does the above casing design meet or exceed BLM's minimum standards? If not provide justification (loading assumptions, casing design criteria).	Y
Will the intermediate pipe be kept at a minimum 1/3 fluid filled to avoid approaching the collapse pressure rating of the casing?	Y
Is well located within Capitan Reef?	N
If yes, does production casing cement tie back a minimum of 50' above the Reef?	
Is well within the designated 4 string boundary.	
Is well located in SOPA but not in R-111-P?	N
If yes, are the first 2 strings cemented to surface and 3 rd string cement tied back 500' into previous casing?	
Is well located in R-111-P and SOPA?	N
If yes, are the first three strings cemented to surface?	
Is 2 nd string set 100' to 600' below the base of salt?	
Is well located in high Cave/Karst?	N
If yes, are there two strings cemented to surface?	
(For 2 string wells) If yes, is there a contingency casing if lost circulation occurs?	
Is well located in critical Cave/Karst?	N
If yes, are there three strings cemented to surface?	

3. Cementing Program

Section	Stage	Slurry:	Sacks	Yield (ft ³ /ft)	Density (lb/gal)	Excess:	TOC	Placement	Description
Surface	1	Surface - Tail	492	1.33	14.8	100%	-	Circulate	Class C+Accel.
Int.	1	Intermediate 1S - Tail	229	1.65	13.2	5%	5,385	Circulate	Class H+Accel., Disper., Salt
Int.	2	Intermediate 2S - Tail BH	768	1.71	13.3	25%	-	Bradenhead	Class C+Accel.
Prod.	1	Production - Tail	881	1.38	13.2	25%	7,002	Circulate	Class H+Ret., Disper., Salt

Offline Cementing Request

Oxy requests a variance to cement the 9.625" and/or 7.625" intermediate casing strings offline in accordance to the approved variance, EC Tran 461365. Please see Offline Cementing Variance attachment for further details.

Bradenhead CBL Request

Oxy requests permission to adjust the CBL requirement after bradenhead cement jobs, on 7-5/8" intermediate casings, as per the agreement reached in the OXY/BLM meeting on September 5, 2019. Please see Bradenhead CBL Variance attachment for further details.

Cement Top and Liner Overlap

- Oxy is requesting permission to have minimum fill of cement behind the 5-1/2" production liner to be 200 ft into previous casing string
The reason for this is so that we can come back and develop shallower benches from the same 7.625"/7.827" mainbore in the future
- Cement will be brought to the top of this liner hanger

4. Pressure Control Equipment

BOP installed and tested before drilling which hole?	Size?	Min. Required WP	Type		✓	Tested to:	Deepest TVD Depth (ft) per Section:
9.875" Hole	13-5/8"	5M	Annular		✓	70% of working pressure	7021
		5M	Blind Ram		✓	250 psi / 5000 psi	
			Pipe Ram				
			Double Ram		✓		
			Other*				
6.75" Hole	13-5/8"	5M	Annular		✓	70% of working pressure	7861
		5M	Blind Ram		✓	250 psi / 5000 psi	
			Pipe Ram				
			Double Ram		✓		
			Other*				

*Specify if additional ram is utilized

BOP/BOPE will be tested by an independent service company to 250 psi low and the high pressure indicated above per 43 CFR part 3170 Subpart 3172 requirements. The System may be upgraded to a higher pressure but still tested to the working pressure listed in the table above. If the system is upgraded all the components installed will be functional and tested.

Pipe rams will be operationally checked each 24 hour period. Blind rams will be operationally checked on each trip out of the hole. These checks will be noted on the daily tour sheets. Other accessories to the BOP equipment will include a Kelly cock and floor safety valve (inside BOP) and choke lines and choke manifold.

	Formation integrity test will be performed per 43 CFR part 3170 Subpart 3172. On Exploratory wells or on that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Will be tested in accordance with 43 CFR part 3170 Subpart 3172.
	A variance is requested for the use of a flexible choke line from the BOP to Choke Manifold. See attached for specs and hydrostatic test chart.
Y	Are anchors required by manufacturer?
	A multibowl or a unionized multibowl wellhead system will be employed. The wellhead and connection to the BOPE will meet all API 6A requirements. The BOP will be tested per 43 CFR part 3170 Subpart 3172 after installation on the surface casing which will cover testing requirements for a maximum of 30 days. If any seal subject to test pressure is broken the system must be tested. We will test the flange connection of the wellhead with a test port that is directly in the flange. We are proposing that we will run the wellhead through the rotary prior to cementing surface casing as discussed with the BLM on October 8, 2015. See attached schematics.

BOP Break Testing Request

Oxy requests permission to adjust the BOP break testing requirements as per the agreement reached in the OXY/BLM meeting on September 5, 2019. Please see BOP Break Testing Variance attachment for further details.

Oxy will use Cameron ADAPT wellhead system that uses an OEC top flange connection. This connection has been fully vetted and verified by API to Spec 6A and carries an API monogram.

5. Mud Program

Section	Depth - MD		Depth - TVD		Type	Weight (ppg)	Viscosity	Water Loss
	From (ft)	To (ft)	From (ft)	To (ft)				
Surface	0	588	0	588	Water-Based Mud	8.6 - 8.8	40-60	N/C
Intermediate	588	7202	588	7021	Saturated Brine-Based or Oil-Based Mud	8.0 - 10.0	35-45	N/C
Production	7202	18671	7021	7861	Water-Based or Oil-Based Mud	8.0 - 9.6	38-50	N/C

Sufficient mud materials to maintain mud properties and meet minimum lost circulation and weight increase requirements will be kept on location at all times. The following is a general list of products: Barite, Bentonite, Gypsum, Lime, Soda Ash, Caustic Soda, Nut Plug, Cedar Fiber, Cotton Seed Hulls, Drilling Paper, Salt Water Clay, CACL2. Oxy will use a closed mud system.

What will be used to monitor the loss or gain of fluid?	PVT/MD Totco/Visual Monitoring
---	--------------------------------

6. Logging and Testing Procedures

Logging, Coring and Testing.		
Yes	Will run GR from TD to surface (horizontal well – vertical portion of hole).	
	Stated logs run will be in the Completion Report and submitted to the BLM.	
No	Logs are planned based on well control or offset log information.	
No	Drill stem test? If yes, explain	
No	Coring? If yes, explain	
Additional logs planned		
No	Resistivity	Interval
No	Density	
Yes	CBL	Production string
Yes	Mud log	Bone Spring – TD
No	PEX	

7. Drilling Conditions

Condition	Specify what type and where?
BH Pressure at deepest TVD	3925 psi
Abnormal Temperature	No
BH Temperature at deepest TVD	143°F

Pump high viscosity sweeps as needed for hole cleaning. The mud system will be monitored visually/manually as well as with an electronic PVT. The necessary mud products for additional weight and fluid loss control will be on location at all times. Appropriately weighted mud will be used to isolate potential gas, oil, and water zones until such time as casing can be cemented into place for zonal

Hydrogen Sulfide (H2S) monitors will be installed prior to drilling out the surface shoe. If H2S is detected in concentrations greater than 100 ppm, the operator will comply with the provisions of 43 CFR part 3170 Subpart 3172. If Hydrogen Sulfide is encountered, measured values and formations will be provided to the BLM.

N	H2S is present
Y	H2S Plan attached

8. Other facets of operation

	Yes/No
Will the well be drilled with a walking/skidding operation? If yes, describe. We plan to drill the 2 well pad in batch by section: all surface sections, intermediate sections and production sections. The wellhead will be secured with a night cap whenever the rig is not over the well.	Yes
Will more than one drilling rig be used for drilling operations? If yes, describe. Oxy requests the option to contract a Surface Rig to drill, set surface casing, and cement for this well. If the timing between rigs is such that Oxy would not be able to preset surface, the Primary Rig will MIRU and drill the well in its entirety per the APD. Please see the attached document for information on the spudder rig.	Yes
Total Estimated Cuttings Volume: 1259 bbls	

State of New Mexico
Energy, Minerals and Natural Resources Department

Submit Electronically
Via E-permitting

Oil Conservation Division
1220 South St. Francis Dr.
Santa Fe, NM 87505

NATURAL GAS MANAGEMENT PLAN

This Natural Gas Management Plan must be submitted with each Application for Permit to Drill (APD) for a new or recompleted well.

Section 1 – Plan Description

Effective May 25, 2021

I. Operator: OXY USA INC. **OGRID:** 16696 **Date:** 0 2/ 2 6/ 2 4

II. Type: ☒ Original ☐ Amendment due to ☐ 19.15.27.9.D(6)(a) NMAC ☐ 19.15.27.9.D(6)(b) NMAC ☐ Other.

If Other, please describe: _____

III. Well(s): Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	API	ULSTR	Footages	Anticipated Oil BBL/D	Anticipated Gas MCF/D	Anticipated Produced Water BBL/D
SEE ATTACHED						

IV. Central Delivery Point Name: WHOMPING WILLOW CTB [See 19.15.27.9(D)(1) NMAC]

V. Anticipated Schedule: Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	API	Spud Date	TD Reached Date	Completion Commencement Date	Initial Flow Back Date	First Production Date
SEE ATTACHED						

VI. Separation Equipment: ☒ Attach a complete description of how Operator will size separation equipment to optimize gas capture.

VII. Operational Practices: ☒ Attach a complete description of the actions Operator will take to comply with the requirements of Subsection A through F of 19.15.27.8 NMAC.

VIII. Best Management Practices: ☒ Attach a complete description of Operator's best management practices to minimize venting during active and planned maintenance.

Section 2 – Enhanced Plan
EFFECTIVE APRIL 1, 2022

Beginning April 1, 2022, an operator that is not in compliance with its statewide natural gas capture requirement for the applicable reporting area must complete this section.

☒ Operator certifies that it is not required to complete this section because Operator is in compliance with its statewide natural gas capture requirement for the applicable reporting area.

IX. Anticipated Natural Gas Production:

Well	API	Anticipated Average Natural Gas Rate MCF/D	Anticipated Volume of Natural Gas for the First Year MCF

X. Natural Gas Gathering System (NGGS):

Operator	System	ULSTR of Tie-in	Anticipated Gathering Start Date	Available Maximum Daily Capacity of System Segment Tie-in

XI. Map. ☐ Attach an accurate and legible map depicting the location of the well(s), the anticipated pipeline route(s) connecting the production operations to the existing or planned interconnect of the natural gas gathering system(s), and the maximum daily capacity of the segment or portion of the natural gas gathering system(s) to which the well(s) will be connected.

XII. Line Capacity. The natural gas gathering system ☐ will ☐ will not have capacity to gather 100% of the anticipated natural gas production volume from the well prior to the date of first production.

XIII. Line Pressure. Operator ☐ does ☐ does not anticipate that its existing well(s) connected to the same segment, or portion, of the natural gas gathering system(s) described above will continue to meet anticipated increases in line pressure caused by the new well(s).

☐ Attach Operator's plan to manage production in response to the increased line pressure.

XIV. Confidentiality: ☐ Operator asserts confidentiality pursuant to Section 71-2-8 NMSA 1978 for the information provided in Section 2 as provided in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and attaches a full description of the specific information for which confidentiality is asserted and the basis for such assertion.

Section 3 - Certifications

Effective May 25, 2021

Operator certifies that, after reasonable inquiry and based on the available information at the time of submittal:

☒ Operator will be able to connect the well(s) to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system; or

☐ Operator will not be able to connect to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system.

If Operator checks this box, Operator will select one of the following:

Well Shut-In. ☐ Operator will shut-in and not produce the well until it submits the certification required by Paragraph (4) of Subsection D of 19.15.27.9 NMAC; or

Venting and Flaring Plan. ☐ Operator has attached a venting and flaring plan that evaluates and selects one or more of the potential alternative beneficial uses for the natural gas until a natural gas gathering system is available, including:

- (a) power generation on lease;
- (b) power generation for grid;
- (c) compression on lease;
- (d) liquids removal on lease;
- (e) reinjection for underground storage;
- (f) reinjection for temporary storage;
- (g) reinjection for enhanced oil recovery;
- (h) fuel cell production; and
- (i) other alternative beneficial uses approved by the division.

Section 4 - Notices

1. If, at any time after Operator submits this Natural Gas Management Plan and before the well is spud:

(a) Operator becomes aware that the natural gas gathering system it planned to connect the well(s) to has become unavailable or will not have capacity to transport one hundred percent of the production from the well(s), no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised venting and flaring plan containing the information specified in Paragraph (5) of Subsection D of 19.15.27.9 NMAC; or

(b) Operator becomes aware that it has, cumulatively for the year, become out of compliance with its baseline natural gas capture rate or natural gas capture requirement, no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised Natural Gas Management Plan for each well it plans to spud during the next 90 days containing the information specified in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and shall file an update for each Natural Gas Management Plan until Operator is back in compliance with its baseline natural gas capture rate or natural gas capture requirement.

2. OCD may deny or conditionally approve an APD if Operator does not make a certification, fails to submit an adequate venting and flaring plan which includes alternative beneficial uses for the anticipated volume of natural gas produced, or if OCD determines that Operator will not have adequate natural gas takeaway capacity at the time a well will be spud.

Page 8

I certify that, after reasonable inquiry, the statements in and attached to this Natural Gas Management Plan are true and correct to the best of my knowledge and acknowledge that a false statement may be subject to civil and criminal penalties under the Oil and Gas Act.

Signature: <i>Leslie T. Reeves</i>
Printed Name: LESLIE REEVES
Title: REGULATORY MANAGER
E-mail Address: LESLIE_REEVES@OXY.COM
Date: 02/26/2024
Phone: 713-497-2492
OIL CONSERVATION DIVISION (Only applicable when submitted as a standalone form)
Approved By:
Title:
Approval Date:
Conditions of Approval:

III. Well(s)

Well Name	API	WELL LOCATION (ULSTR)	Footages	ANTICIPATED OIL BBL/D	ANTICIPATED GAS MCF/D	ANTICIPATED PROD WATER BBL/D
Heads CC 9-4 Federal Com 13H	PENDING	O-Sec. 9-T24S-R29E	909' FSL 1456' FEL	1,400	5,100	2,500
Heads CC 9-4 Federal Com 14H	PENDING	O-Sec. 9-T24S-R29E	909' FSL 1426' FEL	1,400	5,100	2,500
Heads CC 9-4 Federal Com 71H	PENDING	M-Sec. 9-T24S-R29E	349' FSL 245' FWL	1,800	4,900	2,200
Heads CC 9-4 Federal Com 72H	PENDING	M-Sec. 9-T24S-R29E	349' FSL 275' FWL	1,800	4,900	2,200
Heads CC 9-4 Federal Com 73H	PENDING	B-Sec. 16-T24S-R29E	933' FNL 1984' FEL	1,800	4,900	2,200
Heads CC 9-4 Federal Com 74H	PENDING	B-Sec. 16-T24S-R29E	933' FNL 1954' FEL	1,800	4,900	2,200
Heads CC 9-4 Federal Com 75H	PENDING	M-Sec. 9-T24S-R29E	349' FSL 305' FWL	1,800	4,900	2,200
Heads CC 9-4 Federal Com 76H	PENDING	B-Sec. 16-T24S-R29E	939' FNL 1925' FEL	1,800	4,900	2,200

V. Anticipated Schedule

Well Name	API	Spud Date	TD Reached Date	Completion Commencement Date	Initial Flow Back Date	First Production Date
Heads CC 9-4 Federal Com 13H	PENDING	TBD	TBD	TBD	TBD	TBD
Heads CC 9-4 Federal Com 14H	PENDING	TBD	TBD	TBD	TBD	TBD
Heads CC 9-4 Federal Com 71H	PENDING	Aug-2025	11/05/2025	12/12/2025	01/01/2026	01/04/2026
Heads CC 9-4 Federal Com 72H	PENDING	Aug-2025	10/25/2025	12/12/2025	01/01/2026	01/04/2026
Heads CC 9-4 Federal Com 73H	PENDING	Aug-2025	12/13/2025	12/17/2025	01/02/2026	01/05/2026
Heads CC 9-4 Federal Com 74H	PENDING	Aug-2025	12/02/2025	12/17/2025	01/02/2026	01/05/2026
Heads CC 9-4 Federal Com 75H	PENDING	TBD	TBD	TBD	TBD	TBD
Heads CC 9-4 Federal Com 76H	PENDING	TBD	TBD	TBD	TBD	TBD

Part VI. Separation Equipment

Operator will size the flowback separator to handle 4,000 Bbls of fluid and 6-10 MMSCFD which is more than the expected peak rates for these wells. Each separator is rated to 1440psig, and pressure control valves and automated communication will cause the wells to shut in in the event of an upset at the facility, therefore no gas will be flared on pad during an upset. Current Oxy practices avoid use of flare or venting on pad, therefore if there is an upset or emergency condition at the facility, the wells will immediately shut down, and reassume production once the condition has cleared.

VII. Operational Practices

Gathering System and Pipeline Notification

Well(s) will be connected to a production facility after flowback operations are complete, where a gas transporter system is in place. The gas produced from production facility is dedicated to Enterprise Field Services, LLC ("Enterprise") and is connected to Enterprise low/high pressure gathering system located in Eddy County, New Mexico. OXY USA INC. ("OXY") provides (periodically) to Enterprise a drilling, completion and estimated first production date for wells that are scheduled to be drilled in the foreseeable future. In addition, OXY and Enterprise have periodic conference calls to discuss changes to drilling and completion schedules. Gas from these wells will be processed at Enterprise's Processing Plant located in Sec. 36, Twn. 24S, Rng. 30E, Eddy County, New Mexico. The actual flow of the gas will be based on compression operating parameters and gathering system pressures.

Flowback Strategy

After the fracture treatment/completion operations, well(s) will be produced to temporary production tanks and gas will be flared or vented. During flowback, the fluids and sand content will be monitored. When the produced fluids contain minimal sand, the wells will be turned to production facilities. Gas sales should start as soon as the wells start flowing through the production facilities, unless there are operational issues on Enterprise system at that time. Based on current information, it is OXY's belief the system can take this gas upon completion of the well(s).

Safety requirements during cleanout operations from the use of underbalanced air cleanout systems may necessitate that sand and non-pipeline quality gas be vented and/or flared rather than sold on a temporary basis.

VIII. Best Management Practices

Below are alternatives considered from a conceptual standpoint to reduce the amount of gas flared.

Power Generation – On lease

- o Only a portion of gas is consumed operating the generator, remainder of gas will be flared

Compressed Natural Gas – On lease

- o Gas flared would be minimal, but might be uneconomical to operate when gas volume declines

NGL Removal – On lease

- o Plants are expensive, residue gas is still flared, and uneconomical to operate when gas volume declines




Permian Drilling Hydrogen Sulfide Drilling Operations Plan

Open drill site. No homes or buildings are near the proposed location.

1. Escape

Personnel shall escape upwind of wellbore in the event of an emergency gas release. Escape can take place through the lease road on the Southeast side of the location. Personnel need to move to a safe distance and block the entrance to location. If the primary route is not an option due to the wind direction, then a secondary egress route should be taken.

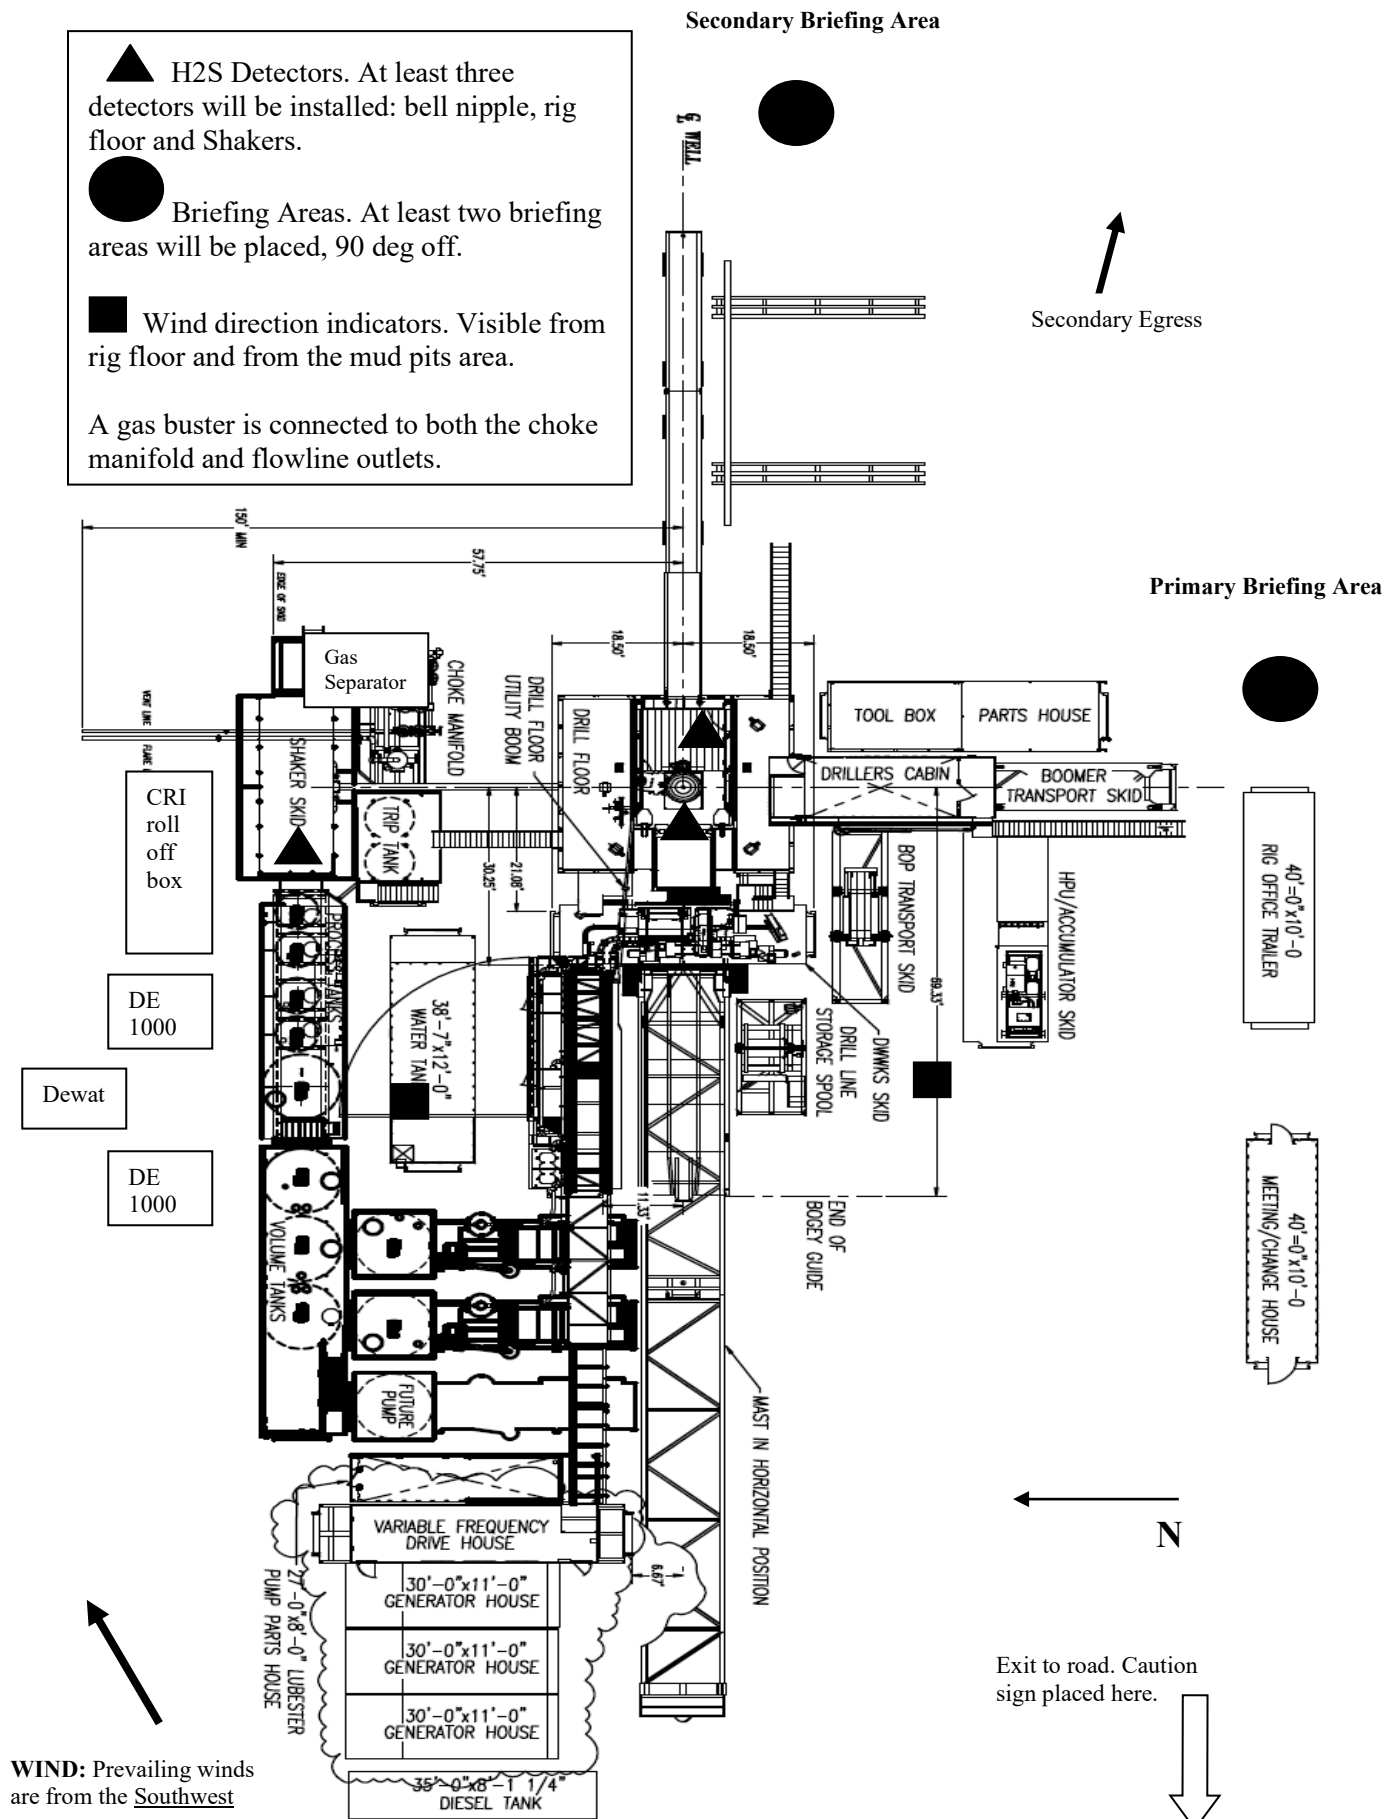



Permian Drilling Hydrogen Sulfide Drilling Operations Plan New Mexico

Scope

This contingency plan establishes guidelines for the public, all company employees, and contract employees who's work activities may involve exposure to hydrogen sulfide (H₂S) gas.

While drilling this well, it is possible to encounter H₂S bearing formations. At all times, the first barrier to control H₂S emissions will be the drilling fluid, which will have a density high enough to control influx.

Objective

1. Provide an immediate and predetermined response plan to any condition when H₂S is detected. All H₂S detections in excess of 10 parts per million (ppm) concentration are considered an Emergency.
2. Prevent any and all accidents, and prevent the uncontrolled release of hydrogen sulfide into the atmosphere.
3. Provide proper evacuation procedures to cope with emergencies.
4. Provide immediate and adequate medical attention should an injury occur.

Discussion

Implementation:	This plan with all details is to be fully implemented before drilling to <u>commence</u> .
Emergency response Procedure:	This section outlines the conditions and denotes steps to be taken in the event of an emergency.
Emergency equipment Procedure:	This section outlines the safety and emergency equipment that will be required for the drilling of this well.
Training provisions:	This section outlines the training provisions that must be adhered to prior to drilling.
Drilling emergency call lists:	Included are the telephone numbers of all persons to be contacted should an emergency exist.
Briefing:	This section deals with the briefing of all people involved in the drilling operation.
Public safety:	Public safety personnel will be made aware of any potential evacuation and any additional support needed.
Check lists:	Status check lists and procedural check lists have been included to insure adherence to the plan.
General information:	A general information section has been included to supply support information.

Hydrogen Sulfide Training

All personnel, whether regularly assigned, contracted, or employed on an unscheduled basis, will receive training from a qualified instructor in the following areas prior to commencing drilling operations on the well:

1. The hazards and characteristics of H₂S.
2. Proper use and maintenance of personal protective equipment and life support systems.
3. H₂S detection.
4. Proper use of H₂S detectors, alarms, warning systems, briefing areas, evacuation procedures and prevailing winds.
5. Proper techniques for first aid and rescue procedures.
6. Physical effects of hydrogen sulfide on the human body.
7. Toxicity of hydrogen sulfide and sulfur dioxide.
8. Use of SCBA and supplied air equipment.
9. First aid and artificial respiration.
10. Emergency rescue.

In addition, supervisory personnel will be trained in the following areas:

1. The effects of H₂S on metal components. If high tensile strength tubular is to be used, personnel will be trained in their special maintenance requirements.
2. Corrective action and shut-in procedures when drilling a well, blowout prevention and well control procedures.
3. The contents and requirements of the H₂S Drilling Operations Plan.

H₂S training refresher must have been taken within one year prior to drilling the well. Specifics on the well to be drilled will be discussed during the pre-spud meeting. H₂S and well control (choke) drills will be performed while drilling the well, at least on a weekly basis. This plan shall be available in the well site. All personnel will be required to carry the documentation proving that the H₂S training has been taken.

Service company and visiting personnel

- A. Each service company that will be on this well will be notified if the zone contains H₂S.
- B. Each service company must provide for the training and equipment of their employees before they arrive at the well site.
- C. Each service company will be expected to attend a well site

Emergency Equipment Requirements

1. **Well control equipment**

The well shall have hydraulic BOP equipment for the anticipated pressures. Equipment is to be tested on installation and follow Oxy Well Control standard, as well as 43 CFR part 3170 Subpart 3172.

Special control equipment:

- A. Hydraulic BOP equipment with remote control on ground.
Remotely operated choke.
- B. Rotating head
- C. Gas buster equipment shall be installed before drilling out of surface pipe.

2. **Protective equipment for personnel**

- A. Four (4) 30-minute positive pressure air packs (2 at each briefing area) on location.
- B. Adequate fire extinguishers shall be located at strategic locations.
- C. Radio / cell telephone communication will be available at the rig.
 - Rig floor and trailers.
 - Vehicle.

3. **Hydrogen sulfide sensors and alarms**

- A. H₂S sensor with alarms will be located on the rig floor, at the bell nipple, and at the flow line. These monitors will be set to alarm at 10 ppm with strobe light, and audible alarm.
- B. Hand operated detectors with tubes.
- C. H₂S monitor tester (to be provided by contract Safety Company.)
- D. There shall be one combustible gas detector on location at all times.

4. **Visual Warning Systems**

- A. One sign located at each location entrance with the following language:

**Caution – potential poison gas
Hydrogen sulfide
No admittance without authorization**

Wind sock – wind streamers:

- A. One 36” (in length) wind sock located at protection center, at height visible from rig floor.
- B. One 36” (in length) wind sock located at height visible from pit areas.

Condition flags

- A. One each condition flag to be displayed to denote conditions.

green – normal conditions
yellow – potential danger
red – danger, H2S present

- B. Condition flag shall be posted at each location sign entrance.

5. Mud Program

The mud program is designed to minimize the risk of having H2S and other formation fluids at surface. Proper mud weight and safe drilling practices will be applied. H2S scavengers will be used to minimize the hazards while drilling. Below is a summary of the drilling program.

Mud inspection devices:

Garrett gas train or hatch tester for inspection of sulfide concentration in mud system.

6. Metallurgy

- A. Drill string, casing, tubing, wellhead, blowout preventers, drilling spools or adapters, kill lines, choke manifold, lines and valves shall be suitable for the H2S service.
- B. All the elastomers, packing, seals and ring gaskets shall be suitable for H2S service.

7. Well Testing

No drill stem test will be performed on this well.

8. Evacuation plan

Evacuation routes should be established prior to well spud for each well and discussed with all rig personnel.

9. Designated area

- A. Parking and visitor area: all vehicles are to be parked at a predetermined safe distance from the wellhead.
- B. There will be a designated smoking area.
- C. Two briefing areas on either side of the location at the maximum allowable distance from the well bore so they offset prevailing winds perpendicularly, or at a 45-degree angle if wind direction tends to shift in the area.

Emergency procedures

- A. In the event of any evidence of H₂S level above 10 ppm, take the following steps:
 - 1. The Driller will pick up off bottom, shut down the pumps, slow down the pipe rotation.
 - 2. Secure and don escape breathing equipment, report to the upwind designated safe briefing / muster area.
 - 3. All personnel on location will be accounted for and emergency search should begin for any missing, the Buddy System will be implemented.
 - 4. Order non-essential personnel to leave the well site, order all essential personnel out of the danger zone and upwind to the nearest designated safe briefing / muster area.
 - 5. Entrance to the location will be secured to a higher level than our usual "Meet and Greet" requirement, and the proper condition flag will be displayed at the entrance to the location.
 - 6. Take steps to determine if the H₂S level can be corrected or suppressed and, if so, proceed as required.
- B. If uncontrollable conditions occur:
 - 1. Take steps to protect and/or remove any public in the down-wind area from the rig – partial evacuation and isolation. Notify necessary public safety personnel and appropriate regulatory entities (i.e. BLM) of the situation.

2. Remove all personnel to the nearest upwind designated safe briefing / muster area or off location.
3. Notify public safety personnel of safe briefing / muster area.
4. An assigned crew member will blockade the entrance to the location. No unauthorized personnel will be allowed entry to the location.
5. Proceed with best plan (at the time) to regain control of the well. Maintain tight security and safety procedures.

C. Responsibility:

1. Designated personnel.
 - a. Shall be responsible for the total implementation of this plan.
 - b. Shall be in complete command during any emergency.
 - c. Shall designate a back-up.

- All personnel:
1. On alarm, don escape unit and report to the nearest upwind designated safe briefing / muster area upw
 2. Check status of personnel (buddy system).
 3. Secure breathing equipment.
 4. Await orders from supervisor.

- Drill site manager:
1. Don escape unit if necessary and report to nearest upwind designated safe briefing / muster area.
 2. Coordinate preparations of individuals to return to point of release with tool pusher and driller (using the buddy system).
 3. Determine H2S concentrations.
 4. Assess situation and take control measures.

- Tool pusher:
1. Don escape unit Report to up nearest upwind designated safe briefing / muster area.
 2. Coordinate preparation of individuals to return to point of release with tool pusher drill site manager (using the buddy system).
 3. Determine H2S concentration.
 4. Assess situation and take control measures.

- Driller:
1. Don escape unit, shut down pumps, continue

- rotating DP.
 - 2. Check monitor for point of release.
 - 3. Report to nearest upwind designated safe briefing / muster area.
 - 4. Check status of personnel (in an attempt to rescue, use the buddy system).
 - 5. Assigns least essential person to notify Drill Site Manager and tool pusher by quickest means in case of their absence.
 - 6. Assumes the responsibilities of the Drill Site Manager and tool pusher until they arrive should they be absent.
- Derrick man
- Floor man #1
- Floor man #2
- Mud engineer:
- 1. Will remain in briefing / muster area until instructed by supervisor.
- 1. Report to nearest upwind designated safe briefing / muster area.
 - 2. When instructed, begin check of mud for ph and H2S level. (Garett gas train.)
- Safety personnel:
- 1. Mask up and check status of all personnel and secure operations as instructed by drill site manager.

Taking a kick

When taking a kick during an H2S emergency, all personnel will follow standard Well control procedures after reporting to briefing area and masking up.

Open-hole logging

All unnecessary personnel off floor. Drill Site Manager and safety personnel should monitor condition, advise status and determine need for use of air equipment.

Running casing or plugging

Following the same “tripping” procedure as above. Drill Site Manager and safety personnel should determine if all personnel have access to protective equipment.

Ignition procedures

The decision to ignite the well is the responsibility of the operator (Oxy Drilling Management). The decision should be made only as a last resort and in a situation where it is clear that:

1. Human life and property are endangered.
2. There is no hope controlling the blowout under the prevailing conditions at the well.

Instructions for igniting the well

1. Two people are required for the actual igniting operation. They must wear self-contained breathing units and have a safety rope attached. One man (tool pusher or safety engineer) will check the atmosphere for explosive gases with the gas monitor. The other man is responsible for igniting the well.
2. Primary method to ignite: 25 mm flare gun with range of approximately 500 feet.
3. Ignite upwind and do not approach any closer than is warranted.
4. Select the ignition site best for protection, and which offers an easy escape route.
5. Before firing, check for presence of combustible gas.
6. After lighting, continue emergency action and procedure as before.
7. All unassigned personnel will remain in briefing area until instructed by supervisor or directed by the Drill Site Manager.

Remember: After well is ignited, burning hydrogen sulfide will convert to sulfur dioxide, which is also highly toxic. **Do not assume the area is safe after the well is ignited.**

Status check list

Note: All items on this list must be completed before drilling to production casing point.

1. H2S sign at location entrance.
2. Two (2) wind socks located as required.
3. Four (4) 30-minute positive pressure air packs (2 at each Briefing area) on location for all rig personnel and mud loggers.
4. Air packs inspected and ready for use.
5. Cascade system and hose line hook-up as needed.
6. Cascade system for refilling air bottles as needed.
7. Condition flag on location and ready for use.
8. H2S detection system hooked up and tested.
9. H2S alarm system hooked up and tested.
10. Hand operated H2S detector with tubes on location.
11. 1 – 100' length of nylon rope on location.
12. All rig crew and supervisors trained as required.
13. All outside service contractors advised of potential H2S hazard on well.
14. No smoking sign posted and a designated smoking area identified.
15. Calibration of all H2S equipment shall be noted on the IADC report.

Checked by: _____ Date: _____

Procedural check list during H2S events

Perform each tour:

1. Check fire extinguishers to see that they have the proper charge.
2. Check breathing equipment to ensure that it is in proper working order.
3. Make sure all the H2S detection system is operative.

Perform each week:

1. Check each piece of breathing equipment to make sure that demand or forced air regulator is working. This requires that the bottle be opened and the mask assembly be put on tight enough so that when you inhale, you receive air or feel air flow.
2. BOP skills (well control drills).
3. Check supply pressure on BOP accumulator stand by source.
4. Check breathing equipment mask assembly to see that straps are loosened and turned back, ready to put on.
5. Check pressure on breathing equipment air bottles to make sure they are charged to full volume. (Air quality checked for proper air grade "D" before bringing to location)
6. Confirm pressure on all supply air bottles.
7. Perform breathing equipment drills with on-site personnel.
8. Check the following supplies for availability.
 - A. Emergency telephone list.
 - B. Hand operated H2S detectors and tubes.

General evacuation plan

1. When the company approved supervisor (Drill Site Manager, consultant, rig pusher, or driller) determines the H2S gas cannot be limited to the well location and the public will be involved, he will activate the evacuation plan.
2. Drill Site Manager or designee will notify local government agency that a hazardous condition exists and evacuation needs to be implemented.
3. Company or contractor safety personnel that have been trained in the use of H2S detection equipment and self-contained breathing equipment will monitor H2S concentrations, wind directions, and area of exposure. They will delineate the outer perimeter of the hazardous gas area. Extension to the evacuation area will be determined from information gathered.
4. Law enforcement personnel (state police, police dept., fire dept., and sheriff's dept.) Will be called to aid in setting up and maintaining road blocks. Also, they will aid in evacuation of the public if necessary.
5. After the discharge of gas has been controlled, company safety personnel will determine when the area is safe for re-entry.

Important: Law enforcement personnel will not be asked to come into a contaminated area. Their assistance will be limited to uncontaminated areas. Constant radio contact will be maintained with them.

Emergency actions

Well blowout – if emergency

1. Evacuate all personnel to “Safe Briefing / Muster Areas” or off location if needed.
2. If sour gas – evacuate rig personnel.
3. If sour gas – evacuate public within 3000 ft radius of exposure.
4. Don SCBA and shut well in if possible using the buddy system.
5. Notify Drilling Superintendent and call 911 for emergency help (fire dept and ambulance) if needed.
6. Implement the Blowout Contingency Plan, and Drilling Emergency Action Plan.
6. Give first aid as needed.

Person down location/facility

1. If immediately possible, contact 911. Give location and wait for confirmation.
2. Don SCBA and perform rescue operation using buddy system.

Toxic effects of hydrogen sulfide

Hydrogen sulfide is extremely toxic. The acceptable ceiling concentration for eight-hour exposure is 10 ppm, which is .001% by volume. Hydrogen sulfide is heavier than air (specific gravity – 1.192) and colorless. It forms an explosive mixture with air between 4.3 and 46.0 percent by volume. Hydrogen sulfide is almost as toxic as hydrogen cyanide and is between five and six times more toxic than carbon monoxide. Toxicity data for hydrogen sulfide and various other gases are compared in table i. Physical effects at various hydrogen sulfide exposure levels are shown in table ii.

Table i
Toxicity of various gases

Common name	Chemical formula	Specific gravity (sc=1)	Threshold limit (1)	Hazardous limit (2)	Lethal concentration (3)
Hydrogen Cyanide	Hcn	0.94	10 ppm	150 ppm/hr	300 ppm
Hydrogen Sulfide	H2S	1.18	10 ppm	250 ppm/hr	600 ppm
Sulfur Dioxide	So2	2.21	5 ppm	-	1000 ppm
Chlorine	Cl2	2.45	1 ppm	4 ppm/hr	1000 ppm
Carbon Monoxide	Co	0.97	50 ppm	400 ppm/hr	1000 ppm
Carbon Dioxide	Co2	1.52	5000 ppm	5%	10%
Methane	Ch4	0.55	90,000 ppm	Combustible above 5% in air	

- 1) threshold limit – concentration at which it is believed that all workers may be repeatedly exposed day after day without adverse effects.
- 2) hazardous limit – concentration that will cause death with short-term exposure.
- 3) lethal concentration – concentration that will cause death with short-term exposure.

Toxic effects of hydrogen sulfide

Table ii
Physical effects of hydrogen sulfide

Percent (%)	Ppm	Concentration Grains 100 std. Ft3*	Physical effects
0.001	<10	00.65	Obvious and unpleasant odor.

0.002	10	01.30	Safe for 8 hours of exposure.
0.010	100	06.48	Kill smell in 3 – 15 minutes. May sting eyes and throat.
0.020	200	12.96	Kills smell shortly; stings eyes and throat.
0.050	500	32.96	Dizziness; breathing ceases in a few minutes; needs prompt artificial respiration.
0.070	700	45.36	Unconscious quickly; death will result if not rescued promptly.
0.100	1000	64.30	Unconscious at once; followed by death within minutes.

*at 15.00 psia and 60'f.

Use of self-contained breathing equipment (SCBA)

1. Written procedures shall be prepared covering safe use of SCBA's in dangerous atmosphere, which might be encountered in normal operations or in emergencies. Personnel shall be familiar with these procedures and the available SCBA.
2. SCBA's shall be inspected frequently at random to insure that they are properly used, cleaned, and maintained.
3. Anyone who may use the SCBA's shall be trained in how to insure proper face-piece to face seal. They shall wear SCBA's in normal air and then wear them in a test atmosphere. (note: such items as facial hair {beard or sideburns} and eyeglasses will not allow proper seal.) Anyone that may be reasonably expected to wear SCBA's should have these items removed before entering a toxic atmosphere. A special mask must be obtained for anyone who must wear eyeglasses or contact lenses.
4. Maintenance and care of SCBA's:
 - a. A program for maintenance and care of SCBA's shall include the following:
 1. Inspection for defects, including leak checks.
 2. Cleaning and disinfecting.
 3. Repair.
 4. Storage.
 - b. Inspection, self-contained breathing apparatus for emergency use shall be inspected monthly.
 1. Fully charged cylinders.
 2. Regulator and warning device operation.
 3. Condition of face piece and connections.
 4. Rubber parts shall be maintained to keep them pliable and prevent deterioration.
 - c. Routinely used SCBA's shall be collected, cleaned and disinfected as frequently as necessary to insure proper protection is provided.
5. Persons assigned tasks that requires use of self-contained breathing equipment shall be certified physically fit (medically cleared) for breathing equipment usage at least annually.
6. SCBA's should be worn when:
 - A. Any employee works near the top or on top of any tank unless test reveals less than 10 ppm of H₂S.

- B. When breaking out any line where H₂S can reasonably be expected.
- C. When sampling air in areas to determine if toxic concentrations of H₂S exists.
- D. When working in areas where over 10 ppm H₂S has been detected.
- E. At any time there is a doubt as to the H₂S level in the area to be entered.

Rescue
First aid for H₂S poisoning

Do not panic!


Remain calm – think!

1. Don SCBA breathing equipment.
2. Remove victim(s) utilizing buddy system to fresh air as quickly as possible. (go up-wind from source or at right angle to the wind. Not down wind.)
3. Briefly apply chest pressure – arm lift method of artificial respiration to clean the victim's lungs and to avoid inhaling any toxic gas directly from the victim's lungs.
4. Provide for prompt transportation to the hospital, and continue giving artificial respiration if needed.
5. Hospital(s) or medical facilities need to be informed, before-hand, of the possibility of H₂S gas poisoning – no matter how remote the possibility is.
6. Notify emergency room personnel that the victim(s) has been exposed to H₂S gas.


Besides basic first aid, everyone on location should have a good working knowledge of artificial respiration.

Revised CM 6/27/2012

**Oxy Single Centrifuge
Closed Loop System – New
Mexico Flex III**
May 28, 2013

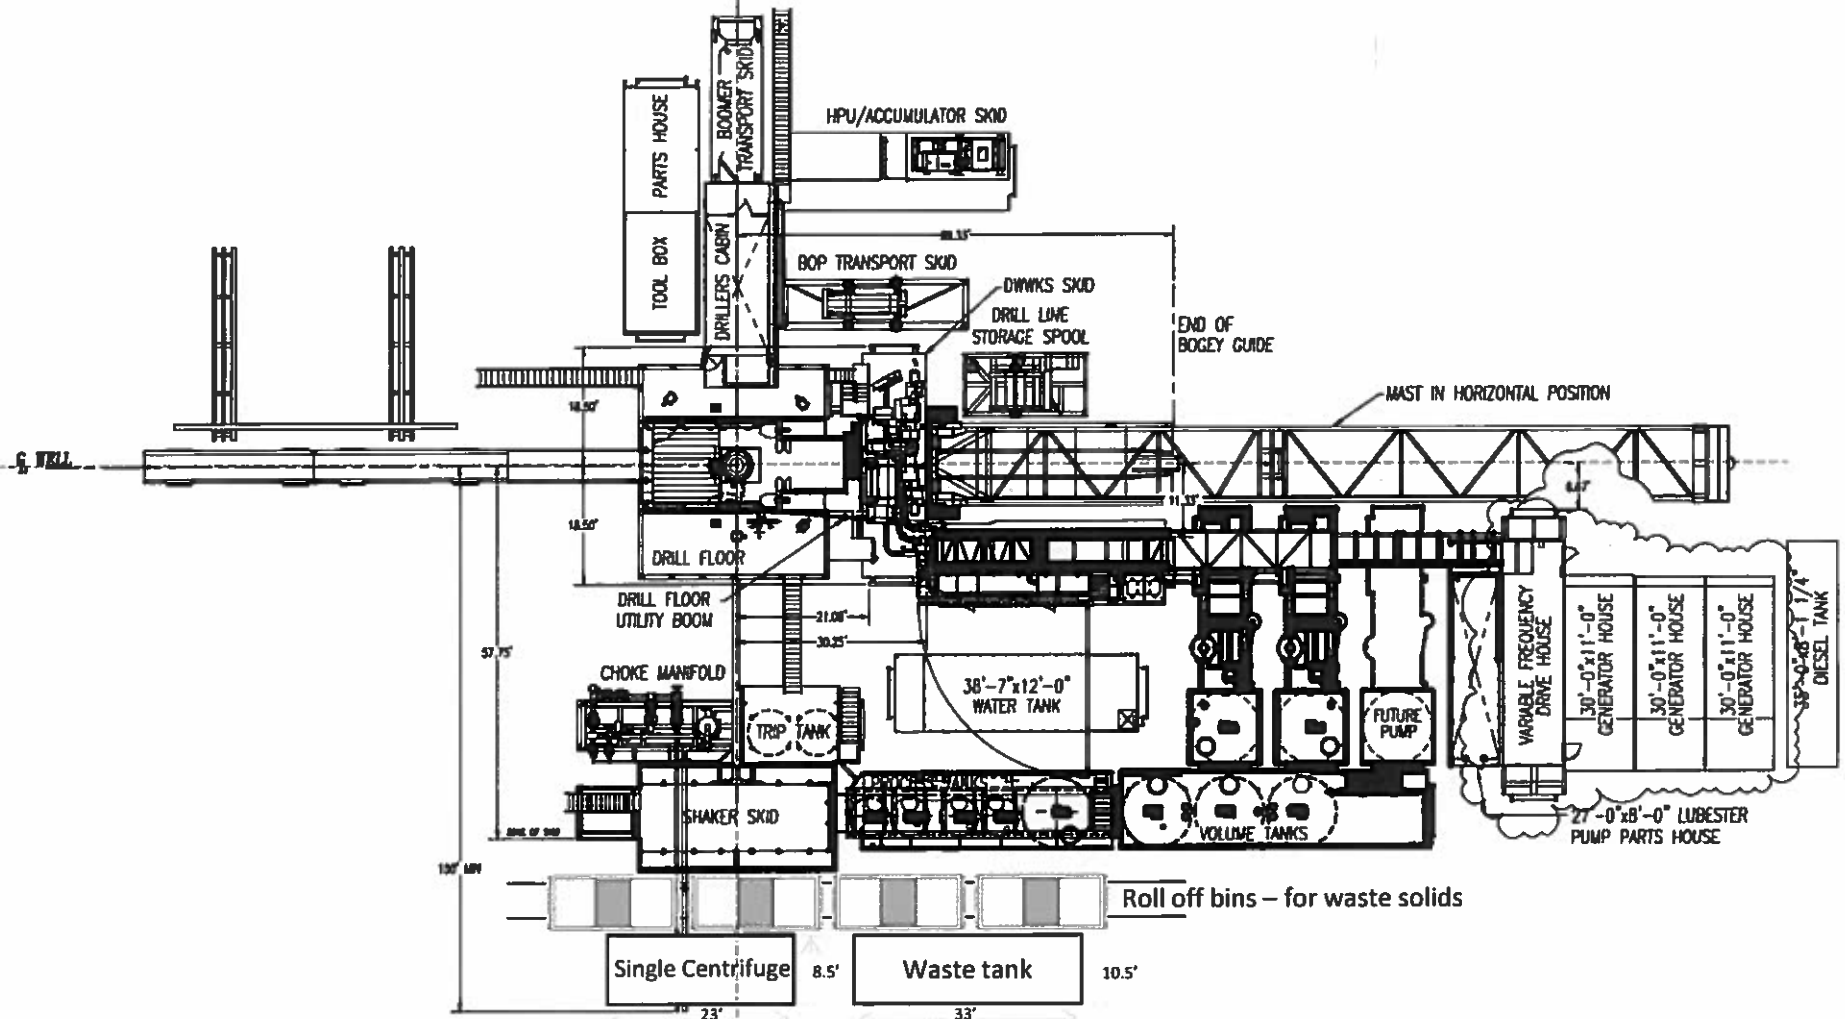

Oxy

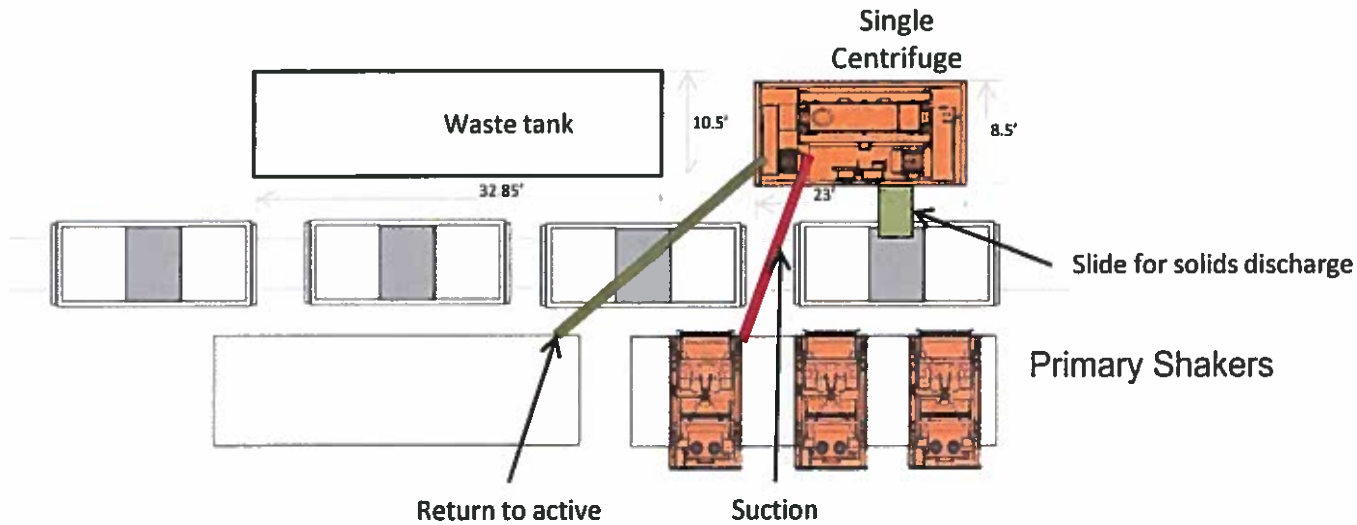

Oxy Single Centrifuge
Closed Loop System – New
Mexico Flex III
May 28, 2013

District I
1625 N. French Dr., Hobbs, NM 88240
Phone:(575) 393-6161 Fax:(575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone:(575) 748-1283 Fax:(575) 748-9720
District III
1000 Rio Brazos Rd., Aztec, NM 87410
Phone:(505) 334-6178 Fax:(505) 334-6170
District IV
1220 S. St Francis Dr., Santa Fe, NM 87505
Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 348323

CONDITIONS

Operator: OXY USA INC P.O. Box 4294 Houston, TX 772104294	OGRID:
	16696
	Action Number:
	348323
Action Type:	
[C-101] BLM - Federal/Indian Land Lease (Form 3160-3)	

CONDITIONS

Created By	Condition	Condition Date
ward.rikala	Notify OCD 24 hours prior to casing & cement	6/18/2024
ward.rikala	Will require a File As Drilled C-102 and a Directional Survey with the C-104	6/18/2024
ward.rikala	Once the well is spud, to prevent ground water contamination through whole or partial conduits from the surface, the operator shall drill without interruption through the fresh water zone or zones and shall immediately set in cement the water protection string	6/18/2024
ward.rikala	Cement is required to circulate on both surface and intermediate1 strings of casing	6/18/2024
ward.rikala	If cement does not circulate on any string, a CBL is required for that string of casing	6/18/2024
ward.rikala	Oil base muds are not to be used until fresh water zones are cased and cemented providing isolation from the oil or diesel. This includes synthetic oils. Oil based mud, drilling fluids and solids must be contained in a steel closed loop system	6/18/2024
