Received by OyCD: A6624/2024 10:00:29 A	Form C-105 1 of 4						
Office District I – (575) 393-6161	Enguery Mineuele and Metunal Deserve		Revised August 1, 2011				
1625 N. French Dr., Hobbs, NM 88240	625 N. French Dr., Hobbs, NM 88240 District II – (575) 748-1283 11 S. First St., Artesia, NM 88210 OIL CONSERVATION DIVISION		WELL API NO.				
<u>District II</u> – (575) 748-1283 811 S. First St., Artesia, NM 88210			30-025-07964				
District III - (505) 334-6178							
1000 Rio Brazos Rd., Aztec, NM 87410			5. Indicate Type of Lease STATE X FEE				
<u>District IV</u> – (505) 476-3460 1220 S. St. Francis Dr., Santa Fe, NM			6. State Oil & Gas Lease No.				
87505							
SUNDRY NOTICES	AND REPORTS ON WELLS		E-7194-0007 7. Lease Name or Uni	t Agreement Name			
(DO NOT USE THIS FORM FOR PROPOSALS TO DRILL OR TO DEEPEN OR PLUG BACK TO A							
DIFFERENT RESERVOIR. USE "APPLICATION FOR PERMIT" (FORM C-101) FOR SUCH PROPOSALS.) 1. Type of Well: Oil Well X Gas Well Other 2. Name of Operator Kratos Operating, LLC 3. Address of Operator			East Hobbs San Andres Unit				
			8. Well Number				
			914				
			9. OGRID Number				
			331946				
			10. Pool name or Wildcat				
PO Box 769, Hobbs, NM 88241			Hobbs; San Andres, East				
4. Well Location			I,				
	30feet from theNorth	line and	_1650feet from the	Westline			
Section 32	Township 18S I	Range 39E	NMPM Lea	County			
11. Elevation (Show whether DR, RKB, RT, GR, etc.)							
3601' GR							
12. Check Appropriate Box to Indicate Nature of Notice, Report or Other Data							
NOTICE OF INTENTION TO: SUBSEQUENT REPORT OF:							
PERFORM REMEDIAL WORK PLUG AND ABANDON REMEDIAL V							

SEE ATTACHED

13. Describe proposed or completed operations. (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work). SEE RULE 19.15.7.14 NMAC. For Multiple Completions: Attach wellbore diagram of

COMMENCE DRILLING OPNS.

CASING/CEMENT JOB

OTHER:

P AND A

XX

PNR

I hereby certify that the information above is true and complete to the best of my knowledge and belief.

CHANGE PLANS

MULTIPLE COMPL

proposed completion or recompletion.

SIGNATURE Cherter Title agent	DATE 6/22/2024
Type or print name M. J. Morch) Merchante-mail address: myonorch pennocoil	PHONE: (575)492-1234
APPROVED BY: King Jointee TITLE Compliance Officer A Conditions of Approval (if as y):	DATE <u>6/25/24</u>

TEMPORARILY ABANDON

PULL OR ALTER CASING

DOWNHOLE COMMINGLE

OTHER:

6/10/2024 Cleared location and set matting board. Rigged up. Pump is stuck. Made back off attempt. Shallow back off. Started laying down rods. Shut down for storm.

6/11/2024 Laid down 44 7/8" and 53 ¼" rods. Installed BOP. Dug out cellar to change the surface connections. Surface head has cement in it. Installed the BOP and worked the anchor free. POOH with tubing to rods. Continued to strip the rods and tubing for the remainder of day. 52 stands and a single and 135 rods recovered.


6/12/2024 Finished stripping rods and tubing. 131 joints 2 7/8" tubing and 166 total rods. Made gauge ring run and set cement retainer at 4175'. Squeezed under the retainer with 50 sacks Class C. Left 15 sacks cement in the tubing after displacing, stung out of the retainer and dumped cement on top of the retainer. POOH and SION.

6/13/2024 Set 5.5" CIBP at 3900'. RIH with tubing and tagged CIBP. Circulated MLF and tested casing to 550#. Good. Spot 25 sx cement on top of CIBP. POOH and top of casing with brine. Rigged up The Wireline Group and ran RBL. TOC at 3340'. Free pipe from 3340' to 604'. Cement from 604' to surface. Rig down wireline and SION.

6/17/2024 Perforated casing at 3125'. Set packer and established rate. Squeeze perfs with 50 sx Class C cement. WOC and tagged cement at 2889'. POOH and perforated at 1951'. Set packer, established rate and squeezed with 50 sx cement. Left packer set and SION.

6/18/2024 Released packer and tagged cement at 1783'. POOH and lay down packer. RIH with tubing to 654' and circulated cement to surface with 65 sx cement. Lay down tubing and rig down. Dug out and removed the wellhead. Good cement in the 7 5/8" x 5 ½". Filled up 5 ½" with 2 sx cement. Installed standard marker, removed the anchors, cleaned the pit, cleared the location and moved out.

Received by OCD: 6/24/2024 10:00:29 AM

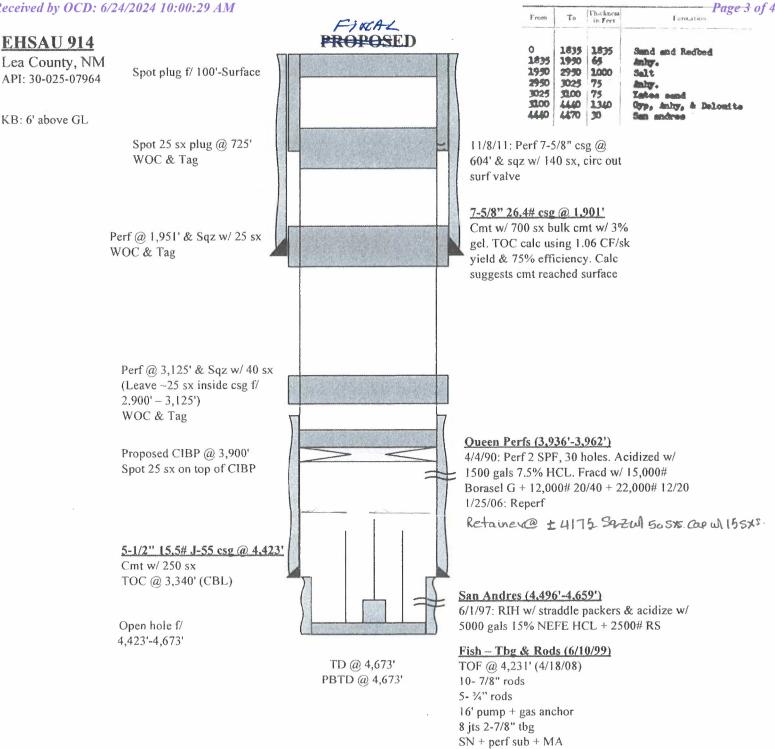

Updated

District I 1625 N. French Dr., Hobbs, NM 88240 Phone:(575) 393-6161 Fax:(575) 393-0720 District II

811 S. First St., Artesia, NM 88210 Phone:(575) 748-1283 Fax:(575) 748-9720

District III 1000 Rio Brazos Rd., Aztec, NM 87410 Phone:(505) 334-6178 Fax:(505) 334-6170

District IV 1220 S. St Francis Dr., Santa Fe, NM 87505 Phone: (505) 476-3470 Fax: (505) 476-3462

State of New Mexico Energy, Minerals and Natural Resources Oil Conservation Division 1220 S. St Francis Dr. Santa Fe, NM 87505

CONDITIONS

Operator:	OGRID:
Kratos Operating, LLC	331946
P. O. Box 769	Action Number:
Hobbs, NM 88241	356878
	Action Type:
	[C-103] Sub. Plugging (C-103P)
CONDITIONS	

Conditions				
			Condition Date	
	kfortner	Need C103Q and maker photo to release	6/25/2024	

CONDITIONS

Action 356878
