

Submit a Copy To Appropriate District  
Office  
District I – (575) 393-6161  
1625 N. French Dr., Hobbs, NM 88240  
District II – (575) 748-1283  
811 S. First St., Artesia, NM 88210  
District III – (505) 334-6178  
1000 Rio Brazos Rd., Aztec, NM 87410  
District IV – (505) 476-3460  
1220 S. St. Francis Dr., Santa Fe, NM  
87505

State of New Mexico  
Energy, Minerals and Natural Resources

Form C-103  
Revised July 18, 2013

OIL CONSERVATION DIVISION  
1220 South St. Francis Dr.  
Santa Fe, NM 87505

WELL API NO. 30-025-28349
5. Indicate Type of Lease STATE <input checked="" type="checkbox"/> FEE <input type="checkbox"/>
6. State Oil & Gas Lease No. 19552
7. Lease Name or Unit Agreement Name South Hobbs G/SA Unit
8. Well Number 146
9. OGRID Number 157984
10. Pool name or Wildcat Hobbs; Grayburg - San Andres
4. Well Location Unit Letter <u>D</u> : <u>75</u> feet from the <u>NORTH</u> line and <u>1205</u> feet from the <u>WEST</u> line Section <u>9</u> Township <u>19S</u> Range <u>38E</u> NMPM County <u>LEA</u>
11. Elevation (Show whether DR, RKB, RT, GR, etc.) 3600' (GL)

SUNDRY NOTICES AND REPORTS ON WELLS

(DO NOT USE THIS FORM FOR PROPOSALS TO DRILL OR TO DEEPEN OR PLUG BACK TO A DIFFERENT RESERVOIR. USE "APPLICATION FOR PERMIT" (FORM C-101) FOR SUCH PROPOSALS.)

1. Type of Well: Oil Well ☒ Gas Well ☐ Other

2. Name of Operator  
Occidental Permian LTD.

3. Address of Operator  
P.O. Box 4294, Houston, TX 77210

12. Check Appropriate Box to Indicate Nature of Notice, Report or Other Data

NOTICE OF INTENTION TO:

PERFORM REMEDIAL WORK ☐ PLUG AND ABANDON ☐  
TEMPORARILY ABANDON ☐ CHANGE PLANS ☐  
PULL OR ALTER CASING ☐ MULTIPLE COMPL ☐  
DOWNHOLE COMMINGLE ☐  
CLOSED-LOOP SYSTEM ☐  
OTHER: ☐

SUBSEQUENT REPORT OF:

REMEDIAL WORK ☐ ALTERING CASING ☐  
COMMENCE DRILLING OPNS. ☐ P AND A ☐  
CASING/CEMENT JOB ☐  
OTHER: ☐ OAP ☒

13. Describe proposed or completed operations. (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work). SEE RULE 19.15.7.14 NMAC. For Multiple Completions: Attach wellbore diagram of proposed completion or recompletion.

Please see procedure attached.

Spud Date:

Rig Release Date:

I hereby certify that the information above is true and complete to the best of my knowledge and belief.

SIGNATURE Roni Mathew TITLE Regulatory Advisor DATE 09/06/2023

Type or print name Roni Mathew E-mail address: roni\_mathew@oxy.com PHONE: 713.215.7827

**For State Use Only**

APPROVED BY: Kerry Fortner TITLE Compliance Officer A DATE 8/27/24  
Conditions of Approval (if any):

Well: SHOU-146

Job Summary: Well Enhancement/OAP

API: 30-25-28349

Job Dates: 11/2/2022 – 11/8/2022

11/2/22: Held TGSM, mipu, mi equipment, rupu, ru equipment, tbg had 250psi, csg had 400psi, killed well, ndwh, nubop, nu hydrill, ru workfloor, laid down esp hanger, secured well in, and sion.

11/3/22: Held TGSM, tbg had 500psi, csg had 700psi, killed well, ru spooler, pooh w/121jts, esp equipment, disassembled esp, laid down esp, rd spooler, pumps were free, motor & cable were good, equipment had a slight coat of asphaltenes, and equipment was negative on norm. Rih w/4-3/4"bit, 121jts, pu 12jts tagging TD4310', pooh w/132jts, secured well in, and sion.

11/4/22: Held TGSM, csg had 700psi, killed well, ruwl, made 6 runs to shoot new perfs@ 4110'-20', 4126'-36', 4158'-68', 4175'-90', 4200'-10', 4215'-30', 4250'-60', 4265'-80'. 3 JSPF. 90 Degree phasing. 285 total shots, rdwl, rih w/5.5"rbp&pk, 122jts, nu stripperhead, set rbp@3990', tested tools which held good, secured well in, and sion.


11/7/22: Held TGSM, tbg had 0psi, csg had 0psi, ru Petroplex acid truck, performed 3 stage pkr&plug acid job w/6000gals of 15%nefe HCL acid, flushed csg, rd acid truck, pooh w/132jts, 5.5"pkr & plug, secured well in, and sion.

11/8/22: Held TGSM, csg had 740psi, killed well, ru CT cable spooler, pu 7jts of 2-3/8"fiberglass tbg, attached ct line to tailpipe, pu esp equipment, assembled esp equipment, ru cable spooler, rih w/esp, 121jts, ran qci penetrator through hanger, landed hanger, and rd spoolers. Rd workfloor, ndbop, nuwh, hooked up flowline, installed swing arm, cleaned location, moved off location, and sion.

**SHU-146****API# 30-025-28349**

TWN 18-S; RNG 38-E

Producer

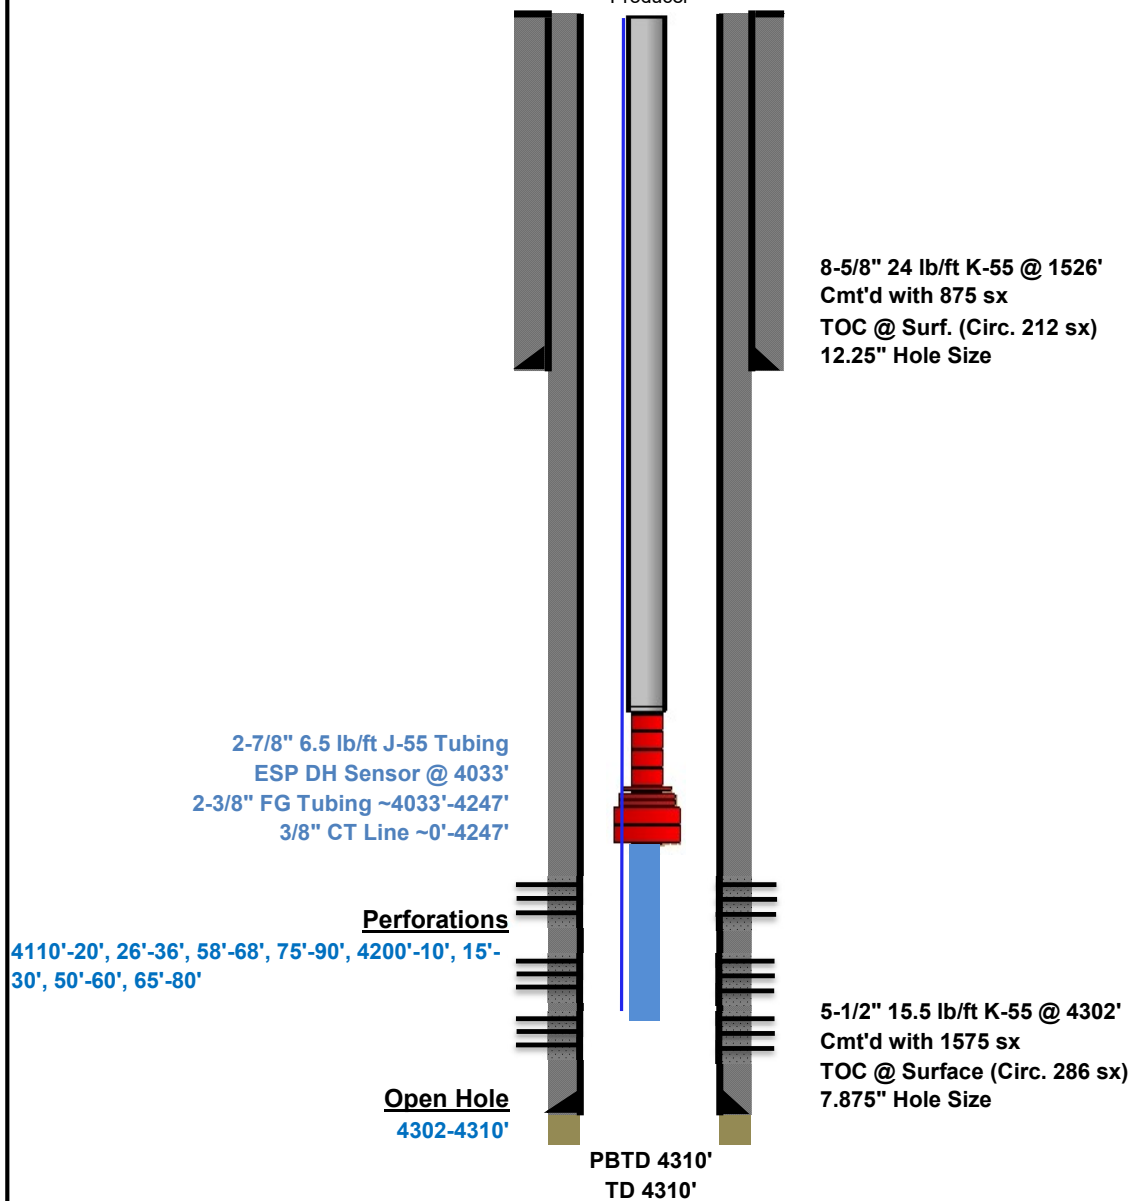

**District I**  
1625 N. French Dr., Hobbs, NM 88240  
Phone:(575) 393-6161 Fax:(575) 393-0720  
**District II**  
811 S. First St., Artesia, NM 88210  
Phone:(575) 748-1283 Fax:(575) 748-9720  
**District III**  
1000 Rio Brazos Rd., Aztec, NM 87410  
Phone:(505) 334-6178 Fax:(505) 334-6170  
**District IV**  
1220 S. St Francis Dr., Santa Fe, NM 87505  
Phone:(505) 476-3470 Fax:(505) 476-3462

**State of New Mexico**  
**Energy, Minerals and Natural Resources**  
**Oil Conservation Division**  
**1220 S. St Francis Dr.**  
**Santa Fe, NM 87505**

CONDITIONS

Action 281879

CONDITIONS

Operator: OCCIDENTAL PERMIAN LTD P.O. Box 4294 Houston, TX 772104294	OGRID: 157984
	Action Number: 281879
	Action Type: [C-103] Sub. Workover (C-103R)

CONDITIONS

Created By	Condition	Condition Date
kfortner	None	8/27/2024
