

District I
1625 N. French Dr., Hobbs, NM 88240
District II
811 S. First St., Artesia, NM 88210
District III
1000 Rio Brazos Rd., Aztec, NM 87410
District IV
1220 S. St. Francis Dr., Santa Fe, NM 87505

State of New Mexico
Energy, Minerals & Natural
Resources

Form C-104
Revised August 1, 2011

Submit one copy to appropriate District Office

Oil Conservation Division
1220 South St. Francis Dr.

☐ AMENDED REPORT

I. REQUEST FOR ALLOWABLE MINERAL AUTHORIZATION TO TRANSPORT

¹ Operator name and Address EOG RESOURCES INC PO BOX 2267 MIDLAND, TEXAS 79702		² OGRID Number 7377	
		³ Reason for Filing Code/ Effective Date NW 02/22/2022	
⁴ API Number 30 - 015-46389	⁵ Pool Name PURPLE SAGE; WOLFCAMP (GAS)		⁶ Pool Code 98220
⁷ Property Code 326217	⁸ Property Name MAS VERDE 25 FEDERAL COM		⁹ Well Number 701H

II. ¹⁰ Surface Location

Ul or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South Line	Feet from the	East/West line	County
M	25	25S	25E		720'	SOUTH	287'	WEST	EDDY

¹¹ Bottom Hole Location

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
D	24	25S	25E		339'	NORTH	344'	WEST	EDDY
¹² Lse Code	¹³ Producing Method Code FLOWING	¹⁴ Gas Connection Date	¹⁵ C-129 Permit Number		¹⁶ C-129 Effective Date		¹⁷ C-129 Expiration Date		

III. Oil and Gas Transporters

¹⁸ Transporter OGRID	¹⁹ Transporter Name and Address	²⁰ O/G/W
372812	EOGRM	OIL
151618	ENTERPRISE FIELD SERVICES	GAS
298751	REGENCY FIELD SERVICES	GAS
36785	DCP MIDSTREAM	GAS

IV. Well Completion Data

²¹ Spud Date 01/08/2020	²² Ready Date 02/22/2022	²³ TD 18,137'	²⁴ PBTD 18,102'	²⁵ Perforations 8615 - 18,102'	²⁶ DHC, MC
²⁷ Hole Size		²⁸ Casing & Tubing Size	²⁹ Depth Set		³⁰ Sacks Cement
17 1/2"		13 3/8"	380'		770 SXS CL C/CIRC
12 1/4"		9 5/8"	1689'		800 SXS CL C/CIRC
8 3/4"		7 5/8"	7301'		1115 SXS CL C/CIRC
6 3/4"		5 1/2"	18,122'		1040 CL H/TOC 5312' CBL

V. Well Test Data

³¹ Date New Oil 02/22/2022	³² Gas Delivery Date 02/22/2022	³³ Test Date 03/05/2022	³⁴ Test Length 24 HRS	³⁵ Tbg. Pressure	³⁶ Csg. Pressure 562
³⁷ Choke Size 120	³⁸ Oil 1195	³⁹ Water 9932	⁴⁰ Gas 4369		⁴¹ Test Method

⁴² I hereby certify that the rules of the Oil Conservation Division have been complied with and that the information given above is true and complete to the best of my knowledge and belief. Signature: Kay Maddox Printed name: Kay Maddox Title: SENIOR REGULATORY SPECIALIST E-mail Address: kay_maddox@eogresources.com Date: 03/23/2022	Oil Conservation Division
	Approved by: PATRICIA MARTINEZ
	Title: PETROLEUM SPECIALIST
	Approval Date: 11/15/2024
	Phone: 432-638-8475

District I
1625 N. French Dr., Hobbs, NM 88240
Phone: (575) 393-6161 Fax: (575) 393-0720

District II
811 S. First St., Artesia, NM 88210
Phone: (575) 748-1283 Fax: (575) 748-9720

District III
1000 Rio Brazos Road, Aztec, NM 87410
Phone: (505) 334-6178 Fax: (505) 334-6170

District IV
1220 S. St. Francis Dr., Santa Fe, NM 87505
Phone: (505) 476-3460 Fax: (505) 476-3462

State of New Mexico
Energy, Minerals & Natural Resources
Department
OIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, NM 87505

FORM C-102

Revised August 1, 2011

**Submit one copy to appropriate
District Office**

☐ **AMENDED REPORT**

WELL LOCATION AND ACREAGE DEDICATION PLAT

¹ API Number 30-015-46389	² Pool Code 98220	³ Pool Name PURPLE SAGE; WOLFCAMP (GAS)
⁴ Property Code 326217	⁵ Property Name MAS VERDE 25 FED COM	
⁷ OGRID No. 7377	⁸ Operator Name EOG RESOURCES, INC.	⁶ Well Number 701H ⁹ Elevation 3549'

¹⁰Surface Location


UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
M	25	25-S	25-E	-	720'	SOUTH	287'	WEST	EDDY

¹¹Bottom Hole Location If Different From Surface

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
D	24	25-S	25-E	—	339'	NORTH	344'	WEST	EDDY

¹² Dedicated Acres	¹³ Joint or Infill	¹⁴ Consolidation Code	¹⁵ Order No.
640 ACRES			

No allowable will be assigned to this completion until all interests have been consolidated or a non-standard unit has been approved by the division.

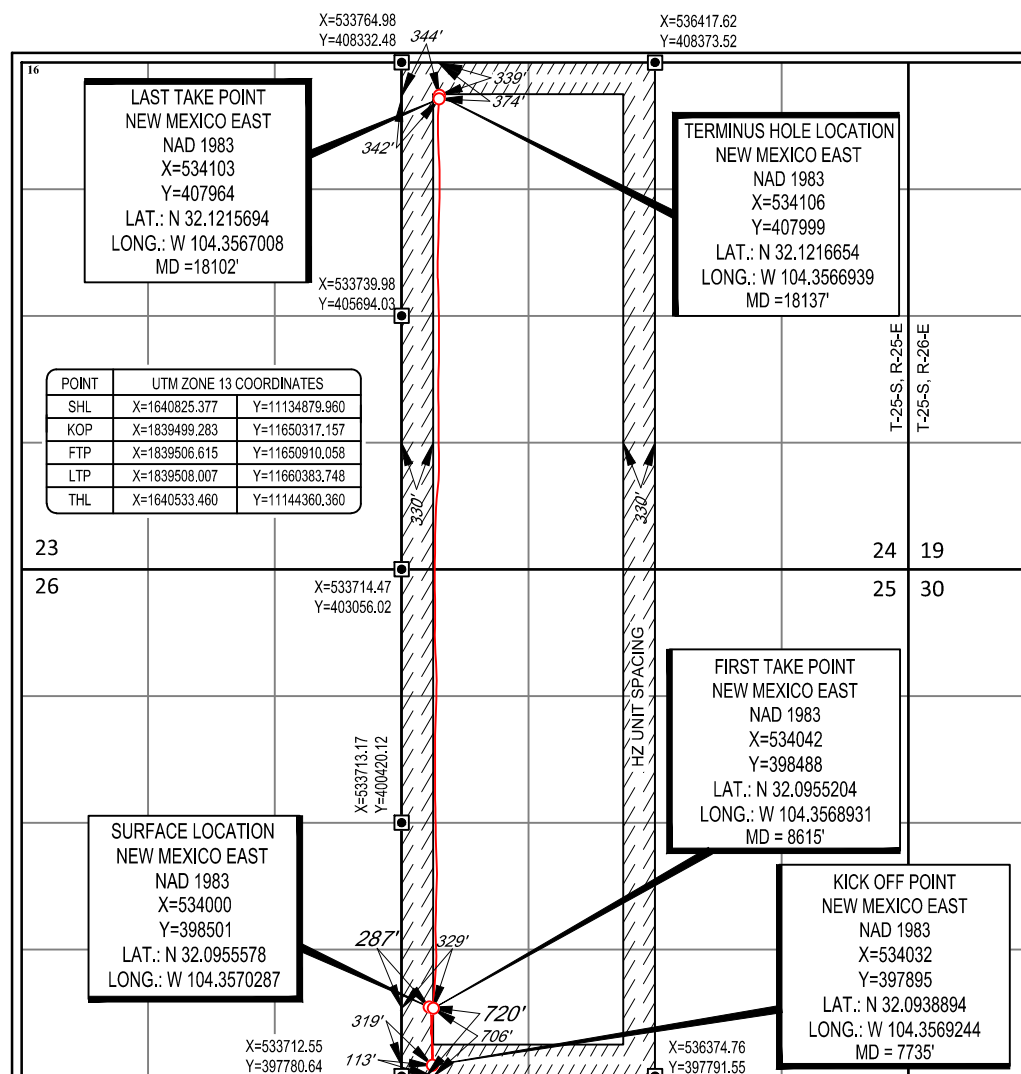

¹⁷OPERATOR CERTIFICATION

I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief, and that this organization either owns a working interest or unleased mineral interest in the land including the proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of such a mineral or working interest, or to a voluntary pooling agreement or a compulsory pooling order heretofore entered by the division.

Kay Maddox 03/22/2022
Signature Date

KAY MADDOX
Printed Name

KAY_MADDOX@EOGRESOURCES.COM


18 SURVEYOR CERTIFICATION

I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true to the best of my belief.


06/28/2018

Date of Survey _____
Signature and Seal of Professional Surveyor _____

Certificate Number

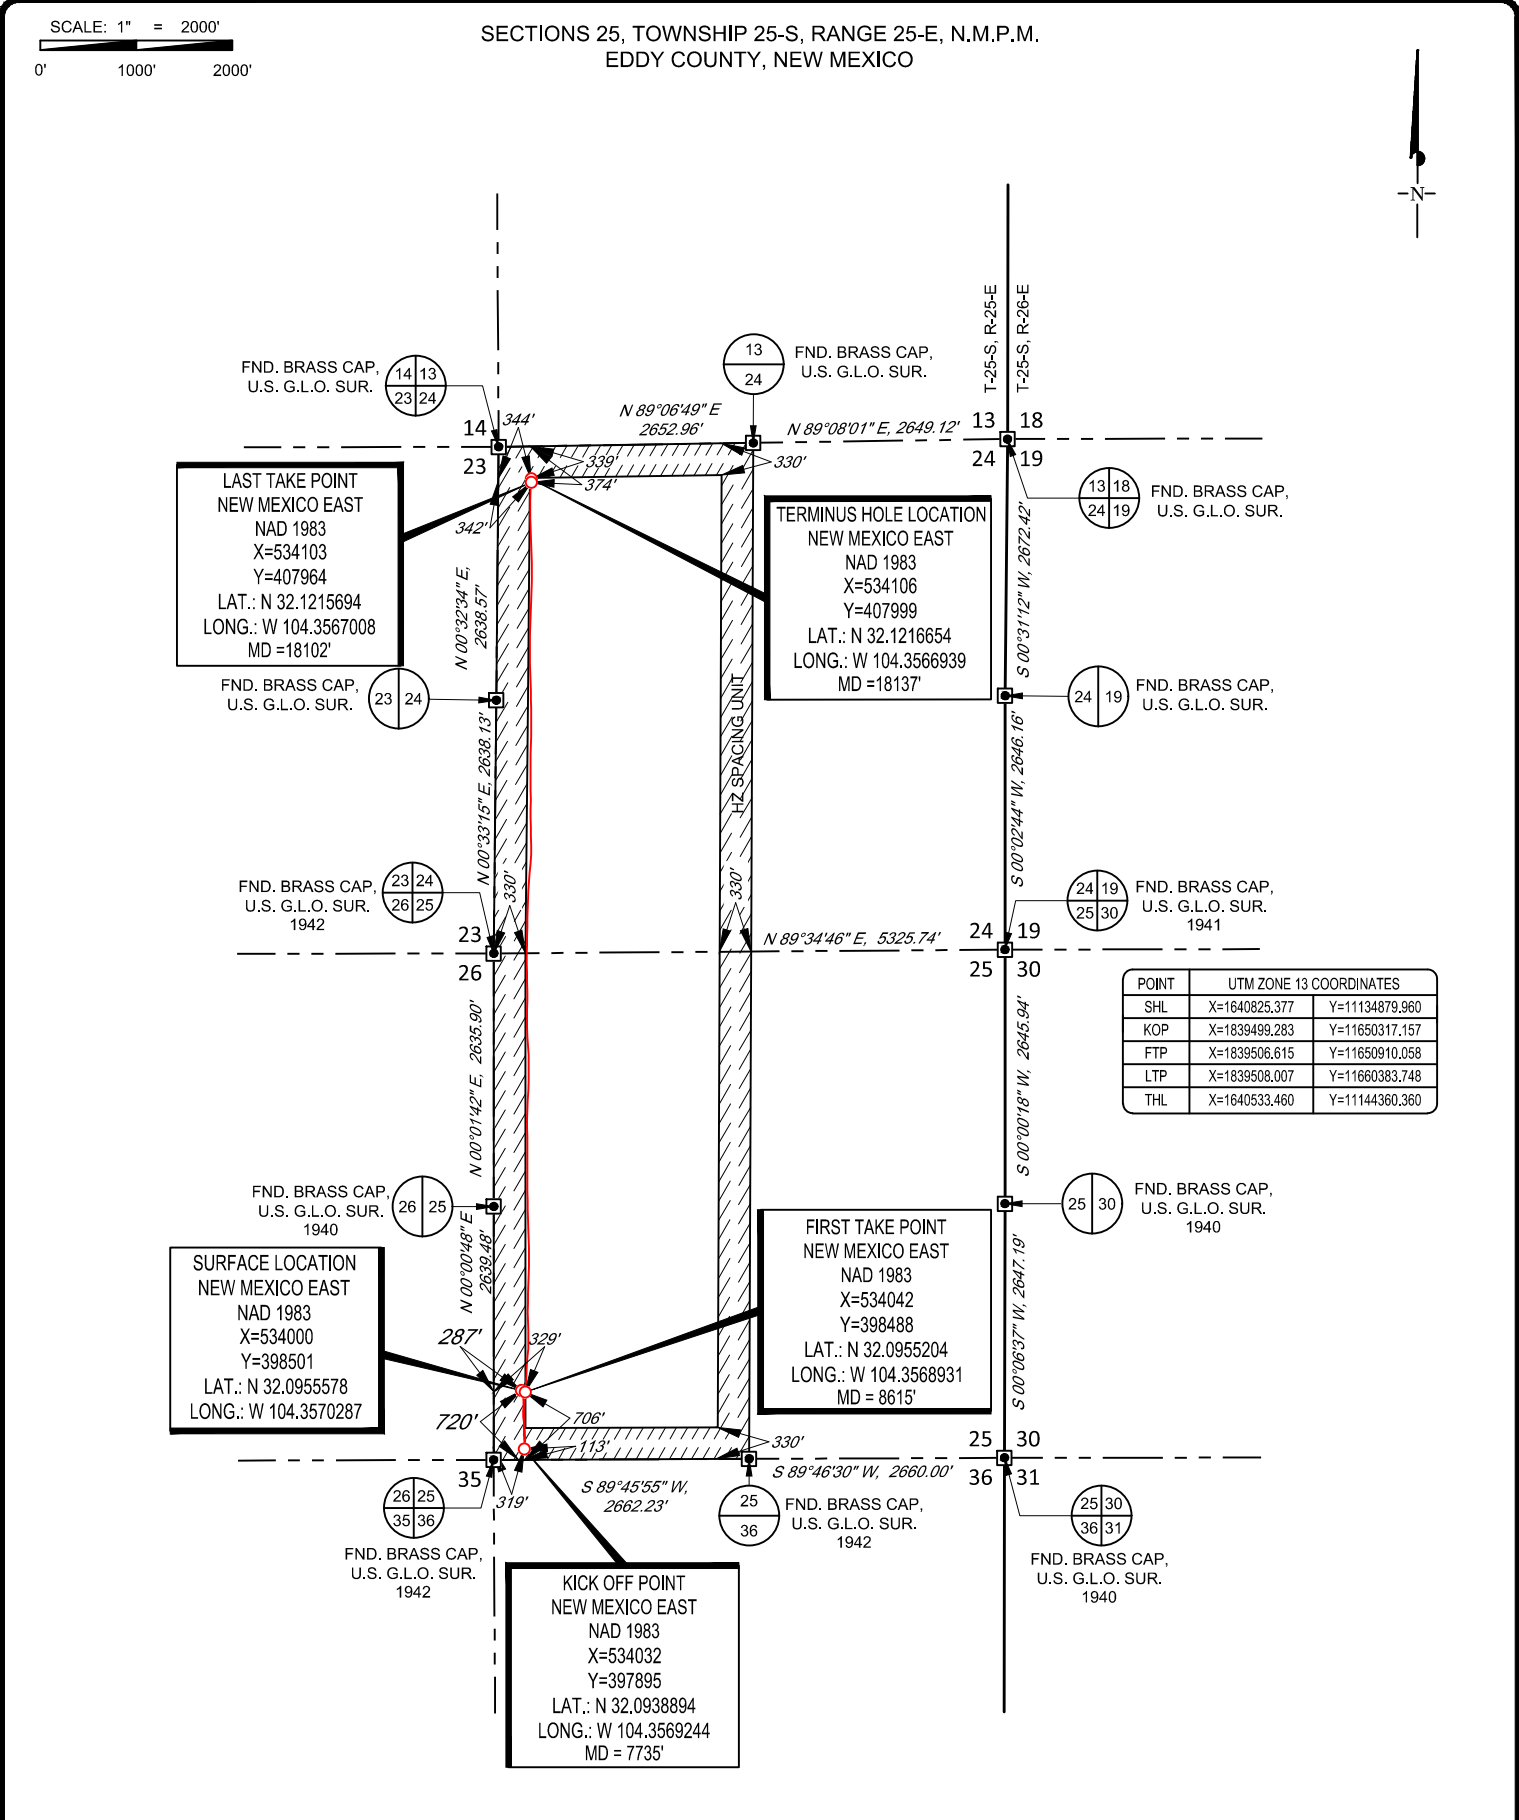

LEASE NAME & WELL NO.: MAS VERDE 25 FED COM 701H
SECTION 25 TWP 25-S RGE 25-E SURVEY N.M.P.M.
COUNTY EDDY STATE NM ELEVATION 3549'
DESCRIPTION 720' FSL & 287' FWL



TOPOGRAPHIC
LOYALTY INNOVATION LEGACY
1400 EVERMAN PARKWAY, Ste. 146 • FT. WORTH, TEXAS 76140
TELEPHONE: (817) 744-7512 • FAX (817) 744-7554
TEXAS FIRM REGISTRATION NO. 10042504
WWW.TOPOGRAPHIC.COM

Ramon A. Dominguez, P.S. No. 24508
December 27, 2021

MAS VERDE 25 FED COM 701H AS-DRILLED	REVISION:
DATE: 12/27/2021	
FILE:AD_MAS_VERDE_25_FED_COM_701H	
DRAWN BY: IMU	
SHEET: 2 OF 2	

- NOTES:
1. ORIGINAL DOCUMENT SIZE: 8.5" X 14"
 2. ALL BEARINGS, DISTANCES, AND COORDINATE VALUES CONTAINED HEREIN ARE GRID BASED UPON THE NEW MEXICO COORDINATE SYSTEM OF 1983, EAST ZONE, U.S. SURVEY FEET.
 3. THIS WELL LOCATION SHOWN HEREON HAS BEEN SURVEYED ON THE GROUND UNDER MY SUPERVISION AND PREPARED ACCORDING TO THE EVIDENCE FOUND AT THE TIME OF SURVEY, AND DATA PROVIDED BY EOG RESOURCES, INC. THIS CERTIFICATION IS MADE AND LIMITED TO THOSE PERSONS OR ENTITIES SHOWN ON THE FACE OF THIS PLAT AND IS NON-TRANSFERABLE. THIS SURVEY IS CERTIFIED FOR THIS TRANSACTION ONLY.
 4. ADJOINER INFORMATION SHOWN FOR INFORMATIONAL PURPOSES ONLY.



Eddy County, NM (NAD 83 NME)

Mas Verde 25 Federal Com #701H

Plan #1

Azimuths to Grid North
True North: 0.01°
Magnetic North: 7.06°








Magnetic Field
Strength: 47534.5nT
Dip Angle: 59.79°
Date: 10/29/2019
Model: IGRF2015

To convert a Magnetic Direction to a Grid Direction, Add 7.06°
To convert a Magnetic Direction to a True Direction, Add 7.05° East
To convert a True Direction to a Grid Direction, Add 0.01°

PROJECT DETAILS: Eddy County, NM (NAD 83 NME)			
Geodetic System: US State Plane 1983			
Datum: North American Datum 1983			
Ellipsoid: GRS 1980			
Zone: New Mexico Eastern Zone			
System Datum: Mean Sea Level			
WELL DETAILS: #701H			
KB = 25 @ 3574.0usft			
Northings	Easting	Latitude	Longitude
398501.00	534000.00	32° 5' 44.003 N	104° 21' 25.302 W

SECTION DETAILS									
Sec	MD	Inc	Azi	TVD	+N/-S	+E/-W	Dleg	TFace	VSect
1	7649.0	3.41	182.18	7612.3	-644.5	40.6	0.00	0.00	-644.1
2	7737.0	3.31	178.94	7700.2	-649.6	40.6	0.24	-119.38	-649.2
3	8671.3	90.13	0.29	8306.2	-76.4	44.2	10.00	-178.65	-76.0
4	11503.4	90.13	0.29	8300.0	2755.6	58.4	0.00	0.00	2756.0
5	11536.6	90.79	0.29	8299.7	2788.9	58.5	2.00	-0.01	2789.3
6	13256.6	90.79	0.29	8276.0	4508.6	67.1	0.00	0.00	4509.0
7	13268.3	90.56	0.29	8275.9	4520.4	67.2	2.00	180.00	4520.8
8	16347.8	90.56	0.29	8246.0	7599.6	82.5	0.00	0.00	7600.0
9	16353.5	90.44	0.29	8245.9	7605.4	82.6	2.00	-180.00	7605.8
10	17647.8	90.44	0.29	8236.0	8899.6	89.0	0.00	0.00	8900.0
11	17665.3	90.09	0.29	8235.9	8917.1	89.1	2.00	180.00	8917.5
12	18244.3	90.09	0.29	8235.0	9496.1	92.0	0.00	0.00	9496.5

WELLBORE TARGET DETAILS (MAP CO-ORDINATES)					
Name	TVD	+N/-S	+E/-W	Northings	Easting
KOP (MV 25 FC #701H)	7732.0	-669.0	43.0	397832.00	534043.00
PBHL (MV 25 FC #701H)	8235.0	9496.1	92.0	407997.10	534092.00
TGT 4 (MV 25 FC #701H)	8236.0	8899.6	89.0	407400.60	534089.02
TGT 3 (MV 25 FC #701H)	8246.0	7599.6	82.5	406100.60	534082.54
TGT 2 (MV 25 FC #701H)	8276.0	4508.6	67.1	403009.60	534067.12
TGT 1 (MV 25 FC #701H)	8300.0	2755.6	58.4	401256.60	534058.37
FTP (MV 25 FC #701H)	8315.2	-389.0	43.0	398112.00	534043.00
Fed PP (MV 25 FC #701H)	8358.0	4557.0	45.0	403058.00	534045.00

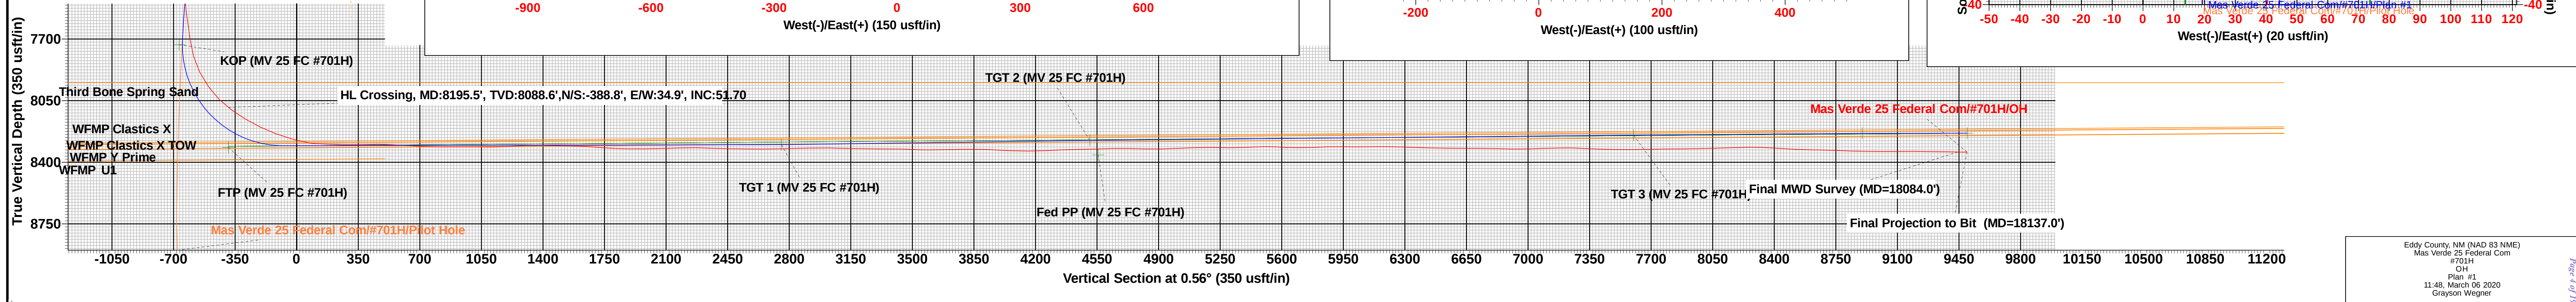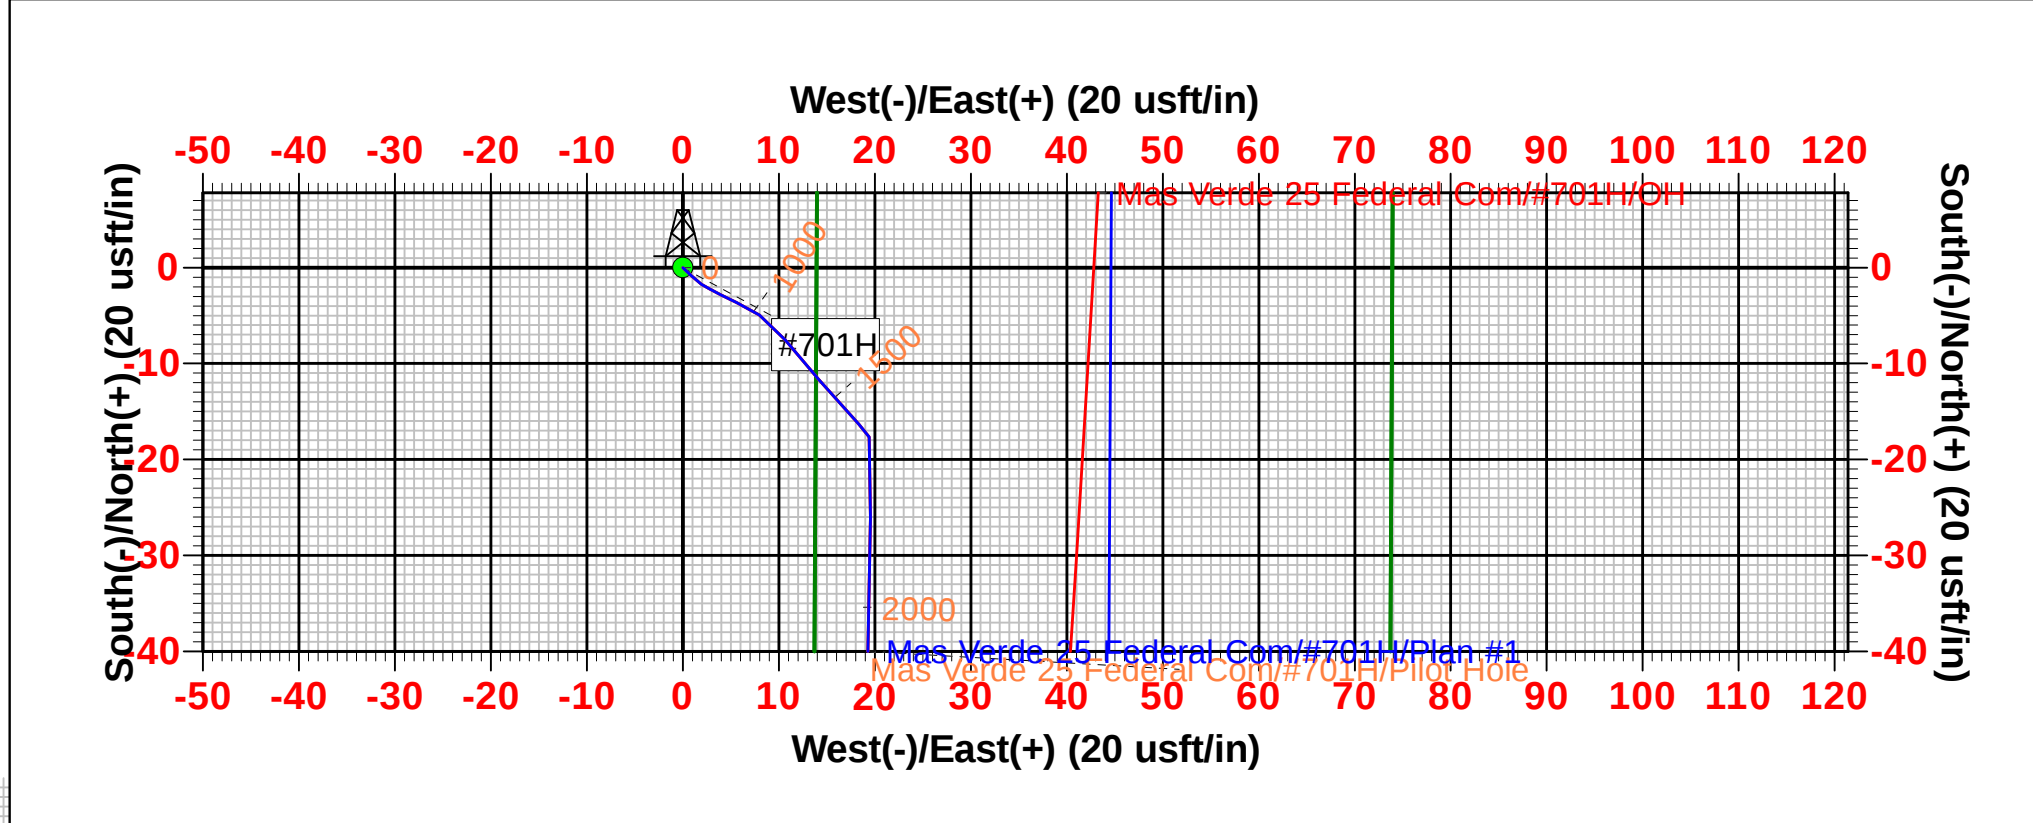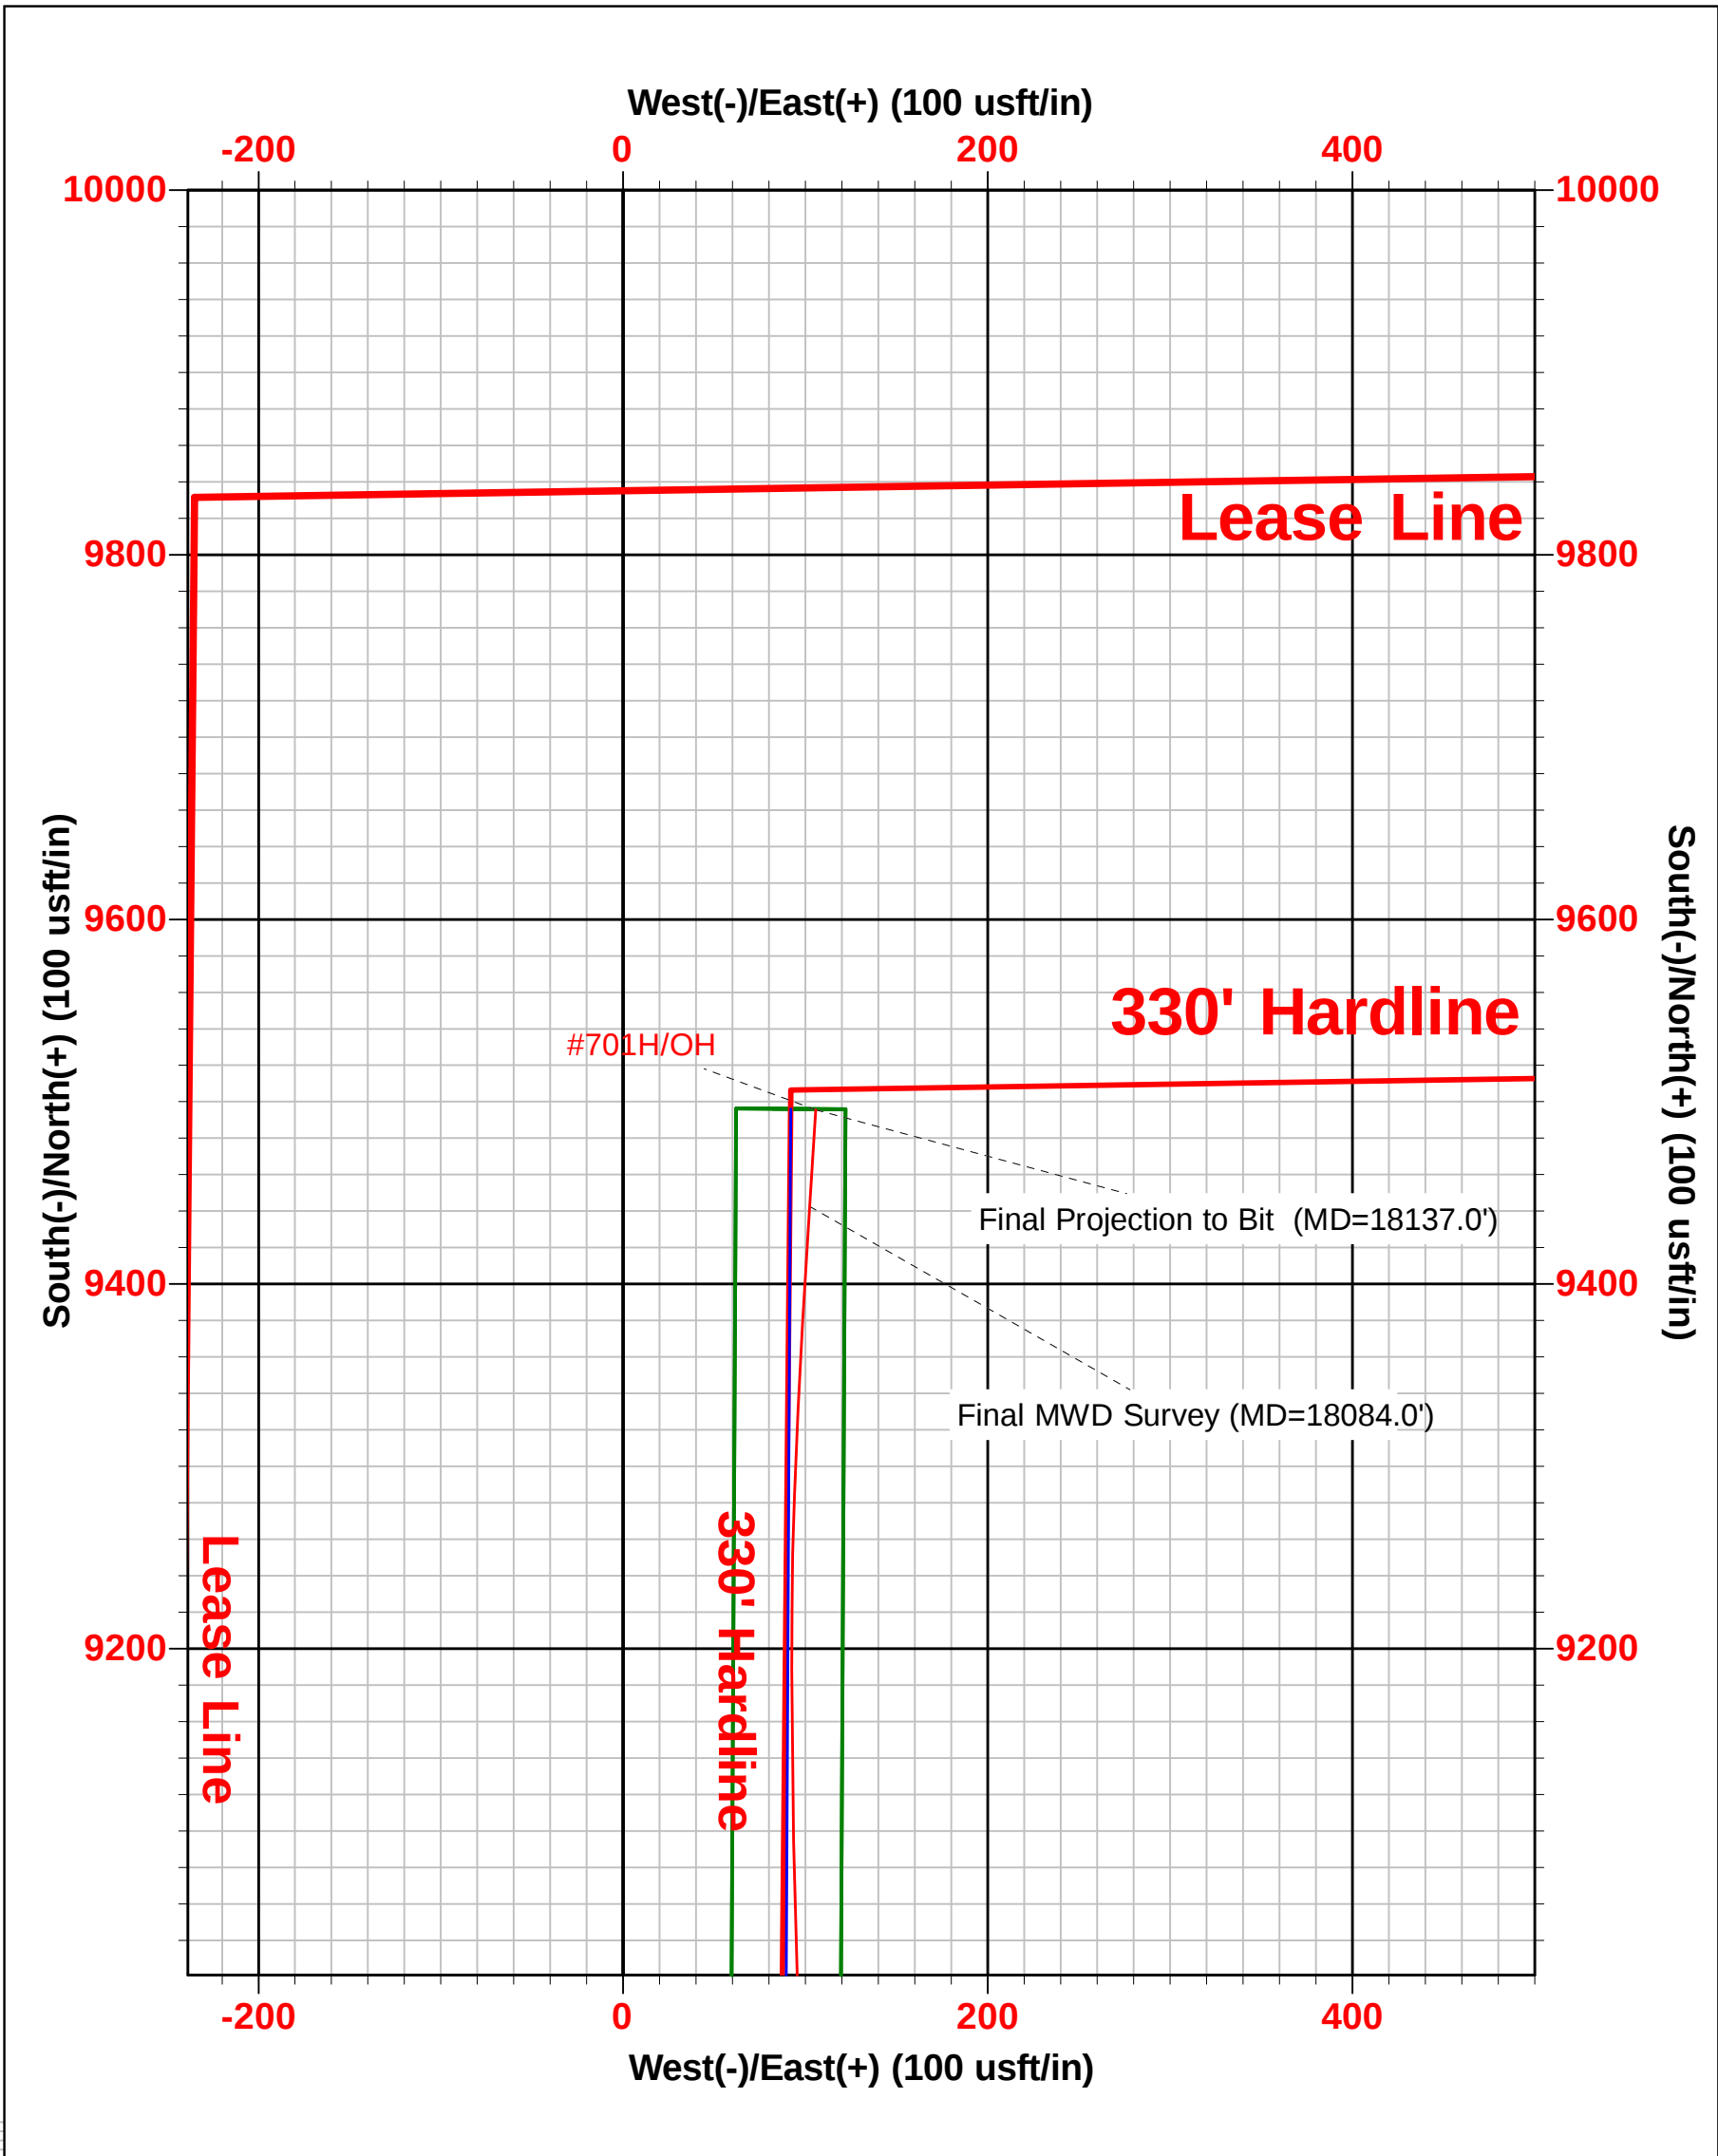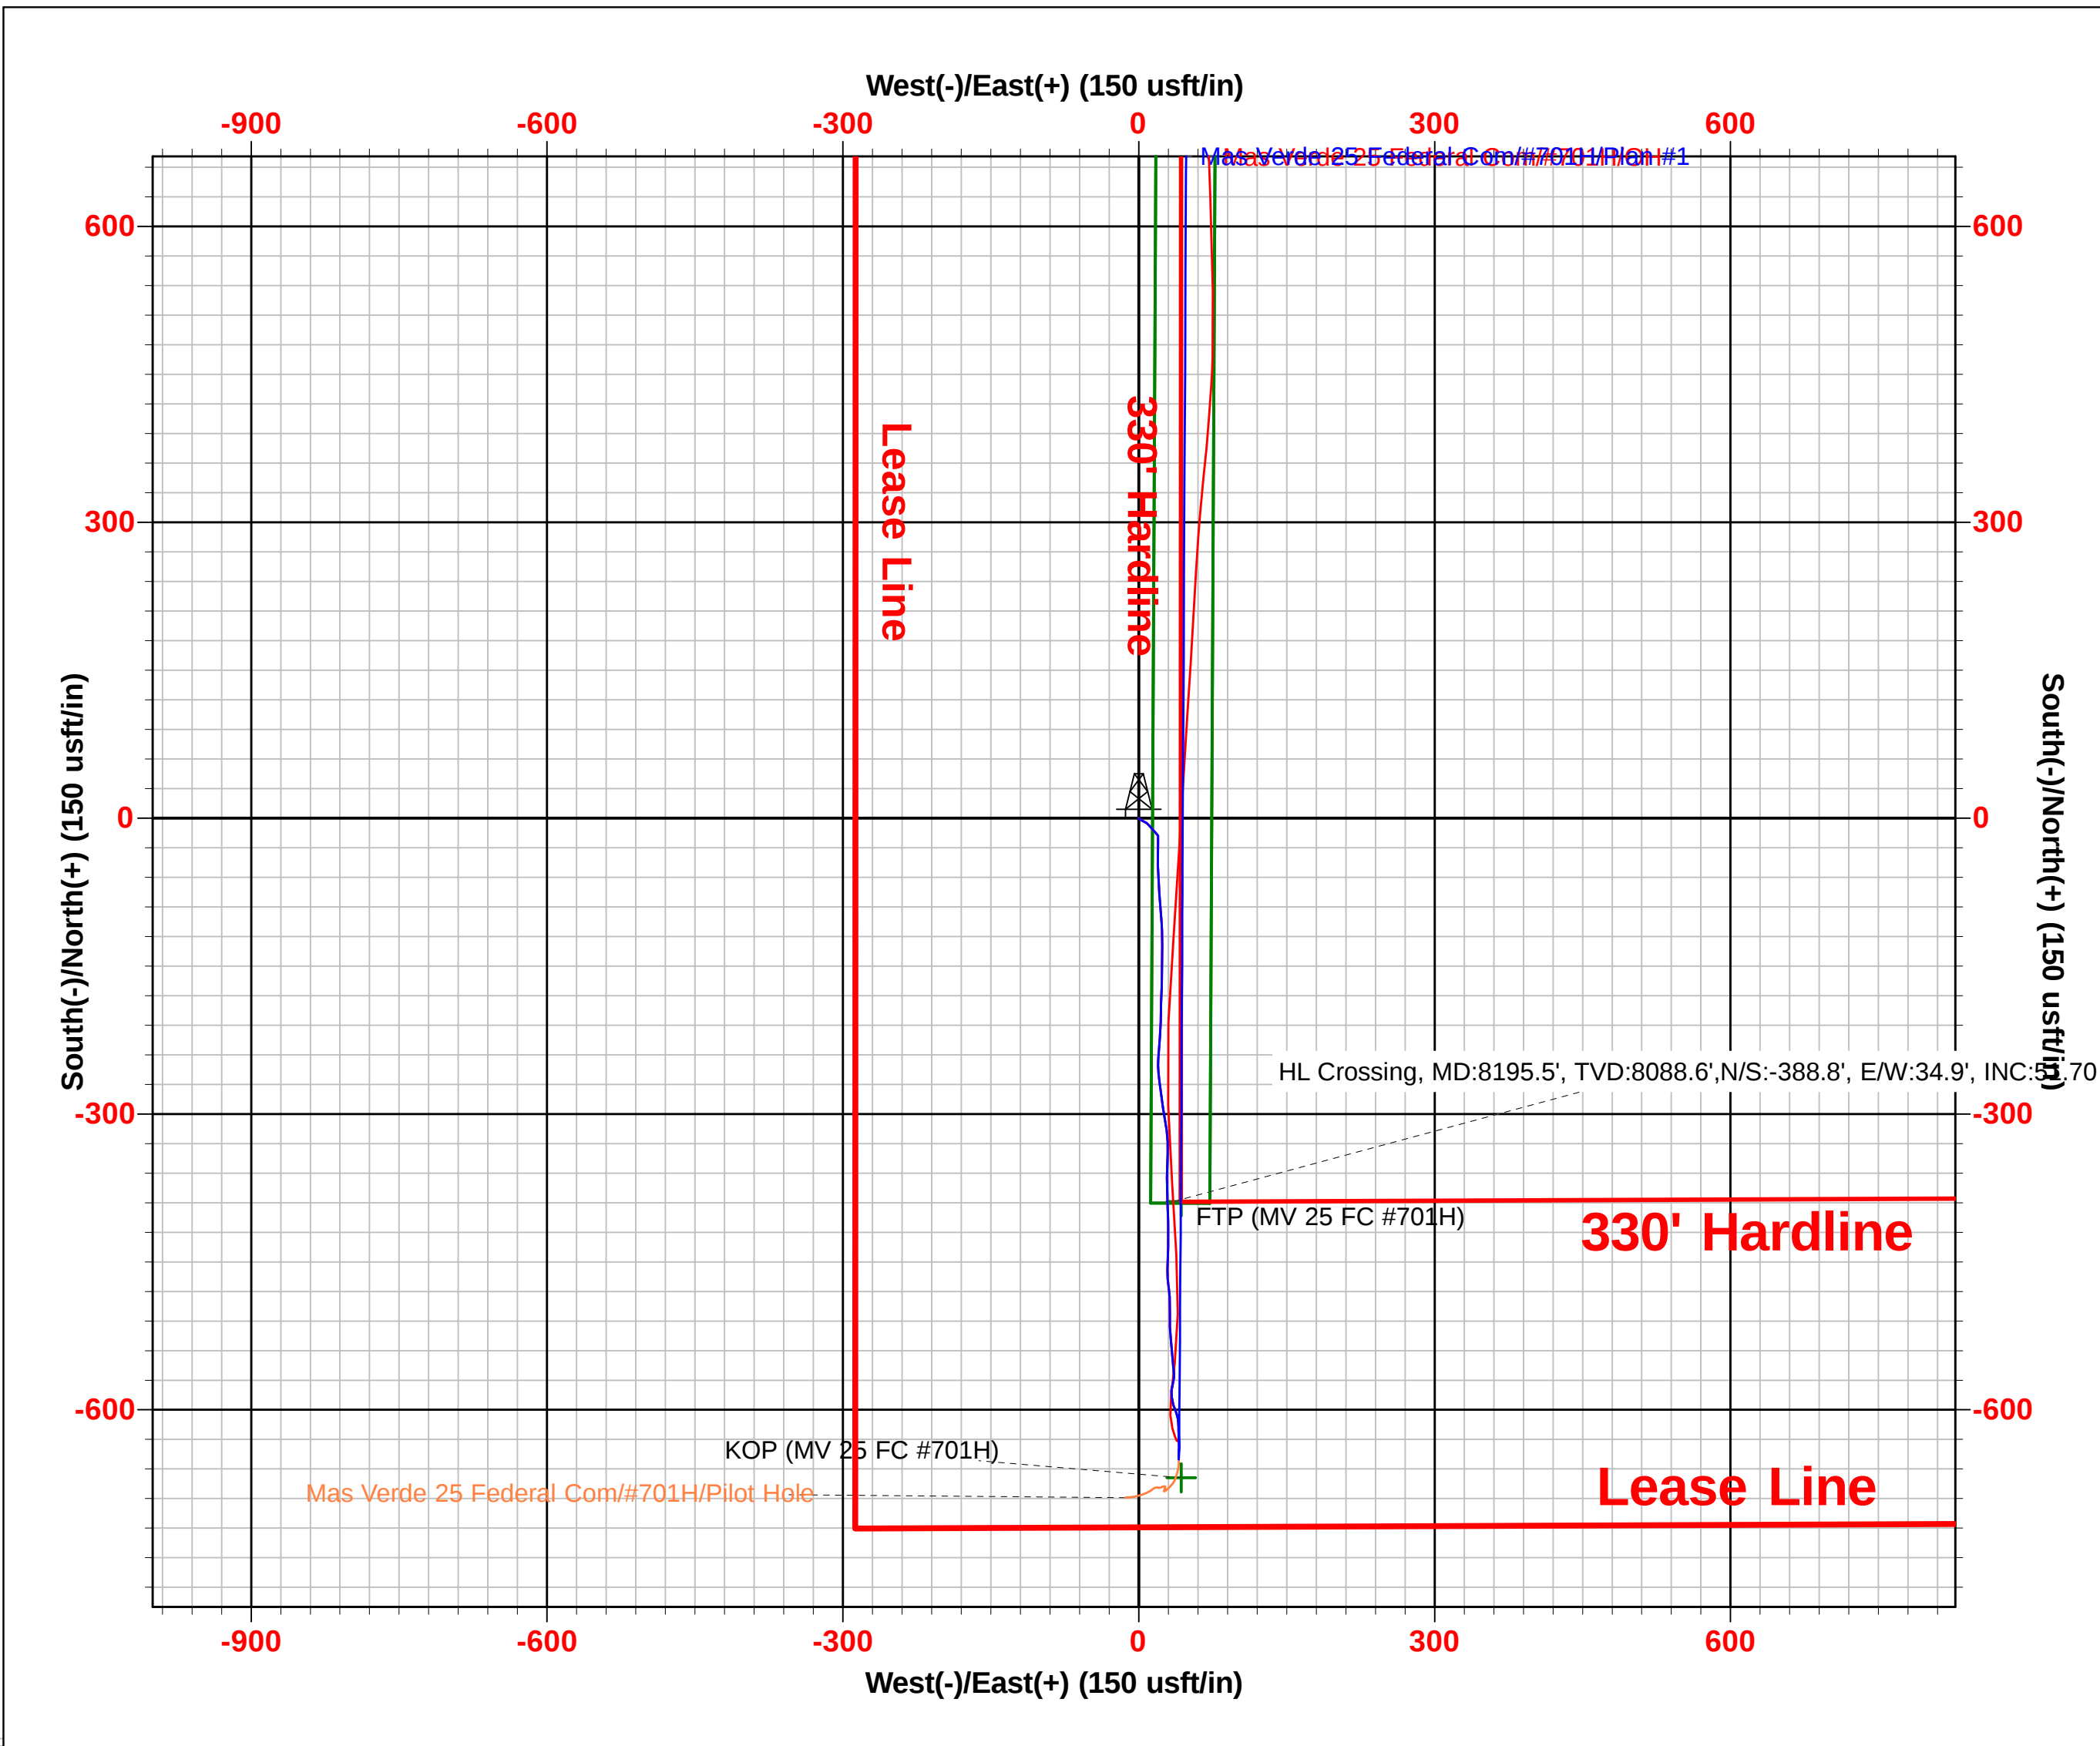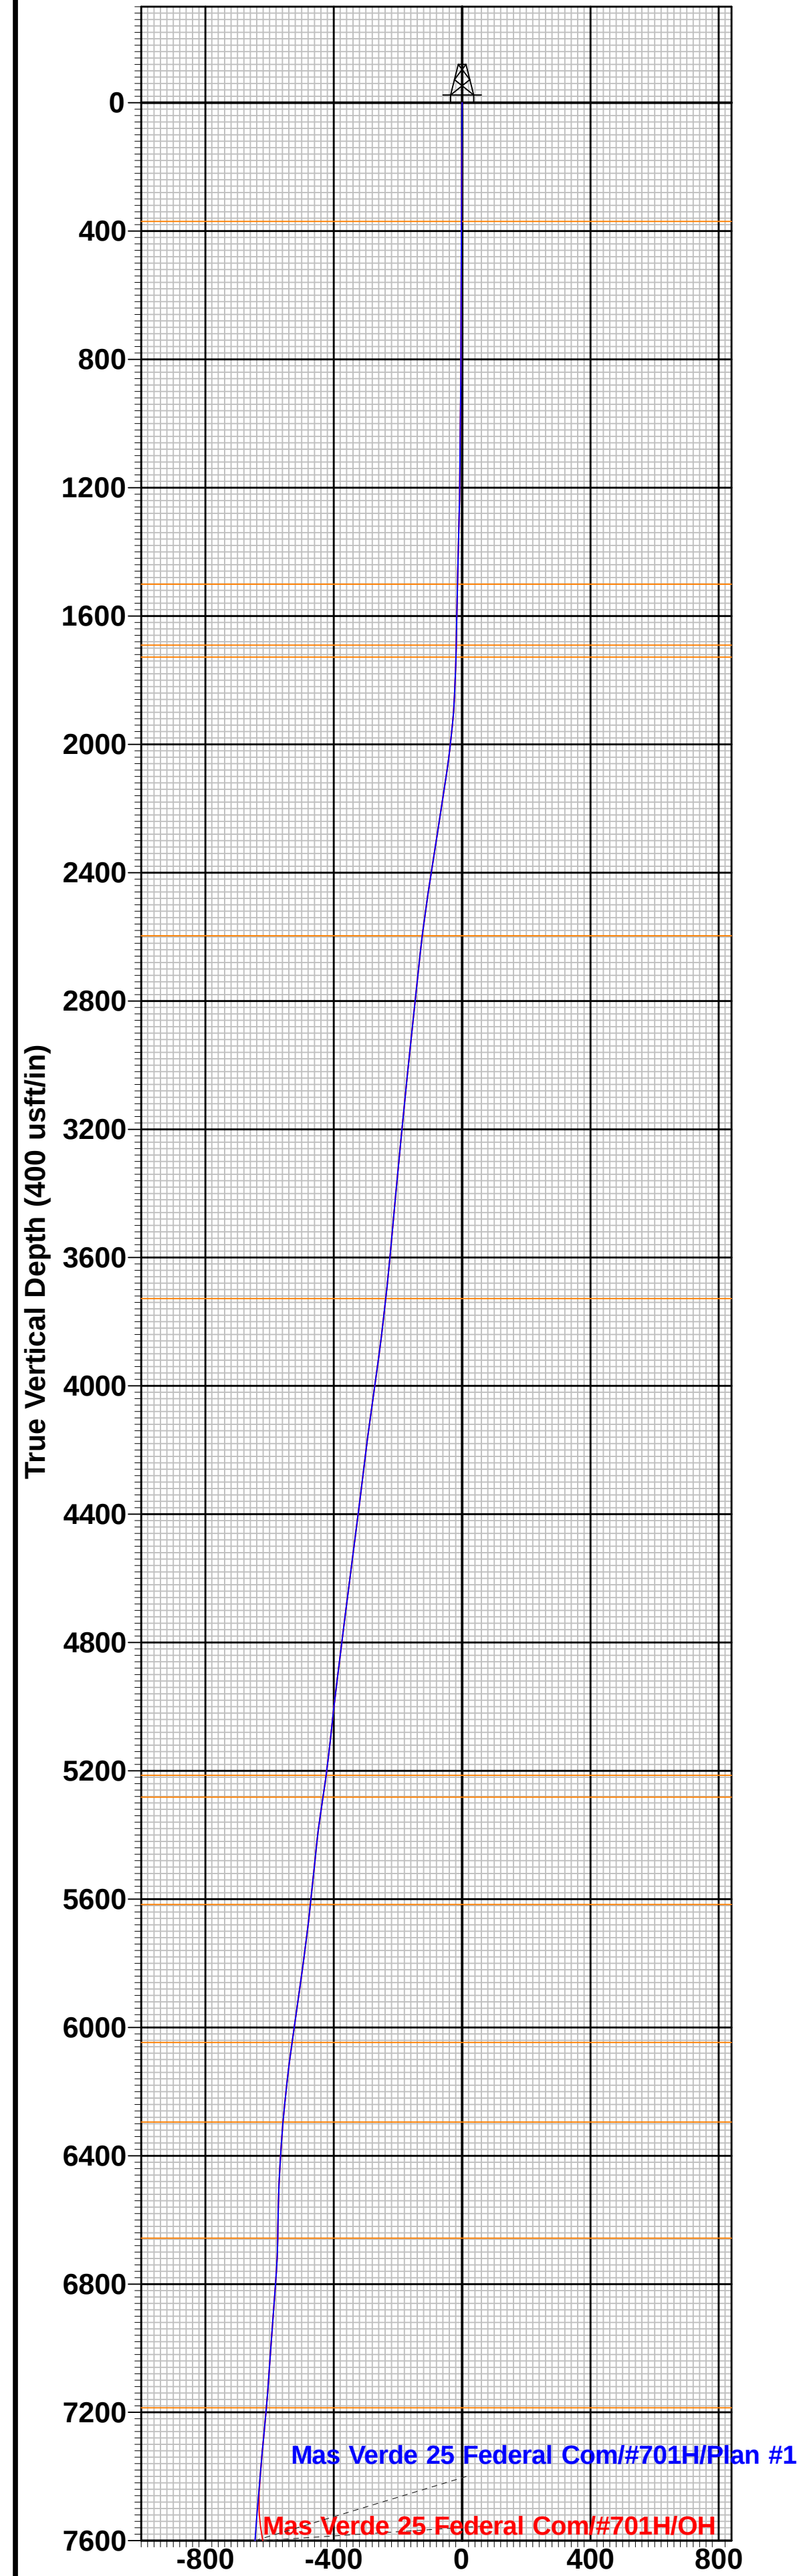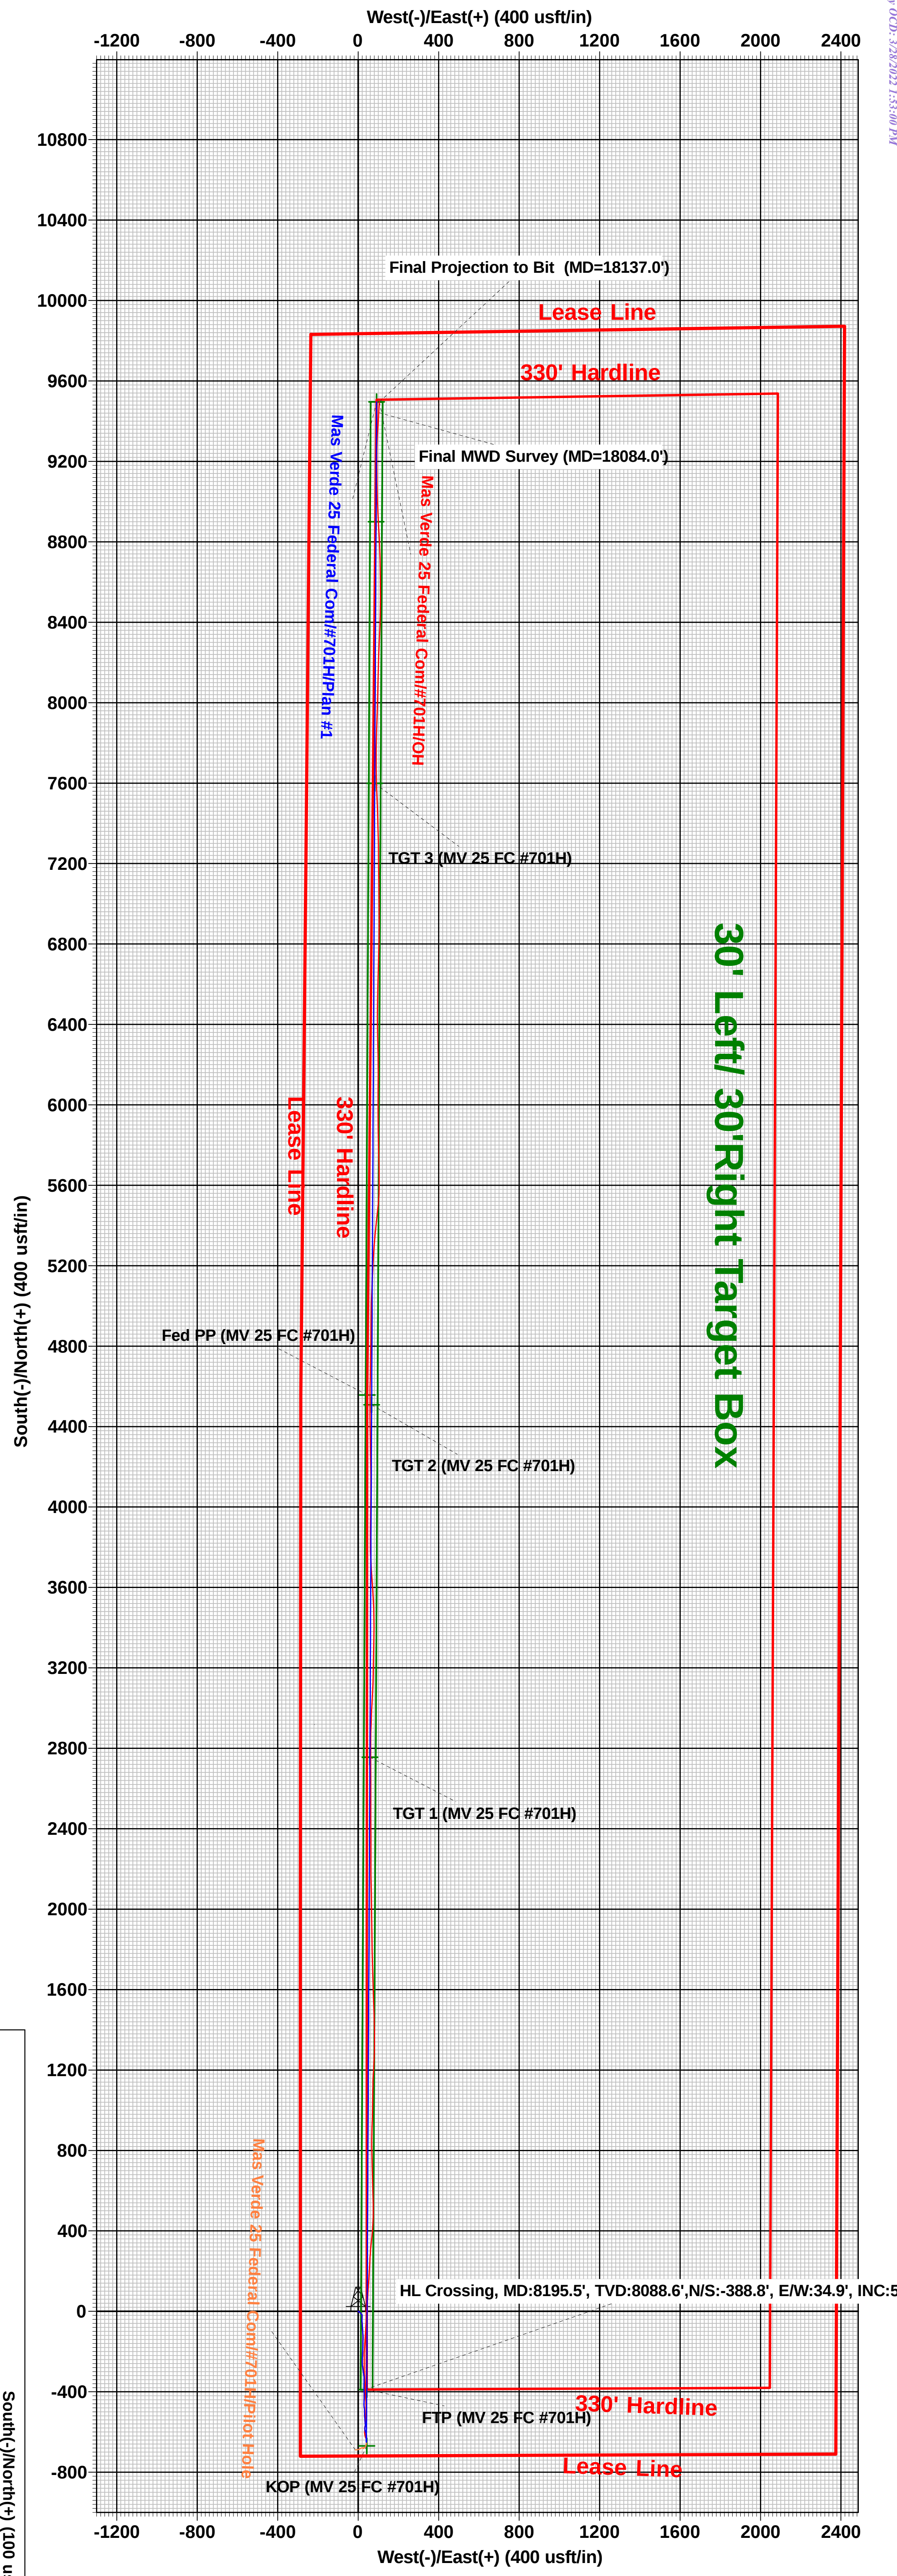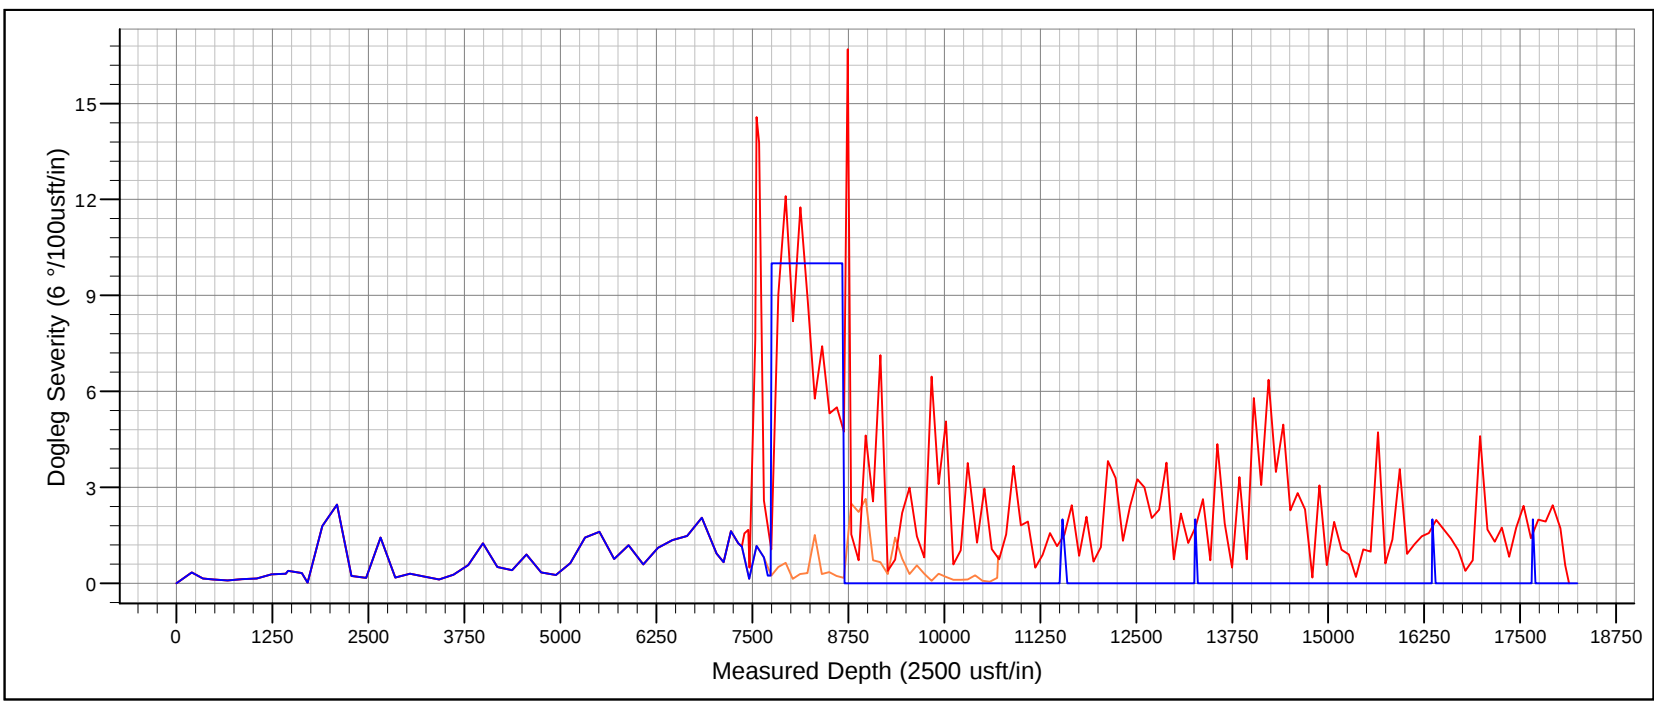



EOG Resources - Midland

Eddy County, NM (NAD 83 NME)

Mas Verde 25 Federal Com

#701H

OH

Design: OH

Final PVA Report

06 March, 2020



Final PVA Report

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #701H
Project:	Eddy County, NM (NAD 83 NME)	TVD Reference:	KB = 25 @ 3574.0usft
Site:	Mas Verde 25 Federal Com	MD Reference:	KB = 25 @ 3574.0usft
Well:	#701H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM

Project		Eddy County, NM (NAD 83 NME)	
Map System:	US State Plane 1983	System Datum:	Mean Sea Level
Geo Datum:	North American Datum 1983		
Map Zone:	New Mexico Eastern Zone		

Site		Mas Verde 25 Federal Com								
Site Position:		Northing:		398,501.00	usft	Latitude:	32° 5' 44.003 N			
From:	Map	Easting:		534,000.00	usft	Longitude:	104° 21' 25.302 W			
Position Uncertainty:		0.0	usft	Slot Radius:		13-3/16	"	Grid Convergence:	-0.01	°

Well		#701H				
Well Position	+N/-S	0.0 usft	Northing:	398,501.00 usft	Latitude:	32° 5' 44.003 N
	+E/-W	0.0 usft	Easting:	534,000.00 usft	Longitude:	104° 21' 25.302 W
Position Uncertainty		0.0 usft	Wellhead Elevation:	usft	Ground Level:	3,549.0 usft

Wellbore	OH				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	IGRF2015	10/29/2019	7.05	59.79	47,534.53549938

Design	OH			
Audit Notes:				
Version:	1.0	Phase:	ACTUAL	Tie On Depth: 7,363.0
Vertical Section:	Depth From (TVD) (usft)	+N/-S (usft)	+E/-W (usft)	Direction (°)
	0.0	0.0	0.0	0.56



Final PVA Report

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #701H
Project:	Eddy County, NM (NAD 83 NME)	TVD Reference:	KB = 25 @ 3574.0usft
Site:	Mas Verde 25 Federal Com	MD Reference:	KB = 25 @ 3574.0usft
Well:	#701H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM

Survey Program		Date	3/6/2020		
From (usft)	To (usft)	Survey (Wellbore)	Tool Name	Description	
197.0	7,363.0	Superior QC (FDIR Corrected Surveys) (P	EOG MWD+IFR1+MS	MWD + IFR1 + Multi-Station Correction	
7,398.0	18,137.0	Total MWD #1 with FDIR (OH)	MWD+IFR1+SAG+FDIR	OWSG MWD + IFR1 + Sag + FDIR Correction	

Survey											
MD (usft)	Inc (°)	Azi (grid_north_azim)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)	
0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.00	0.0	0.0	
197.0	0.67	133.46	197.0	-0.8	0.8	0.34	0.34	0.00	0.0	0.0	
345.0	0.46	125.55	345.0	-1.7	1.9	0.15	-0.14	-5.34	0.0	0.0	
480.0	0.34	110.41	480.0	-2.2	2.8	0.12	-0.09	-11.21	0.0	0.0	
664.0	0.47	123.20	664.0	-2.8	3.9	0.09	0.07	6.95	0.0	0.0	
854.0	0.69	112.37	854.0	-3.7	5.6	0.13	0.12	-5.70	0.0	0.0	
1,044.0	0.94	123.42	1,044.0	-4.9	8.0	0.15	0.13	5.82	0.0	0.0	
1,234.0	1.35	140.94	1,233.9	-7.5	10.7	0.28	0.22	9.22	0.0	0.0	
1,424.0	1.91	139.10	1,423.8	-11.7	14.2	0.30	0.29	-0.97	0.0	0.0	
1,451.0	1.93	136.03	1,450.8	-12.3	14.8	0.39	0.07	-11.37	0.0	0.0	
1,635.0	1.36	140.85	1,634.7	-16.3	18.3	0.32	-0.31	2.62	0.0	0.0	
1,709.0	1.35	141.25	1,708.7	-17.6	19.4	0.02	-0.01	0.54	0.0	0.0	
1,899.0	4.11	190.60	1,898.5	-26.1	19.6	1.78	1.45	25.97	0.0	0.0	
2,089.0	8.55	176.52	2,087.3	-46.9	19.2	2.46	2.34	-7.41	0.0	0.0	
2,279.0	8.98	176.66	2,275.1	-75.8	20.9	0.23	0.23	0.07	0.0	0.0	
2,469.0	8.70	175.53	2,462.8	-104.9	22.9	0.17	-0.15	-0.59	0.0	0.0	
2,659.0	6.11	181.75	2,651.2	-129.3	23.7	1.43	-1.36	3.27	0.0	0.0	
2,849.0	6.27	178.99	2,840.1	-149.8	23.6	0.18	0.08	-1.45	0.0	0.0	
3,040.0	5.83	182.62	3,030.1	-169.9	23.3	0.31	-0.23	1.90	0.0	0.0	
3,229.0	5.44	182.21	3,218.2	-188.5	22.5	0.21	-0.21	-0.22	0.0	0.0	
3,419.0	5.35	180.05	3,407.3	-206.3	22.2	0.12	-0.05	-1.14	0.0	0.0	



Final PVA Report

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #701H
Project:	Eddy County, NM (NAD 83 NME)	TVD Reference:	KB = 25 @ 3574.0usft
Site:	Mas Verde 25 Federal Com	MD Reference:	KB = 25 @ 3574.0usft
Well:	#701H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM

Survey										
MD (usft)	Inc (°)	Azi (grid_north_azim)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
3,609.0	5.36	185.49	3,596.5	-224.0	21.3	0.27	0.01	2.86	0.0	0.0
3,800.0	6.42	183.27	3,786.5	-243.6	19.8	0.57	0.55	-1.16	0.0	0.0
3,989.0	8.38	172.91	3,973.9	-267.8	20.9	1.25	1.04	-5.48	0.0	0.0
4,179.0	7.46	170.87	4,162.1	-293.7	24.6	0.51	-0.48	-1.07	0.0	0.0
4,370.0	6.68	171.06	4,351.6	-316.9	28.3	0.41	-0.41	0.10	0.0	0.0
4,560.0	7.63	182.55	4,540.2	-340.4	29.4	0.90	0.50	6.05	0.0	0.0
4,749.0	7.01	181.15	4,727.6	-364.5	28.7	0.34	-0.33	-0.74	0.0	0.0
4,939.0	7.22	177.57	4,916.2	-388.0	28.9	0.26	0.11	-1.88	0.0	0.0
5,129.0	6.02	178.05	5,104.9	-409.9	29.8	0.63	-0.63	0.25	0.0	0.0
5,319.0	8.70	181.58	5,293.3	-434.2	29.7	1.43	1.41	1.86	0.0	0.0
5,509.0	5.65	181.99	5,481.8	-458.0	29.0	1.61	-1.61	0.22	0.0	0.0
5,699.0	6.50	170.98	5,670.7	-477.9	30.4	0.76	0.45	-5.79	0.0	0.0
5,889.0	8.31	181.67	5,859.1	-502.3	31.6	1.19	0.95	5.63	0.0	0.0
6,080.0	7.87	174.36	6,048.3	-529.1	32.5	0.59	-0.23	-3.83	0.0	0.0
6,270.0	5.75	174.95	6,236.9	-551.5	34.6	1.12	-1.12	0.31	0.0	0.0
6,460.0	3.20	178.32	6,426.3	-566.3	35.6	1.35	-1.34	1.77	0.0	0.0
6,650.0	0.80	232.82	6,616.2	-572.4	34.7	1.48	-1.26	28.68	0.0	0.0
6,841.0	4.40	184.00	6,807.0	-580.5	33.2	2.05	1.88	-25.56	0.0	0.0
7,031.0	4.56	161.42	6,996.4	-595.0	35.1	0.93	0.08	-11.88	0.0	0.0
7,126.0	3.95	159.44	7,091.1	-601.6	37.4	0.66	-0.64	-2.08	0.0	0.0
7,221.0	5.31	168.74	7,185.8	-609.0	39.4	1.63	1.43	9.79	0.0	0.0
7,316.0	5.25	181.64	7,280.4	-617.6	40.2	1.25	-0.06	13.58	0.0	0.0
7,363.0	5.10	175.87	7,327.2	-621.9	40.2	1.15	-0.32	-12.28	0.0	0.0
7,398.0	4.56	174.90	7,362.1	-624.8	40.5	1.56	-1.54	-2.77	0.2	0.0
7,445.0	4.28	184.45	7,409.0	-628.4	40.5	1.67	-0.60	20.32	0.8	-0.3
7,461.0	4.34	183.77	7,424.9	-629.6	40.4	0.49	0.37	-4.25	1.0	-0.4
7,540.0	2.44	306.41	7,503.9	-631.6	38.9	7.62	-2.41	155.24	-4.9	-3.3



Final PVA Report

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #701H
Project:	Eddy County, NM (NAD 83 NME)	TVD Reference:	KB = 25 @ 3574.0usft
Site:	Mas Verde 25 Federal Com	MD Reference:	KB = 25 @ 3574.0usft
Well:	#701H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM

Survey										
MD (usft)	Inc (°)	Azi (grid_north_azim)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
7,555.0	4.23	328.98	7,518.8	-630.9	38.3	14.58	11.93	150.47	-7.6	-1.6
7,590.0	8.94	338.55	7,553.6	-627.3	36.7	13.77	13.46	27.34	-14.0	-1.1
7,650.0	8.36	348.18	7,612.9	-618.7	34.1	2.60	-0.97	16.05	-26.6	1.1
7,745.0	7.71	353.67	7,707.0	-605.6	32.0	1.06	-0.68	5.78	-45.0	3.7
7,756.7	8.69	356.41	7,718.5	-603.9	31.8	9.02	8.38	23.47	-46.9	5.9
KOP (MV 25 FC #701H)										
7,840.0	15.95	5.97	7,799.9	-586.2	32.6	9.02	8.71	11.48	-58.8	14.4
7,935.0	27.44	6.57	7,888.0	-551.4	36.5	12.10	12.09	0.63	-73.6	12.7
8,030.0	34.64	0.81	7,969.4	-502.6	39.4	8.19	7.58	-6.06	-86.8	3.0
8,124.0	45.39	356.81	8,041.3	-442.3	37.9	11.75	11.44	-4.26	-95.7	-0.2
8,195.5	51.70	356.69	8,088.6	-388.8	34.9	8.83	8.83	-0.16	-100.9	3.5
HL Crossing, MD:8195.5', TVD:8088.6', N/S:-388.8', E/W:34.9', INC:51.70										
8,219.0	53.78	356.66	8,102.8	-370.1	33.8	8.83	8.83	-0.14	-101.9	4.8
8,314.0	59.22	357.45	8,155.2	-291.0	29.7	5.77	5.73	0.83	-100.3	11.1
FTP (MV 25 FC #701H)										
8,409.0	64.38	2.88	8,200.1	-207.4	30.1	7.41	5.43	5.72	-88.2	14.8
8,504.0	69.33	3.91	8,237.5	-120.2	35.2	5.30	5.21	1.08	-66.9	9.5
8,599.0	74.54	3.43	8,266.9	-30.1	41.0	5.51	5.48	-0.51	-39.2	3.6
8,693.0	79.00	3.35	8,288.4	61.2	46.4	4.75	4.74	-0.09	-17.5	-1.5
8,742.0	87.16	3.88	8,294.3	109.7	49.5	16.69	16.65	1.08	-11.5	-4.3
8,788.0	87.84	3.69	8,296.3	155.6	52.5	1.53	1.48	-0.41	-9.4	-7.1
8,883.0	88.01	3.03	8,299.8	250.3	58.1	0.72	0.18	-0.69	-5.7	-12.2
8,978.0	91.24	6.00	8,300.4	345.0	65.6	4.62	3.40	3.13	-4.9	-19.2
9,073.0	91.02	3.58	8,298.5	439.7	73.5	2.56	-0.23	-2.55	-6.5	-26.7
9,168.0	86.69	358.37	8,300.4	534.6	75.1	7.13	-4.56	-5.48	-4.4	-27.8
9,263.0	87.06	358.35	8,305.6	629.4	72.4	0.39	0.39	-0.02	1.0	-24.6
9,358.0	87.73	358.15	8,309.9	724.3	69.5	0.74	0.71	-0.21	5.5	-21.3



Final PVA Report

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #701H
Project:	Eddy County, NM (NAD 83 NME)	TVD Reference:	KB = 25 @ 3574.0usft
Site:	Mas Verde 25 Federal Com	MD Reference:	KB = 25 @ 3574.0usft
Well:	#701H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM

Survey										
MD (usft)	Inc (°)	Azi (grid_north_azim)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
9,453.0	89.24	359.60	8,312.4	819.2	67.6	2.20	1.59	1.53	8.2	-18.9
9,548.0	90.36	2.21	8,312.7	914.2	69.1	2.99	1.18	2.75	8.7	-20.0
9,643.0	89.47	1.13	8,312.9	1,009.1	71.9	1.47	-0.94	-1.14	9.1	-22.2
9,737.0	89.36	0.38	8,313.8	1,103.1	73.1	0.81	-0.12	-0.80	10.2	-23.0
9,832.0	94.52	3.70	8,310.6	1,198.0	76.5	6.46	5.43	3.49	7.3	-25.9
9,927.0	92.52	1.53	8,304.8	1,292.7	80.8	3.10	-2.11	-2.28	1.6	-29.8
10,022.0	88.45	358.97	8,304.0	1,387.6	81.3	5.06	-4.28	-2.69	1.0	-29.7
10,118.0	88.81	358.54	8,306.3	1,483.6	79.2	0.58	0.37	-0.45	3.5	-27.1
10,213.0	88.86	357.56	8,308.2	1,578.5	75.9	1.03	0.05	-1.03	5.7	-23.4
10,307.0	85.43	358.43	8,312.9	1,672.3	72.7	3.76	-3.65	0.93	10.5	-19.7
10,426.0	86.85	358.94	8,320.9	1,791.0	69.9	1.27	1.19	0.43	18.8	-16.4
10,521.0	89.66	359.09	8,323.8	1,886.0	68.3	2.96	2.96	0.16	21.9	-14.3
10,616.0	90.65	359.30	8,323.6	1,980.9	67.0	1.07	1.04	0.22	21.9	-12.5
10,711.0	91.07	358.72	8,322.1	2,075.9	65.3	0.75	0.44	-0.61	20.6	-10.3
10,806.0	92.37	359.36	8,319.3	2,170.9	63.7	1.53	1.37	0.67	18.0	-8.3
10,901.0	89.07	0.49	8,318.1	2,265.8	63.6	3.67	-3.47	1.19	17.0	-7.7
10,996.0	87.79	359.33	8,320.7	2,360.8	63.5	1.82	-1.35	-1.22	19.8	-7.1
11,090.0	89.52	359.89	8,322.9	2,454.8	62.8	1.93	1.84	0.60	22.2	-5.9
11,185.0	89.21	0.24	8,323.9	2,549.8	62.9	0.49	-0.33	0.37	23.5	-5.6
11,280.0	89.80	359.63	8,324.8	2,644.8	62.8	0.89	0.62	-0.64	24.5	-5.0
11,375.0	91.29	359.55	8,323.9	2,739.7	62.1	1.57	1.57	-0.08	23.8	-3.8
11,391.4	91.31	359.74	8,323.5	2,756.2	62.0	1.16	0.15	1.15	23.5	-3.7
TGT 1 (MV 25 FC #701H)										
11,469.0	91.43	0.63	8,321.6	2,833.7	62.3	1.16	0.15	1.15	22.5	-3.5
11,564.0	91.19	2.05	8,319.5	2,928.7	64.5	1.52	-0.25	1.49	21.7	-5.3
11,659.0	89.10	3.05	8,319.2	3,023.6	68.7	2.44	-2.20	1.05	22.7	-9.0
11,754.0	88.55	2.44	8,321.2	3,118.4	73.3	0.86	-0.58	-0.64	26.0	-13.1



Final PVA Report

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #701H
Project:	Eddy County, NM (NAD 83 NME)	TVD Reference:	KB = 25 @ 3574.0usft
Site:	Mas Verde 25 Federal Com	MD Reference:	KB = 25 @ 3574.0usft
Well:	#701H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM

Survey										
MD (usft)	Inc (°)	Azi (grid_north_azim)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
11,849.0	89.36	0.63	8,322.9	3,213.4	75.8	2.09	0.85	-1.91	29.0	-15.2
11,944.0	89.34	1.28	8,324.0	3,308.4	77.4	0.68	-0.02	0.68	31.4	-16.3
12,038.0	89.84	0.35	8,324.6	3,402.3	78.7	1.12	0.53	-0.99	33.4	-17.1
12,133.0	87.22	357.83	8,327.1	3,497.3	77.2	3.83	-2.76	-2.65	37.1	-15.2
12,229.0	89.84	356.06	8,329.5	3,593.1	72.1	3.29	2.73	-1.84	40.9	-9.6
12,324.0	91.10	356.13	8,328.8	3,687.9	65.7	1.33	1.33	0.07	41.4	-2.7
12,419.0	91.10	358.41	8,326.9	3,782.7	61.1	2.40	0.00	2.40	40.9	2.3
12,514.0	89.24	0.88	8,326.7	3,877.7	60.5	3.25	-1.96	2.60	42.0	3.4
12,608.0	86.43	1.11	8,330.2	3,971.6	62.2	3.00	-2.99	0.24	46.8	2.3
12,703.0	88.36	0.90	8,334.5	4,066.5	63.8	2.04	2.03	-0.22	52.4	1.1
12,798.0	89.54	359.06	8,336.3	4,161.5	63.8	2.30	1.24	-1.94	55.5	1.6
12,893.0	93.09	358.58	8,334.1	4,256.4	61.8	3.77	3.74	-0.51	54.6	4.0
12,988.0	92.54	359.04	8,329.4	4,351.3	59.9	0.75	-0.58	0.48	51.3	6.4
13,083.0	90.66	359.91	8,326.8	4,446.3	59.0	2.18	-1.98	0.92	49.9	7.8
13,146.4	91.45	359.80	8,325.6	4,509.7	58.8	1.26	1.25	-0.17	49.6	8.3
TGT 2 (MV 25 FC #701H)										
13,178.0	91.85	359.75	8,324.7	4,541.2	58.7	1.26	1.25	-0.17	49.0	8.6
13,192.7	91.76	359.99	8,324.2	4,556.0	58.7	1.76	-0.62	1.64	48.7	8.7
Fed PP (MV 25 FC #701H)										
13,273.0	91.26	1.31	8,322.1	4,636.2	59.6	1.76	-0.62	1.64	47.4	8.2
13,368.0	88.76	1.23	8,322.1	4,731.2	61.7	2.63	-2.63	-0.08	48.3	6.5
13,463.0	88.30	0.73	8,324.5	4,826.1	63.3	0.72	-0.48	-0.53	51.6	5.4
13,558.0	92.40	0.20	8,324.0	4,921.1	64.1	4.35	4.32	-0.56	52.0	5.1
13,653.0	91.87	1.90	8,320.4	5,016.0	65.8	1.87	-0.56	1.79	49.4	3.8
13,748.0	92.15	2.27	8,317.1	5,110.9	69.3	0.49	0.29	0.39	46.9	0.8
13,843.0	89.18	3.34	8,316.0	5,205.8	73.9	3.32	-3.13	1.13	46.8	-3.3
13,938.0	88.75	3.91	8,317.7	5,300.5	80.0	0.75	-0.45	0.60	49.4	-8.8



Final PVA Report

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #701H
Project:	Eddy County, NM (NAD 83 NME)	TVD Reference:	KB = 25 @ 3574.0usft
Site:	Mas Verde 25 Federal Com	MD Reference:	KB = 25 @ 3574.0usft
Well:	#701H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM

Survey										
MD (usft)	Inc (°)	Azi (grid_north_azim)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
14,033.0	93.78	6.13	8,315.6	5,395.1	88.3	5.79	5.29	2.34	48.3	-16.6
14,128.0	90.88	5.85	8,311.7	5,489.5	98.2	3.07	-3.05	-0.29	45.4	-26.0
14,223.0	86.76	1.43	8,313.7	5,584.3	104.2	6.36	-4.34	-4.65	48.1	-31.8
14,318.0	88.57	358.66	8,317.6	5,679.2	104.3	3.48	1.91	-2.92	52.9	-31.3
14,413.0	93.26	358.22	8,316.0	5,774.1	101.7	4.96	4.94	-0.46	52.3	-28.3
14,508.0	91.43	359.39	8,312.2	5,869.0	99.7	2.29	-1.93	1.23	49.4	-25.8
14,603.0	88.75	359.26	8,312.0	5,964.0	98.6	2.82	-2.82	-0.14	50.1	-24.2
14,698.0	90.53	0.54	8,312.6	6,059.0	98.4	2.31	1.87	1.35	51.7	-23.6
14,793.0	90.70	0.51	8,311.6	6,154.0	99.3	0.18	0.18	-0.03	51.6	-24.0
14,888.0	88.33	358.83	8,312.4	6,248.9	98.7	3.06	-2.49	-1.77	53.3	-23.0
14,983.0	87.81	358.66	8,315.6	6,343.9	96.7	0.58	-0.55	-0.18	57.4	-20.4
15,078.0	88.53	0.34	8,318.6	6,438.8	95.8	1.92	0.76	1.77	61.4	-19.1
15,173.0	89.39	0.85	8,320.4	6,533.8	96.8	1.05	0.91	0.54	64.0	-19.6
15,268.0	89.80	1.60	8,321.0	6,628.8	98.8	0.90	0.43	0.79	65.6	-21.1
15,363.0	89.65	1.49	8,321.5	6,723.7	101.4	0.20	-0.16	-0.12	67.0	-23.2
15,458.0	89.00	0.72	8,322.6	6,818.7	103.2	1.06	-0.68	-0.81	69.0	-24.6
15,553.0	88.10	0.44	8,325.0	6,913.7	104.2	0.99	-0.95	-0.29	72.3	-25.1
15,648.0	92.43	359.25	8,324.6	7,008.6	103.9	4.73	4.56	-1.25	72.8	-24.4
15,743.0	91.87	359.44	8,321.0	7,103.6	102.9	0.62	-0.59	0.20	70.2	-22.8
15,838.0	90.57	359.44	8,319.0	7,198.5	101.9	1.37	-1.37	0.00	69.1	-21.4
15,933.0	87.23	358.82	8,320.8	7,293.5	100.5	3.58	-3.52	-0.65	71.8	-19.5
16,028.0	88.06	358.56	8,324.7	7,388.4	98.3	0.92	0.87	-0.27	76.6	-16.9
16,122.0	89.04	357.97	8,327.1	7,482.3	95.5	1.22	1.04	-0.63	79.9	-13.5
16,217.0	90.40	357.67	8,327.5	7,577.2	91.9	1.47	1.43	-0.32	81.3	-9.5
16,240.4	90.48	358.03	8,327.4	7,600.6	91.0	1.57	0.33	1.54	81.4	-8.5
TGT 3 (MV 25 FC #701H)										
16,312.0	90.71	359.13	8,326.6	7,672.2	89.2	1.57	0.33	1.54	81.2	-6.3



Final PVA Report

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #701H
Project:	Eddy County, NM (NAD 83 NME)	TVD Reference:	KB = 25 @ 3574.0usft
Site:	Mas Verde 25 Federal Com	MD Reference:	KB = 25 @ 3574.0usft
Well:	#701H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM

Survey										
MD (usft)	Inc (°)	Azi (grid_north_azim)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
16,407.0	91.30	0.92	8,325.0	7,767.2	89.3	1.98	0.62	1.88	80.3	-5.9
16,502.0	89.86	1.63	8,324.0	7,862.1	91.4	1.69	-1.52	0.75	80.0	-7.5
16,597.0	91.03	2.26	8,323.3	7,957.1	94.6	1.40	1.23	0.66	80.0	-10.2
16,692.0	91.67	1.52	8,321.0	8,052.0	97.7	1.03	0.67	-0.78	78.5	-12.9
16,786.0	91.73	1.16	8,318.2	8,145.9	99.9	0.39	0.06	-0.38	76.4	-14.6
16,881.0	91.55	1.82	8,315.5	8,240.9	102.4	0.72	-0.19	0.69	74.5	-16.6
16,976.0	87.27	2.70	8,316.5	8,335.8	106.1	4.60	-4.51	0.93	76.2	-19.9
17,071.0	86.72	1.20	8,321.5	8,430.6	109.4	1.68	-0.58	-1.58	81.9	-22.7
17,166.0	87.32	0.12	8,326.4	8,525.4	110.5	1.30	0.63	-1.14	87.5	-23.3
17,261.0	88.80	359.37	8,329.6	8,620.4	110.0	1.75	1.56	-0.79	91.5	-22.4
17,356.0	88.39	358.70	8,332.0	8,715.3	108.4	0.83	-0.43	-0.71	94.5	-20.3
17,450.0	87.40	357.39	8,335.4	8,809.2	105.2	1.75	-1.05	-1.39	98.7	-16.7
17,538.5	89.45	356.76	8,337.8	8,897.5	100.7	2.42	2.32	-0.72	101.8	-11.7
TGT 4 (MV 25 FC #701H)										
17,545.0	89.60	356.71	8,337.9	8,904.1	100.3	2.42	2.32	-0.72	101.9	-11.3
17,640.0	89.30	358.02	8,338.8	8,998.9	96.0	1.41	-0.32	1.38	103.0	-6.5
17,736.0	90.89	359.09	8,338.7	9,094.9	93.6	2.00	1.66	1.11	103.0	-3.6
17,830.0	89.18	359.70	8,338.6	9,188.9	92.6	1.93	-1.82	0.65	103.1	-2.1
17,925.0	89.60	1.98	8,339.6	9,283.9	94.0	2.44	0.44	2.40	104.3	-3.0
18,021.0	88.91	3.48	8,340.9	9,379.8	98.5	1.72	-0.72	1.56	105.7	-7.1
18,084.0	89.27	3.52	8,341.9	9,442.6	102.4	0.57	0.57	0.06	106.8	-10.6
Final MWD Survey (MD=18084.0')										
18,135.4	89.27	3.52	8,342.5	9,493.9	105.5	0.00	0.00	0.00	107.5	-13.5
PBHL (MV 25 FC #701H)										
18,137.0	89.27	3.52	8,342.5	9,495.5	105.6	0.00	0.00	0.00	107.5	-13.6
Final Projection to Bit (MD=18137.0')										



Final PVA Report

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #701H
Project:	Eddy County, NM (NAD 83 NME)	TVD Reference:	KB = 25 @ 3574.0usft
Site:	Mas Verde 25 Federal Com	MD Reference:	KB = 25 @ 3574.0usft
Well:	#701H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM

Design Annotations					
Measured Depth (usft)	Vertical Depth (usft)	Local Coordinates			
		+N/-S (usft)	+E/-W (usft)	Comment	
8,195.5	8,088.6	-388.8	34.9	HL Crossing, MD:8195.5', TVD:8088.6',N/S:-388.8', E/W:34.9', INC:51.70	
18,084.0	8,341.9	9,442.6	102.4	Final MWD Survey (MD=18084.0')	
18,137.0	8,342.5	9,495.5	105.6	Final Projection to Bit (MD=18137.0')	

Checked By: _____ Approved By: _____ Date: _____

I CERTIFY THIS SURVEY TO BE TRUE AND CORRECT TO THE BEST OF MY BELIEF AND KNOWLEDGE
KAY MADDOX 03/10/2022

Intent ☐ As Drilled ☐

API #		
Operator Name:	Property Name:	Well Number

Kick Off Point (KOP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

First Take Point (FTP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

Last Take Point (LTP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

Is this well the defining well for the Horizontal Spacing Unit? ☐Is this well an infill well? ☐

If infill is yes please provide API if available, Operator Name and well number for Defining well for Horizontal Spacing Unit.

API #		
Operator Name:	Property Name:	Well Number

KZ 06/29/2018

Submit To Appropriate District Office Two Copies <u>District I</u> 1625 N. French Dr., Hobbs, NM 88240 <u>District II</u> 811 S. First St., Artesia, NM 88210 <u>District III</u> 1000 Rio Brazos Rd., Aztec, NM 87410 <u>District IV</u> 1220 S. St. Francis Dr., Santa Fe, NM 87505		State of New Mexico Energy, Minerals and Natural Resources Oil Conservation Division 1220 South St. Francis Dr. Santa Fe, NM 87505			Form C-105 Revised August 1, 2011					
WELL COMPLETION OR RECOMPLETION REPORT AND LOG										
4. Reason for filing: ☒ COMPLETION REPORT (Fill in boxes #1 through #31 for State and Fee wells only) ☐ C-144 CLOSURE ATTACHMENT (Fill in boxes #1 through #9, #15 Date Rig Released and #32 and/or #33; attach this and the plat to the C-144 closure report in accordance with 19.15.17.13.K NMAC)								5. Lease Name or Unit Agreement Name MAS VERDE 25 FEDERAL COM		
								6. Well Number: 701H		
7. Type of Completion: ☒ NEW WELL ☐ WORKOVER ☐ DEEPENING ☐ PLUGBACK ☐ DIFFERENT RESERVOIR ☐ OTHER _____										
8. Name of Operator EOG RESOURCES INC							9. OGRID 7377			
10. Address of Operator PO BOX 2267 MIDLAND, TEXAS 79702							11. Pool name or Wildcat PURPLE SAGE; WOLFCAMP (GAS)			
12. Location	Unit Ltr	Section	Township	Range	Lot	Feet from the	N/S Line	Feet from the	E/W Line	County
Surface:	M	25	25S	25E		720	SOUTH	287	WEST	EDDY
BH:	D	24	25S	25E		339	NORTH	344	WEST	EDDY
13. Date Spudded 01/08/2020	14. Date T.D. Reached 03/01/2020		15. Date Rig Released 03/03/2020			16. Date Completed (Ready to Produce) 02/22/2022		17. Elevations (DF and RKB, RT, GR, etc.) 3549' GL		
18. Total Measured Depth of Well MD 18,137' TVD 8342'			19. Plug Back Measured Depth MD 18,102' TVD 8342'			20. Was Directional Survey Made? YES		21. Type Electric and Other Logs Run None		
22. Producing Interval(s), of this completion - Top, Bottom, Name WOLFCAMP 8615 - 18,102'										
23. CASING RECORD (Report all strings set in well)										
CASING SIZE		WEIGHT LB./FT.		DEPTH SET		HOLE SIZE		CEMENTING RECORD		AMOUNT PULLED
13 3/8"		54.5# J-55		380'		17 1/2"		770 CL C/CIRC		
9 5/8"		40# J-55		1689'		12 1/4"		800 CL C/CIRC		
7 5/8"		29.7# ECP 110		7301'		8 3/4"		1115 CL C/CIRC		
5 1/2"		20# ECP 110		18,122'		6 3/4"		1040 CL H/TOC 5312'		CBL
24. LINER RECORD						25. TUBING RECORD				
SIZE	TOP	BOTTOM	SACKS CEMENT	SCREEN	SIZE	DEPTH SET	PACKER SET			
26. Perforation record (interval, size, and number)						27. ACID, SHOT, FRACTURE, CEMENT, SQUEEZE, ETC.				
8615 - 18,102' 3 1/8", 2064 holes						DEPTH INTERVAL		AMOUNT AND KIND MATERIAL USED		
						8615 - 18,102		FRAC W/23,336,100 lbs proppant, 396,809 bbls load fld		
						7279 - 8439		CMT FOR KO PLUG, 336 CL H		
						8439-9579' 9589-10,739'		CMT PLUGS, 240 SXS CL C CMT ON BOTH PLUGS		
28. PRODUCTION										
Date First Production 02/22/2022		Production Method (<i>Flowing, gas lift, pumping - Size and type pump</i>) Flowing				Well Status (<i>Prod. or Shut-in</i>) Producing				
Date of Test 03/05/2022	Hours Tested 24	Choke Size 120	Prod'n For Test Period	Oil - Bbl 1195	Gas - MCF 4369	Water - Bbl. 9932	Gas - Oil Ratio 3655			
Flow Tubing Press.	Casing Pressure 562	Calculated 24-Hour Rate	Oil - Bbl.	Gas - MCF	Water - Bbl.	Oil Gravity - API - (<i>Corr.</i>) 47				
29. Disposition of Gas (<i>Sold, used for fuel, vented, etc.</i>) SOLD								30. Test Witnessed By		
31. List Attachments C-102, C-104, C-103, Directional Survey, H spacing										
32. If a temporary pit was used at the well, attach a plat with the location of the temporary pit.										
33. If an on-site burial was used at the well, report the exact location of the on-site burial:										
Latitude _____ Longitude _____ NAD 1927 1983										
I hereby certify that the information shown on both sides of this form is true and complete to the best of my knowledge and belief Printed Signature Kay Maddox Name Kay Maddox Title Senior Regulatory Specialist Date 03/23/2022 E-mail Address kay_maddox@eogresources.com										

This form is to be filed with the appropriate District Office of the Division not later than 20 days after the completion of any newly-drilled or deepened well and not later than 60 days after completion of closure. When submitted as a completion report, this shall be accompanied by one copy of all electrical and radio-activity logs run on the well and a summary of all special tests conducted, including drill stem tests. All depths reported shall be measured depths. In the case of directionally drilled wells, true vertical depths shall also be reported. For multiple completions, items 11, 12 and 26-31 shall be reported for each zone.

Southeastern New Mexico			Northwestern New Mexico			
T. Anhy	Rustler	392'	T. Canyon	Brushy 3725'	T. Ojo Alamo	T. Penn A"
T. Salt		481'	T. Strawn		T. Kirtland	T. Penn. "B"
B. Salt		1446'	T. Atoka		T. Fruitland	T. Penn. "C"
T. Yates			T. Miss		T. Pictured Cliffs	T. Penn. "D"
T. 7 Rivers			T. Devonian		T. Cliff House	T. Leadville
T. Queen			T. Silurian		T. Menefee	T. Madison
T. Grayburg			T. Montoya		T. Point Lookout	T. Elbert
T. San Andres			T. Simpson		T. Mancos	T. McCracken
T. Glorieta			T. McKee		T. Gallup	T. Ignacio Otzte
T. Paddock			T. Ellenburger		Base Greenhorn	T. Granite
T. Blinebry			T. Gr. Wash		T. Dakota	
T. Tubb			T. Delaware Sand		T. Morrison	
T. Drinkard			T. Bone Springs		T. Todilto	
T. Abo			T. 1st BS Sand	6089'	T. Entrada	
T. Wolfcamp		8243'	T. 2nd BS Sand	6623'	T. Wingate	
T. Penn			T.		T. Chinle	
T. Cisco (Bough C)			T.		T. Permian	

No. 1, from.....to.....

No. 2, from.....to.....

No. 3, from.....to.....

No. 4, from.....to.....

Include data on rate of water inflow and elevation to which water rose in hole.

No. 1, from.....to.....feet.....
 No. 2, from.....to.....feet.....
 No. 3, from.....to.....feet.....

From	To	Thickness In Feet	Lithology

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
<https://www.emnrd.nm.gov/ocd/contact-us>

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

ACKNOWLEDGMENTS

Action 93605

ACKNOWLEDGMENTS

Operator: EOG RESOURCES INC 5509 Champions Drive Midland, TX 79706	OGRID: 7377
	Action Number: 93605
	Action Type: [C-104] Completion Packet (C-104C)

ACKNOWLEDGMENTS

☒	I hereby certify that the required Water Use Report has been, or will be, submitted for this wells completion.
☒	I hereby certify that the required FracFocus disclosure has been, or will be, submitted for this wells completion.

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
<https://www.emnrd.nm.gov/oed/contact-us>

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 93605

CONDITIONS

Operator: EOG RESOURCES INC 5509 Champions Drive Midland, TX 79706	OGRID: 7377
	Action Number: 93605
	Action Type: [C-104] Completion Packet (C-104C)

CONDITIONS

Created By	Condition	Condition Date
plmartinez	File 3160-4 Completion Report within 10 days of BLM approval.	11/15/2024
