

Well Name: EL PASO	Well Location: T29N / R9W / SEC 20 / NESW / 36.707901 / -107.80481	County or Parish/State: SAN JUAN / NM
Well Number: 1	Type of Well: OTHER	Allottee or Tribe Name:
Lease Number: NMNM0560422	Unit or CA Name:	Unit or CA Number:
US Well Number: 3004511795	Operator: HILCORP ENERGY COMPANY	

Subsequent Report

Sundry ID: 2829168

Type of Submission: Subsequent Report

Type of Action: Water Shut-off

Date Sundry Submitted: 12/30/2024

Time Sundry Submitted: 09:32

Date Operation Actually Began: 11/05/2024

Actual Procedure: Hilcorp Energy set a 7" CIBP @ 2050 ft. 3 1/2 inch, 9.3# J-55 tubing was landed @ 2031 ft. See attached reports.

SR Attachments

Actual Procedure

El_Paso_1_Water_Shutoff_Sundry_20241230093210.pdf

Well Name: EL PASO

Well Location: T29N / R9W / SEC 20 /
NESW / 36.707901 / -107.80481

County or Parish/State: SAN
JUAN / NM

Well Number: 1

Type of Well: OTHER

Allottee or Tribe Name:

Lease Number: NMNM0560422

Unit or CA Name:

Unit or CA Number:

US Well Number: 3004511795

Operator: HILCORP ENERGY
COMPANY

Operator

I certify that the foregoing is true and correct. Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction. Electronic submission of Sundry Notices through this system satisfies regulations requiring a

Operator Electronic Signature: CHERYLENE WESTON

Signed on: DEC 30, 2024 09:32 AM

Name: HILCORP ENERGY COMPANY

Title: Operations/Regulatory Tech - Sr

Street Address: 1111 TRAVIS STREET

City: HOUSTON

State: TX

Phone: (713) 289-2615

Email address: CWESTON@HILCORP.COM

Field

Representative Name:

Street Address:

City:

State:

Zip:

Phone:

Email address:

BLM Point of Contact

BLM POC Name: MATTHEW H KADE

BLM POC Title: Petroleum Engineer

BLM POC Phone: 5055647736

BLM POC Email Address: MKADE@BLM.GOV

Disposition: Accepted

Disposition Date: 01/03/2025

Signature: Matthew Kade



Well Operations Summary L48

Well Name: EL PASO #1

API: 3004511795	Field: BLANCO MESAVERDE (PRORATED GAS	State: NEW MEXICO
Permit to Drill (PTD) #:	Sundry #:	Rig/Service: BWD 105

Jobs

Actual Start Date: 11/5/2024 End Date: 11/7/2024

Report Number 1	Report Start Date 11/5/2024	Report End Date 11/5/2024
--------------------	--------------------------------	------------------------------

Operation

ACCEPT HEC #105 AT 06:00 ON 11/05/2024. CREW TRAVELED TO LOCATION. (EARLY)
HOLD PJSM. MOB FROM THE LARGO FEDERAL #100 TO THE EL PASO #1 (4 MILE MOVE).
SPOT RIG AND EQUIPMENT. BDW.

SITP: 0 PSI
SICP: 0 PSI
SIBHP: 0 PSI
BDW: 0 MIN

R/D WH. X/O TO 2-1/16" HANDLING TOOLS. PULL TUBING SLIPS. STACK OUT 2-1/16" TUBING. N/D WH. PULL 2-1/16" TUBING SEAL. N/D CENTER SECTION OF W/H. PULL 3-1/2" SEAL SUB. N/U BOP. R/U RIG FLOOR. FUNCTION TEST AND PRESSURE TEST BOP (GOOD).

TOOH W/ ALL 2-1/16" TUBING, X/O TO 3-1/2" HANDLING TOOLS.

PT 3-1/2 PIPE RAMS (GOOD). PULL 3-1/2" TUBING HANGER.

TOOH W/ 3-1/2" TUBING. L/D 2-7/8" SCREEN.

X/O TO 2-3/8" HANDLING TOOLS. P/U SELECT 7" CSG SCRAPER. TALLY AND P/U 2-3/8" TUBING PAST PERFS TO 2117' (TOP PERF AT 1962').

TOOH W/ ALL 2-3/8" TUBING. L/D 7" CSG SCRAPER.

SHUT IN WELL. SECURED LOCATION. DEBRIEFED CREW. SDFN.

CREW TRAVELED HOME. EXTRA TIME FOR EARLY START.

Report Number 2	Report Start Date 11/6/2024	Report End Date 11/6/2024
--------------------	--------------------------------	------------------------------

Operation

CREW TRAVEL TO LOCATION.
HOLD PJSM. DISCUSS DAYS ACTIVITIES. BDW.

SITP: 0 PSI
SICP: 0 PSI
SIBHP: 0 PSI
BDW: 0 MIN

P/U SELECT 7" RBP. TIH. SET RBP AT 1924'.

L/D 1 JT. LOAD CASING. CIRCULATE WELL CLEAN.

PT CSG TO 680 PSI. PRESSURE HELD SOLID FOR 30 MIN. GOOD TEST.

TOOH W/ ALL TBG.

MIRU THE WIRELINE GROUP. HOLD PJSM. RIH W/ RBL. POOH **LOGGING FROM 1924' TO SURFACE** UNDER 500 PSI. SEND LOG TO ENGINEER. R/D TWG.

TIH W/ RETRIEVING HEAD. LATCH RBP. WELL DID NOT SUCK OR BLOW. TOOH. L/D 7" RBP. P/U SELECT 7" ASI-X PACKER. TIH.

SET PACKER AT 2113'. PT FROM 2113' TO 2184'. PRESSURE FELL FROM 600 PSI TO 320 PSI IN 11 MIN (FAIL, 30 PSI/MIN LOSS). P/U TUBING. SET PACKER AT 2144'. PT FROM 2144' TO 2184' (GOOD). L/D TUBING. SET PACKER AT 2113'. FIGHT AIR. GET TEST TO LEVEL OUT AT 530 PSI FOR 30 MIN. RELEASE PACKER. TOOH ABOVE TOP PERF. EOT AT 1922'.

SHUT IN WELL. SECURED LOCATION. WINTERIZE EQUIPMENT. DEBRIEFED CREW. SDFN.

CREW TRAVELED HOME.

Report Number 3	Report Start Date 11/7/2024	Report End Date 11/7/2024
--------------------	--------------------------------	------------------------------

Operation

CREW TRAVEL TO LOCATION. SNOW PACK ROADS.
HELD PJSM WITH RIG CREW ON TODAY'S OPERATIONS. BDW.

SITP: 0 PSI
SICP: 0 PSI
SIBHP: 0 PSI
BDW: 0 MIN

TOOH W/ 2-3/8" TUBING. L/D ASI-X PACKER. TIH, **SET 7" CIBP AT 2050'**. BETWEEN MIDDLE SET AND LOWER SET OF PERFS. **L/D ALL 2-3/8"**

TUBING. L/D SETTING TOOL.

X/O TO 3-1/2" HANDLING TOOLS. P/U NEW JET PUMP ASSEMBLY. TALLY AND **TIH W/ 3-1/2" EUE TBG.** L/D 4 JTS 3-1/2" TBG. P/U 3-1/2" PUP JTS.



Well Operations Summary L48

Well Name: EL PASO #1

API: 3004511795	Field: BLANCO MESAVERDE (PRORATED GAS)	State: NEW MEXICO
	Sundry #:	Rig/Service: BWD 105

Operation

P/U 3-1/2" TUBING HANGER
LAND TUBING AS FOLLOWS:

- TUBING HANGER
1 - JT 2-3-1/2" J-55 YELLOW TUBING (32.40')
3 - 3-1/2" J-55 PUP JOINTS (20.20')
60 - 3-1/2" J-55 YELLOW TUBING (1953.30')
1 - 3 1/2" EUE X 2-7/8" ST-L X/O (0.92')
1 - 2-7/8" ST-L JET PUMP (1.84')
1 - 2-3/8" WIRE WRAP SCREEN (8.80')
1- 2-3/8" BULL PLUG (0.2')

PBTD - 2184'
CIBP - 2050'
EOT - 2030.66'
JET PUMP - 2019.82'
KB - 12'

X/O TO 2-1/16" HANDLING TOOLS, P/U NEW DIFFUSER. TALLY AND TIH W/ TUBING. SPACE OUT. L/D 4 JOINTS
SET TUBING IN SLIPS AS FOLLOWS.

- 4 - 2-1/16" J-55 PUP JOINTS (30.20')
60 - 2-1/16" J-55 YELLOW TUBING (1,945.58)
1-2-1/16" X 1.66 X/O (0.38')
1 - 1.66" J-55 J-55 YELLOW TUBING (33.13')

R/D FLOOR. NIPPLE DOWN BOP, R/U 3-1/2" SEAL SUB, NIPPLE UP MOTIVE WELLHEAD. R/U 2-1/16" TUBING SEAL, NIPPLE UP MOTIVE RETURN
WELLHEAD. SET SLIPS. PLUMB SURFACE EQUIPMENT

R/U AIR UNIT. TEST JET PUMP (GOOD). UNLOAD WELL. GOT GOOD MIST UP 2-1/16" TUBING. R/D AIR UNIT.


R/D HEC #105. PREP FOR RIG MOVE. CHAIN UP RIG. CREW TRAVEL HOME. **RIG RELEASED TO THE GRAMBLING #3 ON 11/7/2024 AT 19:00.**



Current Schematic - Version 1

Well Name: EL PASO #1

API / UWI 3004511795	Surface Legal Location 020-029N-009W-K	Field Name BLANCO MESAVERDE (PRORATED GAS)	Route 0805	State/Province NEW MEXICO	Well Configuration Type
Ground Elevation (ft) 5,696.00	Original KB/RT Elevation (ft) 5,708.00	Tubing Hanger Elevation (ft)	RKB to GL (ft) 12.00	KB-Casing Flange Distance (ft)	KB-Tubing Hanger Distance (ft)

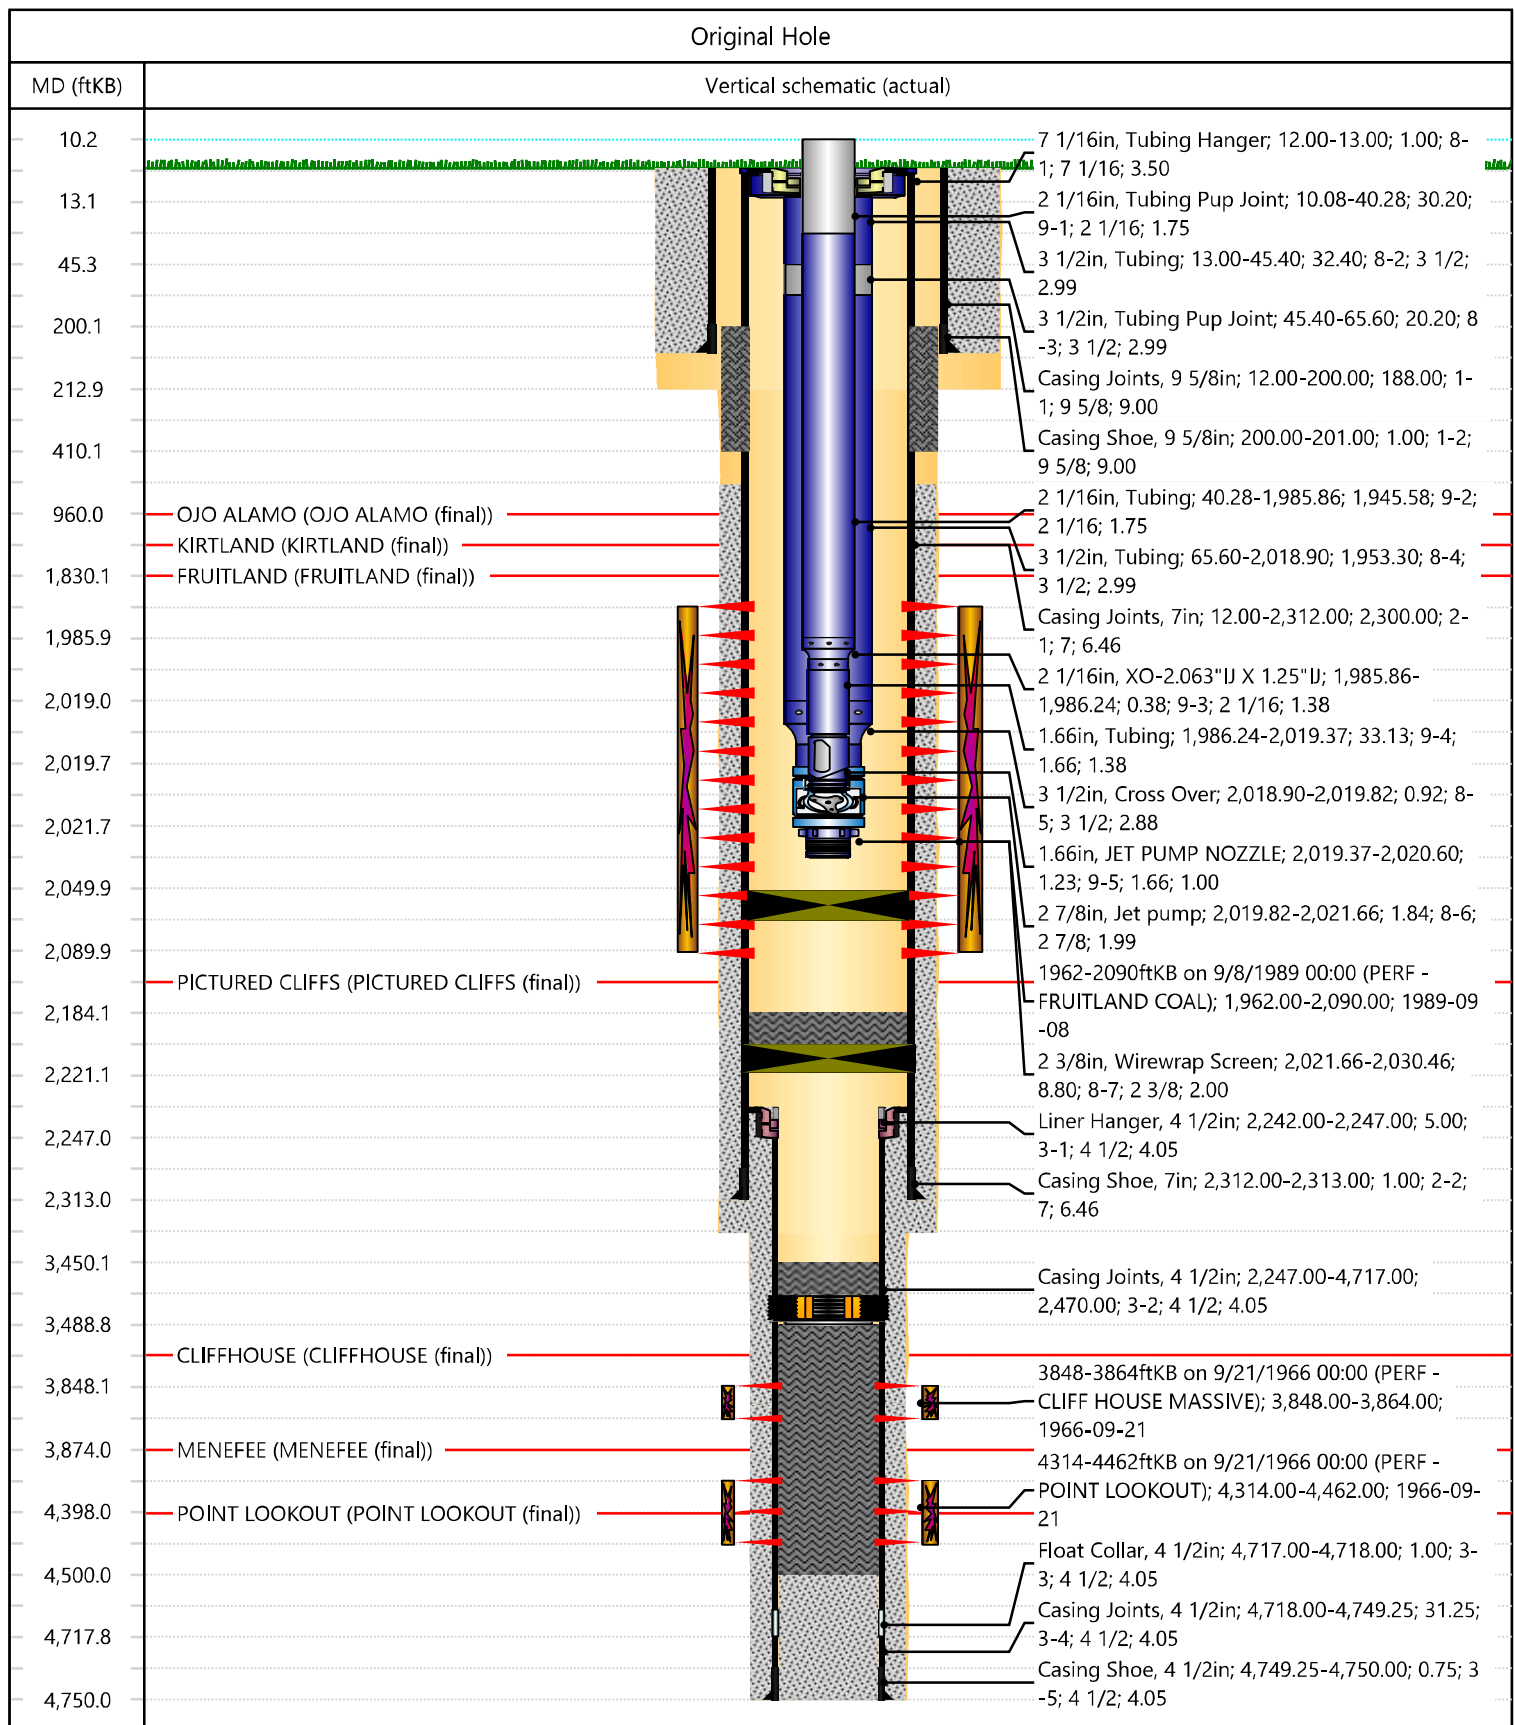

WellViewAdmin@hilcorp.com

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
<https://www.emnrd.nm.gov/oed/contact-us>

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 416965

CONDITIONS

Operator: HILCORP ENERGY COMPANY 1111 Travis Street Houston, TX 77002	OGRID: 372171
	Action Number: 416965
	Action Type: [C-103] Sub. Workover (C-103R)

CONDITIONS

Created By	Condition	Condition Date
mkuehling	None	6/12/2025
