Received by OCD: 7/1/2025 2:19:01 PM

Phone: (505) 476-3441 General Information Phone: (505) 629-6116

State of New Mexico Energy, Minerals and Natural Resources

Form C-103<sup>1</sup> of 4 Revised July 18, 2013

WELL API NO.

Online Phone Directory Visit: https://www.emnrd.nm.gov/ocd/contact-us/	OIL CONSERVATION DIVISION 1220 South St. Francis Dr. Santa Fe, NM 87505		5. Indicate Type of Lease STATE FEE  6. State Oil & Gas Lease No.		
(DO NOT USE THIS FORM FOR PROPOSA DIFFERENT RESERVOIR. USE "APPLICA"		OR PLUG BACK TO A	7. Lease Name or U	Jnit Agreement Name	
PROPOSALS.)  1. Type of Well: Oil Well G	8. Well Number				
2. Name of Operator	as Well Other		9. OGRID Number		
3. Address of Operator			10. Pool name or Wildcat		
4. Well Location					
Unit Letter:_	feet from the	line and	feet from	theline	
Section	Township	Range		County	
	11. Elevation (Show wheth	er DR, RKB, RT, GR, etc	:.)		
•	propriate Box to Indica		1		
TEMPORARILY ABANDON	ENTION TO: PLUG AND ABANDON  CHANGE PLANS  MULTIPLE COMPL	REMEDIAL WOR COMMENCE DRI CASING/CEMEN	ILLING OPNS.□ F	ORT OF: ALTERING CASING  PAND A	
CLOSED-LOOP SYSTEM  OTHER:		OTHER:			
13. Describe proposed or complet of starting any proposed work proposed completion or recon	t). SEE RULE 19.15.7.14 N	IMAC. For Multiple Co			
		<u> </u>		_	
I hereby certify that the information ab	ove is true and complete to	the best of my knowledg	e and belief.		
SIGNATURE Alicia Fulta	TITLE_		DAT	`E	
Type or print name  For State Use Only	E-mail ac	ldress:	PHO	NE:	
APPROVED BY:Conditions of Approval (if any):	TITLE		DAT	E	



Post Office Box 61229 Houston, TX 77208-1229

1111 Travis St Houston, TX 77002

Phone: 713/209-2400

### PROPOSED PROCEDURE TO REPAIR

NORTHEAST DRINKARD UNIT #813 (30-025-06772)

- 1. MIRU
- 2. NM WELLHEAD. NU BOPD. TEST BOP.
- PULL TUBING OUT OF THE HOLE WHILE SCANNING. ENSURE THAT THE SCANNER IS CALIBRATED FOR LINED TUBING. LAY DOWN ALL RED BAND AND GREEN BAND JOINTS.
- 4. PICK AND RUN IN THE HOLE WITH PACKER AND RBP. SET RBP AT LEAST 500' ABOVE TOP PERFS. SET PACKER. LOAD AND TEST CASING TO 550 PSI.
- PULL OUT OF THE HOLE WITH TOOLS AND RUN BACK IN THE HOLE WITH A BIT AND BAILER. CLEAN OUT THE WELLBORE TO THE PBTD. PULL OUT OF THE HOLE AND LAY DOWN ALL TOOLS.
- PICK UP WORK STRING AND RUN IN HOLE WITH AN INJECTION PACKER WITH PUMP OUT PLUG. SET PACKER WITHIN 100' OF TOP PERFORMATIONS.
- 7. LOAD AND TEST CASING TO 550 PSI FOR 30 MINUTES. PULL OUT OF THE HOLE AND LAY DOWN WORK STRING.
- RIG UP TUBING TESTERS AND TEST INJECTION TUBING WHILE RUNNING IN THE HOLE. CIRCULATE PACKER FLUID. LATCH ONTO PACKER. PUMP OUT PLUG.
- CONTACT NMOCD WITH AT LEAST 24 HOURS NOTICE, TO SCHEDULE MIT TEST. RUN MIT AT 550 PSI FOR 30 MINUTES AND SUBMIT PASSING TEST AS SOON AS POSSIBLE.
- 10. RDMO




## **Current/Proposed WBD**

### Well Name: NORTHEAST DRINKARD UNIT 813W

2002506772		Field Name Eunice		Well Configuration Type Vertical
Original KB/RT Elevation (ft) 3,400.00	RKB to GL (ft) 11.00	Original Spud Date 10/2/1949 00:00	PBTD (All) Original Hole - 6,595.0	Total Depth All (TVD)

| Most Recent Job | Secondary Job Type | Secondary Job Type | LOE-Repair/Maint; Check TD | Actual Start Date | Loe-Repair/Maint; Check TD | Actual Start Date | Loe-Repair/Maint; Check TD | Alp/2019 | Alp/2019

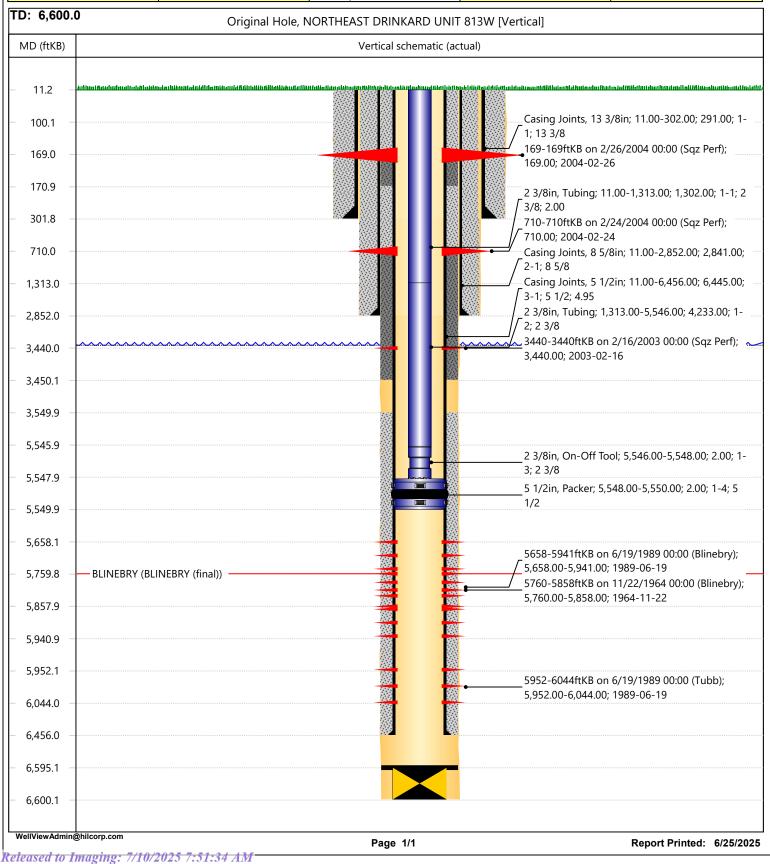

Sante Fe Main Office Phone: (505) 476-3441

General Information Phone: (505) 629-6116

Online Phone Directory https://www.emnrd.nm.gov/ocd/contact-us

# State of New Mexico Energy, Minerals and Natural Resources Oil Conservation Division 1220 S. St Francis Dr. Santa Fe, NM 87505

CONDITIONS

Action 480780

### **CONDITIONS**

Operator:	OGRID:
APACHE CORPORATION	873
303 Veterans Airpark Ln	Action Number:
Midland, TX 79705	480780
	Action Type:
	[C-103] NOI Workover (C-103G)

### CONDITIONS

Created By	Condition	Condition Date
gcordero	If the workover requires tubing change same tube size shall be replaced as prescribed by the respective order and the packer shall not be set more than 100 ft above the top of the injection interval.	7/10/2025
gcordero	Passing MIT test in accordance with 19.15.26.11 NMAC.	7/10/2025
