

C-104 Submit Electronically Via OCD Permitting	State of New Mexico Energy, Minerals & Natural Resources Department OIL CONSERVATION DIVISION	Revised July 9, 2024
---	--	----------------------

REQUEST FOR ALLOWABLE AND AUTHORIZATION TO TRANSPORT**Section 1 - Operator and Well Information**

Submittal Type: ☐ Test Allowable (C-104RT) ☒ New Well (C-104NW) ☐ Recomplete (C-104RC) ☐ Pay Add (C-104RC) ☐ Amended	
Operator Name: EOG Resources, INC	OGRID: 7377
Property Name and Well Number: PEACHTREE 25 FED COM 747H	Property Code: 331002
Mineral Owner: ☐ State ☐ Fee ☐ Tribal ☒ Federal	API Number: 30-025-49370
Pool Name: SANDERS TANK; UPPER WOLFCAMP	Pool Code: 98097

Section 2 – Surface Location

UL	Section	Township	Range	Lot	Ft. from N/S	Ft. from E/W	Latitude	Longitude	County
B	25	26S	33E		163' FNL	2276' FEL	32.0212192	103.5248852	LEA

Section 3 – Completion Information

Producing Method	Ready Date	Perforations MD	Perforations TVD
FLOWING	1/24/2022	13,287'-23,561'	13,064'-13,183'

Section 4 – Action IDs for Submissions and Order Numbers

List Action IDs for Drilling Sundries	Was an Order required / needed (Y/N), if yes list Order number:
C-104 RT Action ID (if C-104NW):	Communitization Agreement ☒ Yes ☐ No, Order No. NMNM105677646
Surface Casing Action ID: 76955	Unit: ☐ Yes ☒ No, Order No.
Intermediate 1 Casing Action ID: 76955	Compulsory Pooling: ☐ Yes ☒ No, Order No.
Intermediate 2 Casing Action ID:	Down Hole Commingling: ☐ Yes ☒ No, Order No.
Production Casing Action ID: 76955	Surface Commingling: ☒ Yes ☐ No, Order No. CTB-1031
All casing was pressure tested in accordance with NMAC ☒ Yes ☐ No	Non-standard Location: ☐ Yes ☒ No ☐ Common ownership Order No.
Liner 1 Action ID:	Non-standard Proration: ☐ Yes ☒ No, Order No.
Casing was installed prior to OCD's Action ID system (Y/N):	Simultaneous Dedication: ☐ Yes ☒ No, Order No.

Section 5 - Operator Signature and Certification

☒ I hereby certify that the required Water Use Report has been, or will be, submitted for this well's completion.	
☒ I hereby certify that the required Fracfocus disclosure has been, or will be, submitted for this well's completion.	
☒ I hereby certify that the rules of the Oil Conservation Division have been complied with and that the information given above is true and complete to the best of my knowledge and belief.	
Name Kristina Agee	
Title REGULATORY SPECIALIST	Date 9/10/2024

**BOTTOM HOLE LOCATION
NEW MEXICO EAST**
NAD 1983
X=792449
Y=383015
LAT.: N 32.0503961
LONG.: W 103.5228330
MD = 23578'

**LAST TAKE POINT
NEW MEXICO EAST**
NAD 1983
X=792450
Y=382998
LAT.: N 32.0503494
LONG.: W 103.5228312
MD = 23561'

POINT	UTM ZONE 13 COORDINATES	
SHL	X=2097460.556	Y=11626416.218
KOP	X=2098089.850	Y=11626518.090
FTP	X=2098136.312	Y=11626766.346
LTP	X=2097952.020	Y=11637019.863
BHL	X=2097950.915	Y=11637036.944

**KICK OFF POINT
NEW MEXICO EAST**
NAD 1983
X=792523
Y=372494
LAT.: N 32.0214757
LONG.: W 103.5228482
MD = 12895'

**FIRST TAKE POINT
NEW MEXICO EAST**
NAD 1983
X=792571
Y=372742
LAT.: N 32.0221579
LONG.: W 103.5226895
MD = 13287'

**SURFACE LOCATION
NEW MEXICO EAST**
NAD 1983
X=791893
Y=372396
LAT.: N 32.0212192
LONG.: W 103.5248852

Certificate Number

Released to Imaging: 10/10/2025 2:47:35 PM



Midland

Lea County, NM (NAD 83 NME)
Peachtree 25 Fed Com
#747H
OH

Design: OH

Midland PVA

01 December, 2021



EOG Resources

Midland PVA

Company:	Midland	Local Co-ordinate Reference:	Well #747H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 26' @ 3383.0usft
Site:	Peachtree 25 Fed Com	MD Reference:	KB = 26' @ 3383.0usft
Well:	#747H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Project	Lea County, NM (NAD 83 NME)		
Map System:	US State Plane 1983	System Datum:	Mean Sea Level
Geo Datum:	North American Datum 1983		
Map Zone:	New Mexico Eastern Zone		

Site	Peachtree 25 Fed Com		
Site Position:		Northing:	372,298.00 usft
From:	Map	Easting:	789,709.00 usft
Position Uncertainty:	0.0 usft	Slot Radius:	13-3/16 "
		Latitude:	32° 1' 15.583 N
		Longitude:	103° 31' 54.959 W
		Grid Convergence:	0.42 °

Well		#747H				
Well Position	+N/-S	0.0 usft	Northing:	372,396.00 usft	Latitude:	32° 1' 16.392 N
	+E/-W	0.0 usft	Easting:	791,893.00 usft	Longitude:	103° 31' 29.583 W
Position Uncertainty		0.0 usft	Wellhead Elevation:	usft	Ground Level:	3,357.0 usft

Wellbore	OH				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	IGRF2020	10/10/2021	6.47	59.71	47,345.74291556

Design	OH				
Audit Notes:					
Version:	1.0	Phase:	ACTUAL	Tie On Depth:	0.0
Vertical Section:	Depth From (TVD) (usft)	+N/-S (usft)	+E/-W (usft)	Direction (°)	
	0.0	0.0	0.0	3.14	

Survey Program	Date	11/29/2021			
From (usft)	To (usft)	Survey (Wellbore)	Tool Name	Description	
199.0	23,578.0	Altitude MWD (OH)	EOG MWD+IFR1	MWD + IFR1	



EOG Resources

Midland PVA

Company: Midland
Project: Lea County, NM (NAD 83 NME)
Site: Peachtree 25 Fed Com
Well: #747H
Wellbore: OH
Design: OH

Local Co-ordinate Reference: Well #747H
TVD Reference: KB = 26' @ 3383.0usft
MD Reference: KB = 26' @ 3383.0usft
North Reference: Grid
Survey Calculation Method: Minimum Curvature
Database: PEDM

Survey											
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)	
0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.00	0.0	0.0	
199.0	0.65	39.38	199.0	0.9	0.7	0.33	0.33	0.00	-1.1	0.0	
313.0	0.75	71.00	313.0	1.6	1.8	0.35	0.09	27.74	-2.3	0.9	
499.0	0.46	52.71	499.0	2.5	3.6	0.19	-0.16	-9.83	-4.3	-0.2	
689.0	1.31	65.92	689.0	3.8	6.2	0.46	0.45	6.95	-7.2	1.0	
879.0	1.57	79.62	878.9	5.2	10.7	0.23	0.14	7.21	-11.5	3.2	
913.0	1.24	82.90	912.9	5.3	11.5	1.00	-0.97	9.65	-12.1	3.8	
1,073.0	1.31	93.19	1,072.8	5.4	15.1	0.15	0.04	6.43	-14.7	6.2	
1,263.0	4.34	100.40	1,262.6	4.0	24.3	1.60	1.59	3.79	-15.3	7.2	
1,452.0	3.87	102.95	1,451.1	1.3	37.6	0.27	-0.25	1.35	-10.7	4.9	
1,547.0	3.93	102.98	1,545.9	-0.2	43.9	0.06	0.06	0.03	-7.8	3.1	
1,737.0	7.40	103.60	1,734.9	-4.5	62.1	1.83	1.83	0.33	-7.7	-0.5	
1,927.0	7.41	107.10	1,923.3	-11.0	85.7	0.24	0.01	1.84	-13.6	-4.2	
2,116.0	8.75	91.99	2,110.5	-15.1	111.7	1.32	0.71	-7.99	-19.2	-10.6	
2,306.0	9.28	95.27	2,298.1	-17.0	141.4	0.39	0.28	1.73	-30.4	-9.7	
2,495.0	9.71	97.58	2,484.6	-20.5	172.4	0.30	0.23	1.22	-43.1	-9.6	
2,685.0	10.37	98.14	2,671.6	-25.0	205.2	0.35	0.35	0.29	-57.3	-11.0	
2,875.0	10.99	97.42	2,858.3	-29.8	240.1	0.33	0.33	-0.38	-73.4	-13.6	
3,065.0	12.99	98.44	3,044.2	-35.3	279.2	1.06	1.05	0.54	-94.3	-14.1	
3,254.0	13.47	85.28	3,228.2	-36.6	322.1	1.61	0.25	-6.96	-112.6	-37.7	
3,349.0	13.13	86.29	3,320.7	-35.0	343.9	0.43	-0.36	1.06	-125.8	-34.5	
3,539.0	10.85	80.54	3,506.5	-30.6	383.1	1.35	-1.20	-3.03	-142.6	-45.0	
3,634.0	8.02	83.05	3,600.2	-28.4	398.5	3.01	-2.98	2.64	-150.6	-36.7	
3,817.0	7.82	83.53	3,781.5	-25.4	423.6	0.12	-0.11	0.26	-157.9	-32.5	
4,007.0	8.36	84.51	3,969.6	-22.6	450.2	0.29	0.28	0.52	-166.2	-27.0	
4,101.0	8.97	79.16	4,062.5	-20.6	464.2	1.07	0.65	-5.69	-167.9	-40.8	
4,196.0	9.70	79.90	4,156.3	-17.8	479.3	0.78	0.77	0.78	-174.5	-36.5	



EOG Resources

Midland PVA

Company:	Midland	Local Co-ordinate Reference:	Well #747H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 26' @ 3383.0usft
Site:	Peachtree 25 Fed Com	MD Reference:	KB = 26' @ 3383.0usft
Well:	#747H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Survey											
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)	
4,291.0	7.93	74.52	4,250.1	-14.6	493.5	2.05	-1.86	-5.66	-175.8	-50.4	
4,386.0	7.09	68.47	4,344.3	-10.7	505.3	1.21	-0.88	-6.37	-173.1	-65.4	
4,480.0	7.79	69.17	4,437.5	-6.4	516.6	0.75	0.74	0.74	-177.4	-59.5	
4,575.0	8.86	75.56	4,531.5	-2.2	529.7	1.49	1.13	6.73	-187.4	-36.0	
4,669.0	8.86	76.68	4,624.4	1.2	543.8	0.18	0.00	1.19	-193.5	-29.7	
4,764.0	6.97	77.74	4,718.5	4.1	556.5	2.00	-1.99	1.12	-197.8	-23.5	
4,859.0	7.09	83.11	4,812.8	6.1	568.0	0.70	0.13	5.65	-201.3	-2.9	
4,954.0	8.13	92.28	4,906.9	6.5	580.5	1.68	1.09	9.65	-202.1	30.0	
5,049.0	8.56	100.36	5,000.9	5.0	594.2	1.31	0.45	8.51	-200.2	57.6	
5,143.0	5.99	99.61	5,094.2	2.9	605.9	2.74	-2.73	-0.80	-203.4	53.7	
5,238.0	3.46	95.15	5,188.9	1.8	613.7	2.69	-2.66	-4.69	-205.2	37.0	
5,333.0	2.92	92.74	5,283.7	1.4	618.9	0.59	-0.57	-2.54	-202.3	28.2	
5,523.0	3.08	89.48	5,473.4	1.2	628.9	0.12	0.08	-1.72	-194.3	17.3	
5,618.0	2.94	88.96	5,568.3	1.3	633.9	0.15	-0.15	-0.55	-189.8	16.1	
5,713.0	2.86	85.12	5,663.2	1.6	638.7	0.22	-0.08	-4.04	-185.8	4.5	
5,902.0	2.68	73.87	5,852.0	3.2	647.6	0.30	-0.10	-5.95	-174.0	-26.6	
6,091.0	2.63	72.78	6,040.8	5.7	656.0	0.04	-0.03	-0.58	-164.2	-23.6	
6,186.0	2.39	73.11	6,135.7	6.9	660.0	0.25	-0.25	0.35	-159.4	-19.5	
6,281.0	2.44	71.32	6,230.6	8.1	663.8	0.10	0.05	-1.88	-153.8	-21.1	
6,376.0	2.21	73.44	6,325.5	9.3	667.4	0.26	-0.24	2.23	-149.2	-12.2	
6,470.0	2.01	71.22	6,419.5	10.4	670.7	0.23	-0.21	-2.36	-143.2	-14.6	
6,564.0	2.54	75.91	6,513.4	11.4	674.3	0.60	0.56	4.99	-138.6	-0.1	
6,659.0	3.02	88.09	6,608.3	12.0	678.9	0.80	0.51	12.82	-130.5	30.2	
6,754.0	2.97	87.93	6,703.1	12.2	683.8	0.05	-0.05	-0.17	-125.9	30.6	
6,848.0	2.91	84.96	6,797.0	12.5	688.6	0.17	-0.06	-3.16	-122.7	25.1	
6,943.0	2.86	85.64	6,891.9	12.9	693.4	0.06	-0.05	0.72	-117.7	27.7	
7,038.0	2.96	84.50	6,986.8	13.3	698.2	0.12	0.11	-1.20	-113.5	26.6	



EOG Resources

Midland PVA

Company:	Midland	Local Co-ordinate Reference:	Well #747H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 26' @ 3383.0usft
Site:	Peachtree 25 Fed Com	MD Reference:	KB = 26' @ 3383.0usft
Well:	#747H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Survey										
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
7,133.0	2.87	81.38	7,081.6	13.9	703.0	0.19	-0.09	-3.28	-110.2	22.1
7,228.0	1.72	113.93	7,176.6	13.6	706.7	1.78	-1.21	34.26	-75.6	75.6
7,322.0	1.79	135.11	7,270.5	12.0	709.0	0.69	0.07	22.53	-39.0	91.8
7,417.0	1.72	135.71	7,365.5	10.0	711.0	0.08	-0.07	0.63	-34.0	85.7
7,512.0	1.75	140.76	7,460.4	7.8	712.9	0.16	0.03	5.32	-22.8	81.3
7,607.0	1.61	150.75	7,555.4	5.5	714.5	0.34	-0.15	10.52	-6.1	76.1
7,796.0	1.48	158.26	7,744.3	0.9	716.7	0.13	-0.07	3.97	4.2	64.5
7,890.0	1.53	170.48	7,838.3	-1.4	717.4	0.34	0.05	13.00	15.8	60.4
7,985.0	1.44	182.60	7,933.3	-3.9	717.5	0.34	-0.09	12.76	25.7	55.9
8,080.0	1.78	192.57	8,028.2	-6.5	717.1	0.46	0.36	10.49	32.3	50.8
8,175.0	2.15	197.25	8,123.2	-9.6	716.3	0.42	0.39	4.93	33.1	48.1
8,270.0	2.07	199.27	8,218.1	-13.0	715.2	0.11	-0.08	2.13	31.3	47.0
8,364.0	1.95	196.75	8,312.1	-16.1	714.2	0.16	-0.13	-2.68	25.9	48.3
8,459.0	2.00	190.86	8,407.0	-19.3	713.4	0.22	0.05	-6.20	17.5	50.5
8,554.0	2.03	188.74	8,501.9	-22.6	712.8	0.08	0.03	-2.23	12.3	51.1
8,649.0	2.17	187.00	8,596.9	-26.0	712.4	0.16	0.15	-1.83	7.3	51.3
8,744.0	2.17	188.28	8,691.8	-29.6	711.9	0.05	0.00	1.35	4.8	51.2
8,838.0	2.15	196.18	8,785.7	-33.0	711.1	0.32	-0.02	8.40	8.3	50.3
8,933.0	2.13	201.92	8,880.7	-36.4	710.0	0.23	-0.02	6.04	9.8	49.4
9,029.0	2.08	205.49	8,976.6	-39.6	708.6	0.15	-0.05	3.72	9.3	48.8
9,218.0	1.84	214.40	9,165.5	-45.2	705.4	0.20	-0.13	4.71	10.3	47.3
9,313.0	1.83	220.68	9,260.4	-47.6	703.5	0.21	-0.01	6.61	12.4	46.1
9,408.0	1.95	224.68	9,355.4	-49.9	701.4	0.19	0.13	4.21	12.5	45.2
9,503.0	1.78	226.08	9,450.3	-52.1	699.2	0.19	-0.18	1.47	10.5	44.9
9,598.0	1.48	234.43	9,545.3	-53.8	697.1	0.40	-0.32	8.79	14.2	43.1
9,693.0	1.19	248.99	9,640.3	-54.9	695.2	0.47	-0.31	15.33	22.4	38.5
9,788.0	1.09	262.32	9,735.3	-55.4	693.4	0.30	-0.11	14.03	28.8	32.5



EOG Resources

Midland PVA

Company:	Midland	Local Co-ordinate Reference:	Well #747H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 26' @ 3383.0usft
Site:	Peachtree 25 Fed Com	MD Reference:	KB = 26' @ 3383.0usft
Well:	#747H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Survey										
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
9,883.0	1.11	277.06	9,830.2	-55.4	691.6	0.30	0.02	15.52	34.3	24.3
9,978.0	1.16	286.56	9,925.2	-55.0	689.8	0.20	0.05	10.00	36.0	18.5
10,073.0	1.61	317.53	10,020.2	-53.7	687.9	0.90	0.47	32.60	38.2	-2.2
10,167.0	2.74	310.86	10,114.1	-51.3	685.3	1.23	1.20	-7.10	34.7	2.1
10,262.0	3.32	315.96	10,209.0	-47.8	681.7	0.67	0.61	5.37	29.7	-0.8
10,357.0	3.28	296.71	10,303.8	-44.6	677.4	1.16	-0.04	-20.26	23.0	8.2
10,452.0	3.85	285.64	10,398.7	-42.5	671.9	0.94	0.60	-11.65	15.1	11.9
10,547.0	3.16	278.15	10,493.5	-41.3	666.2	0.87	-0.73	-7.88	7.7	13.4
10,642.0	2.37	272.59	10,588.4	-40.8	661.7	0.88	-0.83	-5.85	1.8	13.8
10,832.0	1.72	293.45	10,778.3	-39.5	655.1	0.51	-0.34	10.98	0.0	13.6
10,927.0	1.63	269.37	10,873.2	-39.0	652.5	0.74	-0.09	-25.35	-8.2	11.9
11,021.0	2.28	255.42	10,967.2	-39.5	649.3	0.85	0.69	-14.84	-14.0	9.3
11,116.0	2.46	258.83	11,062.1	-40.3	645.5	0.24	0.19	3.59	-17.3	10.2
11,306.0	4.31	252.66	11,251.7	-43.3	634.7	0.99	0.97	-3.25	-29.5	7.8
11,400.0	3.02	260.59	11,345.5	-44.7	628.8	1.47	-1.37	8.44	-34.1	12.3
11,495.0	2.36	264.00	11,440.4	-45.3	624.4	0.71	-0.69	3.59	-37.8	14.5
11,590.0	2.35	249.12	11,535.4	-46.2	620.7	0.64	-0.01	-15.66	-44.1	3.8
11,779.0	2.62	241.35	11,724.2	-49.7	613.3	0.23	0.14	-4.11	-52.3	-2.8
11,873.0	2.50	243.46	11,818.1	-51.6	609.5	0.16	-0.13	2.24	-56.6	-0.7
11,969.0	2.89	238.09	11,914.0	-53.8	605.6	0.48	0.41	-5.59	-60.8	-6.2
12,063.0	2.57	230.68	12,007.9	-56.4	602.0	0.51	-0.34	-7.88	-63.9	-14.3
12,158.0	2.51	224.46	12,102.8	-59.3	598.9	0.30	-0.06	-6.55	-66.2	-21.4
12,253.0	1.77	229.47	12,197.7	-61.7	596.3	0.80	-0.78	5.27	-71.4	-15.4
12,346.0	1.38	347.87	12,290.7	-61.5	595.0	2.92	-0.42	127.31	20.0	71.3
12,393.0	6.22	17.95	12,337.6	-58.6	595.6	10.79	10.30	64.00	49.9	52.1
12,441.0	11.43	14.69	12,385.0	-51.5	597.6	10.90	10.85	-6.79	40.2	54.6
12,536.0	16.13	13.78	12,477.2	-29.5	603.2	4.95	4.95	-0.96	25.0	53.0



EOG Resources

Midland PVA

Company:	Midland	Local Co-ordinate Reference:	Well #747H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 26' @ 3383.0usft
Site:	Peachtree 25 Fed Com	MD Reference:	KB = 26' @ 3383.0usft
Well:	#747H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Survey											
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)	
12,630.0	16.95	12.71	12,567.3	-3.5	609.3	0.93	0.87	-1.14	14.4	49.1	
12,725.0	22.78	14.25	12,656.7	27.9	616.9	6.16	6.14	1.62	8.9	42.3	
12,820.0	25.37	12.41	12,743.4	65.6	625.8	2.84	2.73	-1.94	3.5	34.0	
12,888.0	26.32	5.35	12,804.6	94.8	630.3	4.73	1.40	-10.38	0.9	29.3	
12,895.0	26.66	5.72	12,810.9	97.9	630.6	5.44	4.92	5.22	1.2	29.0	
KOP, MD:12895.0', TVD:12810.9', N/S:97.9', E/W:630.6', INC:26.66											
12,932.0	28.50	7.51	12,843.7	114.9	632.6	5.44	4.96	4.85	2.1	26.8	
13,027.0	35.09	12.32	12,924.4	164.1	641.4	7.43	6.94	5.06	2.2	17.6	
13,029.9	35.30	12.33	12,926.7	165.8	641.8	7.12	7.12	0.23	2.2	17.2	
LL Crossing, MD:13029.9', TVD:12926.7', N/S:165.8', E/W:641.8', INC:35.30											
13,121.0	41.78	12.51	12,998.0	221.2	654.0	7.12	7.12	0.20	4.5	4.0	
13,186.5	47.36	12.05	13,044.6	266.1	663.7	8.54	8.53	-0.70	8.2	-6.5	
FTP Crossing, MD:13186.5', TVD:13044.6', N/S:266.1', E/W:663.7', INC:47.36											
13,216.0	49.88	11.87	13,064.1	287.7	668.3	8.54	8.53	-0.61	10.2	-11.5	
13,311.0	63.34	7.08	13,116.3	365.8	681.1	14.77	14.17	-5.04	15.0	-24.3	
13,358.0	68.88	3.41	13,135.3	408.6	685.0	13.78	11.79	-7.81	15.7	-28.0	
13,399.0	74.32	0.18	13,148.3	447.4	686.2	15.23	13.27	-7.88	15.3	-29.2	
13,450.0	80.47	358.61	13,159.4	497.2	685.6	12.43	12.06	-3.08	13.0	-29.0	
13,501.0	81.16	359.18	13,167.5	547.5	684.7	1.75	1.35	1.12	12.0	-28.4	
13,596.0	85.69	359.80	13,178.4	641.9	683.8	4.81	4.77	0.65	17.3	-28.3	
13,690.0	89.12	0.60	13,182.7	735.7	684.2	3.75	3.65	0.85	21.3	-29.3	
13,785.0	90.38	0.65	13,183.1	830.7	685.2	1.33	1.33	0.05	21.5	-31.0	
13,880.0	91.02	358.32	13,181.9	925.7	684.3	2.54	0.67	-2.45	20.0	-30.8	
13,975.0	91.25	357.42	13,180.0	1,020.6	680.8	0.98	0.24	-0.95	17.9	-28.0	
14,069.0	91.13	358.32	13,178.1	1,114.5	677.3	0.97	-0.13	0.96	15.6	-25.2	
14,164.0	91.81	358.18	13,175.6	1,209.5	674.4	0.73	0.72	-0.15	12.9	-23.0	
14,259.0	89.43	356.30	13,174.6	1,304.3	669.9	3.19	-2.51	-1.98	11.6	-19.1	



EOG Resources

Midland PVA

Company:	Midland	Local Co-ordinate Reference:	Well #747H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 26' @ 3383.0usft
Site:	Peachtree 25 Fed Com	MD Reference:	KB = 26' @ 3383.0usft
Well:	#747H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Survey										
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
14,354.0	89.31	356.64	13,175.7	1,399.2	664.0	0.38	-0.13	0.36	12.4	-14.0
14,448.0	90.07	358.13	13,176.2	1,493.1	659.7	1.78	0.81	1.59	12.6	-10.4
14,543.0	91.13	359.19	13,175.2	1,588.0	657.5	1.58	1.12	1.12	11.3	-8.9
14,638.0	89.23	357.65	13,174.9	1,683.0	654.9	2.57	-2.00	-1.62	10.7	-6.9
14,733.0	90.71	359.81	13,174.9	1,777.9	652.8	2.76	1.56	2.27	10.5	-5.5
14,827.0	87.72	358.60	13,176.2	1,871.9	651.5	3.43	-3.18	-1.29	11.5	-4.9
14,922.0	86.79	359.20	13,180.8	1,966.8	649.6	1.16	-0.98	0.63	15.7	-3.8
15,016.0	86.82	359.52	13,186.0	2,060.6	648.6	0.34	0.03	0.34	20.7	-3.4
15,111.0	89.15	0.43	13,189.3	2,155.6	648.6	2.63	2.45	0.96	23.7	-4.1
15,206.0	88.56	0.39	13,191.2	2,250.5	649.2	0.62	-0.62	-0.04	25.4	-5.5
15,301.0	88.98	359.17	13,193.3	2,345.5	648.9	1.36	0.44	-1.28	27.1	-5.8
15,396.0	89.82	359.24	13,194.3	2,440.5	647.5	0.89	0.88	0.07	27.8	-5.2
15,490.0	91.25	358.40	13,193.4	2,534.5	645.6	1.76	1.52	-0.89	26.7	-3.9
15,585.0	92.48	359.16	13,190.3	2,629.4	643.6	1.52	1.29	0.80	23.3	-2.6
15,680.0	92.17	358.73	13,186.4	2,724.3	641.8	0.56	-0.33	-0.45	19.1	-1.5
15,775.0	93.09	359.41	13,182.1	2,819.2	640.3	1.20	0.97	0.72	14.5	-0.7
15,869.0	92.37	358.37	13,177.6	2,913.1	638.5	1.34	-0.77	-1.11	9.7	0.4
15,964.0	90.60	357.24	13,175.1	3,008.0	634.8	2.21	-1.86	-1.19	7.0	3.4
16,059.0	88.98	357.40	13,175.5	3,102.9	630.4	1.71	-1.71	0.17	7.0	7.1
16,154.0	88.17	356.50	13,177.9	3,197.7	625.4	1.27	-0.85	-0.95	9.1	11.5
16,249.0	89.17	357.26	13,180.1	3,292.5	620.2	1.32	1.05	0.80	11.0	15.9
16,344.0	89.17	357.95	13,181.4	3,387.4	616.2	0.73	0.00	0.73	11.7	19.2
16,439.0	90.10	358.58	13,182.0	3,482.4	613.3	1.18	0.98	0.66	11.6	21.4
16,533.0	91.19	359.41	13,181.0	3,576.4	611.7	1.46	1.16	0.88	9.8	22.4
16,628.0	91.11	358.01	13,179.1	3,671.3	609.6	1.48	-0.08	-1.47	7.2	23.8
16,723.0	89.17	359.69	13,178.8	3,766.3	607.6	2.70	-2.04	1.77	6.3	25.0
16,817.0	88.28	358.74	13,180.9	3,860.3	606.4	1.38	-0.95	-1.01	7.6	25.7



EOG Resources

Midland PVA

Company:	Midland	Local Co-ordinate Reference:	Well #747H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 26' @ 3383.0usft
Site:	Peachtree 25 Fed Com	MD Reference:	KB = 26' @ 3383.0usft
Well:	#747H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Survey										
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
16,912.0	88.61	359.40	13,183.5	3,955.2	604.8	0.78	0.35	0.69	9.5	26.5
17,006.0	87.97	358.50	13,186.3	4,049.1	603.1	1.17	-0.68	-0.96	11.6	27.6
17,101.0	88.47	359.96	13,189.3	4,144.1	601.8	1.62	0.53	1.54	13.8	28.1
17,196.0	88.84	0.49	13,191.5	4,239.1	602.2	0.68	0.39	0.56	15.4	27.1
17,291.0	88.16	359.20	13,194.0	4,334.0	601.9	1.53	-0.72	-1.36	17.1	26.6
17,400.0	91.50	359.81	13,194.3	4,443.0	601.0	3.11	3.06	0.56	16.6	26.8
17,480.0	92.37	0.71	13,191.6	4,523.0	601.4	1.56	1.09	1.12	13.3	25.9
17,575.0	93.52	0.97	13,186.7	4,617.8	602.7	1.24	1.21	0.27	7.7	23.8
17,670.0	91.27	1.07	13,182.8	4,712.7	604.4	2.37	-2.37	0.11	3.7	21.4
17,764.0	91.86	1.94	13,180.2	4,806.6	606.9	1.12	0.63	0.93	1.1	18.2
17,859.0	89.06	1.45	13,179.4	4,901.6	609.7	2.99	-2.95	-0.52	0.4	14.7
17,954.0	89.73	1.79	13,180.4	4,996.5	612.4	0.79	0.71	0.36	1.4	11.4
18,049.0	91.13	2.79	13,179.7	5,091.5	616.2	1.81	1.47	1.05	0.6	6.9
18,143.0	91.83	2.89	13,177.3	5,185.3	620.9	0.75	0.74	0.11	-1.8	1.5
18,238.0	89.48	0.36	13,176.2	5,280.3	623.5	3.63	-2.47	-2.66	-2.9	-1.8
18,333.0	88.08	358.82	13,178.2	5,375.2	622.9	2.19	-1.47	-1.62	-0.8	-1.8
18,428.0	88.25	358.92	13,181.3	5,470.2	621.0	0.21	0.18	0.11	2.2	-0.7
18,523.0	89.29	0.95	13,183.3	5,565.1	620.9	2.40	1.09	2.14	4.2	-1.2
18,617.0	89.48	1.44	13,184.3	5,659.1	622.8	0.56	0.20	0.52	5.3	-3.9
18,712.0	90.10	1.28	13,184.7	5,754.1	625.1	0.67	0.65	-0.17	5.6	-6.8
18,807.0	90.52	1.00	13,184.2	5,849.1	627.0	0.53	0.44	-0.29	5.1	-9.4
18,902.0	90.07	0.46	13,183.7	5,944.1	628.2	0.74	-0.47	-0.57	4.6	-11.3
18,997.0	89.93	0.75	13,183.7	6,039.0	629.2	0.34	-0.15	0.31	4.6	-13.0
19,091.0	89.90	0.47	13,183.8	6,133.0	630.2	0.30	-0.03	-0.30	4.7	-14.7
19,186.0	92.06	2.21	13,182.2	6,228.0	632.4	2.92	2.27	1.83	3.1	-17.6
19,281.0	89.73	359.30	13,180.7	6,323.0	633.7	3.92	-2.45	-3.06	1.6	-19.5
19,375.0	89.73	358.80	13,181.1	6,416.9	632.1	0.53	0.00	-0.53	2.1	-18.6



EOG Resources

Midland PVA

Company:	Midland	Local Co-ordinate Reference:	Well #747H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 26' @ 3383.0usft
Site:	Peachtree 25 Fed Com	MD Reference:	KB = 26' @ 3383.0usft
Well:	#747H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Survey										
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
19,470.0	89.85	357.48	13,181.5	6,511.9	629.0	1.40	0.13	-1.39	2.4	-16.3
19,565.0	89.82	357.28	13,181.8	6,606.8	624.7	0.21	-0.03	-0.21	2.7	-12.6
19,660.0	89.51	357.17	13,182.3	6,701.7	620.1	0.35	-0.33	-0.12	3.3	-8.7
19,755.0	90.24	357.66	13,182.5	6,796.6	615.8	0.93	0.77	0.52	3.5	-5.1
19,850.0	90.49	357.32	13,181.9	6,891.5	611.6	0.44	0.26	-0.36	2.9	-1.6
19,945.0	91.30	357.09	13,180.4	6,986.4	607.0	0.89	0.85	-0.24	1.4	2.3
20,040.0	90.52	359.18	13,178.9	7,081.3	603.9	2.35	-0.82	2.20	-0.1	4.7
20,135.0	90.29	358.86	13,178.3	7,176.3	602.3	0.41	-0.24	-0.34	-0.8	5.7
20,229.0	90.77	358.51	13,177.4	7,270.2	600.1	0.63	0.51	-0.37	-1.7	7.1
20,324.0	89.20	359.40	13,177.4	7,365.2	598.4	1.90	-1.65	0.94	-1.6	8.2
20,419.0	88.33	359.04	13,179.5	7,460.2	597.1	0.99	-0.92	-0.38	0.4	8.8
20,514.0	88.19	358.61	13,182.3	7,555.1	595.2	0.48	-0.15	-0.45	3.3	10.0
20,609.0	88.19	357.82	13,185.3	7,650.0	592.2	0.83	0.00	-0.83	6.3	12.3
20,704.0	87.69	357.74	13,188.8	7,744.9	588.5	0.53	-0.53	-0.08	9.7	15.3
20,799.0	89.76	358.57	13,190.9	7,839.8	585.5	2.35	2.18	0.87	11.8	17.7
20,893.0	90.29	1.81	13,190.8	7,933.8	585.8	3.49	0.56	3.45	11.8	16.7
20,988.0	90.83	2.20	13,189.9	8,028.7	589.1	0.70	0.57	0.41	10.9	12.7
21,083.0	91.61	1.63	13,187.9	8,123.7	592.3	1.02	0.82	-0.60	8.8	8.8
21,177.0	91.53	1.06	13,185.3	8,217.6	594.5	0.61	-0.09	-0.61	6.3	5.9
21,272.0	90.83	359.62	13,183.3	8,312.6	595.1	1.69	-0.74	-1.52	4.3	4.7
21,366.0	91.14	359.45	13,181.7	8,406.6	594.3	0.38	0.33	-0.18	2.7	4.8
21,461.0	91.86	0.45	13,179.2	8,501.5	594.2	1.30	0.76	1.05	0.2	4.1
21,555.0	89.90	0.10	13,177.8	8,595.5	594.7	2.12	-2.09	-0.37	-1.2	3.0
21,650.0	90.13	359.74	13,177.8	8,690.5	594.5	0.45	0.24	-0.38	-1.3	2.5
21,745.0	90.04	0.02	13,177.6	8,785.5	594.3	0.31	-0.09	0.29	-1.4	2.0
21,839.0	90.13	0.19	13,177.5	8,879.5	594.5	0.20	0.10	0.18	-1.5	1.1
21,934.0	89.40	359.37	13,177.9	8,974.5	594.1	1.16	-0.77	-0.86	-1.1	0.8



EOG Resources

Midland PVA

Company:	Midland	Local Co-ordinate Reference:	Well #747H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 26' @ 3383.0usft
Site:	Peachtree 25 Fed Com	MD Reference:	KB = 26' @ 3383.0usft
Well:	#747H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Survey										
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
22,029.0	90.01	358.90	13,178.4	9,069.5	592.7	0.81	0.64	-0.49	-0.6	1.5
22,124.0	89.93	357.90	13,178.4	9,164.5	590.0	1.06	-0.08	-1.05	-0.6	3.5
22,218.0	90.77	358.52	13,177.8	9,258.4	587.1	1.11	0.89	0.66	-1.2	5.8
22,313.0	91.39	358.33	13,176.1	9,353.4	584.5	0.68	0.65	-0.20	-3.0	7.7
22,408.0	90.97	359.44	13,174.1	9,448.3	582.7	1.25	-0.44	1.17	-4.9	8.8
22,503.0	90.04	359.23	13,173.3	9,543.3	581.6	1.00	-0.98	-0.22	-5.8	9.2
22,598.0	90.07	358.85	13,173.2	9,638.3	580.0	0.40	0.03	-0.40	-5.8	10.2
22,693.0	90.43	358.73	13,172.8	9,733.3	578.0	0.40	0.38	-0.13	-6.3	11.5
22,787.0	90.15	358.96	13,172.3	9,827.3	576.1	0.39	-0.30	0.24	-6.7	12.7
22,882.0	89.06	359.55	13,172.9	9,922.2	574.8	1.30	-1.15	0.62	-6.1	13.2
22,976.0	89.20	359.43	13,174.4	10,016.2	574.0	0.20	0.15	-0.13	-4.6	13.4
23,071.0	88.11	358.52	13,176.6	10,111.2	572.3	1.49	-1.15	-0.96	-2.4	14.4
23,166.0	89.03	359.00	13,179.0	10,206.1	570.2	1.09	0.97	0.51	0.0	15.8
23,261.0	88.95	358.43	13,180.6	10,301.1	568.1	0.61	-0.08	-0.60	1.6	17.2
23,356.0	89.48	358.00	13,181.9	10,396.0	565.1	0.72	0.56	-0.45	2.9	19.5
23,451.0	89.17	357.69	13,183.1	10,491.0	561.6	0.46	-0.33	-0.33	4.0	22.4
Last MWD Survey (MD=23451.0')										
23,578.0	89.17	357.69	13,184.9	10,617.8	556.5	0.00	0.00	0.00	5.9	26.6
Projection to Bit (MD=23578.0')										



EOG Resources

Midland PVA

Company: Midland
Project: Lea County, NM (NAD 83 NME)
Site: Peachtree 25 Fed Com
Well: #747H
Wellbore: OH
Design: OH

Local Co-ordinate Reference: Well #747H
TVD Reference: KB = 26' @ 3383.0usft
MD Reference: KB = 26' @ 3383.0usft
North Reference: Grid
Survey Calculation Method: Minimum Curvature
Database: PEDM

Design Annotations

Measured Depth (usft)	Vertical Depth (usft)	Local Coordinates		Comment
		+N/-S (usft)	+E/-W (usft)	
12,895.0	12,810.9	97.9	630.6	KOP, MD:12895.0', TVD:12810.9', N/S:97.9', E/W:630.6', INC:26.66
13,029.9	12,926.7	165.8	641.8	LL Crossing, MD:13029.9', TVD:12926.7', N/S:165.8', E/W:641.8', INC:35.30
13,186.5	13,044.6	266.1	663.7	FTP Crossing, MD:13186.5', TVD:13044.6', N/S:266.1', E/W:663.7', INC:47.36
23,451.0	13,183.1	10,491.0	561.6	Last MWD Survey (MD=23451.0')
23,578.0	13,184.9	10,617.8	556.5	Projection to Bit (MD=23578.0')

Checked By: _____ Approved By: _____ Date: _____



Lea County, NM (NAD 83 NME)

Peachtree 25 Fed Com #747H

Plan #2

PROJECT DETAILS: Lea County, NM (NAD 83 NME)

Geodetic System: US State Plane 1983
Datum: North American Datum 1983
Ellipsoid: GRS 1980
Zone: New Mexico Eastern Zone
System Datum: Mean Sea Level


WELL DETAILS: #747H

KB = 26' @ 3383.0usft 3357.0
Northing 372396.00 Easting 791893.00 Latitude 32° 1' 16.392 N Longitude 103° 31' 29.583 W

SECTION DETAILS

Sec	MD	Inc	Azi	TVD	+N/-S	+E/-W	Dleg	TFace	VSect	Target
1	0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.0	
2	1050.0	0.00	0.00	1050.0	0.0	0.0	0.00	0.00	0.0	
3	1339.7	5.79	92.34	1339.2	-0.6	14.6	2.00	92.34	0.2	
4	7598.3	5.79	92.34	7565.8	-26.4	645.9	0.00	0.00	9.0	
5	7888.0	0.00	0.00	7855.0	-27.0	660.5	2.00	180.00	9.2	Brushy Top(PT 25 FC #747H)
6	12373.7	0.00	0.00	12340.7	-27.0	660.5	0.00	0.00	9.2	
7	12840.3	28.00	359.58	12789.0	84.8	659.7	6.00	359.58	120.8	
8	12917.3	28.00	359.58	12857.0	120.9	659.4	0.00	0.00	156.9	
9	13535.6	89.83	359.58	13161.0	625.1	655.7	10.00	0.00	660.1	TGT#1(PT 25 FC #747H)
10	16194.7	89.83	359.58	13169.0	3284.1	636.2	0.00	0.00	3314.0	TGT#2(PT 25 FC #747H)
11	16207.6	89.57	359.58	13169.1	3297.0	636.1	2.00	178.79	3326.9	
12	17530.3	89.57	359.58	13179.0	4619.6	626.5	0.00	0.00	4647.0	
13	17551.8	90.00	359.58	13179.1	4641.1	626.3	2.00	0.00	4668.5	
14	23529.8	90.00	359.58	13179.0	10619.0	583.0	0.00	0.00	10635.0	PBHL(PT 25 FC #747H)

To convert a Magnetic Direction to a Grid Direction, Add 6.04°
To convert a Magnetic Direction to a True Direction, Add 6.47° East
To convert a True Direction to a Grid Direction, Subtract 0.43°

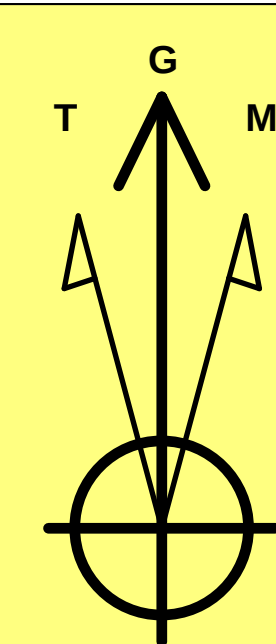

Azimuths to Grid North
True North: -0.43°
Magnetic North: 6.04°







Magnetic Field
Strength: 47345.7nT
Dip Angle: 59.71°
Date: 10/10/2021
Model: IGRF2020

CASING DETAILS

No casing data is available


WELLBORE TARGET DETAILS (MAP CO-ORDINATES)

Name	TVD	+N/-S	+E/-W	Northing	Easting
Brushy Top(PT 25 FC #747H)	7855.0	-27.0	660.5	372369.00	792553.50
FTP(PT 25 FC #747H)	13160.0	266.0	660.0	372662.00	792553.00
TGT#1(PT 25 FC #747H)	13169.0	3284.1	636.2	375680.10	792529.18
PBHL(PT 25 FC #747H)	13179.0	10619.0	583.0	383015.00	792476.00
TGT#2(PT 25 FC #747H)	13179.0	4619.6	626.5	377015.60	792519.50

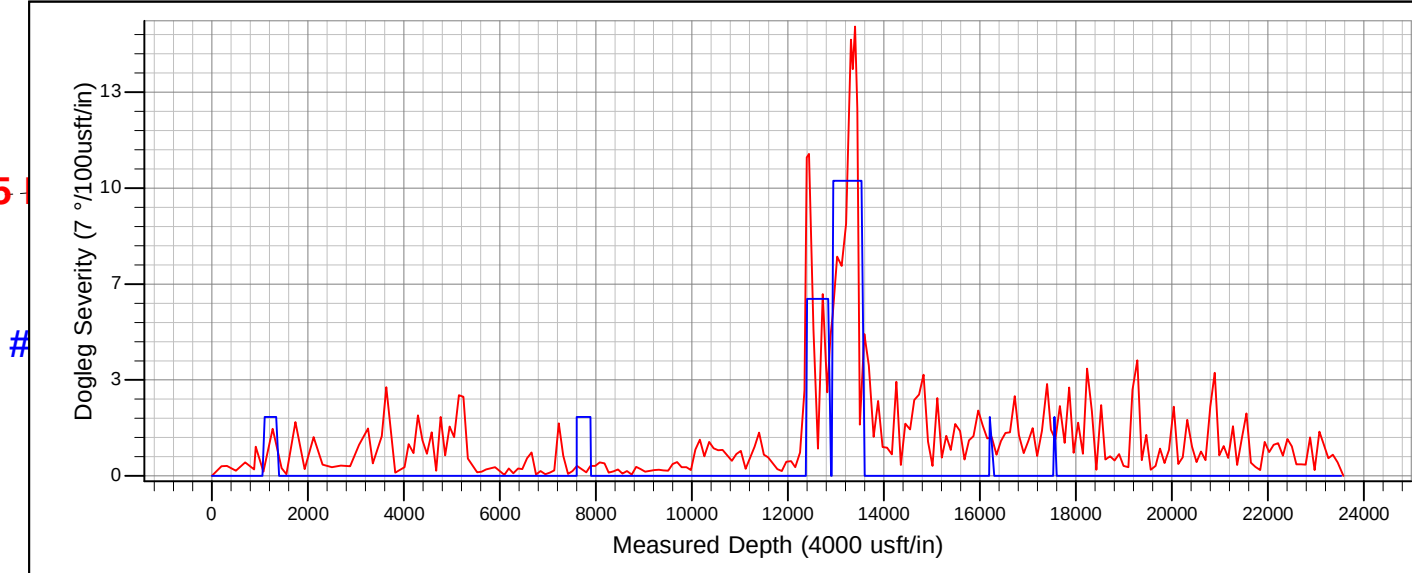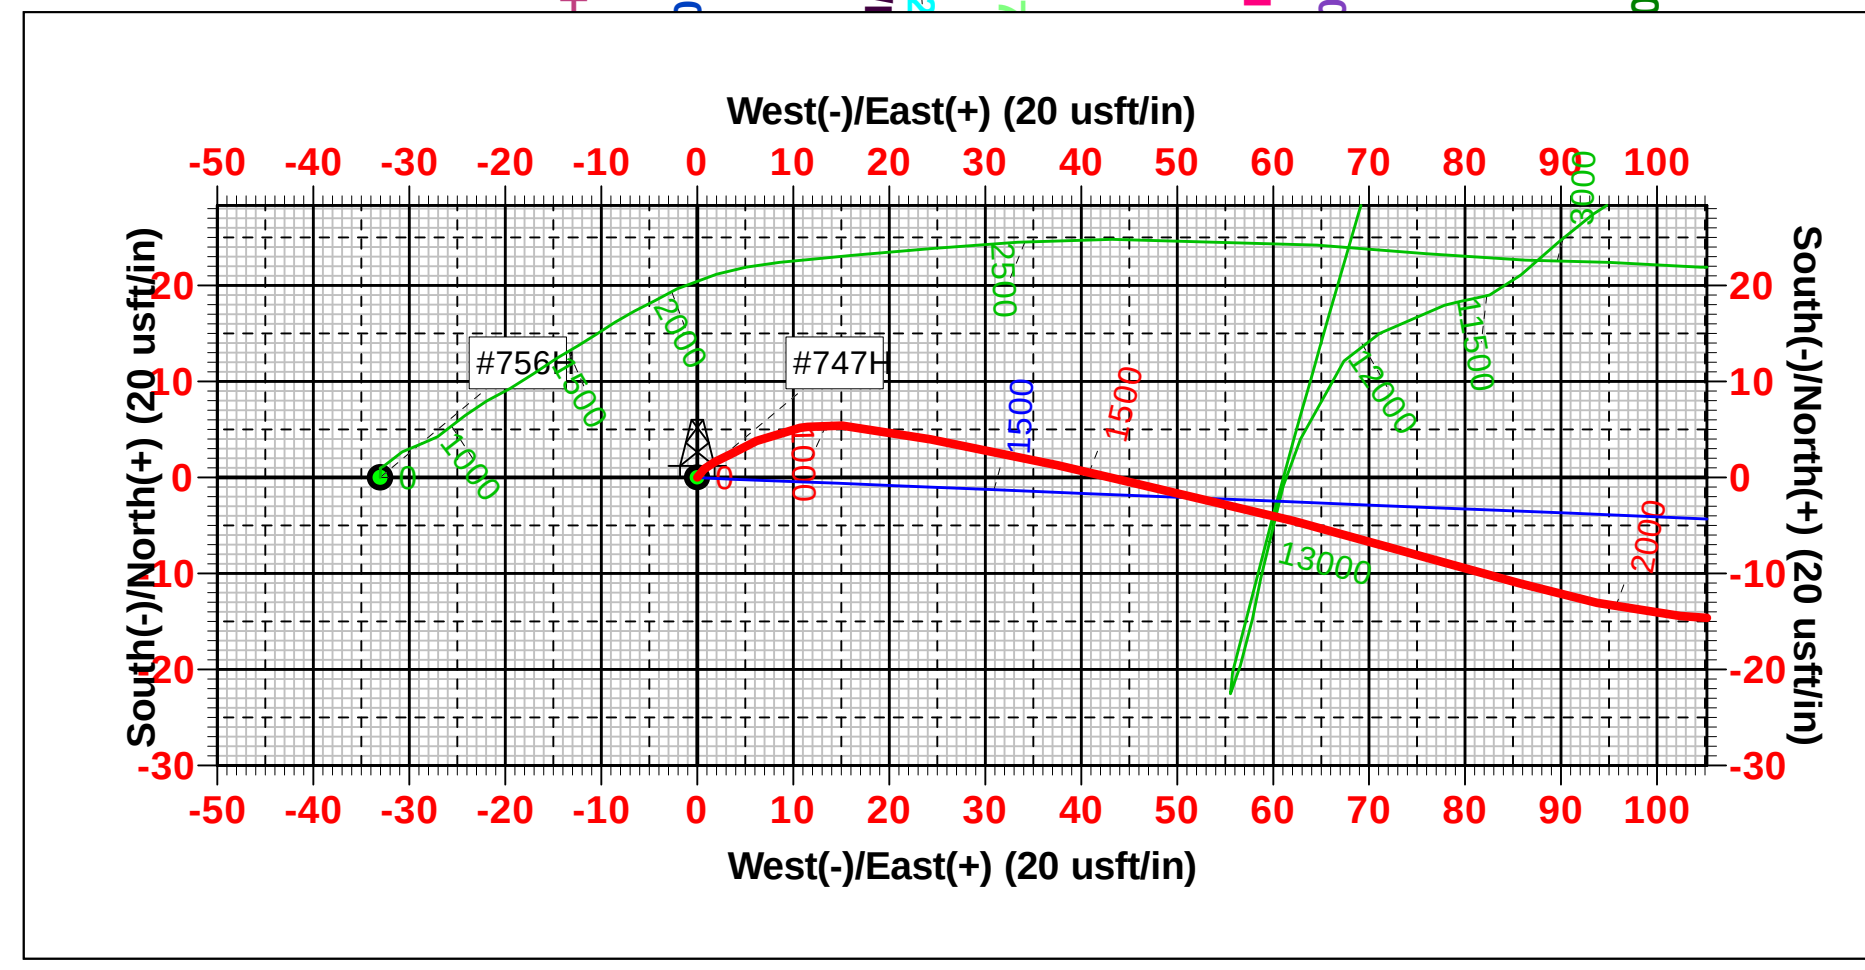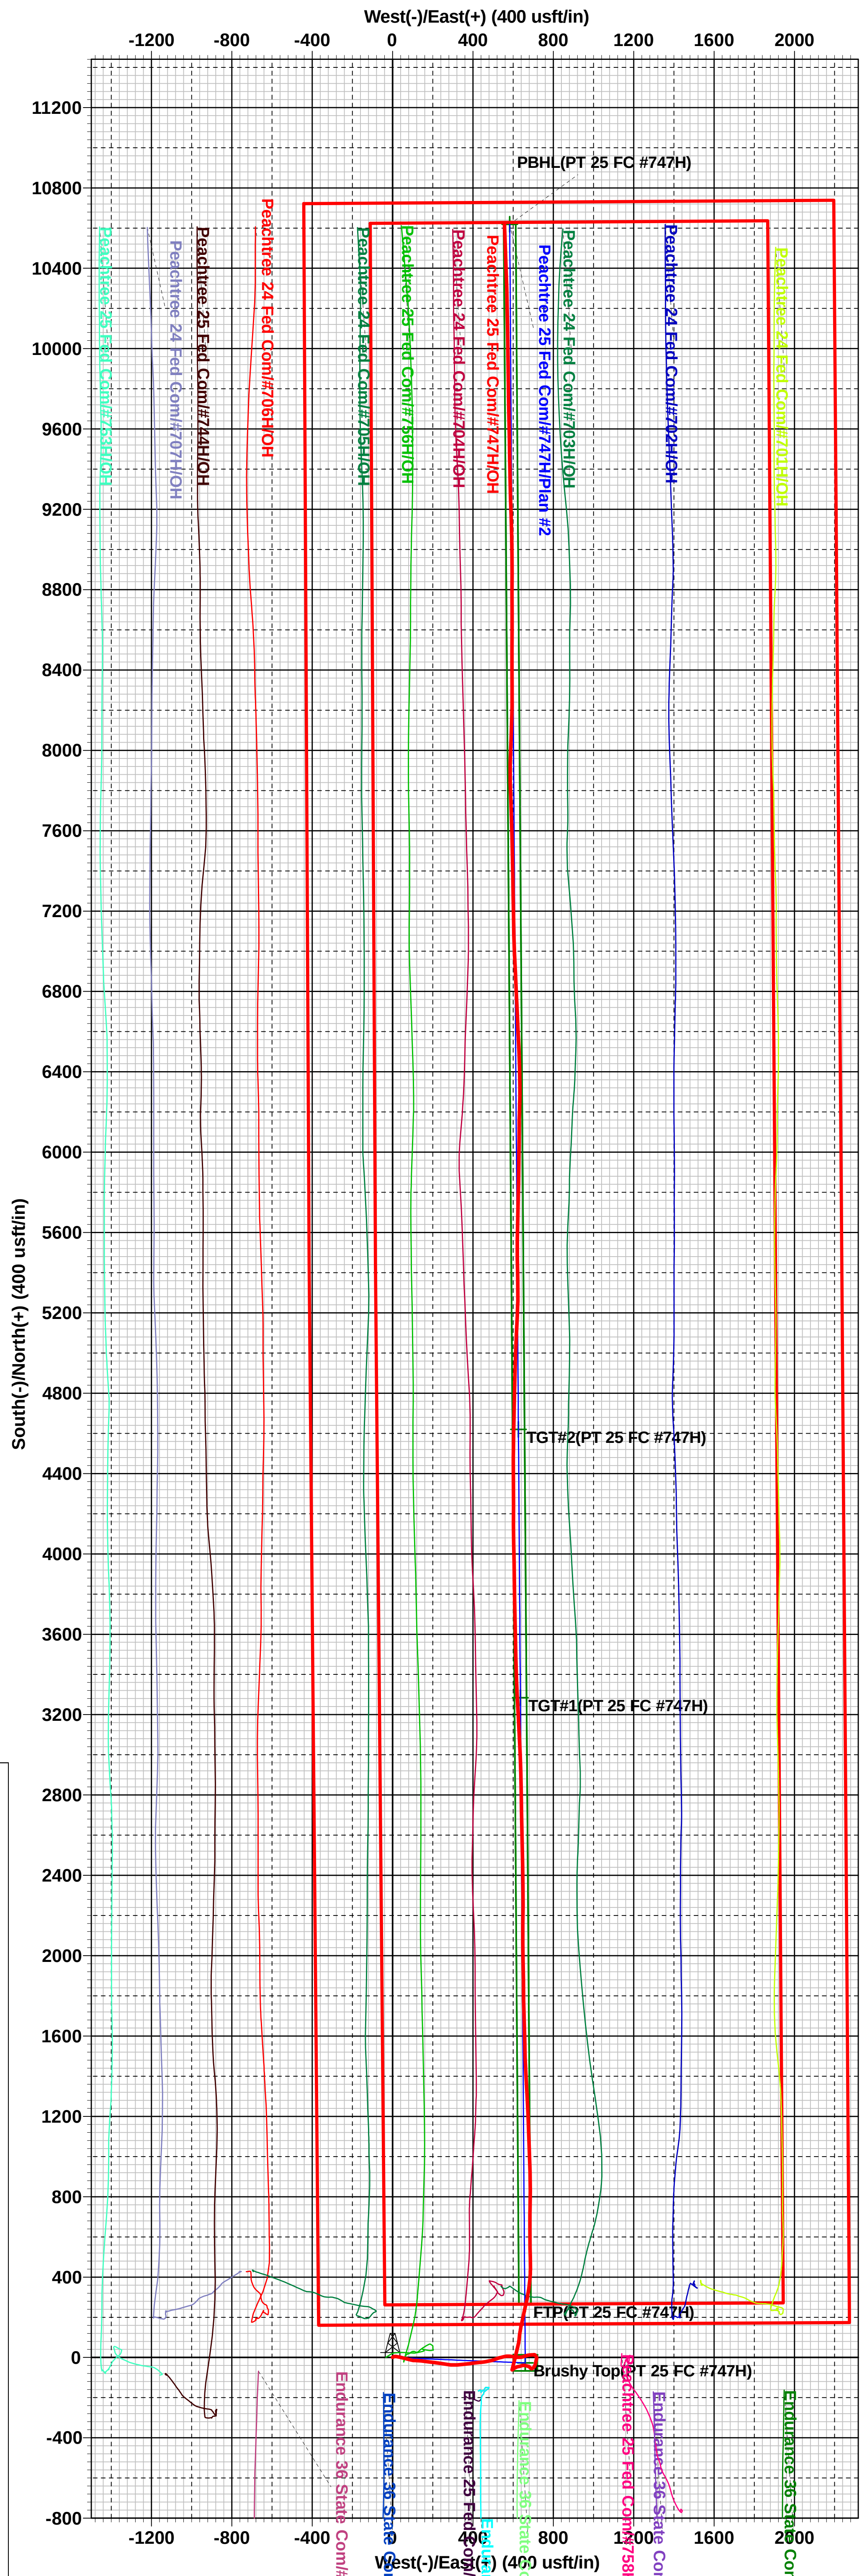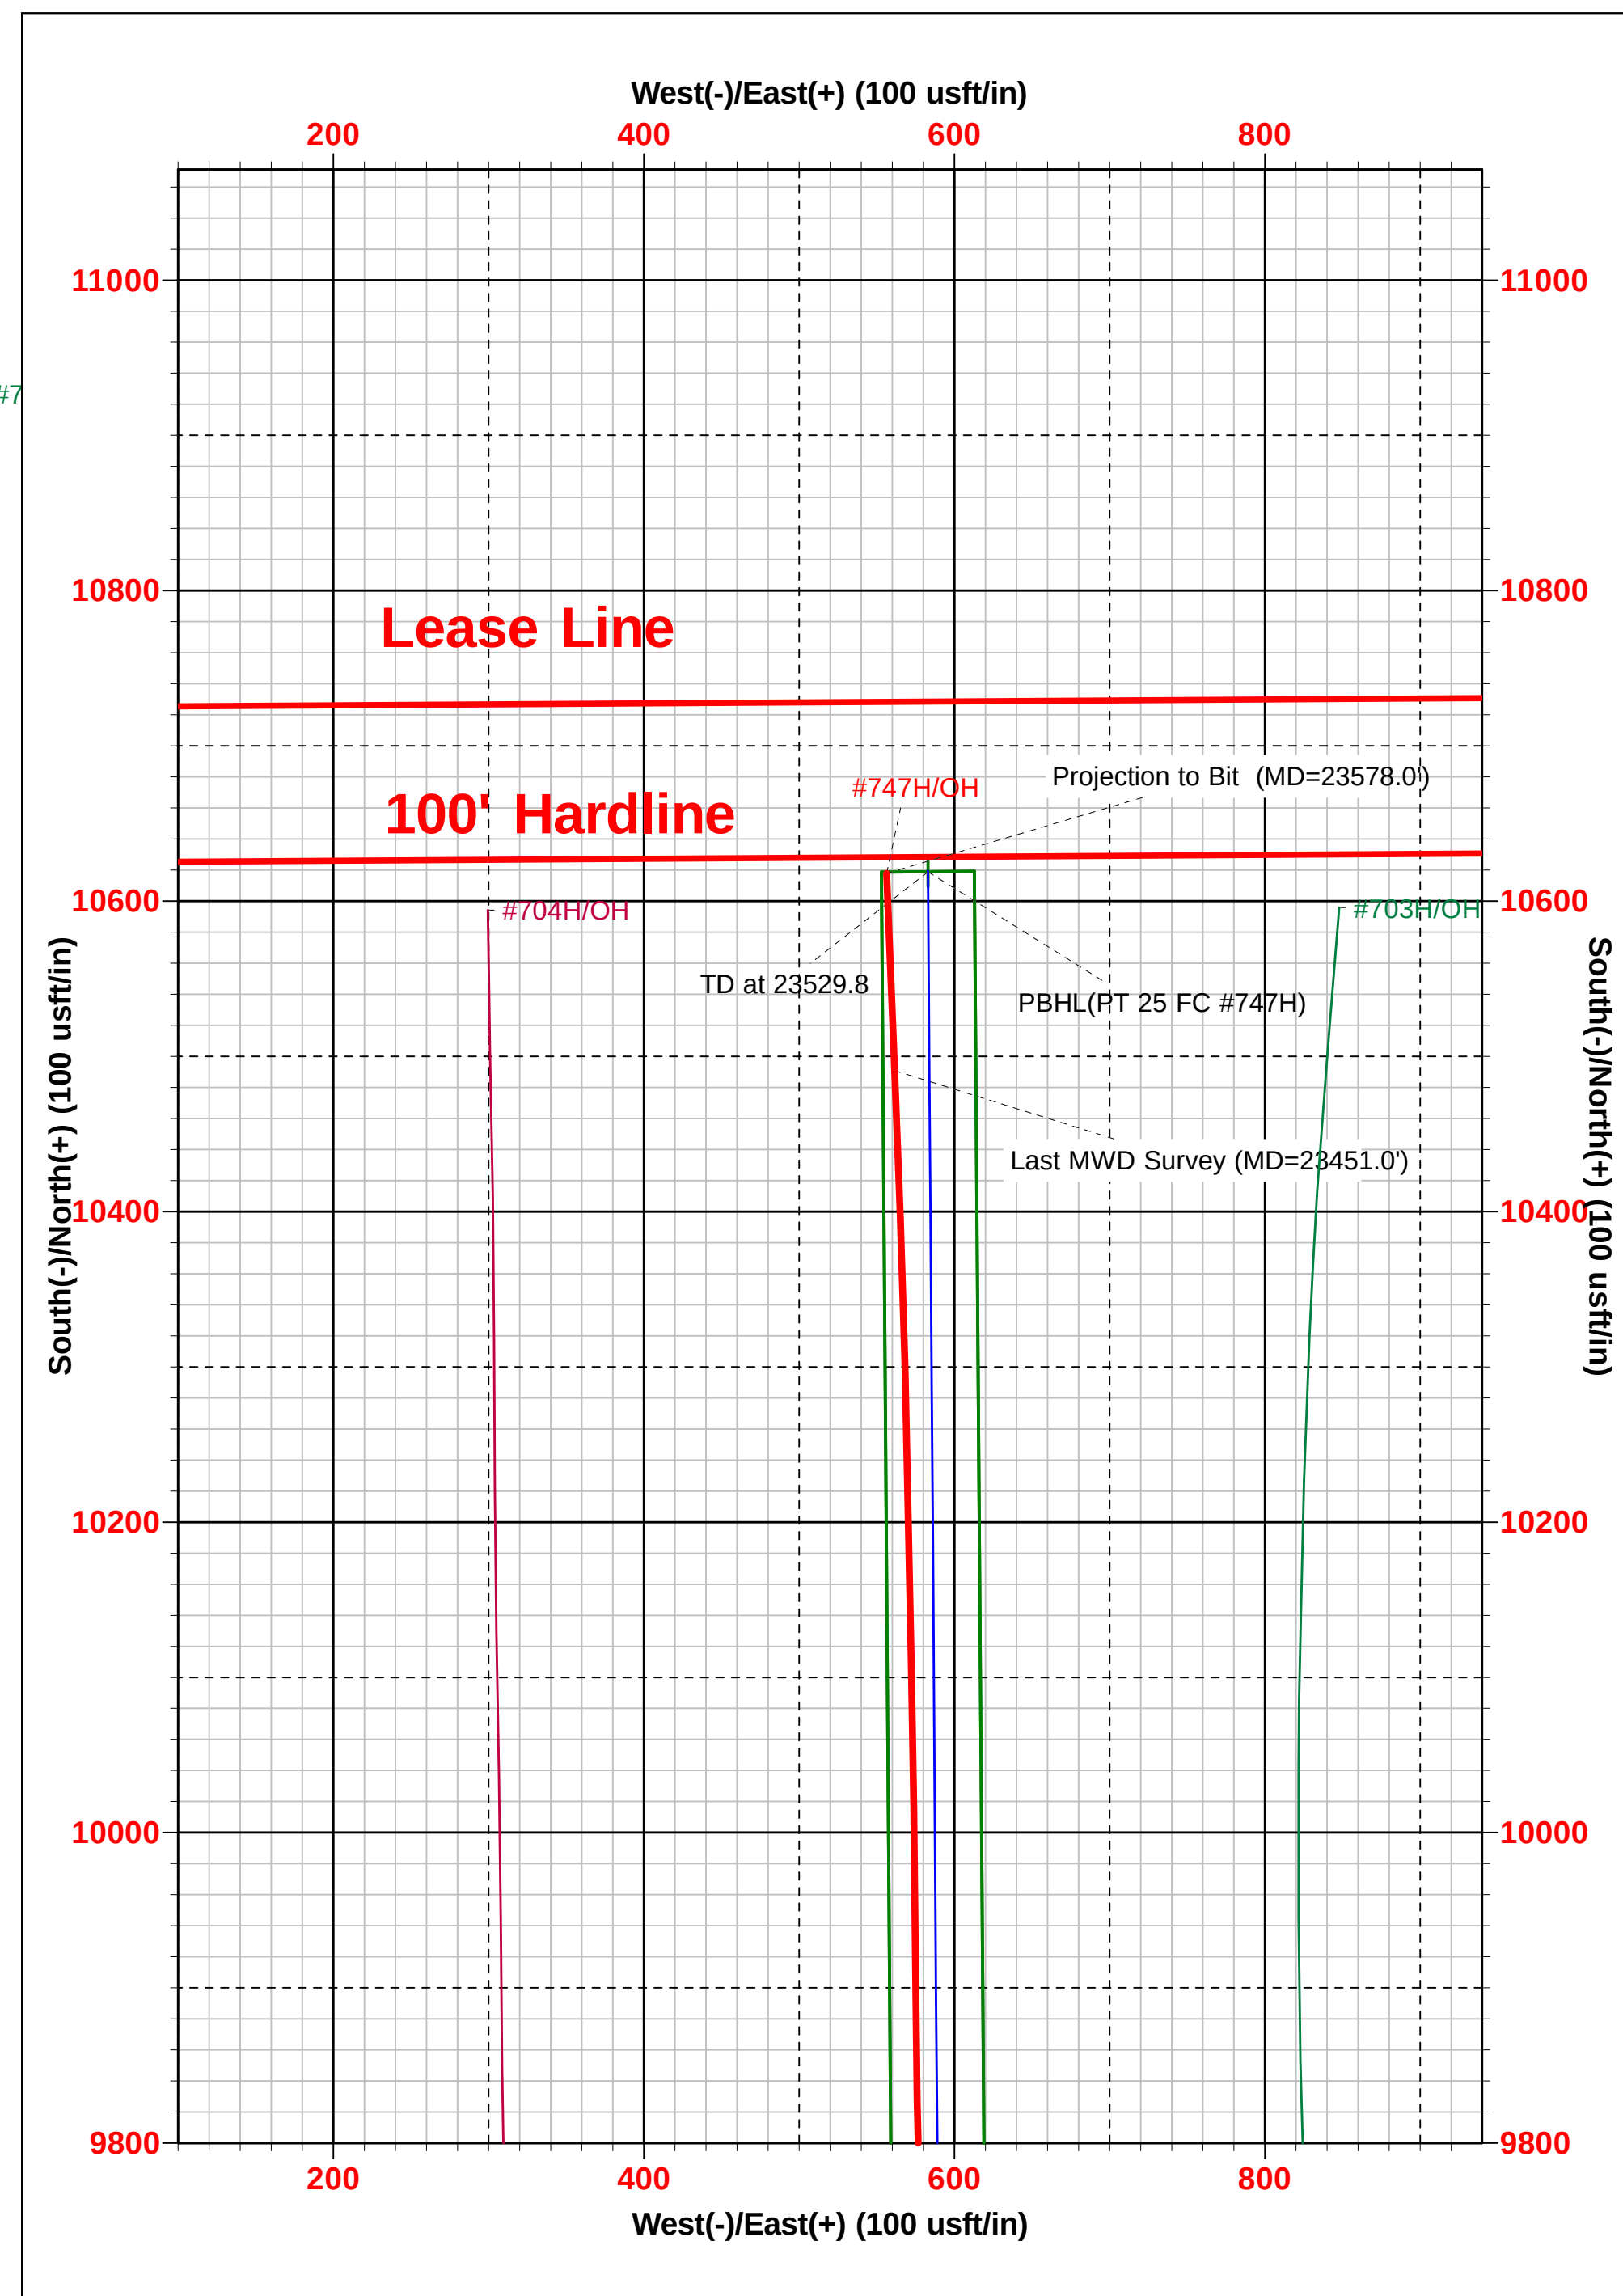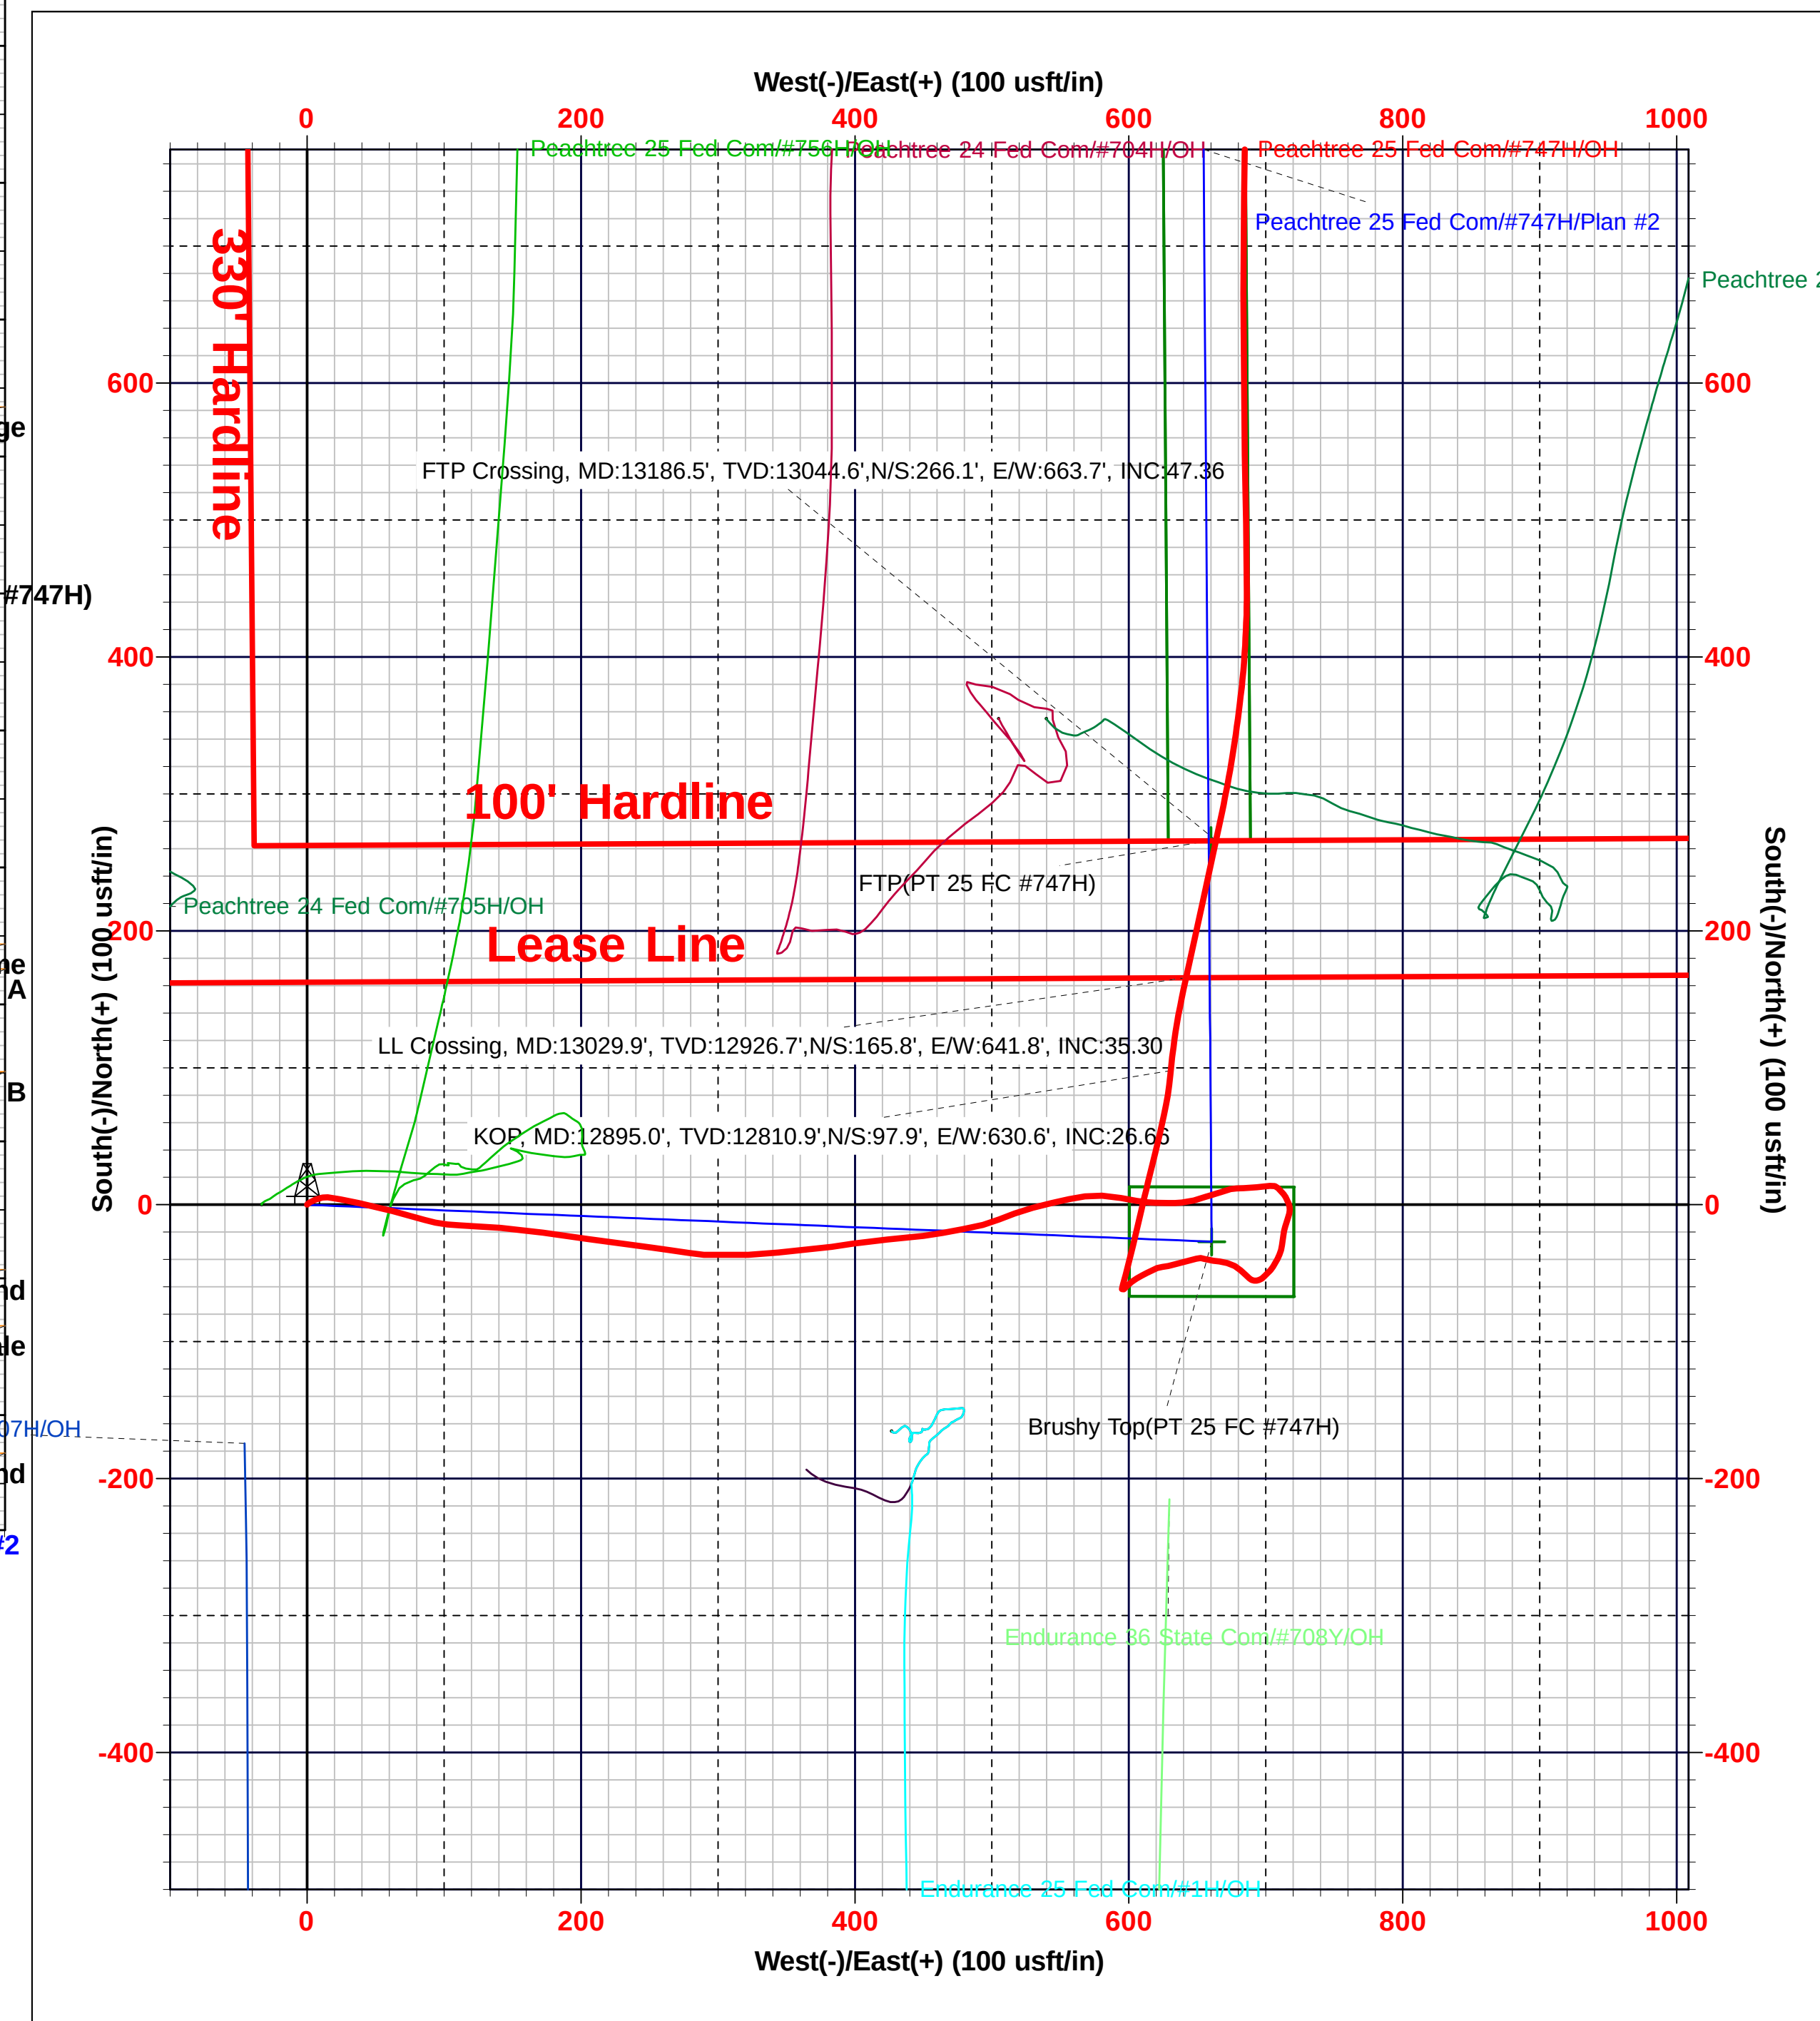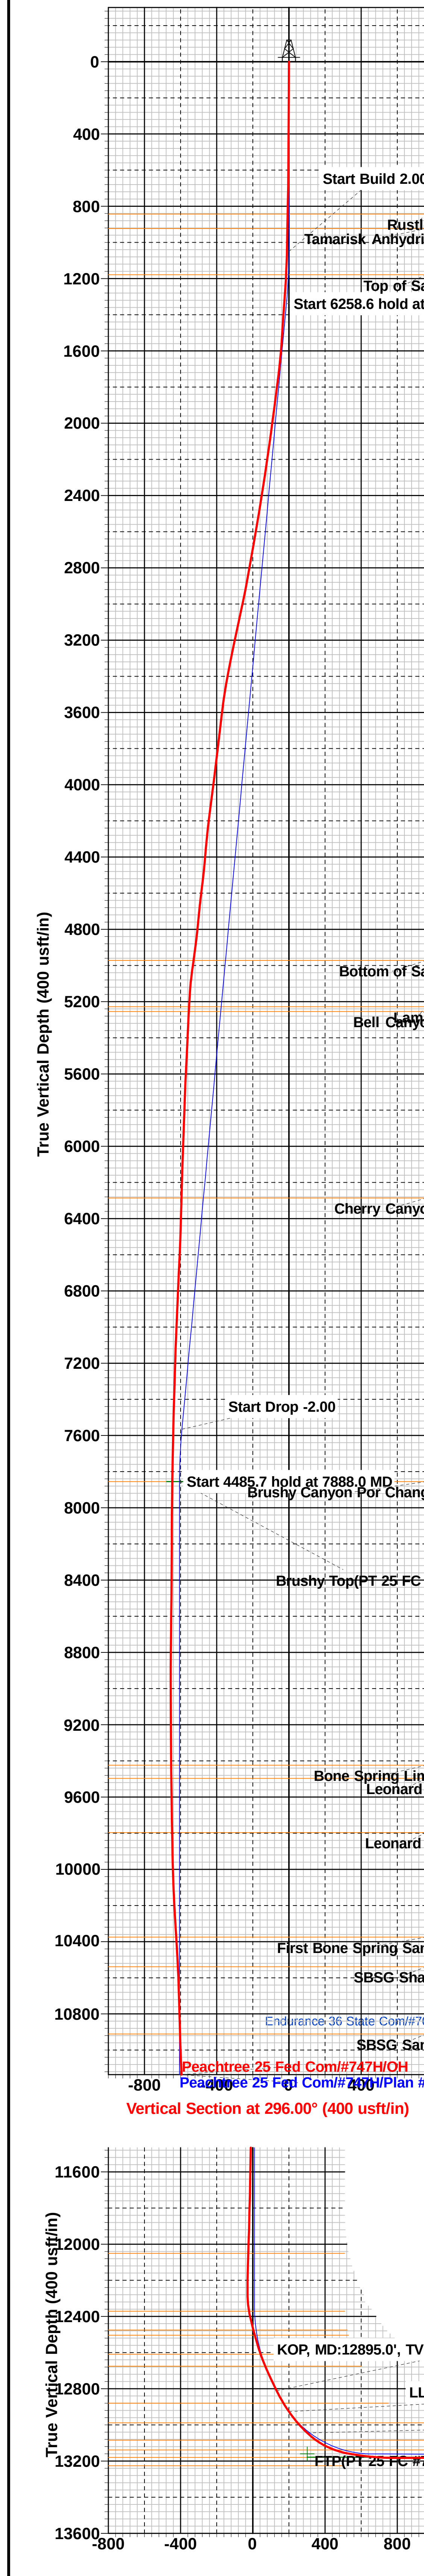

South Formations				North Formations			
Formation/Zone	MD	TVD	W/O/G	Formation/Zone	MD	TVD	W/O/G
T. Anhy RUSTLER	843'			T. San Jose			
T. Salt	1179'			T. Nacimiento			
B. Salt	4,972'			T. Ojo Alamo			
T. Yates				T. Kirtland			
T. 7 Rivers				T. Fruitland			
T. Queen				T. Pictured Cliffs			
T. Grayburg				T. Lewis Shale			
T. San Andres				T. Chacra			
T. Glorieta				T. Cliff House			
T. Yeso				T. Menefee			
T. Paddock				T. Point Lookout			
T. Blinebry				T. Mancos			
T.Tubb				T. Gallup			
T. Drinkard				T. Greenhorn			
T. Abo				T. Graneros			
T. Wolfcamp	12,475'	12,417'		T. Dakota			
T. Penn				T. Morrison			
T. Cisco				T. Bluff			
T. Canyon				T.Todilto			
T. Strawn				T. Entrada			
T. Atoka				T. Wingate			
T. Morrow				T. Chinle			
T. Barnett Shale				T. Permian			
T. Miss				T. Penn A"			
T. Woodford Shale				T. Penn. "B"			
T. Devonian				T. Penn. "C"			
T. Silurian				T. Penn. "D"			
T. Fusselman				T. Leadville			
T. Montoya				T. Madison			
T. Simpson				T. Elbert			
T. McKee				T. McCracken			
T. Waddell				T. Ignacio Otzte			
T. Connel				T. Granite			
T. Ellenburger				T. Hermosa			
T. Gr. Wash				T. De Chelly			
T. Delaware Sand				T. Pinkerton			
T. Lamar Lime							
T. Bell Canyon							
T. Cherry Canyon							
T. Brushy Canyon	7,855'						
T. Bone Springs							
T. 1st BS Sand	10,375'	10,267'					
T. 2nd BS Carbonate							
T. 2nd BS Sand	10,911'	10,867'					
T. 3rd BS Carbonate							
T. 3rd BS Sand							

Well Name				Rig Name	API #	County	State	Rig Release
PEACHTREE 25 FED.COM #747H				PIONEER 77	30025493700000	LEA	NEW MEXICO	2021-11-20T00:00:00
Top Perf	Bottom Perf	Sec.	Blk	Range/Survey	Latitude	Longitude	Conductor Date	
13287	23561	25	26S	33E	32.021094	-103.5244212	2021-09-15T00:00:00	
GL (ft)	KB (ft)	CTOP (ft)	MD (ft)		TVD (ft)	KOP (ft)	Spud Date	
3357	3383	5928	23578		13185.22	12895	2021-10-08T00:00:00	

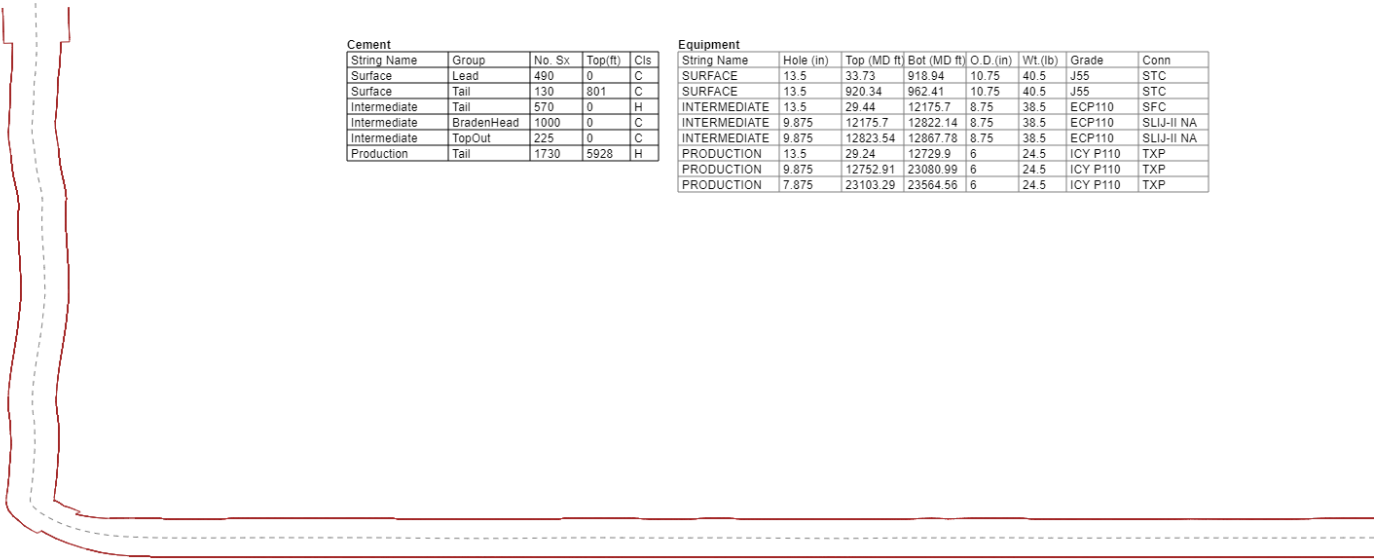

Well Name: PEACHTREE 25 FED COM	Well Location: T26S / R33E / SEC 25 / NWNE / 32.0212192 / -103.5248852	County or Parish/State: LEA / NM
Well Number: 747H	Type of Well: OIL WELL	Allottee or Tribe Name:
Lease Number: NMNM122622	Unit or CA Name:	Unit or CA Number:
US Well Number: 3002549370	Well Status: Producing Oil Well	Operator: EOG RESOURCES INCORPORATED

Notification

Sundry ID:	2658525	Type of Action:	First Production
Type of Submission:	Notification	Time Sundry Submitted:	3:02:00 PM
Date Sundry Submitted:	Feb 23, 2022		
First Production Date:	Jan 24, 2022		
US Well Number:	3002549370		
First Production Remarks:	11/20/2021 RIG RELEASED 11/23/2021 MIRU TEST VOID TO 5000 PSI, SEALS AND FLANGES TO 8500 PSI 12/23/2021 BEGIN PERF AND FRAC 01/04/2022 FINISH 37 STAGES PERF & FRAC, 13,287-23,561' W/ 3 1/8" 2775 SHOTS, FRAC 25,146,502 LBS PROPPANT + 469,739 BBLS LOAD FLUID 1/6/2022 DRILLED OUT PLUGS AND CLEAN OUT WELLBORE 1/24/2022 OPENED WELL TO FLOWBACK – DATE OF FIRST PRODUCTION		
Disposition:	Accepted		
Accepted Date:	02/28/2022		

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
<https://www.emnrd.nm.gov/ocd/contact-us>

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

ACKNOWLEDGMENTS

Action 514019

ACKNOWLEDGMENTS

Operator: EOG RESOURCES INC 5509 Champions Drive Midland, TX 79706	OGRID: 7377
	Action Number: 514019
	Action Type: [C-104] Completion Packet - New Well (C-104NW)

ACKNOWLEDGMENTS

☒	I hereby certify that the required Water Use Report has been, or will be, submitted for this wells completion.
☒	I hereby certify that the required FracFocus disclosure has been, or will be, submitted for this wells completion.
☒	I hereby certify that the rules of the Oil Conservation Division have been complied with and that the information given above is true and complete to the best of my knowledge and belief.

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
<https://www.emnrd.nm.gov/oed/contact-us>

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 514019

CONDITIONS

Operator: EOG RESOURCES INC 5509 Champions Drive Midland, TX 79706	OGRID: 7377
	Action Number: 514019
	Action Type: [C-104] Completion Packet - New Well (C-104NW)

CONDITIONS

Created By	Condition	Condition Date
plmartinez	None	10/10/2025
