I hereby certify that the information above is true and complete to the best of my knowledge and belief.

SIGNATURE

TITLE BUS. SVC. Spec. II

DATE

11-14-2001

Type or print name

Roy L. Wheeler, Jr.

Telephone No. 915 758-6778


APPROVED BY


TITLE

DISTRICT SUPERVISOR

DATE 1/30/0/

Conditions of approval, if any

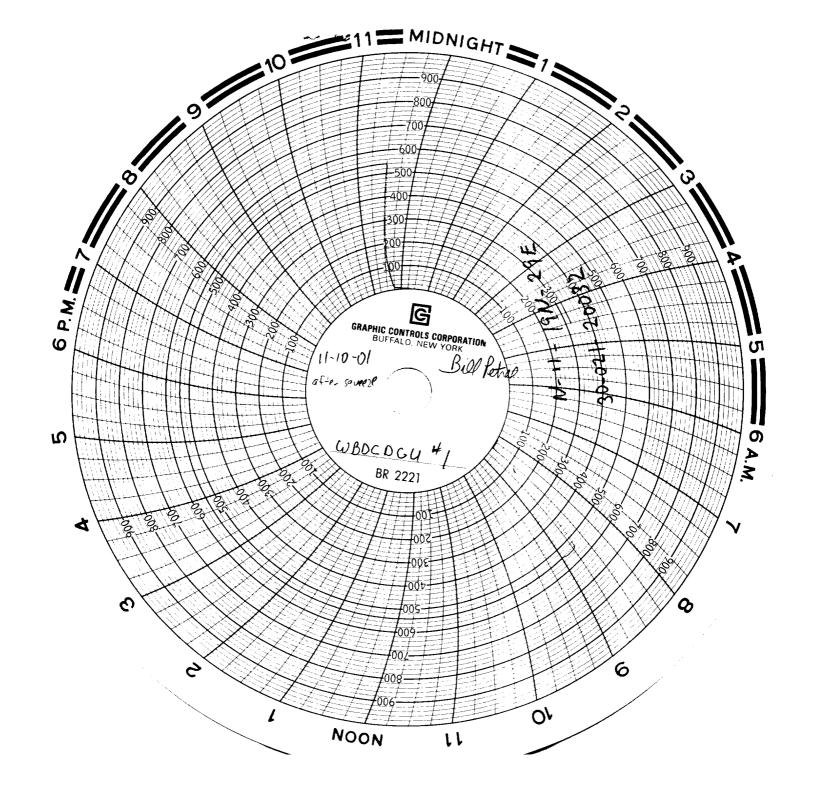



## State of New Mexico

Form C-103

Submit 3 copies to Appropriate District Office	pmit 3 copies Appropriate Energy, Minerals and Natural Resources Department		
DISTRICT I	OIL CONSERV	ATION DIVISION	WELL API NO.
P.O. Box 1980, Hobbs, NM 88241			30-021-20032
DISTRICT II		Pacheco St.	
P.O. Box Drawer DD, Artesia, NM 8	38210 Santa	Fe, NM 87505	5. Indicate Type of Lease STATE ✓ FEE ☐
DISTRICT III			6. State Oil / Gas Lease No.
1000 Rio Brazos Rd., Aztec, NM 87	410		L-5852
SUNDRY NOTICES AND REPORTS ON WELLS  (DO NOT USE THIS FORM FOR PROPOSALS TO DRILL OR TO DEEPEN OR PLUG BACK TO A  DIFFERENT RESERVOIR. USE "APPLICATION FOR PERMIT"  (FORM C-101) FOR SUCH PROPOSALS.)			
			7. Lease Name or Unit Agreement Name
			West Bravo Dome CDG Unit
1. Type of Well OIL GAS COS Supply Well			]
WELL WELL OTHER CO2 Supply Well.			
2. Name of Operator			8. Well No.
Amerada Hess Corporation			
3. Address of Operator P.O. Box 840, Seminole, TX 79360			9. Pool Name or Wildcat West Bravo Dome
4. Well Location			
Unit Letter N : 660 Feet From The South Line and 1980 Feet From The West Line			
Section 11 Township 19N Range 29E NMPM Harding COUNTY			
10. Elevation (Show whether DF, RKB, RT,GR, etc.) 4566' GR			
Check Appropriate Box to Indicate Nature of Notice, Report, or Other Data			
	• • •		BSEQUENT REPORT OF:
NOTICE OF INT			
PERFORM REMEDIAL WORK	PLUG AND ABANDON	REMEDIAL WORK	ALTERING CASING  RATIONS PLUG AND ABANDONMENT
TEMPORARILY ABANDON	CHANGE PLANS	COMMENCE DRILLING OPE	
PULL OR ALTER CASING		CASING TEST AND CEMEN	
OTHER:		UOTHER:	
12. Describe Proposed or Completed Operations (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work) SEE RULE 1103.			
Plan to MIRU pulling unit. Remove wellhead, install BOP & TOH w/tbg. & pkr. TIH w/CIBP & press. test csg. to 500 PSI for 30 min., obtaining chart. TA well. If csg. does not hold, TIH w/pkr. testing at intervals to determine leak interval. Cement squeeze, press. test csg. to 500 PSI for 30 min. obtaining chart & TA well.			
	stibe and complete to the best of my knowledge and	1 hollef	
		Bus. Svc. Spec. II	DATE 11/01/2001
SIGNATURE	many mile		
	Dov I Whooler Ir		TELEPHONE NO. 015-758-6778

TITLE DISTRICT SUPERVISOR

DATE 11/6/2001

APPROVED BY\_
