

DISTRICT I
1625 N. FRENCH DR., HOBBES, NM 86240
Phone: (575) 393-6161 Fax: (575) 393-0720

DISTRICT II
811 S. FIRST ST., ARTESIA, NM 88210
Phone: (575) 748-1283 Fax: (575) 748-8720

DISTRICT III
1000 RIO BRAZOS RD., AZTEC, NM 87410
Phone: (505) 334-6178 Fax: (505) 334-6170

DISTRICT IV
1220 S. ST. FRANCIS DR., SANTA FE, NM 87505
Phone: (505) 476-3460 Fax: (505) 476-3462

State of New Mexico
Energy, Minerals & Natural Resources Department
OIL CONSERVATION DIVISION
1220 SOUTH ST. FRANCIS DR.
Santa Fe, New Mexico 87505

Form C-102
Revised August 1, 2011
Submit one copy to appropriate
District Office

☒ AMENDED REPORT
AS-DRILLED

WELL LOCATION AND ACREAGE DEDICATION PLAT

API Number 30-015-45910	Pool Code 53805	Pool Name SAND DUNES; BONE SPRING, SOUTH
Property Code 325417	Property Name TODD 36-25 STATE FED COM	Well Number 235H
OGRID No. 6137	Operator Name DEVON ENERGY PRODUCTION COMPANY, L.P.	Elevation 3508.8'


Surface Location

UL or lot No.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
0	36	23-S	31-E		330	SOUTH	1636	EAST	EDDY

Bottom Hole Location If Different From Surface

UL or lot No.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
A	25	23-S	31-E		115	NORTH	403	EAST	EDDY
Dedicated Acres 640	Joint or Infill	Consolidation Code	Order No.						

NO ALLOWABLE WILL BE ASSIGNED TO THIS COMPLETION UNTIL ALL INTERESTS HAVE BEEN CONSOLIDATED
OR A NON-STANDARD UNIT HAS BEEN APPROVED BY THE DIVISION

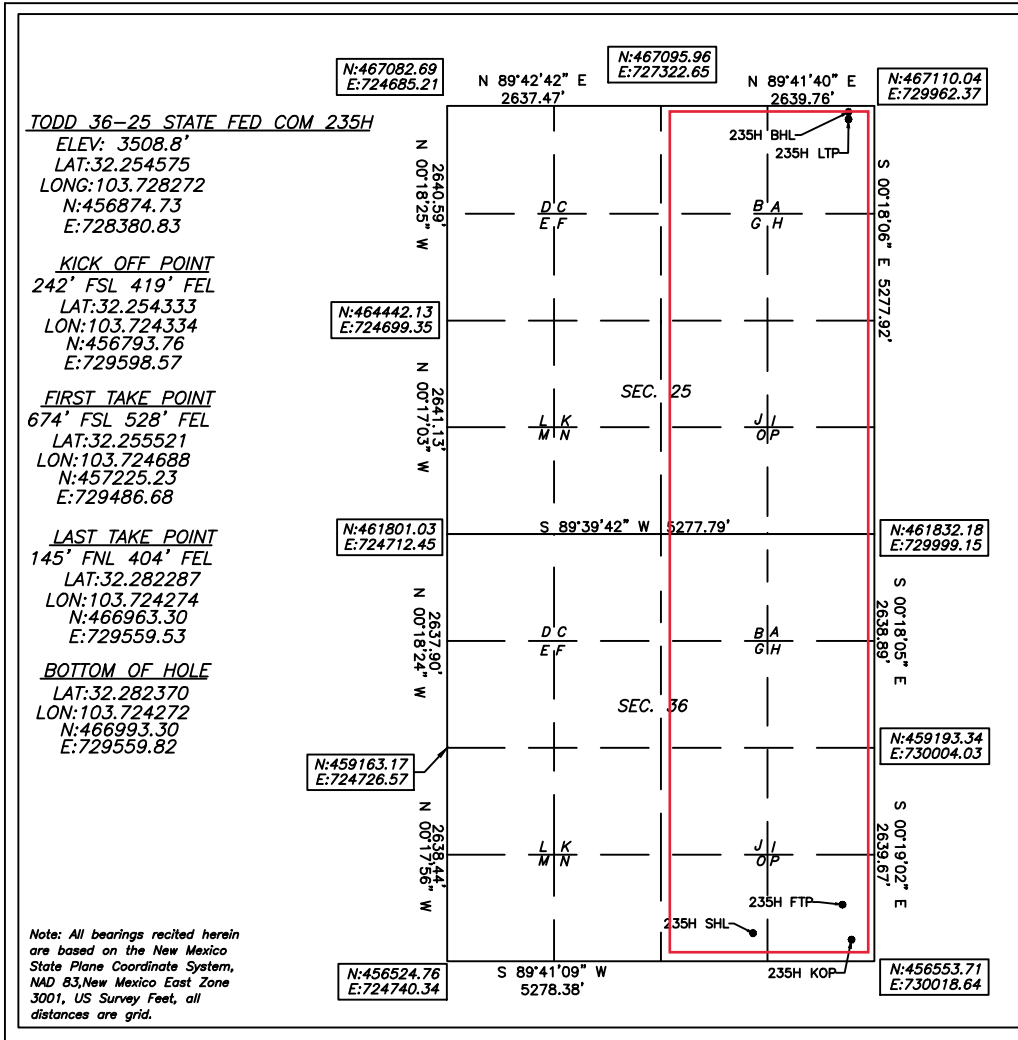

OPERATOR CERTIFICATION

I hereby certify that the information herein is true and complete to the best of my knowledge and belief, and that this organization either owns a working interest or unleased mineral interest in the land including the proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of such mineral or working interest, or to a voluntary pooling agreement or a compulsory pooling order heretofore entered by the division.

Jenny Harms 5-18-2020
Signature Date

JENNY HARMS

Printed Name

JENNY.HARMS@DVN.COM

E-mail Address


SURVEYOR CERTIFICATION

I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief.

9/2019

Date of Survey

Signature & Seal of Professional Surveyor



04/29/20

Certificate No. 22404

B.L. LAMAN

DRAWN BY: CM

Intent ☐ As Drilled ☐

API #		
Operator Name:	Property Name:	Well Number

Kick Off Point (KOP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

First Take Point (FTP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

Last Take Point (LTP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

Is this well the defining well for the Horizontal Spacing Unit? ☐

Is this well an infill well? ☐

If infill is yes please provide API if available, Operator Name and well number for Defining well for Horizontal Spacing Unit.

API #		
Operator Name:	Property Name:	Well Number

Devon

SURVEY REPORT

Todd 36-25 Fed Com 235H

HP 466

I, Deanna Jacobs, certify the surveys supplied on
Todd 36-25 State Com 235H are correct and accurate to the best of my
knowledge and are supported by actual field data.

Deanna Jacobs

Date: 4/28/2020

Devon Energy

Eddy County, NM (NAD83 NME)

Todd 36-25 State Fed Com

235H

ST1

Survey: SDI ST1 Surveys

Standard Survey Report

26 August, 2019



Scientific Drilling, Intl

Survey Report

Company:	Devon Energy	Local Co-ordinate Reference:	Well 235H
Project:	Eddy County, NM (NAD83 NME)	TVD Reference:	KB = 23' @ 3532.00usft (H&P 466)
Site:	Todd 36-25 State Fed Com	MD Reference:	KB = 23' @ 3532.00usft (H&P 466)
Well:	235H	North Reference:	Grid
Wellbore:	ST1	Survey Calculation Method:	Minimum Curvature
Design:	ST1	Database:	Midland District

Project	Eddy County, NM (NAD83 NME)		
Map System:	US State Plane 1983	System Datum:	Mean Sea Level
Geo Datum:	North American Datum 1983		
Map Zone:	New Mexico Eastern Zone		Using geodetic scale factor

Site		Todd 36-25 State Fed Com			
Site Position:		Northing:	456,874.40 usft	Latitude:	32° 15' 16.470 N
From:	Map	Easting:	728,320.84 usft	Longitude:	103° 43' 42.476 W
Position Uncertainty:	0.00 usft	Slot Radius:	13-3/16 "	Grid Convergence:	0.32 °

Well	235H					
Well Position	+N/-S	0.00 usft	Northing:	456,874.74 usft	Latitude:	32° 15' 16.470 N
	+E/-W	0.00 usft	Easting:	728,380.84 usft	Longitude:	103° 43' 41.778 W
Position Uncertainty		0.00 usft	Wellhead Elevation:	0.00 usft	Ground Level:	3,509.00 usft

Wellbore	ST1				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	HDGM	8/6/2019	6.73	59.93	47,914

Design	ST1				
Audit Notes:					
Version:	1.0	Phase:	ACTUAL	Tie On Depth:	6,242.00
Vertical Section:	Depth From (TVD) (usft)	+N/-S (usft)	+E/-W (usft)	Direction (bearing)	
	0.00	0.00	0.00	6.66	

Survey Program	Date	8/26/2019			
From (usft)	To (usft)	Survey (Wellbore)	Tool Name	Description	
243.00	5,961.00	SDI Survey #1 (OH)	MWD+HDGM	OWSG MWD + HDGM	
6,096.00	6,242.00	SDI Survey #2 (OH)	MWD+HDGM	OWSG MWD + HDGM	
6,338.00	20,690.00	SDI ST1 Surveys (ST1)	MWD+HDGM	OWSG MWD + HDGM	

Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (bearing)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
6,242.00	14.70	89.19	6,159.80	-48.08	814.61	46.72	0.00	0.00	0.00	
6,338.00	21.58	97.35	6,250.99	-50.17	844.34	48.09	7.62	7.17	8.50	
6,433.00	23.01	98.33	6,338.89	-55.10	880.04	47.34	1.56	1.51	1.03	
6,529.00	24.31	98.18	6,426.81	-60.63	918.17	46.27	1.36	1.35	-0.16	
6,550.00	24.71	97.98	6,445.92	-61.85	926.79	46.05	1.95	1.90	-0.95	
6,645.00	24.40	98.09	6,532.33	-67.37	965.88	45.10	0.33	-0.33	0.12	
6,741.00	23.62	97.70	6,620.02	-72.74	1,004.57	44.26	0.83	-0.81	-0.41	
6,837.00	21.11	98.20	6,708.79	-77.78	1,040.75	43.45	2.62	-2.61	0.52	
6,932.00	19.32	99.45	6,797.94	-82.80	1,073.19	42.22	1.94	-1.88	1.32	

Scientific Drilling, Intl

Survey Report

Company:	Devon Energy	Local Co-ordinate Reference:	Well 235H
Project:	Eddy County, NM (NAD83 NME)	TVD Reference:	KB = 23' @ 3532.00usft (H&P 466)
Site:	Todd 36-25 State Fed Com	MD Reference:	KB = 23' @ 3532.00usft (H&P 466)
Well:	235H	North Reference:	Grid
Wellbore:	ST1	Survey Calculation Method:	Minimum Curvature
Design:	ST1	Database:	Midland District

Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (bearing)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
7,028.00	17.19	101.67	6,889.10	-88.28	1,102.75	40.21	2.33	-2.22	2.31
7,123.00	17.36	101.82	6,979.82	-94.02	1,130.37	37.71	0.18	0.18	0.16
7,218.00	17.45	102.47	7,070.47	-100.00	1,158.15	34.99	0.23	0.09	0.68
7,314.00	14.98	100.71	7,162.64	-105.42	1,184.40	32.66	2.62	-2.57	-1.83
7,409.00	12.38	98.65	7,254.94	-109.23	1,206.53	31.44	2.78	-2.74	-2.17
7,504.00	10.22	97.57	7,348.09	-111.87	1,224.96	30.95	2.28	-2.27	-1.14
7,600.00	7.94	93.99	7,442.89	-113.46	1,240.02	31.12	2.45	-2.38	-3.73
7,695.00	5.64	97.28	7,537.21	-114.50	1,251.20	31.38	2.45	-2.42	3.46
7,790.00	4.22	101.04	7,631.86	-115.76	1,259.26	31.06	1.53	-1.49	3.96
7,886.00	2.54	99.20	7,727.69	-116.78	1,264.82	30.70	1.75	-1.75	-1.92
7,981.00	1.08	85.77	7,822.64	-117.05	1,267.80	30.77	1.59	-1.54	-14.14
8,076.00	0.93	4.54	7,917.63	-116.22	1,268.75	31.71	1.38	-0.16	-85.51
8,171.00	1.18	357.18	8,012.61	-114.47	1,268.76	33.45	0.30	0.26	-7.75
8,267.00	1.99	352.03	8,108.58	-111.83	1,268.48	36.04	0.86	0.84	-5.36
8,361.00	3.36	358.66	8,202.47	-107.46	1,268.19	40.34	1.49	1.46	7.05
8,456.00	2.45	0.00	8,297.35	-102.65	1,268.13	45.12	0.96	-0.96	1.41
8,551.00	2.07	351.46	8,392.27	-98.92	1,267.87	48.79	0.53	-0.40	-8.99
8,647.00	2.01	339.68	8,488.21	-95.63	1,267.03	51.96	0.44	-0.06	-12.27
8,742.00	2.03	331.98	8,583.15	-92.58	1,265.66	54.83	0.29	0.02	-8.11
8,837.00	2.03	327.42	8,678.10	-89.68	1,263.96	57.52	0.17	0.00	-4.80
8,933.00	1.83	324.26	8,774.04	-87.00	1,262.15	59.97	0.24	-0.21	-3.29
8,964.00	1.76	324.19	8,805.03	-86.21	1,261.59	60.68	0.23	-0.23	-0.23
9,011.00	1.49	320.52	8,852.01	-85.16	1,260.78	61.64	0.62	-0.57	-7.81
9,107.00	1.71	296.29	8,947.97	-83.56	1,258.70	62.99	0.73	0.23	-25.24
9,202.00	2.48	288.22	9,042.91	-82.29	1,255.47	63.87	0.87	0.81	-8.49
9,297.00	2.75	273.86	9,137.81	-81.49	1,251.25	64.17	0.74	0.28	-15.12
9,392.00	3.25	278.36	9,232.68	-80.95	1,246.31	64.14	0.58	0.53	4.74
9,488.00	3.60	270.94	9,328.51	-80.50	1,240.60	63.92	0.59	0.36	-7.73
9,583.00	3.71	270.79	9,423.31	-80.41	1,234.55	63.31	0.12	0.12	-0.16
9,678.00	4.12	266.20	9,518.09	-80.59	1,228.07	62.38	0.54	0.43	-4.83
9,774.00	4.08	269.19	9,613.85	-80.87	1,221.21	61.31	0.23	-0.04	3.11
9,869.00	4.20	267.16	9,708.60	-81.09	1,214.36	60.29	0.20	0.13	-2.14
9,964.00	3.95	267.00	9,803.36	-81.43	1,207.62	59.17	0.26	-0.26	-0.17
10,060.00	3.95	245.00	9,899.14	-83.01	1,201.32	56.88	1.57	0.00	-22.92
10,155.00	13.68	274.21	9,992.93	-83.57	1,187.11	54.68	10.96	10.24	30.75
10,250.00	23.33	293.51	10,082.99	-75.21	1,158.57	59.67	11.90	10.16	20.32
10,297.00	27.81	302.87	10,125.40	-65.54	1,140.81	67.21	12.81	9.53	19.91
10,346.00	32.03	311.36	10,167.88	-50.73	1,121.44	79.67	12.18	8.61	17.33
10,441.00	38.43	331.81	10,245.71	-7.87	1,088.43	118.41	14.05	6.74	21.53
10,519.63	42.84	345.10	10,305.48	39.62	1,069.97	163.44	12.33	5.61	16.90
FTP[T36-25/235H]									
10,536.00	43.94	347.57	10,317.37	50.54	1,067.32	173.99	12.33	6.69	15.08
10,632.00	47.91	5.02	10,384.40	118.85	1,063.25	241.36	13.67	4.14	18.18

Scientific Drilling, Intl

Survey Report

Company:	Devon Energy	Local Co-ordinate Reference:	Well 235H
Project:	Eddy County, NM (NAD83 NME)	TVD Reference:	KB = 23' @ 3532.00usft (H&P 466)
Site:	Todd 36-25 State Fed Com	MD Reference:	KB = 23' @ 3532.00usft (H&P 466)
Well:	235H	North Reference:	Grid
Wellbore:	ST1	Survey Calculation Method:	Minimum Curvature
Design:	ST1	Database:	Midland District

Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (bearing)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
10,727.00	58.10	11.36	10,441.53	193.75	1,074.31	317.04	11.97	10.73	6.67	
10,822.00	71.07	10.57	10,482.21	277.81	1,090.56	402.42	13.67	13.65	-0.83	
10,918.00	77.22	13.21	10,508.43	368.12	1,109.61	494.33	6.93	6.41	2.75	
11,014.00	81.74	12.18	10,525.96	460.17	1,130.34	588.16	4.82	4.71	-1.07	
11,109.00	83.35	12.14	10,538.28	552.26	1,150.18	681.92	1.70	1.69	-0.04	
11,204.00	84.29	11.66	10,548.51	644.67	1,169.66	775.98	1.11	0.99	-0.51	
11,299.00	85.08	11.58	10,557.31	737.32	1,188.71	870.21	0.84	0.83	-0.08	
11,395.00	86.71	9.02	10,564.18	831.52	1,205.83	965.76	3.16	1.70	-2.67	
11,490.00	88.73	6.36	10,567.96	925.58	1,218.53	1,060.66	3.51	2.13	-2.80	
11,585.00	90.37	2.88	10,568.71	1,020.25	1,226.18	1,155.58	4.05	1.73	-3.66	
11,681.00	91.65	3.36	10,567.02	1,116.09	1,231.40	1,251.38	1.42	1.33	0.50	
11,776.00	91.51	1.00	10,564.40	1,210.98	1,235.01	1,346.04	2.49	-0.15	-2.48	
11,871.00	92.32	0.91	10,561.22	1,305.91	1,236.59	1,440.52	0.86	0.85	-0.09	
11,966.00	90.13	0.54	10,559.19	1,400.88	1,237.80	1,534.98	2.34	-2.31	-0.39	
12,062.00	90.54	0.75	10,558.63	1,496.87	1,238.88	1,630.45	0.48	0.43	0.22	
12,157.00	90.54	0.33	10,557.74	1,591.86	1,239.77	1,724.91	0.44	0.00	-0.44	
12,252.00	87.21	359.30	10,559.60	1,686.83	1,239.47	1,819.20	3.67	-3.51	-1.08	
12,348.00	87.11	359.28	10,564.36	1,782.70	1,238.28	1,914.29	0.11	-0.10	-0.02	
12,443.00	87.61	359.86	10,568.73	1,877.60	1,237.57	2,008.46	0.81	0.53	0.61	
12,538.00	87.69	359.02	10,572.63	1,972.51	1,236.64	2,102.63	0.89	0.08	-0.88	
12,633.00	89.16	0.07	10,575.24	2,067.47	1,235.88	2,196.85	1.90	1.55	1.11	
12,729.00	88.62	0.40	10,577.10	2,163.45	1,236.28	2,292.23	0.66	-0.56	0.34	
12,824.00	90.13	0.76	10,578.13	2,258.44	1,237.24	2,386.69	1.63	1.59	0.38	
12,919.00	88.59	359.86	10,579.20	2,353.43	1,237.75	2,481.10	1.88	-1.62	-0.95	
13,014.00	90.91	359.73	10,579.61	2,448.42	1,237.41	2,575.41	2.45	2.44	-0.14	
13,110.00	92.29	0.24	10,576.93	2,544.38	1,237.39	2,670.72	1.53	1.44	0.53	
13,205.00	92.75	0.04	10,572.75	2,639.29	1,237.62	2,765.01	0.53	0.48	-0.21	
13,300.00	93.20	0.68	10,567.82	2,734.16	1,238.22	2,859.31	0.82	0.47	0.67	
13,396.00	93.73	1.40	10,562.02	2,829.96	1,239.96	2,954.67	0.93	0.55	0.75	
13,491.00	92.42	359.68	10,556.92	2,924.82	1,240.85	3,048.99	2.27	-1.38	-1.81	
13,587.00	92.52	359.78	10,552.79	3,020.73	1,240.40	3,144.20	0.15	0.10	0.10	
13,682.00	90.67	358.43	10,550.14	3,115.67	1,238.91	3,238.33	2.41	-1.95	-1.42	
13,777.00	90.10	358.30	10,549.50	3,210.63	1,236.20	3,332.34	0.62	-0.60	-0.14	
13,873.00	90.47	358.37	10,549.03	3,306.59	1,233.41	3,427.32	0.39	0.39	0.07	
13,968.00	89.83	358.00	10,548.78	3,401.54	1,230.40	3,521.29	0.78	-0.67	-0.39	
14,063.00	90.07	358.27	10,548.86	3,496.49	1,227.31	3,615.24	0.38	0.25	0.28	
14,158.00	90.70	358.66	10,548.22	3,591.45	1,224.77	3,709.26	0.78	0.66	0.41	
14,254.00	90.54	357.00	10,547.18	3,687.38	1,221.13	3,804.12	1.74	-0.17	-1.73	
14,349.00	89.87	356.82	10,546.84	3,782.24	1,216.01	3,897.74	0.73	-0.71	-0.19	
14,444.00	91.44	357.51	10,545.76	3,877.11	1,211.31	3,991.43	1.81	1.65	0.73	
14,540.00	92.89	357.65	10,542.13	3,972.95	1,207.26	4,086.16	1.52	1.51	0.15	
14,635.00	90.74	358.68	10,539.12	4,067.85	1,204.22	4,180.06	2.51	-2.26	1.08	
14,731.00	89.23	358.30	10,539.15	4,163.81	1,201.69	4,275.09	1.62	-1.57	-0.40	
14,826.00	87.98	358.89	10,541.46	4,258.76	1,199.37	4,369.12	1.45	-1.32	0.62	

Scientific Drilling, Intl

Survey Report

Company:	Devon Energy	Local Co-ordinate Reference:	Well 235H
Project:	Eddy County, NM (NAD83 NME)	TVD Reference:	KB = 23' @ 3532.00usft (H&P 466)
Site:	Todd 36-25 State Fed Com	MD Reference:	KB = 23' @ 3532.00usft (H&P 466)
Well:	235H	North Reference:	Grid
Wellbore:	ST1	Survey Calculation Method:	Minimum Curvature
Design:	ST1	Database:	Midland District

Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (bearing)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
14,922.00	90.13	359.51	10,543.04	4,354.73	1,198.03	4,464.28	2.33	2.24	0.65
15,017.00	86.31	359.11	10,545.99	4,449.66	1,196.88	4,558.44	4.04	-4.02	-0.42
15,113.00	86.00	358.67	10,552.43	4,545.42	1,195.03	4,653.35	0.56	-0.32	-0.46
15,208.00	86.10	359.18	10,558.98	4,640.18	1,193.25	4,747.26	0.55	0.11	0.54
15,304.00	87.34	359.80	10,564.47	4,736.02	1,192.40	4,842.35	1.44	1.29	0.65
15,399.00	90.13	1.16	10,566.57	4,830.98	1,193.19	4,936.76	3.27	2.94	1.43
15,495.00	88.96	359.91	10,567.33	4,926.97	1,194.09	5,032.21	1.78	-1.22	-1.30
15,590.00	90.13	1.52	10,568.08	5,021.95	1,195.27	5,126.69	2.09	1.23	1.69
15,685.00	90.88	1.73	10,567.24	5,116.91	1,197.97	5,221.32	0.82	0.79	0.22
15,780.00	90.54	1.01	10,566.07	5,211.87	1,200.24	5,315.90	0.84	-0.36	-0.76
15,876.00	91.51	1.24	10,564.35	5,307.84	1,202.12	5,411.44	1.04	1.01	0.24
15,971.00	92.12	1.85	10,561.34	5,402.76	1,204.68	5,506.01	0.91	0.64	0.64
16,066.00	90.07	0.93	10,559.53	5,497.70	1,206.99	5,600.59	2.37	-2.16	-0.97
16,162.00	88.99	1.20	10,560.31	5,593.68	1,208.77	5,696.13	1.16	-1.13	0.28
16,257.00	91.95	2.31	10,559.53	5,688.62	1,211.68	5,790.76	3.33	3.12	1.17
16,352.00	89.60	1.27	10,558.25	5,783.56	1,214.65	5,885.40	2.71	-2.47	-1.09
16,448.00	87.95	0.41	10,560.30	5,879.52	1,216.05	5,980.88	1.94	-1.72	-0.90
16,543.00	87.69	359.32	10,563.92	5,974.45	1,215.83	6,075.15	1.18	-0.27	-1.15
16,639.00	87.98	359.91	10,567.54	6,070.38	1,215.19	6,170.35	0.68	0.30	0.61
16,734.00	89.26	359.79	10,569.83	6,165.35	1,214.94	6,264.65	1.35	1.35	-0.13
16,829.00	90.44	359.24	10,570.08	6,260.35	1,214.13	6,358.91	1.37	1.24	-0.58
16,925.00	91.24	359.21	10,568.67	6,356.33	1,212.83	6,454.09	0.83	0.83	-0.03
17,021.00	91.51	358.65	10,566.37	6,452.28	1,211.04	6,549.19	0.65	0.28	-0.58
17,116.00	93.60	359.48	10,562.13	6,547.17	1,209.49	6,643.26	2.37	2.20	0.87
17,211.00	92.38	358.36	10,557.18	6,642.02	1,207.70	6,737.26	1.74	-1.28	-1.18
17,307.00	91.04	359.34	10,554.31	6,737.95	1,205.78	6,832.33	1.73	-1.40	1.02
17,402.00	87.01	359.38	10,555.93	6,832.91	1,204.72	6,926.53	4.24	-4.24	0.04
17,498.00	86.30	359.56	10,561.53	6,928.75	1,203.83	7,021.61	0.76	-0.74	0.19
17,593.00	87.25	359.67	10,566.87	7,023.59	1,203.19	7,115.74	1.01	1.00	0.12
17,688.00	89.19	359.85	10,569.83	7,118.54	1,202.80	7,210.00	2.05	2.04	0.19
17,783.00	91.24	0.64	10,569.47	7,213.53	1,203.20	7,304.40	2.31	2.16	0.83
17,878.00	90.30	0.03	10,568.19	7,308.52	1,203.76	7,398.81	1.18	-0.99	-0.64
17,973.00	89.73	359.61	10,568.17	7,403.52	1,203.46	7,493.14	0.75	-0.60	-0.44
18,068.00	90.64	359.21	10,567.86	7,498.51	1,202.48	7,587.37	1.05	0.96	-0.42
18,163.00	88.12	358.64	10,568.89	7,593.48	1,200.70	7,681.50	2.72	-2.65	-0.60
18,259.00	88.28	359.62	10,571.90	7,689.42	1,199.24	7,776.62	1.03	0.17	1.02
18,354.00	90.64	359.49	10,572.80	7,784.41	1,198.51	7,870.88	2.49	2.48	-0.14
18,449.00	91.01	359.01	10,571.43	7,879.39	1,197.26	7,965.08	0.64	0.39	-0.51
18,545.00	91.45	359.59	10,569.37	7,975.36	1,196.09	8,060.26	0.76	0.46	0.60
18,640.00	91.31	0.94	10,567.08	8,070.33	1,196.53	8,154.64	1.43	-0.15	1.42
18,735.00	89.63	359.89	10,566.30	8,165.32	1,197.22	8,249.07	2.09	-1.77	-1.11
18,831.00	88.63	359.83	10,567.76	8,261.31	1,196.98	8,344.38	1.04	-1.04	-0.06
18,926.00	91.24	1.04	10,567.87	8,356.30	1,197.70	8,438.81	3.03	2.75	1.27

Scientific Drilling, Intl

Survey Report

Company:	Devon Energy	Local Co-ordinate Reference:	Well 235H
Project:	Eddy County, NM (NAD83 NME)	TVD Reference:	KB = 23' @ 3532.00usft (H&P 466)
Site:	Todd 36-25 State Fed Com	MD Reference:	KB = 23' @ 3532.00usft (H&P 466)
Well:	235H	North Reference:	Grid
Wellbore:	ST1	Survey Calculation Method:	Minimum Curvature
Design:	ST1	Database:	Midland District

Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (bearing)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
19,021.00	87.72	359.68	10,568.73	8,451.27	1,198.30	8,533.22	3.97	-3.71	-1.43	
19,117.00	87.27	0.21	10,572.93	8,547.18	1,198.21	8,628.47	0.72	-0.47	0.55	
19,212.00	88.82	0.04	10,576.17	8,642.12	1,198.42	8,722.79	1.64	1.63	-0.18	
19,307.00	90.03	359.49	10,577.12	8,737.11	1,198.03	8,817.10	1.40	1.27	-0.58	
19,403.00	89.36	358.07	10,577.63	8,833.09	1,195.98	8,912.19	1.64	-0.70	-1.48	
19,498.00	90.23	357.79	10,577.97	8,928.02	1,192.55	9,006.09	0.96	0.92	-0.29	
19,594.00	91.17	357.43	10,576.80	9,023.93	1,188.55	9,100.88	1.05	0.98	-0.38	
19,689.00	90.24	357.83	10,575.63	9,118.84	1,184.62	9,194.70	1.07	-0.98	0.42	
19,784.00	88.89	356.94	10,576.35	9,213.74	1,180.29	9,288.45	1.70	-1.42	-0.94	
19,880.00	88.89	356.20	10,578.21	9,309.55	1,174.54	9,382.95	0.77	0.00	-0.77	
19,976.00	90.23	0.38	10,578.95	9,405.48	1,171.68	9,477.90	4.57	1.40	4.35	
20,071.00	88.19	356.08	10,580.26	9,500.40	1,168.75	9,571.84	5.01	-2.15	-4.53	
20,166.00	91.61	1.97	10,580.43	9,595.33	1,167.13	9,665.94	7.17	3.60	6.20	
20,262.00	91.61	2.46	10,577.73	9,691.22	1,170.84	9,761.61	0.51	0.00	0.51	
20,357.00	89.93	0.14	10,576.45	9,786.17	1,173.00	9,856.18	3.01	-1.77	-2.44	
20,452.00	91.04	2.74	10,575.65	9,881.13	1,175.38	9,950.77	2.98	1.17	2.74	
20,547.00	89.13	0.27	10,575.51	9,976.09	1,177.88	10,045.37	3.29	-2.01	-2.60	
20,633.00	89.53	0.55	10,576.51	10,062.08	1,178.49	10,130.86	0.57	0.47	0.33	
FINAL MWD Survey (20633.00' MD)										
20,690.00	89.53	0.55	10,576.98	10,119.07	1,179.04	10,187.53	0.00	0.00	0.00	
FINAL Proj. to Bit (20690.00' MD) - BHL.NEW[T36-25\235H] - BHL[T36-25\235H]										

Survey Annotations					
Measured Depth (usft)	Vertical Depth (usft)	Local Coordinates			
		+N/-S (usft)	+E/-W (usft)	Comment	
20,633.00	10,576.51	10,062.08	1,178.49	FINAL MWD Survey (20633.00' MD)	
20,690.00	10,576.98	10,119.07	1,179.04	FINAL Proj. to Bit (20690.00' MD)	

Checked By: _____ Approved By: _____ Date: _____
