



Weatherford


Evaluation, Drilling & Intervention

10000 West County Rd. 116

P.O. Box 61028

Midland, TX USA 79711

Tel. (432) 561-8892 Fax (432) 561-8895



Devon Energy
333 W. Sherridan Ave
Oklahoma City, OK, 73102

Date: October 26, 2012

Attention: John Pergean

15-40219

Re: Devon Energy
Well: Regulus 26 Federal #2H
Eddy County, New Mexico

Enclosed, please find the original survey performed on the referenced well by Precision Energy Services, Inc. (P-5 No. 676004), a Weatherford company. Other information required by your office is as follows:

Name & Title Of Surveyor	Well Number	Surveyed Depths	Dates Performed	Type of Survey
Justin Nguyen MWD Supervisor	2H	8637' MD 13500' MD	10/14/2012 10/25/2012	Measurement While Drilling


A notarized plan vs. actual is attached to the survey report. If any other information is required, please contact the undersigned at the letterhead address and phone number.

Jesse Aguilar
MWD Ops. Coordinator

On this, the 26th day of October, 2012, before me a notary public, the undersigned officer, personally appeared Jesse Aguilar, known to me (or satisfactorily proven) to be the person whose name is subscribed to the within instrument, and acknowledged that he executed the same for the purposes therein contained.

In witness hereof, I hereunto set my hand and official seal.

Notary Public





Regulus 26 Federal #2H Eddy Co, NM



KB ELEV: 3511
GL ELEV: 3491

SECTION DETAILS

Sec	MD	Inc	Azi	TVD	+N/-S	+E/-W	DLeg	TFace	VSec	Target
1	12109.00	97.17	271.11	9148.35	-44.76	-3115.36	0.00	0.00	3115.58	
2	12553.00	88.31	270.54	9127.15	-38.39	-3558.36	2.00	-176.30	3558.53	
3	13597.91	88.31	270.54	9158.00	-28.57	-4602.77	0.00	0.00	4602.86	

WELL DETAILS

Name	+N/-S	+E/-W	Northing	Easting	Latitude	Longitude	Slot
Regulus 26 Federal #2H	0.00	0.00	594763.81	695529.25	32°38'02.589N	103°49'56.824W	N/A

TARGET DETAILS

Name	TVD	+N/-S	+E/-W	Northing	Easting	Shape
PBHL	9158.00	-28.57	-4602.77	594735.24	690926.48	Rectangle (1128x50)

FIELD DETAILS

Eddy Co., NM (NAD 83)

Geodetic System: US State Plane Coordinate System 1983

Ellipsoid: GRS 1980

Zone: New Mexico, Eastern Zone

Magnetic Model: IGRF2010

System Datum: Mean Sea Level

Local North: Grid North

SITE DETAILS

Regulus 26 Federal #2H

Site Centre Northing: 594763.81

Easting: 695529.25


Ground Level: 3491.00

Positional Uncertainty: 0.00

Convergence: 0.27


LEGEND

- Regulus 26 Federal #2H, 1, Gyro
- Regulus 26 Federal #2H, 1, Plan #6
- Wft Svy

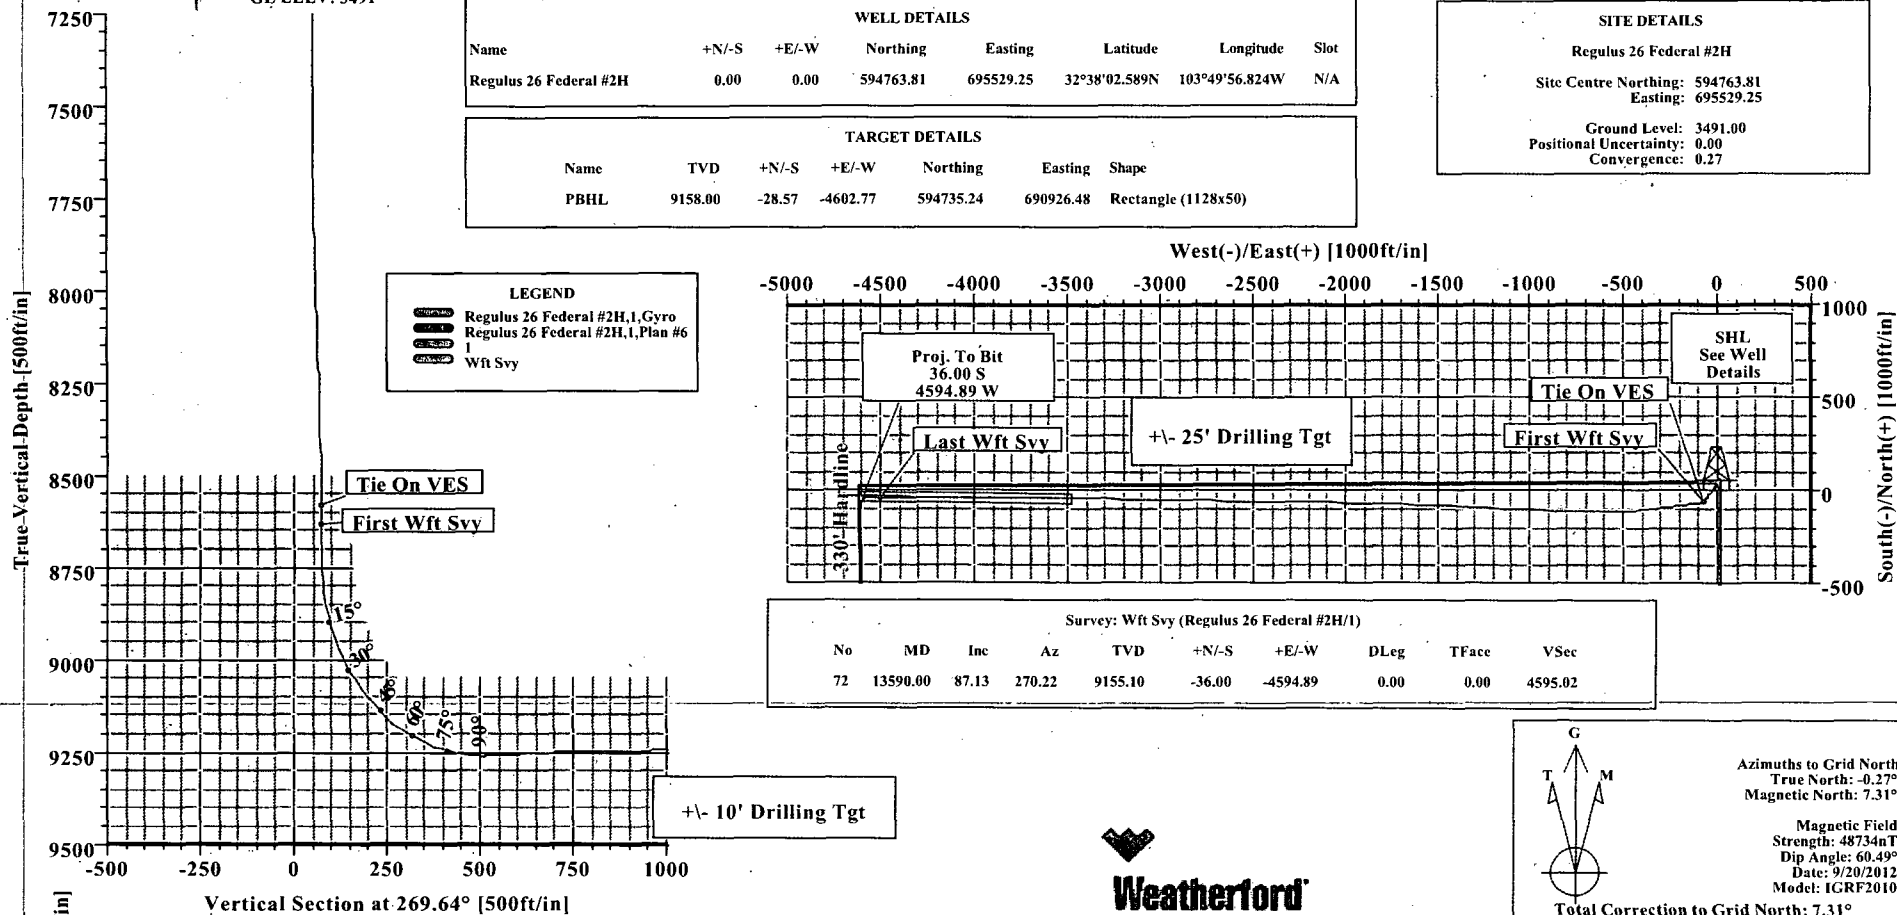


Survey: Wft Svy (Regulus 26 Federal #2H/1)

No	MD	Inc	Az	TVD	+N/-S	+E/-W	DLeg	TFace	VSec
72	13590.00	87.13	270.22	9155.10	-36.00	-4594.89	0.00	0.00	4595.02



Vertical Section at 269.64° [500ft/in]

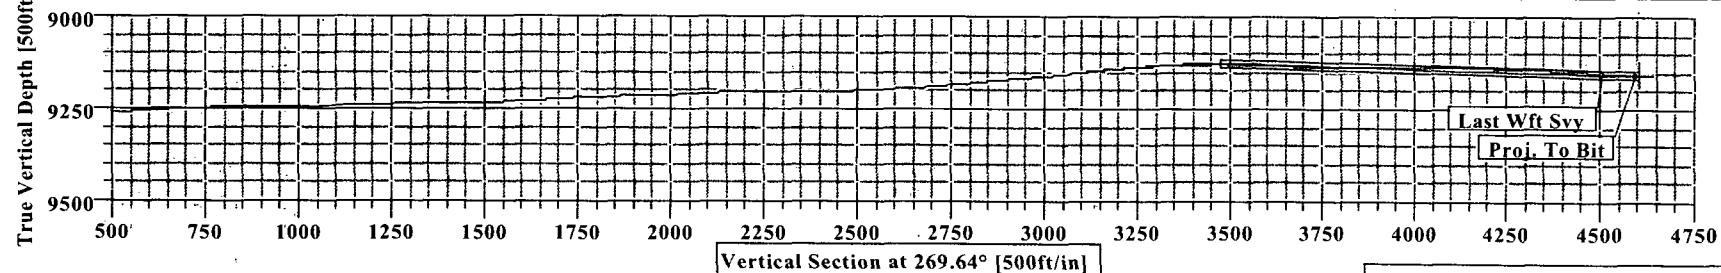

Survey: Wft Svy (Regulus 26 Federal #2H/1)

Created By: Russell W. Joyner

Date: 10/25/2012



Weatherford WFT Survey Report X & Y's

**Weatherford**

Company: Devon Energy	Date: 10/25/2012	Time: 06:59:34	Page: 2
Field: Eddy Co. NM (NAD 83)	Co-ordinate (NE) Reference: Well: Regulus 26 Federal #2H Grid: North		
Site: Regulus 26 Federal #2H	Vertical (TVD) Reference: SITE 351.10		
Well: Regulus 26 Federal #2H	Section (VS) Reference: Well (0.00N 0.00E 269.64Azi)		
Wellpath: 1	Survey Calculation Method: Minimum Curvature	Db: Sybase	

Survey

MD ft	Incl deg	Azim deg	TVD ft	N/S ft	E/W ft	DLS deg/100ft	VS ft	MapN ft	MapE ft	Comment
9392.00	73.91	263.99	9244.68	-103.27	-404.69	15.34	405.33	594660.54	695124.56	
9424.00	79.09	264.38	9252.15	-106.42	-435.63	16.23	436.29	594657.39	695093.62	
9455.00	84.11	265.44	9256.68	-109.14	-466.17	16.54	466.85	594654.67	695063.08	
9502.00	90.84	268.00	9258.75	-111.82	-513.02	15.32	513.71	594651.99	695016.23	
9564.00	92.80	268.88	9256.78	-113.51	-574.96	3.46	575.66	594650.30	694954.29	
9659.00	93.36	271.87	9251.68	-112.89	-669.81	3.20	670.50	594650.92	694859.44	
9753.00	91.89	271.92	9247.37	-109.78	-763.66	1.56	764.33	594654.03	694765.59	
9847.00	90.07	271.53	9245.76	-106.95	-857.60	1.98	858.25	594656.86	694671.65	
9942.00	91.05	271.92	9244.83	-104.09	-952.55	1.11	953.18	594659.72	694576.70	
10037.00	91.82	271.98	9242.45	-100.86	-1047.46	0.81	1048.07	594662.95	694481.79	
10131.00	91.82	272.63	9239.47	-97.08	-1141.34	0.69	1141.92	594666.73	694387.91	
10225.00	90.91	273.00	9237.23	-92.47	-1235.20	1.05	1235.75	594671.34	694294.05	
10319.00	91.61	272.91	9235.16	-87.62	-1329.05	0.75	1329.57	594676.19	694200.20	
10414.00	90.07	272.36	9233.77	-83.26	-1423.93	1.72	1424.43	594680.55	694105.32	
10508.00	91.40	272.54	9232.56	-79.24	-1517.84	1.43	1518.31	594684.57	694011.41	
10602.00	92.73	272.61	9229.18	-75.02	-1611.68	1.42	1612.12	594688.79	693917.57	
10697.00	94.06	272.27	9223.55	-70.98	-1706.42	1.44	1706.84	594692.83	693822.83	
10791.00	92.31	271.65	9218.33	-67.77	-1800.22	1.97	1800.61	594696.04	693729.03	
10886.00	91.33	271.45	9215.31	-65.20	-1895.14	1.05	1895.51	594698.61	693634.11	
10980.00	92.38	271.49	9212.27	-62.79	-1989.06	1.12	1989.41	594701.02	693540.19	
11074.00	93.08	271.36	9207.79	-60.46	-2082.92	0.76	2083.26	594703.35	693446.33	
11169.00	90.91	271.13	9204.49	-58.40	-2177.83	2.30	2178.16	594705.41	693351.42	
11263.00	89.79	270.52	9203.91	-57.04	-2271.82	1.36	2272.13	594706.77	693257.43	
11357.00	90.77	270.43	9203.45	-56.26	-2365.81	1.05	2366.12	594707.55	693163.44	
11452.00	91.68	270.55	9201.42	-55.45	-2460.79	0.97	2461.09	594708.36	693068.46	
11546.00	92.73	270.76	9197.80	-54.38	-2554.71	1.14	2555.00	594709.43	692974.54	
11641.00	94.06	270.78	9192.18	-53.10	-2649.53	1.40	2649.81	594710.71	692879.72	
11735.00	95.04	270.84	9184.72	-51.78	-2743.23	1.04	2743.50	594712.03	692786.02	
11830.00	96.24	271.10	9175.39	-50.18	-2837.75	1.29	2838.01	594713.63	692691.50	
11925.00	94.27	271.13	9166.69	-48.34	-2932.33	2.07	2932.58	594715.47	692596.92	
12019.00	95.74	271.06	9158.48	-46.55	-3025.95	1.57	3026.18	594717.26	692503.30	
12114.00	97.02	271.16	9147.93	-44.72	-3120.34	1.35	3120.56	594719.09	692408.91	
12208.00	94.83	271.45	9138.23	-42.59	-3213.81	2.35	3214.02	594721.22	692315.44	
12303.00	92.87	271.48	9131.85	-40.17	-3308.56	2.06	3308.75	594723.64	692220.69	
12397.00	91.40	270.71	9128.35	-38.37	-3402.48	1.77	3402.65	594725.44	692126.77	
12492.00	89.44	270.21	9127.65	-37.61	-3497.47	2.13	3497.63	594726.20	692031.78	
12587.00	87.69	269.88	9130.03	-37.53	-3592.43	1.87	3592.60	594726.28	691936.82	
12681.00	88.32	269.54	9133.30	-38.01	-3686.37	0.76	3686.54	594725.80	691842.88	
12775.00	89.58	269.62	9135.02	-38.70	-3780.35	1.34	3780.52	594725.11	691748.90	
12870.00	91.12	269.71	9134.44	-39.25	-3875.35	1.62	3875.52	594724.56	691653.90	
12964.00	89.30	270.49	9134.10	-39.09	-3969.34	2.11	3969.51	594724.72	691559.91	
13059.00	88.67	270.14	9135.78	-38.57	-4064.32	0.76	4064.49	594725.24	691464.93	
13153.00	89.72	270.03	9137.10	-38.43	-4158.31	1.12	4158.47	594725.38	691370.94	
13248.00	87.55	270.66	9139.36	-37.86	-4253.28	2.38	4253.43	594725.95	691275.97	
13342.00	88.53	270.41	9142.58	-36.98	-4347.22	1.08	4347.36	594726.83	691182.03	
13437.00	86.21	270.13	9146.94	-36.53	-4442.11	2.46	4442.25	594727.28	691087.14	
13500.00	87.13	270.22	9150.60	-36.34	-4505.00	1.47	4505.14	594727.47	691024.25	Last Wft Svy
13590.00	87.13	270.22	9155.10	-36.00	-4594.89	0.00	4595.02	594727.81	690934.36	Proj. To Bit



Weatherford

WFT Survey Report X & Y's



Company: Devon Energy	Date: 10/25/2012	Time: 06:59:34	Page: 3
Field: Eddy Co. NM (NAD:83)	Co-ordinate(NE) Reference: Well: Regulus 26 Federal #2H	Grid: North	
Site: Regulus 26 Federal #2H	Vertical (TVD) Reference: SITE: 3511-0		
Well: Regulus 26 Federal #2H	Section (VS) Reference: Well: (0.00N:0.00E:269.64Azi)		
Wellpath: 1	Survey Calculation Method: Minimum Curvature	Db: Sybase	

Annotation

MD	TVD	
ft.	ft.	
8585.00	8580.50	Tie On VES
8637.00	8632.47	First Wft Svy
13500.00	9150.60	Last Wft Svy
13590.00	9155.10	Proj. To Bit

**McVAY DRILLING COMPANY**

P.O. Box 2450
Hobbs, New Mexico 88241
(575) 397-3311
FAX: 39-DRILL

Well Name and Num: Regulus 26 Fed 2H
Location: Sec. 26, T19S, R31E
Operator: Devon
Drilling Contractor: McVay Drilling Company


The undersigned certifies that he is an authorized representative of the drilling contractor who drilled the above described well and that he has conducted deviation tests and obtained the following results:


<u>Degrees @</u>	<u>Depth</u>	<u>Degrees @</u>	<u>Depth</u>	<u>Degrees @</u>	<u>Depth</u>	<u>Degrees @</u>	<u>Depth</u>
1.00	351	12.08	8867	89.86	11588		
1.00	829	15.95	8920	89.70	12060		
1.63	1117	22.39	8983	91.65	12532		
1.05	1620	46.73	9203	90.49	12815		
2.30	2120	64.80	9330	92.87	13382		
1.58	2281	84.11	9455	91.89	13855		
0.91	3130	92.80	9564				
2.10	4604	91.89	9753				
1.50	4887	90.07	9847				
1.20	5456	91.82	10032				
0.30	6480	91.40	10508				
0.60	7340	91.33	10886				
2.10	7715	90.91	11159				
2.60	8092	92.70	11546				
2.00	8378	92.88	11925				
1.65	8712	92.02	12114				
7.94	8826	89.44	12492				

By: Hobbs

Subscribed and sworn to before me this 31st day of October, 2012

Tina Flemens
Notary Public, Lea County, New Mexico





A GYRO TECHNOLOGIES INC. COMPANY

PO Box 261021
Corpus Christi, Texas 78426
(361) 767-0602 • (800) 606-GYRO • Fax (361) 767-0612

October 23, 2012



Devon Energy Production Company
333 West Sheridan Ave
Oklahoma City, Oklahoma 73102-5010

Attn: Patti Riechers

Re: **Regulus 26 Federal No. 002H**

Please find enclosed a copy of the survey from 0' to 8,585' ran on the above referenced well.


If I can be of any further service, please do not hesitate to call me at 800-606-4976.

Sincerely,


Keith Havelka
Operations

STATE OF TEXAS §
COUNTY OF NUECES §

This instrument was acknowledged before me on the 24th day of October
A.D. 2012, by Keith Havelka.




Laura Ballew
Notary Public, State of Texas



Company: Devon Energy Production Company
 Lease/Well: Regulus 26 Federal/No. 002H
 Location: S26 T19s R31e
 Rig Name: McVay #10
 State/County: New Mexico/Eddy
 Latitude: 32.63, Longitude: -103.83
 GRID North is 0.27 Degrees East of True North
 VS-Azi: 0.00 Degrees

VES
 VAUGHN ENERGY SERVICES

RECEIVED
 FEB 12 2013
 NMOCD ARTESIA

RKB : 20 Feet

DRILLOG HA GYRO SURVEY CALCULATIONS

Filename: ...26 federal #2h gyro survey.ut

Minimum Curvature Method

Report Date/Time: 10/23/2012 / 08:47

Vaughn Energy Services

(432) 563-5444

Gardendale, TX

Surveyor: Dustin Wedel


Regulus 26 Federal No. 002H / API 30-015-40219

Measured Depth FT	Incl Angle Deg	Drift Direction Deg	TVD FT	+N/-S FT	+E/-W FT	Vertical Section FT	Closure Distance FT	Closure Direction Deg	Dogleg Severity Deg/100
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	****
100.00	0.27	8.70	100.00	0.23	0.04	0.23	0.23	8.70	0.27
200.00	0.53	17.41	200.00	0.91	0.21	0.91	0.93	13.06	0.27
300.00	0.68	6.15	299.99	1.94	0.41	1.94	1.99	12.01	0.19
400.00	0.83	354.89	399.98	3.26	0.41	3.26	3.29	7.21	0.21
500.00	1.28	343.93	499.97	5.06	0.04	5.06	5.06	0.44	0.49
600.00	1.72	332.97	599.93	7.47	-0.95	7.47	7.53	352.72	0.53
700.00	2.00	328.38	699.88	10.29	-2.55	10.29	10.61	346.08	0.31
800.00	2.27	323.80	799.81	13.38	-4.64	13.38	14.16	340.88	0.32
900.00	2.20	323.16	899.73	16.52	-6.96	16.52	17.92	337.15	0.08
1000.00	2.13	322.53	999.66	19.53	-9.24	19.53	21.61	334.67	0.08
1100.00	1.81	334.94	1099.60	22.43	-11.04	22.43	25.00	333.80	0.53
1200.00	1.49	347.35	1199.56	25.13	-11.99	25.13	27.85	334.49	0.48
1300.00	1.35	353.63	1299.53	27.57	-12.41	27.57	30.24	335.77	0.21
1400.00	1.22	359.91	1399.51	29.81	-12.54	29.81	32.34	337.18	0.19
1500.00	1.30	14.85	1499.48	31.97	-12.25	31.97	34.24	339.03	0.34
1600.00	1.39	29.78	1599.45	34.12	-11.36	34.12	35.96	341.58	0.36
1700.00	1.85	31.98	1699.41	36.54	-9.90	36.54	37.86	344.84	0.47
1800.00	2.32	34.19	1799.35	39.59	-7.91	39.59	40.37	348.70	0.47

Measured Depth FT	Incl Angle Deg	Drift Direction Deg	TVD FT	+N/-S FT	+E/-W FT	Vertical Section FT	Closure Distance FT	Closure Direction Deg	Dogleg Severity Deg/100
1900.00	2.45	39.44	1899.26	42.91	-5.41	42.91	43.25	352.81	0.26
2000.00	2.59	44.69	1999.16	46.17	-2.46	46.17	46.24	356.95	0.27
2100.00	2.56	45.02	2099.06	49.36	0.70	49.36	49.36	0.82	0.03
2200.00	2.53	45.35	2198.96	52.48	3.85	52.48	52.62	4.20	0.03
2300.00	1.92	47.56	2298.89	55.16	6.65	55.16	55.56	6.88	0.61
2400.00	1.31	49.77	2398.85	57.03	8.76	57.03	57.70	8.74	0.61
2500.00	0.92	37.00	2498.83	58.41	10.12	58.41	59.28	9.83	0.46
2600.00	0.52	24.22	2598.82	59.46	10.78	59.46	60.43	10.28	0.42
2700.00	0.53	350.10	2698.82	60.33	10.89	60.33	61.31	10.23	0.31
2800.00	0.54	315.98	2798.81	61.13	10.48	61.13	62.02	9.73	0.32
2900.00	0.82	313.34	2898.81	61.96	9.63	61.96	62.71	8.83	0.28
3000.00	1.10	310.71	2998.79	63.08	8.38	63.08	63.64	7.56	0.28
3100.00	0.93	289.97	3098.78	63.99	6.89	63.99	64.36	6.14	0.40
3200.00	0.75	269.24	3198.77	64.26	5.47	64.26	64.49	4.87	0.35
3300.00	0.98	221.93	3298.76	63.61	4.25	63.61	63.75	3.82	0.72
3400.00	1.21	174.62	3398.74	61.93	3.78	61.93	62.05	3.49	0.90
3500.00	2.53	192.93	3498.69	58.73	3.38	58.73	58.83	3.30	1.44
3600.00	3.85	211.24	3598.53	53.71	1.15	53.71	53.72	1.22	1.66
3700.00	4.21	210.63	3698.28	47.68	-2.47	47.68	47.74	357.04	0.36
3800.00	4.57	210.02	3797.99	41.07	-6.33	41.07	41.55	351.24	0.36
3900.00	4.09	207.37	3897.70	34.45	-9.96	34.45	35.86	343.87	0.52
4000.00	3.61	204.71	3997.48	28.43	-12.92	28.43	31.22	335.56	0.51
4100.00	3.58	205.45	4097.28	22.75	-15.57	22.75	27.57	325.60	0.06
4200.00	3.55	206.18	4197.09	17.15	-18.28	17.15	25.07	313.17	0.06
4300.00	3.31	211.14	4296.91	11.91	-21.14	11.91	24.26	299.39	0.38
4400.00	3.06	216.09	4396.75	7.28	-24.20	7.28	25.27	286.74	0.37
4500.00	2.63	212.38	4496.63	3.18	-27.00	3.18	27.19	276.73	0.48
4600.00	2.19	208.68	4596.54	-0.42	-29.15	-0.42	29.15	269.17	0.47
4700.00	1.89	215.28	4696.48	-3.45	-31.02	-3.45	31.21	263.66	0.37
4800.00	1.60	221.88	4796.43	-5.84	-32.90	-5.84	33.42	259.94	0.35
4900.00	1.33	224.60	4896.40	-7.70	-34.65	-7.70	35.50	257.46	0.28
5000.00	1.06	227.33	4996.38	-9.16	-36.15	-9.16	37.29	255.78	0.28
5100.00	1.07	227.20	5096.36	-10.43	-37.52	-10.43	38.94	254.47	0.01
5200.00	1.09	227.08	5196.34	-11.71	-38.90	-11.71	40.63	253.25	0.01
5300.00	1.06	223.86	5296.33	-13.02	-40.23	-13.02	42.29	252.07	0.07
5400.00	1.03	220.64	5396.31	-14.36	-41.46	-14.36	43.88	250.89	0.07
5500.00	0.90	221.96	5496.29	-15.63	-42.57	-15.63	45.35	249.84	0.13
5600.00	0.77	223.29	5596.28	-16.71	-43.56	-16.71	46.65	249.02	0.13
5700.00	0.69	224.04	5696.28	-17.63	-44.44	-17.63	47.81	248.36	0.08



Vaughn Energy Services
(432) 563-5444
Gardendale, TX
Surveyor: Dustin Wedel
Regulus 26 Federal No. 002H / API 30-015-40219

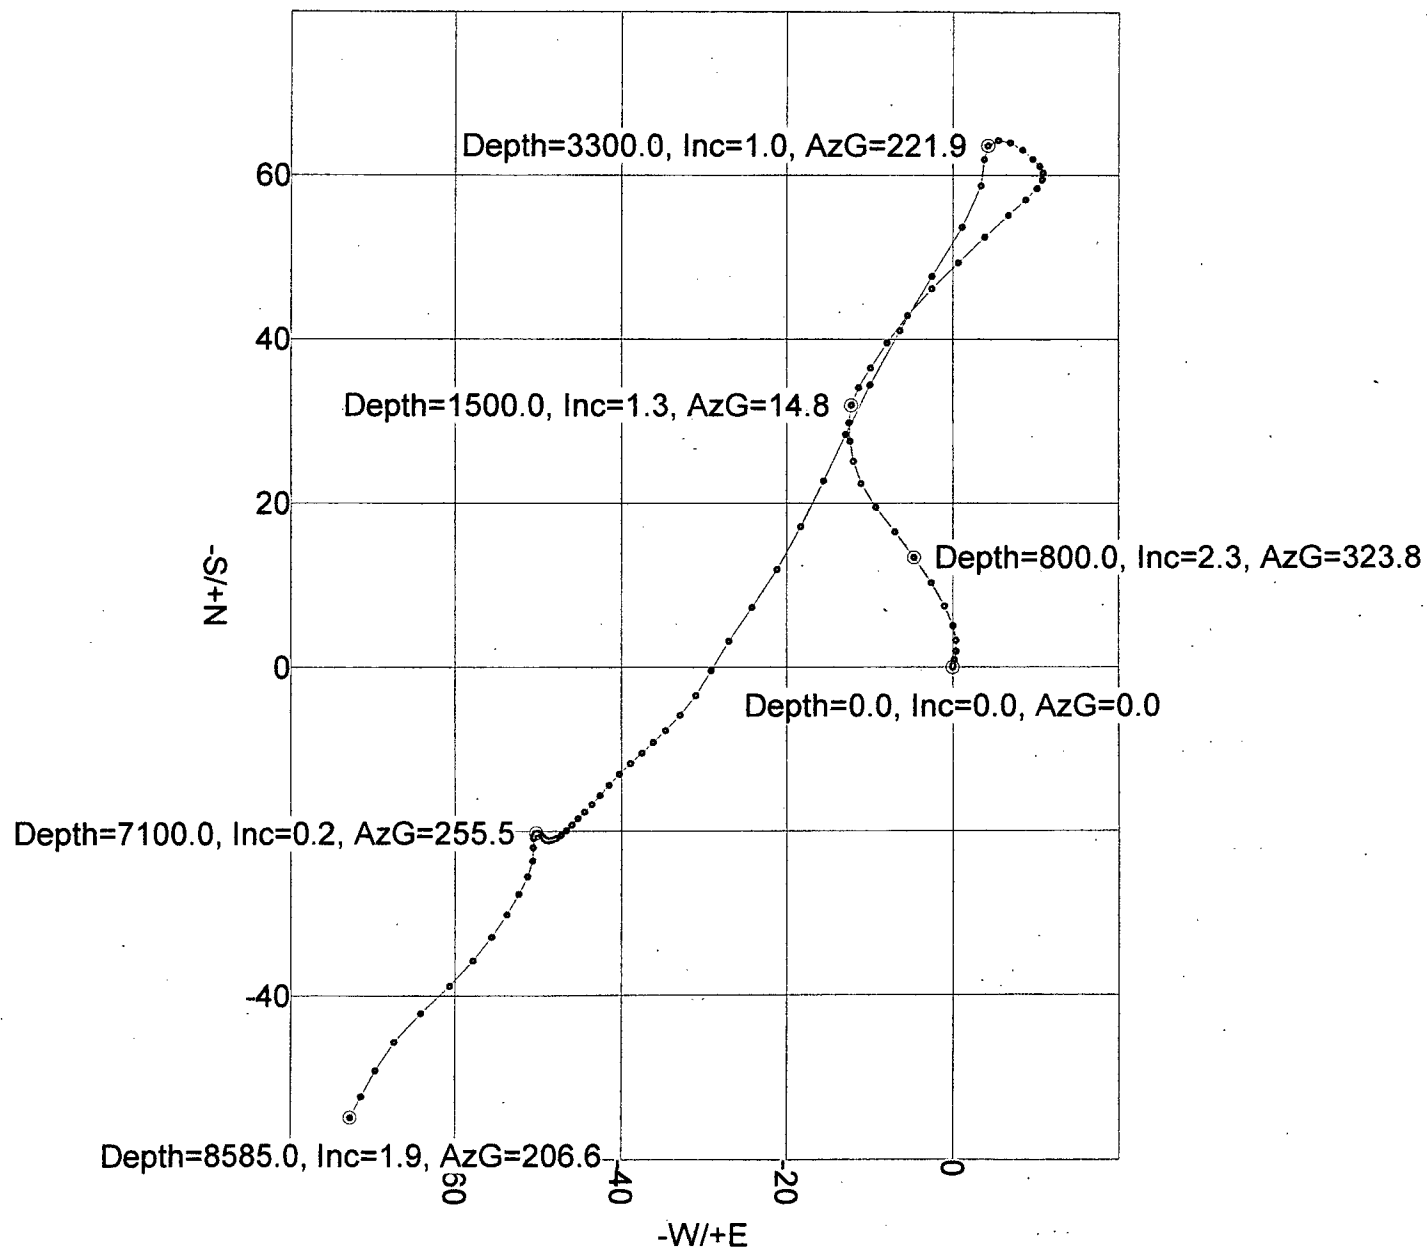

VES Survey Date: 10/15/2012



Stimulations Summary

District PERMIAN BASIN	County EDDY	Field Name HACKBERRY	Project Group PB NEW MEXICO	State/Province NM						
Surface Legal Location SEC26 T19S R31E	API/UWI 3001540219	Latitude (°) 32° 38' 2.601" N	Longitude (°) 103° 49' 56.808" W	Ground Elev... 3,491.00	KB - GL (ft) 20.00	Orig KB Elev (ft) 3,511.00	Tubing Head Elevation (ft)			
HYDRAULIC FRAC , 11/12/2012 08:43 , BONE SPRING, OH , 13,156.0 ftKB - 13,516.0 ftKB, BAKER HUGHES , OTTAWA Bulk Sand 224394.4 LB; SU										
Proppant De...	Total Clean Volu...	Pre Trt S/I Prs (psi)	Pst Trt S/I Prs (psi)	P Break (psi)	ISIP (psi)	Avg Treat Pressur...	Q Treat Avg (bbl/...	P Max (psi)	Q Treat Max (bbl/...	Conc Max...
289,925.1	4953.30	0.0	2,339.0		2,600.0	5,343.0	71	5,600.0	81	4.00
HYDRAULIC FRAC , 11/12/2012 13:13 , BONE SPRING, OH , 12,620.0 ftKB - 12,979.0 ftKB, BAKER HUGHES , OTTAWA Bulk Sand 225273.7 LB; SU										
Proppant De...	Total Clean Volu...	Pre Trt S/I Prs (psi)	Pst Trt S/I Prs (psi)	P Break (psi)	ISIP (psi)	Avg Treat Pressur...	Q Treat Avg (bbl/...	P Max (psi)	Q Treat Max (bbl/...	Conc Max...
289,925.1	5069.20	0.0	2,525.0		2,798.0	5,018.0	80	5,555.0	81	4.00
HYDRAULIC FRAC , 11/12/2012 13:13 , BONE SPRING, OH , 12,083.0 ftKB - 12,443.0 ftKB, BAKER HUGHES , OTTAWA Bulk Sand 350440.1 LB; SU										
Proppant De...	Total Clean Volu...	Pre Trt S/I Prs (psi)	Pst Trt S/I Prs (psi)	P Break (psi)	ISIP (psi)	Avg Treat Pressur...	Q Treat Avg (bbl/...	P Max (psi)	Q Treat Max (bbl/...	Conc Max...
289,925.1	6003.90	0.0	2,525.0		2,768.0	5,036.0	80	5,268.0	80	4.00
HYDRAULIC FRAC , 11/12/2012 13:13 , BONE SPRING, OH , 11,546.0 ftKB - 11,906.0 ftKB, BAKER HUGHES , OTTAWA Bulk Sand 226013.6 LB; SU										
Proppant De...	Total Clean Volu...	Pre Trt S/I Prs (psi)	Pst Trt S/I Prs (psi)	P Break (psi)	ISIP (psi)	Avg Treat Pressur...	Q Treat Avg (bbl/...	P Max (psi)	Q Treat Max (bbl/...	Conc Max...
289,925.1	5063.90	0.0	2,510.0		2,886.0	5,017.0	80	5,580.0	80	4.00
HYDRAULIC FRAC , 11/12/2012 13:13 , BONE SPRING, OH , 11,010.0 ftKB - 11,370.0 ftKB, BAKER HUGHES , OTTAWA Bulk Sand 226013.6 LB; SU										
Proppant De...	Total Clean Volu...	Pre Trt S/I Prs (psi)	Pst Trt S/I Prs (psi)	P Break (psi)	ISIP (psi)	Avg Treat Pressur...	Q Treat Avg (bbl/...	P Max (psi)	Q Treat Max (bbl/...	Conc Max...
289,925.1	5063.90	0.0	2,566.0		2,782.0	4,833.0	80	5,790.0	80	4.00
HYDRAULIC FRAC , 11/13/2012 08:20 , BONE SPRING, OH , 10,473.0 ftKB - 10,833.0 ftKB, BAKER HUGHES , OTTAWA Bulk Sand 226326.2 LB; SU										
Proppant De...	Total Clean Volu...	Pre Trt S/I Prs (psi)	Pst Trt S/I Prs (psi)	P Break (psi)	ISIP (psi)	Avg Treat Pressur...	Q Treat Avg (bbl/...	P Max (psi)	Q Treat Max (bbl/...	Conc Max...
292,599.9	4983.40	0.0	2,657.0		2,657.0	4,833.0	80	5,790.0	80	4.00
HYDRAULIC FRAC , 11/13/2012 16:53 , BONE SPRING, OH , 9,937.0 ftKB - 10,296.0 ftKB, BAKER HUGHES , OTTAWA Bulk Sand 249299.8 LB; SUP										
Proppant De...	Total Clean Volu...	Pre Trt S/I Prs (psi)	Pst Trt S/I Prs (psi)	P Break (psi)	ISIP (psi)	Avg Treat Pressur...	Q Treat Avg (bbl/...	P Max (psi)	Q Treat Max (bbl/...	Conc Max...
324,998.0	5162.70	0.0	2,551.0		2,956.0	4,539.0	79	5,140.0	80	4.00
HYDRAULIC FRAC , 11/13/2012 16:53 , BONE SPRING, OH , 9,400.0 ftKB - 9,760.0 ftKB, BAKER HUGHES , OTTAWA Bulk Sand 252554 LB; SUPER										
Proppant De...	Total Clean Volu...	Pre Trt S/I Prs (psi)	Pst Trt S/I Prs (psi)	P Break (psi)	ISIP (psi)	Avg Treat Pressur...	Q Treat Avg (bbl/...	P Max (psi)	Q Treat Max (bbl/...	Conc Max...
324,998.0	5181.90	0.0	2,525.0		2,832.0	5,070.0	80	5,771.0	80	4.00
