

CHEVRON

Fren
Eddy County, NM
Skelly Unit #960
VH - Job #32K0810637

RECEIVED

NOV 08 2010
HOBBSUCD

30-015-34326

Survey: Actual

SDI Standard Survey Report

24 September, 2010


This survey is correct to the best of my knowledge and is supported by actual field data.

Richardson

Notorized this date 5th of October, 2010.

Carrie Reed

Notary Signature
County of Midland
State of Texas



Scientific Drilling International, Inc.
SDI Standard Survey Report

Company:	CHEVRON	Local Co-ordinate Reference:	Well Skelly Unit #960
Project:	Fren	TVD Reference:	WELL @ 0.0usft (Original Well Elev)
Site:	Eddy County, NM	MD Reference:	WELL @ 0.0usft (Original Well Elev)
Well:	Skelly Unit #960	North Reference:	Grid
Wellbore:	VH - Job #32K0810637	Survey Calculation Method:	Minimum Curvature
Design:	VH - Job #32K0810637	Database:	EDM-Regulatory

Project	Fren		
Map System:	US State Plane 1927 (Exact solution)	System Datum:	Mean Sea Level
Geo Datum:	NAD 1927 (NADCON CONUS)		
Map Zone:	New Mexico East 3001		

Well	Skelly Unit #960, Vertical					
Well Position	+N/-S	0.0 usft	Northing:	667,318.15 usft	Latitude:	32° 50' 0.960 N
	+E/-W	0.0 usft	Easting:	649,288.64 usft	Longitude:	103° 50' 50.290 W
Position Uncertainty		0.0 usft	Wellhead Elevation:	usft	Ground Level:	0.0 usft

Wellbore	VH - Job #32K0810637				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	BGGM2010	8/27/2010	7.92	60.73	49,099

Design	VH - Job #32K0810637			
Audit Notes:				
Version:	1.0	Phase:	ACTUAL	Tie On Depth: 0.0
Vertical Section:	Depth From (TVD) (usft)	+N/-S (usft)	+E/-W (usft)	Direction (°)
	0.0	0.0	0.0	319.37

Survey Program		Date	9/24/2010		
From (usft)	To (usft)	Survey (Wellbore)	Tool Name	Description	
100.0	6,444.0	Actual (VH - Job #32K0810637)	Keeper	Keeper Gyro	

Survey								
Measured Depth (usft)	Inclination (°)	Azimuth (°)	True Vertical Depth	North/South (usft)	East/West (usft)	Closure Azimuth (°)	Closure Distance (usft)	
0.0	0.00	0.00	0.0	0.0	0.0	0.0	0.00	0.0
100.0	0.11	276.89	100.0	0.0	-0.1	276.89	0.1	
200.0	0.11	251.08	200.0	0.0	-0.3	268.35	0.3	
300.0	0.71	185.29	300.0	-0.7	-0.4	213.20	0.8	
400.0	0.82	183.59	400.0	-2.0	-0.5	194.97	2.1	
500.0	0.84	186.02	500.0	-3.4	-0.7	190.78	3.5	
600.0	0.85	187.91	600.0	-4.9	-0.8	189.65	5.0	
700.0	0.75	190.25	700.0	-6.3	-1.1	189.51	6.4	
800.0	0.88	185.64	799.9	-7.7	-1.2	189.19	7.8	
900.0	0.84	184.62	899.9	-9.2	-1.4	188.53	9.3	
1,000.0	0.92	180.73	999.9	-10.7	-1.4	187.69	10.8	
1,100.0	0.73	171.45	1,099.9	-12.1	-1.4	186.40	12.2	
1,200.0	0.76	147.17	1,199.9	-13.3	-0.9	183.89	13.4	
1,300.0	0.91	84.32	1,299.9	-13.8	0.2	178.99	13.8	
1,400.0	1.33	66.22	1,399.9	-13.3	2.1	171.02	13.4	
1,500.0	1.68	59.17	1,499.8	-12.0	4.4	159.86	12.8	
1,600.0	1.78	60.55	1,599.8	-10.5	7.0	146.28	12.7	

Scientific Drilling International, Inc.
SDI Standard Survey Report

Company:	CHEVRON	Local Co-ordinate Reference:	Well Skelly Unit #960
Project:	Fren	TVD Reference:	WELL @ 0.0usft (Original Well Elev)
Site:	Eddy County, NM	MD Reference:	WELL @ 0.0usft (Original Well Elev)
Well:	Skelly Unit #960	North Reference:	Grid
Wellbore:	VH - Job #32K0810637	Survey Calculation Method:	Minimum Curvature
Design:	VH - Job #32K0810637	Database:	EDM-Regulatory

Survey							
Measured Depth (usft)	Inclination (°)	Azimuth (°)	True Vertical Depth	North/South (usft)	East/West (usft)	Closure Azimuth (°)	Closure Distance (usft)
1,700.0	1.75	68.87	1,699.7	-9.2	9.8	133.22	13.5
1,800.0	1.45	70.93	1,799.7	-8.2	12.4	123.59	14.9
1,900.0	1.18	68.25	1,899.7	-7.5	14.6	117.09	16.4
2,000.0	0.75	61.70	1,999.7	-6.8	16.1	112.77	17.5
2,100.0	0.44	40.36	2,099.7	-6.2	16.9	109.99	18.0
2,200.0	0.30	34.47	2,199.7	-5.7	17.3	108.06	18.2
2,300.0	0.26	325.62	2,299.7	-5.2	17.3	106.83	18.1
2,400.0	0.52	279.35	2,399.7	-5.0	16.8	106.56	17.5
2,500.0	0.66	276.65	2,499.7	-4.8	15.8	107.10	16.5
2,600.0	0.66	272.41	2,599.6	-4.8	14.6	108.04	15.4
2,700.0	0.69	281.74	2,699.6	-4.6	13.4	108.93	14.2
2,800.0	0.80	289.14	2,799.6	-4.3	12.2	109.25	12.9
2,900.0	0.94	291.56	2,899.6	-3.7	10.8	109.09	11.4
3,000.0	1.08	297.98	2,999.6	-3.0	9.2	108.02	9.6
3,100.0	1.19	298.35	3,099.6	-2.0	7.4	105.42	7.7
3,200.0	1.28	301.58	3,199.6	-1.0	5.6	99.90	5.6
3,300.0	1.39	302.25	3,299.5	0.3	3.6	85.83	3.6
3,400.0	1.47	304.93	3,399.5	1.6	1.5	42.56	2.2
3,500.0	1.53	300.35	3,499.5	3.1	-0.7	347.18	3.1
3,600.0	1.67	290.07	3,599.4	4.2	-3.2	322.74	5.3
3,700.0	1.51	286.53	3,699.4	5.1	-5.8	311.10	7.8
3,800.0	1.43	288.91	3,799.4	5.9	-8.3	305.35	10.2
3,900.0	1.13	295.69	3,899.3	6.7	-10.4	302.94	12.3
4,000.0	0.97	298.59	3,999.3	7.5	-12.0	302.18	14.2
4,100.0	0.75	310.15	4,099.3	8.4	-13.2	302.32	15.7
4,200.0	0.64	302.17	4,199.3	9.1	-14.2	302.61	16.9
4,300.0	0.66	307.12	4,299.3	9.7	-15.1	302.75	18.0
4,400.0	0.29	301.80	4,399.3	10.2	-15.8	302.87	18.8
4,500.0	0.33	299.86	4,499.3	10.5	-16.3	302.81	19.4
4,600.0	0.45	302.47	4,599.3	10.8	-16.9	302.76	20.0
4,700.0	0.40	297.20	4,699.3	11.2	-17.5	302.66	20.8
4,800.0	0.39	297.41	4,799.3	11.5	-18.1	302.49	21.5
4,900.0	0.23	330.00	4,899.3	11.9	-18.5	302.65	22.0
5,000.0	0.40	15.57	4,999.3	12.4	-18.5	303.75	22.3
5,100.0	0.50	25.15	5,099.3	13.1	-18.2	305.69	22.5
5,200.0	0.52	21.99	5,199.3	13.9	-17.9	307.89	22.7
5,300.0	0.57	44.65	5,299.3	14.7	-17.4	310.24	22.8
5,400.0	0.76	65.12	5,399.3	15.3	-16.4	313.04	22.5
5,500.0	0.28	81.88	5,499.3	15.6	-15.6	315.13	22.1
5,600.0	0.29	110.68	5,599.3	15.6	-15.1	315.92	21.7
5,700.0	0.33	109.76	5,699.3	15.4	-14.6	316.55	21.2
5,800.0	0.18	118.41	5,799.3	15.2	-14.2	317.05	20.8
5,900.0	0.23	125.95	5,899.3	15.0	-13.9	317.29	20.5
6,000.0	0.45	126.02	5,999.2	14.7	-13.4	317.63	19.9

Scientific Drilling International, Inc.
SDI Standard Survey Report

Company:	CHEVRON	Local Co-ordinate Reference:	Well Skelly Unit #960
Project:	Fren	TVD Reference:	WELL @ 0.0usft (Original Well Elev)
Site:	Eddy County, NM	MD Reference:	WELL @ 0.0usft (Original Well Elev)
Well:	Skelly Unit #960	North Reference:	Grid
Wellbore:	VH - Job #32K0810637	Survey Calculation Method:	Minimum Curvature
Design:	VH - Job #32K0810637	Database:	EDM-Regulatory

Survey							
Measured Depth (usft)	Inclination (°)	Azimuth (°)	True Vertical Depth	North/South (usft)	East/West (usft)	Closure Azimuth (°)	Closure Distance (usft)
6,100.0	0.57	124.43	6,099.2	14.2	-12.7	318.21	19.0
6,200.0	0.58	126.37	6,199.2	13.6	-11.9	318.92	18.0
6,300.0	0.27	123.49	6,299.2	13.2	-11.2	319.49	17.3
6,400.0	0.13	179.60	6,399.2	12.9	-11.1	319.46	17.0
6,444.0	0.08	328.19	6,443.2	12.9	-11.1	319.37	17.0



Scientific Drilling
Directional Drilling Operations

Project: Fren
Eddy County, NM
Well: Skelly Unit #960
Wellbore: VH - Job #32K0810637
Design: VH - Job #32K0810637




Azimuths to Grid North
True North: -0.26°
Magnetic North: 7.66°

Magnetic Field
Strength: 49099.1nT
Dip Angle: 60.73°
Date: 8/27/2010
Model: BGGM2010

WELL DETAILS: Skelly Unit #960
WELL @ 0.0usft (Original Well Elev)
Ground Level: 0.0

+N/-S	+E/-W	Northing	Easting	Latitude	Longitude	Slot
0.0	0.0	667318.15	649288.64	32° 50' 0.960 N	103° 50' 50.290 W	

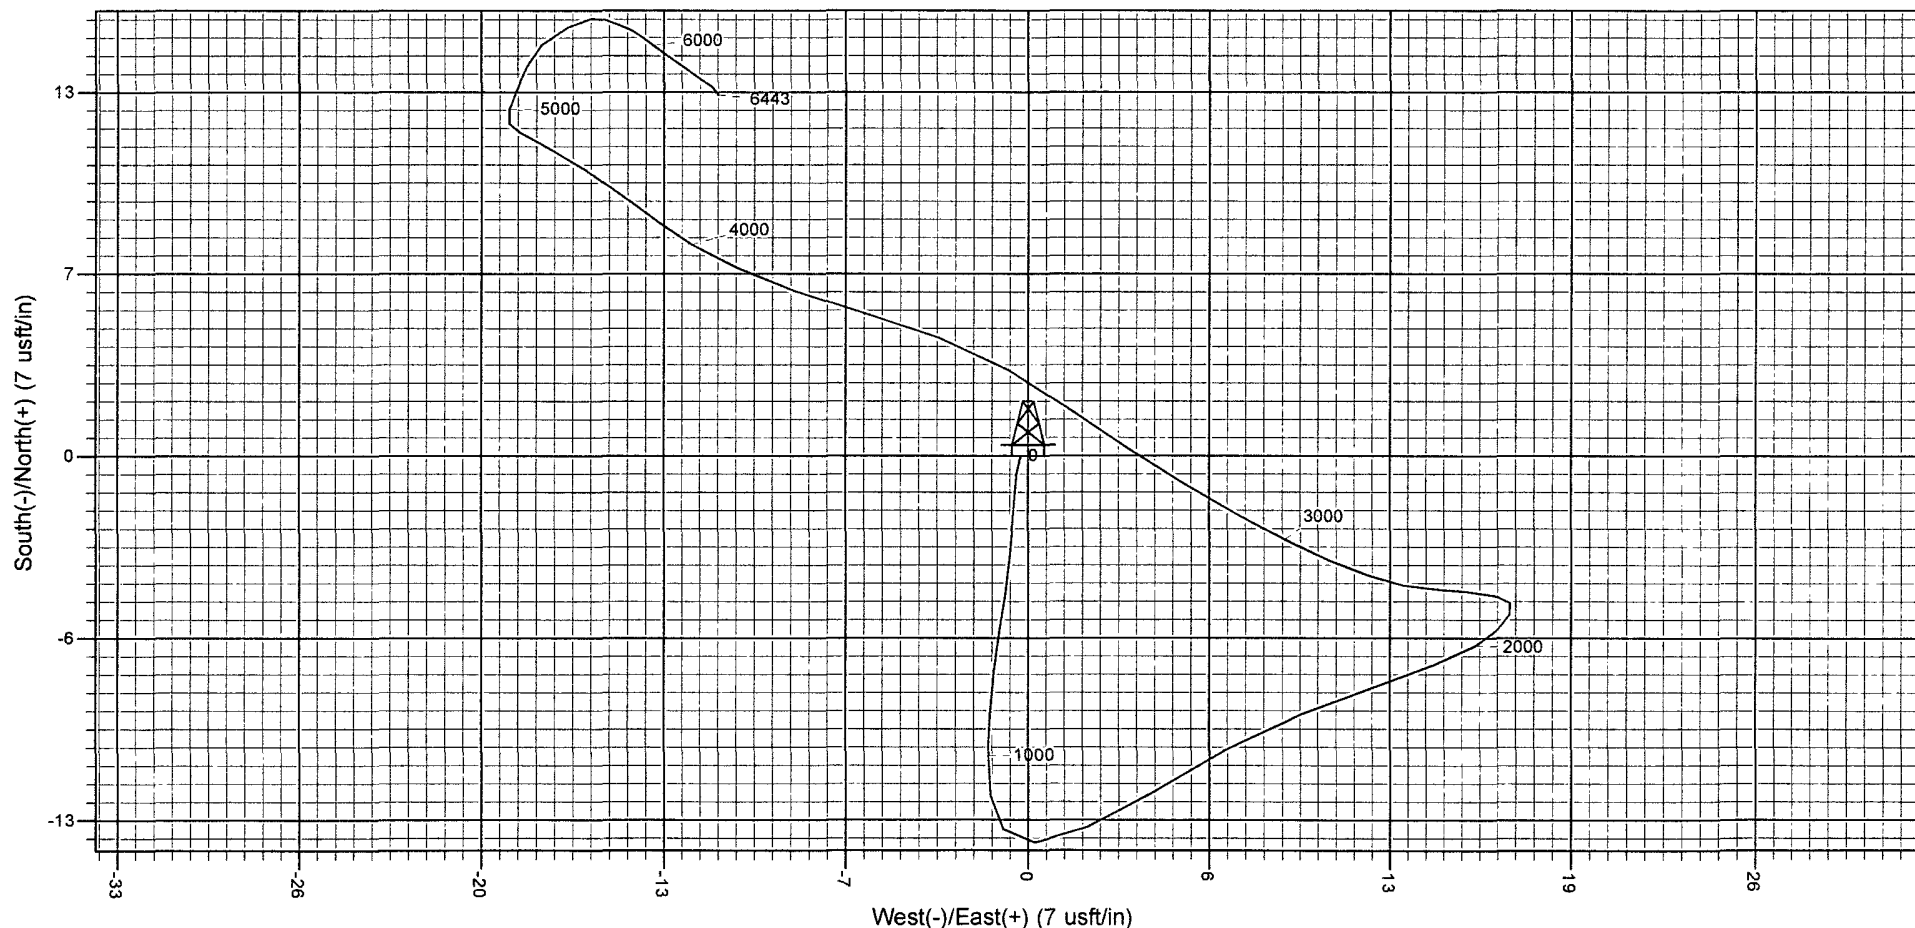

PROJECT DETAILS: Fren
Geodetic System: US State Plane 1927 (Exact solution)
Datum: NAD 1927 (NADCON CONUS)
Ellipsoid: Clarke 1866
Zone: New Mexico East 3001
System Datum: Mean Sea Level

SITE DETAILS: Eddy County, NM
Site Centre Latitude: 32° 50' 20.400 N
Longitude: 103° 51' 14.400 W
Positional Uncertainty: 0.0
Convergence: 0.26
Local North: Grid
