

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

Sundry Notices and Reports on Wells

2004 NOV 2 00 10 10

1. Type of Well

GAS

RECEIVED

CTO FARMINGTON

Lease Number

NMSF078138

6. If Indian, All. or
Tribe Name

7. Unit Agreement Name

2. Name of Operator

BURLINGTON

RESOURCES OIL & GAS COMPANY

3. Address & Phone No. of Operator

PO Box 4289, Farmington, NM 87499 (505) 326-8700

4. Location of Well, Footage, Sec., T, R, M

1475' FNL, 765' FWL, Sec. 23, T-30-N, R-11-W, NMP

Well Name & Number

Hartman Com 23 #1M

API Well No.

30-045-30839

Field and Pool

Otero Chacra/
Blanco Mesaverde

County and State

San Juan Co, NM

12. CHECK APPROPRIATE BOX TO INDICATE NATURE OF NOTICE, REPORT, OTHER DATA

Type of Submission

☒ Notice of Intent

☐ Subsequent Report

☐ Final Abandonment

Type of Action

☐ Abandonment

☐ Recompletion

☐ Plugging Back

☐ Casing Repair

☐ Altering Casing

☒ Other -

☐ Change of Plans

☐ New Construction

☐ Non-Routine Fracturing

☐ Water Shut off

☐ Conversion to Injection

13. Describe Proposed or Completed Operations

The location of the subject well has been moved from 1480' FNL, 660' FWL and the Dakota formation will not be drilled and completed in this wellbore. The well will produce as a Chacra/Mesaverde commingle. The well name of the subject well has been changed from Hartman Com 23 #1M to Hartman Com #6B. Attached is the revised C-102 plat and operations plan.

14. I hereby certify that the foregoing is true and correct.

Signed Tammy Jones Title Regulatory Specialist Date 11/1/04

(This space for Federal or State Office use)

APPROVED BY Tammy Jones Title EP/RAW Team Date 11/10/04

CONDITION OF APPROVAL, if any:

Title 18 U.S.C. Section 1001, makes it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

NMOCD

DISTRICT I
1625 N. French Dr., Hobbs, N.M. 88240

State of New Mexico
Energy, Minerals & Natural Resources Department

Form C-102
Revised August 15, 2000

DISTRICT II
811 South First, Artesia, N.M. 88210

DISTRICT III
1000 Rio Brazos Rd., Aztec, N.M. 87410

DISTRICT IV
2040 South Pacheco, Santa Fe, NM 87505

OIL CONSERVATION DIVISION
2040 South Pacheco
Santa Fe, NM 87505

Submit to Appropriate District Office
State Lease - 4 Copies
Fee Lease - 3 Copies

☐ AMENDED REPORT

WELL LOCATION AND ACREAGE DEDICATION PLAT

*API Number 30-045-30839	*Pool Code 82329/72319	*Pool Name Otero Chacra/Blanco Mesaverde
*Property Code 7098	*Property Name HARTMAN COM	*Well Number 6B
*GRID No. 14538	*Operator Name BURLINGTON RESOURCES OIL AND GAS COMPANY LP	*Elevation 5954'


¹⁰ Surface Location

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
E	23	30-N	11-W		1475'	NORTH	765'	WEST	SAN JUAN

¹¹ Bottom Hole Location If Different From Surface

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
*Dedicated Acres Cha: NW/159.77 MV: N/318.63			**Joint or Infill		**Consolidation Code		**Order No.		

NO ALLOWABLE WILL BE ASSIGNED TO THIS COMPLETION UNTIL ALL INTERESTS HAVE BEEN CONSOLIDATED
OR A NON-STANDARD UNIT HAS BEEN APPROVED BY THE DIVISION

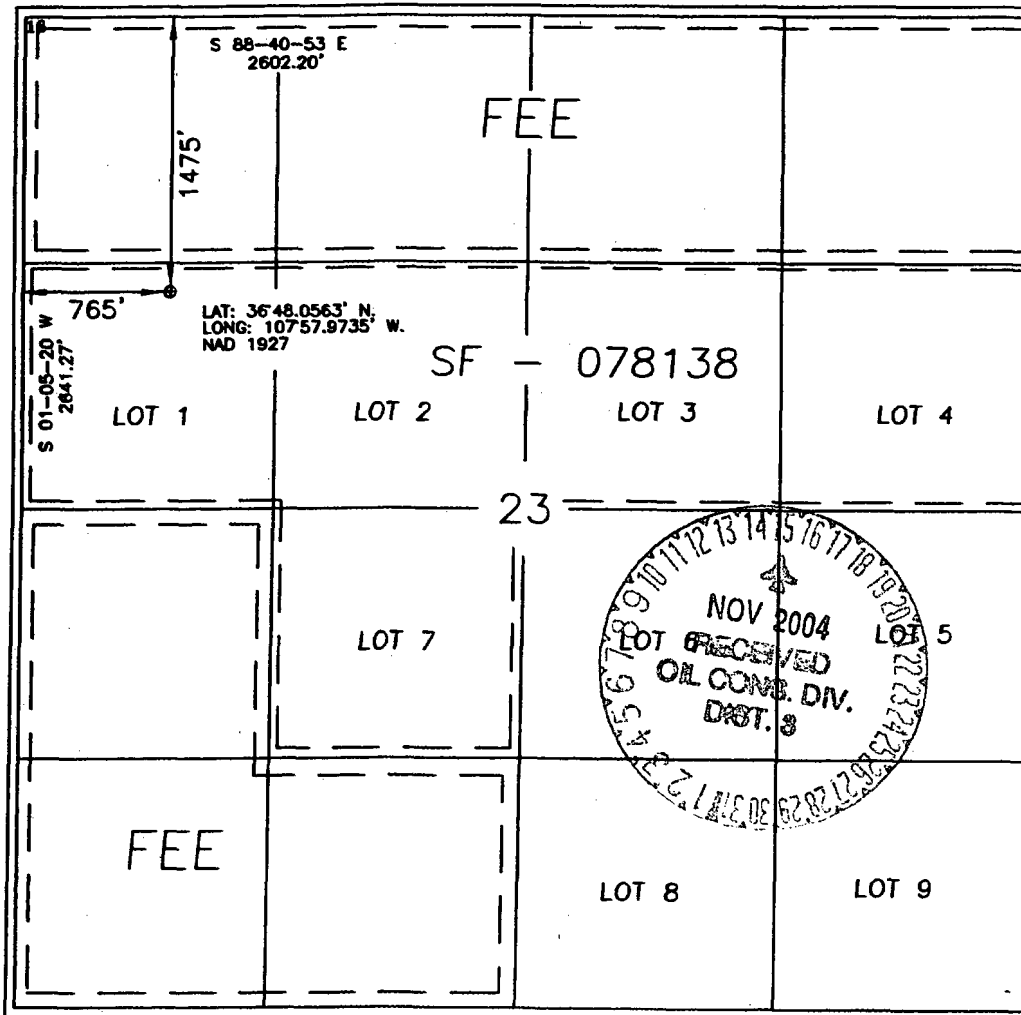

17 OPERATOR CERTIFICATION

I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief.

Tammy Jones
Signature
Tammy Jones
Printed Name
Regulatory Specialist
Title
10-29-04
Date

18 SURVEYOR CERTIFICATION

I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief.

Date of Survey 10-26-04

Signature and Seal of Professional Surveyor

Glen W. Russell
Signature
NEW MEXICO
15703
Certificate Number

OPERATIONS PLAN

Well Name: Hartman Com #6B
Surface Location: 1475' FNL, 765' FWL, Section 23, T-30-N, R-11-W
San Juan County, Colorado
Latitude 36° 48.0563'N, Longitude 107° 57.9735'W
Formation: Otero Chacra/Blanco Mesaverde
Elevation: 5954' GR

<u>Formation Tops:</u>	<u>Top</u>	<u>Bottom</u>	<u>Contents</u>
Surface	San Jose	1026'	aquifer
Ojo Alamo	1026'	1111'	aquifer
Kirtland	1111'	1836'	gas
Fruitland	1836'	2366'	gas
Pictured Cliffs	2366'	2528'	gas
Lewis	2528'	3126'	gas
Intermediate TD	2628'		
Huerfanito Bentonite	3126'	3386'	gas
Chacra	3386'	4036'	gas
Massive Cliff House	4036'	4171'	gas
Menefee	4171'	4681'	gas
Point Lookout	4681'		gas
Total Depth	5081'		

Logging Program:

Cased hole logging - Gamma Ray; Cement bond from surface to TD
Open hole logging - none
Mud Logs/Coring/DST - none

Mud Program:

<u>Interval- MD</u>	<u>Type</u>	<u>Weight</u>	<u>Vis.</u>	<u>Fluid Loss</u>
0- 200'	Spud	8.4-9.0	40-50	no control
200- 2628'	LSND	8.4-9.0	30-60	no control
2628- 5081'	Air/Mist	n/a	n/a	n/a

Pit levels will be visually monitored to detect gain or loss of fluid control.

Casing Program (as listed, the equivalent, or better):

<u>Hole Size</u>	<u>Measured Depth</u>	<u>Csg Size</u>	<u>Weight</u>	<u>Grade</u>
12 1/4"	0' - 200'	9 5/8"	32.3#	H-40
8 3/4"	0' - 2628'	7"	20.0/23.0#	J-55
6 1/4"	2528' - 5081'	4 1/2"	10.5#	J-55

Tubing Program: 0' - 5081' 2 3/8" 4.7# J-55

BOP Specifications, Wellhead and Tests:

Surface to Intermediate TD -

11" 2000 psi minimum double gate BOP stack (Reference Figure #1).
After nipple-up prior to drilling out surface casing, rams and casing will be tested to 600 psi for 30 minutes.

Intermediate TD to Total Depth -

11" 2000 psi minimum double gate BOP stack (Reference Figure #1).
After nipple-up prior to drilling out intermediate casing, rams and casing will be tested to 1500 psi for 30 minutes.

BOP Specifications, Wellhead and Tests (cont'd):Surface to Total Depth -

2" nominal, 2000 psi minimum choke manifold (Reference Figure #3).

Completion Operations -

7 1/16" 2000 psi double gate BOP stack (Reference Figure #2).

After nipple-up prior to completion, pipe rams, casing and liner top will be tested to 2000 psi for 15 minutes.

Wellhead -

9 5/8" x 7" x 2 3/8" x 2000 psi tree assembly.

General -

- Pipe rams will be actuated once each day and blind rams will be actuated once each trip to test proper functioning.
- An upper kelly cock valve with handle available and drill string valves to fit each drill string will be available on the rig floors at all times.
- BOP pit level drill will be conducted weekly for each drill crew.
- All BOP tests & drills will be recorded in daily drilling reports.
- Blind and pipe rams will be equipped with extension hand wheels.

Cementing:9 5/8" surface casing -

Pre-Set Drilled Cement with 39 sx Type I, II cement with 20% flyash mixed at 14.5 ppg, 1.61 cu ft per sack yield. (63 cu ft of slurry, bring cement to surface) Wait on cement for 24 hours for pre-set holes before pressure testing or drilling out from under surface.

Conventionally Drilled

Cement with 147 sx Type III cement with 0.25 pps Celloflake, 2% CaCl. (188 cu ft of slurry, 200% excess, bring cement to surface) Wait on cement for 8 hrs for conventionally set holes before pressure testing or drilling out from under surface. Wait on cement appropriate time until cement achieves 250 psi compressive strength at 60 degrees F. prior to nipple up of BOPE. Wait on cement for 8 hrs for conventionally set holes before pressure testing or drilling out from under surface. Test casing to 600 psi for 30 minutes.

Saw tooth guide shoe on bottom. Bowspring centralizers will be run in accordance with Onshore Order #2.

7" intermediate casing -

Lead w/215 sx Premium Lite with 3% calcium chloride, 0.25 pps celloflake, 5 pps LCM-1, 0.4% fluid loss, 0.4% sodium metasilicate. Tail with 90 sx Type III cmt w/1% calcium chloride, 0.25 pps celloflake, 0.2% fluid loss (582 cu.ft. of slurry, 50% excess to circulate to surface). WOC minimum of 8 hours before drilling out intermediate casing. If cement does not circulate to surface, a CBL or temp survey will be run to determine TOC. Test casing to 1500 psi for 30 minutes.

7" intermediate casing alternative two stage:

Stage collar set 300' above the top of the Fruitland. First stage: Lead with 57 sacks Premium Lite cmt w/3% calcium chloride, 0.25 pps Celloflake, 0.4% fluid loss, 5 pps LCM-1, 0.4% sodium metasilicate. Tail with 90 sacks with Type III cement with 1% calcium chloride, 0.25 pps Celloflake, 0.2% fluid loss. Second stage: cement with 158 sacks with Premium Lite cement with 3% calcium chloride, 0.25 pps Celloflake, 5 pps LCM-1, 0.4% fluid loss, 0.4% sodium metasilicate (582 cu. ft.-50% excess to circulate to surface).

Cement nose guide shoe on bottom with float collar spaced on top of shoe joint. Bowspring centralizers spaced every fourth joint off bottom, to the base of the Ojo Alamo at 1111'. Two turbolating centralizers at the base of the Ojo Alamo at 1111'. Bowspring centralizers spaced every fourth joint from the base of the Ojo Alamo to the base of the surface casing.

4 1/2" Production Liner -

Pump 171 sxs Premium Lite HS FM w/0.25 pps celloflake, 0.3% CD-32, 6.25 pps LCM-1, 1% fluid loss, 6% gel, 7 pps CSE (339 cu.ft., 30% excess to circulate liner). WOC a minimum of 18 hrs prior to completing.

Note: If open hole logs are run, cement volumes will be based on 25% excess over caliper volumes.

Cement nose guide shoe on bottom with float collar spaced on top of shoe joint. The liner hanger will have a rubber packoff.

- If hole conditions permit, an adequate water spacer will be pumped ahead of each cement job to prevent cement/ mud contamination or cement hydration.

Special Drilling Operations (Air/Mist Drilling):

The following equipment will be operational while gas/mist drilling:

- An anchored blooie line will be utilized to discharge all cuttings and circulating medium to the blow pit a minimum of 100' from the wellhead.
- The blooie line will be equipped with an automatic igniter or pilot light.
- Compressors will be located a minimum of 100' from the wellhead in the opposite direction from the blooie line.
- Engines will have spark arresters or water cooled exhaust.
- The rotating head will be properly lubricated and maintained.
- A float valve will be utilized above the bit.
- Mud circulating equipment, water, and mud materials will be sufficient to maintain control of the well.

Additional Information:

- The Chacra and Mesa Verde formations will be completed and commingled.
- No abnormal temperatures or hazards are anticipated.
- Anticipated pore pressures are as follows:

Fruitland Coal	150 psi
Pictured Cliffs	260 psi
Mesa Verde	375 psi
- Sufficient LCM will be added to the mud system to maintain well control, if lost circulation is encountered below the top of the Pictured Cliffs.
- The northwest quarter of Section 23 is dedicated to the Chacra and the north half of Section 23 is dedicated to the Mesaverde in this well.
- This gas is dedicated.

Sean Corrigan
Drilling Engineer

November 1, 2004
Date
