

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
OMB No. 1004-0136
Expires November 30, 2000


APPLICATION FOR PERMIT TO DRILL OR REENTER

1a. Type of Work: <input checked="" type="checkbox"/> DRILL <input type="checkbox"/> REENTER		5. Lease Serial No. SF-078277
1b. Type of Well: <input type="checkbox"/> Oil Well <input checked="" type="checkbox"/> Gas Well <input type="checkbox"/> Other <input type="checkbox"/> Single Zone <input checked="" type="checkbox"/> Multiple Zone		6. If Indian, Allottee or Tribe Name
2. Name of Operator CONOCOPHILLIPS COMPANY		7. If Unit or CA Agreement, Name and No.
Contact: VICKI WESTBY E-Mail: VICKI.R.WESTBY@CONOCOPHILLIPS.COM		8. Lease Name and Well No. SAN JUAN 29-5 UNIT 20C
3a. Address 4001 PENBROOK ODESSA, TX 79762	3b. Phone No. (include area code) Ph: 915-368-1352	9. API Well No. 3003929334
4. Location of Well (Report location clearly and in accordance with any State requirements*) At surface NENW 295FNL 2120FWL At proposed prod. zone NENW 295FNL 2120FWL		10. Field and Pool, or Exploratory BLANCO MESAVERDE
14. Distance in miles and direction from nearest town or post office*		11. Sec., T., R., M., or Blk. and Survey or Area Sec 7 T29N R5W Mer NMP
15. Distance from proposed location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any)	16. No. of Acres in Lease 114.73	12. County or Parish RIO ARRIBA
18. Distance from proposed location to nearest well, drilling, completed, applied for, on this lease, ft.	19. Proposed Depth 6022 MD	13. State NM
21. Elevations (Show whether DF, KB, RT, GL, etc.) 6544	22. Approximate date work will start	17. Spacing Unit dedicated to this well 320 w/
20. BLM/BIA Bond No. on file		23. Estimated duration

24. Attachments

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, shall be attached to this form:

1. Well plat certified by a registered surveyor.
2. A Drilling Plan.
3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO shall be filed with the appropriate Forest Service Office).
4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).
5. Operator certification
6. Such other site specific information and/or plans as may be required by the authorized officer.

25. Signature (Electronic Submission)	Name (Printed/Typed) VICKI WESTBY Ph: 915-368-1352	Date 11/03/2004
Title AGENT		
Approved by (Signature) 	Name (Printed/Typed) Office FFO	Date 5-18-05

Application approval does not warrant or certify the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

Additional Operator Remarks (see next page)

Electronic Submission #50662 verified by the BLM Well Information System
For CONOCOPHILLIPS COMPANY, sent to the Farmington

DRILLING OPERATIONS AUTHORIZED ARE
SUBJECT TO COMPLIANCE WITH ATTACHED
"GENERAL REQUIREMENTS".

This action is subject to technical and
procedural review pursuant to 43 CFR 3165.3
and appeal pursuant to 43 CFR 3165.4

** OPERATOR-SUBMITTED ** OPERATOR-SUBMITTED ** OPERATOR-SUBMITTED **

NMCCD

District I
PO Box 1980, Hobbs, NM 88241-1980

District II
PO Drawer DD, Artesia, NM 88211-0719

District III
1000 Rio Brazos Rd., Aztec, NM 87410

District IV
PO Box 2088, Santa Fe, NM 87504-2088

State of New Mexico
Energy, Minerals & Natural Resources Department

OIL CONSERVATION DIVISION
PO Box 2088
Santa Fe, NM 87504-2088

Form C-102
Revised February 21, 1994
Instructions on back
Submit to Appropriate District Office
State Lease - 4 Copies
Fee Lease - 3 Copies

☐ AMENDED REPORT

WELL LOCATION AND ACREAGE DEDICATION PLAT

*API Number 30-039-29334		*Pool Code 72319	*Pool Name BLANCO MESAVERDE
*Property Code 31325	*Property Name SAN JUAN 29-5 UNIT		*Well Number 20C
*GRID No. 217817	*Operator Name CONOCOPHILLIPS COMPANY		*Elevation 6544'


¹⁰ Surface Location

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
C	7	29N	5W		295	NORTH	2120	WEST	RIO ARriba

¹¹ Bottom Hole Location If Different From Surface

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
¹² Dedicated Acres 32.0 Acres - W/2					¹³ Joint or Infill	¹⁴ Consolidation Code	¹⁵ Order No.		

NO ALLOWABLE WILL BE ASSIGNED TO THIS COMPLETION UNTIL ALL INTERESTS HAVE BEEN CONSOLIDATED
OR A NON-STANDARD UNIT HAS BEEN APPROVED BY THE DIVISION

<div><p>¹⁶</p><p>2120' 295' 5276.04'</p><p>LAT: 36°44.7942' N LONG: 107°23.9968' W DATUM: NAD27</p><p>LEASE SF-078277</p><p>LOT 2 LOT 1</p><p>TRACT 37</p><p>LOT 3</p><p>LOT 4</p><p>5280.00'</p><p>5282.64'</p></div>	<div><p>¹⁷ OPERATOR CERTIFICATION</p><p>I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief</p><p><i>Vicki Westby (pj)</i></p><p>Signature Vicki R. Westby</p><p>Printed Name Staff Agent</p><p>Title 11/3/04</p><p>Date</p></div>
	<div><p>¹⁸ SURVEYOR CERTIFICATION</p><p>I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief</p><p>Date of Survey: AUGUST 3, 2004</p><p>Signature and Seal of Professional Surveyor</p><p></p><p>JASON C. EDWARDS</p><p>Certificate Number 15269</p></div>

Submit 3 Copies To Appropriate District Office

District I

1625 N. French Dr., Hobbs, NM 88240

District II

1301 W. Grand Ave., Artesia, NM 88210

District III

1000 Rio Brazos Rd., Aztec, NM 87410

District IV

1220 S. St. Francis Dr., Santa Fe, NM 87505

State of New Mexico
Energy, Minerals and Natural Resources

OIL CONSERVATION DIVISION

1220 South St. Francis Dr.
Santa Fe, NM 87505

Form C-103

May 27, 2004

WELL API NO.

5. Indicate Type of Lease

STATE ☐ FEE ☐

6. State Oil & Gas Lease No.

7. Lease Name or Unit Agreement Name

SAN JUAN 29-5 UNIT

8. Well Number 20C

9. OGRID Number 217817

10. Pool name or Wildcat

BLANCO MESAVERDE

SUNDRY NOTICES AND REPORTS ON WELLS

(DO NOT USE THIS FORM FOR PROPOSALS TO DRILL OR TO DEEPEN OR PLUG BACK TO A DIFFERENT RESERVOIR. USE "APPLICATION FOR PERMIT" (FORM C-101) FOR SUCH PROPOSALS)

1. Type of Well: Oil Well ☐ Gas Well ☒ Other ☐

2. Name of Operator

ConocoPhillips Company

3. Address of Operator

4001 Penbrook, Odessa, TX 79762

4. Well Location

Unit Letter C 295 feet from the NORTH line and 2120 feet from the WEST line
Section 7 Township 29N Range 5W NMPM RIO ARRIBA County

11. Elevation (Show whether DR, RKB, RT, GR, etc.)
6544 GL

Pit or Below-grade Tank Application ☒ Closure ☐

Pit type DRILL Depth to Groundwater 40' Distance from nearest fresh water well <0.5 MILE Distance from nearest surface water 450'

Liner Thickness:

mil

Below-Grade Tank: Volume

bbbs; Construction Material

12. Check Appropriate Box to Indicate Nature of Notice, Report or Other Data

NOTICE OF INTENTION TO:

PERFORM REMEDIAL WORK ☐ PLUG AND ABANDON ☐
TEMPORARILY ABANDON ☐ CHANGE PLANS ☐
PULL OR ALTER CASING ☐ MULTIPLE COMPL ☐

OTHER: ☐

SUBSEQUENT REPORT OF:

REMEDIAL WORK ☐ ALTERING CASING ☐
COMMENCE DRILLING OPNS. ☐ P AND A ☐
CASING/CEMENT JOB ☐

OTHER: ☐

13. Describe proposed or completed operations. (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work). SEE RULE 11.03. For Multiple Completions: Attach wellbore diagram of proposed completion or recompletion.

ConocoPhillips' Generic Pit Plan is on file at the NMOCD in Aztec, NM. See the attached diagram that details the location of the pit in reference to the proposed wellhead. The drill pit will be lined. The drill pit will be closed after the well has been completed. The solids left after the water has been disposed of will be sampled and NMOCD approval will be obtained prior to closure of this pit.

I hereby certify that the information above is true and complete to the best of my knowledge and belief. I further certify that any pit or below-grade tank has been/will be constructed or closed according to NMOCD guidelines ☐, a general permit ☐ or an (attached) alternative OCD-approved plan ☐

SIGNATURE Vicki Westby

TITLE Staff Agent

DATE 11/03/04

Type or print name

E-mail address:

Telephone No.

For State Use Only

APPROVED BY:

TITLE


DEPUTY OIL & GAS INSPECTOR, DIST. 29

DATE

MAY 20 2005

Conditions of Approval (if any):




CONOCOPHILLIPS COMPANY SAN JUAN 29-5 UNIT #20C
295' FNL & 2120' FWL, SECTION 7, T29N, R5W, NMPM
RIO ARriba COUNTY, NEW MEXICO ELEVATION: 6544'

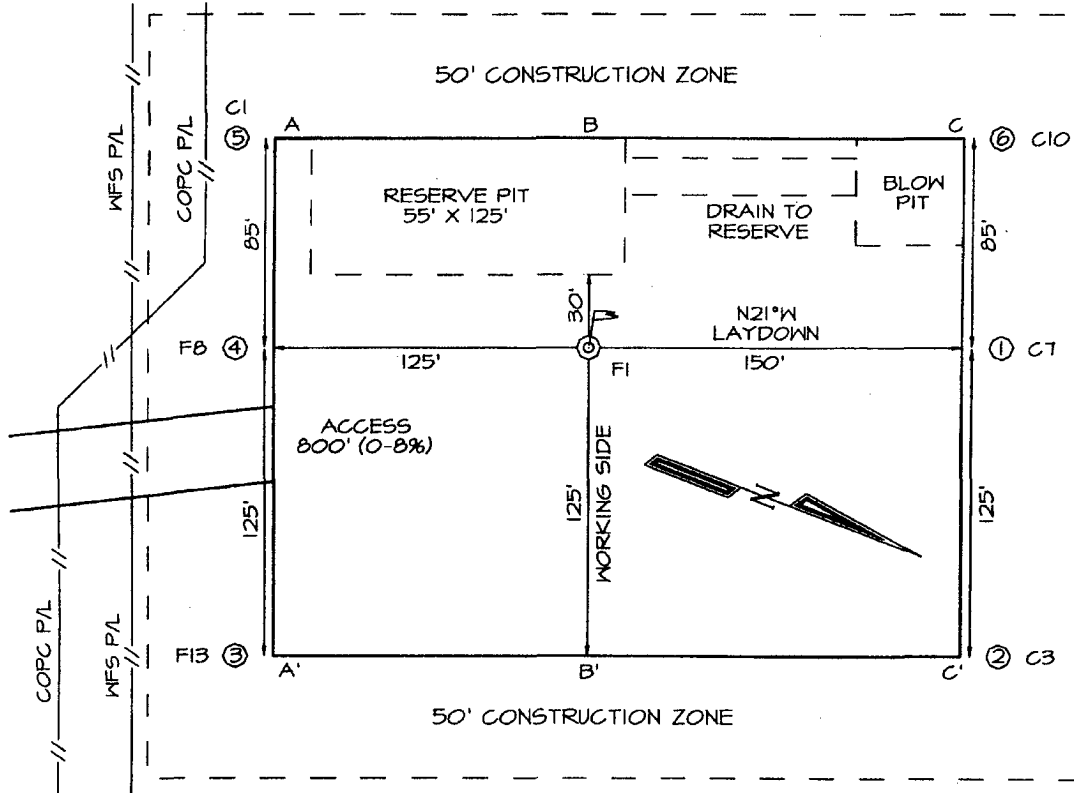

LATITUDE: 36.74657° N
LONGITUDE: 107.39995° W
 DATUM: NAD1927

PLAT NOTE:

SURFACE OWNER
 Bureau of Land
 Management

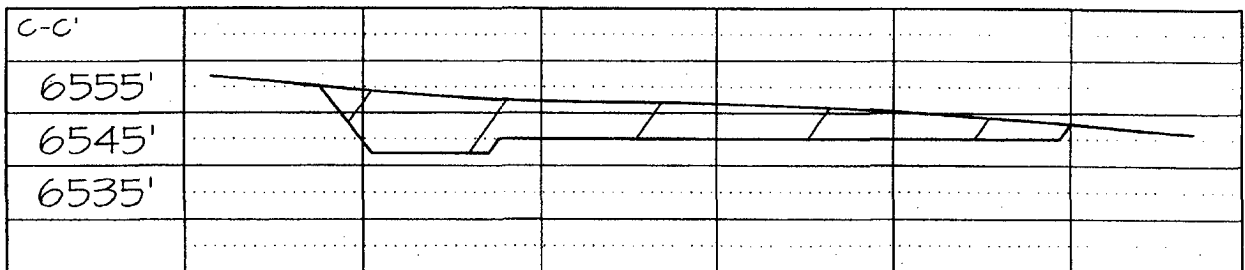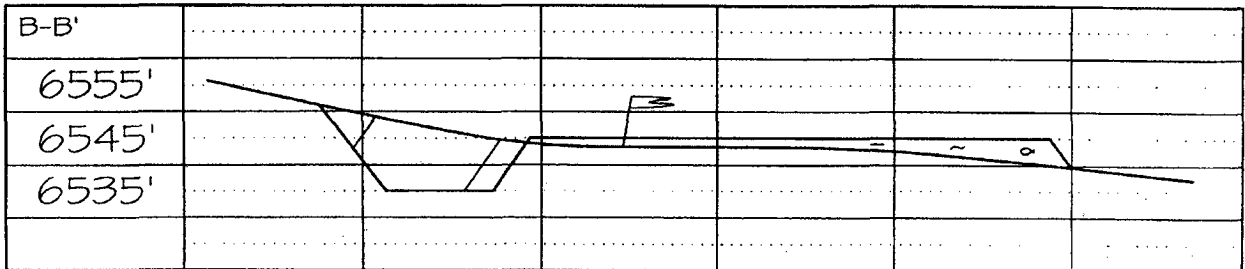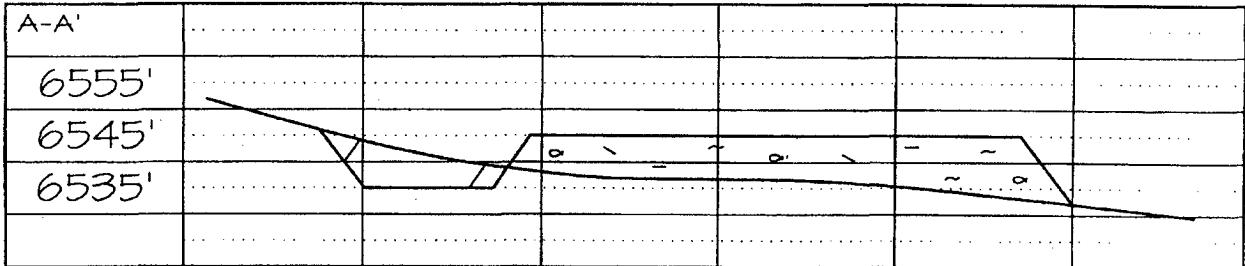



San Juan Business Unit

PROJECT PROPOSAL - New Drill / Sidetrack

SAN JUAN 29-5 20C

Lease:		AFE #:		AFE \$:	
Field Name: hPHILLIPS 29-5		Rig:	State: NM	County: RIO ARRIBA	API #:
Geoscientist: Glaser, Terry J		Phone: (832)486-2332	Prod. Engineer: Moody, Craig E.		Phone: 486-2334
Res. Engineer: Johnson, Tom B.		Phone: (832)-486-2347	Proj. Field Lead: Fransen, Eric E.		Phone:
Primary Objective (Zones):					
Zone	Zone Name				
RON	BLANCO MESAVERDE (PRORATED GAS)				

Location: Surface					Straight Hole	
Latitude: 36.75	Longitude: -107.40	X:	Y:	Section: 7	Range: 5W	
Footage X: 2120 FWL	Footage Y: 295 FNL	Elevation: 6544	(FT)	Township: 29N		
Tolerance:						
Location Type: Summer Only		Start Date (Est.):		Completion Date:		
Formation Data: Assume KB = 6557		Units = FT		Date In Operation:		
Formation Call & Casing Points	Depth (TVD in Ft)	SS (Ft)	Depletion (Yes/No)	BHP (PSIG)	BHT	
SURFACE CSG	213	6344	<input type="checkbox"/>			
NCMT	1397	5160	<input type="checkbox"/>			
OJAM	2597	3960	<input type="checkbox"/>			
KRLD	2797	3760	<input type="checkbox"/>			
FRLD	3197	3360	<input type="checkbox"/>			
PCCF	3497	3060	<input type="checkbox"/>			
LEWS	3697	2860	<input type="checkbox"/>			
Intermediate Casing	3797	2760	<input type="checkbox"/>			
CHRA	4507	2050	<input type="checkbox"/>			
CLFH	5307	1250	<input type="checkbox"/>	575		
MENF	5397	1160	<input type="checkbox"/>			
PTLK	5672	885	<input type="checkbox"/>			
MNCS	5922	635	<input type="checkbox"/>			
Total Depth	6022	535	<input type="checkbox"/>			
Remarks						
Severe Lost Circulation is possible. 12 1/4" Hole. 9 5/8" 32.3 ppf, H-40, STC casing. Circulate cement to surface.						
Possible water flows.						
Possible gas.						
8 3/4" Hole. 7", 20 ppf, J-55, STC Casing. Circulate cement to surface.						
Gas; possibly wet						
Gas.						
Gas.						
6 1/4" Hole. 4 1/2", 10.5 ppf, J-55, STC casing. Circulate cement a minimum of 100' inside the previous casing string. No open hole logs. Cased hole TDT with GR to surface.						

Reference Wells:		
Reference Type	Well Name	Comments

Logging Program:	
Intermediate Logs:	<input type="checkbox"/> Log only if show <input type="checkbox"/> GR/ILD <input type="checkbox"/> Triple Combo
TD Logs:	<input type="checkbox"/> Triple Combo <input type="checkbox"/> Dipmeter <input type="checkbox"/> RFT <input type="checkbox"/> Sonic <input type="checkbox"/> VSP <input checked="" type="checkbox"/> TDT
Additional Information:	

Comments: General/Work Description -

Drilling Mud Program:

Surface: spud mud

Intermediate: fresh water mud with bentonite and polymer as needed

Below Intermediate: air/mist drilling media with foamer, polymer, & corrosion inhibitor as needed

Printed on: 11/3/2004 8:21:54 AM

San Juan 29-5 # 20C

SURFACE CASING :

Drill Bit Diameter	12.25"	
Casing Outside Diameter	9.625"	Casing Inside Diam. 9.001"
Casing Weight	32.3	ppf
Casing Grade	H-40	
Shoe Depth	230'	
Cement Yield	123	cuft/sk
Excess Cement	125	%
Cement Required	147	sx

SHOE 230', 9.625", 32.3 ppf, H-40 STC

INTERMEDIATE CASING :

Drill Bit Diameter	8.75"	
Casing Outside Diameter	7"	Casing Inside Diam. 6.456"
Casing Weight	20	ppf
Casing Grade	J-55	
Shoe Depth	3797'	
Lead Cement Yield	288	cuft/sk
Lead Cement Excess	150	%
Tail Cement Length	759.4'	
Tail Cement Yield	133	cuft/sk
Tail Cement Excess	150	%
Lead Cement Required	380	sx
Tail Cement Required	222	sx

SHOE 3797', 7", 20 ppf, J-55 STC

PRODUCTION CASING :

Drill Bit Diameter	6.25"	
Casing Outside Diameter	4.5"	Casing Inside Diam. 4.000"
Casing Weight	10.5	ppf
Casing Grade	J-55	
Top of Cement	3597'	200' inside intermediate casing
Shoe Depth	6022'	
Cement Yield	145	cuft/sk
Cement Excess	50	%
Cement Required	254	sx

SHOE 6022', 4.5", 10.5 ppf, J-55 STC

SAN JUAN 29-5 #20C

9-5/8" Surface Casing		
Cement Recipe	Class C Standard Cement	
	+ 3% Calcium Chloride	
	+0.25 lb/sx Flocele	
Cement Volume	147	sx
Cement Yield	1.21	cuft/sx
Slurry Volume	179.8	cuft
	32.0	bbls
Cement Density	15.6	ppg
Water Required	5.29	gal/sx

7" Intermediate Casing		
Lead Slurry		
Cement Recipe	Standard Cement	
	+ 3% Econolite (extender)	
	+ 10 lb/sx Pheno Seal	
Cement Required	380	sx
Cement Yield	2.88	cuft/sx
Slurry Volume	1094.0	cuft
	194.9	bbls
Cement Density	11.5	ppg
Water Required	16.91	gal/sx

7" Intermediate Casing		
Tail Slurry		
Cement Slurry	50 / 50 POZ:Standard Cement	
	+ 2% Bentonite	
	+ 6 lb/sx Pheno Seal	
Cement Required	222	sx
Cement Yield	1.33	cuft/sx
Slurry Volume	295.1	cuft
	52.6	bbls
Cement Density	13.5	ppg
Water Required	5.52	gal/sx

4-1/2" Production Casing		
Cement Recipe	50 / 50 POZ:Standard Cement	
	+ 3% Bentonite	
	+ 3.5 lb/sx PhenoSeal	
	+ 0.2% CFR-3 Friction Reducer	
	+ 0.1% HR-5 Retarder	
	+ 0.8% Halad-9 Fluid Loss Additive	
Cement Quantity	252	sx
Cement Yield	1.45	cuft/sx
Cement Volume	366.0	cuft
	65.2	
Cement Density	13.1	ppg
Water Required	6.47	gal/sx

9-5/8" Surface Casing		
Cement Recipe	Class G Standard Cement	
	+ 2% S001 Calcium Chloride	
	+0.25 lb/sx D029 Cellophane Flakes	
Cement Volume	148	sx
Cement Yield	1.16	cuft/sx
Cement Volume	171.5	cuft
Cement Density	15.8	ppg
Water Required	4.983	gal/sx


7" Intermediate Casing		
Lead Slurry		
Cement Recipe	Class G Standard Cement	
	+0.25 lb/sx D029 Cellophane Flakes	
	+ 3% D079 Extender	
	+ 0.20% D046 Antifoam	
	+ 10 lb/sx Pheno Seal	
Cement Required	403	sx
Cement Yield	2.72	cuft/sx
Slurry Volume	1095.3	cuft
	195.1	bbls
Cement Density	11.7	ppg
Water Required	15.74	gal/sx

7" Intermediate Casing		
Tail Slurry		
Cement Slurry	50 / 50 POZ:Standard Cement	
	+0.25 lb/sx D029 Cellophane Flakes	
	+ 2% D020 Bentonite	
	+ 1.5 lb/sx D024 Gilsonite Extender	
	+ 2% S001 Calcium Chloride	
	+ 0.10% D046 Antifoam	
	+ 6 lb/sx Pheno Seal	
Cement Required	225	sx
Cement Yield	1.31	cuft/sx
Slurry Volume	294.9	cuft
	52.5	bbls
Cement Density	13.5	ppg
Water Required	5.317	gal/sx


4-1/2" Production Casing		
Cement Recipe	50 / 50 POZ:Class G Standard Cement	
	+0.25 lb/sx D029 Cellophane Flakes	
	+ 3% D020 Bentonite	
	+ 1.0 lb/sx D024 Gilsonite Extender	
	+ 0.25% D167 Fluid Loss	
	+ 0.15% D065 Dispersant	
	+ 0.1% D800 Retarder	
	+ 0.1% D046 Antifoamer	
	+ 3.5 lb/sx PhenoSeal	
Cement Quantity	254	sx
Cement Yield	1.44	cuft/sx
Cement Volume	365.8	cuft
	65.2	
Cement Density	13	ppg
Water Required	6.43	gal/sx

BLOWOUT PREVENTER ARRANGEMENT & PROGRAM

For Drilling to Intermediate Casing Point & Setting 7" Intermediate Casing

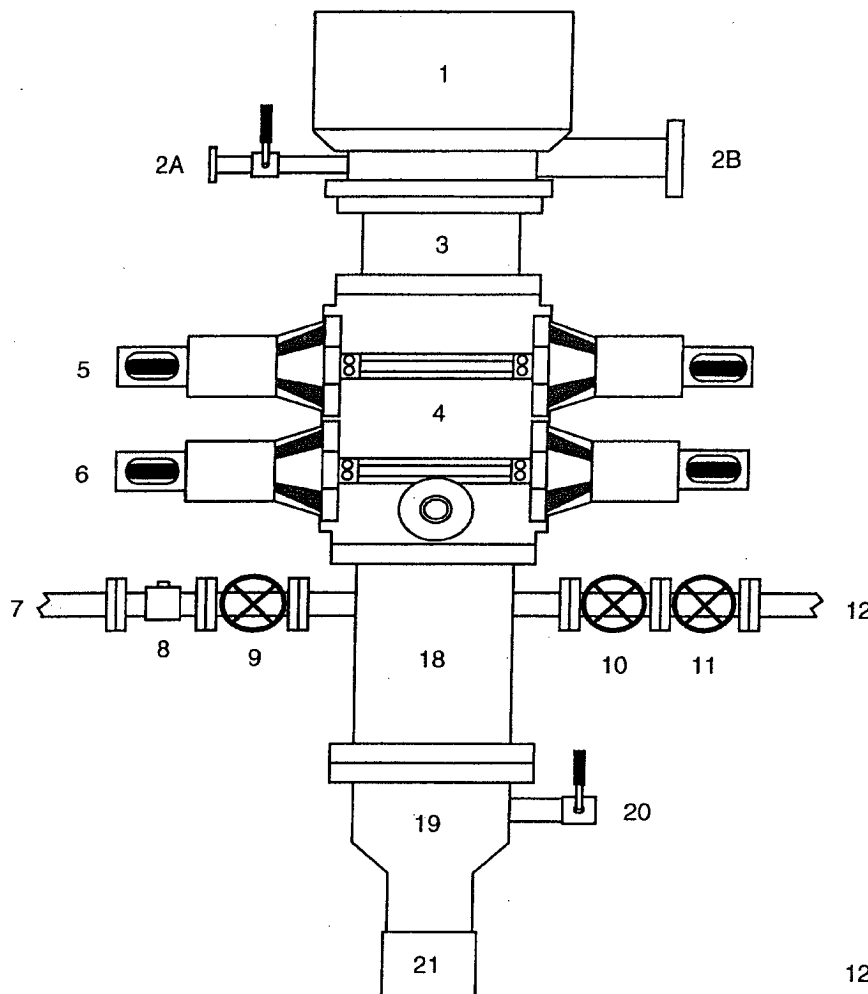

1. Rotating Head
- 2A. Fill-up Line & valve
- 2B. Flowline
3. Spacer Spool
4. Double Ram BOP (11", 3000 psi)
5. Pipe Rams
6. Blind Rams
7. Kill Line
8. Kill Line Check Valve
9. Kill Line Valve
10. Inner Choke Line Valve (3")
11. Outer Choke Line Valve (3")
12. Choke Line (3")
13. Variable Choke
14. Choke Line Valve (2")
15. Panic Line Valve (3")
16. Choke Manifold Pressure Gauge
17. Choke Line (2")
18. Mud Cross Spacer Spool
19. Casing Head "A" Section
20. Casing Head "A" Section 2" Valve
21. 9 5/8" Casing Collar

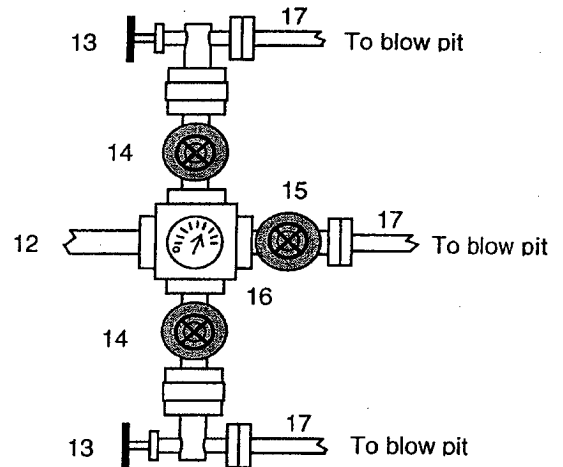

A 12-1/4" hole will be drilled to approximately 220' and the 9-5/8" surface casing will be run and cemented. The Casing Head "A" Section will be screwed onto the 9-5/8" surface casing stub. The BOP will be installed on the Casing Head "A" Section. A test plug will be set in the wellhead and the pipe rams and choke manifold will be tested to 200 psi to 300 psi (low pressure test) for 10 minutes and to 1000 psi (high pressure test) for 10 minutes. Then the test plug will be removed, and the **9-5/8" casing will be pressure tested** against closed blind rams to 200 psi to 300 psi for 10 minutes and **to 1000 psi for 30 minutes** (this value is one 44% of the minimum internal yield pressure of the 9-5/8" casing). (Note: per regulatory requirements we will wait on cement at least 8 hrs after placement before testing the 9-5/8" surface casing). Then an 8-3/4" hole will be drilled to intermediate casing point and 7" intermediate casing will be run and cemented.


In addition to the equipment in the above diagram the following equipment will comprise the BOP system:

1. Upper Kelly cock Valve with handle
2. Stab-in TIW valve for all drillstrings in use


Revision Date: September 1, 2004

BLOWOUT PREVENTER ARRANGEMENT & PROGRAM

For Drilling to TD and Setting 4.5 inch Casing

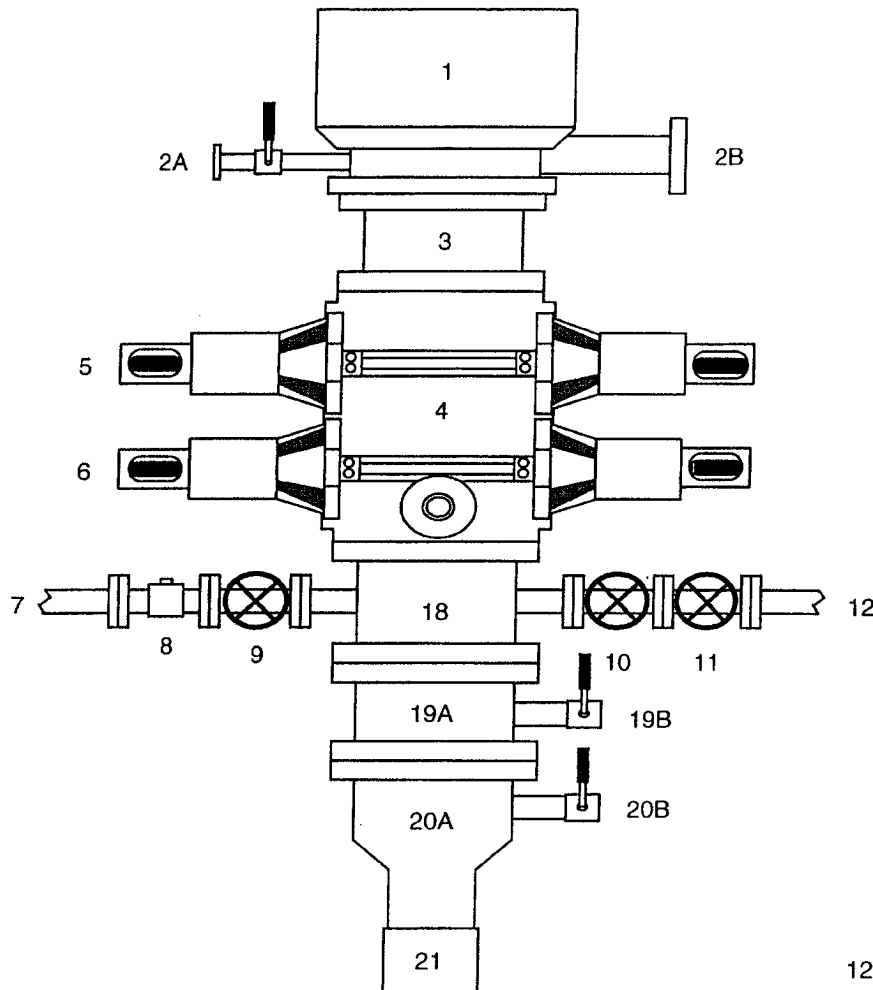

1. Rotating Head
- 2A. Fill-up Line & valve
- 2B. Blooie Line (for Air Drilling)
3. Spacer Spool
4. Double Ram BOP (11", 3000 psi)
5. Pipe Rams
6. Blind Rams
7. Kill Line
8. Kill Line Check Valve
9. Kill Line Valve
10. Inner Choke Line Valve (3")
11. Outer Choke Line Valve (3")
12. Choke Line (3")
13. Variable Choke
14. Choke Line Valve (2")
15. Panic Line Valve (3")
16. Choke Manifold Pressure Gauge
17. Choke Line (2")
18. Mud Cross Spacer Spool
- 19A Csg Spool "B" Section (11", 3M)
- 19B "B" Section Csg Valve (2", 3M)
- 20A Csg Head "A" Section (11", 3M)
- 20B "A" Section Csg Valve (2", 3M)
21. 9 5/8" Casing Collar

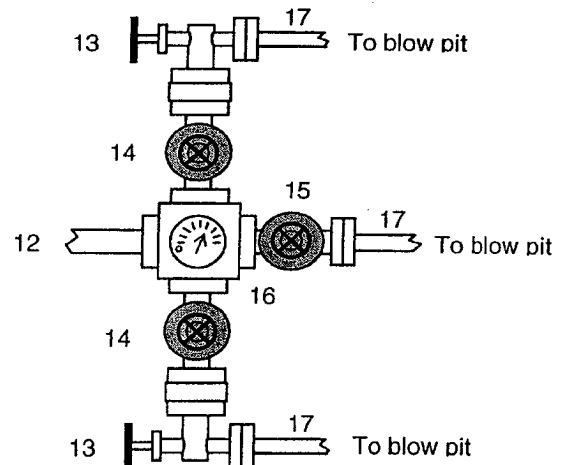

After the 7" intermediate casing has been run and cemented, the Casing Spool ("B" Section) will be installed on the wellhead ("A" Section) and the BOP will be installed on the Casing Spool. A test plug will be set in the wellhead and the pipe rams, blind rams, and choke manifold will be tested to 200 psi to 300 psi (low pressure test) for 10 minutes and to 3000 psi (high pressure test) for 10 minutes. Then the test plug will be removed and the 7" casing will be pressure tested against closed blind rams to 200 psi to 300 psi for 10 minutes and to 1800 psi for 30 minutes - this test pressure is 48% of the minimum internal yield strength of 3740 psi for the 7", 20#, J-55, STC casing. Then we will air drill the 6-1/4" hole to TD and run and cement the 4-1/2" casing.

In addition to the equipment in the above diagram the following equipment will comprise the BOP system:

1. Upper Kelly cock Valve with handle
2. Stab-in TIW valve for all drillstrings in use

Revision Date: September 1, 2004

Property : SAN JUAN 29-5 UNIT Well #: 20C

Surface Location:

Unit: C Section: 7 Township: 29N Range: 5W

County: RIO ARRIBA State: New Mexico

Footage: 295 from the NORTH line, 2120 from the WEST line.

CATHODIC PROTECTION

ConocoPhillips (COP) proposes to drill a cathodic protection deep well groundbed for the subject well. COP will drill a hole vertically at the surface large enough to accommodate 20 feet of 8 inch diameter PVC pipe for surface casing to assist in further drilling and loading. Casing may be cemented in place for stability if needed. COP will drill a 6-7/8" hole to an anticipated minimum depth of 300'(maximum depth of 500'). Cement plugs will not be used unless more than one water zone is encountered. Prior drilling history for the area indicates only one zone to that depth. If more than one water zone is encountered, notification will be made and details of cement and casing will be provided.

All drilling activity will remain on the existing well pad and a Farmington based company will be doing the drilling for ConocoPhillips.
