CHACO 2308-16I #148H BASIN MC/NAGEEZI GL Horizontal

(page 1)

Spud: 2/3/14

Completed: 5/27/14

Pulled tieback & run gas

lift: 7/22/14 OIL CONS. DIV DIST. 3 JUL 23 2014


SHL: 1531' FSL & 281' FEL NE/4 NE/4 Section 16 (I), T23N, R8W

BHL: 378' FSL & 231' FWL

SW/4 SW/4 Section 16(M), T23N, R 8W

SAN JUAN NM Elevation: 6866' API: 30-045-35500

Tops	MD	TVD
Ojo Alamo	837'	837'
Kirtland	984'	984'
Pictured Cliffs	1440′	1432 ′
Lewis	1643'	1628'
Chacra	1826'	1802′
Cliff House	2971'	2880 ′
Menefee	3018'	2925′
Point Lookout	3951'	3805′
Mancos	4148'	3991'
Gallup	4513'	4337'

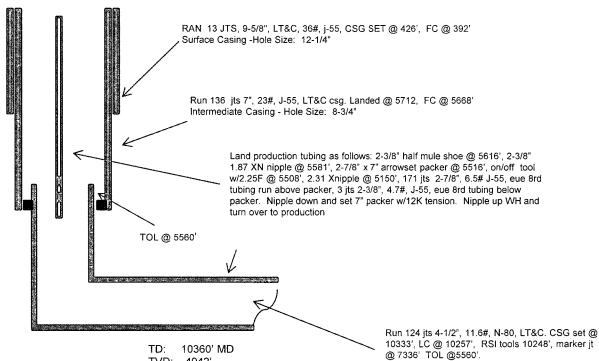

TVD: 4942' PBTD:10257' MD 10333', LC @ 10257', RSI tools 10248', marker jt

Final Casing - Hole Size: 6-1/8"

НО	LE S IZ E	CASING	CEMENT	VOLUME	CMT TOP
	12-1/4"	9-5/8"	250 sx	222 cu.ft.	Surface
	8-3/4"	7"	822 s x	1225 cu. ft.	Surface
	6-1/8"	4-1/2"	380 sx	1386 cu. ft.	TOL 5560'
			respected to the design of the	To-conference and transfer of the second of the second control that the second of the	TO THE THE STATE OF THE STATE O

LH 7/22/14

CHACO 2308-16I #148H

Gallup 4th:

9008'-9280'-

with 24, 0,40"

Gallup 1st:

10041'-10175' +

