




Downhole Well Profile - with Schematic

Well Name: Jicarilla Apache 14G

API/UWI 30039296580000	XTO Accounting ID 77898	Permit Number	State/Province New Mexico	County Rio Arriba
Location T26N-R05W-S34	Spud Date 4/22/2006 00:00	Original KB Elevation (ft) 6,624.00	Ground/Corrected Ground Elevation (ft) 6,612.00	KB-Ground Distance (ft) 12.00

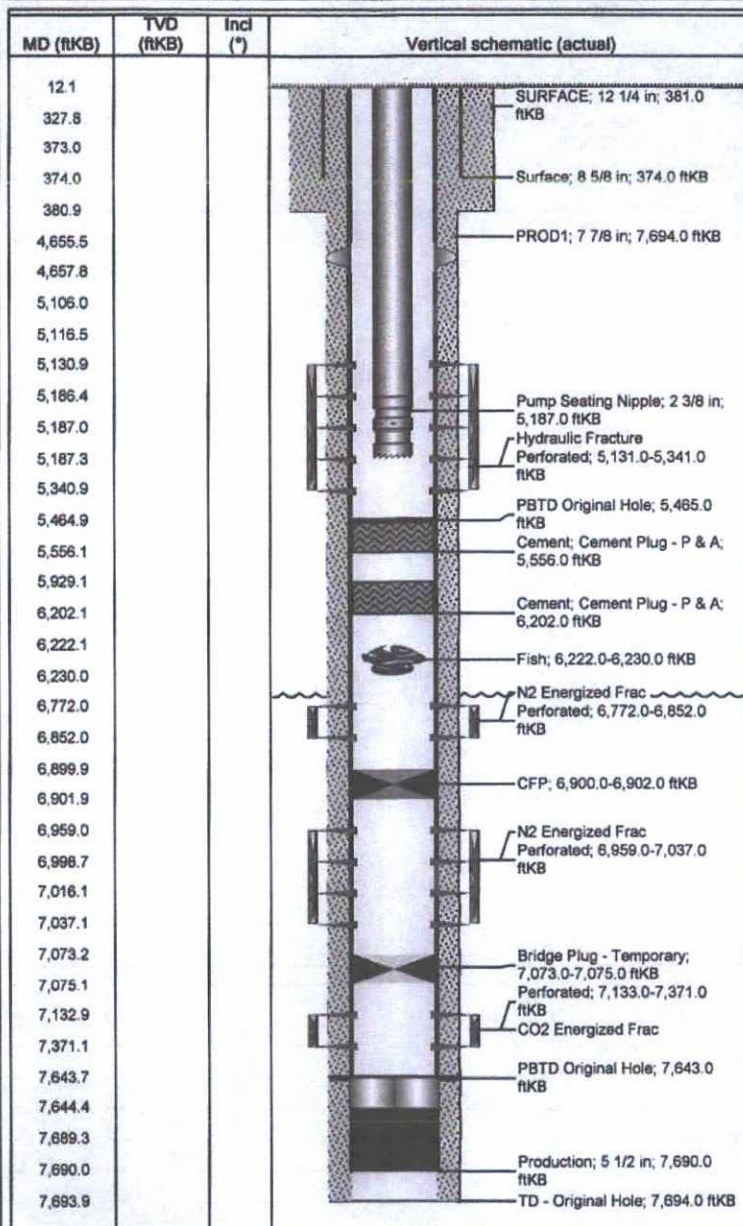

Wellbores				
Wellbore Name Original Hole		Parent Wellbore Original Hole		Wellbore API/UWI
Start Depth (ftKB)		Profile Type Vertical		Kick Off Depth (ftKB)
Section Des		Size (in)	Act Top (ftKB)	Act Btm (ftKB)
Zones				
Zone Name		Top (ftKB)	Btm (ftKB)	Current Status
Mesaverde		5,131.0	5,341.0	
Mancos		6,772.0	7,037.0	
Dakota		7,133.0	7,371.0	
Casing Strings				
Csg Des		Set Depth (ftKB)	OD (in)	WVLen (lb/ft)
Surface		374.0	8 5/8	24.00
Production		7,690.0	5 1/2	15.50
Cement				
Des		Type		String
Surface Casing Cement		Casing		Surface, 374.0ftKB
Production Casing Cement		Casing		Production, 7,690.0ftKB
Cement Plug - P & A		Plug		Production, 7,690.0ftKB
Cement Plug - P & A		Plug		Production, 7,690.0ftKB
Tubing Strings				
Tubing Description		Run Date		Set Depth (ftKB)
Tubing - Production		4/25/2016		5,187.4
Item Des		OD (in)	Wt (lb/ft)	Grade
Tubing		2 3/8	4.70	J-55
Pump Seating Nipple		2 3/8		1
Notched Collar		2 3/8		1
Rod Strings				
Rod Description		Run Date		Set Depth (ftKB)
Item Des		OD (in)	Wt (lb/ft)	Grade
Other In Hole				
Run Date		Des		OD (in)
3/27/2016		Bridge Plug - Temporary		4.9
4/3/2016		CFP		4.9
4/18/2016		Fish		3.82
Perforations				
Date		Top (ftKB)	Btm (ftKB)	Zone
8/1/2006		5,131.0	5,341.0	Mesaverde, Original Hole
4/3/2016		6,772.0	6,852.0	Mancos, Original Hole
3/28/2016		6,959.0	7,037.0	Mancos, Original Hole
6/10/2006		7,133.0	7,371.0	Dakota, Original Hole


2



Downhole Well Profile - with Schematic

Well Name: Jicarilla Apache 14G

API/UWI 30039296580000	XTO Accounting ID 77898	Permit Number	State/Province New Mexico	County Rio Arriba
Location T26N-R05W-S34	Spud Date 4/22/2006 00:00	Original KB Elevation (ft) 6,624.00	Ground/Corrected Ground Elevation (ft) 6,612.00	KB-Ground Distance (ft) 12.00

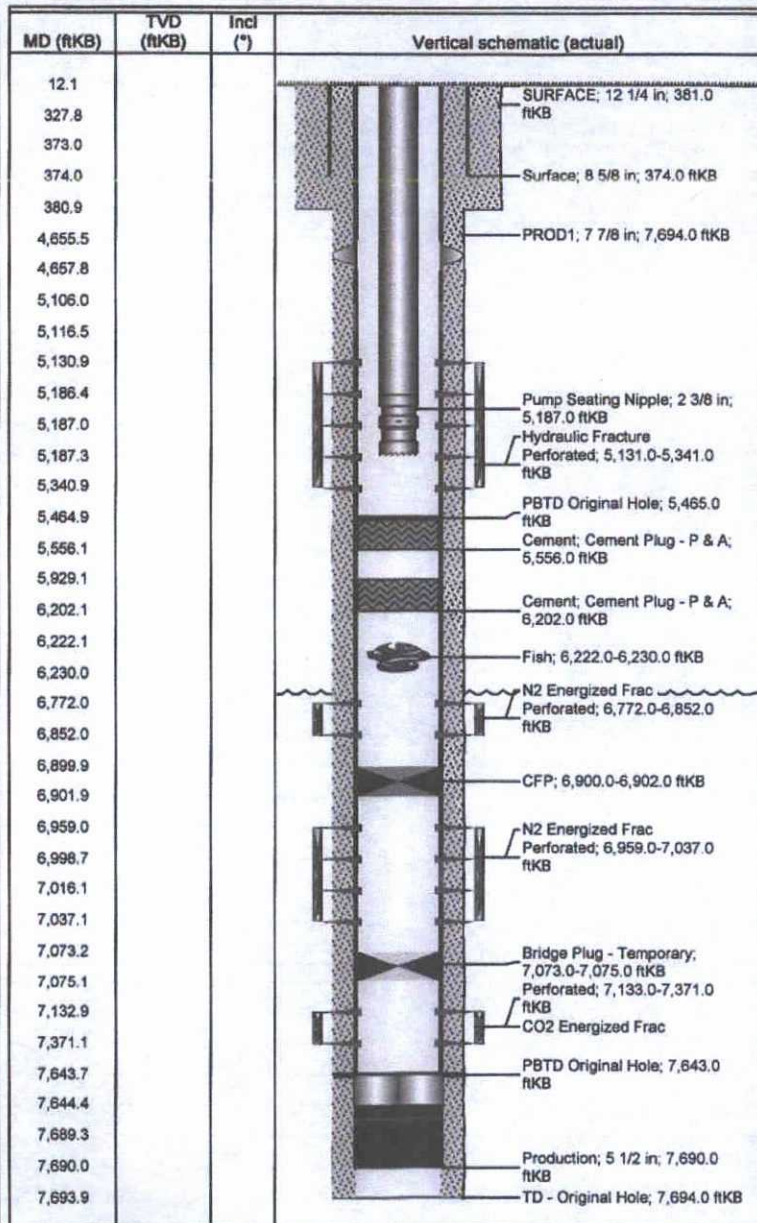

Stimulations & Treatments						
Frac #	Top Perf (ftKB)	Bottom Perf (ftKB)	AIR (bbl/min)	MIR (bbl/min)	TWP (bbl)	Total Proppant (lb)
1.00	6,959	7,037	13.5	18.50		10,137.0
2.00	6,772	6,852	12.5	14.10		69,700.0
