

101-30-039-07731

4359

427-30-039-24262

DATA SHEET FOR DEEP GROUND BED CATHODIC PROTECTION WELLS
NORTHWESTERN NEW MEXICO

(Submit 3 copies to OCD Aztec Office)

Operator MERIDIAN OIL Location: Unit NE Sec. 35 Twp 30 Rng 7

Name of Well/Wells or Pipeline Serviced SAN JUAN 30-6 UNIT #101, #427

cps 140w

Elevation 6850' Completion Date 6/30/64 Total Depth 400' Land Type* N/A

Casing, Sizes, Types & Depths N/A

If Casing is cemented, show amounts & types used N/A

If Cement or Bentonite Plugs have been placed, show depths & amounts used
N/A

Depths & thickness of water zones with description of water when possible:
Fresh, Clear, Salty, Sulphur, Etc. N/A

Depths gas encountered: N/A


Type & amount of coke breeze used: 4950 lbs.

Depths anodes placed: 375', 369', 363', 357', 351', 345'

Depths vent pipes placed: N/A

Vent pipe perforations: N/A

Remarks: gb #2



If any of the above data is unavailable, please indicate so. Copies of all logs, including Drillers Log, Water Analyses & Well Bore Schematics should be submitted when available. Unplugged abandoned wells are to be included.

*Land Type may be shown: F-Federal; I-Indian; S-State; P-Fee.
If Federal or Indian, add Lease Number.

WELL CASING
CATHODIC PROTECTION CONSTRUCTION REPORT
DAILY LOG

Date 6-30-64


Well Name <u>Wilson No. 7 30-6 #101</u>			CPS No. <u>140 W</u>		
Location <u>NE 35-30-7</u>			Work Order No. <u>184-32798-90-54</u>		
Anode Hole Depth <u>400</u>	Total Drilling Rig Time <u>24 Hrs</u>	Type & Size Bit Used <u>8243X=100 6 1/4 Rock- 7911=300'</u>		No. Sacks Mud Used <u>0</u>	
No. Sacks Lost Circulation Mat'l Used <u>0</u>	Anode Depth				
	# 1 <u>375</u>	# 2 <u>369</u>	# 3 <u>363</u>	# 4 <u>357</u>	# 5 <u>351</u>
Total Lbs. Coke Used <u>33 Sacks - 4950</u>	Anode Output (Volts)				
	# 1 <u>2.9</u>	# 2 <u>2.8</u>	# 3 <u>3.3</u>	# 4 <u>2.7</u>	# 5 <u>3.0</u>
Total Circuit Resistance	No. Ft. Surface Cable Conduit				
Volts <u>11.8</u>	Amps <u>7.4</u>	Ohms <u>1.59</u>	<u>173</u>		

Drilling Log (Attach Hereto). ☐

Remarks: Water No. 1 GND Bed,

Construction Completed

Farrell
(Signature)

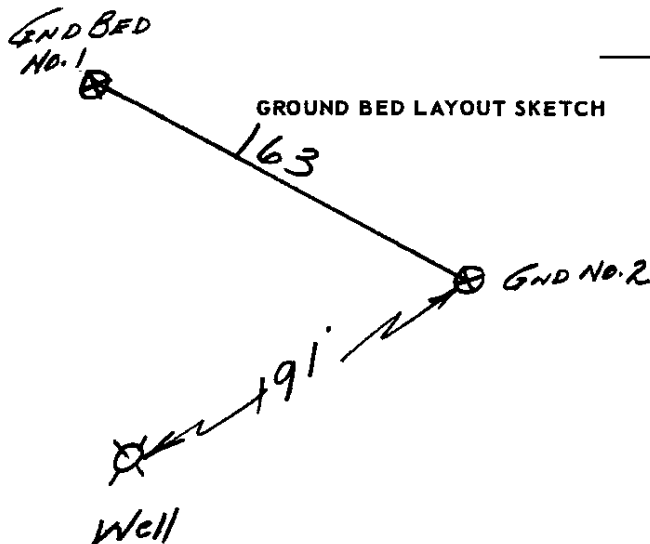

2363'

0
Rect

