

#2 30-045-07424
#3 30-045-20919

DATA SHEET FOR DEEP GROUND BED CATHODIC PROTECTION WELLS
NORTHWESTERN NEW MEXICO
(Submit 3 copies to OCD Aztec Office)

Operator MERIDIAN OIL Location: Unit SW Sec. 14 Twp 28 Rng 8

Name of Well/Wells or Pipeline Serviced HARDIE D #2, #3

cps 506w

Elevation 6347' Completion Date 12/2/63 Total Depth 260' Land Type* N/A

Casing, Sizes, Types & Depths N/A

If Casing is cemented, show amounts & types used N/A

If Cement or Bentonite Plugs have been placed, show depths & amounts used
N/A

Depths & thickness of water zones with description of water when possible:

Fresh, Clear, Salty, Sulphur, Etc. N/A

Depths gas encountered: N/A

Type & amount of coke breeze used: 2640 lbs.

Depths anodes placed: 233', 178', 172', 166', 160', 135', 35'

Depths vent pipes placed: N/A

Vent pipe perforations: N/A

Remarks: gb #1

If any of the above data is unavailable, please indicate so. Copies of all logs, including Drillers Log, Water Analyses & Well Bore Schematics should be submitted when available. Unplugged abandoned wells are to be included.

*Land Type may be shown: F-Federal; I-Indian; S-State; P-Fee.
If Federal or Indian, add Lease Number.

RECEIVED

MAY 31 1991

OIL CON. DIV
DIST. 3

WELL CASING
CATHODIC PROTECTION CONSTRUCTION REPORT
DAILY LOG

Date 12-2-63

Well Name <u>Hardie "D" No. 2</u>			CPS No. <u>506W</u>		
Location <u>SK² 14-28-8</u>			Work Order No. <u>54196</u>		
Anode Hole Depth <u>260</u>	Total Drilling Rig Time <u>12 Hrs</u>	Type & Size Bit Used <u>6 1/4 WM. 2793 X</u>		No. Sacks Mud Used <u>0</u>	
No. Sacks Lost Circulation Mat'l Used <u>0</u>	Anode Depth				
	# 1 <u>233</u>	# 2 <u>178</u>	# 3 <u>172</u>	# 4 <u>166</u>	# 5 <u>160</u>
Total Lbs. Coke Used <u>2640 (24 sks)</u>	Anode Output (Volts)				
	# 1 <u>3.0</u>	# 2 <u>2.0</u>	# 3 <u>2.0</u>	# 4 <u>2.5</u>	# 5 <u>3.0</u>
Total Circuit Resistance		No. Ft. Surface Cable/Conduit			
Volts <u>12.0</u>	Amps <u>8.2</u>	Ohms <u>1.46</u>	<u>583</u>		

Drilling Log (Attach Hereto) ☐

Remarks:

Static c/s. 79 R. 600' NK


P.E.M. Rectifier 28V 12A Scr. # 637266

All Construction Completed

Arreola

(Signature)

GROUND BED LAYOUT SKETCH

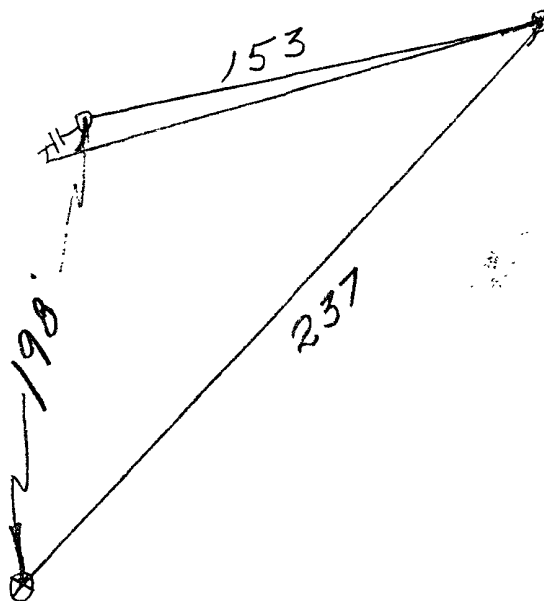

10R
B
1727'

DAILY DRILLING REPORT

LEASE Hardie WELL NO. 0-2 CONTRACTOR L. E. Wilson RIG NO. 0-6 REPORT NO. 1-29 DATE 1-29 19 59

MORNING										DAYLIGHT										EVENING																			
Driller					Total Men In Crew					Driller					Total Men In Crew					Driller					Total Men In Crew														
FROM	TO	FORMATION	WT. BIT	R.P.M.	FROM	TO	FORMATION	WT. BIT	R.P.M.	FROM	TO	FORMATION	WT. BIT	R.P.M.	FROM	TO	FORMATION	WT. BIT	R.P.M.	FROM	TO	FORMATION	WT. BIT	R.P.M.															
92	22	Hardie																																					
92	41	Shale																																					
110	120	Hardie																																					
120	260	Hardie Shale																																					
BIT NO.					NO. DC					SIZE					LENG.					NO. DC					SIZE					LENG.									
SERIAL NO.					NO. DC					SIZE					LENG.					NO. DC					SIZE					LENG.									
SIZE					STANDS					SINGLES					STANDS					SINGLES					STANDS					SINGLES									
TYPE					DOWN ON KELLY					DOWN ON KELLY					DOWN ON KELLY					DOWN ON KELLY					DOWN ON KELLY					DOWN ON KELLY									
MAKE					TOTAL DEPTH					TOTAL DEPTH					TOTAL DEPTH					TOTAL DEPTH					TOTAL DEPTH					TOTAL DEPTH									
MUD RECORD					MUD, ADDITIVES USED AND RECEIVED					MUD, ADDITIVES USED AND RECEIVED					MUD, ADDITIVES USED AND RECEIVED					MUD, ADDITIVES USED AND RECEIVED					MUD, ADDITIVES USED AND RECEIVED					MUD, ADDITIVES USED AND RECEIVED									
Time					Time					Time					Time					Time					Time					Time									
FROM					TO					FROM					TO					FROM					TO					FROM					TO				
TIME BREAKDOWN					TIME BREAKDOWN					TIME BREAKDOWN					TIME BREAKDOWN					TIME BREAKDOWN					TIME BREAKDOWN					TIME BREAKDOWN									
Left Bloomfield at 6:00 AM. Arrived at Rig at 7:30 AM. Drilled to 260 ft. Left Rig at 5:00 PM. 10 hrs.																																							
Remarks: Left Bloomfield at 6:00 AM. Arrived at Rig at 7:30 AM. Drilled out to 260 ft. Finished at 5:00 PM. 10 hrs.																																							

SIGNED: Toolpusher

Oil Karsels
