

30-039-07894
30-039-84177

DATA SHEET FOR DEEP GROUND BED CATHODIC PROTECTION WELLS
NORTHWESTERN NEW MEXICO
(Submit 3 copies to OCD Aztec Office)

Operator MERIDIAN OIL Location: Unit NE Sec. 11 Twp 30 Rng 7

Name of Well/Wells or Pipeline Serviced SAN JUAN 30-6 UNIT #64, #419
cps 162w

Elevation 6749' Completion Date 8/19/64 Total Depth 370' Land Type* N/A

Casing, Sizes, Types & Depths N/A

If Casing is cemented, show amounts & types used N/A

If Cement or Bentonite Plugs have been placed, show depths & amounts used
N/A

Depths & thickness of water zones with description of water when possible:
Fresh, Clear, Salty, Sulphur, Etc. N/A

Depths gas encountered: N/A

Type & amount of coke breeze used: 5100 lbs.

Depths anodes placed: 345', 339', 333', 327', 321', 315'

Depths vent pipes placed: N/A

Vent pipe perforations: N/A

Remarks: qb #2

RECEIVED
MAY 31 1991
OIL CON. DIV
DIST. 3

If any of the above data is unavailable, please indicate so. Copies of all logs, including Drillers Log, Water Analyses & Well Bore Schematics should be submitted when available. Unplugged abandoned wells are to be included.

*Land Type may be shown: F-Federal; I-Indian; S-State; P-Fee.
If Federal or Indian, add Lease Number.

CATHODIC PROTECTION CONSTRUCTION REPORT
DAILY LOG

Date 8-19-64

Well Name <u>Horwell No. 5B 30-6 #64</u>			CPS No. <u>162W</u>		
Location <u>NE 11-30-7</u>			Work Order No. <u>52183 40542 -90-54</u>		
Anode Hole Depth <u>370</u>	Total Drilling Rig Time <u>24</u>	Type & Size Bit Used <u>6 1/4 Rock 10758X</u>		No. Sacks Mud Used <u>0</u>	
No. Sacks Lost Circulation Mat'l Used <u>0</u>	Anode Depth				
	# 1 <u>345</u>	# 2 <u>339</u>	# 3 <u>333</u>	# 4 <u>327</u>	# 5 <u>321</u>
Total Lbs. Coke Used <u>345ks</u>	Anode Output (Volts)				
<u>5100</u>	# 1 <u>3.0</u>	# 2 <u>3.0</u>	# 3 <u>2.9</u>	# 4 <u>2.9</u>	# 5 <u>2.7</u>
Total Circuit Resistance Volts <u>11.7</u>	Amps <u>8.3</u>	Ohms <u>1.41</u>		No. Ft. Surface Cable Conduit <u>134'</u>	


Drilling Log (Attach Hereto). ☐

Remarks: 5 Anodes = 12.0 V 7.3 A = 164-5

All Construction Completed

Garrels
(Signature)

GROUND BED LAYOUT SKETCH

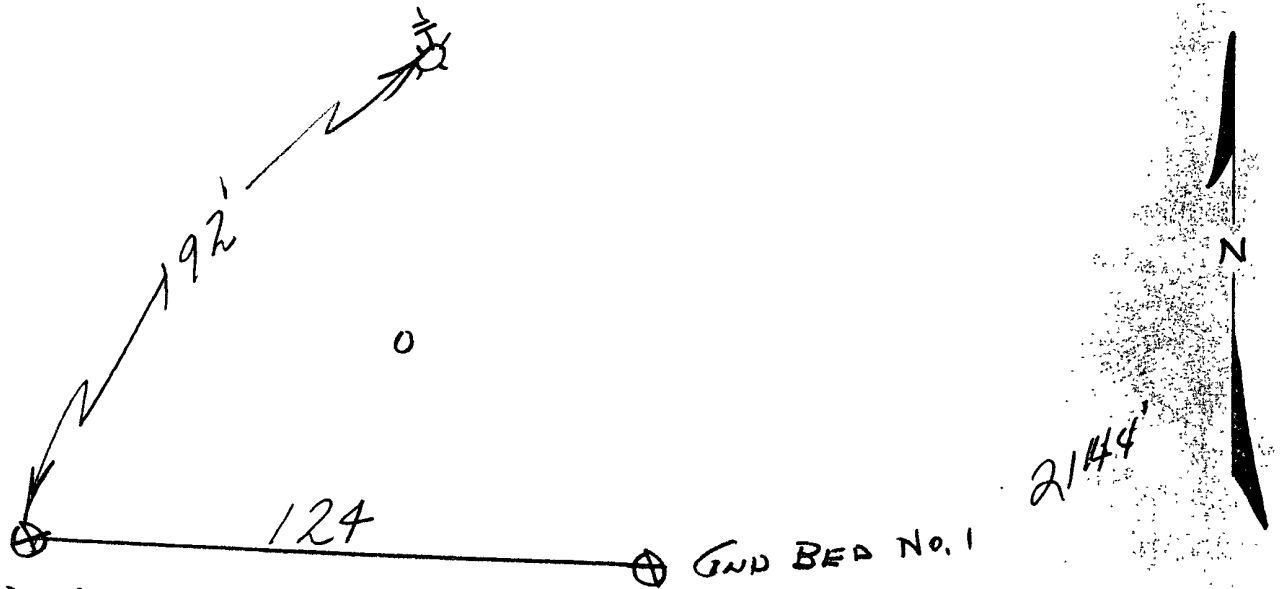

EL PASO NATURAL GAS COMPANY
DRILLING DEPARTMENT

DAILY DRILLING REPORT

LEASE H. 11-11 WELL NO. 3 CONTRACTOR K.F. Wilson RIG NO. D-2 REPORT NO. 191 DATE 11/13

MORNING DAYLIGHT EVENING

Driller			Total Men In Crew			Driller			Total Men In Crew		
FROM	TO	FORMATION	WT. BIT	R.P.M.		FROM	TO	FORMATION	WT. BIT	R.P.M.	
0	110	SS				250	300	SS			
110	300	SS				300	325	SS			
300	325	SS				325	370	SS			

Driller			Total Men In Crew			Driller			Total Men In Crew		
FROM	TO	FORMATION	WT. BIT	R.P.M.		FROM	TO	FORMATION	WT. BIT	R.P.M.	
0	110	SS				250	300	SS			
110	300	SS				300	325	SS			
300	325	SS				325	370	SS			

Driller			Total Men In Crew			Driller			Total Men In Crew		
FROM	TO	FORMATION	WT. BIT	R.P.M.		FROM	TO	FORMATION	WT. BIT	R.P.M.	
0	110	SS				250	300	SS			
110	300	SS				300	325	SS			
300	325	SS				325	370	SS			

Driller			Total Men In Crew			Driller			Total Men In Crew		
FROM	TO	FORMATION	WT. BIT	R.P.M.		FROM	TO	FORMATION	WT. BIT	R.P.M.	
0	110	SS				250	300	SS			
110	300	SS				300	325	SS			
300	325	SS				325	370	SS			

Driller			Total Men In Crew			Driller			Total Men In Crew		
FROM	TO	FORMATION	WT. BIT	R.P.M.		FROM	TO	FORMATION	WT. BIT	R.P.M.	
0	110	SS				250	300	SS			
110	300	SS				300	325	SS			
300	325	SS				325	370	SS			

Driller			Total Men In Crew			Driller			Total Men In Crew		
FROM	TO	FORMATION	WT. BIT	R.P.M.		FROM	TO	FORMATION	WT. BIT	R.P.M.	
0	110	SS				250	300	SS			
110	300	SS				300	325	SS			
300	325	SS				325	370	SS			

SIGNED: Toolpusher

Company Engineer

O. J. L. L. L.

RIG TIME = 24

11:00 AM
11:15 AM
11:30 AM

REMARKS: LEFT YARD AT 7:00 AM
LEFT YARD AT 8:00 AM
LEFT YARD AT 9:00 AM
LEFT YARD AT 10:00 AM
LEFT YARD AT 11:00 AM
LEFT YARD AT 12:00 PM
LEFT YARD AT 1:00 PM
LEFT YARD AT 2:00 PM
LEFT YARD AT 3:00 PM
LEFT YARD AT 4:00 PM
LEFT YARD AT 5:00 PM
LEFT YARD AT 6:00 PM
LEFT YARD AT 7:00 PM
LEFT YARD AT 8:00 PM
LEFT YARD AT 9:00 PM
LEFT YARD AT 10:00 PM
LEFT YARD AT 11:00 PM
LEFT YARD AT 12:00 AM
