

WELL CASING
CATHODIC PROTECTION CONSTRUCTION REPORT
DAILY LOG

#274 30-045-27963

San Juan repro Form 71-7

Drilling Log (Attach Hereto) ☐

Completion Date 5-17-93


CPS #	Well Name Line or Plant	Work Order #	Static	Ins Union Check
2394-W	ROSA UNIT #274	L179	600'S = 6.55 ML	☐ Good ☐ Bad None
Location	Anode Size	Anode Type	Size Bit	
B-16-31-06	2" x 60"	ANOTEC	7 7/8"	
Depth Drilled	Depth Logged	Drilling Rig Time	Total Lbs. Coke Used	Lost Circulation Mat'l Used
400'	386'			
Anode Depth				
# 1 360'	# 2 350'	# 3 340'	# 4 330'	# 5 320'
# 6 310'	# 7 300'	# 8 285'	# 9 275'	# 10 265'
Anode Output (Amps)				
# 1 4.0	# 2 4.3	# 3 3.7	# 4 3.8	# 5 4.0
# 6 4.4	# 7 4.1	# 8 4.1	# 9 4.4	# 10 4.0
Anode Depth				
# 11 255'	# 12 245'	# 13 235'	# 14 225'	# 15 210'
# 16	# 17	# 18	# 19	# 20
Anode Output (Amps)				
# 11 4.1	# 12 4.4	# 13 4.4	# 14 4.3	# 15 3.8
# 16	# 17	# 18	# 19	# 20
Total Circuit Resistance				
Volts 11.91	Amps 19.5	Ohms .61	No. 8 C.P. Cable Used	No. 2 C.P. Cable Used

Remarks: 11/16 SET 59' OF 8" PVC CASING, AND CEMENTED WITH 13 SACKS. NO GAS, WATER, OR BOULDERS WERE ENCOUNTERED DURING CASING. Drilled 400', Logged 386'. Driller said water at 70'. Took sample. Installed 386' of 1" PVC Vent pipe, perforated bottom 290'.

Rectifier Size: Solar v Solar A
Addn'l Depth _____
Depth Credit: 114'
Extra Cable: 210'
Ditch & 1 Cable: 190'
25' Meter Pole: -
20' Meter Pole: -
10' Stub Pole: -

All Construction Completed

GROUND BED LAYOUT SKETCH

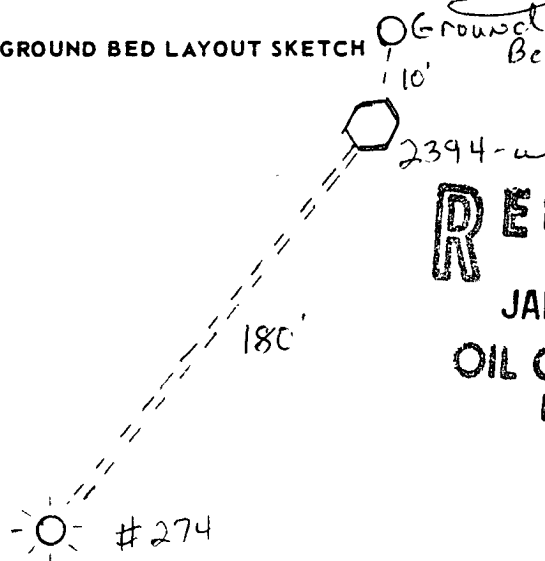

RECEIVED
JAN 31 1994
OIL CON. DIV.
DIST. 3

Well NOT TIED IN yet
