

B #2 30-045-09966
#16 30-045-24203

DATA SHEET FOR DEEP GROUND BED CATHODIC PROTECTION WELLS
NORTHWESTERN NEW MEXICO
(Submit 3 copies to OCD Aztec Office)

Operator TENNECO Location: Unit NE Sec. 4 Twp 30 Rng 10

Name of Well/Wells or Pipeline Serviced ATLANTIC B #2, #16

cps 324w

Elevation 6337' Completion Date 12/6/68 Total Depth 380' Land Type* N/A

Casing, Sizes, Types & Depths N/A

If Casing is cemented, show amounts & types used N/A

If Cement or Bentonite Plugs have been placed, show depths & amounts used
N/A

Depths & thickness of water zones with description of water when possible:
Fresh, Clear, Salty, Sulphur, Etc. WET SPOTS 100' TO 120' & 140' TO 200'

Depths gas encountered: N/A


Type & amount of coke breeze used: N/A

Depths anodes placed: 359', 353', 347', 341', 335', 329', 323', 317', 213', 207'

Depths vent pipes placed: 353' OF 3/4"

Vent pipe perforations: N/A

Remarks: qb #2



If any of the above data is unavailable, please indicate so. Copies of all logs, including Drillers Log, Water Analyses & Well Bore Schematics should be submitted when available. Unplugged abandoned wells are to be included.

*Land Type may be shown: F-Federal; I-Indian; S-State; P-Fee.
If Federal or Indian, add Lease Number.

WELL CASING
CATHODIC PROTECTION CONSTRUCTION REPORT
DAILY LOG

Date 12-6-68

Insert #88 (380')

Well Name <u>ATLANTIC #2B</u>			CPS No. <u>324W</u>		
Location <u>NEH-30-10</u>			Work Order No. <u>184-52064-50-20</u>		
Anode Hole Depth <u>380'</u>	Total Drilling Rig Time <u>22 HRS</u>	Type & Size Bit Used <u>7 1/8" SER #68488 (380')</u>		No. Sacks Mud Used <u>1</u>	
No. Sacks Lost Circulation Mat'l Used	Anode Depth	#1	#2	#3	#4
	<u>#1 359'</u>	<u>#2 353'</u>	<u>#3 347'</u>	<u>#4 341'</u>	<u>#5 335'</u>
Total Lbs. Coke Used	Anode Output (Volts)	#1	#2	#3	#4
	<u>#1 3.3</u>	<u>#2 3.4</u>	<u>#3 3.0</u>	<u>#4 2.7</u>	<u>#5 3.5</u>
Total Circuit Resistance	No. Ft. Surface Cable Conduit				
Volts <u>12</u>	Amps <u>12</u>	Ohms <u>1.00</u>	<u>3,294' ON ANODES. 180' SURFACE CABLE = 3,481'</u>		

Drilling Log (Attach Hereto). ☐ #7 = 323' #8 = 317' #9 = 213' #10 = 207'
#7 = 4.6 #8 = 4.5 #9 = 3.0 #10 = 3.2

Remarks:

3/4" VENT ON #2 ANODE


50# BAROSOS

POWED IN NEW #8 POSITIVE CABLE FROM RECTIFIER TO GND BED #1

All Construction Completed

Wilbur Z. Smith
(Signature)

GROUND BED LAYOUT SKETCH

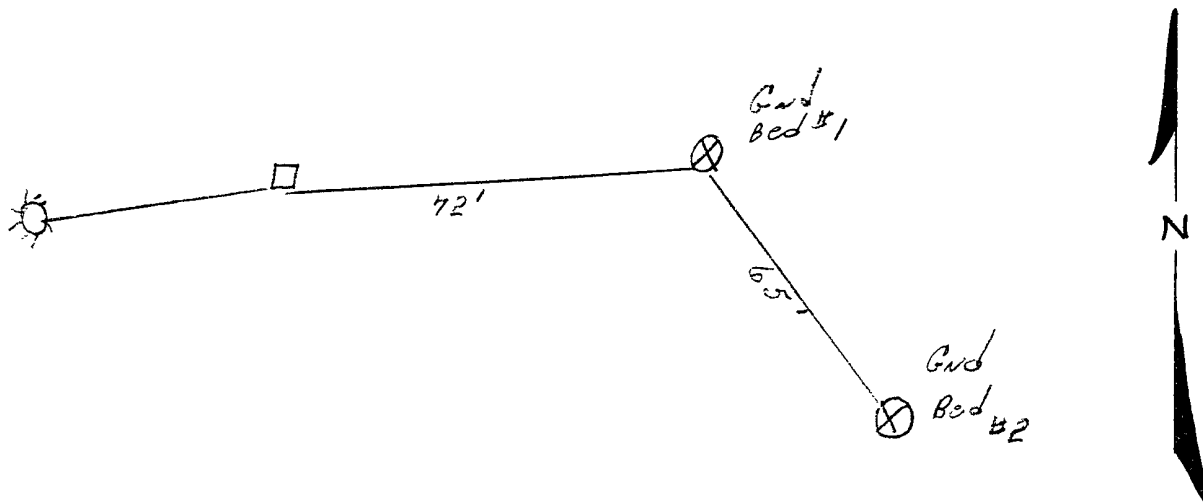

DAILY DRILLING REPORT

Sum 7488 (380 ft.)

[illegible]

SIGNED: Toolpusher

Wilbur F. Frost
