

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

SUBMIT IN TRIPLICATE*
(Other instructions on reverse side)

Budget Bureau No. 1004-0135
Expires August 31, 1985

SUNDRY NOTICES AND REPORTS ON WELLS

(Do not use this form for proposals to drill or to deepen or plug back to a different reservoir.
Use "APPLICATION FOR PERMIT" for such proposals.)

RECEIVED

JUN 28 1985

5. LEASE DESIGNATION AND SERIAL NO.

Jicarilla Contract 148
6. IF INDIAN, ALLOTTEE OR TRIBE NAME

7. UNIT AGREEMENT NAME

8. FARM OR LEASE NAME

Jicarilla Contract 148

9. WELL NO.

33

10. FIELD AND POOL, OR WILDCAT

W Lindrith GLP DK

11. SEC., T., R., M., OR BLK. AND
SURVEY OR AREA

SE/NE Sec15, T25N, R5W

12. COUNTY OR PARISH 13. STATE

Rio Arriba NM

1. OIL WELL ☒ GAS WELL ☐ OTHER ☐

2. NAME OF OPERATOR

Amoco Production Co.

BUREAU OF LAND MANAGEMENT
FARMINGTON RESOURCE AREA

3. ADDRESS OF OPERATOR

501 Airport Drive, Farmington, N M 87401

4. LOCATION OF WELL Report location clearly and in accordance with any State requirements.*
(See also space 17 below.)
AT SURFACE

1990' FNL x 720' FEL

14. PERMIT NO.

15. ELEVATIONS (Show whether DF, RT, GR, etc.)

7005' GR

16. Check Appropriate Box To Indicate Nature of Notice, Report, or Other Data

NOTICE OF INTENTION TO:

TEST WATER SHUT-OFF

FRACURE TREAT

SHEED OR ACIDIZE

REPAIR WELL

(Other)

PULL OR ALTER CASING

MULTIPLE COMPLETE

ABANDON*

CHANGE PLANT

SUBSEQUENT REPORT OF:

WATER SHUT-OFF

FRACURE TREATMENT

SHOOTING OR ACIDIZING

(Other)

Spud and Set Casing

REPAIRING WELL

ALTERING CASING

ABANDONMENT*

(NOTE: Report results of multiple completion on Well
Completion or Recompletion Report and Log form.)

17. DESCRIBE PROPOSED OR COMPLETED OPERATIONS (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work. If well is directionally drilled, give subsurface locations and measured and true vertical depths for all markers and zones pertinent to this work.)*

Spud a 12 1/4" hole on 5-14-85 at 1145 hrs. Drilled to 325'. Set 8 5/8", 24#, K55 casing at 317' and cemented with 354 cu.ft. Class B Portland. Circulated cement to surface. Pressure tested casing to 1000 psi for 30 minutes. Drilled a 7-7/8" hole to a TD of 7750' on 5-27-85. Set 5-1/2", 17#, K55 casing at 7750'. Stage 1: cemented with 236 cu.ft. Class B Portland and tailed in with 389 cu.ft. Class B Portland. Stage 2: cemented with 956 cu. ft. Class B Portland. Ran temperature survey (attached) which indicated the top of the cement to be at 1200'.

The DV tool was set at 5390' and the rig was released on 5-28-85.

18. I hereby certify that the foregoing is true and correct

SIGNED

BDS Shaw

TITLE

Adm. Supervisor

DATE

6-21-85

(This space for Federal or State office use)

APPROVED BY

TITLE

CONDITIONS OF APPROVAL, IF ANY:

DATE

JUL 01 1985

ACCEPTED FOR RECORD

FARMINGTON RESOURCE AREA

BY

RM

*See Instructions on Reverse Side

NMOCC

WILSON
SERVICE COMPANY

FORM 432-2

TEMPERATURE SURVEY

COMPANY.....Amoco Production.....
WELL.....33.....LEASE Jicarilla Contract 148.....
COUNTY.....Rio Arriba.....STATE.....New Mexico.....
SEC.....15.....TWP.....25N.....RGE.....5W.....

APPROX. TOP CEMENT.....1200'.....

Survey Begins at.....100'.....Ft. Ends at.....5335'.....Ft.
Approx. Fill-Up.....Max. Temp.....
Log Measured From.....KB.....Run No.....1.....

Casing Size	Casing Depth	Diam of Hole	Depth
5 1/2" from	to	from 7 7/8" to	
from	to	from	to


Date of Cementing.....5/28/85.....Time.....12:15 AM.....
Date of Survey.....5/28/85.....Time.....9:30 AM.....
Amount of Cement.....As Per Report.....

Recorded by.....Ebert.....Witnessed by.....

REMARKS OR OTHER DATA

DV Tool Approx 5390'.....

TEMPERATURE IN DEGREES FAHRENHEIT

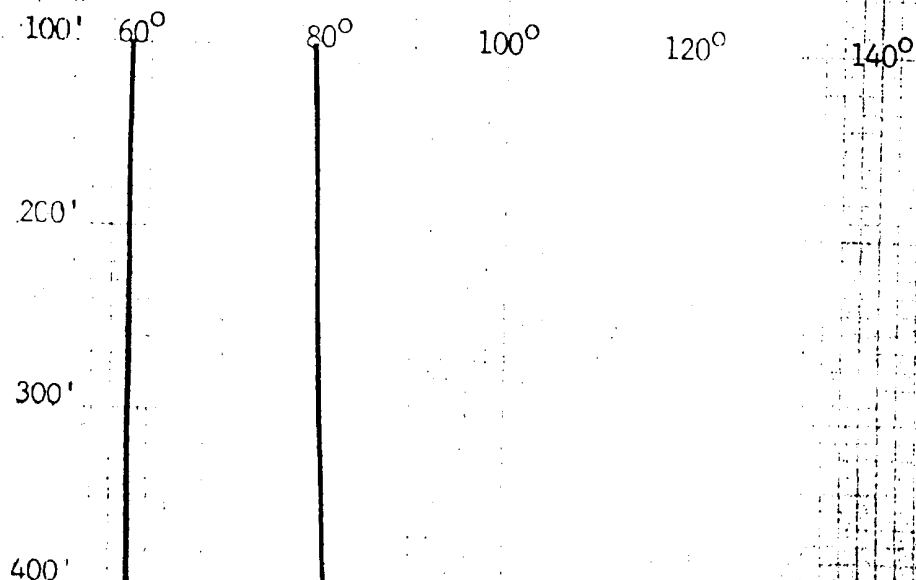

500'

600'

700'

800'

900'

1000'

1100'

1200'

1300'

1400'

1500'

1600'

1700'

Anomaly 1200'

1800'

1900'

2000'

2100'

2200'

2300'

2400'

2500'

2600'


2700'

2800'

2900'

3000'

3100'

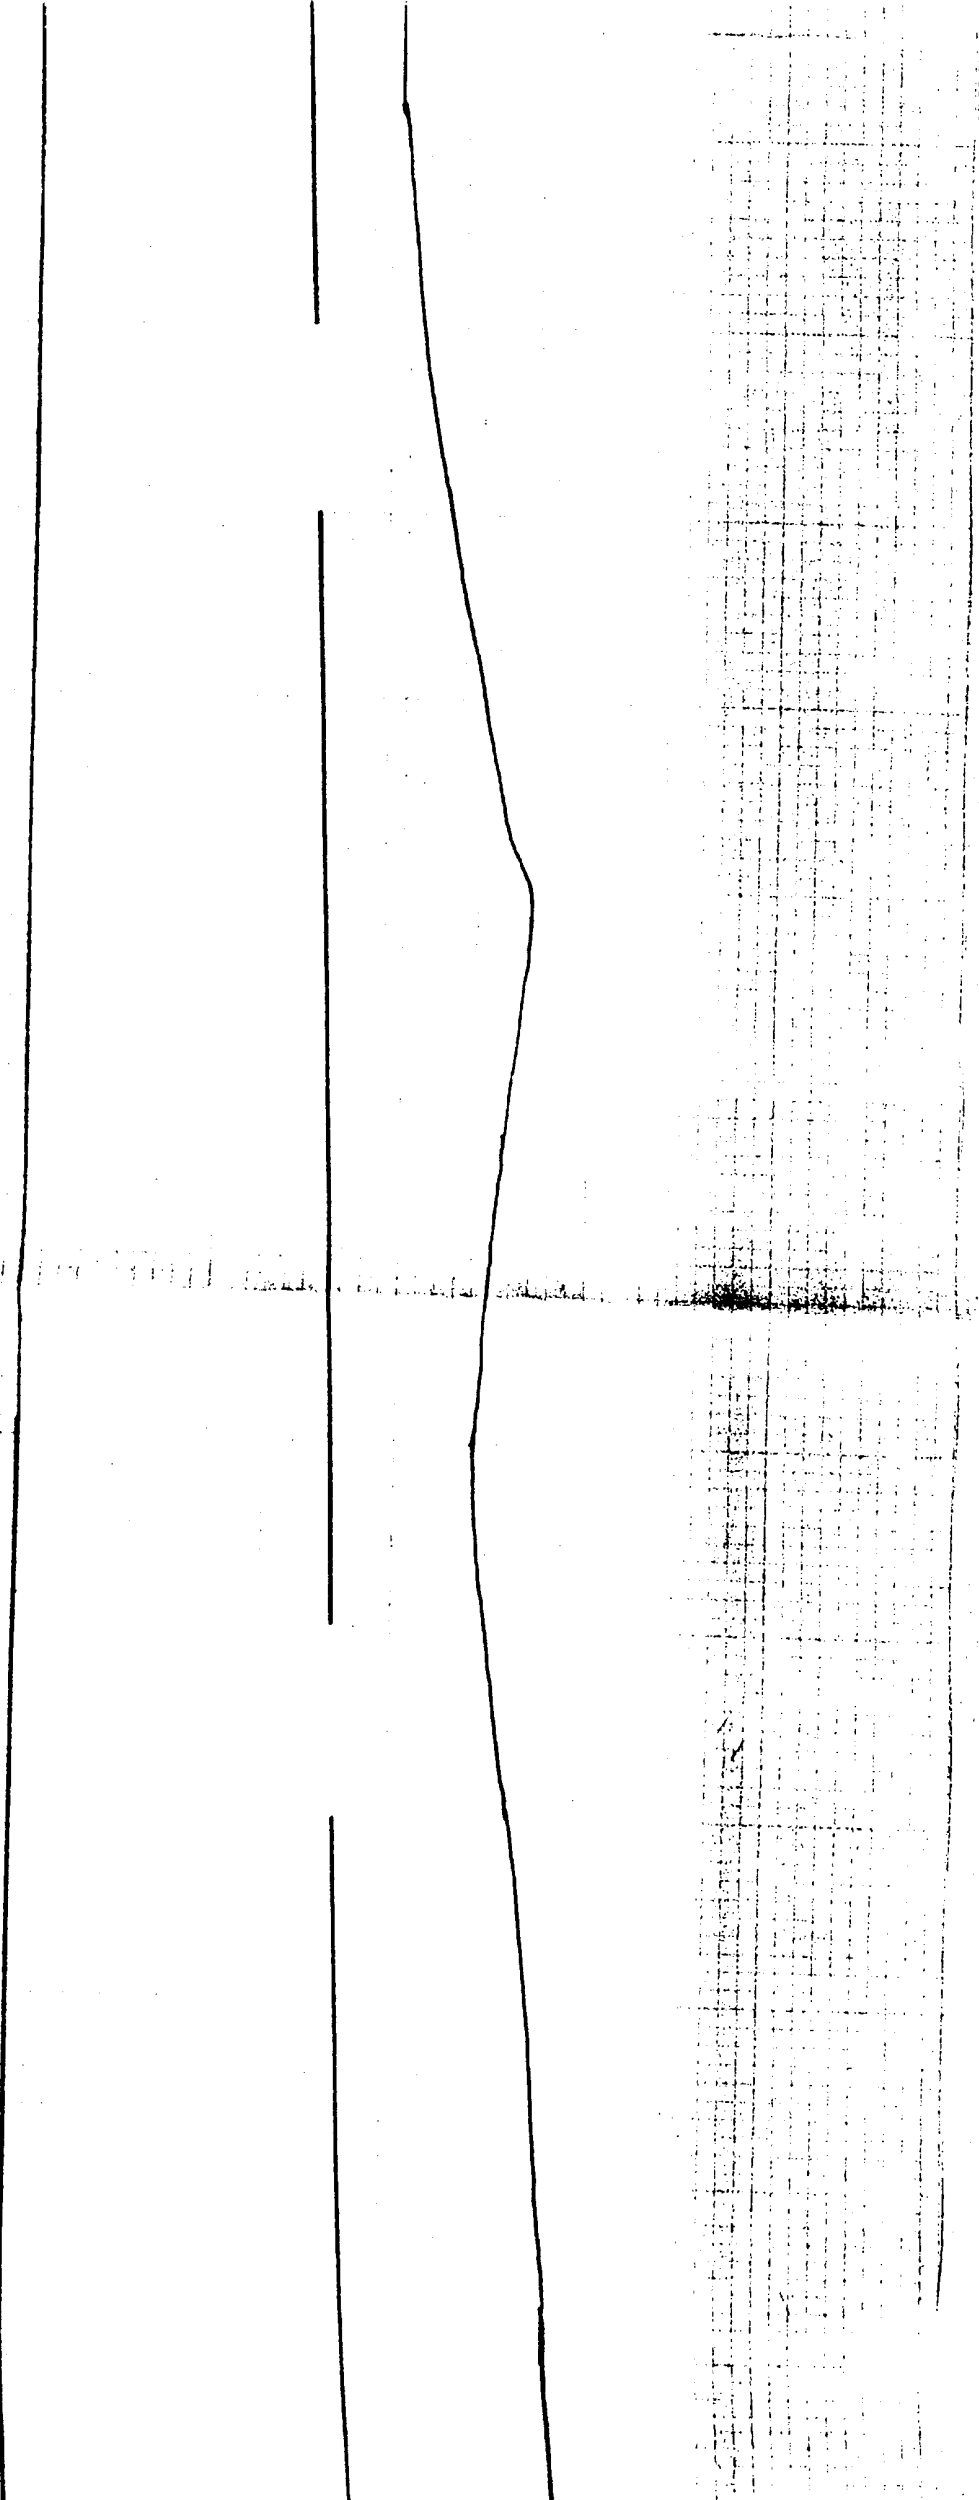

3100'

3200'

3300'

3400'

3500'

3600'

3700'

3800'

3900'

4000'

4100'

4200'

4300'

4400'

4500'

4600'

4700'

4800'

4900'

5000'

5100'

5200'

5300'

TD Surveyed 5335'
