

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

SUBMIT IN TRIPPLICATE
(Other instructions on reverse side)

Budget Bureau No. 1004-0135
Expires August 31, 1985
LEASE DESIGNATION AND SERIAL NO.

SUNDRY NOTICES AND REPORTS ON WELLS

(This unit may be used for proposals to drill or to deepen or plug back to the bottom of a well.
Use "APPLICATION FOR PERMIT" for such proposals.)

RECEIVED
DEC 20 1985

Jicarilla Apache A-118

Jicarilla Apache Tribe

1. UNIT AGREEMENT NAME

2. FARM OR LEASE NAME

Jicarilla Apache A-118

3. WELL NO.

19

10. FIELD AND POOL, OR WILDCAT

Ojito Gallup-Dakota

11. SEC., T., R., M., OR BLK. AND
SUBST. OR AREA

SE/SE Sec 36, T26N, R3W

12. COUNTY OR PARISH
Rio Arriba

13. STATE
New Mexico

1. OIL WELL ☐ GAS WELL ☒ OTHER

2. NAME OF OPERATOR

Amoco Production Co.

3. ADDRESS OF OPERATOR

501 Airport Drive, Farmington, N M 87401

4. LOCATION OF WELL (Report location clearly and in accordance with any State requirements.
See also space 17 below.)

At surface

970' FSL X 490' FEL

BUREAU OF LAND MANAGEMENT
FARMINGTON RESOURCE AREA

14. PERMIT NO.

15. ELEVATIONS (Show whether of, RT, GR, etc.)

7384' GR

16.

Check Appropriate Box To Indicate Nature of Notice, Report, or Other Data

NOTICE OF INTENTION TO:

SUBSEQUENT REPORT OF:

TEST WATER SHUT-OFF

FRACTURE TREAT

SHOOT OR ACIDIZE

REPAIR WELL

(Other)

PULL OR ALTER CASING

MULTIPLE COMPLETE

ABANDON*

CHANGE PLANS

WATER SHUT-OFF

FRACTURE TREATMENT

SHOOTING OR ACIDIZING

(Other) Spud and Set Casing

REPAIRING WELL

ALTERING CASING

ABANDONMENT*

X

17. DESCRIBE PROPOSED OR COMPLETED OPERATIONS (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work. If well is directionally drilled, give subsurface locations and measured and true vertical depths for all markers and zones pertinent to this work.)

(Note: Report results of multiple completion on Well Completion or Recompletion Report and Log form.)

Spud a 12 1/4" hole on 10-31-85 at 0700 hours. Drilled to 330'. Set 8 5/8", 24#, J-55 casing at 330' and cemented with 325 cu. ft. Class B Portland. Circulated cement to surface. Pressure tested casing to 1000 psi for 30 minutes. Drilled a 7 7/8" hole to a TD of 8396' on 11-17-85. Set 5 1/2", 17# and 15.5# K-55 casing at 8396'. Stage 1: cemented with 319 cu. ft. Class B and tailed in with 354 cu. ft. Class B. Stage 2: cemented with 814 cu. ft. Class B. Ran a temperature survey (attached) which indicated the top of the cement to be at 100'. The DV tool was set at 4963' and the rig was released on 11-18-85.

NOV 3 1986
OIL CON. DIV.
DIST. 3

I hereby certify that the foregoing is true and correct

SIGNED

AS Shaw

TITLE Adm. Supervisor

DATE 11-25-85

(This space for Federal or State office use)

ACCEPTED FOR RECORD

APPROVED BY

CONDITIONS OF APPROVAL, IF ANY:

TITLE

DATE

NOV 02

*See Instructions on Reverse Side

NMOCC

FARMINGTON RESOURCE AREA

U.S.C. Section 1001, makes it a crime for any person knowingly and willfully to make to any department or agency of the States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

RECEIVED

FORM 100-1
BUREAU OF LAND MANAGEMENT
FARMINGTON REGIONAL OFFICE

WILSON SERVICE COMPANY

TEMPERATURE SURVEY

COMPANY Amoco Production
WELL #19 LEASE Jicarilla Apache Tribal
COUNTY Rio Arriba STATE "A" 118
SEC. 36 TWP. 26N RGE. 3W

APPROX. TOP CEMENT 100'

Survey Begins at 50' Ft. Ends at 4885' Ft.
Approx. Fill-Up Max. Temp.
Log Measured From GL Run No. 1


Casing Size	Casing Depth	Diam of Hole	Depth
<u>5 1/2"</u> from <u> </u> to <u> </u>	<u> </u> from <u> </u> to <u> </u>	<u>6 1/2"</u> from <u> </u> to <u> </u>	<u> </u>
from <u> </u> to <u> </u>	from <u> </u> to <u> </u>	from <u> </u> to <u> </u>	<u> </u>

Date of Cementing 11/17/85 Time 7:00 pm
Date of Survey 11/18/85 Time 7:00 am
Amount of Cement As Per Report

Recorded by Wilson/Bizzell Witnessed by

REMARKS OR OTHER DATA

TEMPERATURE IN DEGREES FAHRENHEIT

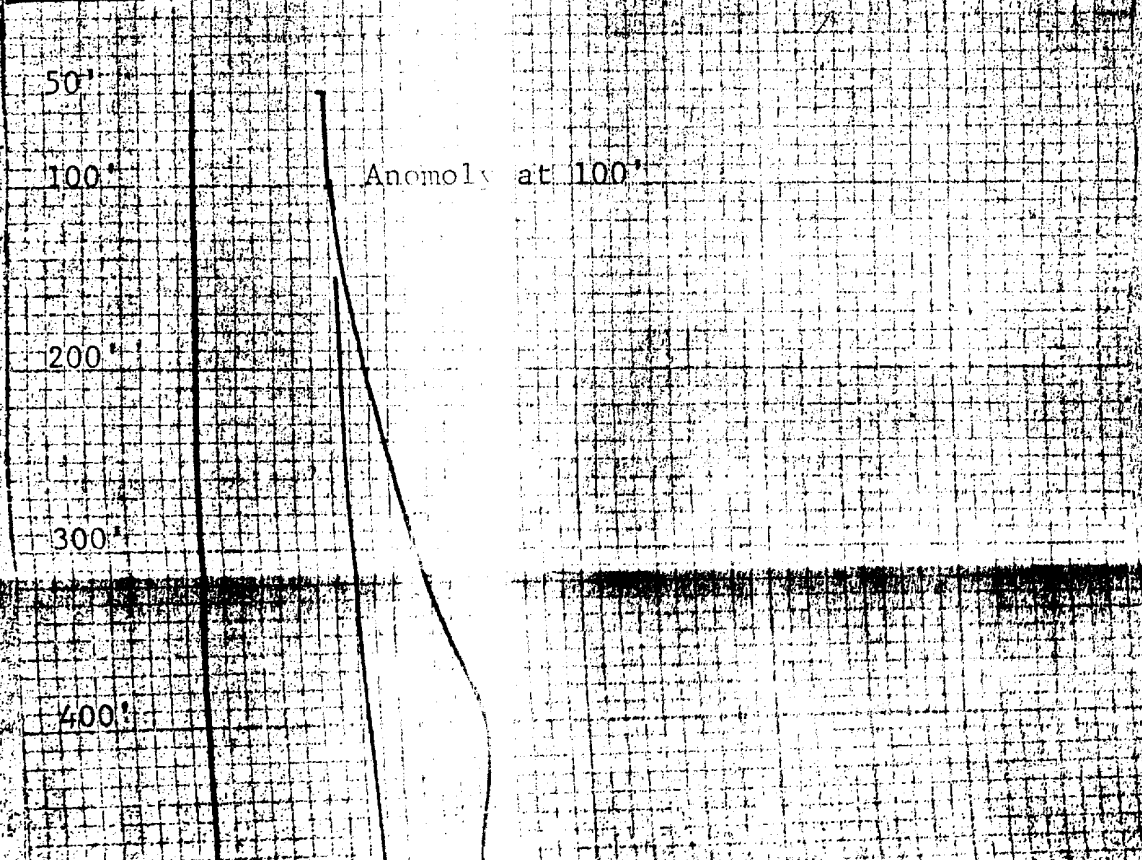

6/10/19

10/10/19

400'

500'

600'

700'

800'

900'

1000'

1100'

1200'

1300'

1400'

1500'

1600'

1700'

1600'

1700'

1800'

1900'

2000'

2100'

2200'

2300'

2400'

2500'

2600'

2700'

2800'

2900'

2500'

2600'

2700'

2800'

2900'

3000'

3100'

3200'

3300'

3400'

3500'

3600'

3700'

3800'

3900'

4000'

4100'

4200'

4300'

4400'

4500'

4700'

4800'

TD Surveyed at 4885'
