



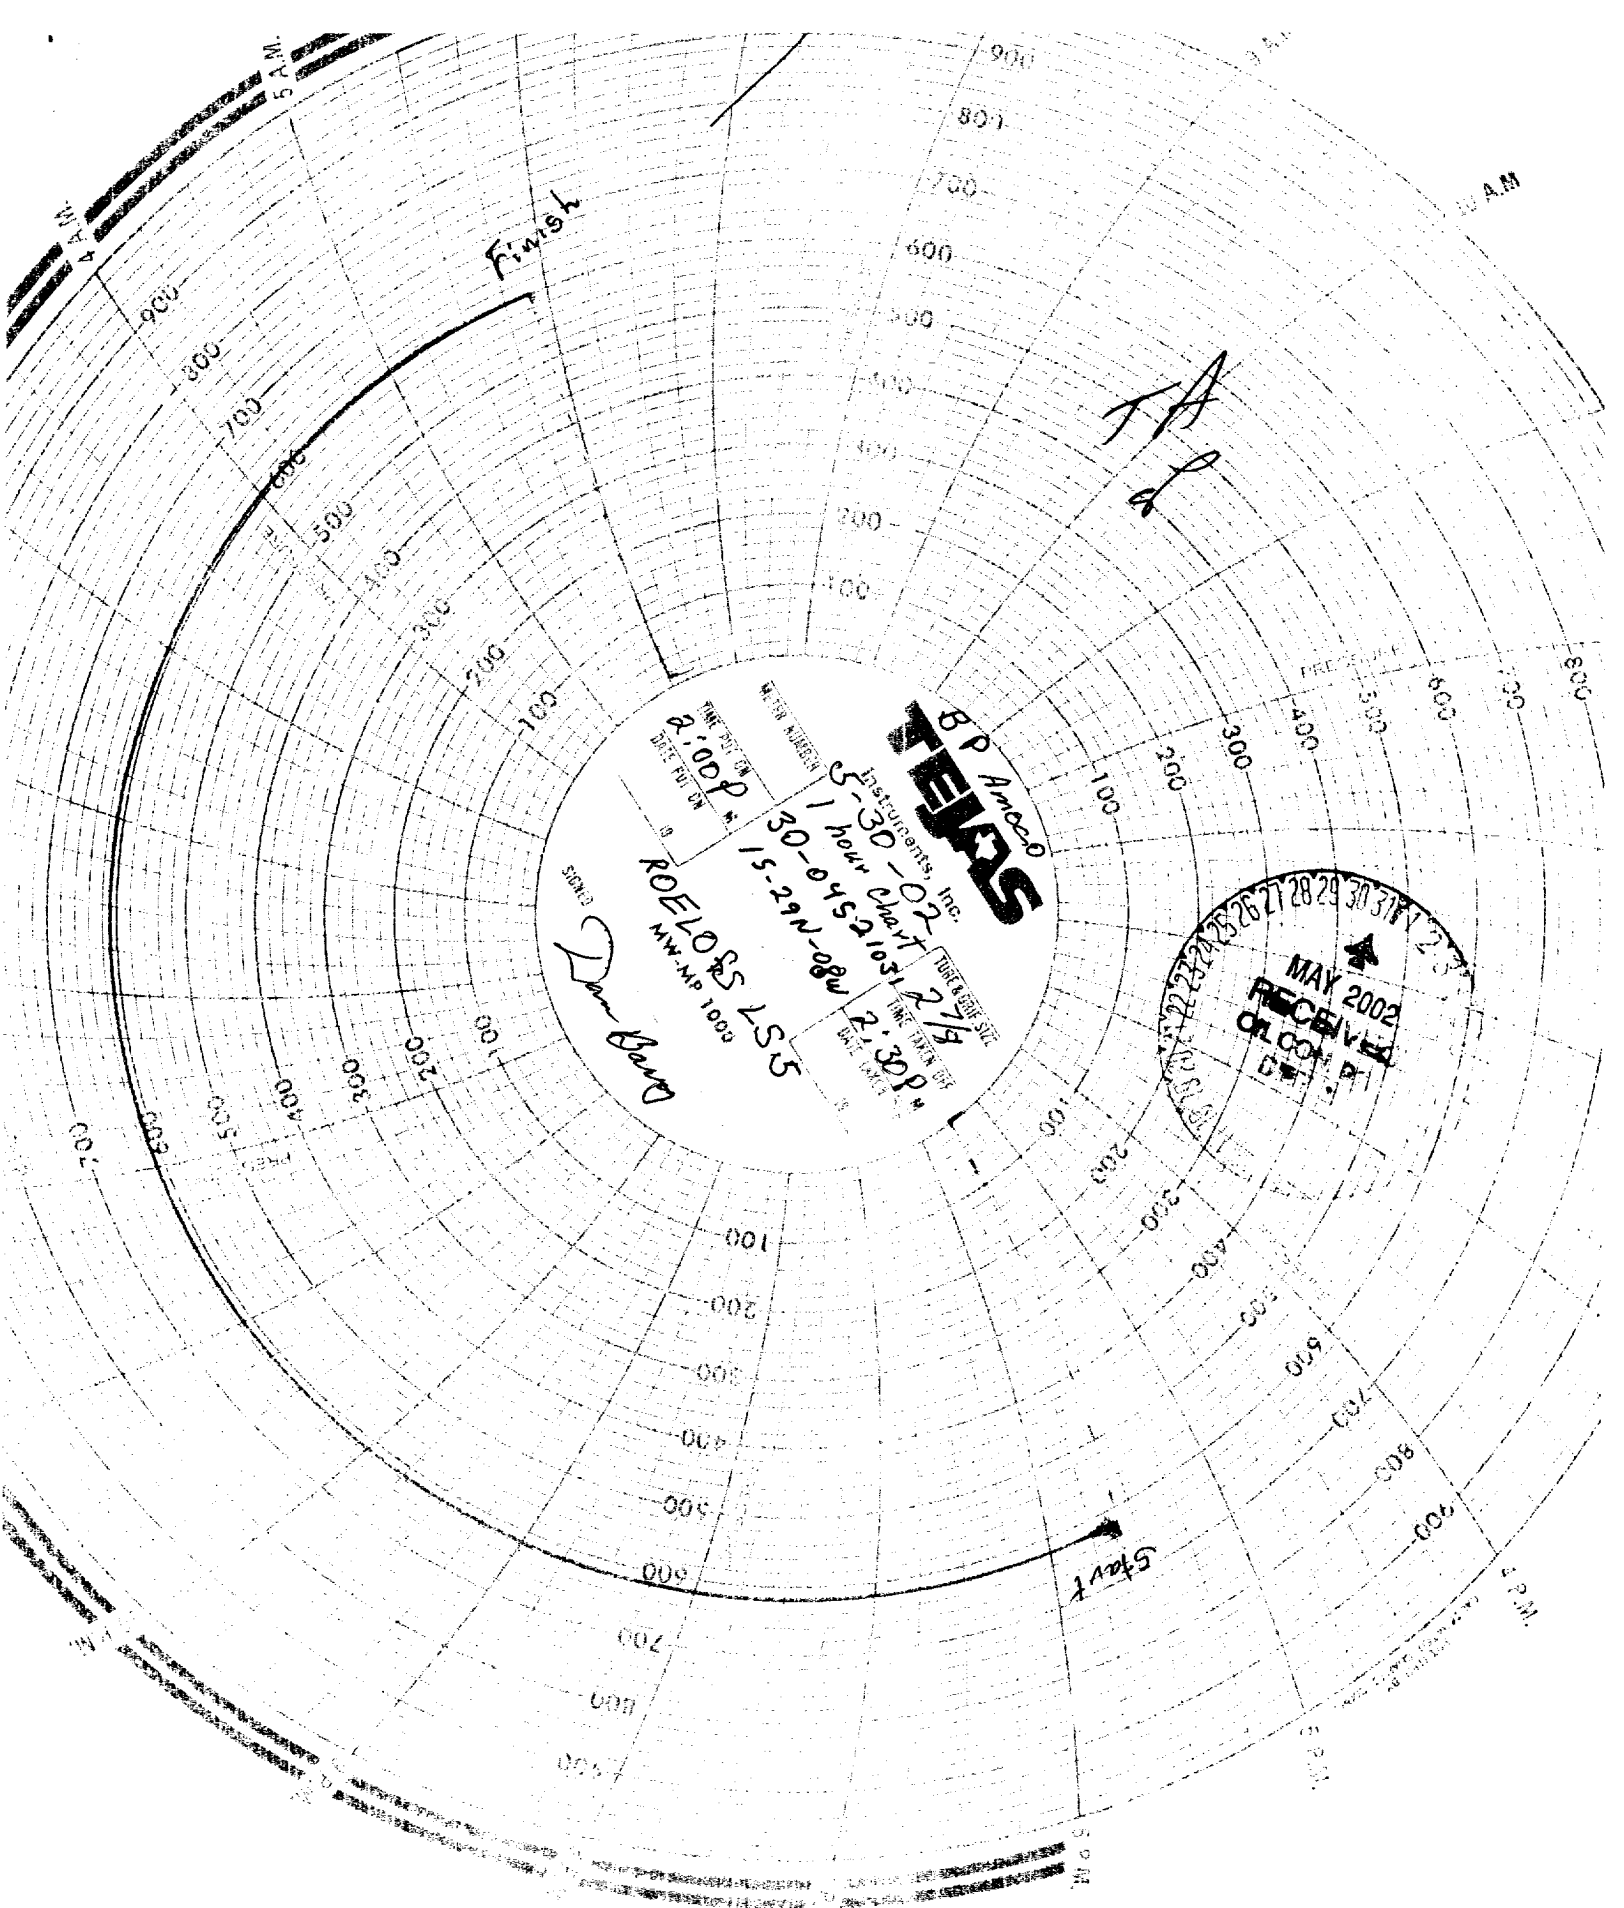

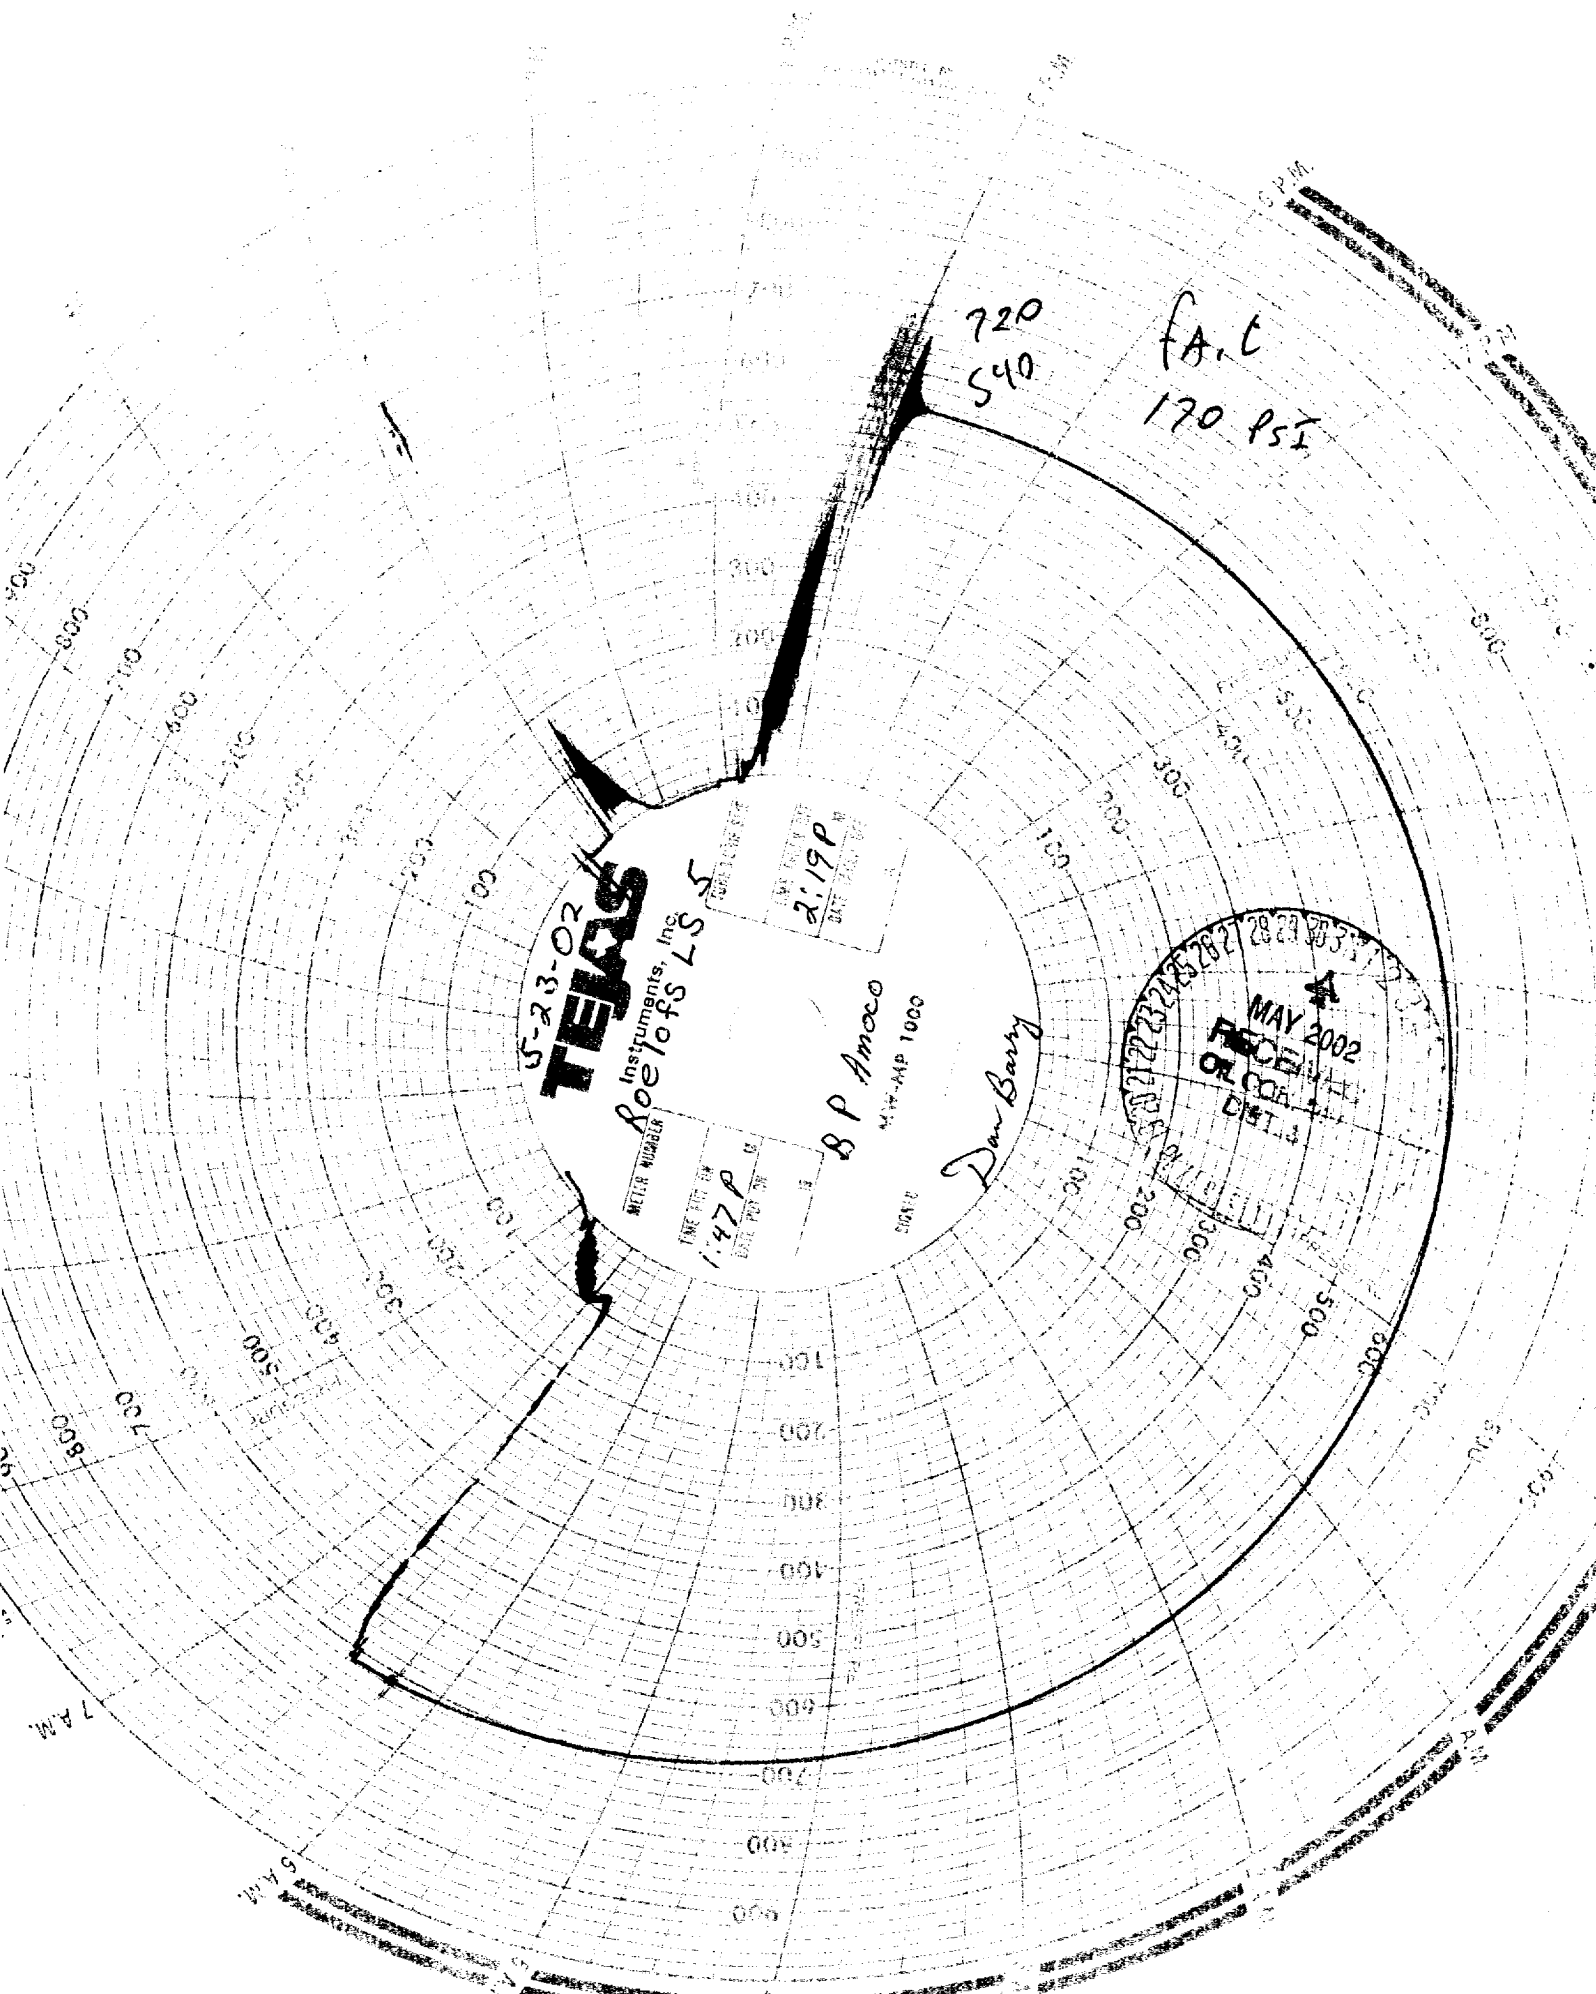

5-23-02
TEJAS

Instruments, Inc.
Roe 10 fs LS 5

METER NUMBER
1:47P

DATE
2:19P

BP Amoco
MAY-MP 1000

Dan Barry

FA.C
170 PSI

MAY 2002
RECEIVED
OFFICE
DET.

LEASE NAME Reelots 155

RUN # _____ DATE 5-28-02

Zero: 6.6.
Csg - 500
RHS: 3148-3436

Comments:

Run 2.343 Gauge Ring
Set G Plug 3100 ft
Pressure Test Csg
for 30 Min Test OK

Fluid Level: _____

S.N.: _____

Tubing Size: _____

End of Tubing 2 7/8" Csg @ 3503

Tag Fill: 3434

PBTD _____

Total Depth _____

FWL 3100



Roelofs LS #5

Sec 15, T29N, R9W

API: 30-045-21031

6750' GL


est. TOC @ surface (circ)

8-5/8" 24# K55 8rd @ 140'
107 cu ft cmt

History:

Completed in May 1973

Est. TOC @ 2210' (tempt surv)



Pictured Cliffs Perforations

3148' - 3436' 30 holes
frac'd w/ 24,000 #'s sand

2-7/8" 6.4# J55 10rd @ 3503'

358 cu ft cmt

PBTD: 3493'

updated: 2/6/02 jad

NOTES:

1. Tubingless completion
