

Submit 1 Copy To Appropriate District Office

District I - (575) 393-6161
1625 N. French Dr., Hobbs, NM 88240
District II - (575) 748-1283
811 S. First St., Artesia, NM 88210
District III - (505) 334-6178
1000 Rio Brazos Rd., Aztec, NM 87410
District IV - (505) 476-3460
1220 S. St. Francis Dr., Santa Fe, NM 87505

State of New Mexico

Energy, Minerals and Natural Resources

HOBBS OGD
MAR 26 2012
CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, NM 87505

RECEIVED

Form C-103

Revised August 1, 2011

SUNDRY NOTICES AND REPORTS ON WELLS (DO NOT USE THIS FORM FOR PROPOSALS TO DRILL OR TO DEEPEN OR PLUG BACK TO A DIFFERENT RESERVOIR. USE "APPLICATION FOR PERMIT" (FORM C-101) FOR SUCH PROPOSALS.)		WELL API NO. 30-025-34264 ✓
1. Type of Well: Oil Well ☐ Gas Well ☐ Other Injection ☒		5. Indicate Type of Lease. STATE ☐ FEE ☒
2. Name of Operator Chesapeake Operating, Inc.		6. State Oil & Gas Lease No.
3. Address of Operator P.O. Box 18496 Oklahoma City, OK 73154-0496		7. Lease Name or Unit Agreement Name CHAMBERS STRAWN UNIT ✓
4. Well Location Unit Letter N : 780' feet from the South line and 1510' feet from the West line Section 8 Township 16S Range 36E NMPM County Lea		8. Well Number 3 ✓
11. Elevation (Show whether DR, RKB, RT, GR, etc.) 3936' GR		9. OGRID Number 147179 ✓
		10. Pool name or Wildcat SHOE BAR; STRAWN, NORTHEAST ✓

12. Check Appropriate Box to Indicate Nature of Notice, Report or Other Data

NOTICE OF INTENTION TO:

PERFORM REMEDIAL WORK ☐ PLUG AND ABANDON ☐
TEMPORARILY ABANDON ☐ CHANGE PLANS ☐
PULL OR ALTER CASING ☐ MULTIPLE COMPL ☐
DOWNHOLE COMMINGLE ☐

SUBSEQUENT REPORT OF:

REMEDIAL WORK ☐ ALTERING CASING ☐
COMMENCE DRILLING OPNS. ☐ P AND A ☐
CASING/CEMENT JOB ☐

OTHER: ☐

OTHER: Pull Tubing/Perform MIT/Return Well to Injection ☒

13. Describe proposed or completed operations. (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work). SEE RULE 19.15.7.14 NMAC. For Multiple Completions: Attach wellbore diagram of proposed completion or recompletion.

Please find work performed on this well form 3/7/12 through 3/15/12. A current well-bore diagram and MIT chart is attached:

3/7/12:

HELD PJSM, MIRU PROWELL WIRELINE TBG & CSG @ 0#, TIH W/ WIRELINE & TAGGED WHAT FEELS TO BE FLAKED OFF IPC @ 11,389' DOWN TO 11,425'. POH W/ WIRELINE, RDMO. HELD PJSM, SPOT LUCKY SERVICES RIG, CONDUCT PARTIAL RIG INSPECTION BUT COULD NOT RIG UP DUE TO HIGH WINDS. SDEN.

3/9/12:

HELD PJSM, MIRU LUCKY WELL SERV., CONDUCT RIG INSPECTION. N/D WH, N/U BOP, DISENGAGED ON/OFF TOOL, POH LAYING DOWN 179 JTS 2 7/8" IPC TBG. SET UP TO SWAB BUT HAD TROUBLE GETTING IN W/ UNDERSIZED SWAB CUPS DUE TO PIECES OF PLASTIC PEELING OFF TBG. SDOWE.

3/12/12:

HELD PJSM CONTINUE POOH LAYING DOWN A TOTAL OF 349 JTS 2 7/8 IPC TBG. RACK AND TALLIED 456 JTS OF NEW 2 7/8 IPC TBG. LOADED TRUCKS W/349 JTS 2 7/8 IPC TBG (SENT TO BE INSPECTED TO SEE WHY COATING IS COMING OFF) R/U HYDRO TESTERS. TIH W/105 JTS TBG--SISDON. (CONTINUED PG. 2)

Spud Date:

Rig Release Date:

I hereby certify that the information above is true and complete to the best of my knowledge and belief.

SIGNATURE

Bryan Arrant

TITLE Regulatory Specialist II

DATE 03/23/2012

Type or print name Bryan Arrant

E-mail address: bryan.arrant@chk.com

PHONE: (405)935-3782

For State Use Only

APPROVED BY:

Bryan Arrant


TITLE

STAFF

DATE 3-27-2012

Conditions of Approval (if any)

MAR 27 2012

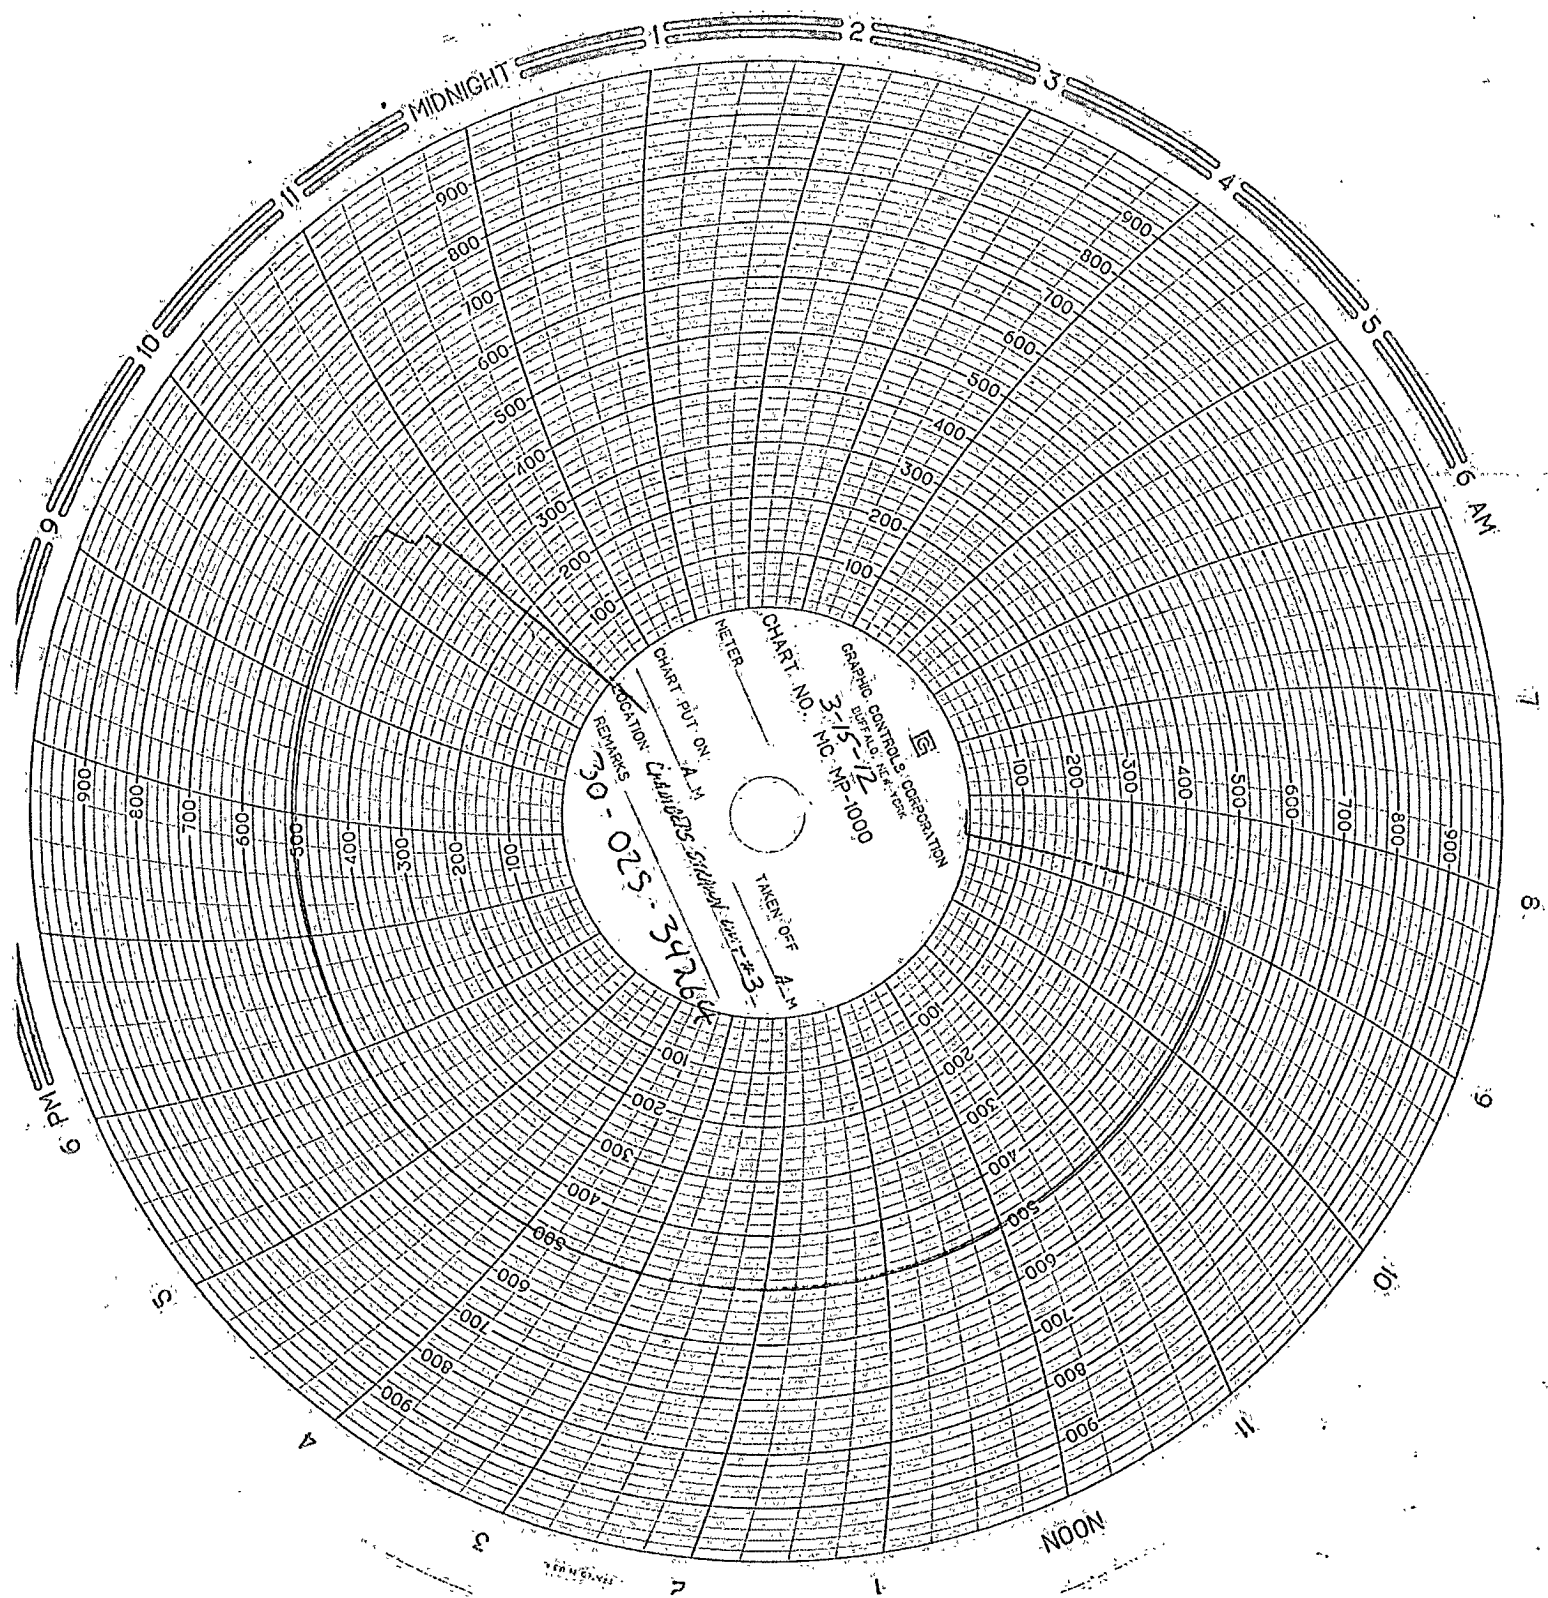

CHAMBERS STRAWN UNIT 3
Unit N, Sec. 8, T-16-S R-36-E
Lea Co., N.M.
30-025-34264
(Continued)

3/13/12:

HELD PJSM CONTINUED HYDRO TESTING IN HOLE W/TBG. SET DOWN ON PKR @ 11,418.96 (359 JTS 2 7/8 L-80 IPC TBG) UNLATCH ON/OFF TOOL--P/U 1 JT AND SISDON

3/14/12:

HELD PJSM DISPLACED CSG W/180 BBLS OF PKR FLUID SET TBG DOWN AND LATCHED ON TO PKR PUMPED 125 BBLS TO LOAD THE CSG--PRESSURED CSG TO 500 PSI FOR 40 MIN--HELD GOOD BLED DOWN PRESSURE OFF OF CSG - SISDON--PREPARE FOR MIT W/OCD IN AM. NOTIFIED MR. MAXIE BROWN W/THE NMOCD TO RUN MIT.

3/15/12:

HELD PJSM R/U PUMP TRUCK - PRESSURE UP CSG TO 500# - CONDUCTED 30 MINUTE MIT TEST WITH CHART - HELD GOOD - BLED OFF PRESSURE R/D PUMP TRUCK & WELL SERVICE RIG - PUT BACK ON INJECTION



Modified Regulatory Wellbore Schematic

CHAMBERS STRAWN UNIT 3

Field: NE Shoe Bar Strawn
County: LEA
State: NEW MEXICO
Elevation: GL 3,936.0 KB 3,952.0 KB Height: 16.0
Location: SEC 8-16S-36E, 780 FSL & 1510 FWL

Spud Date: 1/31/1998
Rig Release Date: 1/31/1998
Initial Compl. Date:
API #: 3002534264
CHK Property #: 812182
1st Sales Date:
PBD: Original Hole: 11,793.0
TD: 11,875.0

VERTICAL - Original Hole, 3/23/2012 12:50:58 PM

Vertical schematic (actual)

