

# PRO WELL TESTING & WI LINE

## FIELD DATA SHEET

COMPANY TEXACO Inc. COMPANY REPRESENTATIVE CLIFFORD JOHNSON

LEASE NAME & NO. EE BLINERY'S FED NCT#1 TEST DATE & TIME 3-19-91 8:00 A.M.

COUNTY LEA STATE N. MEXICO ELEVATION 3324 RT FORMATION JAL-MAT

UNIT K SECTION 21 TOWNSHIP 23S RANGE 39E

TEST TYPE 4-PT. INITIAL ☒ ANNUAL ☐ SPECIAL ☐ TYPE WELL Dual Completion (Langhly Mat)

COMPLETION DATE 3-19-91 TDE 3608 PBTDE OSH 3490-3607 PKR@ 2962, 3327

CONNECTION  METER RUN 2.067 TAPS FLANGE

CASING SIZE 7" WT. 20#, 23# DIA. 6.456, 6.366 SET@ 3490

TUBING SIZE 2 3/8 WT. 4.7# DIA. 2" SET@ 2976


PERFORATIONS FROM 2983' TO 3223'

PRODUCING THRU PRO-WELL TESTING SEPARATOR.

| TIME<br>DATE | ELAP.<br>HR | TBG.<br>PRES | CASING<br>PRES | W/H<br>TEMP | METER OR PROVER |           |      | ORIF.<br>SIZE | CHOKE<br>SIZE | MCFD | REMARKS              |
|--------------|-------------|--------------|----------------|-------------|-----------------|-----------|------|---------------|---------------|------|----------------------|
|              |             |              |                |             | PRES            | DIFF      | TEMP |               |               |      |                      |
| 8:00AM       | .0          | START        | 4-POINT        | TEST        | THRU            | SEPARATOR | TO   |               | 645           |      |                      |
| 8:15AM       | .15         | 150          | 0              | N/A         | 50              | 16        | N/A  | 1.500         | 25/64         | 503  | 1 <sup>st</sup> RATE |
| 8:30AM       | .30         | 150          | 0              | N/A         | 50              | 16        | N/A  | 1.500         | 25/64         | 503  |                      |
| 8:45AM       | .45         | 150          | 0              | N/A         | 50              | 16        | N/A  | 1.500         | 25/64         | 503  |                      |
| 9:00AM       | 1.0         | 150          | 0              | N/A         | 50              | 16        | N/A  | 1.500         | 25/64         | 503  |                      |
| 9:15AM       | 1.25        | 200          | 0              | N/A         | 50              | 9         | N/A  | 1.500         | 17 1/2/64     | 377  | 2 <sup>nd</sup> RATE |
| 9:30AM       | 1.50        | 220          | 0              | N/A         | 50              | 9         | N/A  | 1.500         | 17 1/2/64     | 377  |                      |
| 9:45AM       | 1.75        | 225          | 0              | N/A         | 50              | 9         | N/A  | 1.500         | 17 1/2/64     | 377  |                      |
| 10:00AM      | 2.0         | 225          | 0              | N/A         | 50              | 9         | N/A  | 1.500         | 17 1/2/64     | 377  |                      |
| 10:15AM      | 2.25        | 255          | 0              | N/A         | 50              | 4         | N/A  | 1.500         | 14/64         | 251  | 3 <sup>rd</sup> RATE |
| 10:30AM      | 2.50        | 255          | 0              | N/A         | 50              | 4         | N/A  | 1.500         | 14/64         | 251  |                      |
| 10:45AM      | 2.75        | 255          | 0              | N/A         | 50              | 5         | N/A  | 1.500         | 14/64         | 281  |                      |
| 11:00AM      | 3.0         | 255          | 0              | N/A         | 50              | 5         | N/A  | 1.500         | 14/64         | 281  |                      |
| 11:15AM      | 3.25        | 270          | 0              | N/A         | 50              | 2         | N/A  | 1.500         | 10 1/2/64     | 178  | 4 <sup>th</sup> RATE |
| 11:30AM      | 3.50        | 275          | 0              | N/A         | 50              | 2         | N/A  | 1.500         | 10 1/2/64     | 178  |                      |
| 11:45AM      | 3.75        | 280          | 0              | N/A         | 50              | 2         | N/A  | 1.500         | 10 1/2/64     | 178  |                      |
| 12:00PM      | 4.0         | 280          | 0              | N/A         | 50              | 2         | N/A  | 1.500         | 10 1/2/64     | 178  |                      |
|              |             | SHUT-IN      | @ 12:00 PM.    |             |                 |           |      |               |               |      |                      |
|              |             |              |                |             |                 |           |      |               |               |      |                      |
|              |             |              |                |             |                 |           |      |               |               |      |                      |
|              |             |              |                |             |                 |           |      |               |               |      |                      |
|              |             |              |                |             |                 |           |      |               |               |      |                      |
|              |             |              |                |             |                 |           |      |               |               |      |                      |
|              |             |              |                |             |                 |           |      |               |               |      |                      |
|              |             |              |                |             |                 |           |      |               |               |      |                      |
|              |             |              |                |             |                 |           |      |               |               |      |                      |

1 hr. SI ↑ 550#

03-20-91 FOUR POINT TEST: FIRST PIONT, TBG PRESS=150#, 25/64 CHK 503 MCFPD;  
 SECOND POINT, TBG PRESS=225#, 17.5/64 CHK 377 MCFPD; THIRD POINT, TBG  
 PRESS=255#, 14/64 CHK 281 MCFPD; FORTH POINT, TBG PRESS=280#, 10.5/64 CHK NO  
 FLUID, SI 12:00 PM, RDPRO WELL TESTING, 1 HR SITP 350#

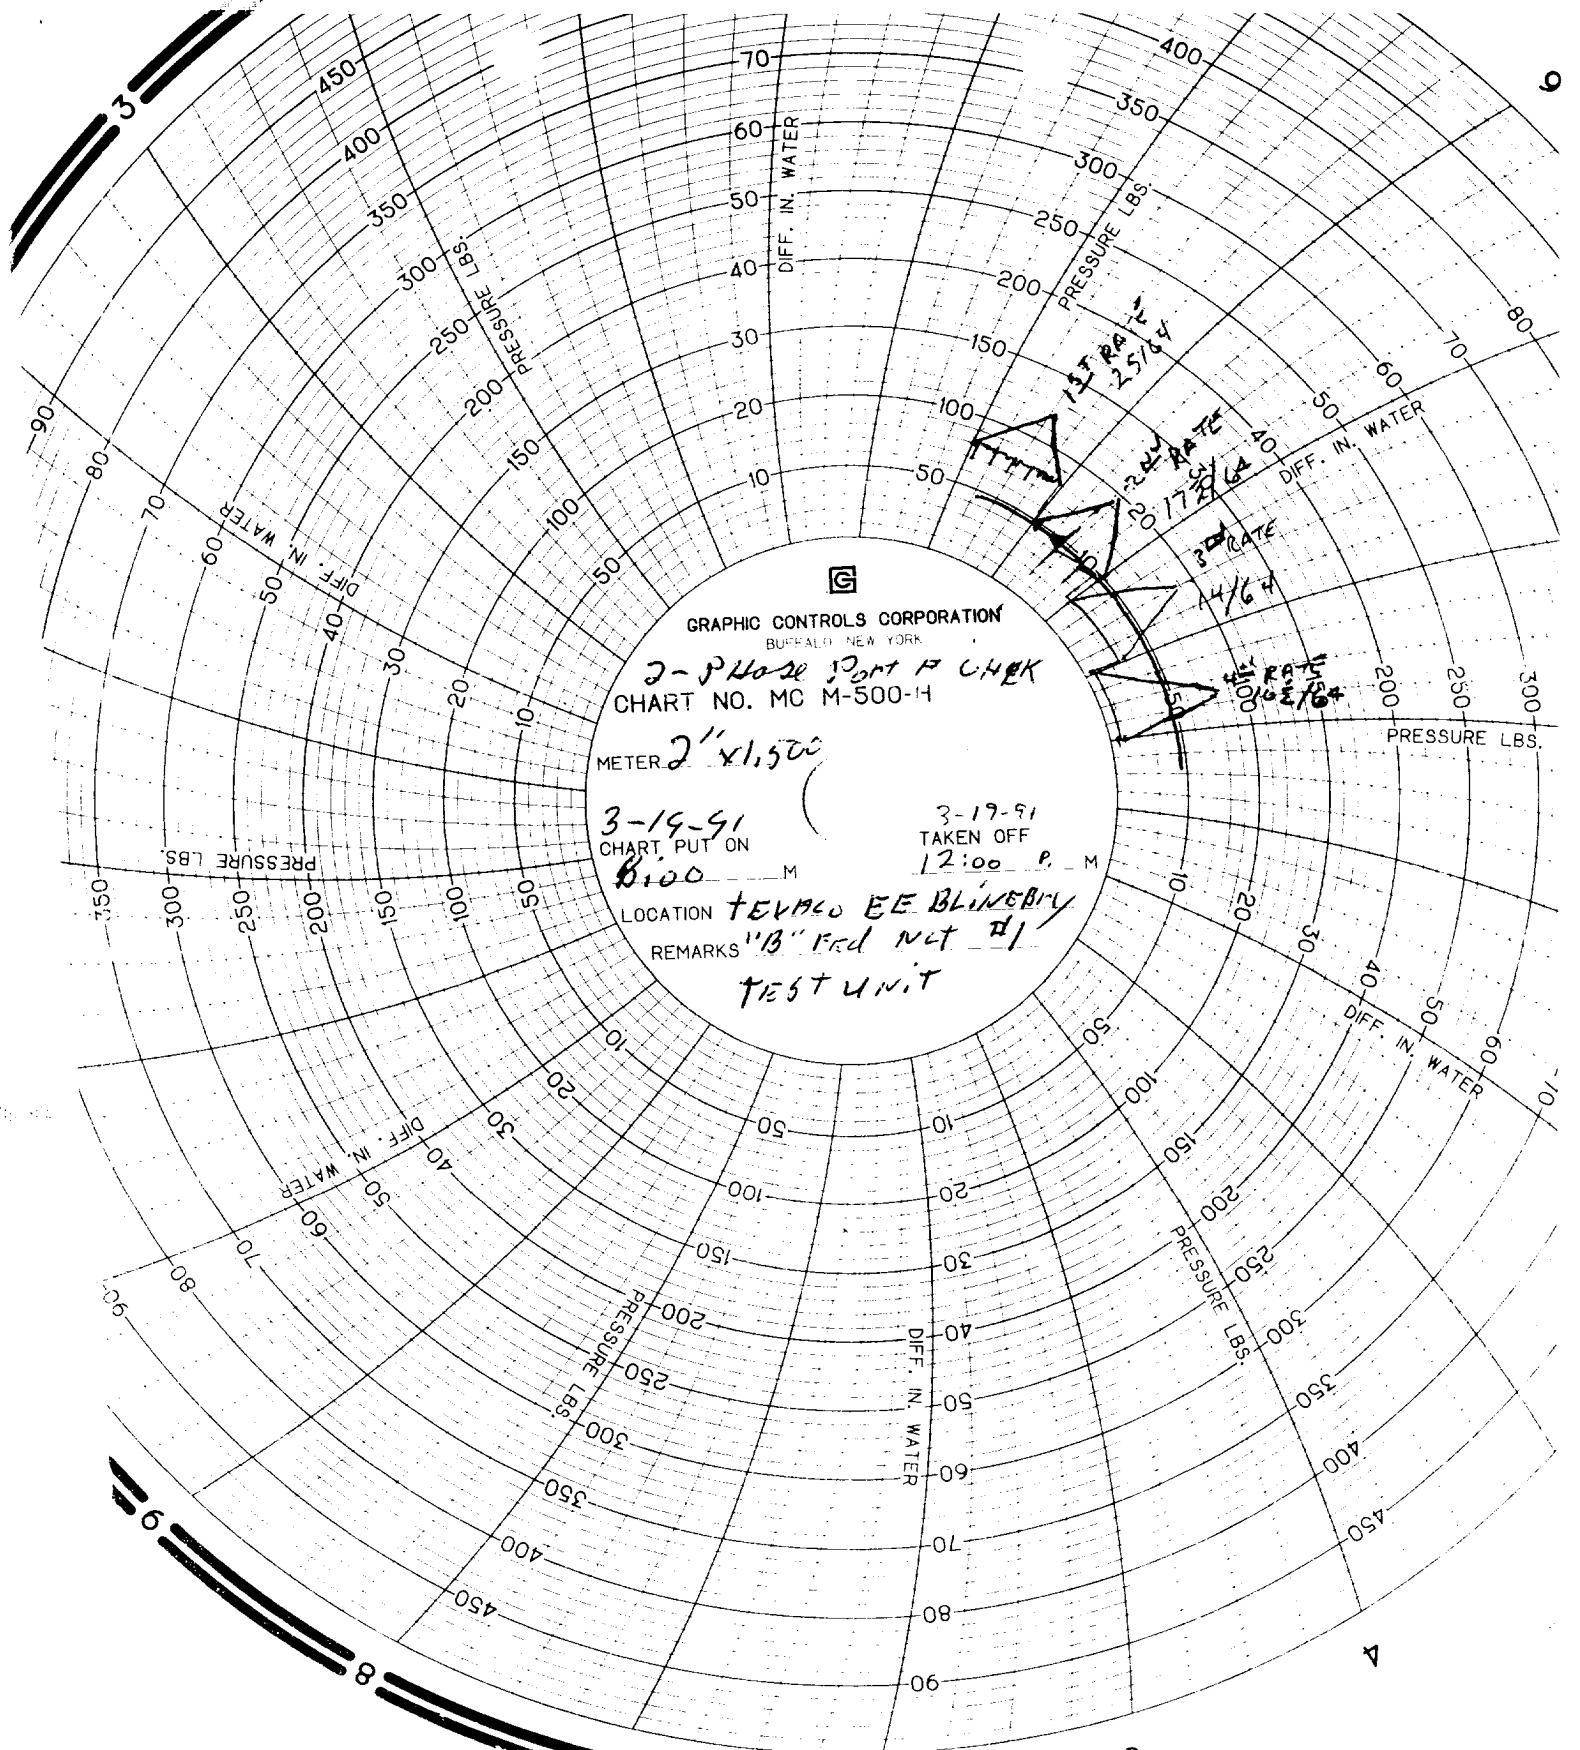

RECEIVED

OCT 21 1991

HOBBS OFFICE
