


Humble Oil & Refining Co. "Federal Knox #1"

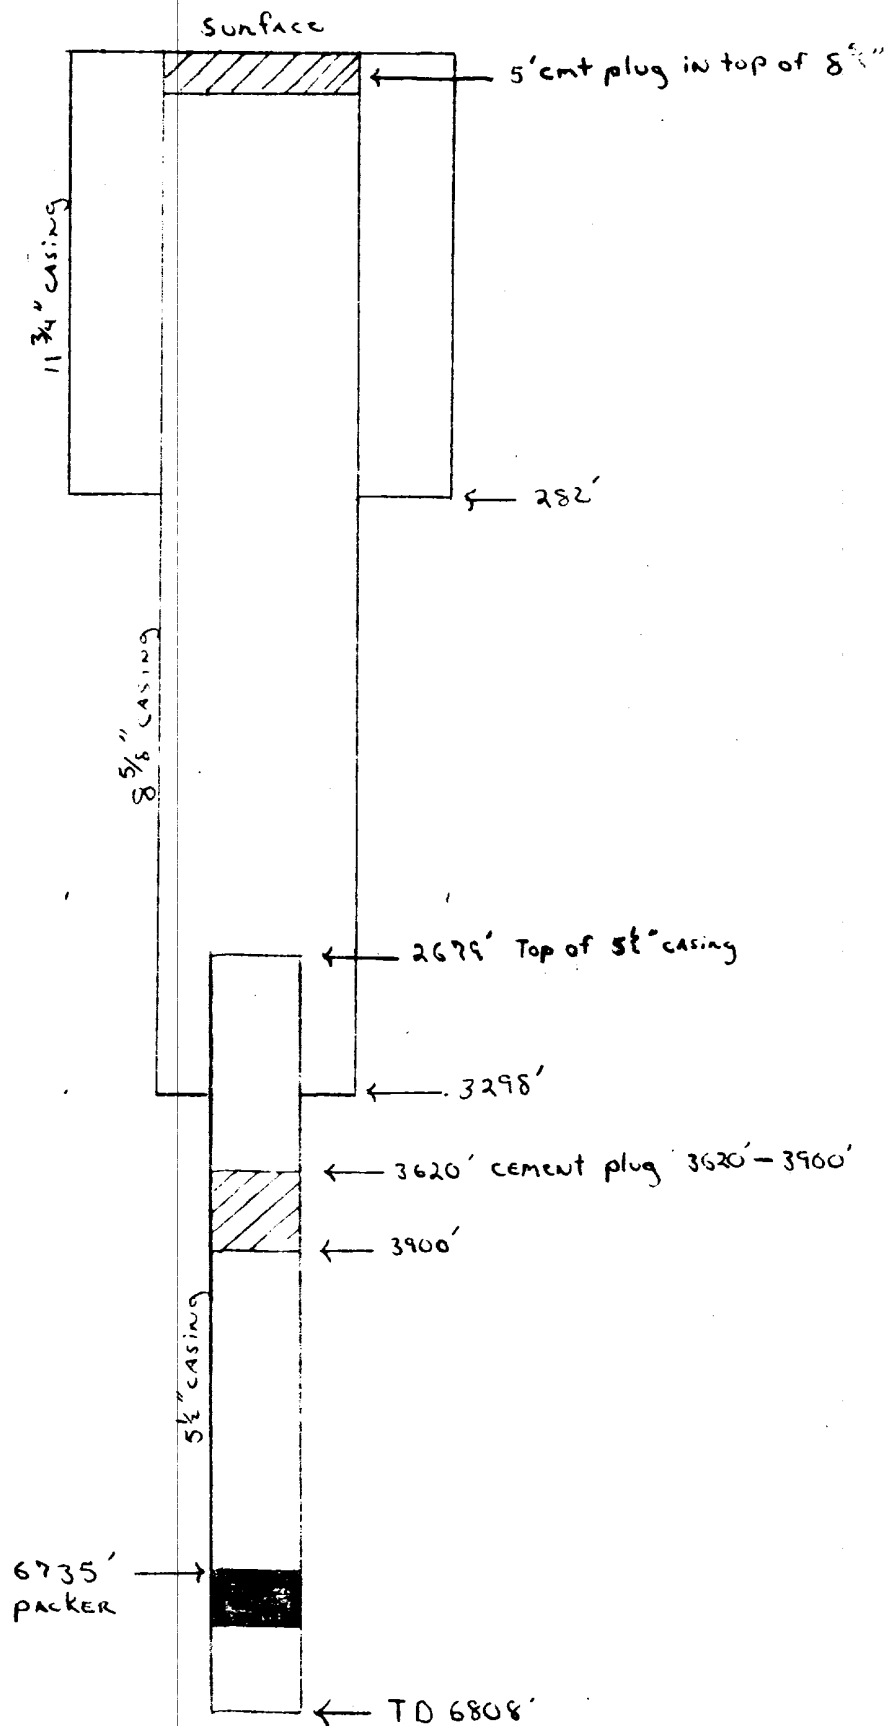

RECEIVED
FEB 28 1983
O.C.D.
HOBBS OFFICE

HUMBLE OIL AND REFINING COMPANY

"FEDERAL KNOX #2"

330' FSL & 660' FWL Sec 18, T24-S, R38-E Elevation: 38185' DF

Casing: 8-5/8" 24# @ 1266' Cemented w/900 sxs
5-1/2" @ 6800' Cemented w/495 sxs

Date Drilled: May 11, 1958

TD: 6800'


Completion: Perforation - 6749-62 w/2 shots per foot, acidize w/500 gal.,
acidize w/3,000 gal., squeezed w/75 sxs
Perforation - 6711-19 w/2 shots per foot, acidize w/500 gal.,
acidize w/3,000 gal.
Perforation - 6723-27 w/4 jet shots per foot, acidize w/5,000 gal.
frac w/10,000 gals refined oil and 10,000 # sand.

Plug & Abandon: Spotted cost, plug area perforation in 5-1/2" casing from
6711 - 6727' with 25 sxs neat cement. Cut off 5-1/2" csg.
@ 3533' and pulled from this depth. Removed wellhead,
spotted cement plug from 1325' to 1175' w/40 sxs regular
cement. Set cement plug from 25' to surface.

RECEIVED
FEB 28 1983
O.C.D.
HOBBS OFFICE

Humble Oil & Refining Co.

"Federal Knox #2"

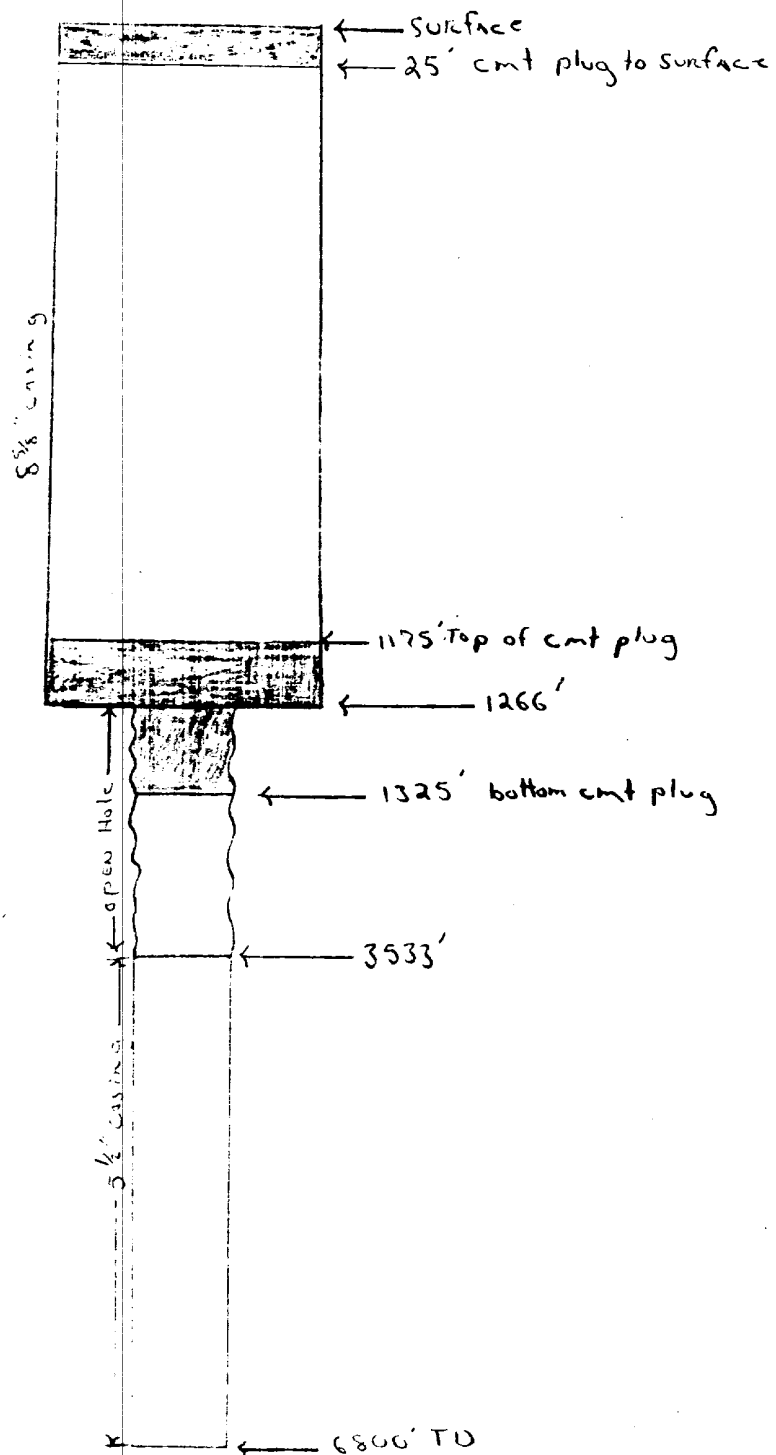

RECEIVED
FEB 28 1983
O.C.D.
HOBBS OFFICE
