

District I
1625 N. French Dr., Hobbs, NM 88240
District II
811 S. First St., Artesia, NM 88210
District III
1000 Rio Brazos Rd., Aztec, NM 87410
District IV
1220 S. St. Francis Dr., Santa Fe, NM 87505

State of New Mexico
Energy, Minerals & Natural
Resources

Form C-104
Revised August 1, 2011

Submit one copy to appropriate District Office

Oil Conservation Division
1220 South St. Francis Dr.

☐ AMENDED REPORT

I. REQUEST FOR ALLOWABLE MINERAL AUTHORIZATION TO TRANSPORT

¹ Operator name and Address EOG RESOURCES INC PO BOX 2267 MIDLAND, TEXAS 79702		² OGRID Number 7377	
		³ Reason for Filing Code/ Effective Date NW 06/23/2021	
⁴ API Number 30 - 025-46966	⁵ Pool Name BOBCAT DRAW; UPPER WOLFCAMP		⁶ Pool Code 98094
⁷ Property Code 39180	⁸ Property Name VACA 24 FEDERAL COM		⁹ Well Number 707H

II. ¹⁰ Surface Location

Ul or lot no. O	Section 24	Township 25S	Range 33E	Lot Idn	Feet from the 618	North/South Line SOUTH	Feet from the 2471	East/West line EAST	County LEA
--------------------	---------------	-----------------	--------------	---------	----------------------	---------------------------	-----------------------	------------------------	---------------

¹¹ Bottom Hole Location

UL or lot no. B	Section 13	Township 25S	Range 33E	Lot Idn	Feet from the 111	North/South line NORTH	Feet from the 1668	East/West line EAST	County LEA
¹² Lse Code	¹³ Producing Method Code FLOWING	¹⁴ Gas Connection Date	¹⁵ C-129 Permit Number		¹⁶ C-129 Effective Date		¹⁷ C-129 Expiration Date		

III. Oil and Gas Transporters

¹⁸ Transporter OGRID	¹⁹ Transporter Name and Address	²⁰ O/G/W
372812	EOGRM	OIL
151618	ENTERPRISE FIELD SERVICES	GAS
298751	REGENCY FIELD SERVICES	GAS
36785	DCP MIDSTREAM	GAS

IV. Well Completion Data

²¹ Spud Date 01/08/2021	²² Ready Date 06/23/2021	²³ TD 22,765'	²⁴ PBTd 22,726	²⁵ Perforations 12,733 - 22,726'	²⁶ DHC, MC
²⁷ Hole Size		²⁸ Casing & Tubing Size		²⁹ Depth Set	
12 1/4"		9 5/8"		1209'	
8 3/4"		7 5/8"		11,908'	
6 3/4"		5 1/2"		22,735'	

V. Well Test Data

³¹ Date New Oil 06/23/2021	³² Gas Delivery Date 06/23/2021	³³ Test Date 06/28/2021	³⁴ Test Length 24 HRS	³⁵ Tbg. Pressure	³⁶ Csg. Pressure 3847
³⁷ Choke Size 34	³⁸ Oil 3932	³⁹ Water 5708	⁴⁰ Gas 6588		⁴¹ Test Method
⁴² I hereby certify that the rules of the Oil Conservation Division have been complied with and that the information given above is true and complete to the best of my knowledge and belief. Signature: Kay Maddox			OIL CONSERVATION DIVISION		
Printed name: Kay Maddox			Approved by: KURT SIMMONS		
Title: SENIOR REGULATORY SPECIALIST			Title: NMOCd, SANTA FE		
E-mail Address: kay_maddox@eogresources.com			Approval Date: 08/20/2021		
Date: 06/30/2021		Phone: 432-638-8475			

District I
1625 N. French Dr., Hobbs, NM 88240
Phone: (575) 393-6161 Fax: (575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone: (575) 748-1283 Fax: (575) 748-9720
District III
1000 Rio Brazos Road, Aztec, NM 87410
Phone: (505) 334-6178 Fax: (505) 334-6170
District IV
1220 S. St. Francis Dr., Santa Fe, NM 87505
Phone: (505) 476-3460 Fax: (505) 476-3462

State of New Mexico
Energy, Minerals & Natural Resources
Department
OIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, NM 87505

FORM C-102

Revised August 1, 2011

Submit one copy to appropriate

District Office

☐ AMENDED REPORT

WELL LOCATION AND ACREAGE DEDICATION PLAT

¹ API Number 30-025-46966	² Pool Code 98094	³ Pool Name BOBCAT DRAW; UPPER WOLFCAMP
⁴ Property Code 39180	⁵ Property Name VACA 24 FED COM	⁶ Well Number 707H
⁷ OGRID No. 7377	⁸ Operator Name EOG RESOURCES, INC.	⁹ Elevation 3332'

¹⁰Surface Location


UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
0	24	25-S	33-E	-	618'	SOUTH	2471'	EAST	LEA

¹¹Bottom Hole Location If Different From Surface

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
B	13	25-S	33-E	-	111'	NORTH	1668'	EAST	LEA

¹² Dedicated Acres 640	¹³ Joint or Infill	¹⁴ Consolidation Code	¹⁵ Order No.
---	-------------------------------	----------------------------------	-------------------------

No allowable will be assigned to this completion until all interests have been consolidated or a non-standard unit has been approved by the division.

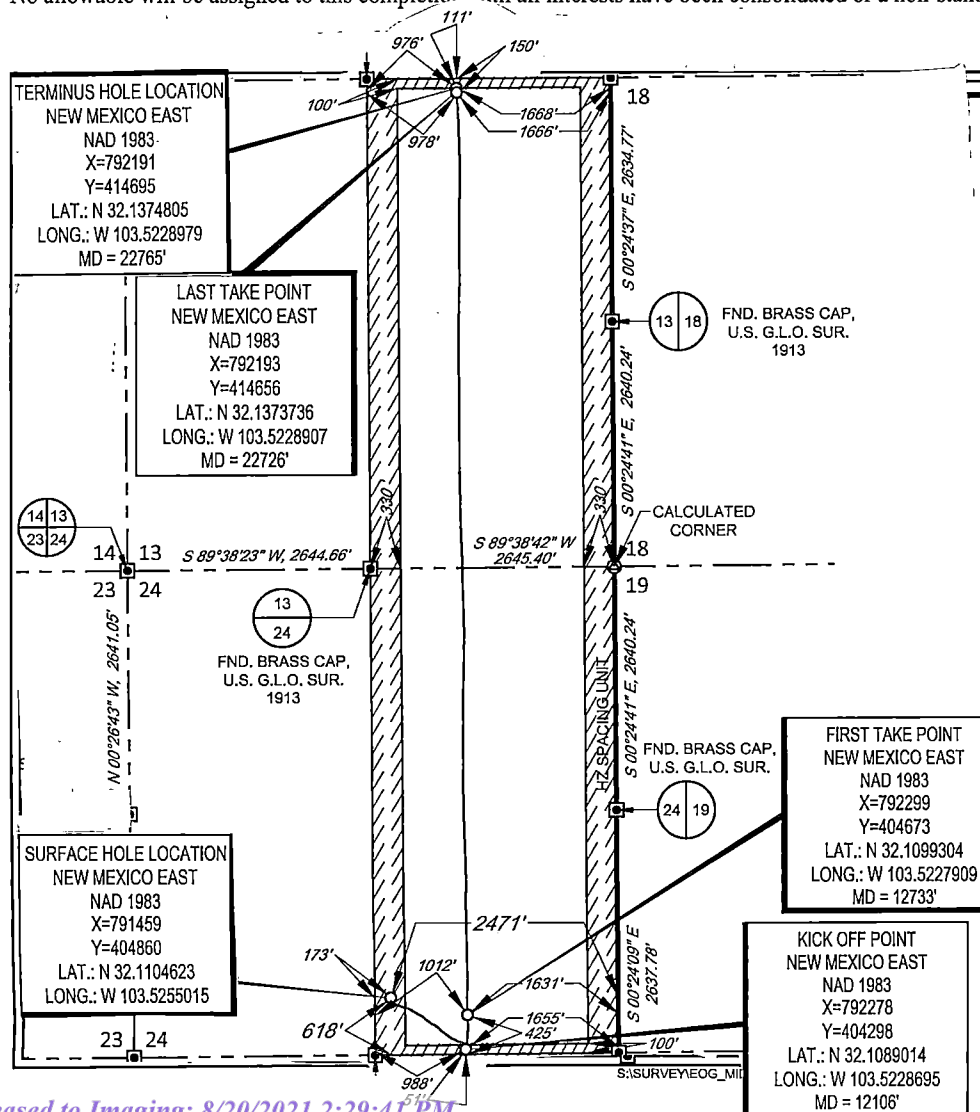¹⁷OPERATOR CERTIFICATION

I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief, and that this organization either owns a working interest or unleased mineral interest in the land including the proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of such a mineral or working interest, or to a voluntary pooling agreement or a compulsory pooling order heretofore entered by the division.

Kay Maddox 06/29/2021
Signature Date

KAY MADDOX

Printed Name

KAY_MADDOX@EOGRESOURCES.COM

E-mail Address

¹⁸SURVEYOR CERTIFICATION

I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true to the best of my belief.


04/13/2019

Date of Survey
Signature and Seal of Professional Surveyor

Ramon A. Dominguez
NEW MEXICO
24508
PROFESSIONAL SURVEYOR

Certificate Number

/ACA_24_FED_COM_707H_REV1.DWG 12/15/2020 9:57:36 AM rdominguez

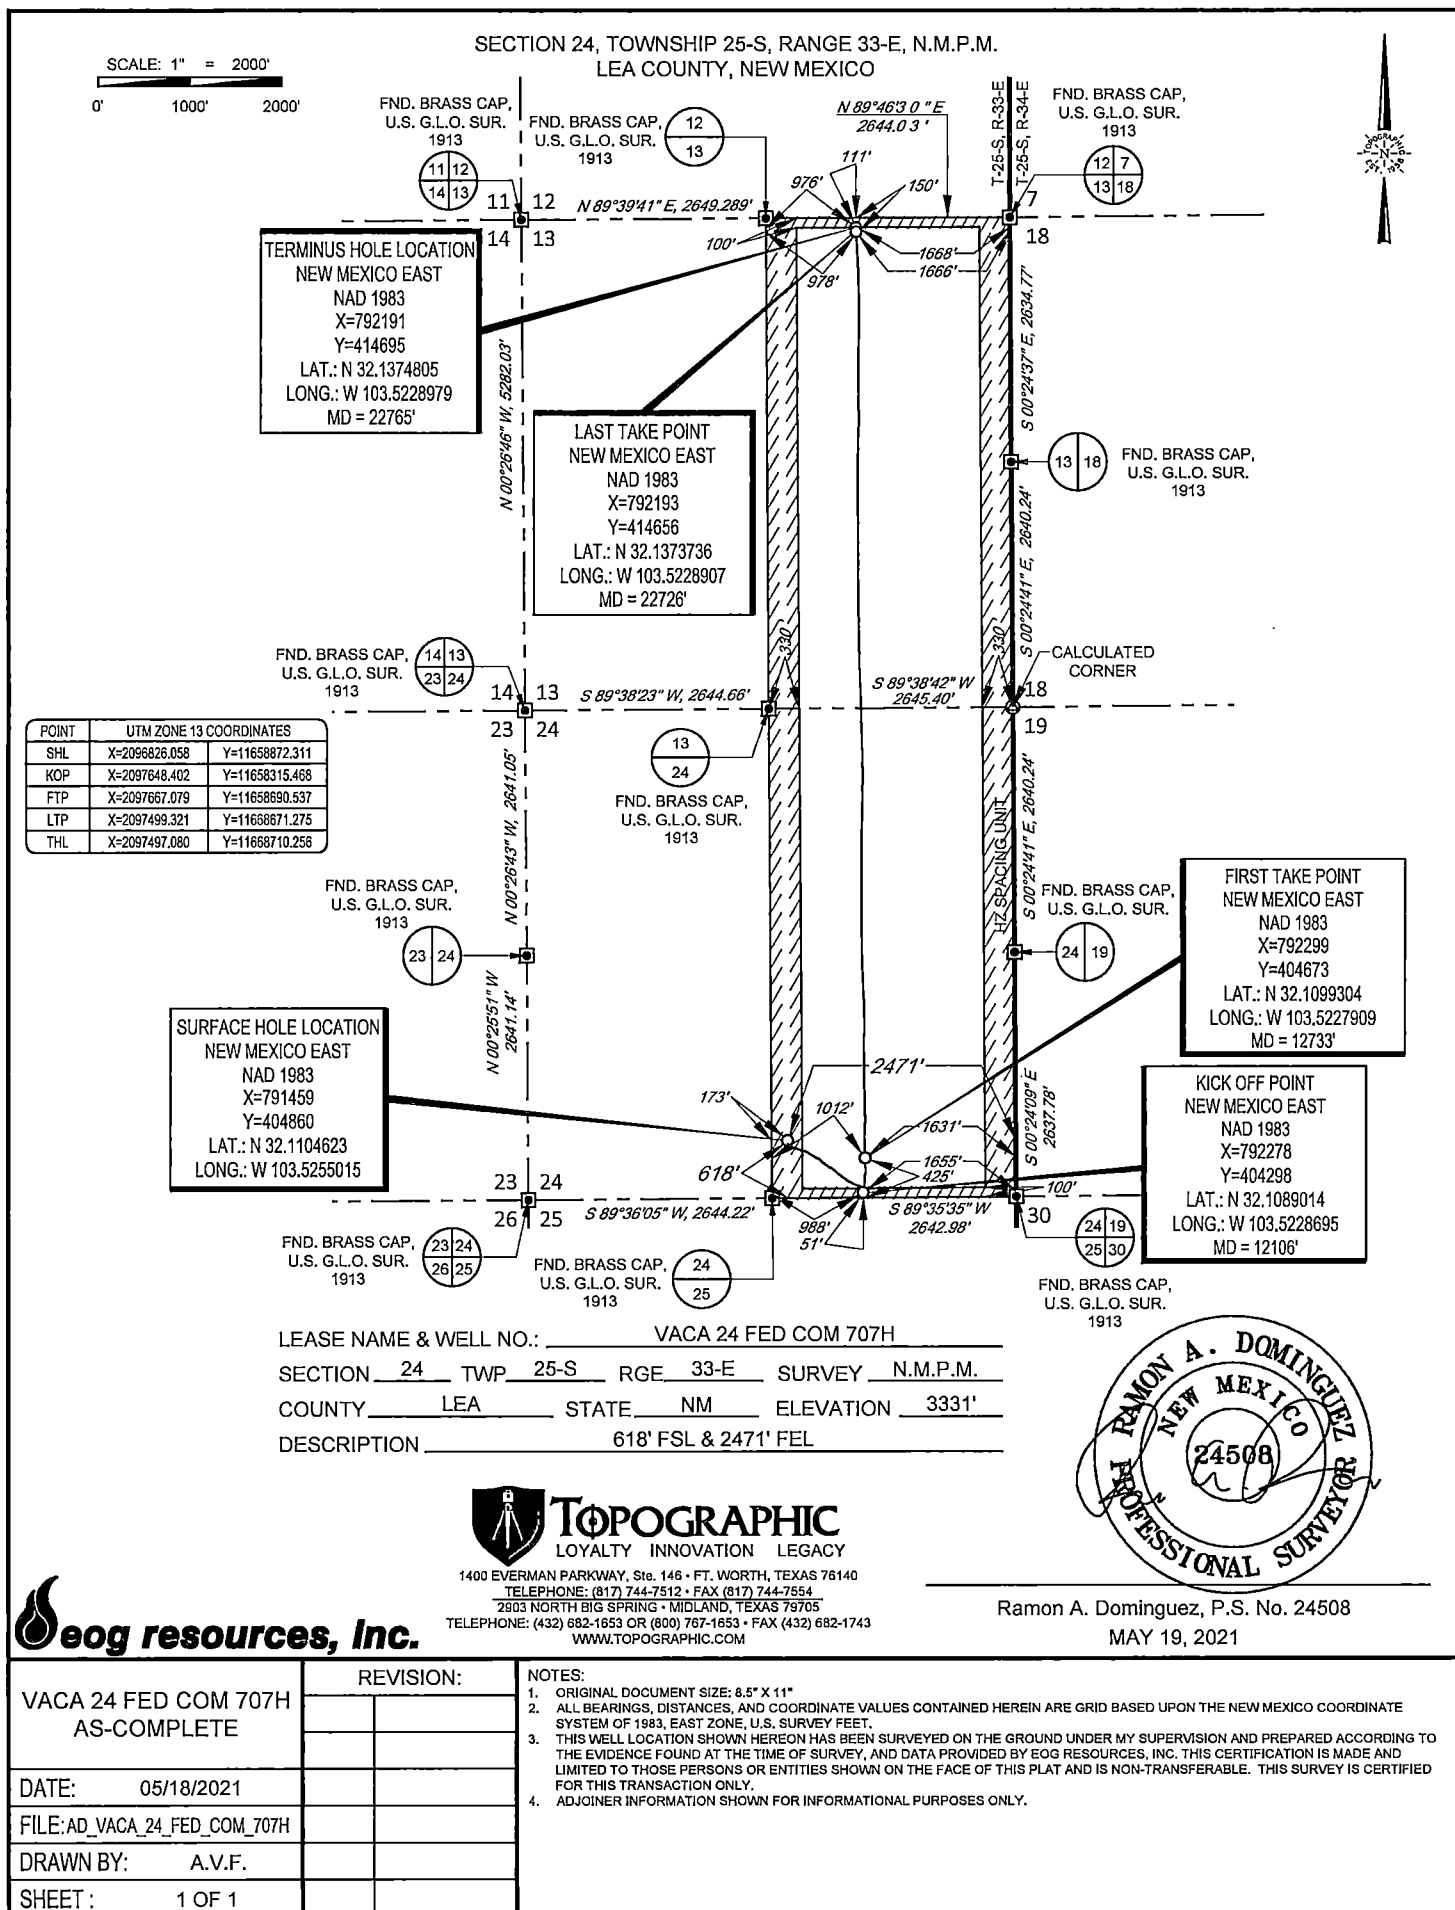



EOG Resources - Midland

Lea County, NM (NAD 83 NME)

Vaca 24 Fed Com

#707H

OH

Design: OH

Midland PVA

23 February, 2021



EOG Resources

Midland PVA

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #707H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 26' @ 3358.0usft
Site:	Vaca 24 Fed Com	MD Reference:	KB = 26' @ 3358.0usft
Well:	#707H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM

Project	Lea County, NM (NAD 83 NME)		
Map System:	US State Plane 1983	System Datum:	Mean Sea Level
Geo Datum:	North American Datum 1983		
Map Zone:	New Mexico Eastern Zone		

Site	Vaca 24 Fed Com		
Site Position:		Northing:	404,270.00 usft
From:	Map	Easting:	789,366.00 usft
Position Uncertainty:	0.0 usft	Slot Radius:	13-3/16 "
		Latitude:	32° 6' 31.982 N
		Longitude:	103° 31' 56.186 W
		Grid Convergence:	0.43 °

Well		#707H				
Well Position	+N/-S	0.0 usft	Northing:	404,860.00 usft	Latitude:	32° 6' 37.666 N
	+E/-W	0.0 usft	Easting:	791,459.00 usft	Longitude:	103° 31' 31.802 W
Position Uncertainty		0.0 usft	Wellhead Elevation:	usft	Ground Level:	3,332.0 usft

Wellbore	OH				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	IGRF2020	2/8/2021	6.56	59.82	47,468.09127271

Design	OH				
Audit Notes:					
Version:	1.0	Phase:	ACTUAL	Tie On Depth:	0.0
Vertical Section:	Depth From (TVD) (usft)	+N/-S (usft)	+E/-W (usft)	Direction (°)	
	0.0	0.0	0.0	4.36	

Survey Program	Date	2/23/2021			
From (usft)	To (usft)	Survey (Wellbore)	Tool Name	Description	
187.0	22,765.0	Driltech MWD (OH)	EOG MWD+IFR1	MWD + IFR1	



EOG Resources

Midland PVA

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #707H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 26' @ 3358.0usft
Site:	Vaca 24 Fed Com	MD Reference:	KB = 26' @ 3358.0usft
Well:	#707H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM

Survey											
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)	
0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.00	0.0	0.0	
187.0	1.49	264.84	187.0	-0.2	-2.4	0.80	0.80	0.00	-2.4	0.0	
302.0	1.32	263.17	301.9	-0.5	-5.2	0.15	-0.15	-1.45	-5.2	-0.1	
392.0	1.32	260.36	391.9	-0.8	-7.3	0.07	0.00	-3.12	-7.3	-0.4	
483.0	1.41	252.18	482.9	-1.3	-9.4	0.24	0.10	-8.99	-9.3	-1.6	
571.0	1.32	242.34	570.9	-2.1	-11.3	0.28	-0.10	-11.18	-11.0	-3.4	
765.0	1.58	163.50	764.8	-5.7	-12.5	0.95	0.13	-40.64	-1.9	-13.6	
860.0	1.67	165.88	859.8	-8.3	-11.8	0.12	0.09	2.51	-5.2	-13.5	
957.0	1.49	166.58	956.7	-10.9	-11.2	0.19	-0.19	0.72	-8.0	-13.4	
1,053.0	1.41	170.71	1,052.7	-13.3	-10.7	0.14	-0.08	4.30	-11.4	-12.7	
1,155.0	1.41	170.71	1,154.7	-15.8	-10.3	0.00	0.00	0.00	-13.9	-12.7	
1,335.0	2.02	191.80	1,334.6	-21.1	-10.6	0.48	0.34	11.72	-22.3	-7.2	
1,434.0	3.87	144.61	1,433.5	-25.5	-9.0	2.93	1.87	-47.67	-10.0	-24.2	
1,527.0	6.16	128.26	1,526.1	-31.2	-3.3	2.88	2.46	-17.58	-3.4	-27.4	
1,623.0	10.20	123.51	1,621.1	-39.0	7.9	4.26	4.21	-4.95	-3.9	-27.9	
1,719.0	12.31	124.74	1,715.3	-49.6	23.4	2.21	2.20	1.28	-9.3	-27.7	
1,815.0	12.22	127.73	1,809.1	-61.6	39.8	0.67	-0.09	3.11	-15.5	-27.6	
1,911.0	11.61	118.50	1,903.0	-72.4	56.3	2.08	-0.64	-9.61	-15.2	-29.8	
2,007.0	12.13	106.02	1,997.0	-79.8	74.5	2.72	0.54	-13.00	-13.3	-29.5	
2,103.0	11.96	106.55	2,090.9	-85.5	93.8	0.21	-0.18	0.55	-18.7	-24.5	
2,199.0	11.87	108.92	2,184.8	-91.5	112.6	0.52	-0.09	2.47	-24.5	-19.2	
2,295.0	11.87	108.66	2,278.8	-97.8	131.3	0.06	0.00	-0.27	-29.2	-15.1	
2,391.0	11.43	107.16	2,372.8	-103.8	149.8	0.56	-0.46	-1.56	-33.2	-11.5	
2,487.0	11.34	106.29	2,466.9	-109.3	167.9	0.20	-0.09	-0.91	-37.2	-7.4	
2,583.0	11.70	104.79	2,561.0	-114.4	186.4	0.49	0.37	-1.56	-41.5	-3.4	
2,679.0	13.19	118.33	2,654.7	-122.1	205.4	3.40	1.55	14.10	-46.1	10.3	
2,775.0	14.51	123.07	2,747.9	-133.8	225.2	1.81	1.37	4.94	-52.5	15.2	



EOG Resources

Midland PVA

Company: EOG Resources - Midland
Project: Lea County, NM (NAD 83 NME)
Site: Vaca 24 Fed Com
Well: #707H
Wellbore: OH
Design: OH

Local Co-ordinate Reference: Well #707H
TVD Reference: KB = 26' @ 3358.0usft
MD Reference: KB = 26' @ 3358.0usft
North Reference: Grid
Survey Calculation Method: Minimum Curvature
Database: EDM

Survey										
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
2,871.0	14.60	122.02	2,840.8	-146.8	245.5	0.29	0.09	-1.09	-61.5	14.7
2,967.0	14.25	120.61	2,933.8	-159.3	265.9	0.52	-0.36	-1.47	-70.3	13.9
3,063.0	13.63	121.14	3,027.0	-171.1	285.8	0.66	-0.65	0.55	-77.8	15.5
3,159.0	13.72	119.03	3,120.3	-182.5	305.4	0.53	0.09	-2.20	-85.6	13.7
3,255.0	14.16	117.27	3,213.4	-193.4	325.8	0.64	0.46	-1.83	-93.7	12.6
3,351.0	14.95	120.08	3,306.4	-205.0	347.0	1.10	0.82	2.93	-101.7	18.9
3,447.0	13.89	133.71	3,399.4	-219.2	366.0	3.69	-1.10	14.20	-102.8	42.4
3,543.0	13.72	130.28	3,492.6	-234.5	383.0	0.87	-0.18	-3.57	-112.6	33.9
3,637.0	12.57	126.94	3,584.1	-247.8	399.7	1.47	-1.22	-3.55	-120.6	26.0
3,733.0	12.31	126.24	3,677.9	-260.2	416.3	0.31	-0.27	-0.73	-126.0	23.9
3,828.0	11.70	125.97	3,770.8	-271.8	432.3	0.64	-0.64	-0.28	-130.5	22.8
3,924.0	10.55	122.28	3,865.0	-282.2	447.6	1.41	-1.20	-3.84	-134.6	14.4
4,020.0	9.94	111.03	3,959.5	-289.9	462.7	2.18	-0.64	-11.72	-136.5	-9.9
4,116.0	10.29	124.74	4,054.0	-297.7	477.5	2.53	0.36	14.28	-136.1	24.1
4,212.0	10.64	127.47	4,148.4	-308.0	491.6	0.63	0.36	2.84	-136.6	30.0
4,308.0	9.32	126.06	4,242.9	-318.0	504.9	1.40	-1.37	-1.47	-138.4	26.0
4,404.0	9.76	132.13	4,337.6	-328.0	517.2	1.14	0.46	6.32	-135.3	39.0
4,500.0	11.26	131.69	4,432.0	-339.7	530.3	1.56	1.56	-0.46	-137.6	35.9
4,595.0	11.70	128.26	4,525.1	-351.9	544.8	0.85	0.46	-3.61	-143.0	26.1
4,691.0	10.38	127.55	4,619.3	-363.2	559.3	1.38	-1.37	-0.74	-146.1	23.3
4,787.0	11.17	127.55	4,713.6	-374.1	573.5	0.82	0.82	0.00	-148.5	22.5
4,883.0	11.78	126.06	4,807.7	-385.5	588.8	0.71	0.64	-1.55	-152.5	17.9
4,979.0	12.66	127.47	4,901.5	-397.7	605.1	0.97	0.92	1.47	-156.8	21.0
5,075.0	11.17	128.08	4,995.5	-409.8	620.7	1.56	-1.55	0.64	-160.9	21.7
5,171.0	9.32	126.76	5,089.9	-420.2	634.3	1.94	-1.93	-1.37	-162.8	17.2
5,267.0	7.91	122.28	5,184.9	-428.4	646.1	1.63	-1.47	-4.67	-162.3	4.5
5,363.0	9.23	119.91	5,279.8	-435.8	658.4	1.42	1.37	-2.47	-161.1	-1.2



EOG Resources

Midland PVA

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #707H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 26' @ 3358.0usft
Site:	Vaca 24 Fed Com	MD Reference:	KB = 26' @ 3358.0usft
Well:	#707H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM

Survey										
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
5,459.0	9.23	119.38	5,374.5	-443.4	671.7	0.09	0.00	-0.55	-160.9	-1.4
5,555.0	9.32	117.10	5,469.3	-450.7	685.4	0.39	0.09	-2.37	-160.7	-6.1
5,651.0	8.88	116.92	5,564.1	-457.6	698.9	0.46	-0.46	-0.19	-160.3	-4.6
5,747.0	8.35	117.71	5,659.0	-464.2	711.7	0.57	-0.55	0.82	-159.2	-0.5
5,843.0	7.91	114.99	5,754.0	-470.2	723.8	0.61	-0.46	-2.83	-157.1	-5.8
5,939.0	8.18	109.63	5,849.1	-475.3	736.2	0.83	0.28	-5.58	-154.1	-16.9
6,035.0	8.97	103.03	5,944.0	-479.3	750.0	1.31	0.82	-6.87	-150.9	-29.4
6,130.0	9.50	108.31	6,037.8	-483.4	764.6	1.05	0.56	5.56	-153.3	-10.6
6,226.0	9.67	113.93	6,132.4	-489.2	779.5	0.99	0.18	5.85	-154.1	7.8
6,322.0	9.15	110.94	6,227.1	-495.2	794.0	0.74	-0.54	-3.11	-154.8	3.1
6,418.0	8.71	110.68	6,322.0	-500.5	808.0	0.46	-0.46	-0.27	-154.5	6.0
6,514.0	8.53	109.98	6,416.9	-505.5	821.4	0.22	-0.19	-0.73	-153.8	7.9
6,610.0	8.35	111.65	6,511.9	-510.5	834.6	0.32	-0.19	1.74	-152.3	16.0
6,705.0	8.71	109.45	6,605.8	-515.4	847.8	0.51	0.38	-2.32	-151.9	13.9
6,801.0	8.62	118.50	6,700.7	-521.3	861.0	1.42	-0.09	9.43	-146.7	40.1
6,897.0	8.53	141.44	6,795.7	-530.3	871.7	3.54	-0.09	23.90	-118.8	91.6
6,993.0	8.27	155.50	6,890.7	-542.1	879.1	2.15	-0.27	14.65	-93.8	111.0
7,089.0	6.07	166.75	6,985.9	-553.4	883.1	2.71	-2.29	11.72	-70.6	117.9
7,185.0	3.43	237.15	7,081.6	-559.9	881.8	6.13	-2.75	73.33	77.2	96.1
7,281.0	1.67	252.71	7,177.5	-561.8	878.1	1.95	-1.83	16.21	86.7	59.9
7,377.0	0.70	281.63	7,273.5	-562.1	876.2	1.16	-1.01	30.12	88.6	4.9
7,473.0	0.79	255.79	7,369.5	-562.2	875.0	0.36	0.09	-26.92	66.8	32.2
7,569.0	0.88	253.24	7,465.5	-562.6	873.6	0.10	0.09	-2.66	56.8	26.4
7,665.0	1.06	236.88	7,561.5	-563.2	872.2	0.34	0.19	-17.04	42.3	33.7
7,761.0	0.70	231.79	7,657.5	-564.1	871.0	0.38	-0.37	-5.30	36.1	32.4
7,857.0	1.32	216.32	7,753.5	-565.3	869.8	0.70	0.65	-16.11	24.4	38.9
7,953.0	1.23	239.52	7,849.4	-566.8	868.3	0.54	-0.09	24.17	35.8	26.6



EOG Resources

Midland PVA

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #707H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 26' @ 3358.0usft
Site:	Vaca 24 Fed Com	MD Reference:	KB = 26' @ 3358.0usft
Well:	#707H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM

Survey										
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
8,049.0	1.32	243.56	7,945.4	-567.8	866.4	0.13	0.09	4.21	35.4	24.1
8,145.0	0.88	248.13	8,041.4	-568.5	864.7	0.47	-0.46	4.76	35.4	21.3
8,241.0	1.14	245.94	8,137.4	-569.2	863.2	0.27	0.27	-2.28	32.8	22.6
8,337.0	0.79	224.23	8,233.4	-570.1	861.9	0.52	-0.36	-22.61	20.6	32.8
8,433.0	0.62	197.51	8,329.4	-571.0	861.2	0.38	-0.18	-27.83	2.6	38.2
8,529.0	1.06	210.52	8,425.3	-572.3	860.6	0.50	0.46	13.55	9.7	36.8
8,625.0	0.97	186.61	8,521.3	-573.9	860.1	0.45	-0.09	-24.91	-7.6	37.2
8,721.0	0.97	200.32	8,617.3	-575.4	859.7	0.24	0.00	14.28	-0.2	38.2
8,817.0	0.97	209.73	8,713.3	-576.9	859.0	0.17	0.00	9.80	4.4	37.8
8,913.0	0.97	197.51	8,809.3	-578.4	858.4	0.22	0.00	-12.73	-5.3	37.7
9,009.0	1.06	211.04	8,905.3	-579.9	857.7	0.27	0.09	14.09	2.0	38.1
9,105.0	1.23	207.53	9,001.3	-581.6	856.7	0.19	0.18	-3.66	-2.3	38.1
9,201.0	1.49	209.11	9,097.2	-583.6	855.7	0.27	0.27	1.65	-3.5	38.2
9,296.0	1.14	202.69	9,192.2	-585.6	854.7	0.40	-0.37	-6.76	-9.9	37.4
9,392.0	1.14	205.07	9,288.2	-587.3	853.9	0.05	0.00	2.48	-10.2	37.8
9,489.0	1.32	230.82	9,385.2	-588.9	852.6	0.59	0.19	26.55	5.2	38.9
9,584.0	1.67	250.86	9,480.1	-590.0	850.5	0.66	0.37	21.09	15.8	35.2
9,680.0	1.76	248.75	9,576.1	-591.0	847.8	0.11	0.09	-2.20	11.6	35.7
9,776.0	0.79	270.72	9,672.1	-591.5	845.8	1.11	-1.01	22.89	22.1	29.3
9,872.0	0.44	43.96	9,768.1	-591.3	845.3	1.18	-0.36	138.79	6.3	-35.7
9,967.0	0.88	48.45	9,863.1	-590.5	846.1	0.47	0.46	4.73	2.3	-36.0
10,063.0	0.79	73.23	9,959.0	-589.8	847.3	0.38	-0.09	25.81	-14.3	-33.4
10,159.0	0.62	339.54	10,055.0	-589.2	847.8	1.08	-0.18	-97.59	33.8	-12.8
10,255.0	0.44	298.93	10,151.0	-588.5	847.3	0.42	-0.19	-42.30	33.2	11.9
10,351.0	1.41	273.97	10,247.0	-588.2	845.8	1.07	1.01	-26.00	23.5	24.7
10,447.0	1.32	267.56	10,343.0	-588.2	843.5	0.18	-0.09	-6.68	18.4	27.0
10,543.0	1.76	291.55	10,439.0	-587.7	841.0	0.80	0.46	24.99	25.3	17.7



EOG Resources

Midland PVA

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #707H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 26' @ 3358.0usft
Site:	Vaca 24 Fed Com	MD Reference:	KB = 26' @ 3358.0usft
Well:	#707H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM

Survey										
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
10,639.0	1.85	343.85	10,534.9	-585.7	839.2	1.66	0.09	54.48	27.0	-8.0
10,735.0	0.97	295.77	10,630.9	-583.8	838.1	1.46	-0.92	-50.08	22.2	13.6
10,830.0	1.41	259.21	10,725.9	-583.7	836.2	0.90	0.46	-38.48	7.9	23.6
10,926.0	1.49	281.27	10,821.8	-583.7	833.8	0.58	0.08	22.98	13.8	19.4
11,022.0	1.49	271.95	10,917.8	-583.4	831.3	0.25	0.00	-9.71	8.0	21.1
11,118.0	0.53	305.79	11,013.8	-583.1	829.7	1.14	-1.00	35.25	17.0	13.8
11,213.0	1.14	266.85	11,108.8	-582.9	828.4	0.84	0.64	-40.99	3.3	21.1
11,309.0	2.37	276.43	11,204.7	-582.7	825.5	1.31	1.28	9.98	3.8	20.4
11,405.0	1.67	270.02	11,300.7	-582.5	822.1	0.77	-0.73	-6.68	-1.9	20.5
11,501.0	1.93	313.00	11,396.6	-581.4	819.5	1.40	0.27	44.77	10.0	17.2
11,597.0	2.81	308.25	11,492.5	-578.8	816.5	0.94	0.92	-4.95	4.5	17.9
11,789.0	1.67	9.07	11,684.4	-573.2	813.3	1.29	-0.59	31.68	12.7	8.9
11,861.0	1.49	31.13	11,756.4	-571.3	813.9	0.87	-0.25	30.64	13.2	3.8
11,957.0	2.11	39.74	11,852.3	-568.9	815.7	0.70	0.65	8.97	10.6	2.0
12,053.0	2.73	27.88	11,948.3	-565.5	817.9	0.83	0.65	-12.35	6.0	3.8
12,106.0	5.95	15.42	12,001.1	-561.8	819.2	6.29	6.07	-23.51	1.0	4.7
KOP, MD:12106.0', TVD:12001.1',N/S:-561.8', E/W:819.2', INC:5.95										
12,149.0	8.62	12.23	12,043.8	-556.5	820.5	6.29	6.22	-7.42	-4.3	4.6
12,245.0	21.90	6.78	12,136.2	-531.5	824.1	13.90	13.83	-5.68	-17.1	1.8
12,291.0	27.67	6.63	12,177.9	-512.4	826.4	12.54	12.54	-0.33	-23.7	0.0
FTP Crossing, MD:12291.0', TVD:12177.9',N/S:-512.4', E/W:826.4', INC:27.67										
12,341.0	33.94	6.52	12,220.8	-487.0	829.3	12.54	12.54	-0.22	-31.0	-2.5
12,437.0	44.76	6.08	12,295.0	-426.6	835.9	11.27	11.27	-0.46	-43.6	-9.1
12,532.0	47.84	4.15	12,360.6	-358.2	842.0	3.56	3.24	-2.03	-46.5	-17.1
12,628.0	57.07	358.87	12,419.1	-282.2	843.8	10.55	9.61	-5.50	-37.7	-22.1
12,724.0	69.03	357.64	12,462.5	-196.8	841.2	12.51	12.46	-1.28	-27.0	-20.1
12,820.0	79.93	357.29	12,488.1	-104.5	837.1	11.36	11.35	-0.36	-15.3	-16.5



EOG Resources

Midland PVA

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #707H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 26' @ 3358.0usft
Site:	Vaca 24 Fed Com	MD Reference:	KB = 26' @ 3358.0usft
Well:	#707H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM

Survey										
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
12,915.0	86.09	0.02	12,499.7	-10.3	834.9	7.08	6.48	2.87	-4.2	-14.8
13,011.0	85.74	1.25	12,506.5	85.4	835.9	1.33	-0.36	1.28	2.8	-16.6
13,108.0	86.79	2.21	12,512.8	182.2	838.9	1.47	1.08	0.99	9.2	-20.2
13,203.0	90.84	357.64	12,514.8	277.1	838.7	6.43	4.26	-4.81	11.3	-20.7
13,299.0	91.01	358.17	12,513.3	373.0	835.2	0.58	0.18	0.55	9.9	-17.9
13,394.0	89.60	359.05	12,512.8	468.0	832.9	1.75	-1.48	0.93	9.5	-16.3
13,491.0	87.67	358.52	12,515.1	564.9	830.9	2.06	-1.99	-0.55	12.0	-14.9
13,587.0	89.69	358.52	12,517.3	660.9	828.4	2.10	2.10	0.00	14.3	-13.1
13,683.0	87.14	359.75	12,519.9	756.8	826.9	2.95	-2.66	1.28	17.1	-12.3
13,779.0	88.64	0.28	12,523.5	852.7	827.0	1.66	1.56	0.55	20.8	-13.0
13,875.0	90.13	0.10	12,524.5	948.7	827.3	1.56	1.55	-0.19	21.9	-14.0
13,971.0	88.29	358.87	12,525.8	1,044.7	826.4	2.31	-1.92	-1.28	23.4	-13.9
14,067.0	90.31	2.12	12,527.0	1,140.7	827.3	3.99	2.10	3.39	24.7	-15.4
14,163.0	89.87	0.10	12,526.8	1,236.7	829.1	2.15	-0.46	-2.10	24.7	-17.9
14,259.0	89.43	358.79	12,527.4	1,332.7	828.2	1.44	-0.46	-1.36	25.4	-17.7
14,355.0	88.55	359.22	12,529.1	1,428.6	826.5	1.02	-0.92	0.45	27.2	-16.7
14,451.0	92.86	357.47	12,527.9	1,524.6	823.7	4.85	4.49	-1.82	26.1	-14.6
14,547.0	93.30	356.85	12,522.8	1,620.3	819.0	0.79	0.46	-0.65	21.1	-10.5
14,643.0	91.10	357.99	12,519.1	1,716.1	814.7	2.58	-2.29	1.19	17.6	-6.9
14,739.0	87.93	358.17	12,519.9	1,812.1	811.5	3.31	-3.30	0.19	18.5	-4.4
14,835.0	88.55	357.91	12,522.9	1,907.9	808.2	0.70	0.65	-0.27	21.6	-1.8
14,931.0	87.41	357.80	12,526.2	2,003.8	804.6	1.19	-1.19	-0.11	25.1	1.1
15,036.0	92.07	359.47	12,526.7	2,108.8	802.1	4.71	4.44	1.59	25.7	2.9
15,132.0	92.86	358.85	12,522.6	2,204.7	800.7	1.05	0.82	-0.65	21.7	3.6
15,228.0	92.42	359.29	12,518.2	2,300.5	799.1	0.65	-0.46	0.46	17.4	4.5
15,324.0	90.92	0.08	12,515.4	2,396.5	798.6	1.77	-1.56	0.82	14.8	4.3
15,420.0	88.37	0.08	12,516.0	2,492.5	798.7	2.66	-2.66	0.00	15.5	3.5



EOG Resources

Midland PVA

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #707H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 26' @ 3358.0usft
Site:	Vaca 24 Fed Com	MD Reference:	KB = 26' @ 3358.0usft
Well:	#707H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM

Survey										
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
15,516.0	89.52	359.73	12,517.7	2,588.5	798.6	1.25	1.20	-0.36	17.4	3.0
15,612.0	90.92	0.79	12,517.4	2,684.5	799.0	1.83	1.46	1.10	17.2	1.9
15,708.0	89.60	359.47	12,516.9	2,780.5	799.2	1.94	-1.37	-1.37	16.8	1.0
15,804.0	90.04	359.64	12,517.2	2,876.5	798.5	0.49	0.46	0.18	17.3	1.0
15,900.0	91.19	359.64	12,516.2	2,972.4	797.9	1.20	1.20	0.00	16.4	1.0
15,996.0	88.81	0.17	12,516.2	3,068.4	797.7	2.54	-2.48	0.55	16.5	0.4
16,092.0	89.78	0.52	12,517.4	3,164.4	798.3	1.07	1.01	0.36	17.8	-0.8
16,189.0	89.25	0.52	12,518.2	3,261.4	799.2	0.55	-0.55	0.00	18.8	-2.4
16,285.0	90.22	1.40	12,518.6	3,357.4	800.8	1.36	1.01	0.92	19.3	-4.7
16,381.0	89.34	2.19	12,519.0	3,453.4	803.8	1.23	-0.92	0.82	19.8	-8.4
16,476.0	88.02	1.05	12,521.2	3,548.3	806.5	1.84	-1.39	-1.20	22.2	-11.7
16,572.0	90.40	0.52	12,522.5	3,644.3	807.8	2.54	2.48	-0.55	23.6	-13.7
16,669.0	91.63	1.05	12,520.8	3,741.2	809.1	1.38	1.27	0.55	22.0	-15.7
16,765.0	93.83	1.58	12,516.2	3,837.1	811.3	2.36	2.29	0.55	17.6	-18.6
16,861.0	92.77	0.08	12,510.7	3,932.9	812.7	1.91	-1.10	-1.56	12.2	-20.7
16,957.0	90.22	358.77	12,508.2	4,028.9	811.7	2.99	-2.66	-1.36	9.8	-20.4
17,053.0	91.19	358.77	12,507.0	4,124.8	809.7	1.01	1.01	0.00	8.8	-19.0
17,149.0	86.35	358.06	12,509.1	4,220.8	807.0	5.10	-5.04	-0.74	11.0	-17.1
17,245.0	87.32	357.97	12,514.4	4,316.5	803.7	1.01	1.01	-0.09	16.4	-14.4
17,341.0	89.60	358.77	12,517.0	4,412.5	801.0	2.52	2.37	0.83	19.1	-12.4
17,437.0	93.12	358.94	12,514.7	4,508.4	799.1	3.67	3.67	0.18	16.9	-11.2
17,533.0	89.78	357.36	12,512.3	4,604.3	796.0	3.85	-3.48	-1.65	14.6	-8.7
17,629.0	91.19	358.85	12,511.4	4,700.2	792.8	2.14	1.47	1.55	14.0	-6.2
17,725.0	89.52	357.36	12,510.9	4,796.2	789.6	2.33	-1.74	-1.55	13.5	-3.7
17,821.0	88.81	357.80	12,512.3	4,892.1	785.6	0.87	-0.74	0.46	15.0	-0.4
17,917.0	89.78	357.45	12,513.4	4,988.0	781.6	1.07	1.01	-0.36	16.3	2.9
18,013.0	92.42	359.20	12,511.6	5,083.9	778.8	3.30	2.75	1.82	14.6	5.0



EOG Resources

Midland PVA

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #707H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 26' @ 3358.0usft
Site:	Vaca 24 Fed Com	MD Reference:	KB = 26' @ 3358.0usft
Well:	#707H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM

Survey										
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
18,110.0	91.80	359.47	12,508.0	5,180.9	777.7	0.70	-0.64	0.28	11.2	5.5
18,206.0	90.13	357.36	12,506.4	5,276.8	775.0	2.80	-1.74	-2.20	9.7	7.4
18,302.0	90.84	358.41	12,505.6	5,372.7	771.5	1.32	0.74	1.09	9.0	10.3
18,398.0	89.08	358.85	12,505.7	5,468.7	769.2	1.89	-1.83	0.46	9.2	11.9
18,494.0	89.08	359.20	12,507.2	5,564.7	767.5	0.36	0.00	0.36	10.9	12.9
18,590.0	89.16	359.03	12,508.7	5,660.6	766.0	0.20	0.08	-0.18	12.5	13.7
18,686.0	89.69	359.82	12,509.6	5,756.6	765.1	0.99	0.55	0.82	13.6	13.9
18,782.0	88.64	358.59	12,511.0	5,852.6	763.8	1.68	-1.09	-1.28	15.1	14.6
18,877.0	90.66	359.91	12,511.6	5,947.6	762.5	2.54	2.13	1.39	15.8	15.2
18,973.0	90.75	359.56	12,510.4	6,043.6	762.1	0.38	0.09	-0.36	14.8	14.9
19,069.0	91.98	359.38	12,508.1	6,139.6	761.2	1.29	1.28	-0.19	12.6	15.1
19,164.0	93.39	0.35	12,503.7	6,234.4	761.0	1.80	1.48	1.02	8.3	14.7
19,260.0	91.28	359.91	12,499.8	6,330.4	761.2	2.25	-2.20	-0.46	4.5	13.8
19,356.0	90.48	358.50	12,498.3	6,426.3	759.8	1.69	-0.83	-1.47	3.2	14.4
19,451.0	90.92	0.43	12,497.2	6,521.3	759.0	2.08	0.46	2.03	2.1	14.6
19,547.0	90.04	0.35	12,496.3	6,617.3	759.6	0.92	-0.92	-0.08	1.5	13.3
19,644.0	89.25	359.03	12,497.1	6,734.3	759.0	1.31	-0.68	-1.13	2.3	13.1
19,760.0	89.78	359.47	12,497.9	6,830.3	757.7	0.72	0.55	0.46	3.3	13.7
19,855.0	90.75	359.73	12,497.4	6,925.3	757.1	1.06	1.02	0.27	3.0	13.7
19,951.0	88.81	359.82	12,497.8	7,021.3	756.7	2.02	-2.02	0.09	3.5	13.4
20,047.0	89.34	0.26	12,499.4	7,117.3	756.7	0.72	0.55	0.46	5.2	12.6
20,143.0	89.78	0.26	12,500.1	7,213.3	757.2	0.46	0.46	0.00	6.0	11.5
20,239.0	90.13	0.52	12,500.2	7,309.3	757.8	0.45	0.36	0.27	6.2	10.1
20,334.0	91.01	1.23	12,499.2	7,404.2	759.3	1.19	0.93	0.75	5.4	8.0
20,430.0	89.78	1.05	12,498.6	7,500.2	761.2	1.29	-1.28	-0.19	4.9	5.4
20,526.0	90.48	2.10	12,498.4	7,596.2	763.8	1.31	0.73	1.09	4.8	2.1
20,622.0	90.84	0.00	12,497.2	7,692.2	765.6	2.22	0.37	-2.19	3.8	-0.3



EOG Resources

Midland PVA

Company:	EOG Resources - Midland	Local Co-ordinate Reference:	Well #707H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	KB = 26' @ 3358.0usft
Site:	Vaca 24 Fed Com	MD Reference:	KB = 26' @ 3358.0usft
Well:	#707H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	EDM

Survey											
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)	
20,718.0	91.28	0.79	12,495.5	7,788.1	766.3	0.94	0.46	0.82	2.2	-1.7	
20,813.0	90.13	359.47	12,494.3	7,883.1	766.5	1.84	-1.21	-1.39	1.1	-2.6	
20,909.0	89.43	358.94	12,494.7	7,979.1	765.1	0.91	-0.73	-0.55	1.6	-1.9	
21,005.0	90.04	359.03	12,495.1	8,075.1	763.4	0.64	0.64	0.09	2.2	-0.9	
21,101.0	90.22	358.59	12,494.9	8,171.1	761.4	0.50	0.19	-0.46	2.1	0.4	
21,197.0	91.28	0.26	12,493.6	8,267.1	760.5	2.06	1.10	1.74	1.0	0.7	
21,293.0	89.08	359.64	12,493.3	8,363.1	760.4	2.38	-2.29	-0.65	0.8	0.1	
21,389.0	89.78	0.52	12,494.3	8,459.0	760.5	1.17	0.73	0.92	1.9	-0.7	
21,485.0	91.01	2.19	12,493.6	8,555.0	762.8	2.16	1.28	1.74	1.4	-3.7	
21,581.0	89.87	0.79	12,492.9	8,651.0	765.3	1.88	-1.19	-1.46	0.8	-6.9	
21,677.0	89.08	2.02	12,493.8	8,746.9	767.6	1.52	-0.82	1.28	1.8	-9.9	
21,773.0	90.13	359.47	12,494.4	8,842.9	768.9	2.87	1.09	-2.66	3.1	-11.8	
21,868.0	90.48	0.00	12,493.9	8,937.9	768.5	0.67	0.37	0.56	3.3	-12.1	
21,964.0	90.84	358.94	12,492.8	9,033.9	767.6	1.17	0.37	-1.10	2.9	-11.9	
22,060.0	87.23	358.85	12,494.4	9,129.9	765.7	3.76	-3.76	-0.09	5.2	-10.7	
22,156.0	86.61	358.15	12,499.6	9,225.7	763.2	0.97	-0.65	-0.73	11.1	-8.9	
22,252.0	87.93	357.27	12,504.2	9,321.5	759.4	1.65	1.37	-0.92	16.4	-5.7	
22,348.0	92.68	358.59	12,503.7	9,417.4	755.9	5.14	4.95	1.37	16.6	-2.9	
22,444.0	91.10	356.83	12,500.5	9,513.3	752.1	2.46	-1.65	-1.83	14.1	0.2	
22,538.0	92.68	356.74	12,497.4	9,607.1	746.8	1.68	1.68	-0.10	11.7	4.8	
22,584.0	92.86	356.30	12,495.2	9,652.9	744.0	1.03	0.39	-0.96	9.8	7.3	
Last MWD Survey (MD=22584.0')											
22,765.0	92.86	356.30	12,486.1	9,833.3	732.4	0.00	0.00	0.00	2.2	17.7	
Projection to Bit (MD=22765.0')											



EOG Resources

Midland PVA

Company: EOG Resources - Midland
Project: Lea County, NM (NAD 83 NME)
Site: Vaca 24 Fed Com
Well: #707H
Wellbore: OH
Design: OH

Local Co-ordinate Reference: Well #707H
TVD Reference: KB = 26' @ 3358.0usft
MD Reference: KB = 26' @ 3358.0usft
North Reference: Grid
Survey Calculation Method: Minimum Curvature
Database: EDM

Design Annotations

Measured Depth (usft)	Vertical Depth (usft)	Local Coordinates		Comment
		+N/-S (usft)	+E/-W (usft)	
12,106.0	12,001.1	-561.8	819.2	KOP, MD:12106.0', TVD:12001.1', N/S:-561.8', E/W:819.2', INC:5.95
12,291.0	12,177.9	-512.4	826.4	FTP Crossing, MD:12291.0', TVD:12177.9', N/S:-512.4', E/W:826.4', INC:27.67
22,584.0	12,495.2	9,652.9	744.0	Last MWD Survey (MD=22584.0')
22,765.0	12,486.1	9,833.3	732.4	Projection to Bit (MD=22765.0')

Checked By: _____ Approved By: _____ Date: _____

I CERTIFY THIS SURVEY TO BE TRUE AND CORRECT TO THE BEST OF MY BELIEF AND KNOWLEDGE
 KAY MADDOX 06/28/2021



Lea County, NM (NAD 83 NME)

Vaca 24 Fed Com #707H

Plan #1

PROJECT DETAILS: Lea County, NM (NAD 83 NME)

Geodetic System: US State Plane 1983
Datum: North American Datum 1983
Ellipsoid: GRS 1980
Zone: New Mexico Eastern Zone
System Datum: Mean Sea Level


WELL DETAILS: #707H

KB = 26' @ 3358.0usft 3332.0
Northing 404860.00 Easting 791459.00 Latitude 32° 6' 37.666 N Longitude 103° 31' 31.802 W

SECTION DETAILS

Sec	MD	Inc	Azi	TVD	+N/-S	+E/-W	Dleg	TFace	VSect	Target
1	0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.0	
2	1250.0	0.00	0.00	1250.0	0.0	0.0	0.00	0.00	0.0	
3	1718.8	9.38	124.30	1716.7	-21.6	31.6	2.00	124.30	-19.1	
4	7371.9	9.38	124.30	7294.3	-540.4	792.4	0.00	0.00	-478.6	
5	7840.7	0.00	0.00	7761.0	-562.0	824.0	2.00	180.00	-497.7	Brushy Top(Vaca 24 Fed Com #707H)
6	12106.2	0.00	0.00	12026.5	-562.0	824.0	0.00	0.00	-497.7	
7	12856.8	90.08	359.59	12504.0	-83.9	820.6	12.00	359.59	-21.3	
8	21689.7	90.08	359.59	12492.0	8748.7	757.7	0.00	0.00	8781.0	TGT#1(Vaca 24 Fed Com #707H)
9	21707.0	90.42	359.59	12491.9	8766.0	757.6	2.00	0.00	8798.3	
10	22777.0	90.42	359.59	12484.0	9836.0	750.0	0.00	0.00	9864.6	PBHL(Vaca 24 Fed Com #707H)

To convert a Magnetic Direction to a Grid Direction, Add 6.13°
To convert a Magnetic Direction to a True Direction, Add 6.56° East
To convert a True Direction to a Grid Direction, Subtract 0.43°

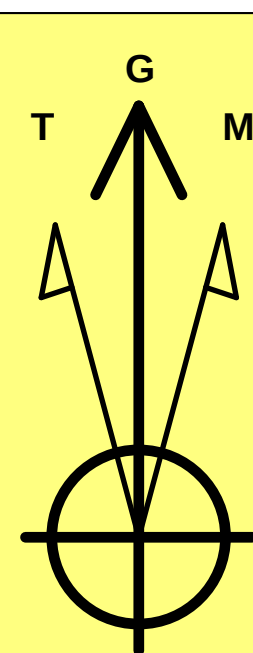

Azimuths to Grid North
True North: -0.43°
Magnetic North: 6.13°








Magnetic Field
Strength: 47468.1nT
Dip Angle: 59.82°
Date: 2/8/2021
Model: IGRF2020

CASING DETAILS

No casing data is available

WELLBORE TARGET DETAILS (MAP CO-ORDINATES)

Name	TVD	+N/-S	+E/-W	Northing	Easting
Brushy Top(Vaca 24 Fed Com #707H)	7761.0	-562.0	824.0	404298.00	792283.00
PBHL(Vaca 24 Fed Com #707H)	12484.0	9836.0	750.0	414696.00	792209.00
TGT#1(Vaca 24 Fed Com #707H)	12492.0	8748.7	757.7	413608.70	792216.74
FTP(Vaca 24 Fed Com #707H)	12504.0	-512.0	824.0	404348.00	792283.00

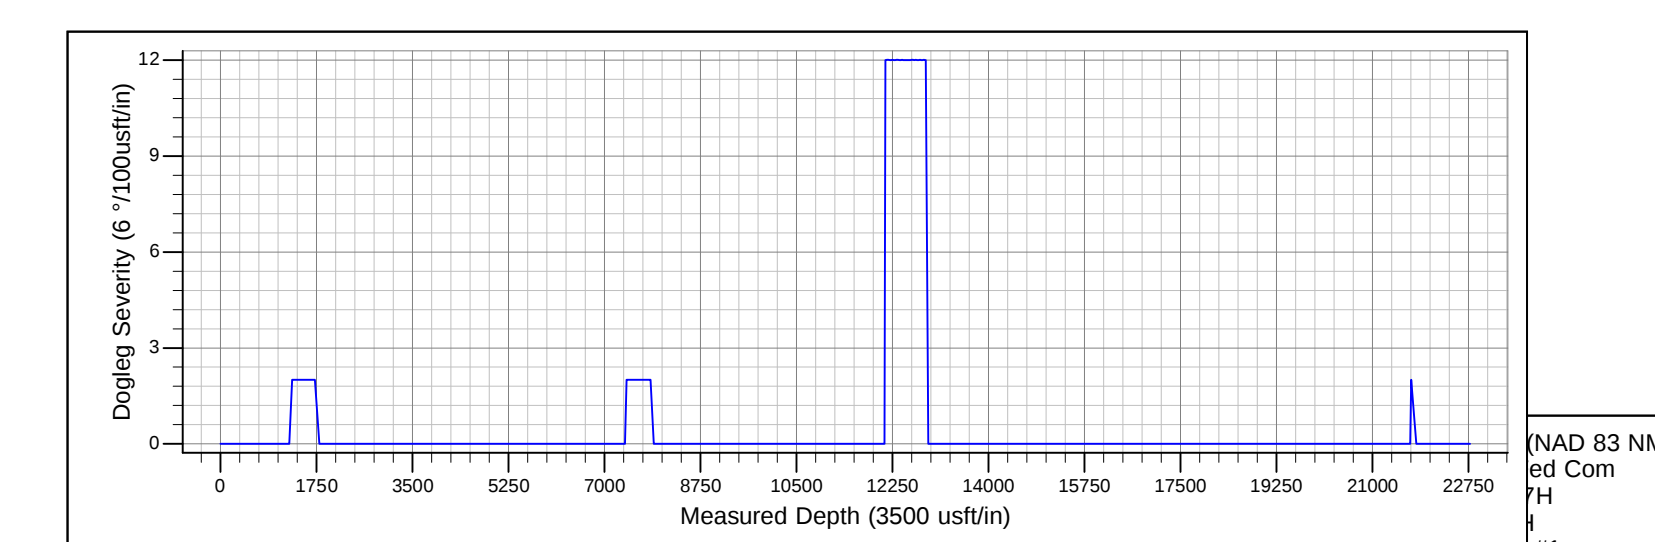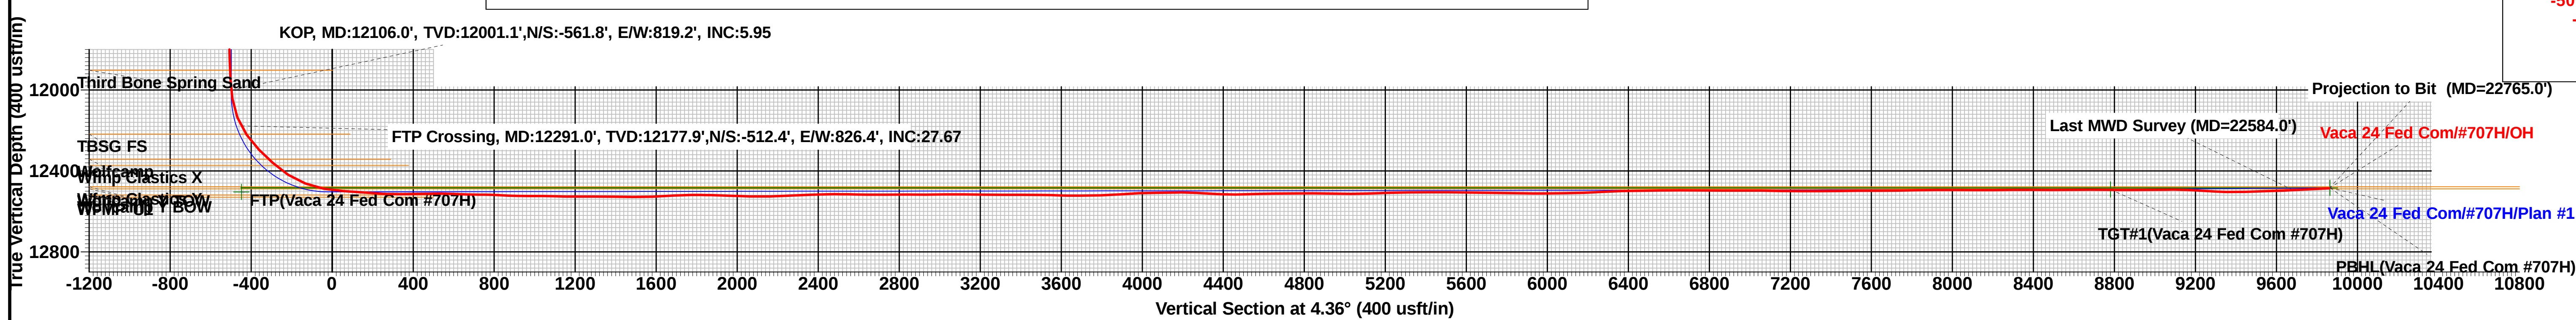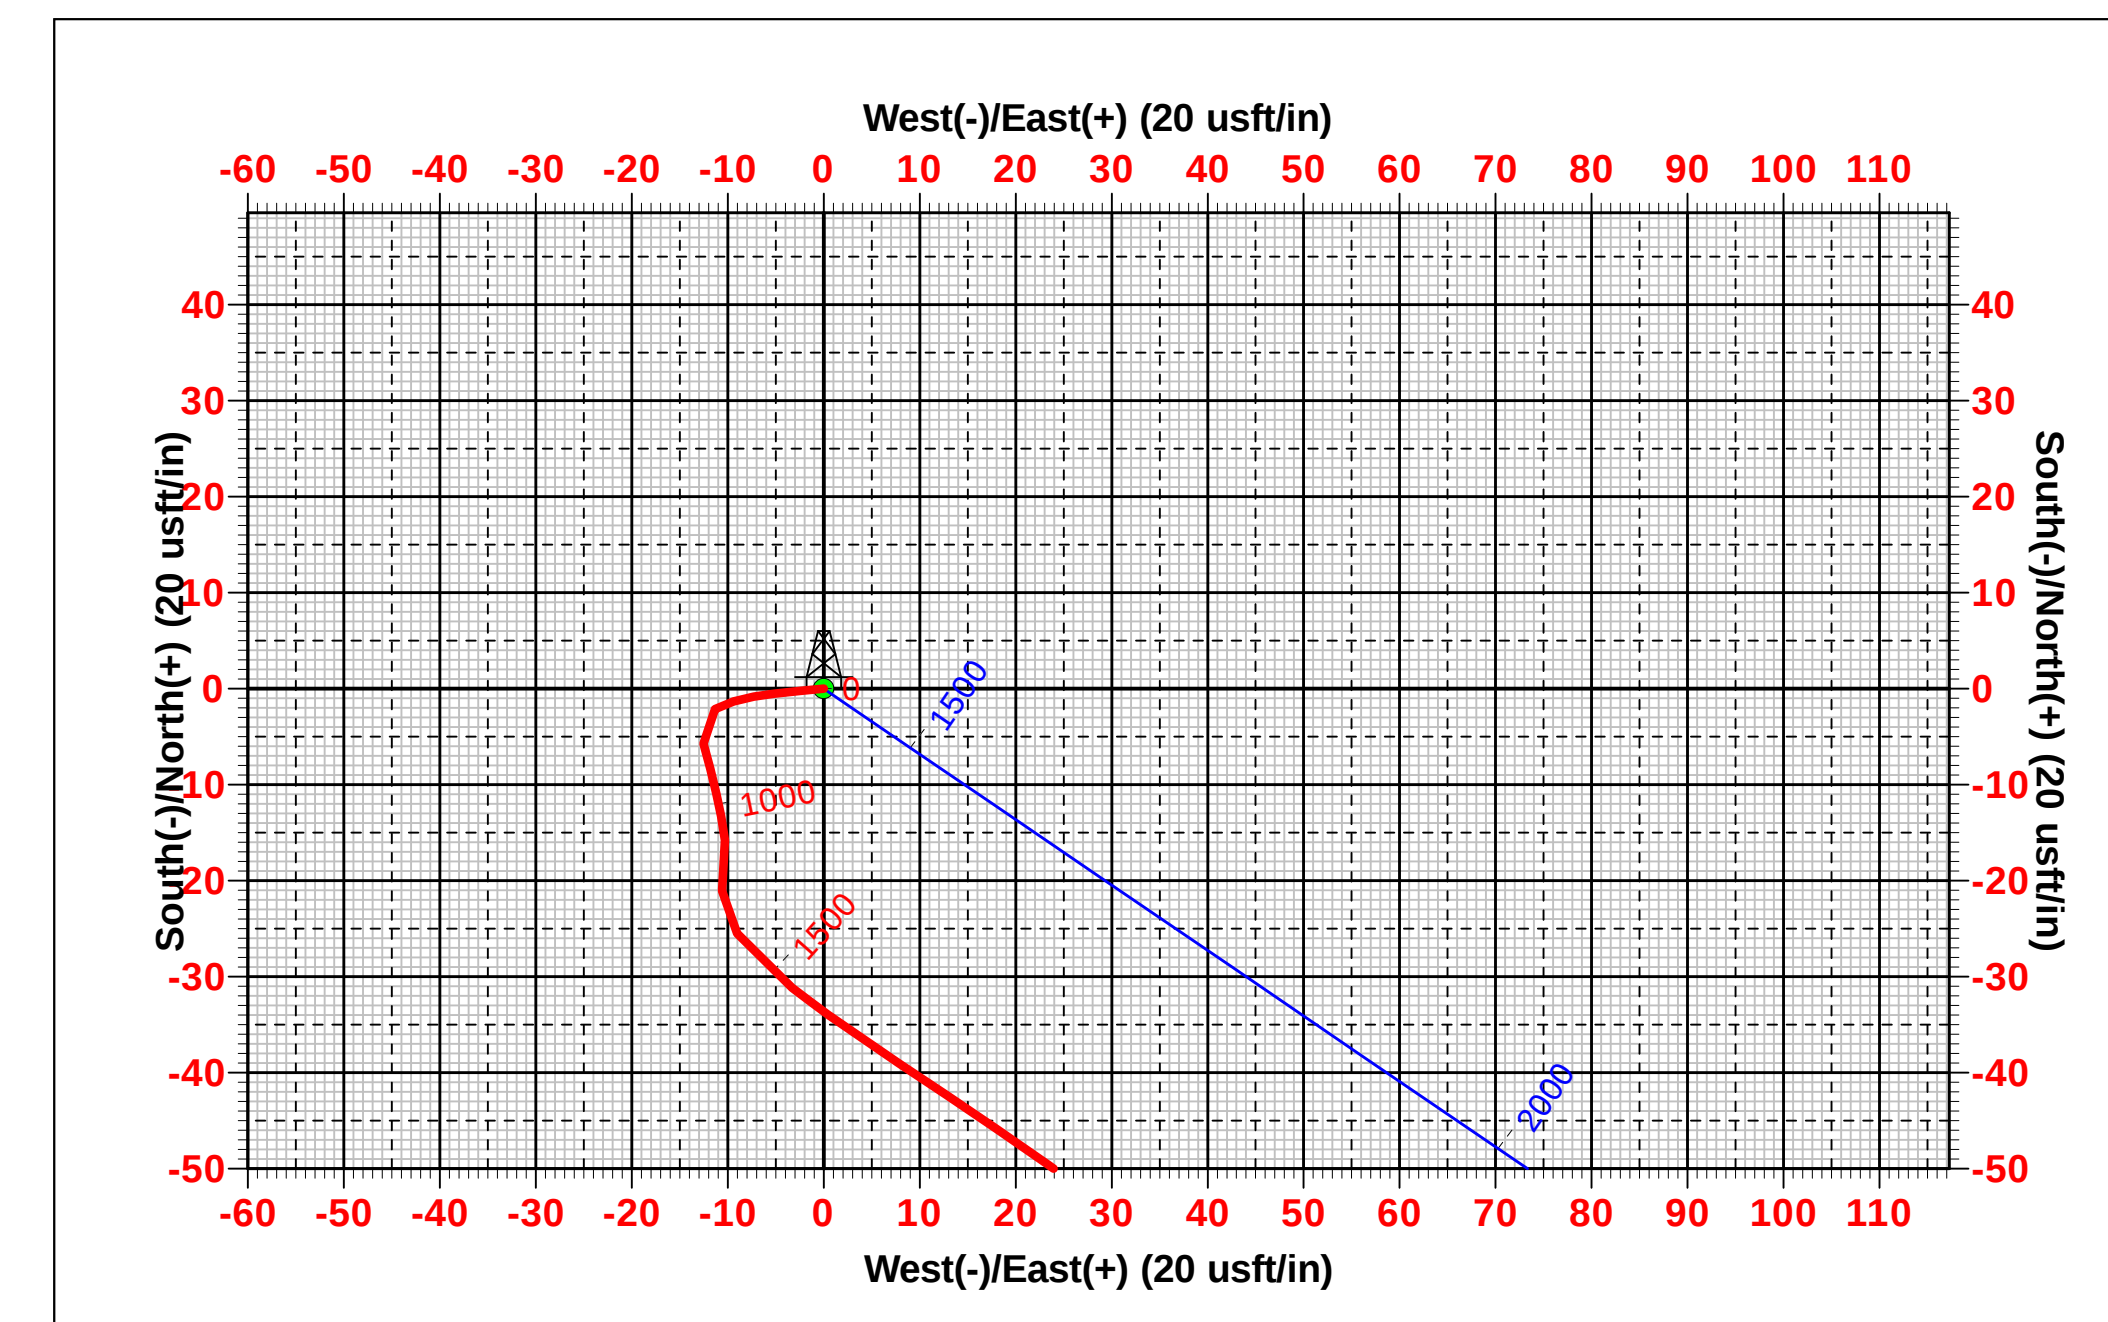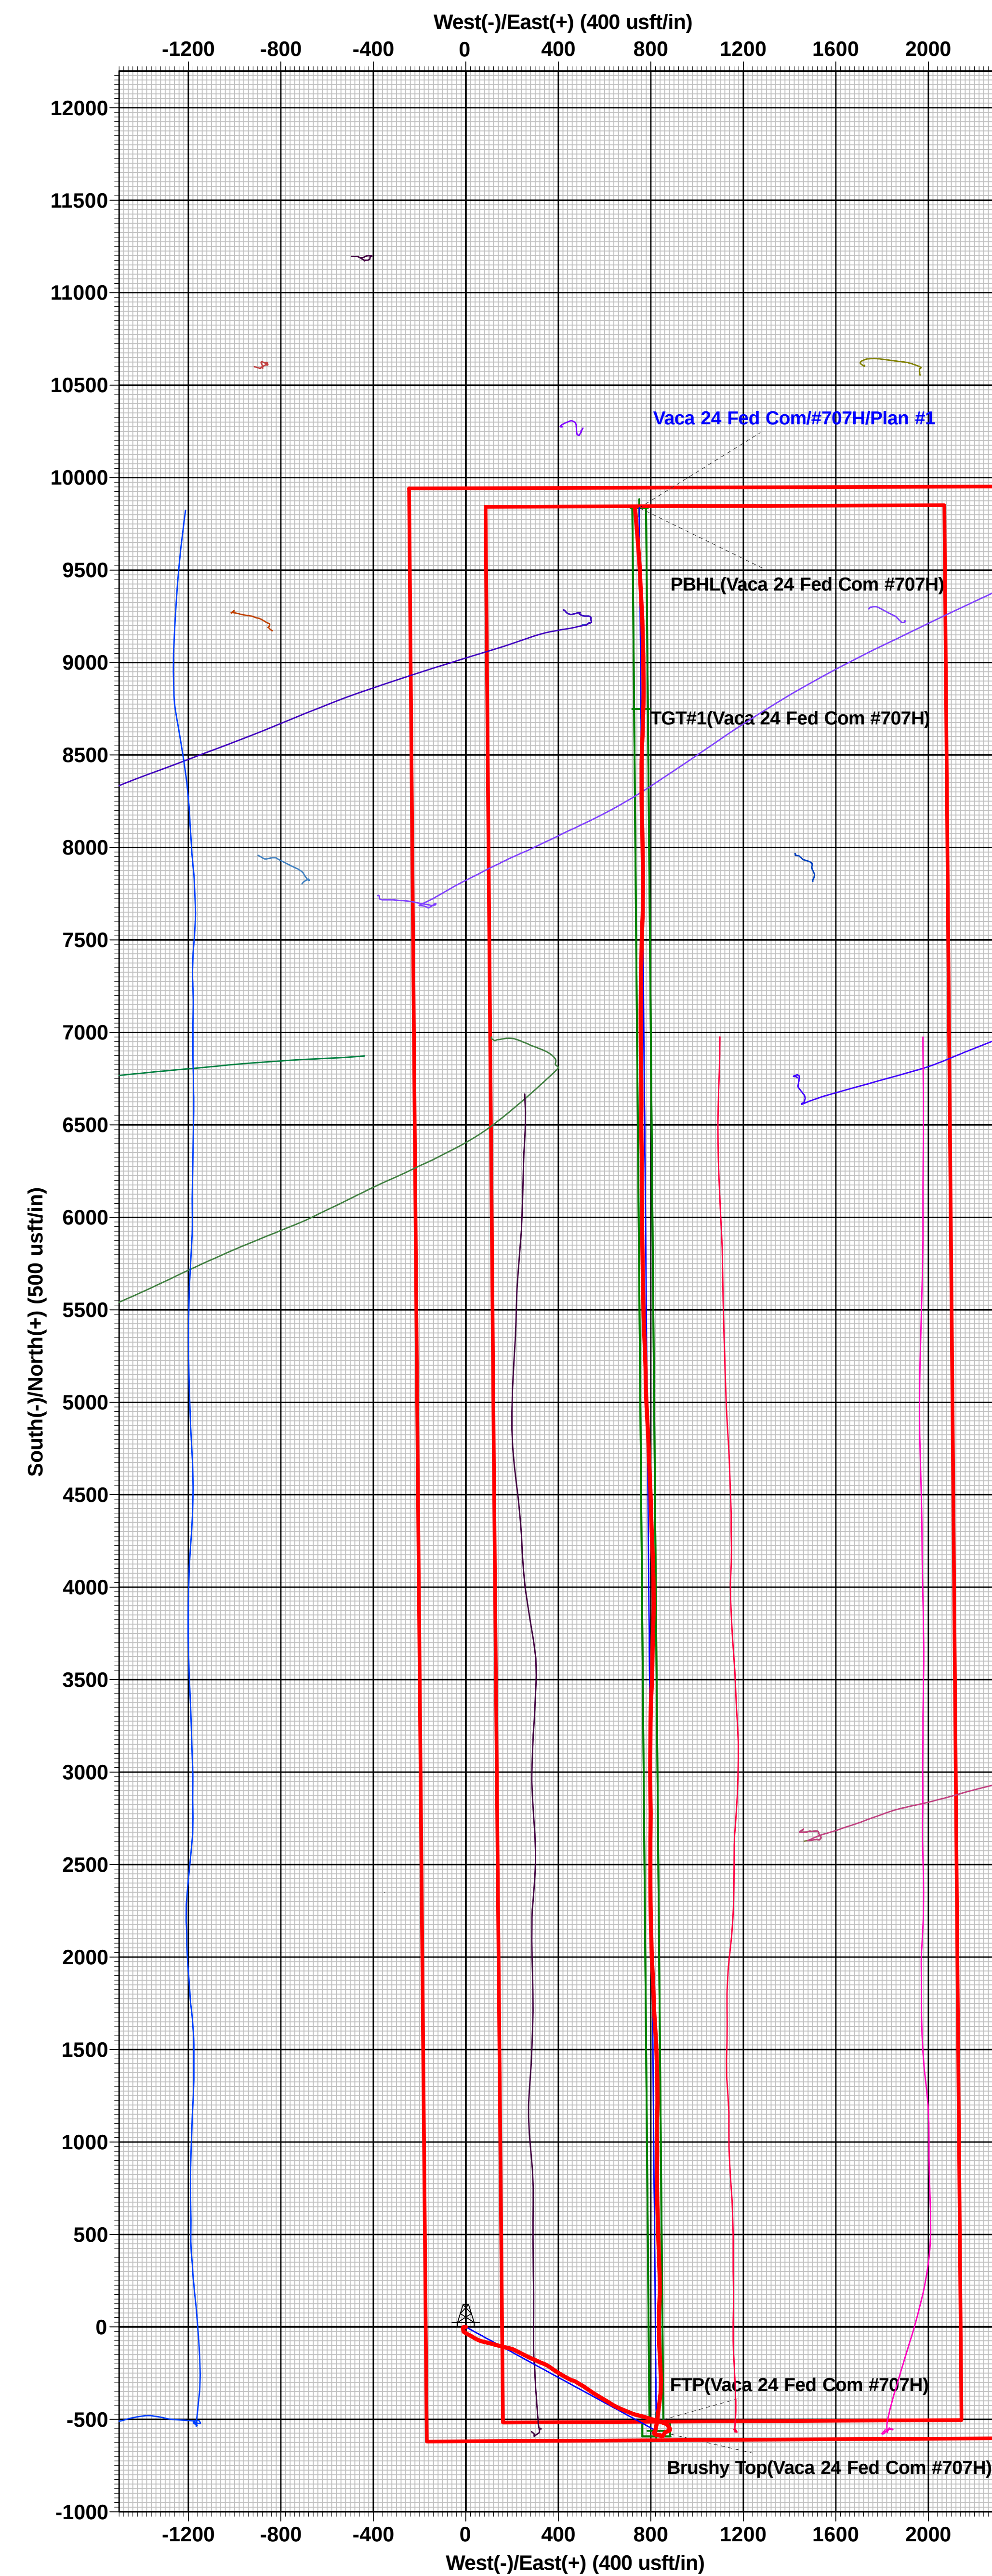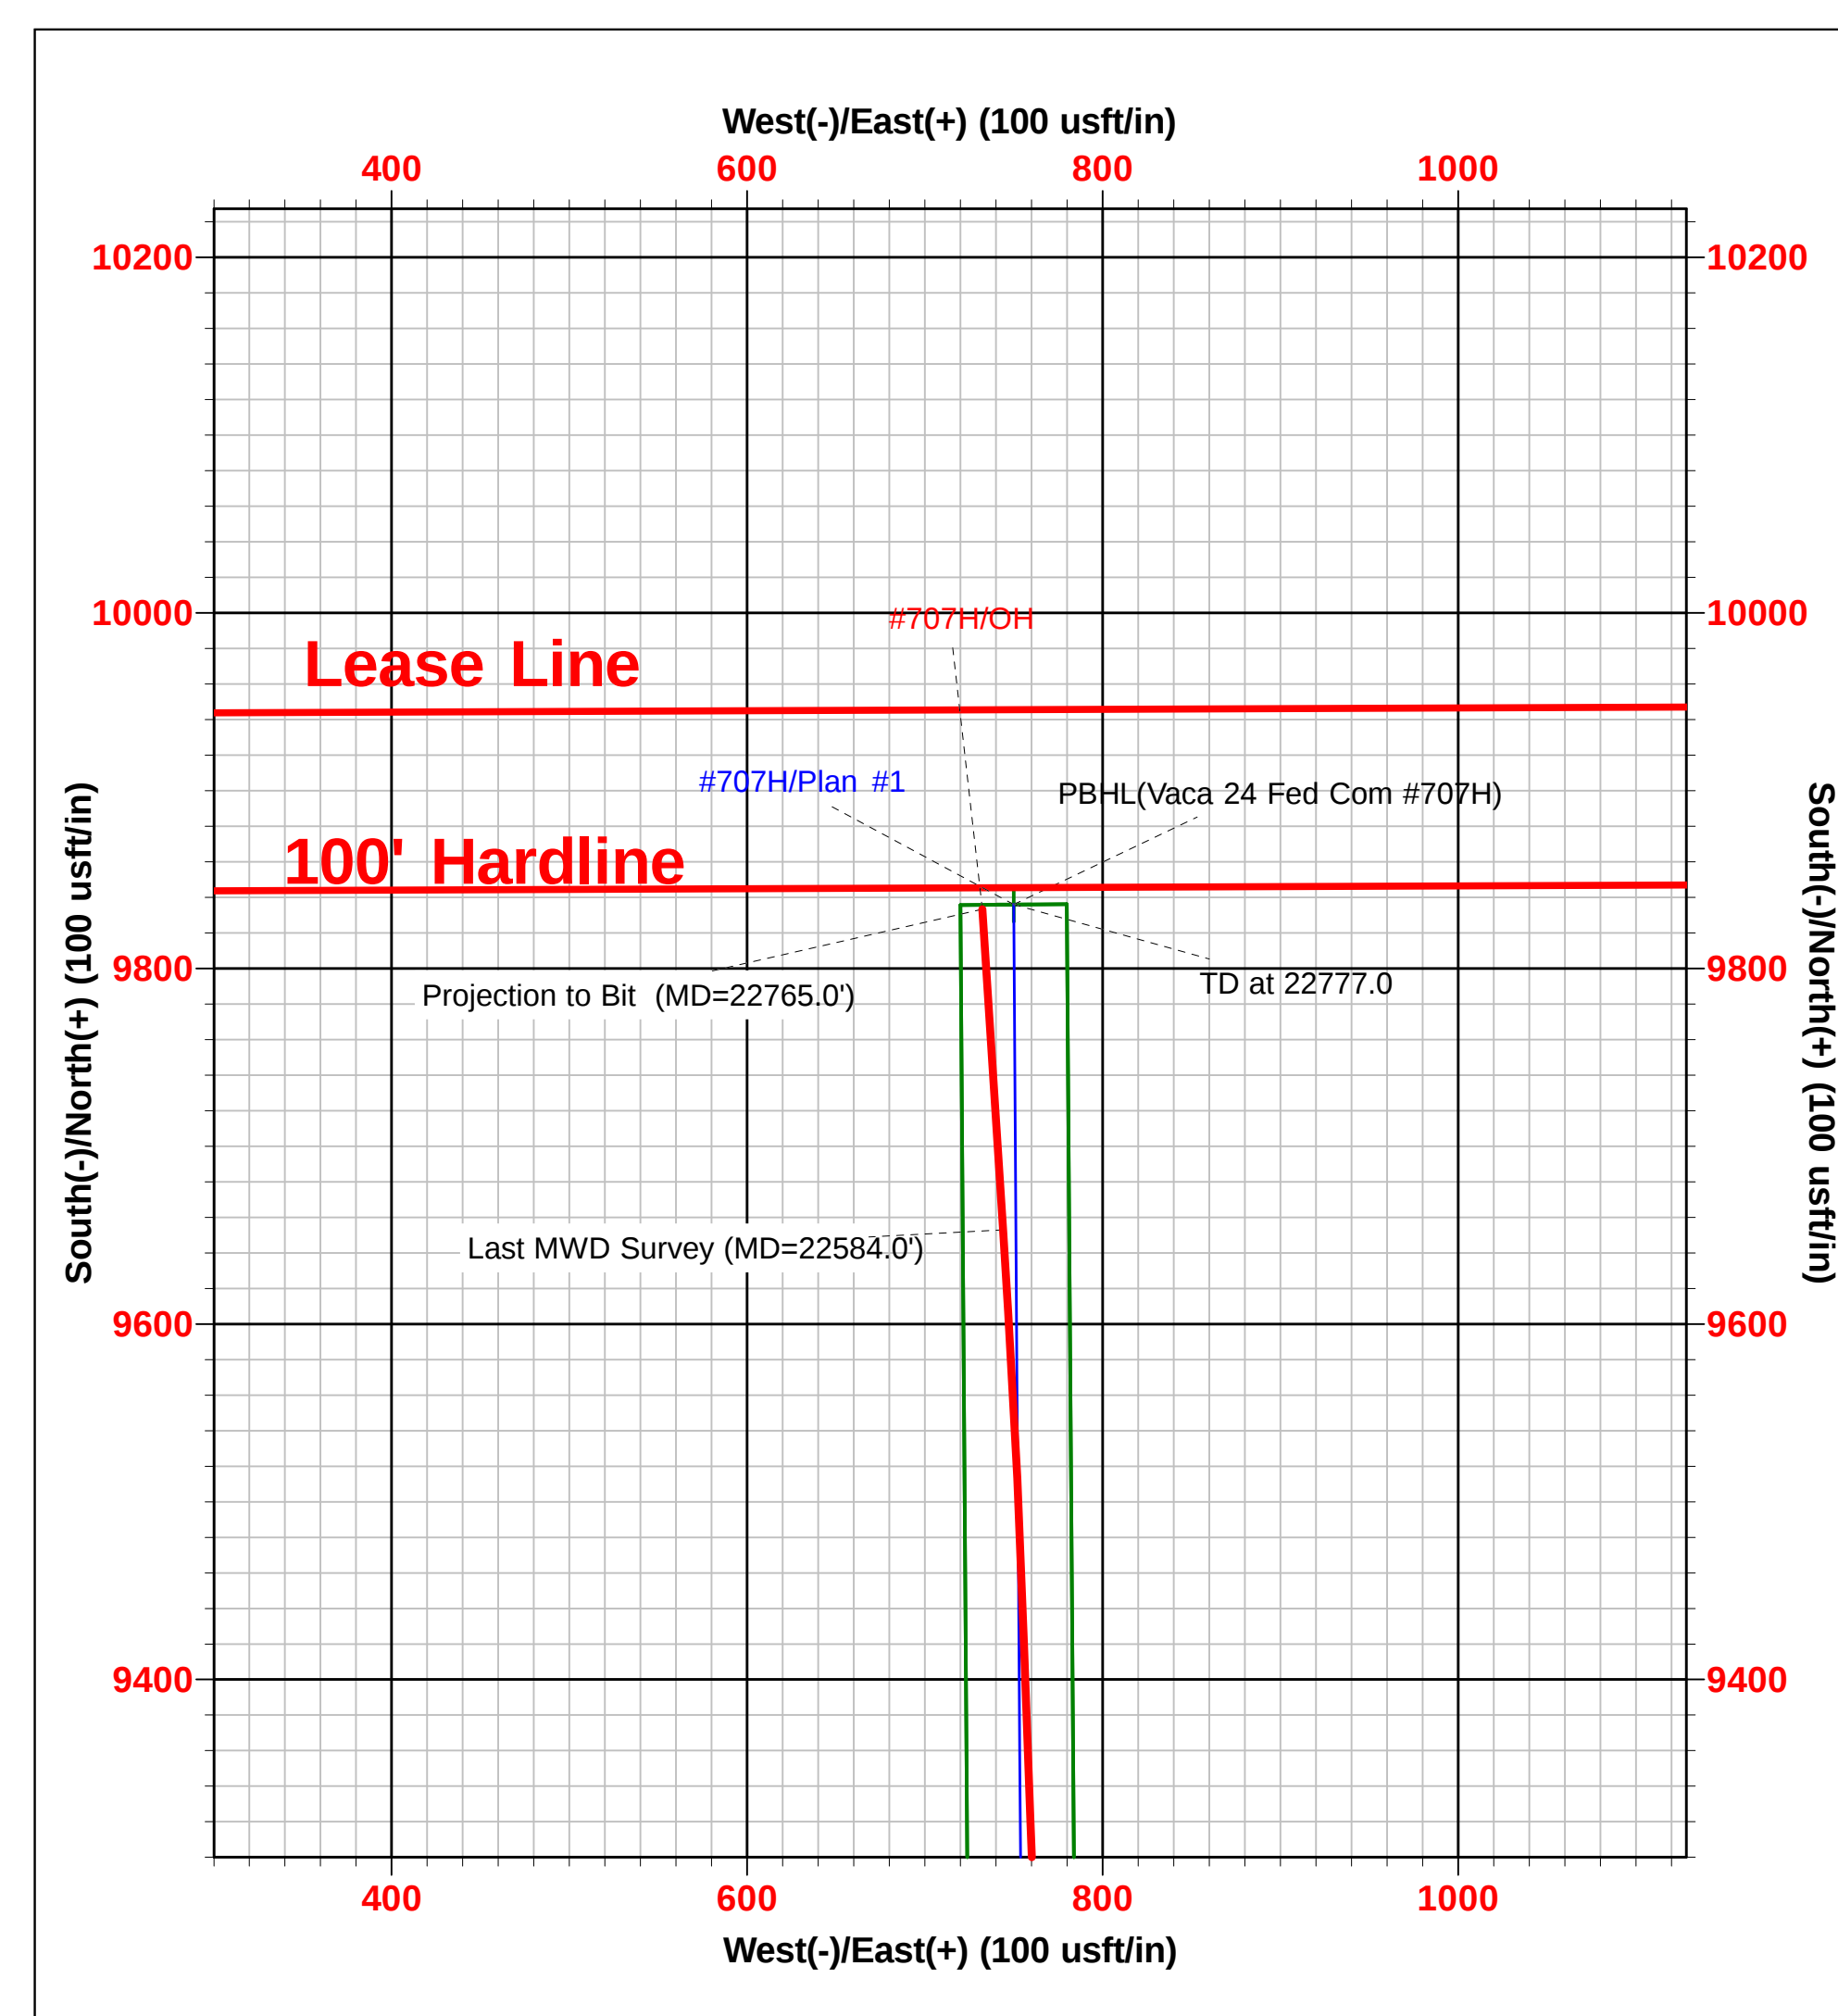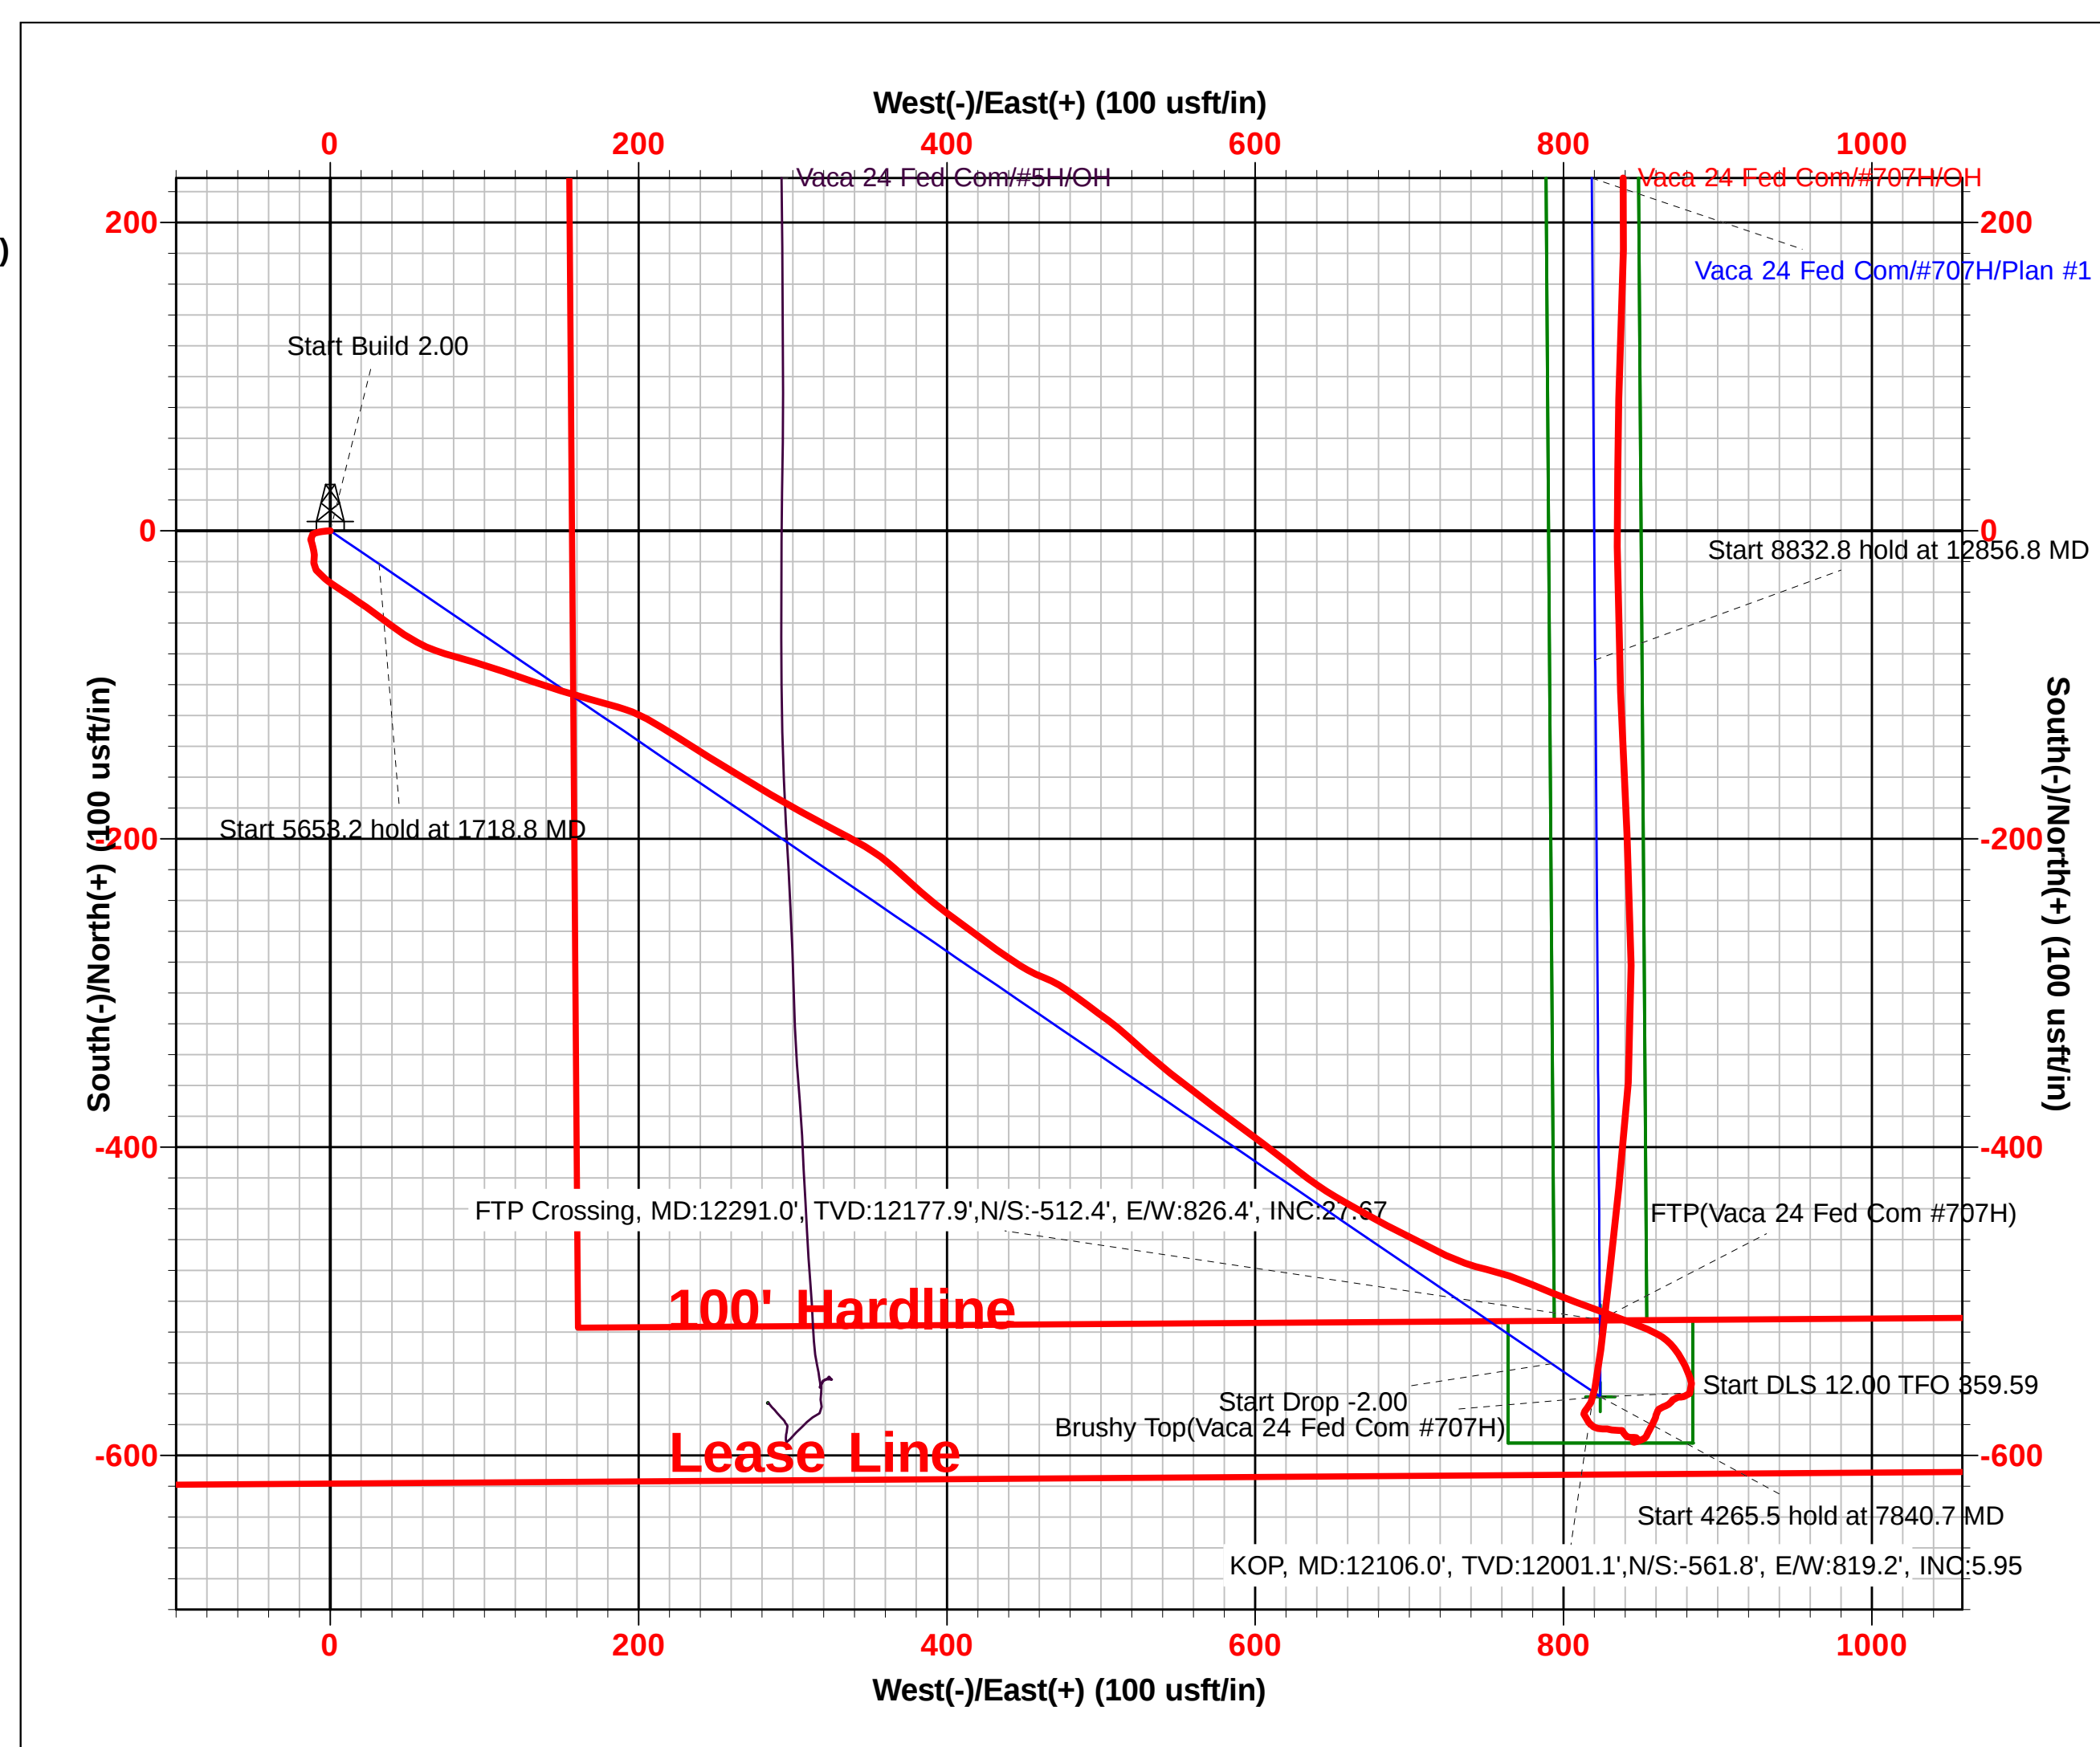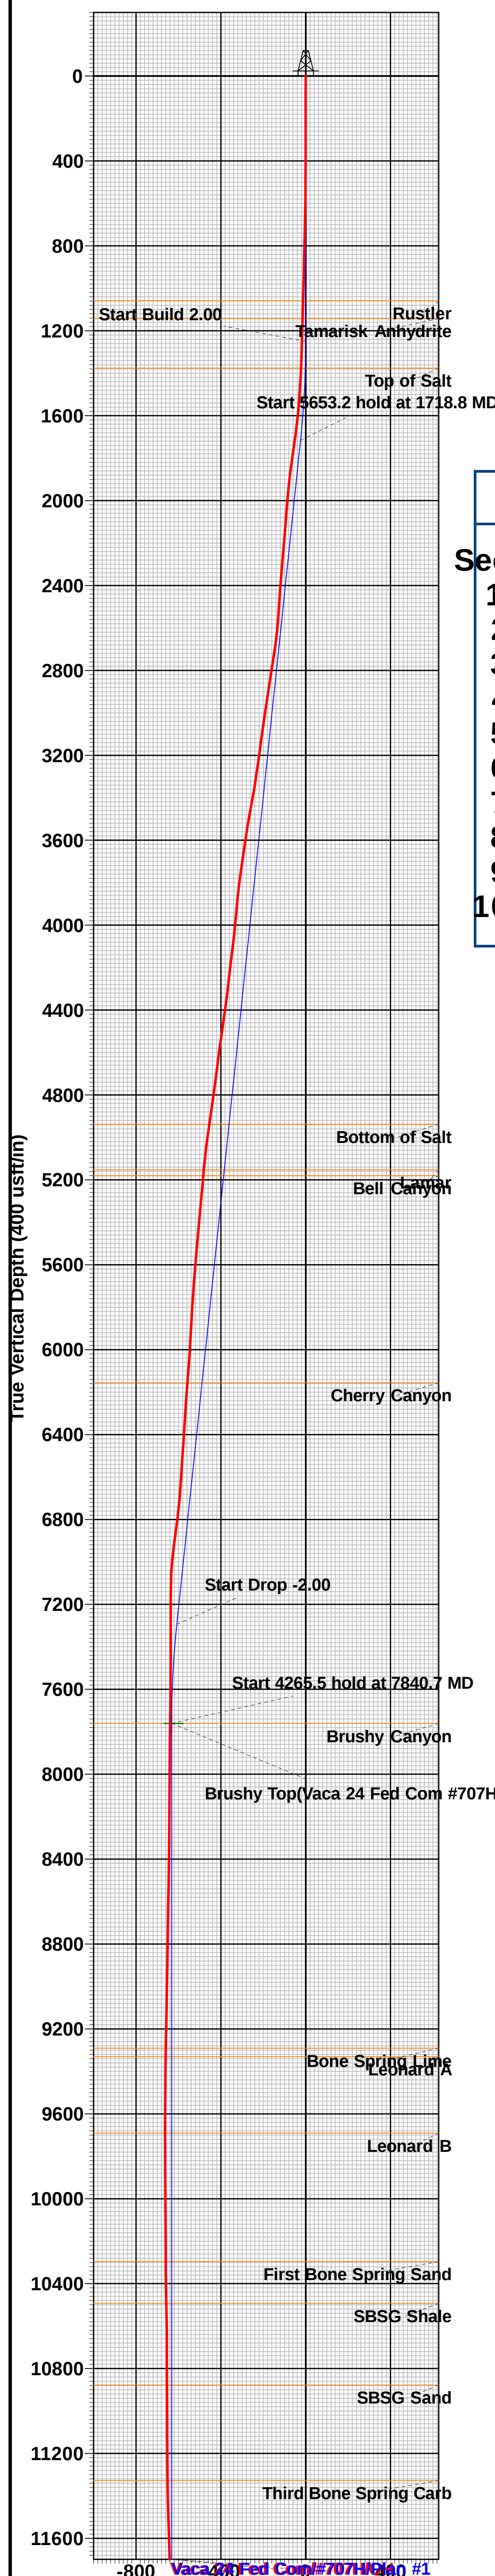

Intent ☐ As Drilled ☐

API #		
Operator Name:	Property Name:	Well Number

Kick Off Point (KOP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

First Take Point (FTP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

Last Take Point (LTP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

Is this well the defining well for the Horizontal Spacing Unit? ☐Is this well an infill well? ☐

If infill is yes please provide API if available, Operator Name and well number for Defining well for Horizontal Spacing Unit.

API #		
Operator Name:	Property Name:	Well Number

KZ 06/29/2018

Well Name: VACA 24 FED COM	Well Location: T25S / R33E / SEC 24 / SWSE / 32.1104623 / -103.5255015	County or Parish/State: LEA / NM
Well Number: 707H	Type of Well: OIL WELL	Allottee or Tribe Name:
Lease Number: NMNM108504	Unit or CA Name:	Unit or CA Number:
US Well Number: 3002546966	Well Status: Drilling Well	Operator: EOG RESOURCES INCORPORATED

Notification

Type of Submission:	Notification	Type of Action:	First Production				
Date Sundry Submitted:	Jun 29, 2021	Time Sundry Submitted:	1:57:14 PM				
First Production Date:	Jun 22, 2021	<table><tr><th>Wellbore Code</th><th>Completion Code</th></tr><tr><td>00</td><td>X1</td></tr></table>		Wellbore Code	Completion Code	00	X1
Wellbore Code	Completion Code						
00	X1						
US Well Number:	3002546966						
First Production Remarks:	02/24/2021 RIG RELEASED 02/26/2021 MIRU TEST VOID TO 5000 PSI, SEALS AND FLANGES TO 8500 PSI 05/03/2021 BEGIN PERF AND FRAC 05/14/2021 FINISH 36 STAGES PERF & FRAC, 12,733 – 22,726’ W/ 3 1/8” 2139 SHOTS, FRAC 24,692,255 LBS PROPPANT + 380,648 BBLS LOAD FLUID 05/17/2021 DRILLED OUT PLUGS AND CLEAN OUT WELLBORE 06/23/2021 OPENED WELL TO FLOWBACK – DATE OF FIRST PRODUCTION						
Disposition:	Accepted						
Accepted Date:	06/30/2021						

Submit To Appropriate District Office Two Copies <u>District I</u> 1625 N. French Dr., Hobbs, NM 88240 <u>District II</u> 811 S. First St., Artesia, NM 88210 <u>District III</u> 1000 Rio Brazos Rd., Aztec, NM 87410 <u>District IV</u> 1220 S. St. Francis Dr., Santa Fe, NM 87505		State of New Mexico Energy, Minerals and Natural Resources Oil Conservation Division 1220 South St. Francis Dr. Santa Fe, NM 87505			Form C-105 Revised August 1, 2011					
WELL COMPLETION OR RECOMPLETION REPORT AND LOG										
4. Reason for filing: ☒ COMPLETION REPORT (Fill in boxes #1 through #31 for State and Fee wells only) ☐ C-144 CLOSURE ATTACHMENT (Fill in boxes #1 through #9, #15 Date Rig Released and #32 and/or #33; attach this and the plat to the C-144 closure report in accordance with 19.15.17.13.K NMAC)								5. Lease Name or Unit Agreement Name		
								VACA 24 FEDERAL COM 6. Well Number: 707H		
7. Type of Completion:										
☒ NEW WELL ☐ WORKOVER ☐ DEEPENING ☐ PLUGBACK ☐ DIFFERENT RESERVOIR ☐ OTHER _____										
8. Name of Operator						9. OGRID				
EOG RESOURCES INC						7377				
10. Address of Operator						11. Pool name or Wildcat				
PO BOX 2267 MIDLAND, TEXAS 79702						BOBCAT DRAW; UPPER WOLFCAMP				
12. Location	Unit Ltr	Section	Township	Range	Lot	Feet from the	N/S Line	Feet from the	E/W Line	County
Surface:	O	24	25S	33E		618'	SOUTH	2471'	EAST	LEA
BH:	B	13	25S	33E		111'	NORTH	1668'	EAST	LEA
13. Date Spudded	14. Date T.D. Reached		15. Date Rig Released			16. Date Completed (Ready to Produce)		17. Elevations (DF and RKB, RT, GR, etc.)		
01/08/2021	02/22/2021		02/24/2021			06/23/2021		3332' GL		
18. Total Measured Depth of Well			19. Plug Back Measured Depth			20. Was Directional Survey Made?		21. Type Electric and Other Logs Run		
MD 22,765' TVD 12,486'			MD 22,726' TVD 12,486'			YES		None		
22. Producing Interval(s), of this completion - Top, Bottom, Name										
WOLFCAMP 12,733 - 22,726'										
CASING RECORD (Report all strings set in well)										
CASING SIZE		WEIGHT LB./FT.		DEPTH SET		HOLE SIZE		CEMENTING RECORD		AMOUNT PULLED
9 5/8"		40# J-55		1209'		12 1/4"		525 CL C/CIRC		
7 5/8"		29.7# HCP 110		11,908'		8 3/4"		1660 CL C/ TOC 42'		ECHO
5 1/2"		20# ECP 110		22,735'		6 3/4"		975 CL H/TOC 11,200'		CBL
24. LINER RECORD						25. TUBING RECORD				
SIZE	TOP	BOTTOM	SACKS CEMENT	SCREEN		SIZE	DEPTH SET	PACKER SET		
26. Perforation record (interval, size, and number)						27. ACID, SHOT, FRACTURE, CEMENT, SQUEEZE, ETC.				
						DEPTH INTERVAL		AMOUNT AND KIND MATERIAL USED		
						12,733 - 22,726		FRAC W/24,692,255 lbs proppant, 380,648 bbls load fld		
PRODUCTION										
Date First Production		Production Method (Flowing, gas lift, pumping - Size and type pump)				Well Status (Prod. or Shut-in)				
06/23/2021		Flowing				Producing				
Date of Test	Hours Tested	Choke Size	Prod'n For Test Period	Oil - Bbl	Gas - MCF	Water - Bbl.	Gas - Oil Ratio			
06/28/2021	24	34		3932	6588	5708	1675			
Flow Tubing Press.	Casing Pressure	Calculated 24-Hour Rate	Oil - Bbl.	Gas - MCF	Water - Bbl.	Oil Gravity - API - (Corr.)				
	3847					44				
29. Disposition of Gas (Sold, used for fuel, vented, etc.)								30. Test Witnessed By		
SOLD										
31. List Attachments										
C-102, C-104, C-103, Directional Survey, H spacing										
32. If a temporary pit was used at the well, attach a plat with the location of the temporary pit.										
33. If an on-site burial was used at the well, report the exact location of the on-site burial:										
Latitude _____ Longitude _____ NAD 1927 1983										
I hereby certify that the information shown on both sides of this form is true and complete to the best of my knowledge and belief										
Signature Kay Maddox			Name Kay Maddox			Title Senior Regulatory Specialist			Date 06/30/2021	
E-mail Address kay_maddox@eogresources.com										

This form is to be filed with the appropriate District Office of the Division not later than 20 days after the completion of any newly-drilled or deepened well and not later than 60 days after completion of closure. When submitted as a completion report, this shall be accompanied by one copy of all electrical and radio-activity logs run on the well and a summary of all special tests conducted, including drill stem tests. All depths reported shall be measured depths. In the case of directionally drilled wells, true vertical depths shall also be reported. For multiple completions, items 11, 12 and 26-31 shall be reported for each zone.

Southeastern New Mexico		Northwestern New Mexico	
T. Anhy Rustler 1059'	T. Canyon Brushy 7761'	T. Ojo Alamo	T. Penn A "
T. Salt 1376'	T. Strawn	T. Kirtland	T. Penn. "B"
B. Salt 4938'	T. Atoka	T. Fruitland	T. Penn. "C"
T. Yates	T. Miss	T. Pictured Cliffs	T. Penn. "D"
T. 7 Rivers	T. Devonian	T. Cliff House	T. Leadville
T. Queen	T. Silurian	T. Menefee	T. Madison
T. Grayburg	T. Montoya	T. Point Lookout	T. Elbert
T. San Andres	T. Simpson	T. Mancos	T. McCracken
T. Glorieta	T. McKee	T. Gallup	T. Ignacio Otzte
T. Paddock	T. Ellenburger	Base Greenhorn	T. Granite
T. Blinebry	T. Gr. Wash	T. Dakota	
T. Tubb	T. Delaware Sand	T. Morrison	
T. Drinkard	T. Bone Springs	T. Todilto	
T. Abo	T. 1ST BONE SPRING SAND 10,296'	T. Entrada	
T. Wolfcamp 12,343'	T. 2ND BONE SPRING SAND 10,878'	T. Wingate	
T. Penn	T. 3RD BONE SPRING SAND 11,903'	T. Chinle	
T. Cisco (Bough C)	T.	T. Permian	

No. 1, from.....to.....
No. 2, from.....to.....
No. 3, from.....to.....
No. 4, from.....to.....

Include data on rate of water inflow and elevation to which water rose in hole.

No. 1, from.....to.....feet.....
 No. 2, from.....to.....feet.....
 No. 3, from.....to.....feet.....

From	To	Thickness In Feet	Lithology

District I
1625 N. French Dr., Hobbs, NM 88240
Phone:(575) 393-6161 Fax:(575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone:(575) 748-1283 Fax:(575) 748-9720
District III
1000 Rio Brazos Rd., Aztec, NM 87410
Phone:(505) 334-6178 Fax:(505) 334-6170
District IV
1220 S. St Francis Dr., Santa Fe, NM 87505
Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

ACKNOWLEDGMENTS

Action 34558

ACKNOWLEDGMENTS

Operator: EOG RESOURCES INC P.O. Box 2267 Midland, TX 79702	OGRID: 7377
	Action Number: 34558
	Action Type: [C-104] Completion Packet (C-104C)

ACKNOWLEDGMENTS

☒	I hereby certify that the required Water Use Report has been, or will be, submitted for this wells completion.
☒	I hereby certify that the required FracFocus disclosure has been, or will be, submitted for this wells completion.

District I
1625 N. French Dr., Hobbs, NM 88240
Phone:(575) 393-6161 Fax:(575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone:(575) 748-1283 Fax:(575) 748-9720
District III
1000 Rio Brazos Rd., Aztec, NM 87410
Phone:(505) 334-6178 Fax:(505) 334-6170
District IV
1220 S. St Francis Dr., Santa Fe, NM 87505
Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 34558

CONDITIONS

Operator: EOG RESOURCES INC P.O. Box 2267 Midland, TX 79702	OGRID: 7377
	Action Number: 34558
	Action Type: [C-104] Completion Packet (C-104C)

CONDITIONS

Created By	Condition	Condition Date
ksimmons	None	8/20/2021
