

I. REQUEST FOR ALLOWABLE MINERAL AUTHORIZATION TO TRANSPORT

¹ Operator name and Address EOG RESOURCES INC PO BOX 2267 MIDLAND, TEXAS 79702		² OGRID Number 7377
		³ Reason for Filing Code/ Effective Date NW 7/8/2022
⁴ API Number 30 - 015-48313	⁵ Pool Name Purple Sage; Wolfcamp	⁶ Pool Code 98220
⁷ Property Code 322721	⁸ Property Name GOLDEN GRAHAM 1 STATE COM	⁹ Well Number 702H

II. ¹⁰ Surface Location

UL or lot no. N	Section 1	Township 26S	Range 28E	Lot Idn	Feet from the 215'	North/South Line SOUTH	Feet from the 1784'	East/West line WEST	County LEA
--------------------	--------------	-----------------	--------------	---------	-----------------------	---------------------------	------------------------	------------------------	---------------

¹¹ Bottom Hole Location

UL or lot no. C	Section 36	Township 25S	Range 28E	Lot Idn	Feet from the 342'	North/South line NORTH	Feet from the 1429'	East/West line WEST	County LEA
¹² Lse Code	¹³ Producing Method Code FLOWING	¹⁴ Gas Connection Date	¹⁵ C-129 Permit Number		¹⁶ C-129 Effective Date		¹⁷ C-129 Expiration Date		

III. Oil and Gas Transporters

¹⁸ Transporter OGRID	¹⁹ Transporter Name and Address	²⁰ O/G/W
372812	EOGRM	OIL
151618	ENTERPRISE FIELD SERVICES	GAS
298751	REGENCY FIELD SERVICES	GAS
36785	DCP MIDSTREAM	GAS

IV. Well Completion Data

²¹ Spud Date 07/14/2021	²² Ready Date 07/8/2022	²³ TD 19,673'	²⁴ PBTD 19,649'	²⁵ Perforations 9,900'-19,649'	²⁶ DHC, MC
²⁷ Hole Size		²⁸ Casing & Tubing Size	²⁹ Depth Set		³⁰ Sacks Cement
12 1/4"		9 5/8"	784'		425 SXS CL C/CIRC
8 3/4"		7 5/8"	9,053'		1396 SXS CL C/CIRC TOC @ SURFACE
6 3/4"		5 1/2"	19,657'		965 SXS CL H/CIRC; TOC @9144' PRESSURE TEST ATTACHED

V. Well Test Data

³¹ Date New Oil 7/8/2022	³² Gas Delivery Date 7/8/2022	³³ Test Date 7/11/2022	³⁴ Test Length 24 HRS	³⁵ Tbg. Pressure	³⁶ Csg. Pressure 960
³⁷ Choke Size 60	³⁸ Oil 1120	³⁹ Water 5170	⁴⁰ Gas 4024		⁴¹ Test Method
⁴² I hereby certify that the rules of the Oil Conservation Division have been complied with and that the information given above is true and complete to the best of my knowledge and belief. Signature: Kristina Agee			OIL CONSERVATION DIVISION		
Printed name: Kristina Agee			Approved by:		
Title: REGULATORY SPECIALIST			Title:		
E-mail Address: kristina_agee@eogresources.com			Approval Date:		
Date: 5/24/2023		Phone: 432-686-6996			

As-Completed Plat
Revised August 1, 2011
Submit one copy to appropriate
District Office
☐ AMENDED REPORT

OPERATOR CERTIFICATION

I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief, and that this organization either owns a working interest or unleased mineral interest in the land including the proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of such a mineral or working interest, or to voluntary pooling agreement or a compulsory pooling order heretofore entered by the division.

Kristina Agee 7/14/2022
Signature Date

Kristina Agee
Print Name

kristina_agee@eogresources.com
E-mail Address

SURVEYORS CERTIFICATION

I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief.

FEBRUARY 8, 2021
Date of Survey

03/25/2022

Ralph B. Chustz, Jr.
Professional Surveyor
26264

Job No.: EOG B200070
RALPH B. CHUSTZ, JR., N.M.P.L.S.
Certificate Number 26264




Eddy County, NM (NAD 83 NME)

Golden Graham 1 State Com #702H










H&P 249

OH

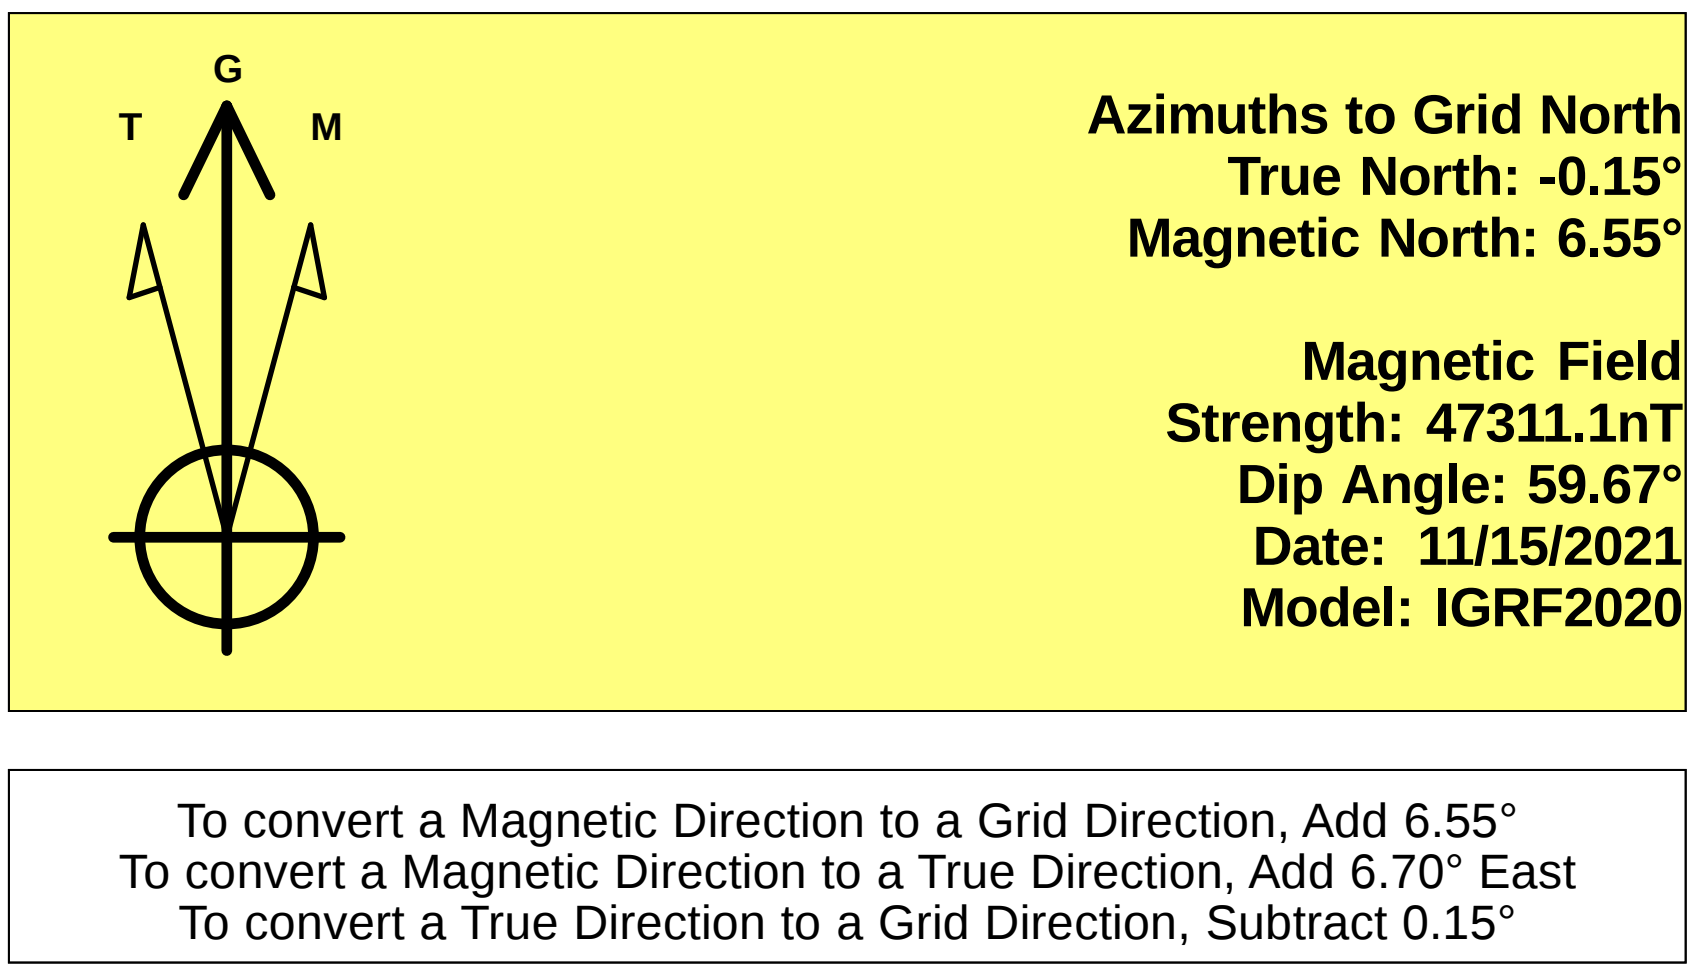

PROJECT DETAILS: Eddy County, NM (NAD 83 NME)			
Geodetic System: US State Plane 1983			
Datum: North American Datum 1983			
Ellipsoid: GRS 1980			
Zone: New Mexico Eastern Zone			
System Datum: Mean Sea Level			

WELL DETAILS: #702H			
KB = 25' @ 2958.0usft (H&P 249)			
2933.0			
Northing	Easting	Latitude	Longitude
387485.00	631116.00	32° 3' 53.801 N	104° 2' 36.637 W

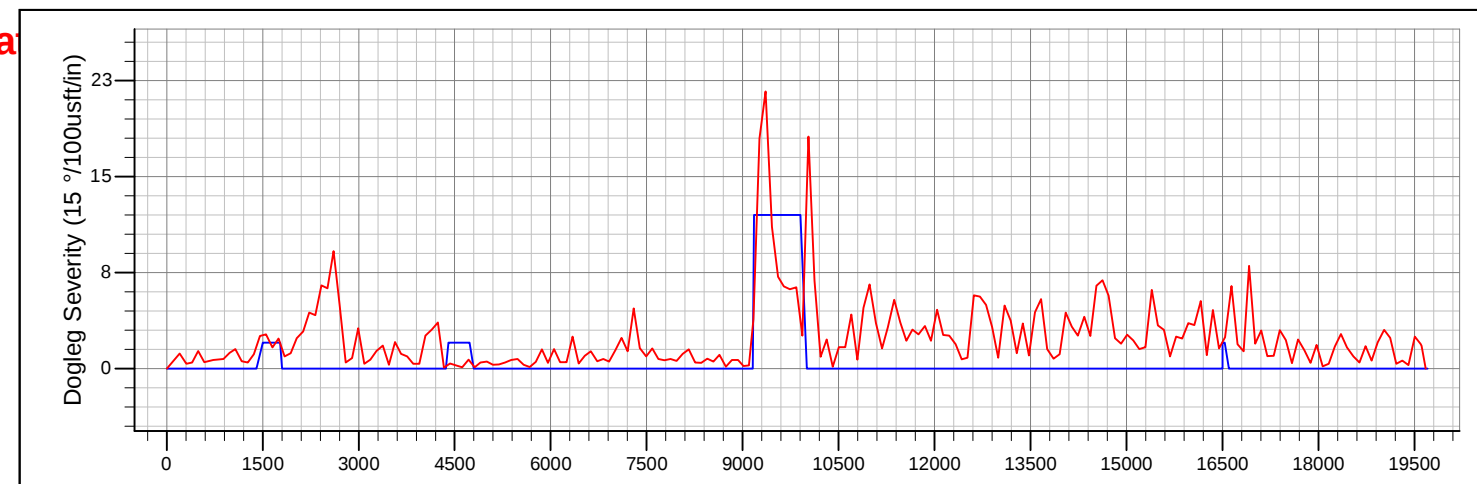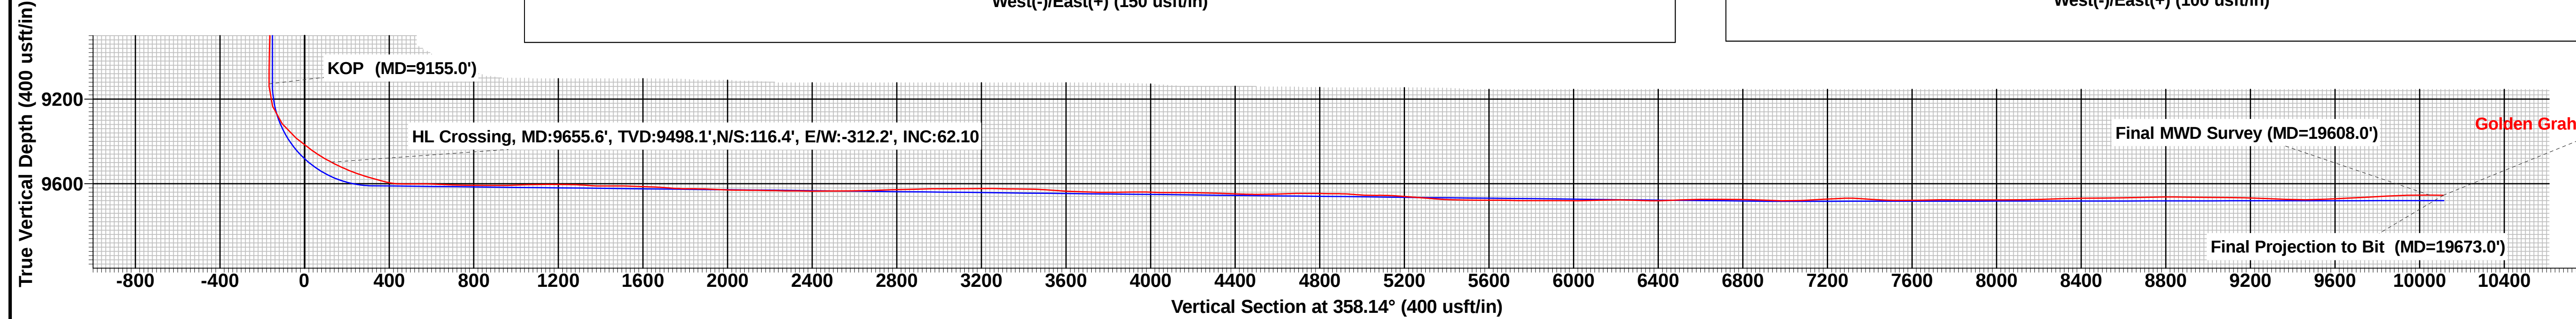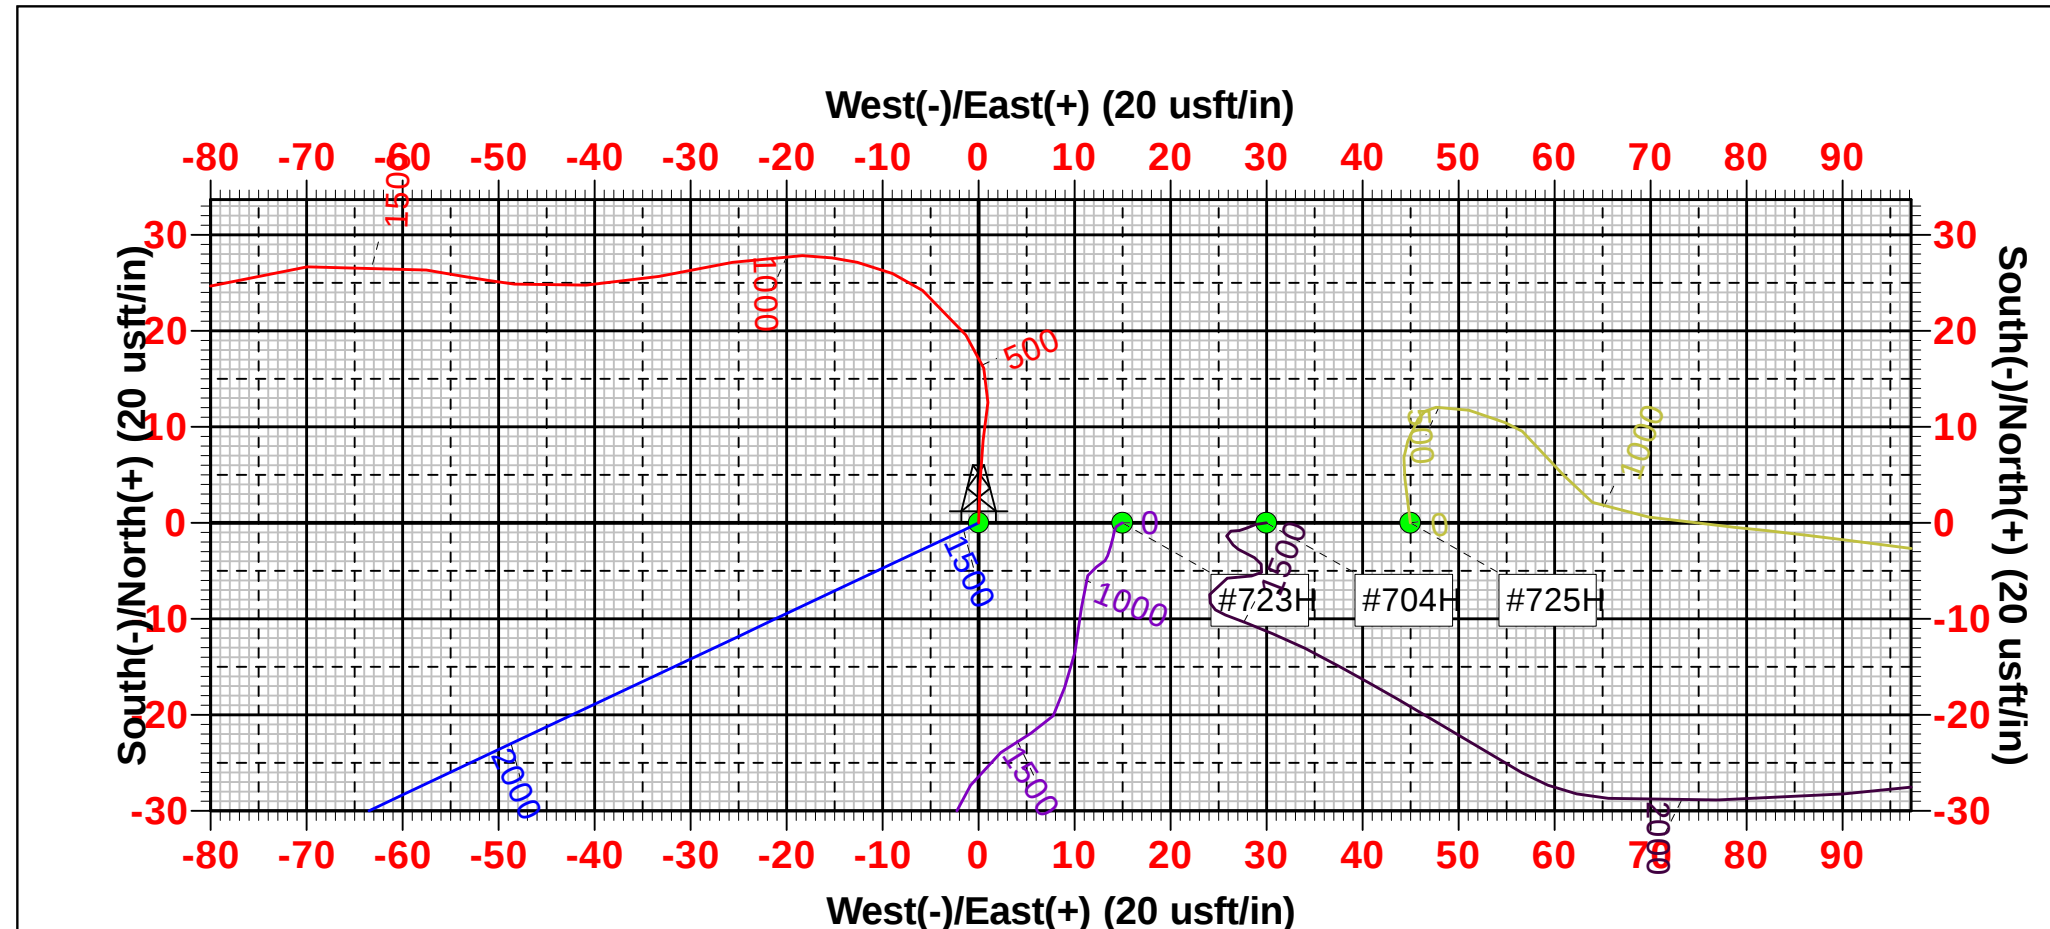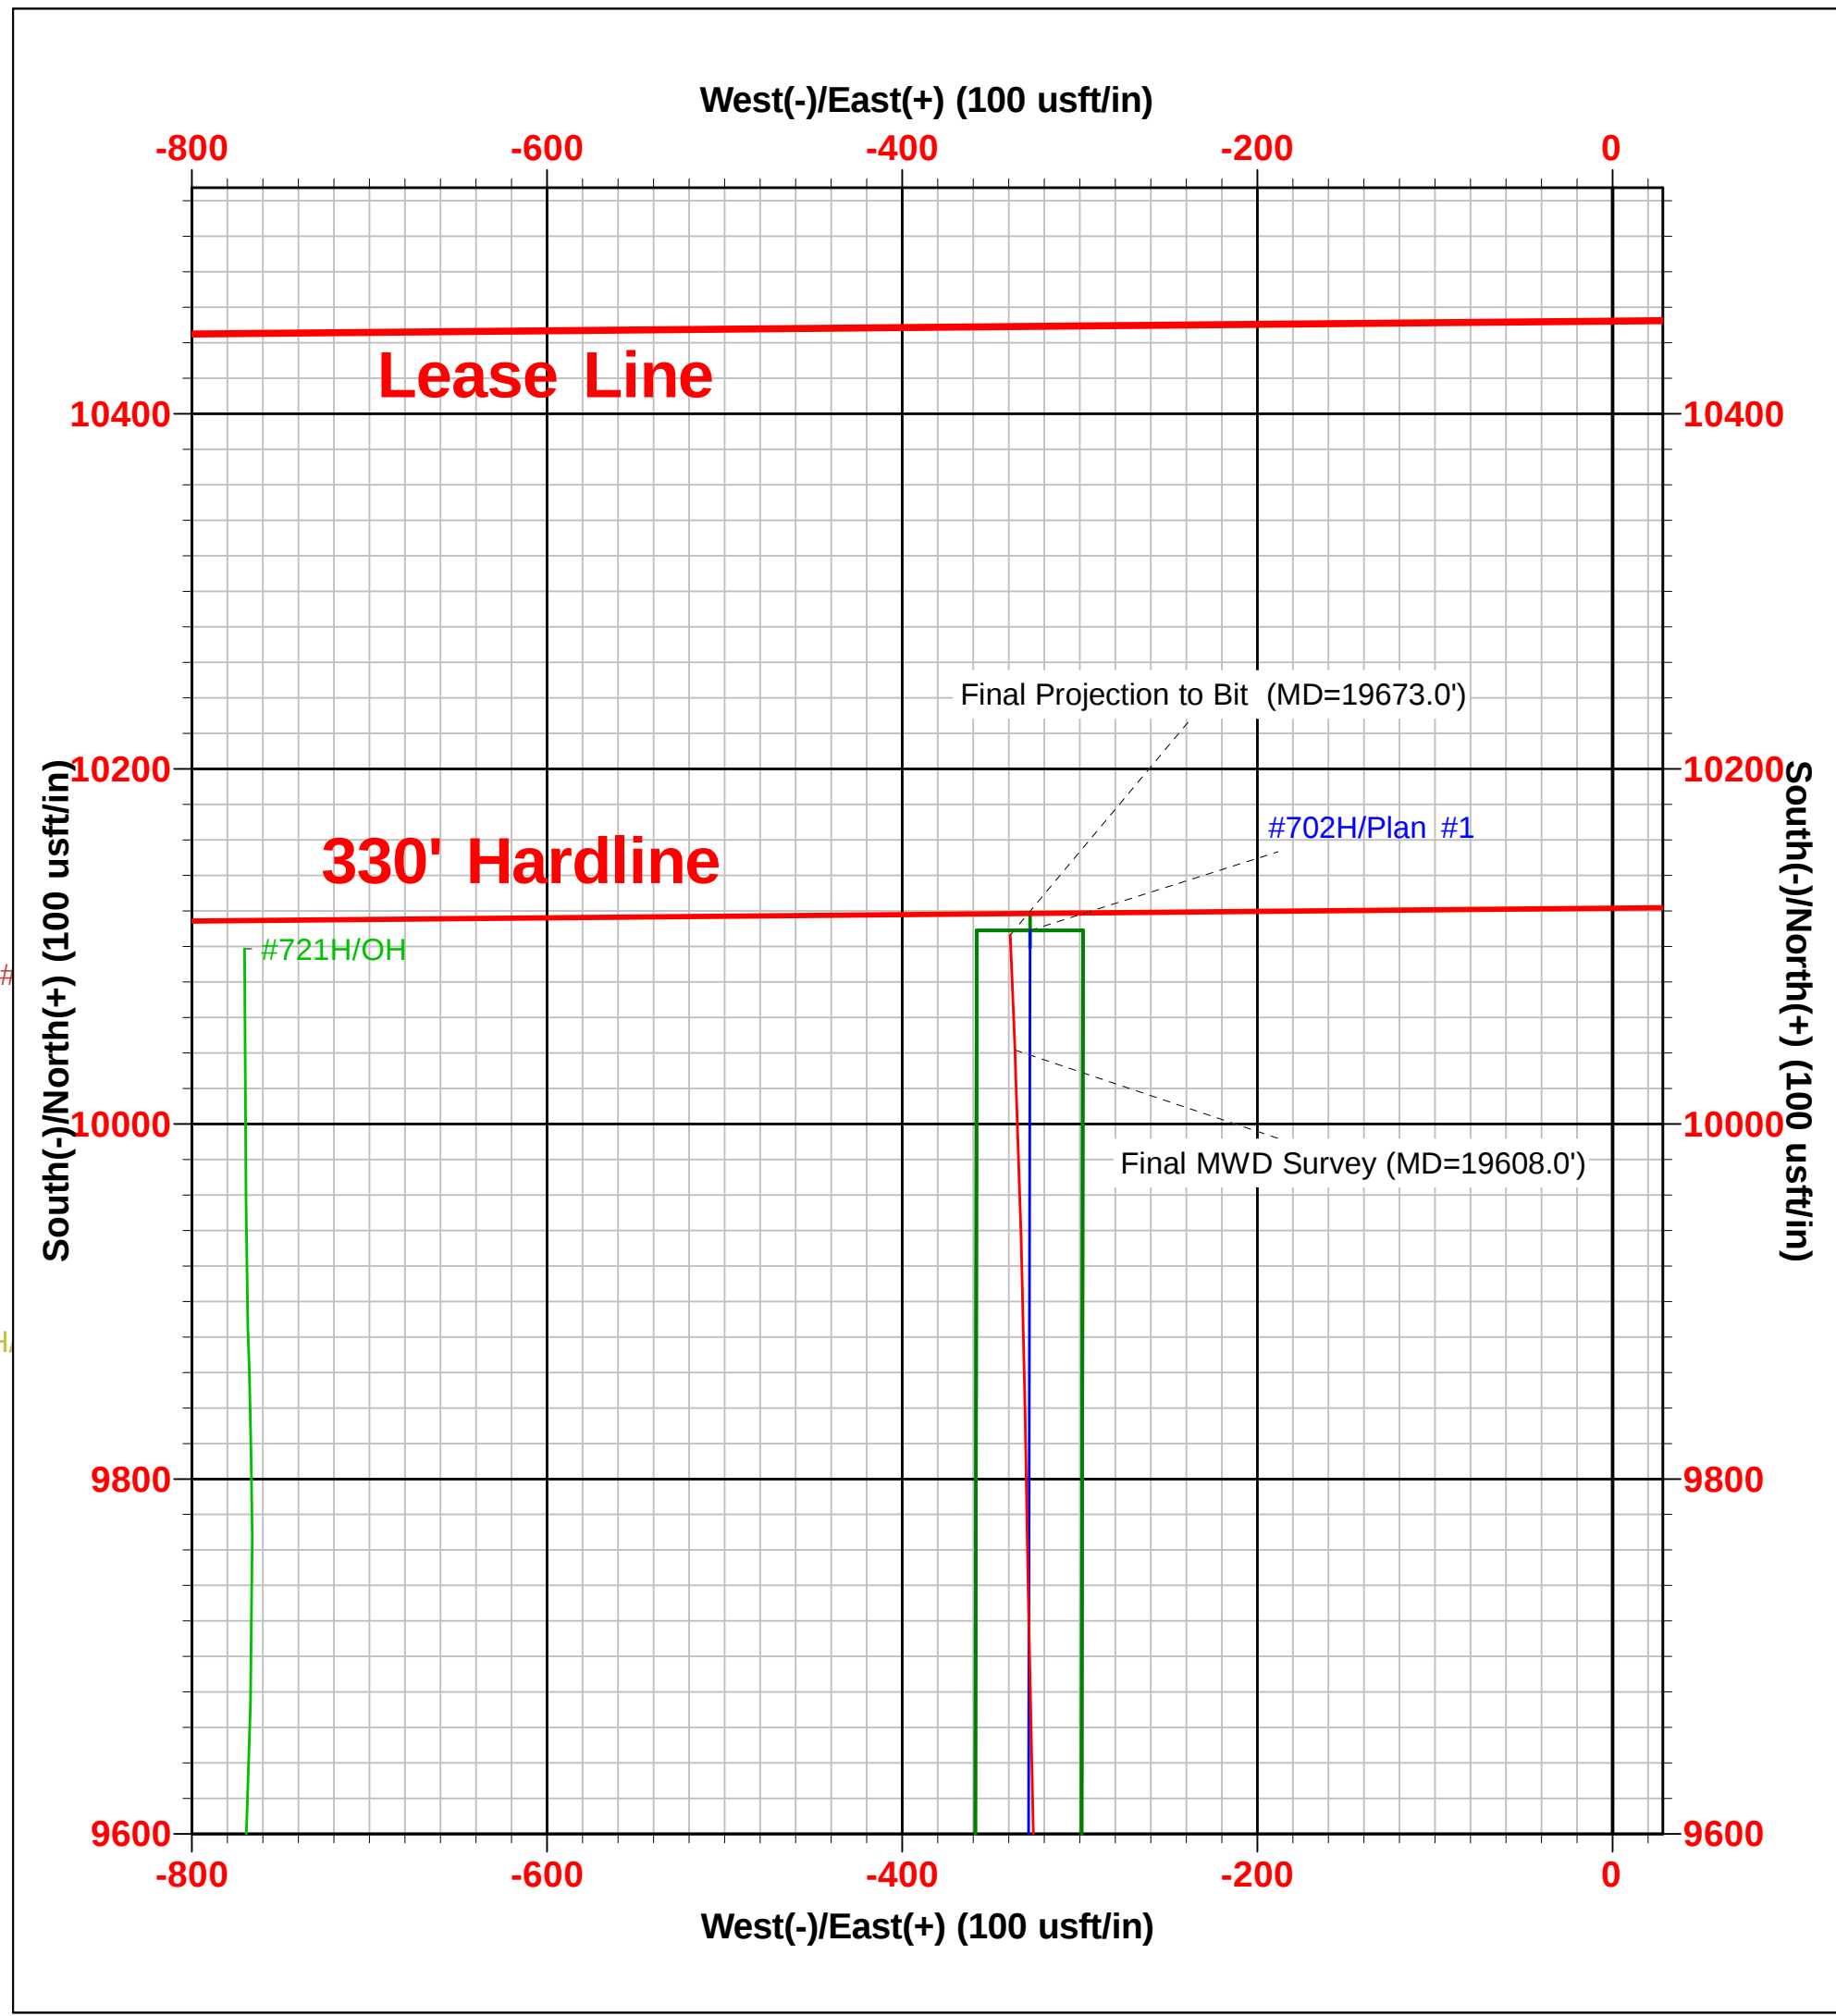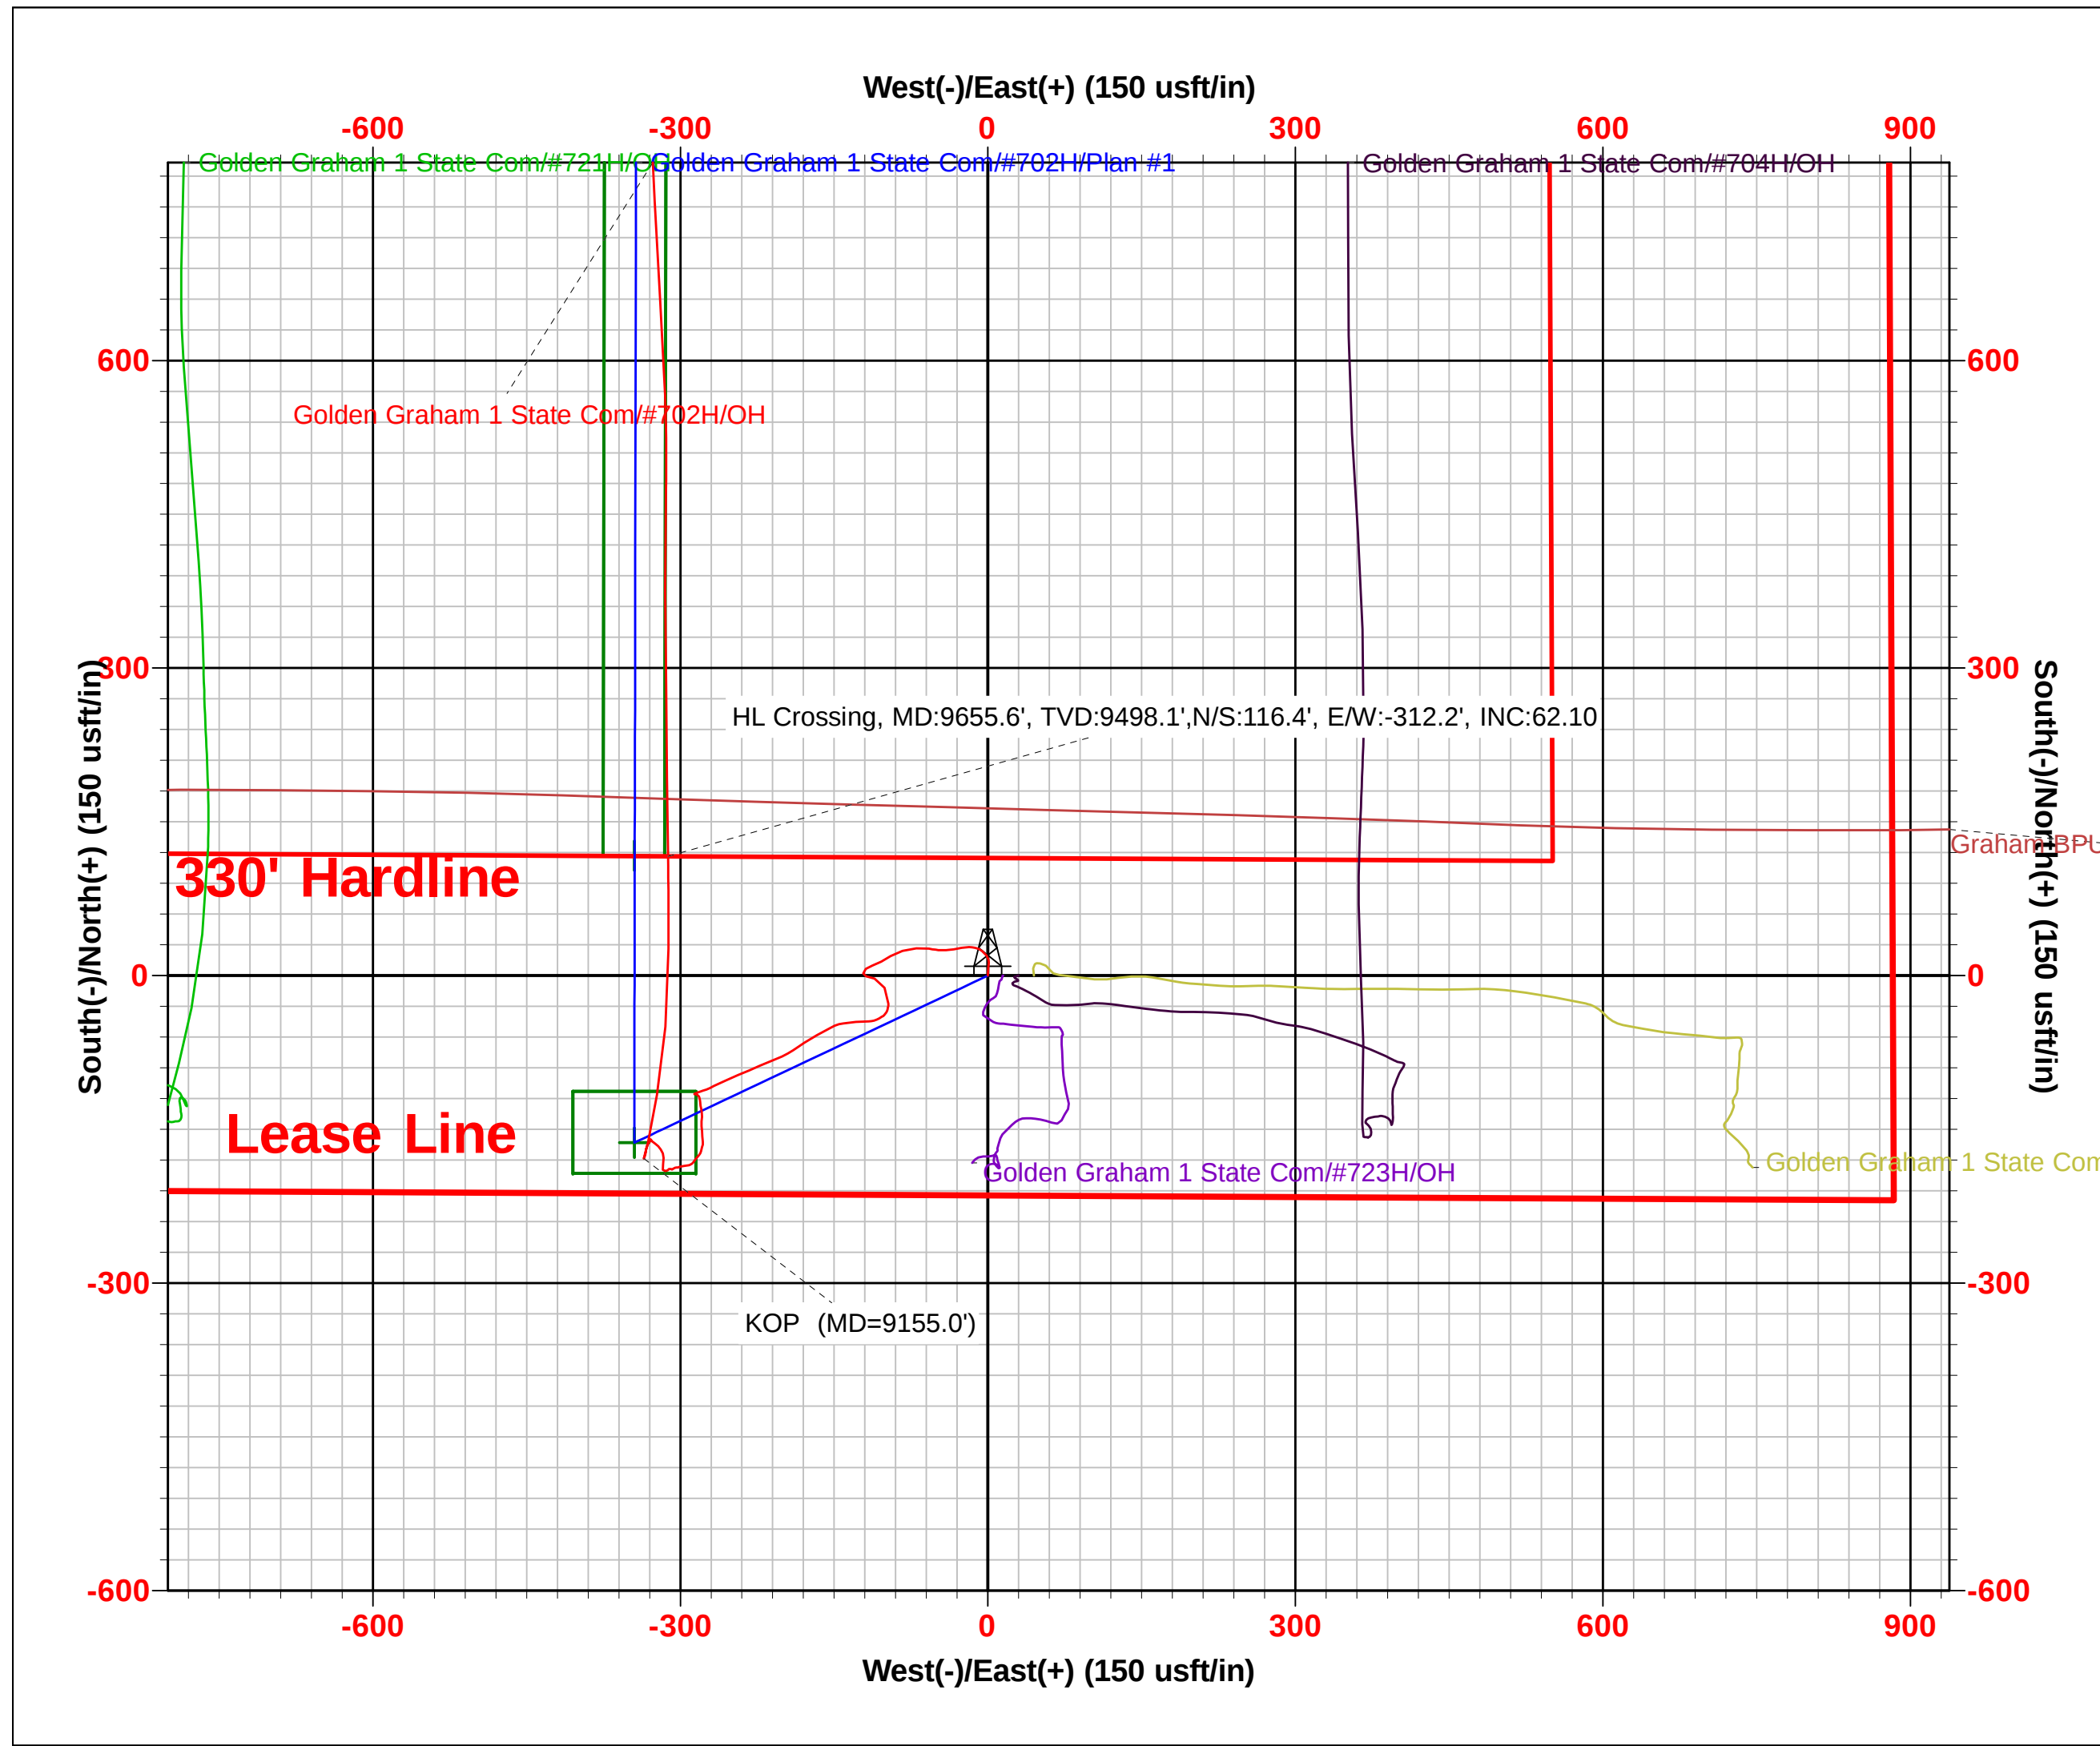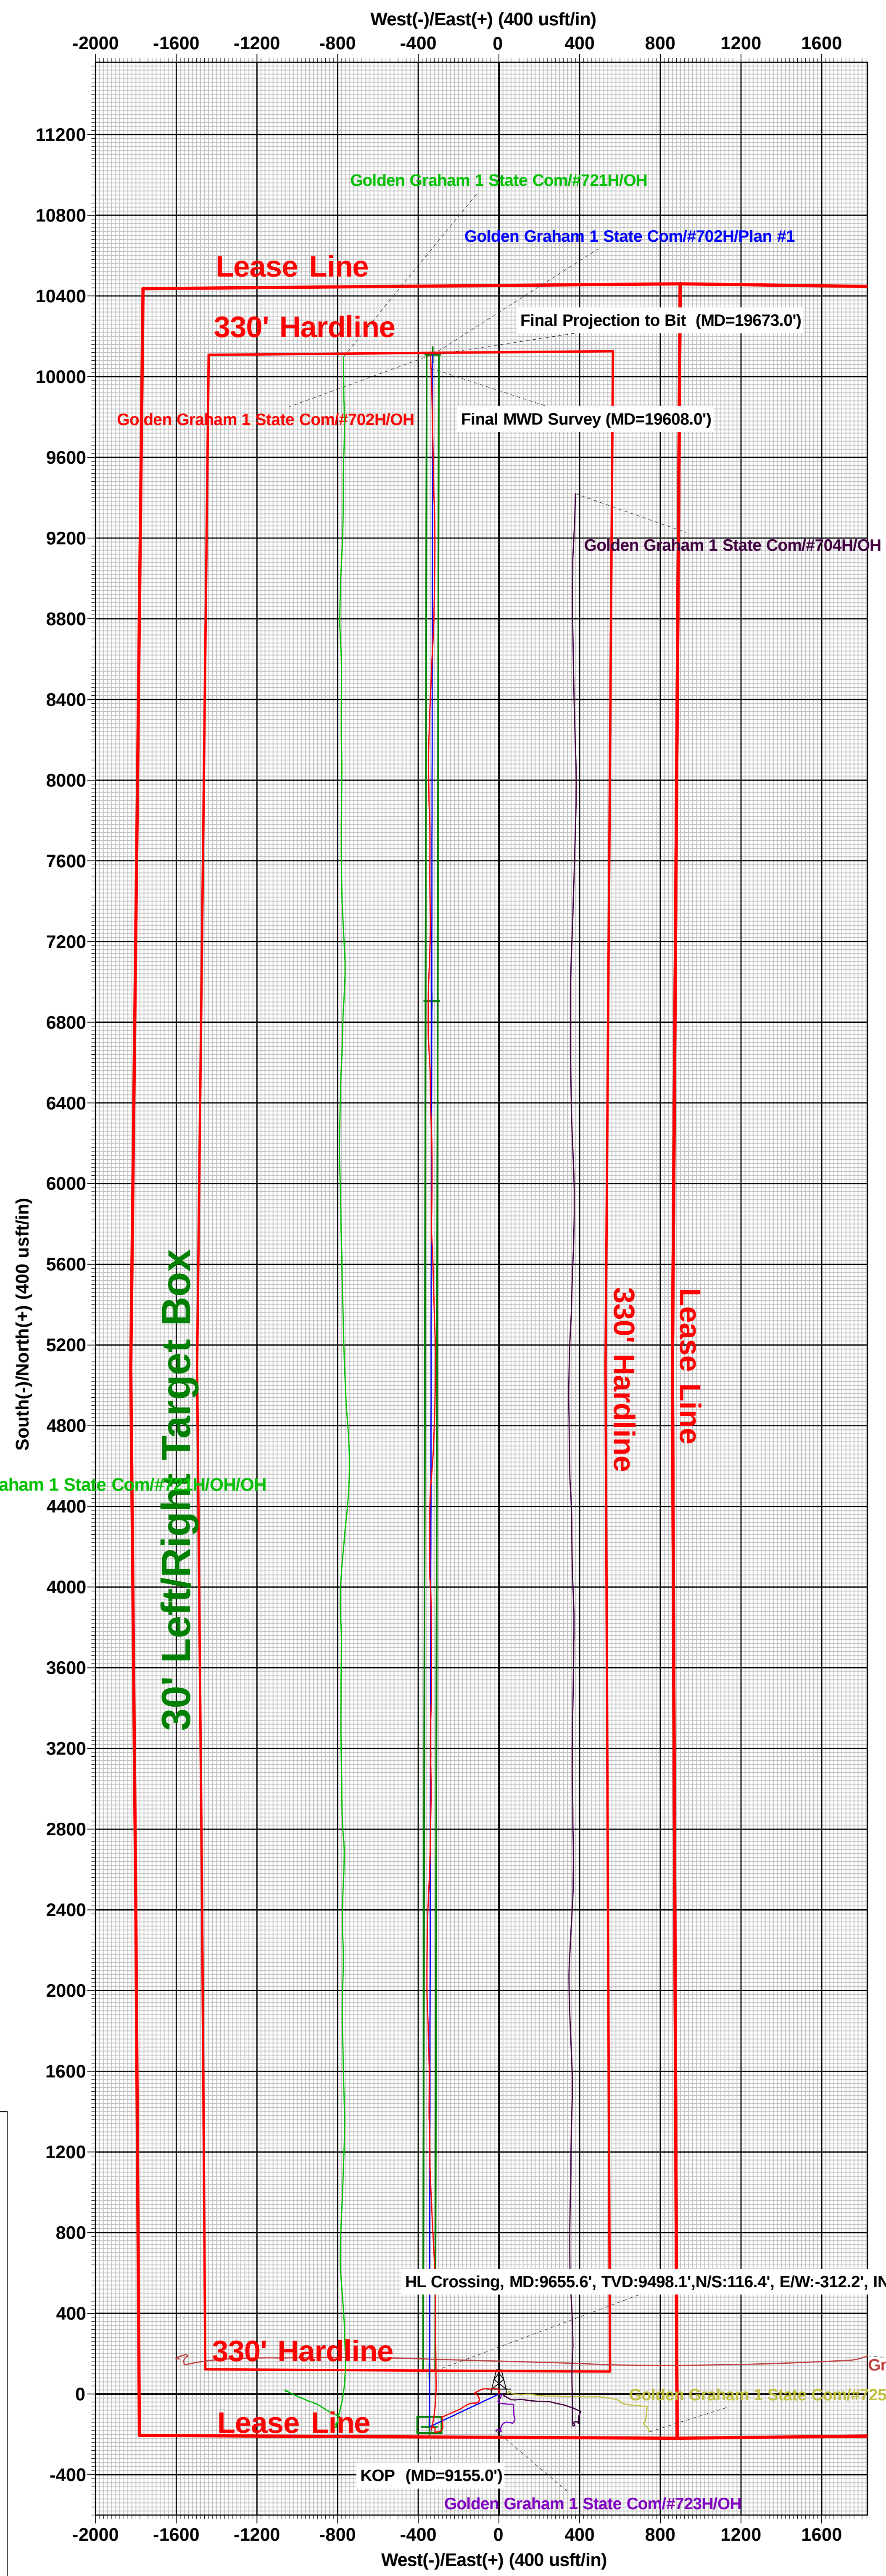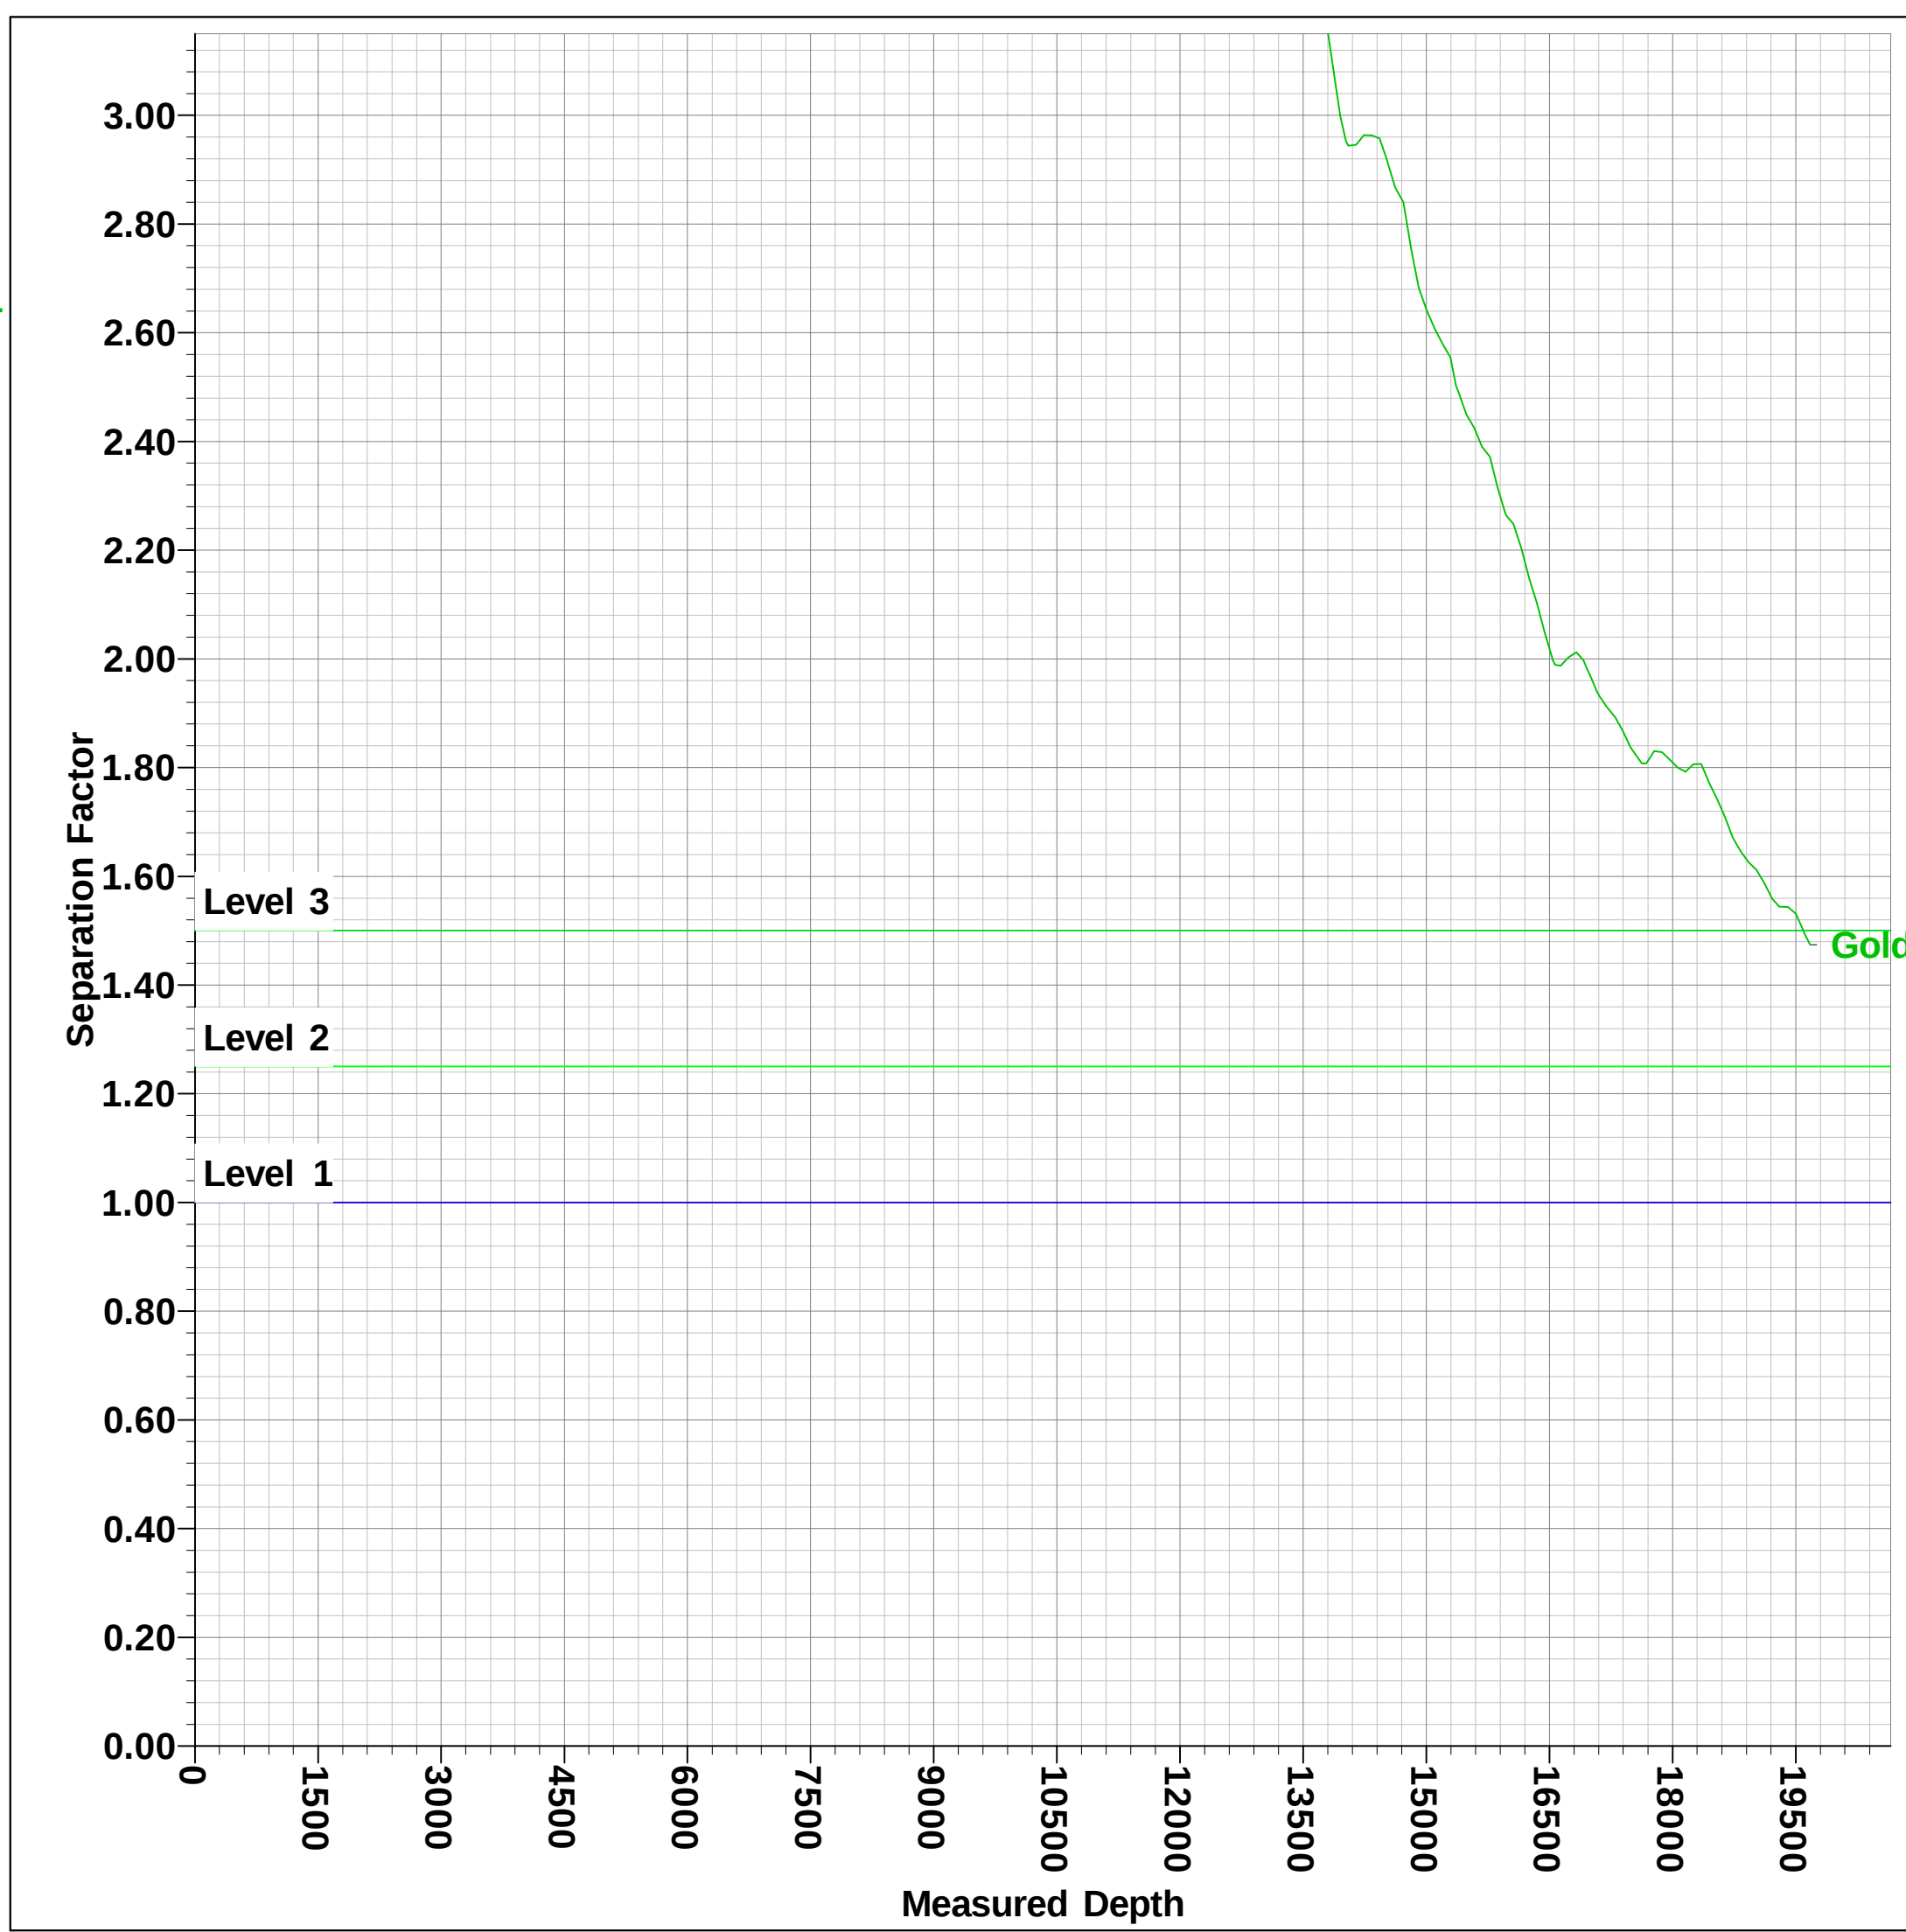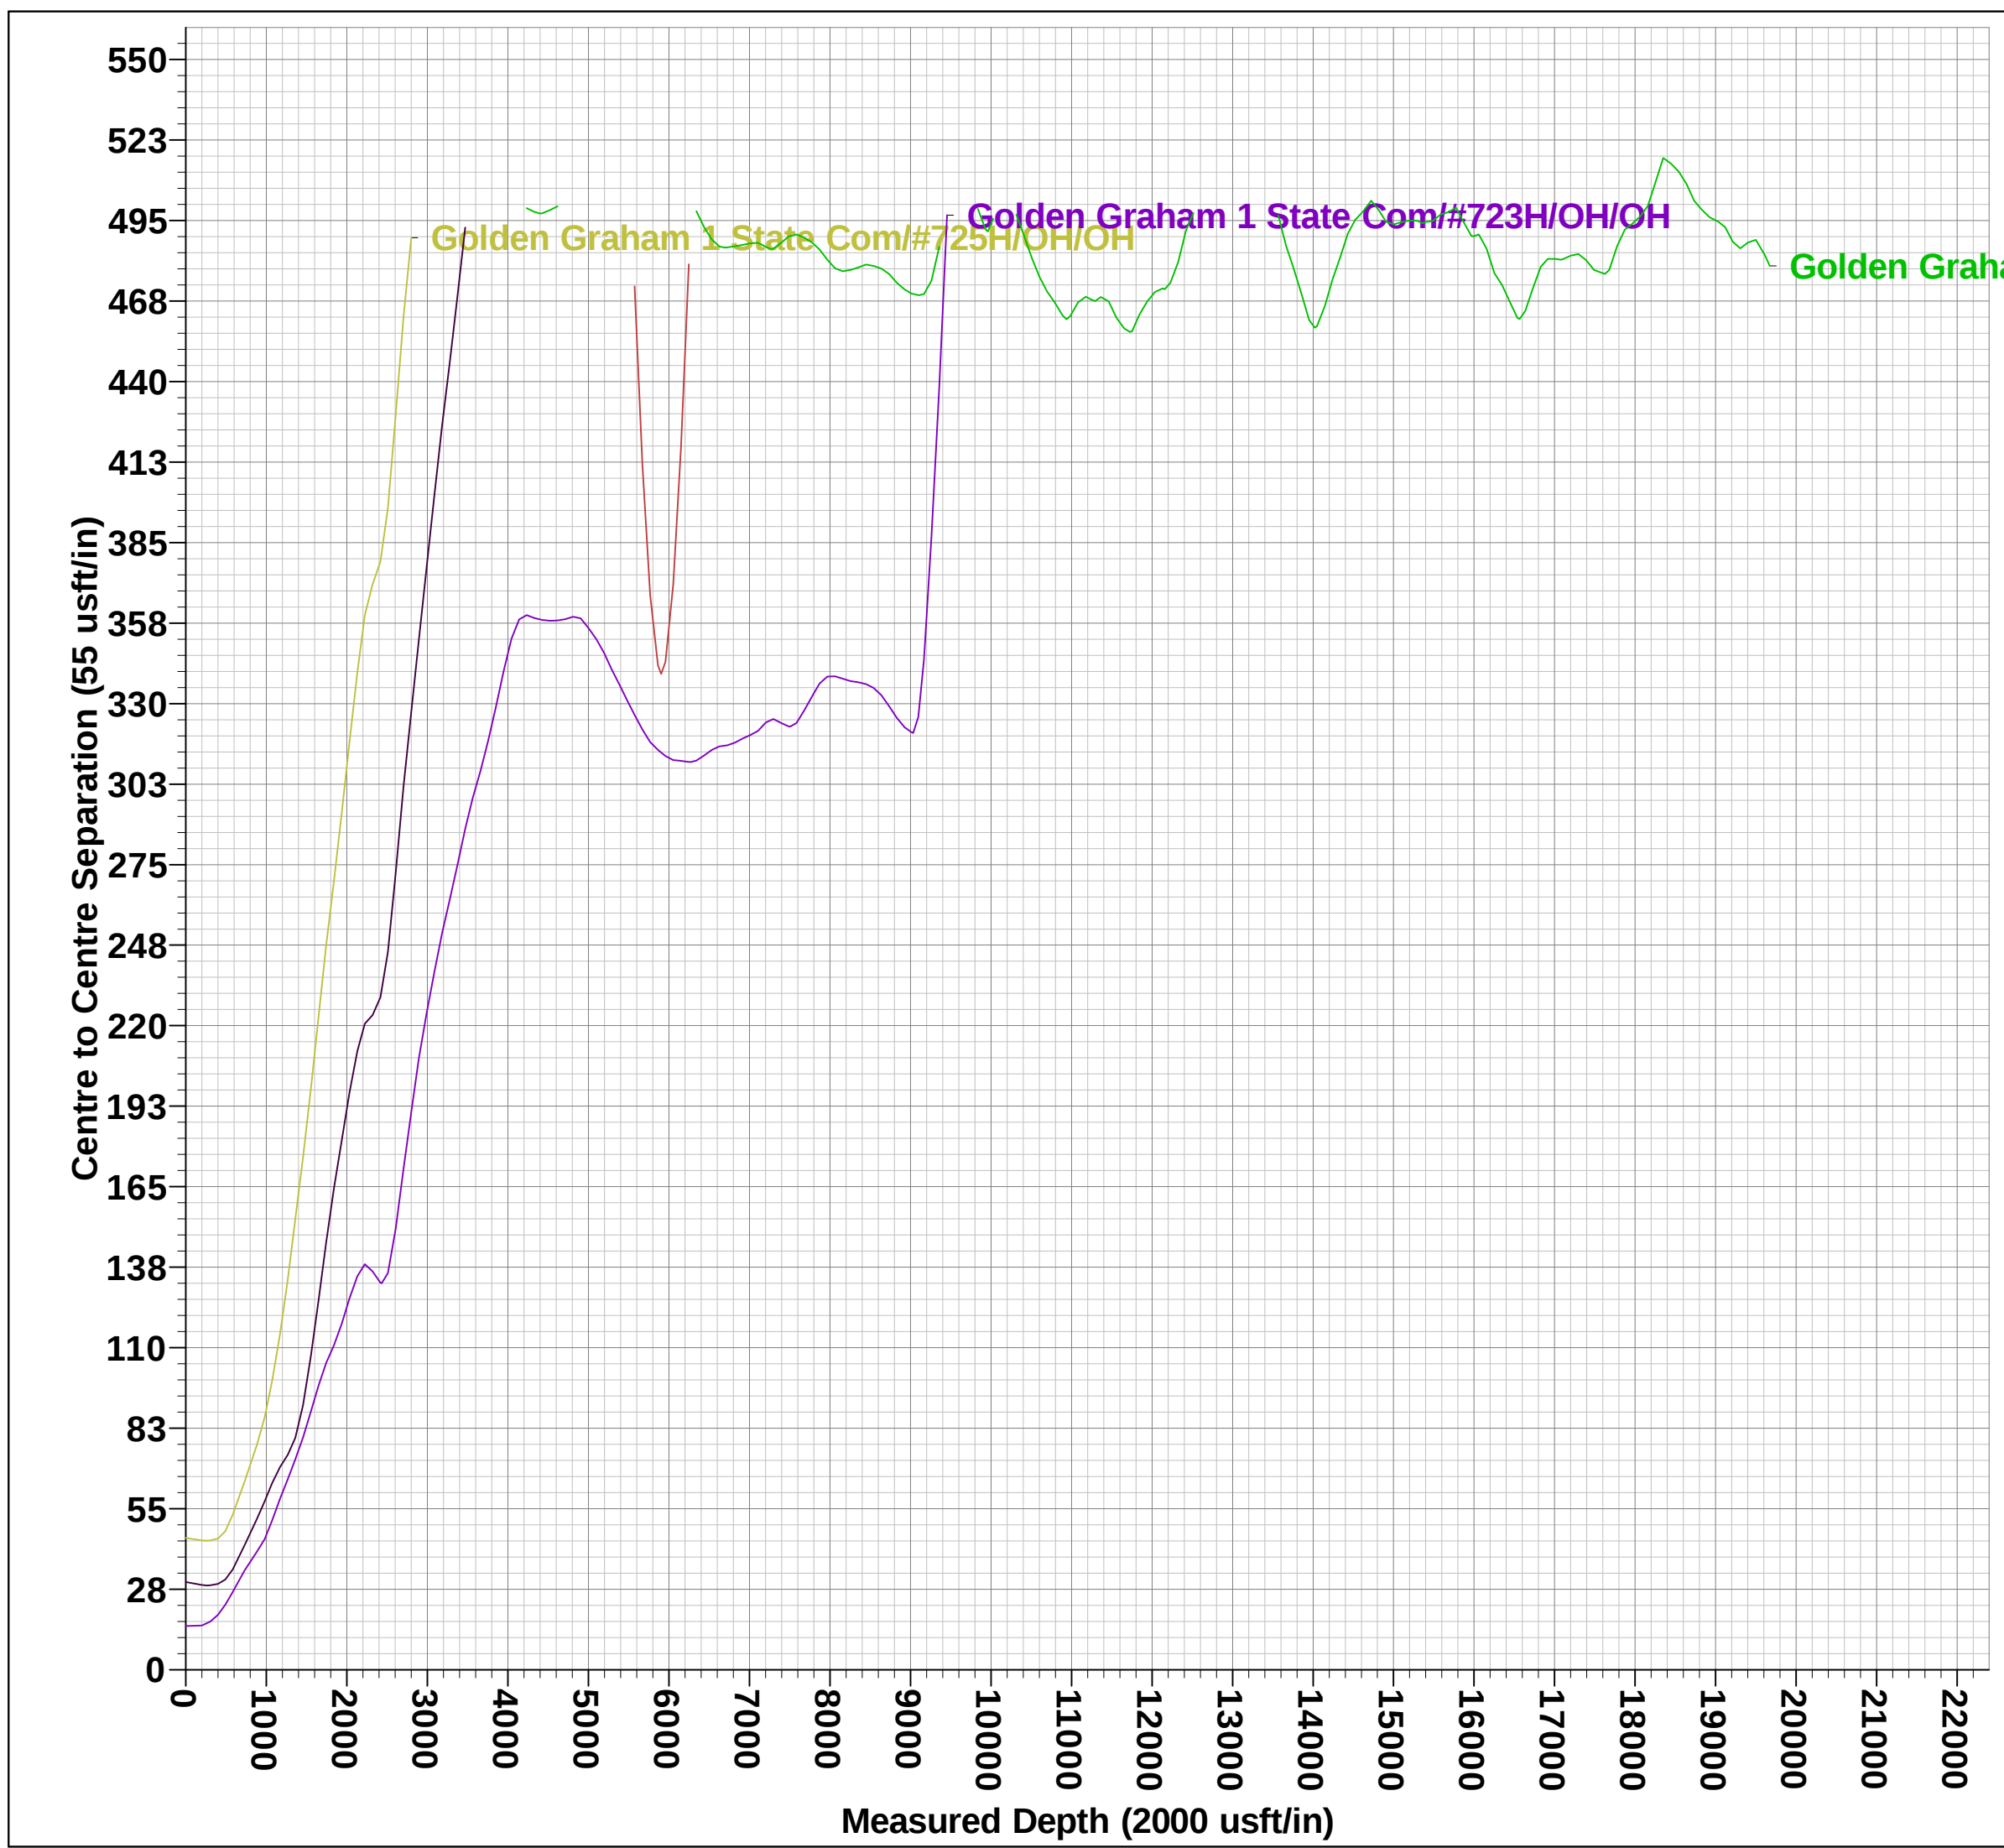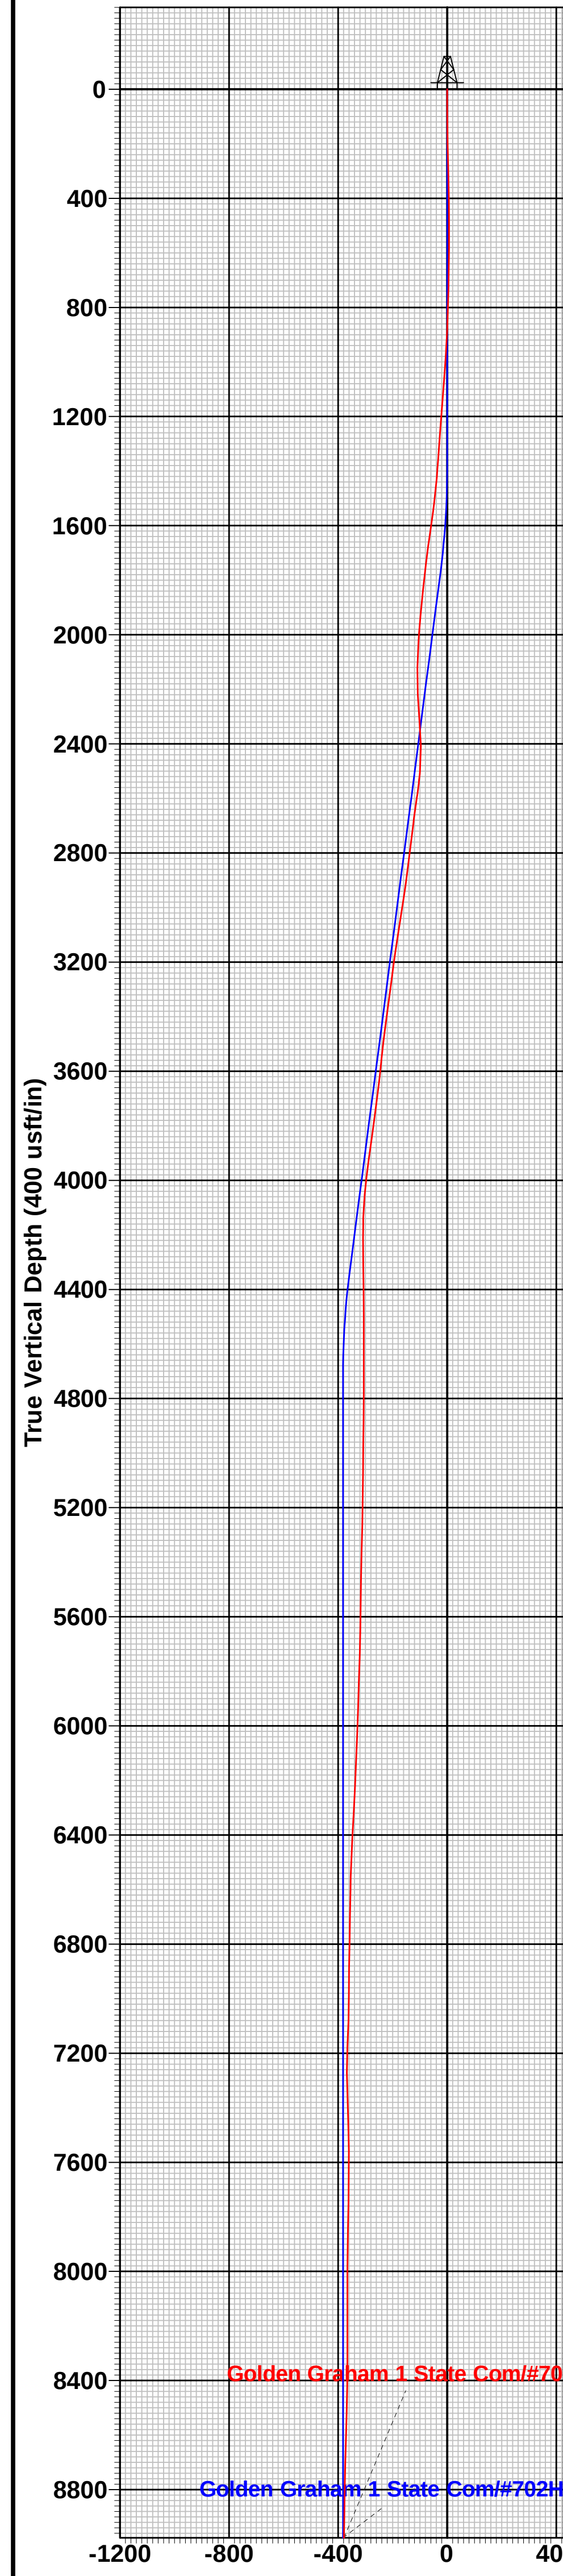



Midland

Eddy County, NM (NAD 83 NME)
Golden Graham 1 State Com
#702H
OH

Design: OH

Final PVA

22 December, 2021



Final PVA

Company:	Midland	Local Co-ordinate Reference:	Well #702H
Project:	Eddy County, NM (NAD 83 NME)	TVD Reference:	KB = 25' @ 2958.0usft (H&P 249)
Site:	Golden Graham 1 State Com	MD Reference:	KB = 25' @ 2958.0usft (H&P 249)
Well:	#702H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Project	Eddy County, NM (NAD 83 NME)		
Map System:	US State Plane 1983	System Datum:	Mean Sea Level
Geo Datum:	North American Datum 1983		
Map Zone:	New Mexico Eastern Zone		

Site	Golden Graham 1 State Com		
Site Position:		Northing:	387,494.00 usft
From:	Map	Easting:	630,031.00 usft
Position Uncertainty:	0.0 usft	Slot Radius:	13-3/16 "
		Latitude:	32° 3' 53.919 N
		Longitude:	104° 2' 49.246 W
		Grid Convergence:	0.15 °

Well		#702H				
Well Position	+N/-S	0.0 usft	Northing:	387,485.00 usft	Latitude:	32° 3' 53.801 N
	+E/-W	0.0 usft	Easting:	631,116.00 usft	Longitude:	104° 2' 36.637 W
Position Uncertainty		0.0 usft	Wellhead Elevation:	usft	Ground Level:	2,933.0 usft

Wellbore	OH				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	IGRF2020	11/15/2021	6.70	59.67	47,311.14974440

Design	OH				
Audit Notes:					
Version:	1.0	Phase:	ACTUAL	Tie On Depth:	0.0
Vertical Section:	Depth From (TVD) (usft)	+N/-S (usft)	+E/-W (usft)	Direction (°)	
	0.0	0.0	0.0	358.14	

Survey Program	Date	12/22/2021			
From (usft)	To (usft)	Survey (Wellbore)	Tool Name	Description	
200.0	19,673.0	Gordon MWD #1 (OH)	EOG MWD+IFR1	MWD + IFR1	



Final PVA

Company:	Midland	Local Co-ordinate Reference:	Well #702H
Project:	Eddy County, NM (NAD 83 NME)	TVD Reference:	KB = 25' @ 2958.0usft (H&P 249)
Site:	Golden Graham 1 State Com	MD Reference:	KB = 25' @ 2958.0usft (H&P 249)
Well:	#702H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Survey											
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)	
0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.00	0.0	0.0	
200.0	2.32	2.06	199.9	4.0	0.1	1.16	1.16	0.00	-4.0	0.0	
305.0	2.66	6.11	304.8	8.6	0.5	0.36	0.32	3.86	-8.6	0.4	
398.0	2.25	9.07	397.8	12.5	1.0	0.46	-0.44	3.18	-12.5	1.0	
491.0	2.36	336.86	490.7	16.1	0.5	1.38	0.12	-34.63	-14.6	-6.8	
584.0	2.53	327.01	583.6	19.6	-1.3	0.49	0.18	-10.59	-17.2	-9.6	
729.0	2.64	305.34	728.5	24.2	-5.8	0.67	0.08	-14.94	-18.7	-16.4	
883.0	2.99	282.93	882.3	27.2	-12.6	0.74	0.23	-14.55	-18.4	-23.7	
979.0	3.97	272.33	978.1	27.8	-18.4	1.22	1.02	-11.04	-19.5	-27.1	
1,074.0	4.90	257.92	1,072.8	27.1	-25.6	1.52	0.98	-15.17	-19.3	-31.9	
1,170.0	4.41	261.03	1,168.5	25.7	-33.3	0.57	-0.51	3.24	-28.8	-30.6	
1,266.0	4.74	264.94	1,264.2	24.8	-40.9	0.47	0.34	4.07	-38.5	-28.3	
1,361.0	4.34	277.16	1,358.9	24.9	-48.4	1.10	-0.42	12.86	-51.1	-18.7	
1,457.0	6.77	280.49	1,454.4	26.4	-57.5	2.55	2.53	3.47	-60.9	-15.8	
1,553.0	8.23	264.22	1,549.6	26.7	-69.9	2.67	1.52	-16.95	-63.0	-35.1	
1,649.0	8.24	253.12	1,644.6	24.0	-83.3	1.65	0.01	-11.56	-62.2	-48.8	
1,745.0	6.82	239.68	1,739.8	19.1	-94.8	2.35	-1.48	-14.00	-51.7	-62.6	
1,841.0	5.92	240.23	1,835.2	13.8	-104.1	0.94	-0.94	0.57	-50.7	-61.1	
1,937.0	5.30	250.23	1,930.8	9.8	-112.5	1.20	-0.65	10.42	-57.4	-51.7	
2,033.0	3.53	231.33	2,026.5	6.5	-119.0	2.36	-1.84	-19.69	-32.7	-66.1	
2,129.0	3.00	181.92	2,122.3	2.1	-121.4	2.89	-0.55	-51.47	30.1	-59.1	
2,224.0	3.18	97.60	2,217.3	-0.7	-118.9	4.37	0.19	-88.76	48.5	28.6	
2,320.0	7.07	108.95	2,312.9	-3.0	-110.7	4.17	4.05	11.82	35.8	27.5	
2,416.0	9.80	148.52	2,407.9	-11.9	-100.8	6.51	2.84	41.22	31.0	14.0	
2,511.0	10.51	182.58	2,501.5	-27.4	-97.0	6.27	0.75	35.85	23.8	9.3	
2,607.0	8.81	236.04	2,596.3	-40.3	-103.5	9.16	-1.77	55.69	21.3	-4.6	
2,703.0	7.79	268.73	2,691.3	-44.6	-116.1	4.96	-1.06	34.05	14.1	-16.4	



Final PVA

Company:	Midland	Local Co-ordinate Reference:	Well #702H
Project:	Eddy County, NM (NAD 83 NME)	TVD Reference:	KB = 25' @ 2958.0usft (H&P 249)
Site:	Golden Graham 1 State Com	MD Reference:	KB = 25' @ 2958.0usft (H&P 249)
Well:	#702H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Survey											
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)	
2,799.0	7.47	266.27	2,786.5	-45.1	-128.8	0.48	-0.33	-2.56	13.6	-20.6	
2,895.0	7.47	260.34	2,881.7	-46.6	-141.2	0.80	0.00	-6.18	15.1	-23.1	
2,990.0	8.95	242.15	2,975.7	-51.1	-153.8	3.13	1.56	-19.15	20.4	-18.7	
3,086.0	8.98	239.91	3,070.5	-58.3	-166.9	0.36	0.03	-2.33	18.5	-17.1	
3,182.0	8.36	238.06	3,165.4	-65.7	-179.3	0.71	-0.65	-1.93	16.8	-15.3	
3,278.0	7.10	235.09	3,260.6	-72.8	-190.1	1.38	-1.31	-3.09	16.9	-12.7	
3,373.0	7.91	246.62	3,354.8	-78.8	-200.9	1.80	0.85	12.14	13.9	-15.0	
3,469.0	7.66	247.27	3,449.9	-83.9	-212.9	0.28	-0.26	0.68	13.1	-15.7	
3,565.0	5.68	247.74	3,545.2	-88.2	-223.2	2.06	-2.06	0.49	14.2	-16.4	
3,661.0	6.74	245.35	3,640.7	-92.3	-232.7	1.14	1.10	-2.49	16.9	-16.1	
3,756.0	7.59	247.68	3,734.9	-97.0	-243.5	0.95	0.89	2.45	16.6	-17.2	
3,852.0	7.76	245.42	3,830.1	-102.1	-255.3	0.36	0.18	-2.35	16.8	-16.9	
3,948.0	8.06	244.13	3,925.1	-107.8	-267.3	0.36	0.31	-1.34	16.3	-16.6	
4,044.0	5.75	251.56	4,020.4	-112.2	-277.9	2.57	-2.41	7.74	14.8	-19.1	
4,140.0	2.84	247.91	4,116.2	-114.6	-284.6	3.04	-3.03	-3.80	21.2	-19.2	
4,235.0	0.63	96.87	4,211.1	-115.6	-286.3	3.58	-2.33	-158.99	-18.0	32.5	
4,331.0	0.62	91.52	4,307.1	-115.7	-285.3	0.06	-0.01	-5.57	-33.0	36.2	
4,426.0	0.81	118.31	4,402.1	-116.0	-284.2	0.40	0.20	28.20	-21.2	56.9	
4,522.0	0.88	134.37	4,498.1	-116.8	-283.0	0.26	0.07	16.73	-9.1	69.0	
4,618.0	0.83	138.66	4,594.1	-117.9	-282.0	0.08	-0.05	4.47	-7.0	74.9	
4,714.0	1.26	166.97	4,690.1	-119.4	-281.3	0.69	0.45	29.49	28.1	71.8	
4,810.0	1.35	167.12	4,786.1	-121.5	-280.9	0.09	0.09	0.16	26.1	71.8	
4,905.0	1.59	182.24	4,881.0	-123.9	-280.7	0.48	0.25	15.92	41.5	62.8	
5,001.0	1.95	169.75	4,977.0	-126.9	-280.4	0.55	0.37	-13.01	24.0	70.0	
5,096.0	2.21	166.32	5,071.9	-130.3	-279.7	0.30	0.27	-3.61	16.4	71.2	
5,192.0	2.16	174.07	5,167.8	-133.9	-279.1	0.31	-0.05	8.07	22.2	68.6	
5,288.0	2.37	184.01	5,263.8	-137.6	-279.0	0.46	0.22	10.35	29.9	64.0	



Final PVA

Company:	Midland	Local Co-ordinate Reference:	Well #702H
Project:	Eddy County, NM (NAD 83 NME)	TVD Reference:	KB = 25' @ 2958.0usft (H&P 249)
Site:	Golden Graham 1 State Com	MD Reference:	KB = 25' @ 2958.0usft (H&P 249)
Well:	#702H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Survey										
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
5,384.0	3.00	186.63	5,359.7	-142.1	-279.5	0.67	0.66	2.73	28.3	62.7
5,479.0	2.77	173.13	5,454.5	-146.9	-279.5	0.75	-0.24	-14.21	8.2	67.0
5,575.0	3.02	175.65	5,550.4	-151.7	-279.0	0.29	0.26	2.62	6.3	66.7
5,671.0	3.07	173.68	5,646.3	-156.8	-278.5	0.12	0.05	-2.05	-1.1	66.8
5,766.0	3.48	177.96	5,741.1	-162.2	-278.1	0.50	0.43	4.51	-1.5	66.8
5,862.0	2.58	199.64	5,837.0	-167.1	-278.8	1.50	-0.94	22.58	18.4	63.8
5,958.0	2.73	191.28	5,932.9	-171.4	-279.9	0.43	0.16	-8.71	4.5	65.4
6,054.0	2.49	223.49	6,028.8	-175.1	-281.8	1.53	-0.25	33.55	34.6	54.2
6,150.0	2.93	219.84	6,124.7	-178.5	-284.8	0.49	0.46	-3.80	26.6	56.2
6,246.0	2.70	211.43	6,220.6	-182.4	-287.6	0.49	-0.24	-8.76	13.4	59.1
6,341.0	3.16	258.21	6,315.5	-184.8	-291.3	2.49	0.48	49.24	48.1	32.3
6,437.0	2.94	264.25	6,411.3	-185.6	-296.3	0.41	-0.23	6.29	46.1	27.4
6,532.0	2.39	247.63	6,506.2	-186.6	-300.6	0.99	-0.58	-17.49	32.1	38.7
6,628.0	1.29	270.07	6,602.2	-187.3	-303.5	1.35	-1.15	23.37	41.5	24.3
6,724.0	0.78	260.29	6,698.2	-187.5	-305.3	0.56	-0.53	-10.19	35.0	30.8
6,820.0	1.25	229.67	6,794.1	-188.2	-306.7	0.73	0.49	-31.90	12.9	44.0
6,915.0	0.76	241.02	6,889.1	-189.2	-308.0	0.55	-0.52	11.95	19.6	40.8
7,011.0	1.25	324.24	6,985.1	-188.7	-309.2	1.44	0.51	86.69	41.7	-14.0
7,107.0	1.86	230.53	7,081.1	-188.8	-311.0	2.40	0.64	-97.61	9.8	41.5
7,203.0	2.92	248.11	7,177.0	-190.7	-314.5	1.33	1.10	18.31	17.9	37.1
7,298.0	2.71	352.97	7,271.9	-189.4	-317.0	4.70	-0.22	110.38	29.6	-24.6
7,394.0	4.01	7.37	7,367.8	-183.8	-316.9	1.60	1.35	15.00	17.0	-30.6
7,490.0	3.17	1.71	7,463.6	-177.8	-316.4	0.95	-0.87	-5.90	14.0	-29.1
7,585.0	2.30	336.11	7,558.5	-173.5	-317.1	1.56	-0.92	-26.95	20.9	-21.3
7,681.0	2.82	325.23	7,654.4	-169.8	-319.2	0.74	0.54	-11.33	20.3	-17.4
7,776.0	2.24	320.62	7,749.3	-166.4	-321.7	0.65	-0.61	-4.85	17.4	-15.9
7,872.0	2.44	303.72	7,845.2	-163.8	-324.6	0.75	0.21	-17.60	17.4	-10.7



Final PVA

Company:	Midland	Local Co-ordinate Reference:	Well #702H
Project:	Eddy County, NM (NAD 83 NME)	TVD Reference:	KB = 25' @ 2958.0usft (H&P 249)
Site:	Golden Graham 1 State Com	MD Reference:	KB = 25' @ 2958.0usft (H&P 249)
Well:	#702H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Survey										
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
7,968.0	1.92	309.99	7,941.2	-161.7	-327.5	0.60	-0.54	6.53	12.5	-12.3
8,064.0	0.86	324.91	8,037.1	-160.0	-329.2	1.16	-1.10	15.54	6.7	-14.7
8,160.0	0.60	121.53	8,133.1	-159.7	-329.1	1.49	-0.27	163.15	-11.8	11.1
8,256.0	0.38	168.61	8,229.1	-160.3	-328.7	0.46	-0.23	49.04	-0.6	16.6
8,352.0	0.22	251.70	8,325.1	-160.6	-328.8	0.43	-0.17	86.55	16.2	2.9
8,448.0	0.93	220.69	8,421.1	-161.3	-329.4	0.78	0.74	-32.30	11.4	10.7
8,543.0	1.45	217.63	8,516.1	-162.8	-330.7	0.55	0.55	-3.22	8.9	11.2
8,639.0	2.30	199.01	8,612.0	-165.6	-332.1	1.08	0.89	-19.40	1.7	13.1
8,735.0	2.29	195.91	8,708.0	-169.3	-333.2	0.13	-0.01	-3.23	-2.8	13.1
8,830.0	1.83	184.04	8,802.9	-172.6	-333.8	0.66	-0.48	-12.49	-8.8	11.8
8,926.0	1.37	200.36	8,898.9	-175.2	-334.3	0.67	-0.48	17.00	-7.8	14.2
9,013.0	1.22	203.75	8,985.8	-177.0	-335.1	0.19	-0.17	3.90	-8.9	14.7
9,096.0	1.03	201.19	9,068.8	-178.6	-335.7	0.24	-0.23	-3.08	-11.1	14.3
9,155.0	1.24	27.95	9,127.8	-178.5	-335.6	3.84	0.36	-293.62	9.3	-15.6
KOP (MD=9155.0')										
9,167.0	1.70	27.12	9,139.8	-178.2	-335.5	3.84	3.84	-6.93	9.2	-15.5
9,263.0	18.91	12.72	9,233.9	-161.6	-331.3	17.99	17.93	-15.00	6.2	-15.3
9,358.0	39.42	9.72	9,316.4	-116.4	-322.8	21.64	21.59	-3.16	-11.7	-20.9
9,454.0	49.45	4.60	9,384.9	-49.8	-314.7	11.09	10.45	-5.33	-35.6	-28.6
9,550.0	55.46	0.34	9,443.4	26.2	-311.5	7.18	6.26	-4.44	-53.4	-33.3
9,645.0	61.45	358.97	9,493.1	107.1	-312.0	6.42	6.31	-1.44	-61.2	-33.1
9,655.6	62.10	359.06	9,498.1	116.4	-312.2	6.19	6.14	0.85	-61.4	-32.9
HL Crossing, MD:9655.6', TVD:9498.1', N/S:116.4', E/W:-312.2', INC:62.10										
9,741.0	67.35	359.75	9,534.6	193.6	-313.0	6.19	6.15	0.81	-57.5	-31.6
9,836.0	73.36	359.31	9,566.5	283.0	-313.7	6.34	6.33	-0.46	-41.9	-31.1
9,932.0	75.83	359.32	9,592.0	375.6	-314.8	2.57	2.57	0.01	-18.3	-29.5
10,027.0	92.93	1.44	9,601.2	469.8	-314.2	18.14	18.00	2.23	-10.4	-29.8



Final PVA

Company:	Midland	Local Co-ordinate Reference:	Well #702H
Project:	Eddy County, NM (NAD 83 NME)	TVD Reference:	KB = 25' @ 2958.0usft (H&P 249)
Site:	Golden Graham 1 State Com	MD Reference:	KB = 25' @ 2958.0usft (H&P 249)
Well:	#702H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Survey											
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)	
10,123.0	87.63	357.53	9,600.8	565.7	-315.0	6.86	-5.52	-4.07	-12.0	-28.7	
10,219.0	87.41	356.67	9,604.9	661.5	-319.9	0.92	-0.23	-0.90	-8.9	-23.7	
10,314.0	89.51	357.20	9,607.5	756.3	-325.0	2.28	2.21	0.56	-7.4	-18.5	
10,410.0	89.51	357.06	9,608.3	852.2	-329.8	0.15	0.00	-0.15	-7.7	-13.5	
10,506.0	91.08	357.44	9,607.8	948.1	-334.4	1.68	1.64	0.40	-9.2	-8.7	
10,601.0	92.62	357.11	9,604.7	1,042.9	-338.9	1.66	1.62	-0.35	-13.4	-4.0	
10,697.0	89.17	359.21	9,603.2	1,138.8	-342.0	4.21	-3.59	2.19	-15.9	-0.8	
10,793.0	89.71	359.60	9,604.2	1,234.8	-343.0	0.69	0.56	0.41	-16.1	0.4	
10,888.0	85.42	358.24	9,608.2	1,329.7	-344.8	4.74	-4.52	-1.43	-13.1	2.3	
10,984.0	91.41	0.20	9,610.9	1,425.6	-346.1	6.56	6.24	2.04	-11.5	3.8	
11,080.0	88.05	0.64	9,611.3	1,521.6	-345.4	3.53	-3.50	0.46	-12.1	3.2	
11,176.0	88.03	359.13	9,614.6	1,617.5	-345.6	1.57	-0.02	-1.57	-9.9	3.6	
11,271.0	85.19	357.99	9,620.2	1,712.3	-347.9	3.22	-2.99	-1.20	-5.3	6.1	
11,367.0	90.24	358.99	9,624.0	1,808.2	-350.5	5.36	5.26	1.04	-2.6	8.8	
11,463.0	87.35	357.13	9,626.1	1,904.1	-353.7	3.58	-3.01	-1.94	-1.7	12.2	
11,559.0	88.17	359.04	9,629.8	2,000.0	-356.9	2.16	0.85	1.99	1.0	15.6	
11,655.0	89.99	1.33	9,631.4	2,095.9	-356.6	3.05	1.90	2.39	1.5	15.5	
11,750.0	88.53	359.26	9,632.6	2,190.9	-356.1	2.67	-1.54	-2.18	1.7	15.1	
11,846.0	89.96	2.11	9,633.9	2,286.9	-355.0	3.32	1.49	2.97	1.9	14.2	
11,942.0	88.39	0.73	9,635.2	2,382.8	-352.6	2.18	-1.64	-1.44	2.2	11.9	
12,038.0	91.69	3.67	9,635.2	2,478.7	-348.9	4.60	3.44	3.06	1.1	8.4	
12,133.0	90.04	1.83	9,633.7	2,573.6	-344.3	2.60	-1.74	-1.94	-1.4	4.0	
12,229.0	92.51	1.62	9,631.6	2,669.5	-341.5	2.58	2.57	-0.22	-4.6	1.3	
12,325.0	90.91	0.75	9,628.7	2,765.5	-339.5	1.90	-1.67	-0.91	-8.6	-0.5	
12,421.0	91.58	0.89	9,626.6	2,861.4	-338.1	0.71	0.70	0.15	-11.7	-1.7	
12,516.0	92.09	1.50	9,623.6	2,956.4	-336.1	0.84	0.54	0.64	-15.8	-3.5	
12,612.0	87.72	358.16	9,623.8	3,052.3	-336.4	5.73	-4.55	-3.48	-16.7	-3.1	



Final PVA

Company:	Midland	Local Co-ordinate Reference:	Well #702H
Project:	Eddy County, NM (NAD 83 NME)	TVD Reference:	KB = 25' @ 2958.0usft (H&P 249)
Site:	Golden Graham 1 State Com	MD Reference:	KB = 25' @ 2958.0usft (H&P 249)
Well:	#702H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Survey										
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
12,708.0	92.65	0.36	9,623.5	3,148.3	-337.6	5.62	5.14	2.29	-18.1	-1.7
12,804.0	88.17	358.75	9,622.8	3,244.3	-338.4	4.96	-4.67	-1.68	-19.9	-0.8
12,900.0	89.43	1.60	9,624.8	3,340.2	-338.1	3.25	1.31	2.97	-18.9	-0.9
12,996.0	88.72	1.96	9,626.3	3,436.2	-335.1	0.83	-0.74	0.37	-18.4	-3.7
13,091.0	85.24	358.83	9,631.3	3,531.0	-334.5	4.92	-3.66	-3.29	-14.5	-4.2
13,186.0	88.39	0.46	9,636.6	3,625.8	-335.0	3.73	3.32	1.72	-10.3	-3.5
13,282.0	87.69	359.56	9,639.9	3,721.8	-335.0	1.19	-0.73	-0.94	-8.0	-3.3
13,378.0	91.05	359.99	9,641.0	3,817.8	-335.4	3.53	3.50	0.45	-8.1	-2.8
13,474.0	90.74	359.06	9,639.5	3,913.7	-336.2	1.02	-0.32	-0.97	-10.6	-1.8
13,569.0	87.80	356.10	9,640.7	4,008.6	-340.2	4.39	-3.09	-3.12	-10.5	2.3
13,665.0	90.43	0.59	9,642.1	4,104.6	-343.0	5.42	2.74	4.68	-10.1	5.3
13,761.0	89.12	359.94	9,642.5	4,200.5	-342.5	1.52	-1.36	-0.68	-10.7	5.0
13,857.0	88.45	359.64	9,644.6	4,296.5	-342.9	0.76	-0.70	-0.31	-9.8	5.5
13,953.0	87.57	0.24	9,647.9	4,392.5	-343.0	1.11	-0.92	0.62	-7.5	5.8
14,049.0	89.31	4.05	9,650.5	4,488.3	-339.4	4.36	1.81	3.97	-6.0	2.4
14,145.0	92.17	5.34	9,649.3	4,584.0	-331.5	3.27	2.98	1.34	-8.3	-5.3
14,241.0	91.75	2.90	9,646.0	4,679.7	-324.6	2.58	-0.44	-2.54	-12.6	-12.1
14,337.0	88.28	1.16	9,646.0	4,775.6	-321.2	4.04	-3.61	-1.81	-13.7	-15.3
14,432.0	89.99	2.87	9,647.4	4,870.5	-317.9	2.55	1.80	1.80	-13.4	-18.5
14,528.0	84.77	359.48	9,651.8	4,966.4	-315.9	6.48	-5.44	-3.53	-10.0	-20.3
14,624.0	90.99	1.76	9,655.3	5,062.2	-314.9	6.90	6.48	2.37	-7.5	-21.2
14,720.0	86.06	359.42	9,657.8	5,158.2	-313.9	5.68	-5.14	-2.44	-6.1	-22.0
14,816.0	85.02	357.39	9,665.3	5,253.8	-316.6	2.37	-1.08	-2.11	0.3	-19.2
14,911.0	86.20	358.79	9,672.5	5,348.5	-319.7	1.92	1.24	1.47	6.5	-15.8
15,007.0	88.56	357.84	9,676.9	5,444.3	-322.5	2.65	2.46	-0.99	9.8	-12.8
15,103.0	90.41	358.83	9,677.8	5,540.3	-325.3	2.19	1.93	1.03	9.6	-9.9
15,199.0	89.45	357.75	9,677.9	5,636.3	-328.2	1.51	-1.00	-1.12	8.6	-6.9



Final PVA

Company:	Midland	Local Co-ordinate Reference:	Well #702H
Project:	Eddy County, NM (NAD 83 NME)	TVD Reference:	KB = 25' @ 2958.0usft (H&P 249)
Site:	Golden Graham 1 State Com	MD Reference:	KB = 25' @ 2958.0usft (H&P 249)
Well:	#702H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Survey											
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)	
15,295.0	88.22	356.73	9,679.9	5,732.1	-332.8	1.66	-1.28	-1.06	9.5	-2.1	
15,391.0	91.50	1.62	9,680.1	5,828.1	-334.2	6.13	3.42	5.09	8.7	-0.5	
15,487.0	88.39	0.79	9,680.2	5,924.0	-332.2	3.35	-3.24	-0.86	7.7	-2.4	
15,583.0	91.25	0.27	9,680.5	6,020.0	-331.3	3.03	2.98	-0.54	6.9	-3.1	
15,679.0	91.75	359.51	9,678.0	6,116.0	-331.5	0.95	0.52	-0.79	3.4	-2.8	
15,774.0	89.51	358.77	9,676.9	6,211.0	-332.9	2.48	-2.36	-0.78	1.3	-1.2	
15,870.0	87.77	357.35	9,679.2	6,306.9	-336.2	2.34	-1.81	-1.48	2.5	2.2	
15,965.0	90.66	359.09	9,680.5	6,401.8	-339.1	3.55	3.04	1.83	2.7	5.3	
16,061.0	93.88	359.62	9,676.7	6,497.7	-340.2	3.40	3.35	0.55	-2.1	6.6	
16,157.0	89.45	357.19	9,673.9	6,593.6	-342.9	5.26	-4.61	-2.53	-6.0	9.4	
16,253.0	90.01	356.35	9,674.4	6,689.4	-348.3	1.05	0.58	-0.87	-6.6	15.0	
16,348.0	89.12	0.59	9,675.1	6,784.4	-350.8	4.56	-0.94	4.46	-7.0	17.7	
16,444.0	88.05	359.55	9,677.5	6,880.4	-350.7	1.55	-1.11	-1.08	-5.7	17.7	
16,540.0	87.83	1.88	9,680.9	6,976.3	-349.5	2.44	-0.23	2.43	-2.6	16.7	
16,636.0	93.91	3.00	9,679.5	7,072.1	-345.4	6.44	6.33	1.17	-4.0	12.7	
16,732.0	92.87	1.52	9,673.8	7,167.9	-341.6	1.88	-1.08	-1.54	-9.5	9.1	
16,828.0	92.39	0.33	9,669.4	7,263.8	-340.1	1.34	-0.50	-1.24	-13.8	7.7	
16,914.0	85.64	358.92	9,670.9	7,349.7	-340.6	8.02	-7.85	-1.64	-12.3	8.4	
17,010.0	87.49	359.16	9,676.6	7,445.5	-342.2	1.94	1.93	0.25	-6.4	10.2	
17,106.0	90.04	0.42	9,678.7	7,541.5	-342.6	2.96	2.66	1.31	-4.2	10.7	
17,201.0	90.94	0.54	9,677.9	7,636.5	-341.8	0.96	0.95	0.13	-4.9	10.0	
17,297.0	90.85	359.58	9,676.4	7,732.5	-341.7	1.00	-0.09	-1.00	-6.3	10.1	
17,393.0	89.03	357.36	9,676.5	7,828.4	-344.3	2.99	-1.90	-2.31	-6.1	12.8	
17,488.0	90.13	359.16	9,677.2	7,923.4	-347.1	2.22	1.16	1.89	-5.3	15.8	
17,584.0	90.10	358.76	9,677.0	8,019.3	-348.9	0.42	-0.03	-0.42	-5.4	17.7	
17,680.0	90.74	0.85	9,676.3	8,115.3	-349.2	2.28	0.67	2.18	-6.0	18.2	
17,776.0	91.69	1.81	9,674.2	8,211.3	-347.0	1.41	0.99	1.00	-7.9	16.1	



Final PVA

Company:	Midland	Local Co-ordinate Reference:	Well #702H
Project:	Eddy County, NM (NAD 83 NME)	TVD Reference:	KB = 25' @ 2958.0usft (H&P 249)
Site:	Golden Graham 1 State Com	MD Reference:	KB = 25' @ 2958.0usft (H&P 249)
Well:	#702H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Survey											
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)	
17,872.0	92.11	1.90	9,671.0	8,307.2	-343.9	0.45	0.44	0.09	-11.0	13.1	
17,968.0	90.43	2.46	9,668.9	8,403.1	-340.2	1.84	-1.75	0.58	-13.0	9.6	
18,064.0	90.60	2.44	9,668.1	8,499.0	-336.1	0.18	0.18	-0.02	-13.8	5.7	
18,159.0	90.66	2.77	9,667.0	8,593.9	-331.8	0.35	0.06	0.35	-14.7	1.5	
18,255.0	92.28	3.05	9,664.5	8,689.7	-326.9	1.71	1.69	0.29	-17.1	-3.2	
18,350.0	90.21	1.55	9,662.5	8,784.6	-323.1	2.69	-2.18	-1.58	-19.0	-6.9	
18,447.0	88.73	0.97	9,663.4	8,881.6	-321.0	1.64	-1.53	-0.60	-18.0	-8.9	
18,542.0	89.62	1.06	9,664.7	8,976.6	-319.3	0.94	0.94	0.09	-16.5	-10.4	
18,638.0	89.76	0.62	9,665.3	9,072.6	-317.9	0.48	0.15	-0.46	-15.9	-11.7	
18,734.0	88.19	0.05	9,667.0	9,168.5	-317.3	1.74	-1.64	-0.59	-14.1	-12.1	
18,830.0	88.05	359.48	9,670.1	9,264.5	-317.7	0.61	-0.15	-0.59	-10.8	-11.6	
18,926.0	87.58	357.57	9,673.8	9,360.4	-320.2	2.05	-0.49	-1.99	-7.0	-9.0	
19,022.0	90.18	358.82	9,675.7	9,456.3	-323.2	3.00	2.71	1.30	-5.1	-5.8	
19,118.0	92.48	358.96	9,673.4	9,552.3	-325.1	2.40	2.40	0.15	-7.2	-3.8	
19,213.0	92.68	358.69	9,669.2	9,647.1	-327.0	0.35	0.21	-0.28	-11.4	-1.7	
19,309.0	93.24	358.91	9,664.2	9,743.0	-329.0	0.63	0.58	0.23	-16.2	0.5	
19,405.0	93.49	358.99	9,658.6	9,838.8	-330.8	0.27	0.26	0.08	-21.7	2.4	
19,501.0	91.16	358.39	9,654.7	9,934.7	-333.0	2.51	-2.43	-0.62	-25.5	4.7	
19,596.0	89.40	357.92	9,654.2	10,029.6	-336.0	1.92	-1.85	-0.49	-25.9	7.9	
19,608.0	89.26	357.76	9,654.4	10,041.6	-336.5	1.77	-1.17	-1.33	-25.7	8.4	
Final MWD Survey (MD=19608.0')											
19,673.0	89.26	357.76	9,655.2	10,106.6	-339.0	0.00	0.00	0.00	-24.8	11.0	
Final Projection to Bit (MD=19673.0')											



Final PVA

Company:	Midland	Local Co-ordinate Reference:	Well #702H
Project:	Eddy County, NM (NAD 83 NME)	TVD Reference:	KB = 25' @ 2958.0usft (H&P 249)
Site:	Golden Graham 1 State Com	MD Reference:	KB = 25' @ 2958.0usft (H&P 249)
Well:	#702H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Design Annotations					
Measured Depth (usft)	Vertical Depth (usft)	Local Coordinates			
		+N/-S (usft)	+E/-W (usft)	Comment	
9,155.0	9,127.8	-178.5	-335.6	KOP (MD=9155.0')	
9,655.6	9,498.1	116.4	-312.2	HL Crossing, MD:9655.6', TVD:9498.1', N/S:116.4', E/W:-312.2', INC:62.10	
19,608.0	9,654.4	10,041.6	-336.5	Final MWD Survey (MD=19608.0')	
19,673.0	9,655.2	10,106.6	-339.0	Final Projection to Bit (MD=19673.0')	

Checked By: _____	Approved By: _____	Date: _____
-------------------	--------------------	-------------

Intent ☐ As Drilled ☐

API #		
Operator Name:	Property Name:	Well Number

Kick Off Point (KOP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

First Take Point (FTP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

Last Take Point (LTP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

Is this well the defining well for the Horizontal Spacing Unit? ☐Is this well an infill well? ☐

If infill is yes please provide API if available, Operator Name and well number for Defining well for Horizontal Spacing Unit.

API #		
Operator Name:	Property Name:	Well Number

KZ 06/29/2018

Submit a Copy To Appropriate District Office
 District I – (575) 393-6161
 1625 N. French Dr., Hobbs, NM 88240
 District II – (575) 748-1283
 811 S. First St., Artesia, NM 88210
 District III – (505) 334-6178
 1000 Rio Brazos Rd., Aztec, NM 87410
 District IV – (505) 476-3460
 1220 S. St. Francis Dr., Santa Fe, NM 87505

State of New Mexico
 Energy, Minerals and Natural Resources

Form C-103
 Revised July 18, 2013

OIL CONSERVATION DIVISION
 1220 South St. Francis Dr.
 Santa Fe, NM 87505

WELL API NO. 30-015-48313
5. Indicate Type of Lease STATE ☒ FEE ☐
6. State Oil & Gas Lease No.
7. Lease Name or Unit Agreement Name GOLDEN GRAHAM 1 STATE COM
8. Well Number 702H
9. OGRID Number 7377
10. Pool name or Wildcat Purple Sage; Wolfcamp
4. Well Location Unit Letter N : 215' feet from the SOUTH line and 1784' feet from the WEST line Section 1 Township 26S Range 28E NMPM County EDDY
11. Elevation (Show whether DR, RKB, RT, GR, etc.) 2933'

12. Check Appropriate Box to Indicate Nature of Notice, Report or Other Data

NOTICE OF INTENTION TO:

PERFORM REMEDIAL WORK ☐ PLUG AND ABANDON ☐
 TEMPORARILY ABANDON ☐ CHANGE PLANS ☐
 PULL OR ALTER CASING ☐ MULTIPLE COMPL ☐
 DOWNHOLE COMMINGLE ☐
 CLOSED-LOOP SYSTEM ☐
 OTHER: ☐

SUBSEQUENT REPORT OF:

REMEDIAL WORK ☐ ALTERING CASING ☐
 COMMENCE DRILLING OPNS. ☐ P AND A ☐
 CASING/CEMENT JOB ☐
 OTHER: COMPLETION ☒

13. Describe proposed or completed operations. (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work). SEE RULE 19.15.7.14 NMAC. For Multiple Completions: Attach wellbore diagram of proposed completion or recompletion.

TOC IS BELOW THE CASING SHOE, ON 5/15/2023 A SUBSEQUENT PRESSURE TEST HELD.
 EOG IS REQUESTING NO REMEDIAL CEMENT AT THIS TIME.

Spud Date:

07/14/2021

Rig Release Date:

12/14/2021

I hereby certify that the information above is true and complete to the best of my knowledge and belief.

SIGNATURE Kristina Agee TITLE REGULATORY SPECIALIST DATE 5/24/2023

Type or print name Kristina Agee E-mail address: kristina_agee@eogresources.com PHONE: (432)686-6996

For State Use Only

APPROVED BY: _____ TITLE _____ DATE _____

Conditions of Approval (if any):



Detailed Job Breakdown



JOB REPORT

COMPANY DETAILS

Company: EOG
Contact: MARK POPE
PHONE:


Email: Mark_pope@eogresources.com

JOB DETAILS

DATE 5/15/2023 5:21:10PM
START TIME 5/15/2023 5:21:10PM
END TIME 5/15/2023 5:54:14PM
Ticket#:
Other:
Other:

Operator:
WELL: GOLDEN GRAHAM 1
Licence #: STATE COM 702H
Contractor:
AFE:

Comments:

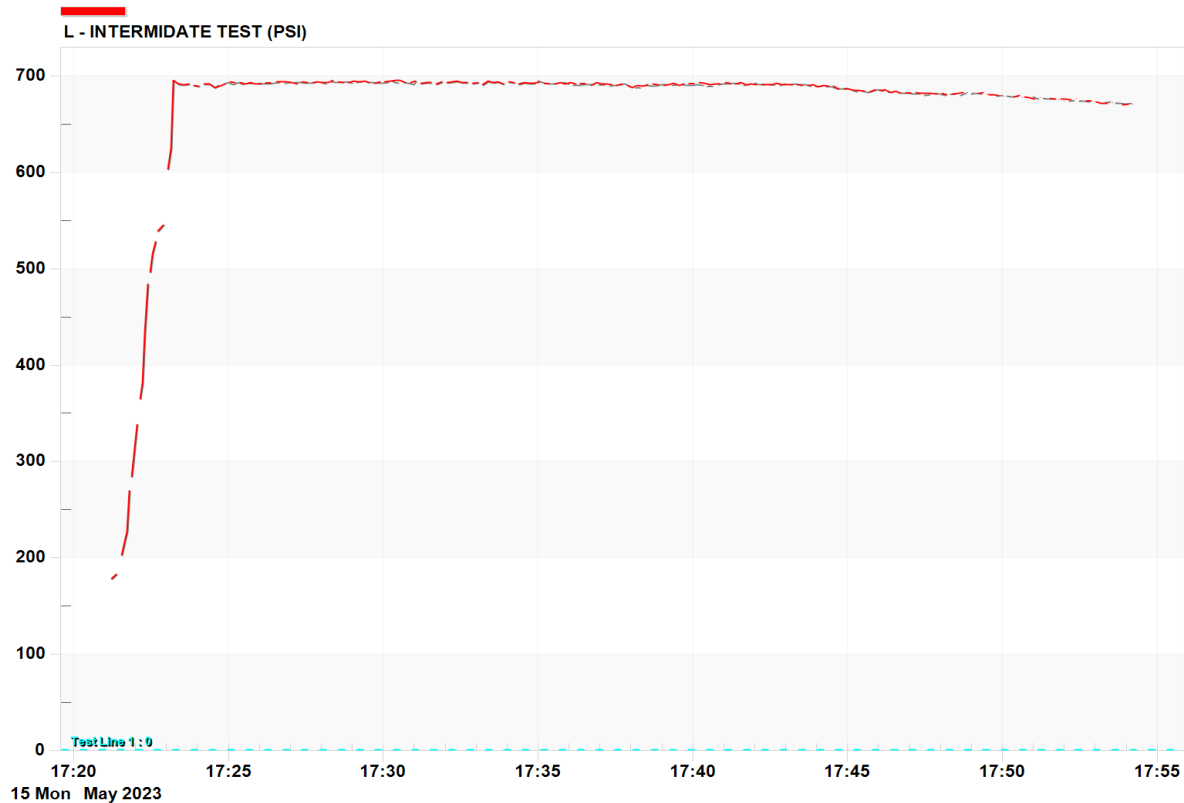

17:21:07

Detailed Job Breakdown

May/15/2023

INTERMEDIATE TEST (PSI)								
Time								
17:21	7.972	178						
17:21	12.972	178						
17:21	17.973	180						
17:21	22.972	183						
17:21	27.972	185						
17:21	32.973	203						
17:21	37.973	203						
17:21	42.972	228						
17:21	47.972	269						
17:21	52.973	285						
17:21	57.972	286						
17:22	2.972	338						
17:22	7.973	365						
17:22	12.973	381						
17:22	17.972	434						
17:22	22.972	484						
17:22	27.973	497						
17:22	32.972	515						
17:22	37.972	528						
17:22	42.973	539						
17:22	47.973	538						
17:22	52.972	546						
17:22	57.972	543						
17:23	2.973	604						
17:23	7.972	625						
17:23	12.972	696						
17:23	17.973	693						
17:23	22.973	692						
17:23	27.972	690						
17:23	32.972	691						
17:23	37.973	690						
17:23	42.972	692						
17:23	47.972	691						
17:23	52.973	691						
17:23	57.973	691						
17:24	2.972	690						
17:24	7.972	692						
17:24	12.973	692						
17:24	17.972	691						
17:24	22.972	692						
17:24	27.973	692						
17:24	32.973	688						
17:24	37.972	692						
17:24	42.972	690						
17:24	47.973	692						
17:24	52.972	692						
17:24	57.972	695						
17:25	2.973	694						

17:25:07

Detailed Job Breakdown

May/15/2023

INTERMEDIATE TEST (PSI)								
Time								
17:25	7.973	692						
17:25	12.972	693						
17:25	17.972	694						
17:25	22.973	694						
17:25	27.972	692						
17:25	32.972	692						
17:25	37.973	693						
17:25	42.973	693						
17:25	47.972	693						
17:25	52.972	692						
17:25	57.973	693						
17:26	2.972	692						
17:26	7.972	693						
17:26	12.973	693						
17:26	17.973	693						
17:26	22.972	693						
17:26	27.972	694						
17:26	32.973	694						
17:26	37.972	695						
17:26	42.972	694						
17:26	47.973	694						
17:26	52.973	694						
17:26	57.972	694						
17:27	2.972	694						
17:27	7.973	695						
17:27	12.972	692						
17:27	17.972	695						
17:27	22.973	694						
17:27	27.973	694						
17:27	32.972	694						
17:27	37.972	694						
17:27	42.973	694						
17:27	47.972	694						
17:27	52.972	694						
17:27	57.973	694						
17:28	2.973	694						
17:28	7.972	693						
17:28	12.972	694						
17:28	17.973	695						
17:28	22.972	696						
17:28	27.972	694						
17:28	32.973	694						
17:28	37.973	694						
17:28	42.972	694						
17:28	47.972	695						
17:28	52.973	694						
17:28	57.972	693						
17:29	2.972	695						

17:29:07

Detailed Job Breakdown

May/15/2023

INTERMEDIATE TEST (PSI)									
Time									
17:29	7.973	694							
17:29	12.973	695							
17:29	17.972	695							
17:29	22.972	695							
17:29	27.973	694							
17:29	32.972	693							
17:29	37.972	694							
17:29	42.973	693							
17:29	47.973	694							
17:29	52.972	694							
17:29	57.972	693							
17:30	2.973	695							
17:30	7.972	694							
17:30	12.972	695							
17:30	17.974	695							
17:30	22.973	696							
17:30	27.972	694							
17:30	32.972	696							
17:30	37.973	694							
17:30	42.972	693							
17:30	47.972	693							
17:30	52.973	693							
17:30	57.973	692							
17:31	2.972	695							
17:31	7.972	693							
17:31	12.973	693							
17:31	17.972	694							
17:31	22.972	694							
17:31	27.973	694							
17:31	32.973	694							
17:31	37.972	691							
17:31	42.972	692							
17:31	47.973	692							
17:31	52.972	694							
17:31	57.972	694							
17:32	2.973	693							
17:32	7.973	695							
17:32	12.972	695							
17:32	17.973	693							
17:32	22.973	695							
17:32	27.972	693							
17:32	32.972	694							
17:32	37.973	694							
17:32	42.973	694							
17:32	47.972	693							
17:32	52.973	693							
17:32	57.973	693							
17:33	2.972	693							

INTERMEDIATE TEST (PSI)									
Time									
17:33	7.972	693							
17:33	12.973	691							
17:33	17.973	694							
17:33	22.972	695							
17:33	27.973	694							
17:33	32.973	694							
17:33	37.972	694							
17:33	42.972	694							
17:33	47.973	694							
17:33	52.973	692							
17:33	57.972	693							
17:34	2.973	694							
17:34	7.973	694							
17:34	12.972	694							
17:34	17.972	694							
17:34	22.973	692							
17:34	27.973	692							
17:34	32.972	694							
17:34	37.973	694							
17:34	42.973	693							
17:34	47.972	694							
17:34	52.972	693							
17:34	57.973	696							
17:35	2.973	694							
17:35	7.972	694							
17:35	12.973	692							
17:35	17.973	693							
17:35	22.972	692							
17:35	27.972	693							
17:35	32.973	692							
17:35	37.973	693							
17:35	42.972	694							
17:35	47.973	694							
17:35	52.973	692							
17:35	57.972	693							
17:36	2.972	694							
17:36	7.973	691							
17:36	12.973	692							
17:36	17.972	691							
17:36	22.973	692							
17:36	27.973	692							
17:36	32.972	692							
17:36	37.972	692							
17:36	42.973	691							
17:36	47.973	692							
17:36	52.972	693							
17:36	57.973	692							
17:37	2.973	692							

17:37:07

Detailed Job Breakdown

May/15/2023

INTERMIDAT E TEST (PSI)								
Time								
17:37	7.972	692						
17:37	12.972	692						
17:37	17.973	691						
17:37	22.973	691						
17:37	27.972	692						
17:37	32.973	690						
17:37	37.973	692						
17:37	42.972	692						
17:37	47.972	693						
17:37	52.973	690						
17:37	57.973	690						
17:38	2.972	689						
17:38	7.973	689						
17:38	12.973	691						
17:38	17.972	688						
17:38	22.972	690						
17:38	27.973	692						
17:38	32.973	692						
17:38	37.972	691						
17:38	42.973	692						
17:38	47.973	691						
17:38	52.972	692						
17:38	57.972	692						
17:39	2.973	691						
17:39	7.973	692						
17:39	12.972	692						
17:39	17.973	692						
17:39	22.973	693						
17:39	27.972	692						
17:39	32.972	691						
17:39	37.973	692						
17:39	42.973	692						
17:39	47.972	691						
17:39	52.973	692						
17:39	57.973	691						
17:40	2.972	692						
17:40	7.972	692						
17:40	12.973	694						
17:40	17.973	692						
17:40	22.972	693						
17:40	27.973	690						
17:40	32.973	691						
17:40	37.972	690						
17:40	42.972	692						
17:40	47.973	692						
17:40	52.973	692						
17:40	57.972	693						
17:41	2.973	693						

17:41:07

Detailed Job Breakdown

May/15/2023

INTERMEDIATE TEST (PSI)								
Time								
17:41	7.973	693						
17:41	12.972	693						
17:41	17.972	693						
17:41	22.973	692						
17:41	27.973	693						
17:41	32.972	693						
17:41	37.973	692						
17:41	42.973	691						
17:41	47.972	692						
17:41	52.972	692						
17:41	57.973	693						
17:42	2.973	692						
17:42	7.972	692						
17:42	12.973	691						
17:42	17.973	692						
17:42	22.972	692						
17:42	27.973	691						
17:42	32.973	692						
17:42	37.973	691						
17:42	42.972	693						
17:42	47.973	692						
17:42	52.973	691						
17:42	57.972	693						
17:43	2.972	691						
17:43	7.973	692						
17:43	12.973	692						
17:43	17.972	693						
17:43	22.973	692						
17:43	27.973	692						
17:43	32.972	690						
17:43	37.972	692						
17:43	42.973	690						
17:43	47.973	691						
17:43	52.972	692						
17:43	57.973	690						
17:44	2.973	689						
17:44	7.972	690						
17:44	12.972	691						
17:44	17.973	690						
17:44	22.973	690						
17:44	27.972	690						
17:44	32.973	690						
17:44	37.973	688						
17:44	42.972	687						
17:44	47.972	688						
17:44	52.973	687						
17:44	57.973	688						
17:45	2.972	687						

17:45:07

Detailed Job Breakdown

May/15/2023

INTERMIDATE TEST (PSI)									
Time									
17:45	7.973	686							
17:45	12.973	685							
17:45	17.972	685							
17:45	22.972	685							
17:45	27.973	686							
17:45	32.973	685							
17:45	37.972	684							
17:45	42.973	684							
17:45	47.973	685							
17:45	52.972	686							
17:45	57.972	687							
17:46	2.973	686							
17:46	7.973	685							
17:46	12.972	686							
17:46	17.973	684							
17:46	22.973	683							
17:46	27.972	684							
17:46	32.972	685							
17:46	37.973	684							
17:46	42.973	682							
17:46	47.972	683							
17:46	52.973	682							
17:46	57.973	683							
17:47	2.972	683							
17:47	7.972	683							
17:47	12.973	683							
17:47	17.973	682							
17:47	22.972	682							
17:47	27.973	681							
17:47	32.973	682							
17:47	37.972	682							
17:47	42.972	683							
17:47	47.973	683							
17:47	52.973	682							
17:47	57.972	682							
17:48	2.973	682							
17:48	7.973	681							
17:48	12.972	681							
17:48	17.972	682							
17:48	22.973	682							
17:48	27.973	682							
17:48	32.972	682							
17:48	37.973	681							
17:48	42.973	683							
17:48	47.972	683							
17:48	52.972	683							
17:48	57.973	682							
17:49	2.973	683							

17:49:07

Detailed Job Breakdown

May/15/2023

INTERMEDIATE TEST (PSI)									
Time									
17:49	7.972	683							
17:49	12.973	682							
17:49	17.973	682							
17:49	22.972	683							
17:49	27.972	683							
17:49	32.973	681							
17:49	37.973	681							
17:49	42.972	681							
17:49	47.973	680							
17:49	52.973	680							
17:49	57.972	681							
17:50	2.972	679							
17:50	7.973	680							
17:50	12.973	680							
17:50	17.972	679							
17:50	22.973	679							
17:50	27.973	680							
17:50	32.972	680							
17:50	37.972	678							
17:50	42.973	679							
17:50	47.973	679							
17:50	52.972	678							
17:50	57.973	680							
17:51	2.973	676							
17:51	7.972	677							
17:51	12.972	678							
17:51	17.973	678							
17:51	22.973	677							
17:51	27.972	678							
17:51	32.973	678							
17:51	37.973	678							
17:51	42.972	676							
17:51	47.972	676							
17:51	52.973	676							
17:51	57.973	675							
17:52	2.972	677							
17:52	7.973	675							
17:52	12.973	676							
17:52	17.972	675							
17:52	22.972	677							
17:52	27.973	675							
17:52	32.973	675							
17:52	37.972	675							
17:52	42.973	674							
17:52	47.973	674							
17:52	52.972	674							
17:52	57.972	674							
17:53	2.973	673							

17:53:07

Detailed Job Breakdown

May/15/2023

INTERMEDIATE TEST (PSI)									
Time									
17:53	7.973	673							
17:53	12.972	672							
17:53	17.973	673							
17:53	22.973	672							
17:53	27.972	674							
17:53	32.972	673							
17:53	37.973	673							
17:53	42.973	673							
17:53	47.972	673							
17:53	52.973	671							
17:53	57.973	672							
17:54	2.972	671							
17:54	7.972	673							
17:54	12.973	671							

Well Name:	Golden Gram 1 State Com #702H
Property Number:	76103
API Number:	30015483130000
Opening Intermediate PSI:	180
Bled Intermediate PSI down to:	N/A
Fluid back to surface:	Yes OBM
Bbls pumped to load casing:	N/A
Bbls pumped to reach 500 psi:	1.25 bbls
Bbls bled back after test:	1 bbls
Start	694 psi
30 min	670 psi
Bleed down, SICP:	175 psi

Submit To Appropriate District Office Two Copies District I 1625 N. French Dr., Hobbs, NM 88240 District II 811 S. First St., Artesia, NM 88210 District III 1000 Rio Brazos Rd., Aztec, NM 87410 District IV 1220 S. St. Francis Dr., Santa Fe, NM 87505		State of New Mexico Energy, Minerals and Natural Resources Oil Conservation Division 1220 South St. Francis Dr. Santa Fe, NM 87505		Form C-105 Revised August 1, 2011						
1. WELL API NO.		30-015-48313								
2. Type of Lease ☒ STATE ☐ FEE ☐ FED/INDIAN										
3. State Oil & Gas Lease No.										
WELL COMPLETION OR RECOMPLETION REPORT AND LOG										
4. Reason for filing: ☒ COMPLETION REPORT (Fill in boxes #1 through #31 for State and Fee wells only) ☐ C-144 CLOSURE ATTACHMENT (Fill in boxes #1 through #9, #15 Date Rig Released and #32 and/or #33; attach this and the plat to the C-144 closure report in accordance with 19.15.17.13.K NMAC)				5. Lease Name or Unit Agreement Name GOLDEN GRAHAM 1 STATE COM						
				6. Well Number: 702H						
7. Type of Completion: ☒ NEW WELL ☐ WORKOVER ☐ DEEPENING ☐ PLUGBACK ☐ DIFFERENT RESERVOIR ☐ OTHER										
8. Name of Operator EOG RESOURCES INC				9. OGRID 7377						
10. Address of Operator PO BOX 2267 MIDLAND, TEXAS 79702				11. Pool name or Wildcat Purple Sage; Wolfcamp						
12. Location	Unit Ltr	Section	Township	Range	Lot	Feet from the	N/S Line	Feet from the	E/W Line	County
Surface:	N	1	26S	28E		215'	SOUTH	1784'	WEST	EDDY
BH:	C	36	25S	28E		342'	NORTH	1429'	WEST	EDDY
13. Date Spudded 07/14/2021	14. Date T.D. Reached 12/21/2021	15. Date Rig Released 12/24/2021		16. Date Completed (Ready to Produce) 7/8/2022		17. Elevations (DF and RKB, RT, GR, etc.) 2933GL				
18. Total Measured Depth of Well MD 19,673' TVD 9,655'		19. Plug Back Measured Depth MD 19,649' TVD 9,655'		20. Was Directional Survey Made? YES		21. Type Electric and Other Logs Run None				
22. Producing Interval(s), of this completion - Top, Bottom, Name WOLFCAMP - 9,900'-19,649'										
23. CASING RECORD (Report all strings set in well)										
CASING SIZE		WEIGHT LB./FT.		DEPTH SET		HOLE SIZE		CEMENTING RECORD		AMOUNT PULLED
9 5/8"		36# J-55		784'		12 1/4"		425 CL C/CIRC		
7 5/8"		29.7# ICP 110		9,053'		8 3/4"		1396 C/CIRC TOC @ SURFACE		
5 1/2"		20# HCP 110		19,657'		6 3/4"		965 CL H/CIRC TOC @ 9144' PRESSURE TEST ATTACHED		
24. LINER RECORD						25. TUBING RECORD				
SIZE	TOP	BOTTOM	SACKS CEMENT	SCREEN	SIZE	DEPTH SET	PACKER SET			
26. Perforation record (interval, size, and number) 9,900'-19,649' 3 1/8", 1956 holes					27. ACID, SHOT, FRACTURE, CEMENT, SQUEEZE, ETC. DEPTH INTERVAL AMOUNT AND KIND MATERIAL USED 9,900'-19,649' FRAC W/23,413,070 lbs proppant, 346,957 bbls load fld					
28. PRODUCTION										
Date First Production 7/8/2022		Production Method (Flowing, gas lift, pumping - Size and type pump) Flowing				Well Status (Prod. or Shut-in) Producing				
Date of Test 7/11/2022	Hours Tested 24	Choke Size 60	Prod'n For Test Period	Oil - Bbl 1120	Gas - MCF 4024	Water - Bbl. 5170	Gas - Oil Ratio 3592			
Flow Tubing Press.	Casing Pressure 960	Calculated 24-Hour Rate	Oil - Bbl.	Gas - MCF	Water - Bbl.	Oil Gravity - API - (Corr.) 44				
29. Disposition of Gas (Sold, used for fuel, vented, etc.) SOLD							30. Test Witnessed By			
31. List Attachments C-102, C-104, C-103, Directional Survey, H spacing,										
32. If a temporary pit was used at the well, attach a plat with the location of the temporary pit.										
33. If an on-site burial was used at the well, report the exact location of the on-site burial: Latitude _____ Longitude _____ NAD 1927 1983										
I hereby certify that the information shown on both sides of this form is true and complete to the best of my knowledge and belief										
Signature Kristina Agee		Printed Name Kristina Agee		Title REGULATORY SPECIALIST			Date 5/24/2023			
E-mail Address kristina_agee@eogresources.com										

This form is to be filed with the appropriate District Office of the Division not later than 20 days after the completion of any newly-drilled or deepened well and not later than 60 days after completion of closure. When submitted as a completion report, this shall be accompanied by one copy of all electrical and radio-activity logs run on the well and a summary of all special tests conducted, including drill stem tests. All depths reported shall be measured depths. In the case of directionally drilled wells, true vertical depths shall also be reported. For multiple completions, items 11, 12 and 26-31 shall be reported for each zone.

Southeastern New Mexico			Northwestern New Mexico				
T. Anhy	Rustler	499'	T. Canyon	Brushy	4,824'	T. Ojo Alamo	T. Penn A"
T. Salt		917'	T. Strawn			T. Kirtland	T. Penn. "B"
B. Salt			T. Atoka			T. Fruitland	T. Penn. "C"
T. Yates			T. Miss			T. Pictured Cliffs	T. Penn. "D"
T. 7 Rivers			T. Devonian			T. Cliff House	T. Leadville
T. Queen			T. Silurian			T. Menefee	T. Madison
T. Grayburg			T. Montoya			T. Point Lookout	T. Elbert
T. San Andres			T. Simpson			T. Mancos	T. McCracken
T. Glorieta			T. McKee			T. Gallup	T. Ignacio Otzte
T. Paddock			T. Ellenburger			Base Greenhorn	T. Granite
T. Blinebry			T. Gr. Wash			T. Dakota	
T. Tubb			T. Delaware Sand			T. Morrison	
T. Drinkard			T. Bone Springs			T. Todilto	
T. Abo			T. 1st BS Sand	7,332'		T. Entrada	
T. Wolfcamp	9,506'		T. 2nd BS Sand	7,994'		T. Wingate	
T. Penn			T.			T. Chinle	
T. Cisco (Bough C)			T.			T. Permian	

No. 1, from.....to.....

No. 2, from.....to.....

No. 3, from.....to.....

No. 4, from.....to.....

Include data on rate of water inflow and elevation to which water rose in hole.

No. 1, from.....to.....feet.....
 No. 2, from.....to.....feet.....
 No. 3, from.....to.....feet.....

From	To	Thickness In Feet	Lithology

District I
1625 N. French Dr., Hobbs, NM 88240
Phone:(575) 393-6161 Fax:(575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone:(575) 748-1283 Fax:(575) 748-9720
District III
1000 Rio Brazos Rd., Aztec, NM 87410
Phone:(505) 334-6178 Fax:(505) 334-6170
District IV
1220 S. St Francis Dr., Santa Fe, NM 87505
Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

ACKNOWLEDGMENTS

Action 318480

ACKNOWLEDGMENTS

Operator: EOG RESOURCES INC 5509 Champions Drive Midland, TX 79706	OGRID: 7377
	Action Number: 318480
	Action Type: [C-104] Completion Packet (C-104C)

ACKNOWLEDGMENTS

☒	I hereby certify that the required Water Use Report has been, or will be, submitted for this wells completion.
☒	I hereby certify that the required FracFocus disclosure has been, or will be, submitted for this wells completion.

District I
1625 N. French Dr., Hobbs, NM 88240
Phone:(575) 393-6161 Fax:(575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone:(575) 748-1283 Fax:(575) 748-9720
District III
1000 Rio Brazos Rd., Aztec, NM 87410
Phone:(505) 334-6178 Fax:(505) 334-6170
District IV
1220 S. St Francis Dr., Santa Fe, NM 87505
Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 318480

CONDITIONS

Operator: EOG RESOURCES INC 5509 Champions Drive Midland, TX 79706	OGRID: 7377
	Action Number: 318480
	Action Type: [C-104] Completion Packet (C-104C)

CONDITIONS

Created By	Condition	Condition Date
smcgrath	None	2/28/2024
