

Form 3160-3
(June 2015)FORM APPROVED
OMB No. 1004-0137
Expires: January 31, 2018

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
APPLICATION FOR PERMIT TO DRILL OR REENTER

1a. Type of work: ☐ DRILL ☐ REENTER 1b. Type of Well: ☐ Oil Well ☐ Gas Well ☐ Other 1c. Type of Completion: ☐ Hydraulic Fracturing ☐ Single Zone ☐ Multiple Zone		5. Lease Serial No. 6. If Indian, Allottee or Tribe Name 7. If Unit or CA Agreement, Name and No. 8. Lease Name and Well No.
2. Name of Operator		9. API Well No. 30-025-54628
3a. Address	3b. Phone No. (include area code)	10. Field and Pool, or Exploratory
4. Location of Well (Report location clearly and in accordance with any State requirements. *) At surface At proposed prod. zone		11. Sec., T. R. M. or Blk. and Survey or Area
14. Distance in miles and direction from nearest town or post office*		12. County or Parish
13. State		
15. Distance from proposed* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any)	16. No of acres in lease	17. Spacing Unit dedicated to this well
18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft.	19. Proposed Depth	20. BLM/BIA Bond No. in file
21. Elevations (Show whether DF, KDB, RT, GL, etc.)	22. Approximate date work will start*	23. Estimated duration
24. Attachments		

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, and the Hydraulic Fracturing rule per 43 CFR 3162.3-3 (as applicable)

- | | |
|---|---|
| 1. Well plat certified by a registered surveyor.
2. A Drilling Plan.
3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office). | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).
5. Operator certification.
6. Such other site specific information and/or plans as may be requested by the BLM. |
|---|---|

25. Signature	Name (Printed/Typed)	Date
Title		
Approved by (Signature)	Name (Printed/Typed)	Date
Title		
Office		

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
 Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Continued on page 2)

*(Instructions on page 2)



Additional Operator Remarks

Location of Well

0. SHL: SESE / 480 FSL / 1155 FEL / TWSP: 20S / RANGE: 33E / SECTION: 15 / LAT: 32.567215 / LONG: -103.646265 (TVD: 0 feet, MD: 0 feet)
PPP: NENE / 100 FNL / 330 FEL / TWSP: 20S / RANGE: 33E / SECTION: 22 / LAT: 32.565626 / LONG: -103.643588 (TVD: 10395 feet, MD: 10550 feet)
PPP: SENE / 1321 FNL / 330 FEL / TWSP: 20S / RANGE: 33E / SECTION: 22 / LAT: 32.562272 / LONG: -103.643586 (TVD: 10514 feet, MD: 11771 feet)
PPP: SESE / 1329 FSL / 330 FEL / TWSP: 20S / RANGE: 33E / SECTION: 27 / LAT: 32.540493 / LONG: -103.643574 (TVD: 10575 feet, MD: 19690 feet)
PPP: NENE / 1 FNL / 330 FEL / TWSP: 20S / RANGE: 33E / SECTION: 27 / LAT: 32.551385 / LONG: -103.64358 (TVD: 10575 feet, MD: 15730 feet)
PPP: NENE / 1 FNL / 330 FEL / TWSP: 20S / RANGE: 33E / SECTION: 34 / LAT: 32.536864 / LONG: -103.643573 (TVD: 10575 feet, MD: 21010 feet)
BHL: SESE / 50 FSL / 330 FEL / TWSP: 20S / RANGE: 33E / SECTION: 34 / LAT: 32.522619 / LONG: -103.643565 (TVD: 10575 feet, MD: 26090 feet)

BLM Point of Contact

Name: JANET D ESTES
Title: ADJUDICATOR
Phone: (575) 234-6233
Email: JESTES@BLM.GOV

C-102 Submit Electronically Via OCD Permitting	State of New Mexico Energy, Minerals & Natural Resources Department OIL CONSERVATION DIVISION	Revised July 9, 2024	
		Submittal Type:	☒ Initial Submittal
			☐ Amended Report
			☐ As Drilled

WELL LOCATION INFORMATION

API Number 30-025-54628	Pool Code 58960	Pool Name Teas; Bone Spring
Property Code 337204	Property Name DONKEY POTROAST FEDERAL COM	Well Number 504H
OGRID No. 229137	Operator Name COG OPERATING LLC	Ground Level Elevation 3590.4'
Surface Owner: ☐ State ☐ Fee ☐ Tribal ☒ Federal		Mineral Owner: ☐ State ☐ Fee ☐ Tribal ☒ Federal

Surface Location

UL	Section	Township	Range	Lot	Ft. from N/S	Ft. from E/W	Latitude	Longitude	County
P	15	20-S	33-E		480 FSL	1155 FEL	32.567215°N	103.646265°W	LEA

Bottom Hole Location

UL	Section	Township	Range	Lot	Ft. from N/S	Ft. from E/W	Latitude	Longitude	County
P	34	20-S	33-E		50 FSL	330 FEL	32.522482°N	103.643565°W	LEA

Dedicated Acres 1920	Infill or Defining Well Infill	Defining Well API Pending 503H	Overlapping Spacing Unit (Y/N)	Consolidation Code Com
Order Numbers.			Well setbacks are under Common Ownership: ☒ Yes ☐ No	

Kick Off Point (KOP)

UL	Section	Township	Range	Lot	Ft. from N/S	Ft. from E/W	Latitude	Longitude	County
P	15	20-S	33-E		480 FSL	1155 FEL	32.567215°N	103.646265°W	LEA



First Take Point (FTP)

UL	Section	Township	Range	Lot	Ft. from N/S	Ft. from E/W	Latitude	Longitude	County
A	22	20-S	33-E		100 FNL	330 FEL	32.565626°N	103.643588°W	LEA

Last Take Point (LTP)

UL	Section	Township	Range	Lot	Ft. from N/S	Ft. from E/W	Latitude	Longitude	County
P	34	20-S	33-E		100 FSL	330 FEL	32.522619°N	103.643565°W	LEA


Unitized Area or Area of Uniform Interest	Spacing Unit Type ☒ Horizontal ☐ Vertical	Ground Floor Elevation:
---	--	-------------------------

OPERATOR CERTIFICATIONS <i>I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief, and, if the well is a vertical or directional well, that this organization either owns a working interest or unleased mineral interest in the land including the proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of a working interest or unleased mineral interest, or to a voluntary pooling agreement or a compulsory pooling order heretofore entered by the division.</i> <i>If this well is a horizontal well, I further certify that this organization has received the consent of at least one lessee or owner of a working interest or unleased mineral interest in each tract (in the target pool or formation) in which any part of the well's completed interval will be located or obtained a compulsory pooling order from the division.</i>  8/29/24		SURVEYOR CERTIFICATIONS <i>I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief.</i>  8/8/24	
Signature Stan Wagner	Signature and Seal of Professional Surveyor 		
Printed Name	Certificate Number 17777	Date of Survey JULY 31, 2024	
Email Address	W.O.#24-665 DRAWN BY: WN PAGE 1 OF 2		

Note: No allowable will be assigned to this completion until all interests have been consolidated or a non-standard unit has been approved by the division.


This grid represents a standard section. You may superimpose a non-standard section, or larger area, over this grid. Operators must outline the dedicated acreage in a red box, clearly show the well surface location and bottom hole location, if it is directionally drilled, with the dimensions from the section lines in the cardinal directions. If this is a horizontal wellbore show on this plat the location of the First Take Point and Last Take Point, and the point within the Completed interval (other than the First Take Point or Last Take Point) that is closest to any outer boundary of the tract.

Surveyors shall use the latest United States government survey or dependent resurvey. Well locations will be in reference to the New Mexico Principal Meridian. If the land is not surveyed, contact the OCD Engineering Bureau. Independent subdivision surveys will not be acceptable.

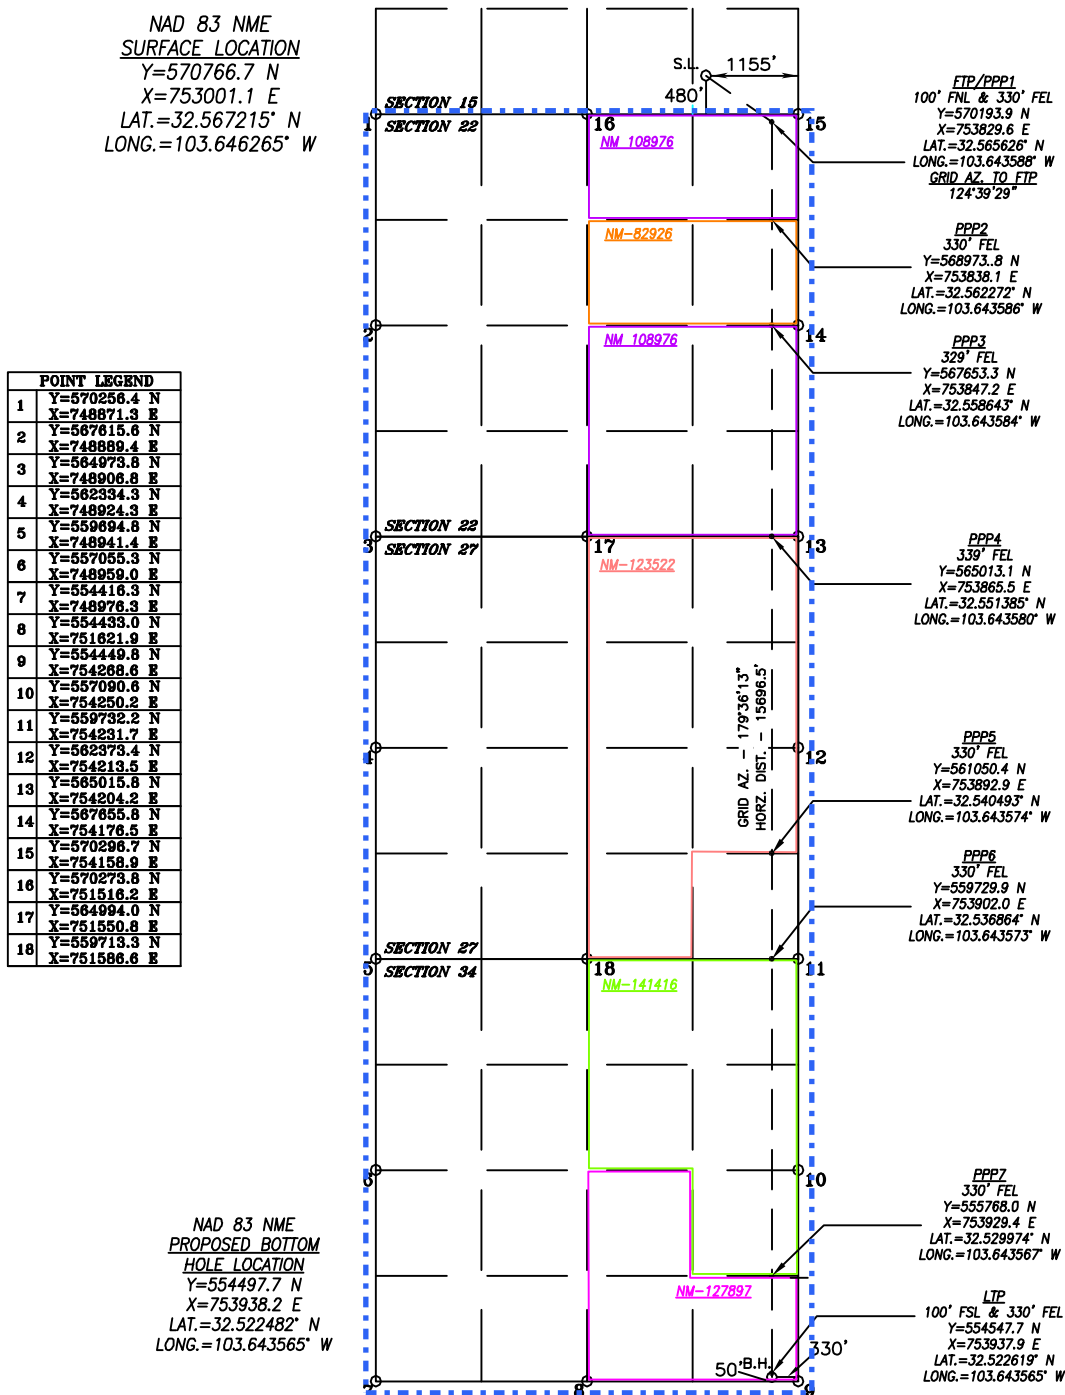


PAGE 2 OF 2

10M CHOKE MANIFOLD CONFIGURATION

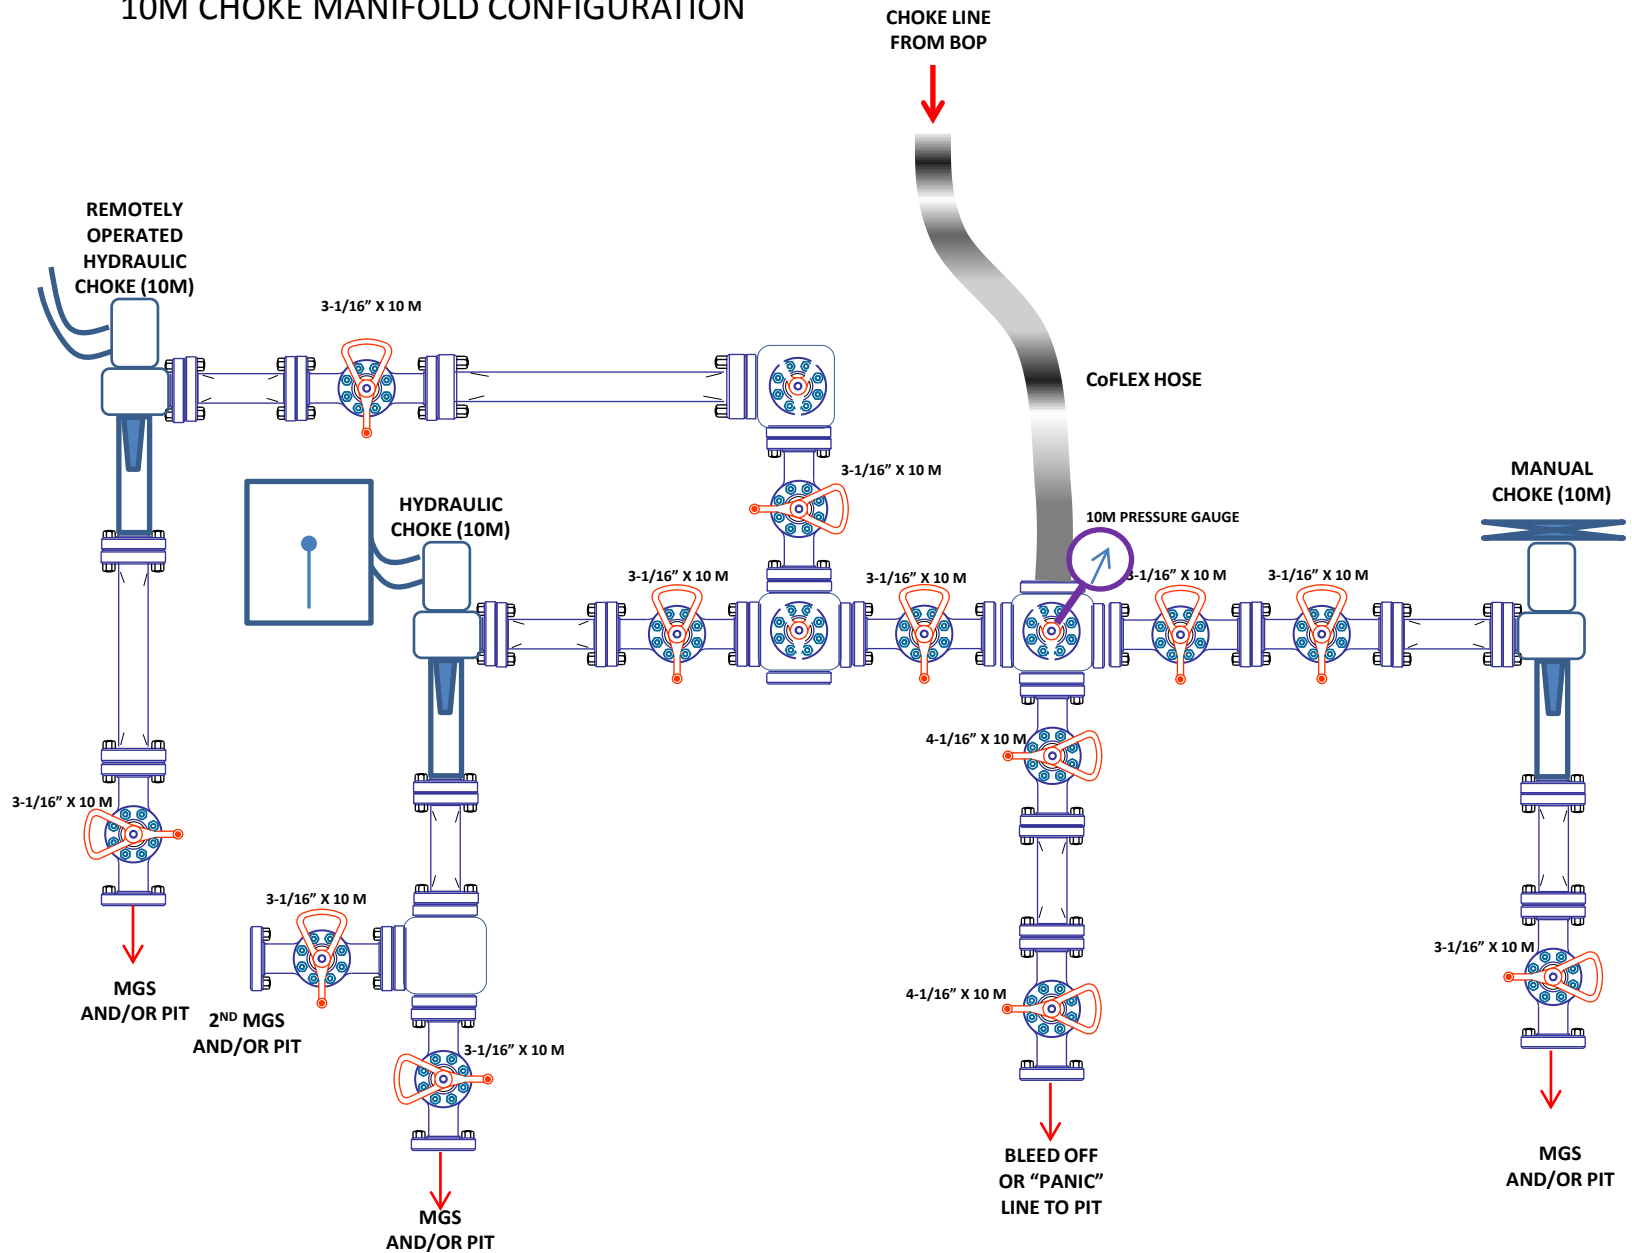

10M REMOTE KILL SCHEMATIC

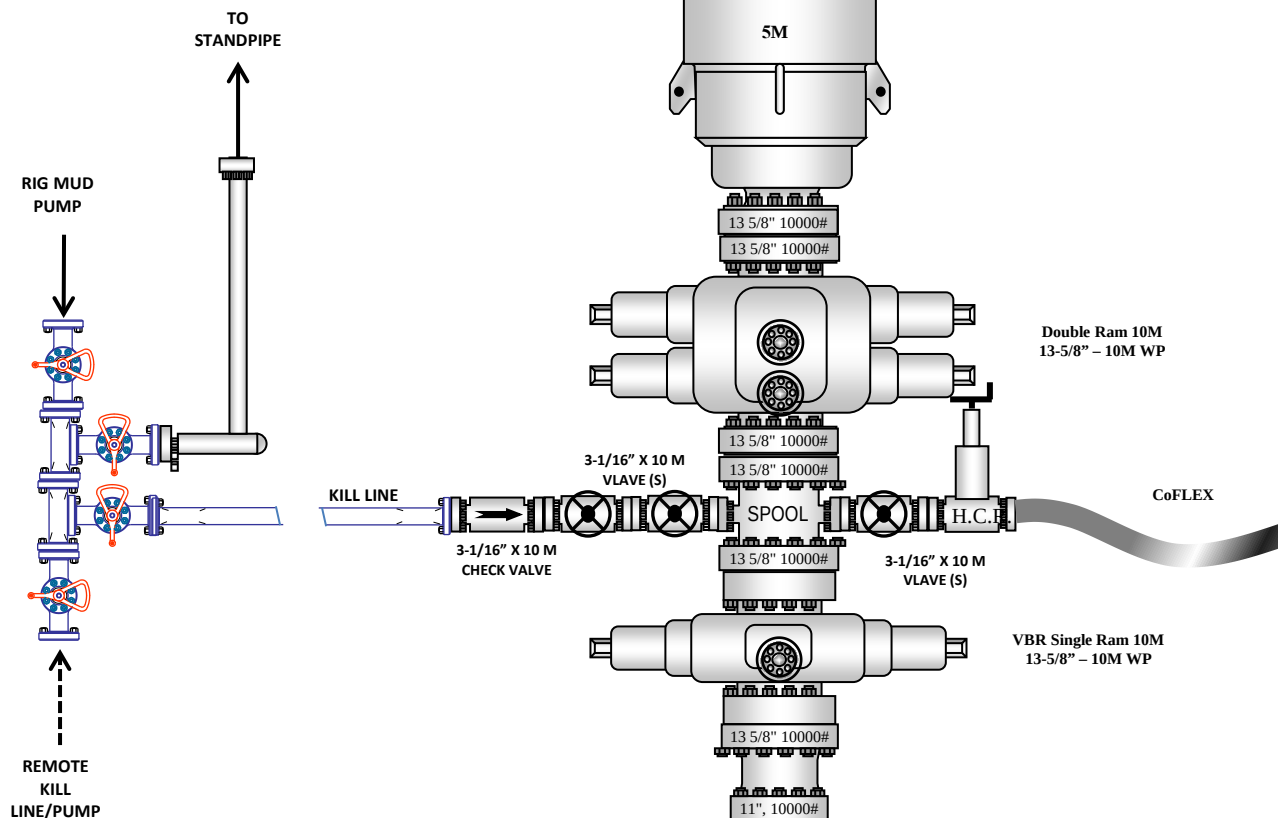

COG Operating, LLC - Donkey Potroast Fed Com 504H

1. Geologic Formations

TVD of target	10,600' EOL	Pilot hole depth	NA
MD at TD:	26,091'	Deepest expected fresh water:	325'

Formation	Depth (TVD) from KB	Water/Mineral Bearing/ Target Zone?	Hazards*
Quaternary Fill	Surface	Water	
Rustler	1333	Water	
Top of Salt	1728	Salt	
USGS Marker Bed 126	2803	Salt	
Base of Salt	3036	Salt Water	
Capitan Reef	3604	Salt Water	
Lamar	5136	Oil/Gas	
Brushy Canyon	6634	Oil/Gas	
Bone Spring	8321	Oil/Gas	
Avalon	8682	Oil/Gas	
1st Bone Spring Sand	9404	Oil/Gas	
1st Bone Spring Shale	9681	Oil/Gas	
2nd Bone Spring Sand	9927	Target Oil/Gas	
3rd Bone Spring Carb	10449	Not Penetrated	

Potash/Reef well archetype: 5-String Design Open 2nd Int x 3rd Int Annulus w/ ICP 3 below relief zone (Figure D). Sundry aims to comply with R-111-Q as passed on 5/10/2024.

2. Casing Program

Hole Size	Casing Interval		Csg. Size	Weight (lbs)	Grade	Conn.	SF Collapse	SF Burst	SF Body	SF Joint
	From	To								
26.00"	0	1433	20.000"	106.5	J55	ER	1.17	1.77	11.04	11.04
17.50"	0	3236	13.375"	54.5	L80-IC	BTC	1.25	1.85	7.04	6.99
12.25"	0	5136	9.625"	40	L80-IC	BTC	2.17	1.53	4.46	4.61
8.750"	0	9785	7.625"	29.7	P110-ICY	W513	1.56	1.95	3.15	3.26
6.75"	0	9585	5.5"	23	P110-CY	BTC	2.16	2.28	3.31	3.28
6.75"	9585	26,091	5.5"	23	P110-CY	W441	1.95	2.28	2.99	2.90
BLM Minimum Safety Factor							1.125	1	1.6 Dry 1.8 Wet	1.6 Dry 1.8 Wet

Intermediate casing will be kept at least 1/3 full while running casing to mitigate collapse. Surface burst based on 0.7 frac gradient at the shoe with Gas Gradient 0.1 psi/ft to surface and
All casing strings will be tested in accordance with Onshore Oil and Gas Order #2 III.B.1.h

The 5 1/2" wedge casing will be run back 200' above KOP to ensure the coupling OD clearance is greater than .422" for the cement bond tie in.

Intend to use new casing meeting API standards.

COG Operating, LLC - Donkey Potroast Fed Com 504H

	Y or N
Is casing new? If used, attach certification as required in Onshore Order #1	Y
Does casing meet API specifications? If no, attach casing specification sheet.	Y
Is premium or uncommon casing planned? If yes attach casing specification sheet.	Y
Does the above casing design meet or exceed BLM's minimum standards? If not provide justification (loading assumptions, casing design criteria).	Y
Will the intermediate pipe be kept at a minimum 1/3 fluid filled to avoid approaching the collapse pressure rating of the casing?	Y
Is well located within Capitan Reef?	Y
If yes, does production casing cement tie back a minimum of 50' above the Reef?	N
Is well within the designated 4 string boundary?	Y
Is well located in SOPA but not in R-111-P?	N
If yes, are the first 2 strings cemented to surface and 3 rd string cement tied back 500' into previous casing?	
Is well located in R-111-P and SOPA?	Y
If yes, are the first three strings cemented to surface?	Y
Is 2 nd string set 100' to 600' below the base of salt?	Y
Is well located in high Cave/Karst?	N
If yes, are there two strings cemented to surface?	
(For 2 string wells) If yes, is there a contingency casing if lost circulation occurs?	
Is well located in critical Cave/Karst?	N
If yes, are there three strings cemented to surface?	

COG Operating, LLC - Donkey Potroast Fed Com 504H

3. Cementing Program

Casing	# Sks	Wt. lb/ gal	Yld ft3/ sack	H ₂ O gal/sk	500# Comp. Strength (hours)	Slurry Description
Surf	807	13.5	1.75	9	12	Lead: Class C + 4% Gel + 1% CaCl ₂
	565	14.8	1.34	6.34	8	Tail: Class C + 2% CaCl ₂
Inter 1	845	12.8	2.26	12.84	12	Lead: Class C + 5% Gel + 1% CaCl ₂
	291	14.8	1.2	5.35	10	50:50 Class H Premium
Inter 2	576	12.8	2.26	12.84	12	Lead: Class C + 5% Gel + 1% CaCl ₂
	262	14.8	1.2	5.35	10	50:50 Class H Premium
Inter 3	160	14.8	1.35	6.6	10	Tail: Class H - Single Slurry
Prod						
	1297	13.2	1.24	5.7	19	Tail: 50:50:2 Class H Blend Single Slurry

Intermediate #1 Salt string cemented to surface. Drill out to wait for 500PSI compressive strength.

Intermediate #2 Reef string will be cemented to surface. Drill out to wait for 500PSI compressive strength.

Intermediate #3 long string cemented Tail single slurry leaving Delaware Mountain group open as a relief zone. Section to be monitored during completions, and then Bradenhead cemented after completion is complete within 180 days to tie back. Drill out of intermediate to wait for 500psi compressive strength.

Production cement tied back 1000' into intermediate 3 string with minimal excess to ensure annulus remains open.

Volumes Subject to Observed Hole Conditions and/or Fluid Caliper Results

Lab reports with the 500 psi compressive strength time for the cement will be onsite for review.

Casing String	TOC	% Excess
Surface	0'	50%
1st Intermediate	0'	50%
2nd Intermediate	0'	50%
3rd Intermediate	7,634'	0%
Production	8,585'	10% OH in Lateral (KOP to EOL)

COG Operating, LLC - Donkey Potroast Fed Com 504H

4. Pressure Control Equipment

N	A variance is requested for the use of a diverter on the surface casing. See attached for schematic.
Y	A variance is requested for the use of BOPE break testing on intermediate skids (in accordance with the 30 day full BOPE test requirements).

BOP installed and tested before drilling which hole?	Size?	Min. Required WP	Type	x	Tested to:
17-1/2"	20"	5M	Annular	x	2500psi
			Blind Ram		5000psi
			Pipe Ram		
			Double Ram		
			Other*		
12 1/4"	13-3/8"	5M	Annular	x	2500psi
			Blind Ram	x	5000psi
			Pipe Ram	x	
			Double Ram	x	
			Other*		
8-3/4"	13-3/8"	5M	Annular	x	2500psi
			Blind Ram	x	5000psi
			Pipe Ram	x	
			Double Ram	x	
			Other*		
6-3/4"	13-3/8"	10M	5M Annular	x	5000psi
			Blind Ram	x	10000psi
			Pipe Ram	x	
			Double Ram	x	
			Other*		

BOP/BOPE will be tested by an independent service company to 250 psi low and the high pressure indicated above per Onshore Order 2 requirements. The System may be upgraded to a higher pressure but still tested to the working pressure listed in the table above. If the system is upgraded all the components installed will be functional and tested.

Pipe rams will be operationally checked each 24 hour period. Blind rams will be operationally checked on each trip out of the hole. These checks will be noted on the daily tour sheets. Other accessories to the BOP equipment will include a Kelly cock and floor safety valve (inside BOP) and choke lines and choke manifold. See attached schematics.

Y	Formation integrity test will be performed per Onshore Order #2.
Y	On Exploratory wells or on that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Will be tested in accordance with Onshore Oil and Gas Order #2 III.B.1.i.
Y	A variance is requested for the use of a flexible choke line from the BOP to Choke Manifold. See attached for specs and hydrostatic test chart.
N	Are anchors required by manufacturer?
Y	A multibowl wellhead is being used. The BOP will be tested per Onshore Order #2 after installation on the surface casing which will cover testing requirements for a maximum of 30 days. If any seal subject to test pressure is broken the system must be tested.

COG Operating, LLC - Donkey Potroast Fed Com 504H

5. Mud Program

Depth		Type	Weight (ppg)	Viscosity	Water Loss
From	To				
0	Surf. Shoe	FW Gel	8.6 - 8.8	28-34	N/C
Surf csg	13.375" Int 1 shoe	Saturated Brine	9 - 10	28-34	N/C
13.375" shoe	9.625" Int 2 shoe	Saturated Brine	9 - 10	28-34	N/C
9.625" Int 2 shoe	7-5/8" Int 3 shoe	Diesel/Brine	8.4 - 9.3	28-34	N/C
7-5/8" Int 3 shoe	Lateral TD	OBM	9.6 - 13.5	35-45	<20

Sufficient mud materials to maintain mud properties and meet minimum lost circulation and weight increase requirements will be kept on location at all times.

What will be used to monitor the loss or gain of fluid?	PVT/Pason/Visual Monitoring
---	-----------------------------

6. Logging and Testing Procedures

Logging, Coring and Testing.	
Y	Will run GR/CNL from TD to surface (horizontal well – vertical portion of hole). Stated logs run will be in the Completion Report and submitted to the BLM.
Y	No Logs are planned based on well control or offset log information.
N	Drill stem test? If yes, explain.
Y	Coring? If yes, explain.

Sidewall coring will be performed for pilot hole operations from Avalon to Strawn.

Additional logs planned		Interval
Y	Resistivity	Pilot Hole TD to ICP
Y	Density	Pilot Hole TD to ICP
Y	CBL	Production casing (If cement not circulated to surface)
Y	Mud log	Intermediate shoe to TD
N	PEX	

COG Operating, LLC - Donkey Potroast Fed Com 504H**7. Drilling Conditions**

Condition	Specify what type and where?
BH Pressure at deepest TVD	7445 psi at 10600' TVD
Abnormal Temperature	NO 165 Deg. F.

No abnormal pressure or temperature conditions are anticipated. Sufficient mud materials to maintain mud properties and weight increase requirements will be kept on location at all times.

Sufficient supplies of Paper/LCM for periodic sweeps to control seepage and losses will be maintained on location.

Hydrogen Sulfide (H₂S) monitors will be installed prior to drilling out the surface shoe. If H₂S is detected in concentrations greater than 100 ppm, the operator will comply with the provisions of Onshore Oil and Gas Order #6. If Hydrogen Sulfide is encountered, measured values and formations will be provided to the BLM.

N H₂S is present

Y H₂S Plan attached


8. Other Facets of Operation

Y	Is it a walking operation?
Y	Is casing pre-set?

x	H ₂ S Plan.
x	BOP & Choke Schematics.
x	Directional Plan

COG Operating LLC
H₂S Equipment Schematic
Terrain: Shinnery sand hills.

Well pad will be 400' x 400'
with cellar in center of pad

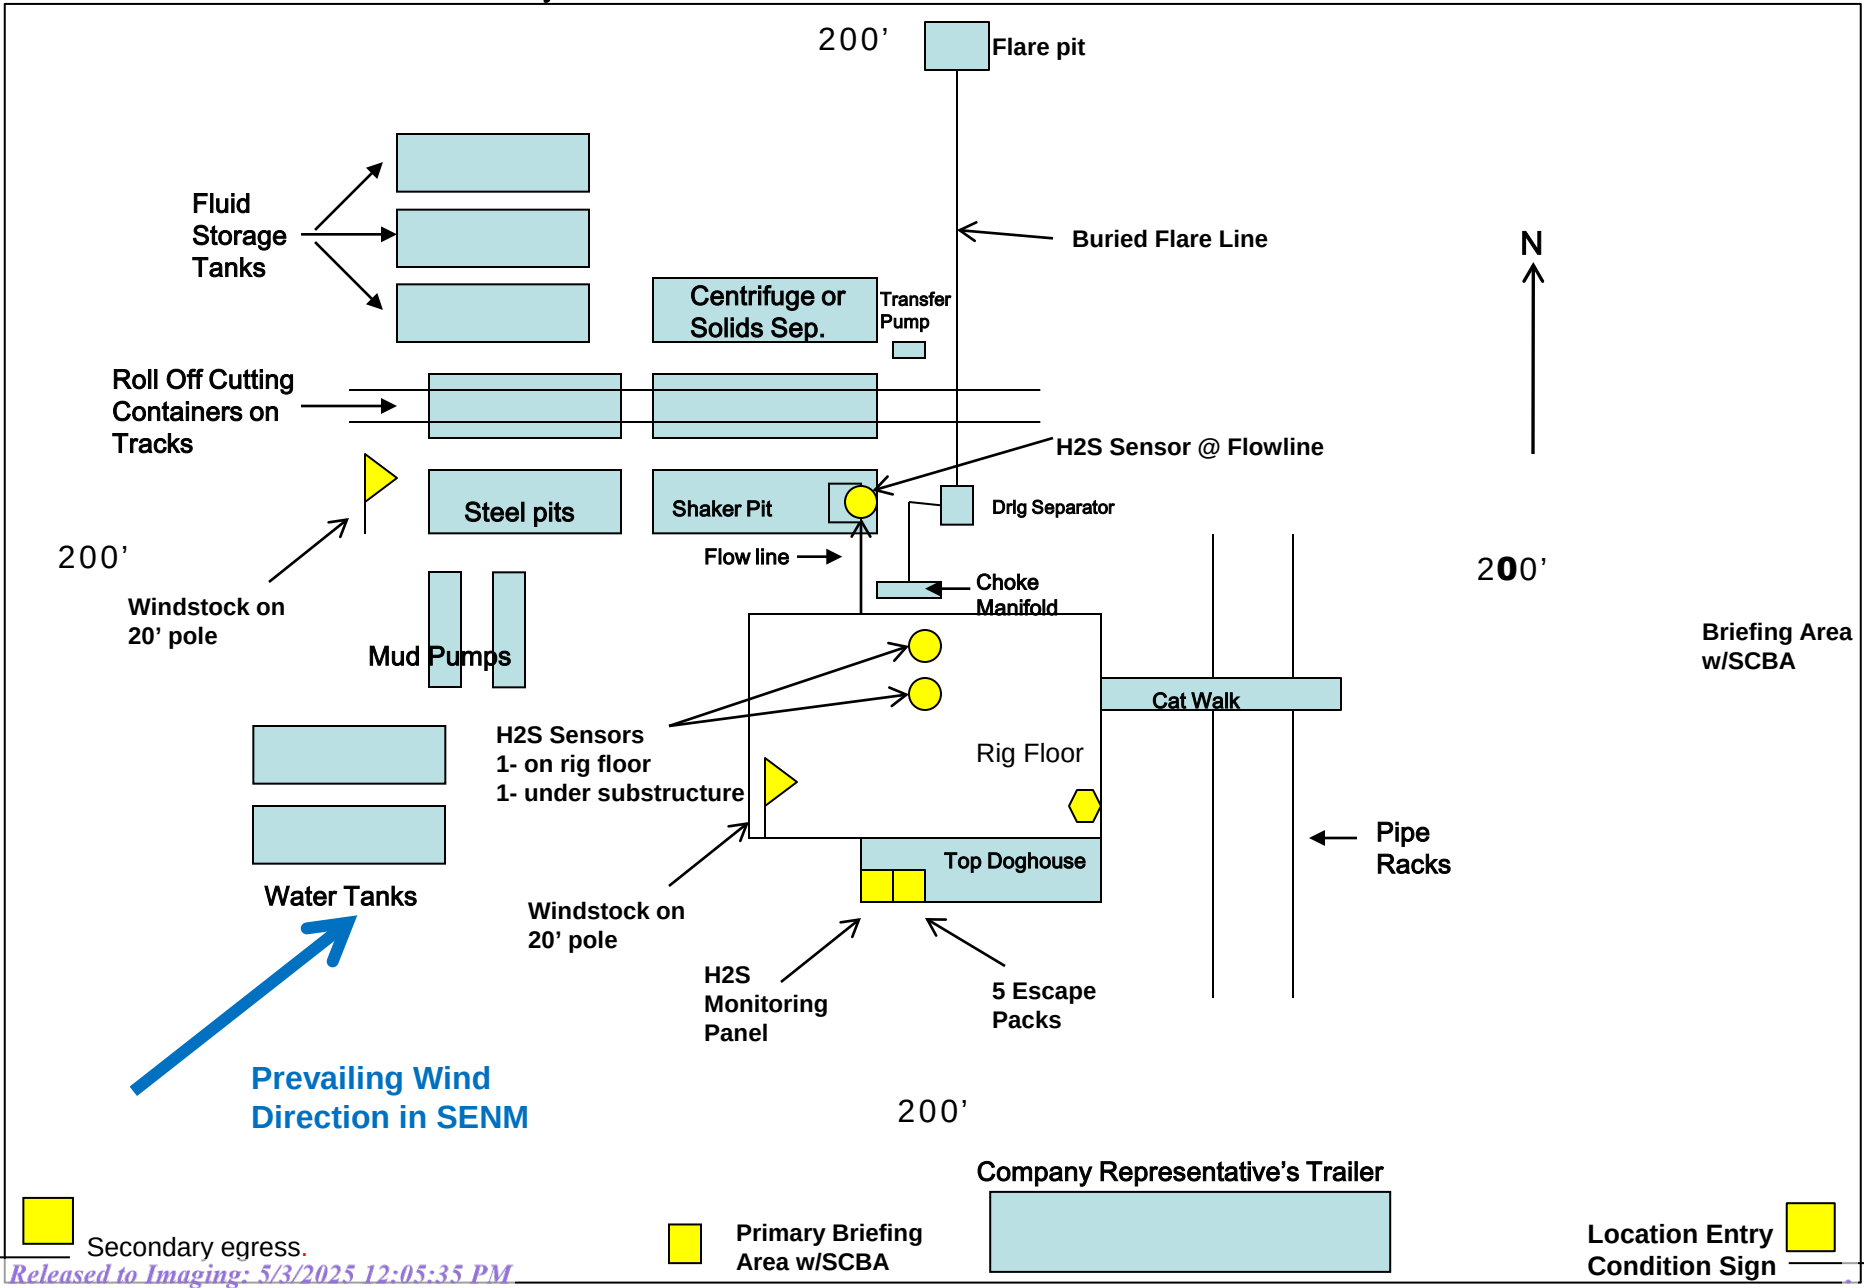

COG OPERATING LLC
HYDROGEN SULFIDE DRILLING OPERATIONS PLAN

1. HYDROGEN SULFIDE TRAINING

All personnel, whether regularly assigned, contracted, or employed on an unscheduled basis, will receive training from a qualified instructor in the following areas prior to commencing drilling operations on this well:

- a. The hazards and characteristics of hydrogen sulfide (H₂S).
- b. The proper use and maintenance of personal protective equipment and life support systems.
- c. The proper use of H₂S detectors, alarms, warning systems, briefing areas, evacuation procedures, and prevailing winds.
- d. The proper techniques for first aid and rescue procedures.

In addition, supervisory personnel will be trained in the following areas:

- a. The effects of H₂S on metal components. If high tensile tubulars are to be used, personnel will be trained in their special maintenance requirements.
- b. Corrective action and shut-in procedures when drilling or reworking a well and blowout prevention and well control procedures.
- c. The contents and requirements of the H₂S Drilling Operations Plan and the Public Protection Plan.

There will be an initial training session just prior to encountering a known or probable H₂S zone (within 3 days or 500 feet) and weekly H₂S and well control drills for all personnel in each crew. The initial training session shall include a review of the site specific H₂S Drilling Operations Plan and the Public Protection Plan. This plan shall be available at the well site. All personnel will be required to carry documentation that they have received the proper training.

2. H₂S SAFETY EQUIPMENT AND SYSTEMS

Note: All H₂S safety equipment and systems will be installed, tested, and operational when drilling reaches a depth of 500 feet above, or three days prior to penetrating the first zone containing or reasonably expected to contain H₂S. If H₂S greater than 100 ppm is encountered in the gas stream we will shut in and install H₂S equipment.

- a. Well Control Equipment:
 - Flare line.
 - Choke manifold with remotely operated choke.
 - Blind rams and pipe rams to accommodate all pipe sizes with properly sized closing unit.
 - Auxiliary equipment to include: annular preventer, mud-gas separator, rotating head.

- b. Protective equipment for essential personnel:
Mark II Surviveair 30-minute units located in the dog house and at briefing areas.
- c. H2S detection and monitoring equipment:
2 - portable H2S monitor positioned on location for best coverage and response. These units have warning lights and audible sirens when H2S levels of 20 ppm are reached.
- d. Visual warning systems:
Caution/Danger signs shall be posted on roads providing direct access to location. Signs will be painted a high visibility yellow with black lettering of sufficient size to be readable at a reasonable distance from the immediate location. Bilingual signs will be used, when appropriate. See example attached.
- e. Mud Program:
The mud program has been designed to minimize the volume of H2S circulated to the surface.
- f. Metallurgy:
All drill strings, casings, tubing, wellhead, blowout preventers, drilling spool, kill lines, choke manifold and lines, and valves shall be suitable for H2S service.
- g. Communication:
Company vehicles equipped with cellular telephone.

COG OPERATING LLC has conducted a review to determine if an H2S contingency plan is required for the above referenced well. We were able to conclude that any potential hazardous volume would be minimal. H2S concentrations of wells in this area from surface to TD are low enough; therefore, we do not believe that an H2S contingency plan is necessary.

W A R N I N G

**YOU ARE ENTERING AN H₂S AREA
AUTHORIZED PERSONNEL ONLY**

- 1. BEARDS OR CONTACT LENSES NOT ALLOWED**
- 2. HARD HATS REQUIRED**
- 3. SMOKING IN DESIGNATED AREAS ONLY**
- 4. BE WIND CONSCIOUS AT ALL TIMES**
- 5. CK WITH COG OPERATING LLC FOREMAN AT MAIN OFFICE**

COG OPERATING LLC

1-575-748-6940

EMERGENCY CALL LIST

	<u>OFFICE</u>	<u>MOBILE</u>
Jenaya Rohlfing	432-683-7443	713-478-0376
Chad Gregory		432-238-5840

EMERGENCY RESPONSE NUMBERS

	<u>OFFICE</u>
STATE POLICE	575-748-9718
EDDY COUNTY SHERIFF	575-746-2701
EMERGENCY MEDICAL SERVICES (AMBULANCE)	911 or 575-746-2701
EDDY COUNTY EMERGENCY MANAGEMENT (HARRY BURGESS)	575-887-9511
STATE EMERGENCY RESPONSE CENTER (SERC)	575-476-9620
CARLSBAD POLICE DEPARTMENT	575-885-2111
CARLSBAD FIRE DEPARTMENT	575-885-3125
NEW MEXICO OIL CONSERVATION DIVISION	575-748-1283
INDIAN FIRE & SAFETY	800-530-8693
HALLIBURTON SERVICES	800-844-8451

DELAWARE BASIN EAST

ZEUS_NME

TARHEEL_DONKEY POTROAST PROJECT

**_DONKEY POTROAST FED COM 504H - Slot DONKEY
POTROAST #504H**

OWB

Plan: PWP0

Standard Planning Report

22 July, 2024

ConocoPhillips
Planning Report

Database:	EDT 17 Permian Prod	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 504H - Slot DONKEY POTROAST #504H
Company:	DELAWARE BASIN EAST	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Project:	ZEUS_NME	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site:	TARHEEL_DONKEY POTROAST PROJECT	North Reference:	Grid
Well:	_DONKEY POTROAST FED COM 504H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OWB		
Design:	PWP0		

Project	ZEUS_NME		
Map System:	US State Plane 1927 (Exact solution)	System Datum:	Mean Sea Level
Geo Datum:	NAD 1927 (NADCON CONUS)		
Map Zone:	New Mexico East 3001		

Site	TARHEEL_DONKEY POTROAST PROJECT		
Site Position:		Northing:	567,544.34 usft
From:	Map	Easting:	710,351.32 usft
Position Uncertainty:	0.0 usft	Slot Radius:	13-3/16 "
		Latitude:	32° 33' 30.358 N
		Longitude:	103° 39' 2.181 W

Well	_DONKEY POTROAST FED COM 504H - Slot DONKEY POTROAST #504H		
Well Position	+N/-S	0.0 usft	Northing:
	+E/-W	0.0 usft	Easting:
Position Uncertainty	3.0 usft	Wellhead Elevation:	usft
Grid Convergence:	0.37 °		
		Latitude:	32° 34' 1.545 N
		Longitude:	103° 38' 44.802 W
		Ground Level:	3,630.0 usft

Wellbore	OWB				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	BGGM2022	9/14/2023	6.57	60.36	47,636.34993692

Design	PWP0			
Audit Notes:				
Version:	Phase:	PLAN	Tie On Depth:	0.0
Vertical Section:	Depth From (TVD) (usft)	+N/-S (usft)	+E/-W (usft)	Direction (°)
	0.0	0.0	0.0	176.71

Plan Survey Tool Program	Date	7/22/2024		
Depth From (usft)	Depth To (usft)	Survey (Wellbore)	Tool Name	Remarks
1	0.0	26,090.3 PWP0 (OWB)	r.5 MWD+IFR1+MS	
			OWSG MWD + IFR1 + Multi-Sl	

ConocoPhillips

Planning Report

Database:	EDT 17 Permian Prod	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 504H - Slot DONKEY POTROAST #504H
Company:	DELAWARE BASIN EAST	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Project:	ZEUS_NME	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site:	TARHEEL_DONKEY POTROAST PROJECT	North Reference:	Grid
Well:	_DONKEY POTROAST FED COM 504H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OWB		
Design:	PWP0		

Plan Sections										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	TFO (°)	Target
0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.00	0.00	
1,500.0	0.00	0.00	1,500.0	0.0	0.0	0.00	0.00	0.00	0.00	
2,183.7	13.67	126.90	2,177.2	-48.7	64.9	2.00	2.00	0.00	126.90	
5,547.4	13.67	126.90	5,445.6	-526.1	700.8	0.00	0.00	0.00	0.00	
6,914.7	0.00	0.00	6,800.0	-623.6	830.7	1.00	-1.00	0.00	180.00	
10,116.7	0.00	0.00	10,002.0	-623.6	830.7	0.00	0.00	0.00	0.00	
11,016.7	90.00	179.61	10,575.0	-1,196.5	834.6	10.00	10.00	19.96	179.61	
26,090.3	90.00	179.61	10,575.0	-16,269.7	936.6	0.00	0.00	0.00	0.00	

ConocoPhillips

Planning Report

Database:	EDT 17 Permian Prod	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 504H - Slot DONKEY POTROAST #504H
Company:	DELAWARE BASIN EAST	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Project:	ZEUS_NME	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site:	TARHEEL_DONKEY POTROAST PROJECT	North Reference:	Grid
Well:	_DONKEY POTROAST FED COM 504H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OWB		
Design:	PWP0		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
0.0	0.00	0.00	0.0	0.0	0.0	0.0	0.00	0.00	0.00	
100.0	0.00	0.00	100.0	0.0	0.0	0.0	0.00	0.00	0.00	
200.0	0.00	0.00	200.0	0.0	0.0	0.0	0.00	0.00	0.00	
300.0	0.00	0.00	300.0	0.0	0.0	0.0	0.00	0.00	0.00	
400.0	0.00	0.00	400.0	0.0	0.0	0.0	0.00	0.00	0.00	
500.0	0.00	0.00	500.0	0.0	0.0	0.0	0.00	0.00	0.00	
600.0	0.00	0.00	600.0	0.0	0.0	0.0	0.00	0.00	0.00	
700.0	0.00	0.00	700.0	0.0	0.0	0.0	0.00	0.00	0.00	
800.0	0.00	0.00	800.0	0.0	0.0	0.0	0.00	0.00	0.00	
900.0	0.00	0.00	900.0	0.0	0.0	0.0	0.00	0.00	0.00	
1,000.0	0.00	0.00	1,000.0	0.0	0.0	0.0	0.00	0.00	0.00	
1,100.0	0.00	0.00	1,100.0	0.0	0.0	0.0	0.00	0.00	0.00	
1,200.0	0.00	0.00	1,200.0	0.0	0.0	0.0	0.00	0.00	0.00	
1,300.0	0.00	0.00	1,300.0	0.0	0.0	0.0	0.00	0.00	0.00	
1,400.0	0.00	0.00	1,400.0	0.0	0.0	0.0	0.00	0.00	0.00	
1,500.0	0.00	0.00	1,500.0	0.0	0.0	0.0	0.00	0.00	0.00	
1,600.0	2.00	126.90	1,600.0	-1.0	1.4	1.1	2.00	2.00	0.00	
1,700.0	4.00	126.90	1,699.8	-4.2	5.6	4.5	2.00	2.00	0.00	
1,800.0	6.00	126.90	1,799.5	-9.4	12.6	10.1	2.00	2.00	0.00	
1,900.0	8.00	126.90	1,898.7	-16.7	22.3	18.0	2.00	2.00	0.00	
2,000.0	10.00	126.90	1,997.5	-26.1	34.8	28.1	2.00	2.00	0.00	
2,100.0	12.00	126.90	2,095.6	-37.6	50.1	40.4	2.00	2.00	0.00	
2,183.7	13.67	126.90	2,177.2	-48.7	64.9	52.4	2.00	2.00	0.00	
2,200.0	13.67	126.90	2,193.1	-51.1	68.0	54.9	0.00	0.00	0.00	
2,300.0	13.67	126.90	2,290.2	-65.3	86.9	70.1	0.00	0.00	0.00	
2,400.0	13.67	126.90	2,387.4	-79.4	105.8	85.4	0.00	0.00	0.00	
2,500.0	13.67	126.90	2,484.6	-93.6	124.7	100.7	0.00	0.00	0.00	
2,600.0	13.67	126.90	2,581.7	-107.8	143.6	115.9	0.00	0.00	0.00	
2,700.0	13.67	126.90	2,678.9	-122.0	162.5	131.2	0.00	0.00	0.00	
2,800.0	13.67	126.90	2,776.1	-136.2	181.4	146.4	0.00	0.00	0.00	
2,900.0	13.67	126.90	2,873.2	-150.4	200.3	161.7	0.00	0.00	0.00	
3,000.0	13.67	126.90	2,970.4	-164.6	219.3	176.9	0.00	0.00	0.00	
3,100.0	13.67	126.90	3,067.6	-178.8	238.2	192.2	0.00	0.00	0.00	
3,200.0	13.67	126.90	3,164.7	-193.0	257.1	207.4	0.00	0.00	0.00	
3,300.0	13.67	126.90	3,261.9	-207.2	276.0	222.7	0.00	0.00	0.00	
3,400.0	13.67	126.90	3,359.1	-221.4	294.9	237.9	0.00	0.00	0.00	
3,500.0	13.67	126.90	3,456.2	-235.6	313.8	253.2	0.00	0.00	0.00	
3,600.0	13.67	126.90	3,553.4	-249.7	332.7	268.5	0.00	0.00	0.00	
3,700.0	13.67	126.90	3,650.6	-263.9	351.6	283.7	0.00	0.00	0.00	
3,800.0	13.67	126.90	3,747.7	-278.1	370.5	299.0	0.00	0.00	0.00	
3,900.0	13.67	126.90	3,844.9	-292.3	389.4	314.2	0.00	0.00	0.00	
4,000.0	13.67	126.90	3,942.1	-306.5	408.3	329.5	0.00	0.00	0.00	
4,100.0	13.67	126.90	4,039.2	-320.7	427.2	344.7	0.00	0.00	0.00	
4,200.0	13.67	126.90	4,136.4	-334.9	446.1	360.0	0.00	0.00	0.00	
4,300.0	13.67	126.90	4,233.6	-349.1	465.0	375.2	0.00	0.00	0.00	
4,400.0	13.67	126.90	4,330.7	-363.3	483.9	390.5	0.00	0.00	0.00	
4,500.0	13.67	126.90	4,427.9	-377.5	502.8	405.7	0.00	0.00	0.00	
4,600.0	13.67	126.90	4,525.0	-391.7	521.7	421.0	0.00	0.00	0.00	
4,700.0	13.67	126.90	4,622.2	-405.9	540.6	436.3	0.00	0.00	0.00	
4,800.0	13.67	126.90	4,719.4	-420.0	559.5	451.5	0.00	0.00	0.00	
4,900.0	13.67	126.90	4,816.5	-434.2	578.4	466.8	0.00	0.00	0.00	
5,000.0	13.67	126.90	4,913.7	-448.4	597.3	482.0	0.00	0.00	0.00	
5,100.0	13.67	126.90	5,010.9	-462.6	616.2	497.3	0.00	0.00	0.00	

ConocoPhillips

Planning Report

Database:	EDT 17 Permian Prod	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 504H - Slot DONKEY POTROAST #504H
Company:	DELAWARE BASIN EAST	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Project:	ZEUS_NME	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site:	TARHEEL_DONKEY POTROAST PROJECT	North Reference:	Grid
Well:	_DONKEY POTROAST FED COM 504H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OWB		
Design:	PWP0		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
5,200.0	13.67	126.90	5,108.0	-476.8	635.1	512.5	0.00	0.00	0.00	
5,300.0	13.67	126.90	5,205.2	-491.0	654.1	527.8	0.00	0.00	0.00	
5,400.0	13.67	126.90	5,302.4	-505.2	673.0	543.0	0.00	0.00	0.00	
5,500.0	13.67	126.90	5,399.5	-519.4	691.9	558.3	0.00	0.00	0.00	
5,547.4	13.67	126.90	5,445.6	-526.1	700.8	565.5	0.00	0.00	0.00	
5,600.0	13.15	126.90	5,496.8	-533.4	710.6	573.4	1.00	-1.00	0.00	
5,700.0	12.15	126.90	5,594.3	-546.6	728.1	587.5	1.00	-1.00	0.00	
5,800.0	11.15	126.90	5,692.3	-558.7	744.2	600.6	1.00	-1.00	0.00	
5,900.0	10.15	126.90	5,790.6	-569.8	759.0	612.5	1.00	-1.00	0.00	
6,000.0	9.15	126.90	5,889.1	-579.9	772.4	623.3	1.00	-1.00	0.00	
6,100.0	8.15	126.90	5,988.0	-588.9	784.4	633.0	1.00	-1.00	0.00	
6,200.0	7.15	126.90	6,087.1	-596.9	795.1	641.6	1.00	-1.00	0.00	
6,300.0	6.15	126.90	6,186.4	-603.8	804.3	649.0	1.00	-1.00	0.00	
6,400.0	5.15	126.90	6,285.9	-609.7	812.2	655.4	1.00	-1.00	0.00	
6,500.0	4.15	126.90	6,385.6	-614.6	818.7	660.6	1.00	-1.00	0.00	
6,600.0	3.15	126.90	6,485.4	-618.4	823.8	664.7	1.00	-1.00	0.00	
6,700.0	2.15	126.90	6,585.3	-621.2	827.5	667.7	1.00	-1.00	0.00	
6,800.0	1.15	126.90	6,685.3	-622.9	829.8	669.6	1.00	-1.00	0.00	
6,900.0	0.15	126.90	6,785.3	-623.6	830.7	670.3	1.00	-1.00	0.00	
6,914.7	0.00	0.00	6,800.0	-623.6	830.7	670.3	1.00	-1.00	0.00	
7,000.0	0.00	0.00	6,885.3	-623.6	830.7	670.3	0.00	0.00	0.00	
7,100.0	0.00	0.00	6,985.3	-623.6	830.7	670.3	0.00	0.00	0.00	
7,200.0	0.00	0.00	7,085.3	-623.6	830.7	670.3	0.00	0.00	0.00	
7,300.0	0.00	0.00	7,185.3	-623.6	830.7	670.3	0.00	0.00	0.00	
7,400.0	0.00	0.00	7,285.3	-623.6	830.7	670.3	0.00	0.00	0.00	
7,500.0	0.00	0.00	7,385.3	-623.6	830.7	670.3	0.00	0.00	0.00	
7,600.0	0.00	0.00	7,485.3	-623.6	830.7	670.3	0.00	0.00	0.00	
7,700.0	0.00	0.00	7,585.3	-623.6	830.7	670.3	0.00	0.00	0.00	
7,800.0	0.00	0.00	7,685.3	-623.6	830.7	670.3	0.00	0.00	0.00	
7,900.0	0.00	0.00	7,785.3	-623.6	830.7	670.3	0.00	0.00	0.00	
8,000.0	0.00	0.00	7,885.3	-623.6	830.7	670.3	0.00	0.00	0.00	
8,100.0	0.00	0.00	7,985.3	-623.6	830.7	670.3	0.00	0.00	0.00	
8,200.0	0.00	0.00	8,085.3	-623.6	830.7	670.3	0.00	0.00	0.00	
8,300.0	0.00	0.00	8,185.3	-623.6	830.7	670.3	0.00	0.00	0.00	
8,400.0	0.00	0.00	8,285.3	-623.6	830.7	670.3	0.00	0.00	0.00	
8,500.0	0.00	0.00	8,385.3	-623.6	830.7	670.3	0.00	0.00	0.00	
8,600.0	0.00	0.00	8,485.3	-623.6	830.7	670.3	0.00	0.00	0.00	
8,700.0	0.00	0.00	8,585.3	-623.6	830.7	670.3	0.00	0.00	0.00	
8,800.0	0.00	0.00	8,685.3	-623.6	830.7	670.3	0.00	0.00	0.00	
8,900.0	0.00	0.00	8,785.3	-623.6	830.7	670.3	0.00	0.00	0.00	
9,000.0	0.00	0.00	8,885.3	-623.6	830.7	670.3	0.00	0.00	0.00	
9,100.0	0.00	0.00	8,985.3	-623.6	830.7	670.3	0.00	0.00	0.00	
9,200.0	0.00	0.00	9,085.3	-623.6	830.7	670.3	0.00	0.00	0.00	
9,300.0	0.00	0.00	9,185.3	-623.6	830.7	670.3	0.00	0.00	0.00	
9,400.0	0.00	0.00	9,285.3	-623.6	830.7	670.3	0.00	0.00	0.00	
9,500.0	0.00	0.00	9,385.3	-623.6	830.7	670.3	0.00	0.00	0.00	
9,600.0	0.00	0.00	9,485.3	-623.6	830.7	670.3	0.00	0.00	0.00	
9,700.0	0.00	0.00	9,585.3	-623.6	830.7	670.3	0.00	0.00	0.00	
9,800.0	0.00	0.00	9,685.3	-623.6	830.7	670.3	0.00	0.00	0.00	
9,900.0	0.00	0.00	9,785.3	-623.6	830.7	670.3	0.00	0.00	0.00	
10,000.0	0.00	0.00	9,885.3	-623.6	830.7	670.3	0.00	0.00	0.00	
10,100.0	0.00	0.00	9,985.3	-623.6	830.7	670.3	0.00	0.00	0.00	
10,116.7	0.00	0.00	10,002.0	-623.6	830.7	670.3	0.00	0.00	0.00	

ConocoPhillips
Planning Report

Database:	EDT 17 Permian Prod	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 504H - Slot DONKEY POTROAST #504H
Company:	DELAWARE BASIN EAST	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Project:	ZEUS_NME	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site:	TARHEEL_DONKEY POTROAST PROJECT	North Reference:	Grid
Well:	_DONKEY POTROAST FED COM 504H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OWB		
Design:	PWP0		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
10,150.0	3.33	179.61	10,035.2	-624.6	830.7	671.3	10.00	10.00	0.00	
10,200.0	8.33	179.61	10,085.0	-629.6	830.7	676.3	10.00	10.00	0.00	
10,250.0	13.33	179.61	10,134.1	-639.0	830.8	685.7	10.00	10.00	0.00	
10,300.0	18.33	179.61	10,182.1	-652.7	830.9	699.3	10.00	10.00	0.00	
10,350.0	23.33	179.61	10,228.9	-670.4	831.0	717.1	10.00	10.00	0.00	
10,400.0	28.33	179.61	10,273.9	-692.2	831.1	738.8	10.00	10.00	0.00	
10,450.0	33.33	179.61	10,316.8	-717.8	831.3	764.4	10.00	10.00	0.00	
10,500.0	38.33	179.61	10,357.3	-747.1	831.5	793.6	10.00	10.00	0.00	
10,550.0	43.33	179.61	10,395.1	-779.7	831.7	826.3	10.00	10.00	0.00	
10,600.0	48.33	179.61	10,430.0	-815.6	832.0	862.1	10.00	10.00	0.00	
10,650.0	53.33	179.61	10,461.5	-854.3	832.2	900.8	10.00	10.00	0.00	
10,700.0	58.33	179.61	10,489.6	-895.7	832.5	942.1	10.00	10.00	0.00	
10,750.0	63.33	179.61	10,514.0	-939.3	832.8	985.7	10.00	10.00	0.00	
10,800.0	68.33	179.61	10,534.4	-984.9	833.1	1,031.2	10.00	10.00	0.00	
10,850.0	73.33	179.61	10,550.9	-1,032.2	833.4	1,078.3	10.00	10.00	0.00	
10,900.0	78.33	179.61	10,563.1	-1,080.6	833.8	1,126.7	10.00	10.00	0.00	
10,950.0	83.33	179.61	10,571.1	-1,130.0	834.1	1,176.0	10.00	10.00	0.00	
11,000.0	88.33	179.61	10,574.7	-1,179.8	834.4	1,225.8	10.00	10.00	0.00	
11,016.7	90.00	179.61	10,575.0	-1,196.5	834.6	1,242.5	10.00	10.00	0.00	
11,100.0	90.00	179.61	10,575.0	-1,279.8	835.1	1,325.7	0.00	0.00	0.00	
11,200.0	90.00	179.61	10,575.0	-1,379.8	835.8	1,425.6	0.00	0.00	0.00	
11,300.0	90.00	179.61	10,575.0	-1,479.8	836.5	1,525.4	0.00	0.00	0.00	
11,400.0	90.00	179.61	10,575.0	-1,579.8	837.2	1,625.3	0.00	0.00	0.00	
11,500.0	90.00	179.61	10,575.0	-1,679.8	837.8	1,725.2	0.00	0.00	0.00	
11,600.0	90.00	179.61	10,575.0	-1,779.8	838.5	1,825.0	0.00	0.00	0.00	
11,700.0	90.00	179.61	10,575.0	-1,879.8	839.2	1,924.9	0.00	0.00	0.00	
11,800.0	90.00	179.61	10,575.0	-1,979.8	839.9	2,024.8	0.00	0.00	0.00	
11,900.0	90.00	179.61	10,575.0	-2,079.8	840.5	2,124.7	0.00	0.00	0.00	
12,000.0	90.00	179.61	10,575.0	-2,179.8	841.2	2,224.5	0.00	0.00	0.00	
12,100.0	90.00	179.61	10,575.0	-2,279.8	841.9	2,324.4	0.00	0.00	0.00	
12,200.0	90.00	179.61	10,575.0	-2,379.8	842.6	2,424.3	0.00	0.00	0.00	
12,300.0	90.00	179.61	10,575.0	-2,479.8	843.2	2,524.1	0.00	0.00	0.00	
12,400.0	90.00	179.61	10,575.0	-2,579.8	843.9	2,624.0	0.00	0.00	0.00	
12,500.0	90.00	179.61	10,575.0	-2,679.8	844.6	2,723.9	0.00	0.00	0.00	
12,600.0	90.00	179.61	10,575.0	-2,779.8	845.3	2,823.8	0.00	0.00	0.00	
12,700.0	90.00	179.61	10,575.0	-2,879.8	846.0	2,923.6	0.00	0.00	0.00	
12,800.0	90.00	179.61	10,575.0	-2,979.8	846.6	3,023.5	0.00	0.00	0.00	
12,900.0	90.00	179.61	10,575.0	-3,079.8	847.3	3,123.4	0.00	0.00	0.00	
13,000.0	90.00	179.61	10,575.0	-3,179.8	848.0	3,223.2	0.00	0.00	0.00	
13,100.0	90.00	179.61	10,575.0	-3,279.8	848.7	3,323.1	0.00	0.00	0.00	
13,200.0	90.00	179.61	10,575.0	-3,379.8	849.3	3,423.0	0.00	0.00	0.00	
13,300.0	90.00	179.61	10,575.0	-3,479.8	850.0	3,522.9	0.00	0.00	0.00	
13,400.0	90.00	179.61	10,575.0	-3,579.7	850.7	3,622.7	0.00	0.00	0.00	
13,500.0	90.00	179.61	10,575.0	-3,679.7	851.4	3,722.6	0.00	0.00	0.00	
13,600.0	90.00	179.61	10,575.0	-3,779.7	852.1	3,822.5	0.00	0.00	0.00	
13,700.0	90.00	179.61	10,575.0	-3,879.7	852.7	3,922.3	0.00	0.00	0.00	
13,800.0	90.00	179.61	10,575.0	-3,979.7	853.4	4,022.2	0.00	0.00	0.00	
13,900.0	90.00	179.61	10,575.0	-4,079.7	854.1	4,122.1	0.00	0.00	0.00	
14,000.0	90.00	179.61	10,575.0	-4,179.7	854.8	4,222.0	0.00	0.00	0.00	
14,100.0	90.00	179.61	10,575.0	-4,279.7	855.4	4,321.8	0.00	0.00	0.00	
14,200.0	90.00	179.61	10,575.0	-4,379.7	856.1	4,421.7	0.00	0.00	0.00	
14,300.0	90.00	179.61	10,575.0	-4,479.7	856.8	4,521.6	0.00	0.00	0.00	
14,400.0	90.00	179.61	10,575.0	-4,579.7	857.5	4,621.4	0.00	0.00	0.00	

ConocoPhillips
Planning Report

Database:	EDT 17 Permian Prod	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 504H - Slot DONKEY POTROAST #504H
Company:	DELAWARE BASIN EAST	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Project:	ZEUS_NME	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site:	TARHEEL_DONKEY POTROAST PROJECT	North Reference:	Grid
Well:	_DONKEY POTROAST FED COM 504H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OWB		
Design:	PWP0		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
14,500.0	90.00	179.61	10,575.0	-4,679.7	858.1	4,721.3	0.00	0.00	0.00	
14,600.0	90.00	179.61	10,575.0	-4,779.7	858.8	4,821.2	0.00	0.00	0.00	
14,700.0	90.00	179.61	10,575.0	-4,879.7	859.5	4,921.0	0.00	0.00	0.00	
14,800.0	90.00	179.61	10,575.0	-4,979.7	860.2	5,020.9	0.00	0.00	0.00	
14,900.0	90.00	179.61	10,575.0	-5,079.7	860.9	5,120.8	0.00	0.00	0.00	
15,000.0	90.00	179.61	10,575.0	-5,179.7	861.5	5,220.7	0.00	0.00	0.00	
15,100.0	90.00	179.61	10,575.0	-5,279.7	862.2	5,320.5	0.00	0.00	0.00	
15,200.0	90.00	179.61	10,575.0	-5,379.7	862.9	5,420.4	0.00	0.00	0.00	
15,300.0	90.00	179.61	10,575.0	-5,479.7	863.6	5,520.3	0.00	0.00	0.00	
15,400.0	90.00	179.61	10,575.0	-5,579.7	864.2	5,620.1	0.00	0.00	0.00	
15,500.0	90.00	179.61	10,575.0	-5,679.7	864.9	5,720.0	0.00	0.00	0.00	
15,600.0	90.00	179.61	10,575.0	-5,779.7	865.6	5,819.9	0.00	0.00	0.00	
15,700.0	90.00	179.61	10,575.0	-5,879.7	866.3	5,919.8	0.00	0.00	0.00	
15,800.0	90.00	179.61	10,575.0	-5,979.7	866.9	6,019.6	0.00	0.00	0.00	
15,900.0	90.00	179.61	10,575.0	-6,079.7	867.6	6,119.5	0.00	0.00	0.00	
16,000.0	90.00	179.61	10,575.0	-6,179.7	868.3	6,219.4	0.00	0.00	0.00	
16,100.0	90.00	179.61	10,575.0	-6,279.7	869.0	6,319.2	0.00	0.00	0.00	
16,200.0	90.00	179.61	10,575.0	-6,379.7	869.7	6,419.1	0.00	0.00	0.00	
16,300.0	90.00	179.61	10,575.0	-6,479.7	870.3	6,519.0	0.00	0.00	0.00	
16,400.0	90.00	179.61	10,575.0	-6,579.7	871.0	6,618.9	0.00	0.00	0.00	
16,500.0	90.00	179.61	10,575.0	-6,679.7	871.7	6,718.7	0.00	0.00	0.00	
16,600.0	90.00	179.61	10,575.0	-6,779.7	872.4	6,818.6	0.00	0.00	0.00	
16,700.0	90.00	179.61	10,575.0	-6,879.7	873.0	6,918.5	0.00	0.00	0.00	
16,800.0	90.00	179.61	10,575.0	-6,979.7	873.7	7,018.3	0.00	0.00	0.00	
16,900.0	90.00	179.61	10,575.0	-7,079.7	874.4	7,118.2	0.00	0.00	0.00	
17,000.0	90.00	179.61	10,575.0	-7,179.7	875.1	7,218.1	0.00	0.00	0.00	
17,100.0	90.00	179.61	10,575.0	-7,279.7	875.7	7,318.0	0.00	0.00	0.00	
17,200.0	90.00	179.61	10,575.0	-7,379.7	876.4	7,417.8	0.00	0.00	0.00	
17,300.0	90.00	179.61	10,575.0	-7,479.7	877.1	7,517.7	0.00	0.00	0.00	
17,400.0	90.00	179.61	10,575.0	-7,579.7	877.8	7,617.6	0.00	0.00	0.00	
17,500.0	90.00	179.61	10,575.0	-7,679.7	878.5	7,717.4	0.00	0.00	0.00	
17,600.0	90.00	179.61	10,575.0	-7,779.7	879.1	7,817.3	0.00	0.00	0.00	
17,700.0	90.00	179.61	10,575.0	-7,879.6	879.8	7,917.2	0.00	0.00	0.00	
17,800.0	90.00	179.61	10,575.0	-7,979.6	880.5	8,017.1	0.00	0.00	0.00	
17,900.0	90.00	179.61	10,575.0	-8,079.6	881.2	8,116.9	0.00	0.00	0.00	
18,000.0	90.00	179.61	10,575.0	-8,179.6	881.8	8,216.8	0.00	0.00	0.00	
18,100.0	90.00	179.61	10,575.0	-8,279.6	882.5	8,316.7	0.00	0.00	0.00	
18,200.0	90.00	179.61	10,575.0	-8,379.6	883.2	8,416.5	0.00	0.00	0.00	
18,300.0	90.00	179.61	10,575.0	-8,479.6	883.9	8,516.4	0.00	0.00	0.00	
18,400.0	90.00	179.61	10,575.0	-8,579.6	884.5	8,616.3	0.00	0.00	0.00	
18,500.0	90.00	179.61	10,575.0	-8,679.6	885.2	8,716.2	0.00	0.00	0.00	
18,600.0	90.00	179.61	10,575.0	-8,779.6	885.9	8,816.0	0.00	0.00	0.00	
18,700.0	90.00	179.61	10,575.0	-8,879.6	886.6	8,915.9	0.00	0.00	0.00	
18,800.0	90.00	179.61	10,575.0	-8,979.6	887.3	9,015.8	0.00	0.00	0.00	
18,900.0	90.00	179.61	10,575.0	-9,079.6	887.9	9,115.6	0.00	0.00	0.00	
19,000.0	90.00	179.61	10,575.0	-9,179.6	888.6	9,215.5	0.00	0.00	0.00	
19,100.0	90.00	179.61	10,575.0	-9,279.6	889.3	9,315.4	0.00	0.00	0.00	
19,200.0	90.00	179.61	10,575.0	-9,379.6	890.0	9,415.3	0.00	0.00	0.00	
19,300.0	90.00	179.61	10,575.0	-9,479.6	890.6	9,515.1	0.00	0.00	0.00	
19,400.0	90.00	179.61	10,575.0	-9,579.6	891.3	9,615.0	0.00	0.00	0.00	
19,500.0	90.00	179.61	10,575.0	-9,679.6	892.0	9,714.9	0.00	0.00	0.00	
19,600.0	90.00	179.61	10,575.0	-9,779.6	892.7	9,814.7	0.00	0.00	0.00	
19,700.0	90.00	179.61	10,575.0	-9,879.6	893.3	9,914.6	0.00	0.00	0.00	

ConocoPhillips
Planning Report

Database:	EDT 17 Permian Prod	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 504H - Slot DONKEY POTROAST #504H
Company:	DELAWARE BASIN EAST	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Project:	ZEUS_NME	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site:	TARHEEL_DONKEY POTROAST PROJECT	North Reference:	Grid
Well:	_DONKEY POTROAST FED COM 504H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OWB		
Design:	PWP0		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
19,800.0	90.00	179.61	10,575.0	-9,979.6	894.0	10,014.5	0.00	0.00	0.00	
19,900.0	90.00	179.61	10,575.0	-10,079.6	894.7	10,114.4	0.00	0.00	0.00	
20,000.0	90.00	179.61	10,575.0	-10,179.6	895.4	10,214.2	0.00	0.00	0.00	
20,100.0	90.00	179.61	10,575.0	-10,279.6	896.1	10,314.1	0.00	0.00	0.00	
20,200.0	90.00	179.61	10,575.0	-10,379.6	896.7	10,414.0	0.00	0.00	0.00	
20,300.0	90.00	179.61	10,575.0	-10,479.6	897.4	10,513.8	0.00	0.00	0.00	
20,400.0	90.00	179.61	10,575.0	-10,579.6	898.1	10,613.7	0.00	0.00	0.00	
20,500.0	90.00	179.61	10,575.0	-10,679.6	898.8	10,713.6	0.00	0.00	0.00	
20,600.0	90.00	179.61	10,575.0	-10,779.6	899.4	10,813.5	0.00	0.00	0.00	
20,700.0	90.00	179.61	10,575.0	-10,879.6	900.1	10,913.3	0.00	0.00	0.00	
20,800.0	90.00	179.61	10,575.0	-10,979.6	900.8	11,013.2	0.00	0.00	0.00	
20,900.0	90.00	179.61	10,575.0	-11,079.6	901.5	11,113.1	0.00	0.00	0.00	
21,000.0	90.00	179.61	10,575.0	-11,179.6	902.1	11,212.9	0.00	0.00	0.00	
21,100.0	90.00	179.61	10,575.0	-11,279.6	902.8	11,312.8	0.00	0.00	0.00	
21,200.0	90.00	179.61	10,575.0	-11,379.6	903.5	11,412.7	0.00	0.00	0.00	
21,300.0	90.00	179.61	10,575.0	-11,479.6	904.2	11,512.6	0.00	0.00	0.00	
21,400.0	90.00	179.61	10,575.0	-11,579.6	904.9	11,612.4	0.00	0.00	0.00	
21,500.0	90.00	179.61	10,575.0	-11,679.6	905.5	11,712.3	0.00	0.00	0.00	
21,600.0	90.00	179.61	10,575.0	-11,779.6	906.2	11,812.2	0.00	0.00	0.00	
21,700.0	90.00	179.61	10,575.0	-11,879.6	906.9	11,912.0	0.00	0.00	0.00	
21,800.0	90.00	179.61	10,575.0	-11,979.6	907.6	12,011.9	0.00	0.00	0.00	
21,900.0	90.00	179.61	10,575.0	-12,079.6	908.2	12,111.8	0.00	0.00	0.00	
22,000.0	90.00	179.61	10,575.0	-12,179.6	908.9	12,211.7	0.00	0.00	0.00	
22,100.0	90.00	179.61	10,575.0	-12,279.5	909.6	12,311.5	0.00	0.00	0.00	
22,200.0	90.00	179.61	10,575.0	-12,379.5	910.3	12,411.4	0.00	0.00	0.00	
22,300.0	90.00	179.61	10,575.0	-12,479.5	911.0	12,511.3	0.00	0.00	0.00	
22,400.0	90.00	179.61	10,575.0	-12,579.5	911.6	12,611.1	0.00	0.00	0.00	
22,500.0	90.00	179.61	10,575.0	-12,679.5	912.3	12,711.0	0.00	0.00	0.00	
22,600.0	90.00	179.61	10,575.0	-12,779.5	913.0	12,810.9	0.00	0.00	0.00	
22,700.0	90.00	179.61	10,575.0	-12,879.5	913.7	12,910.8	0.00	0.00	0.00	
22,800.0	90.00	179.61	10,575.0	-12,979.5	914.3	13,010.6	0.00	0.00	0.00	
22,900.0	90.00	179.61	10,575.0	-13,079.5	915.0	13,110.5	0.00	0.00	0.00	
23,000.0	90.00	179.61	10,575.0	-13,179.5	915.7	13,210.4	0.00	0.00	0.00	
23,100.0	90.00	179.61	10,575.0	-13,279.5	916.4	13,310.2	0.00	0.00	0.00	
23,200.0	90.00	179.61	10,575.0	-13,379.5	917.0	13,410.1	0.00	0.00	0.00	
23,300.0	90.00	179.61	10,575.0	-13,479.5	917.7	13,510.0	0.00	0.00	0.00	
23,400.0	90.00	179.61	10,575.0	-13,579.5	918.4	13,609.9	0.00	0.00	0.00	
23,500.0	90.00	179.61	10,575.0	-13,679.5	919.1	13,709.7	0.00	0.00	0.00	
23,600.0	90.00	179.61	10,575.0	-13,779.5	919.8	13,809.6	0.00	0.00	0.00	
23,700.0	90.00	179.61	10,575.0	-13,879.5	920.4	13,909.5	0.00	0.00	0.00	
23,800.0	90.00	179.61	10,575.0	-13,979.5	921.1	14,009.3	0.00	0.00	0.00	
23,900.0	90.00	179.61	10,575.0	-14,079.5	921.8	14,109.2	0.00	0.00	0.00	
24,000.0	90.00	179.61	10,575.0	-14,179.5	922.5	14,209.1	0.00	0.00	0.00	
24,100.0	90.00	179.61	10,575.0	-14,279.5	923.1	14,309.0	0.00	0.00	0.00	
24,200.0	90.00	179.61	10,575.0	-14,379.5	923.8	14,408.8	0.00	0.00	0.00	
24,300.0	90.00	179.61	10,575.0	-14,479.5	924.5	14,508.7	0.00	0.00	0.00	
24,400.0	90.00	179.61	10,575.0	-14,579.5	925.2	14,608.6	0.00	0.00	0.00	
24,500.0	90.00	179.61	10,575.0	-14,679.5	925.8	14,708.4	0.00	0.00	0.00	
24,600.0	90.00	179.61	10,575.0	-14,779.5	926.5	14,808.3	0.00	0.00	0.00	
24,700.0	90.00	179.61	10,575.0	-14,879.5	927.2	14,908.2	0.00	0.00	0.00	
24,800.0	90.00	179.61	10,575.0	-14,979.5	927.9	15,008.1	0.00	0.00	0.00	
24,900.0	90.00	179.61	10,575.0	-15,079.5	928.6	15,107.9	0.00	0.00	0.00	
25,000.0	90.00	179.61	10,575.0	-15,179.5	929.2	15,207.8	0.00	0.00	0.00	

ConocoPhillips
Planning Report

Database:	EDT 17 Permian Prod	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 504H - Slot DONKEY POTROAST #504H
Company:	DELAWARE BASIN EAST	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Project:	ZEUS_NME	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site:	TARHEEL_DONKEY POTROAST PROJECT	North Reference:	Grid
Well:	_DONKEY POTROAST FED COM 504H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OWB		
Design:	PWP0		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
25,100.0	90.00	179.61	10,575.0	-15,279.5	929.9	15,307.7	0.00	0.00	0.00	
25,200.0	90.00	179.61	10,575.0	-15,379.5	930.6	15,407.5	0.00	0.00	0.00	
25,300.0	90.00	179.61	10,575.0	-15,479.5	931.3	15,507.4	0.00	0.00	0.00	
25,400.0	90.00	179.61	10,575.0	-15,579.5	931.9	15,607.3	0.00	0.00	0.00	
25,500.0	90.00	179.61	10,575.0	-15,679.5	932.6	15,707.2	0.00	0.00	0.00	
25,600.0	90.00	179.61	10,575.0	-15,779.5	933.3	15,807.0	0.00	0.00	0.00	
25,700.0	90.00	179.61	10,575.0	-15,879.5	934.0	15,906.9	0.00	0.00	0.00	
25,800.0	90.00	179.61	10,575.0	-15,979.5	934.6	16,006.8	0.00	0.00	0.00	
25,900.0	90.00	179.61	10,575.0	-16,079.5	935.3	16,106.6	0.00	0.00	0.00	
26,000.0	90.00	179.61	10,575.0	-16,179.5	936.0	16,206.5	0.00	0.00	0.00	
26,090.3	90.00	179.61	10,575.0	-16,269.7	936.6	16,296.7	0.00	0.00	0.00	





Design Targets										
Target Name - hit/miss target - Shape	Dip Angle (°)	Dip Dir. (°)	TVD (usft)	+N/-S (usft)	+E/-W (usft)	Northing (usft)	Easting (usft)	Latitude	Longitude	
LTP (DONKEY POTROAST) - plan misses target center by 40.3usft at 26000.0usft MD (10575.0 TVD, -16179.5 N, 936.0 E) - Circle (radius 50.0)	90.00	179.65	10,575.0	-16,219.7	936.3	554,485.81	712,754.64	32° 31' 20.989 N	103° 38' 35.090 W	
PBHL (DONKEY POTROAST) - plan hits target center - Rectangle (sides W100.0 H15,700.0 D20.0)	0.00	359.62	10,575.0	-16,269.7	936.6	554,435.82	712,754.96	32° 31' 20.494 N	103° 38' 35.090 W	
FTP (DONKEY POTROAST) - plan misses target center by 273.6usft at 10550.0usft MD (10395.1 TVD, -779.7 N, 831.7 E) - Circle (radius 50.0)	0.00	0.00	10,575.0	-573.6	830.7	570,131.91	712,649.03	32° 33' 55.816 N	103° 38' 35.139 W	

Casing Points					
Measured Depth (usft)	Vertical Depth (usft)	Name	Casing Diameter (")	Hole Diameter (")	
26,090.3	10,575.0	5-1/2" Production Casing	5-1/2	6-3/4	



Project: ZEUS_NME
Site: TARHEEL_DONKEY POTROAST PROJECT
Well: DONKEY POTROAST FED COM 504H
Wellbore: OWB
Design: PWP0

SECTION DETAILS								
MD	Inc	Azi	TVD	+N/-S	+E/-W	Dleg	TFace	VSect
0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.0
1500.0	0.00	0.00	1500.0	0.0	0.0	0.00	0.00	0.0
2183.7	13.67	126.90	2177.2	-48.7	64.9	2.00	126.90	52.4
5547.4	13.67	126.90	5445.6	-526.1	700.8	0.00	0.00	565.5
6914.7	0.00	0.00	6800.0	-623.6	830.7	1.00	180.00	670.3
10116.7	0.00	0.00	10002.0	-623.6	830.7	0.00	0.00	670.3
11016.7	90.00	179.61	10575.0	-1196.5	834.6	10.00	179.61	1242.5
26090.3	90.00	179.61	10575.0	-16269.7	936.6	0.00	0.00	16296.7

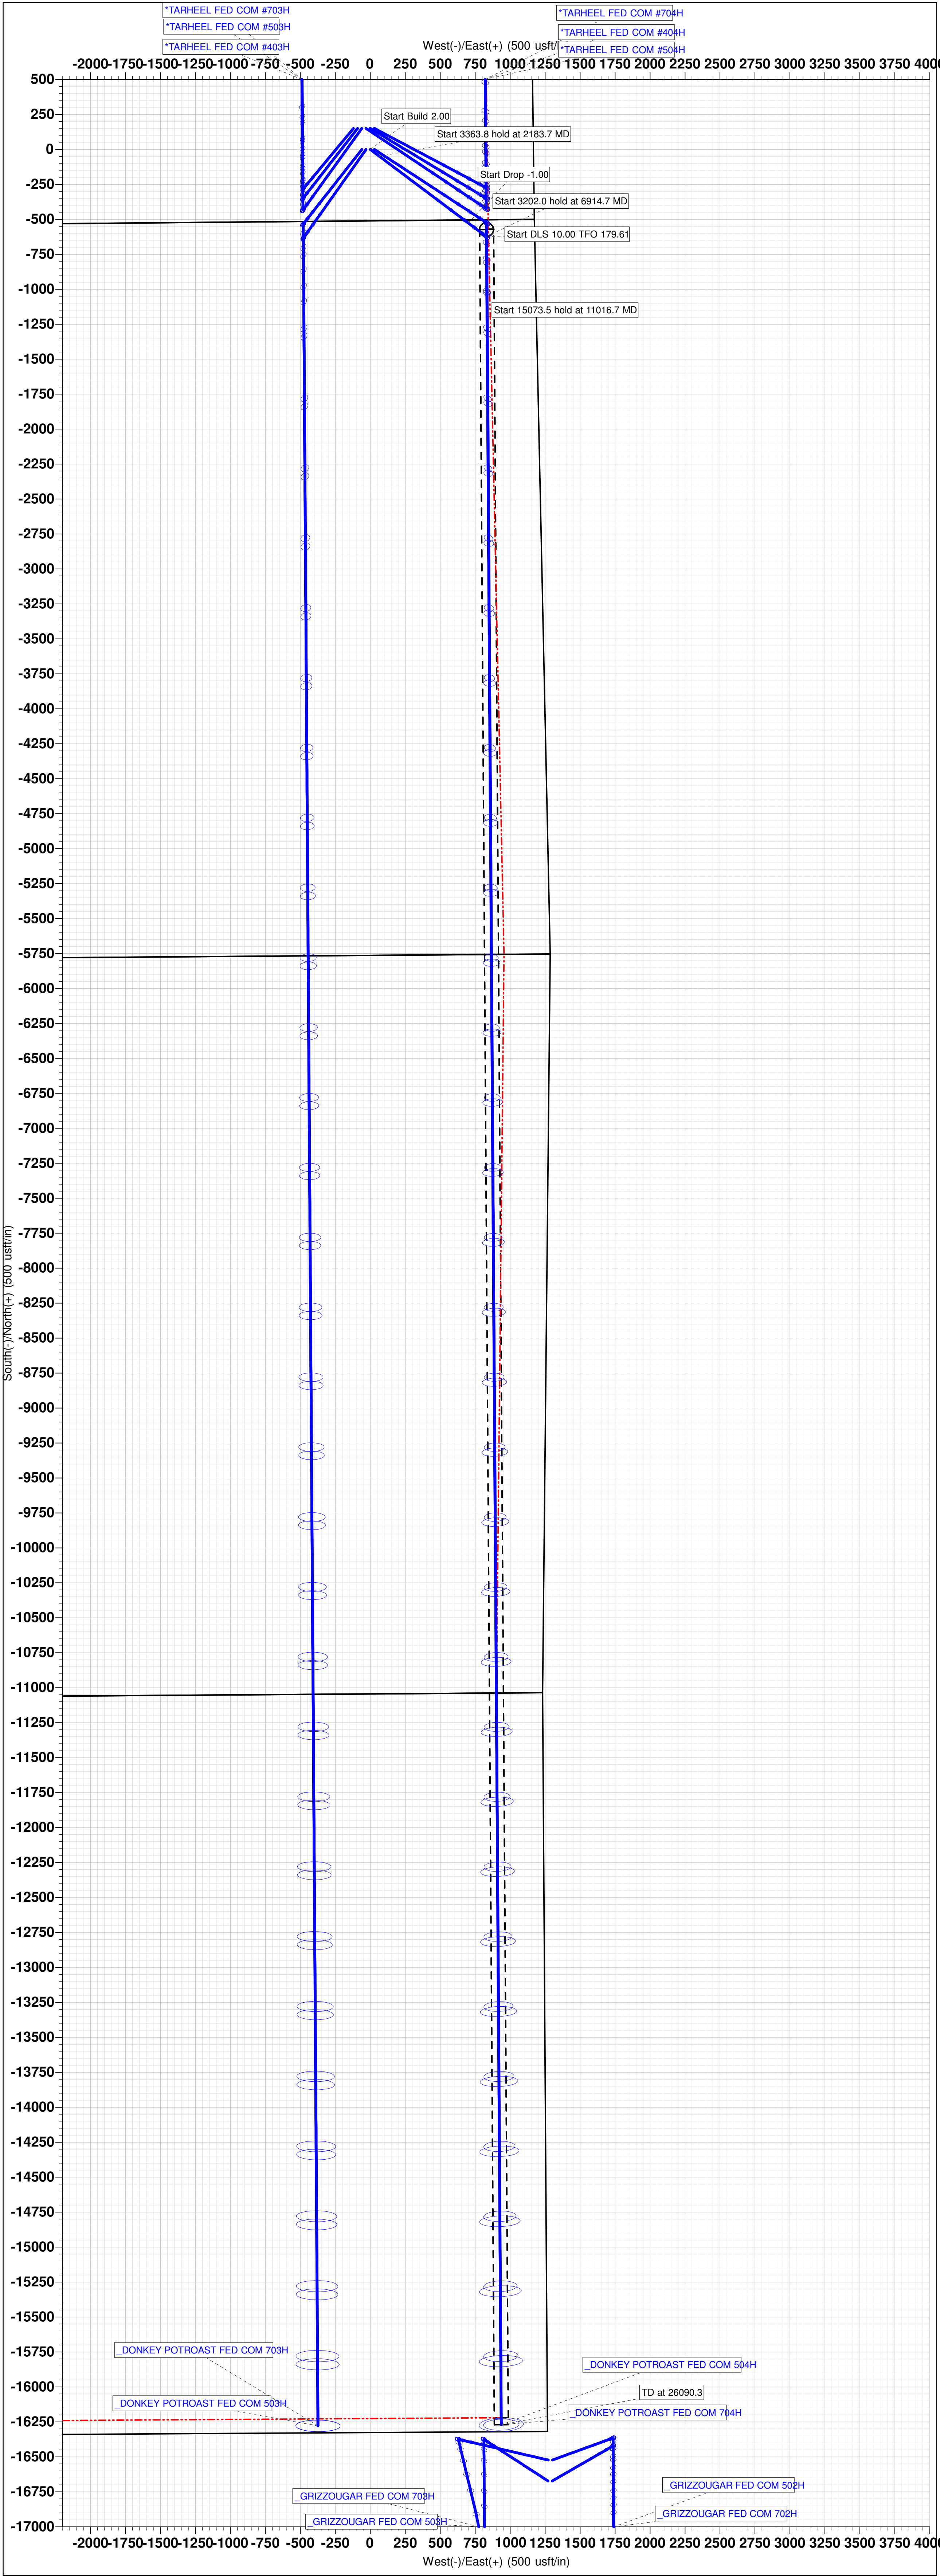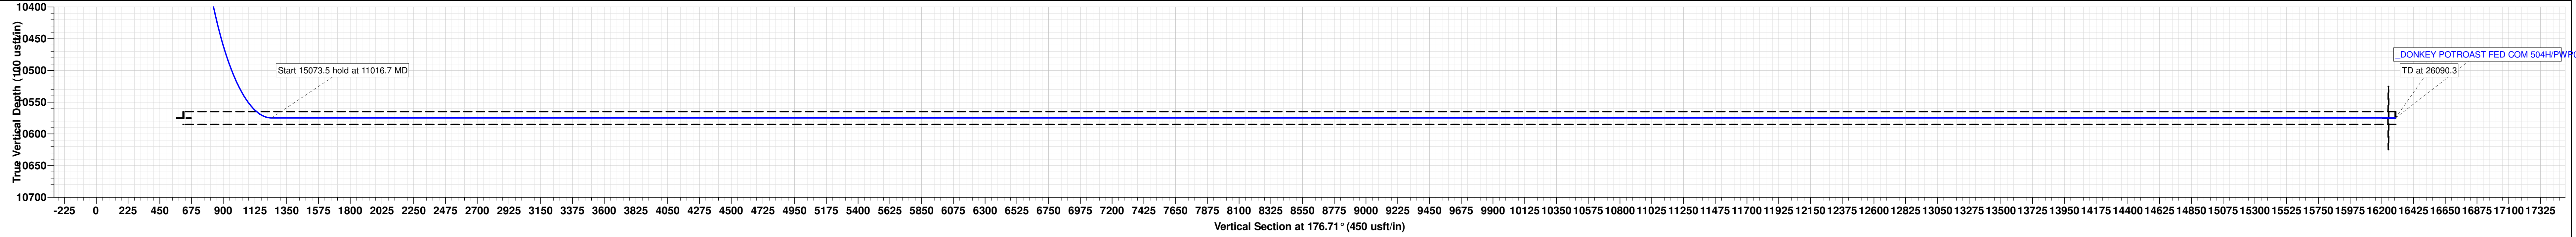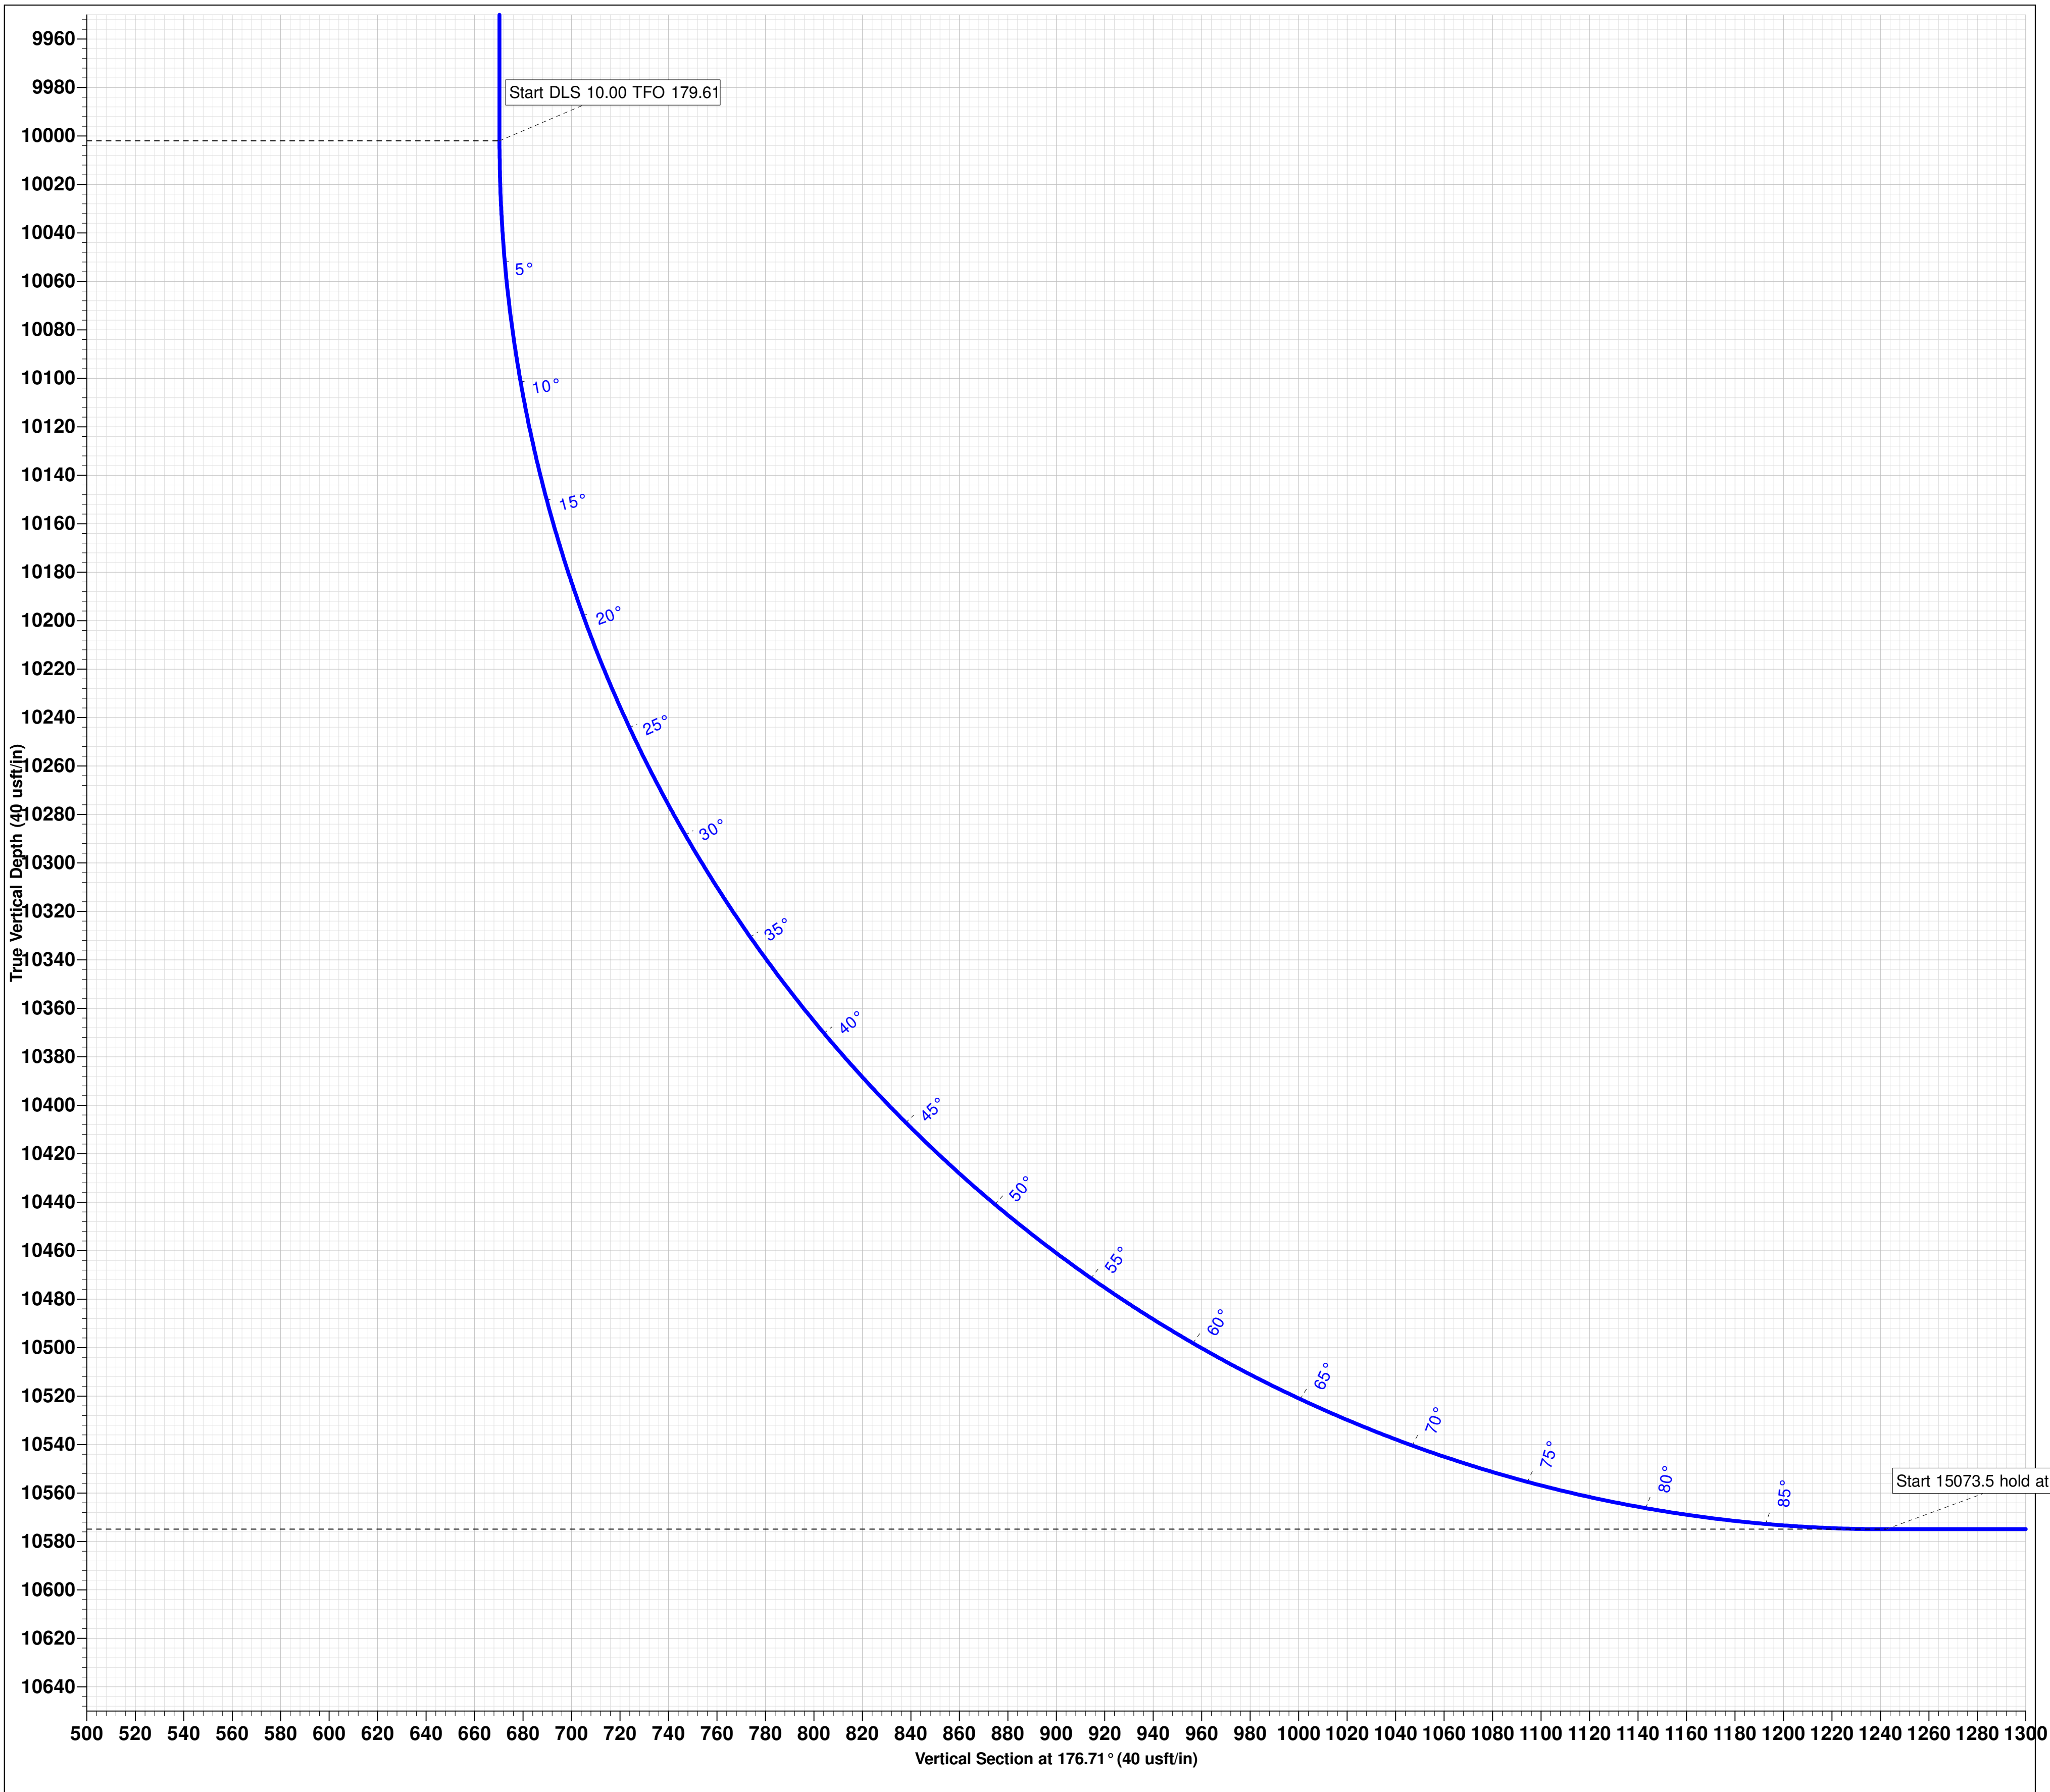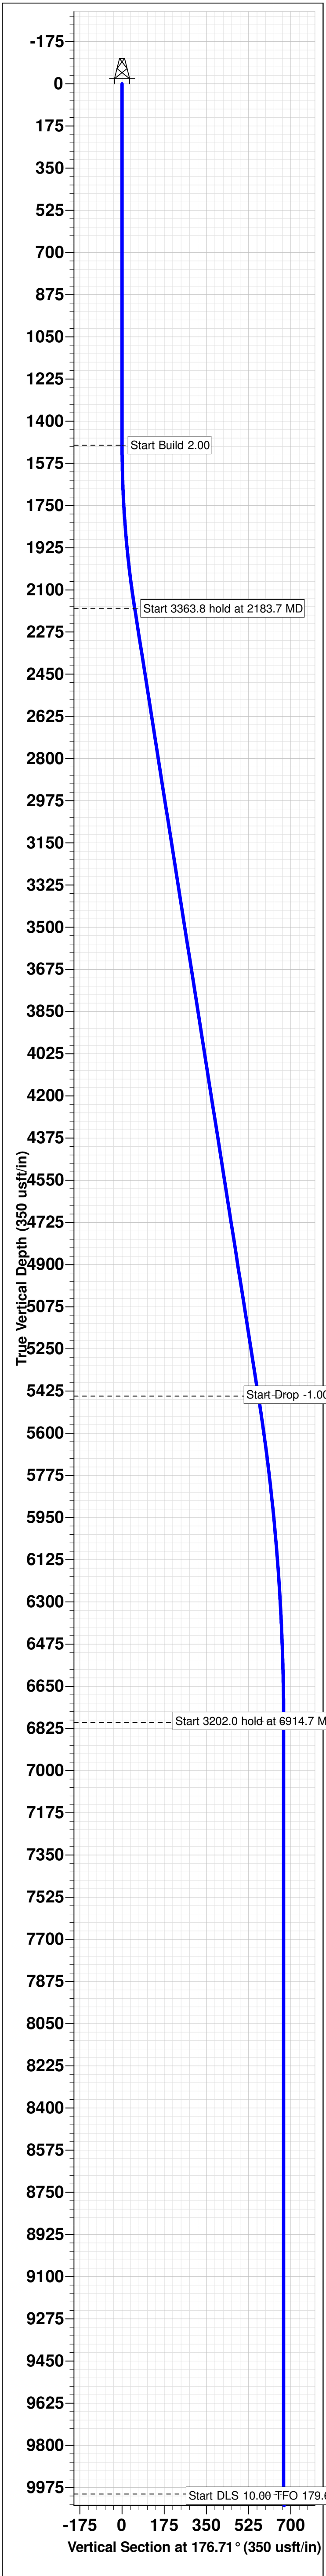

DELAWARE BASIN EAST

ZEUS_NME

TARHEEL_DONKEY POTROAST PROJECT

_DONKEY POTROAST FED COM 504H

OWB

PWP0

Anticollision Report

22 July, 2024

ConocoPhillips
Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 504H - Slot DONKEY POTROAST #504H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 504H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Reference	PWP0		
Filter type:	NO GLOBAL FILTER: Using user defined selection & filtering criteria		
Interpolation Method:	Stations	Error Model:	ISCWSA
Depth Range:	Unlimited	Scan Method:	Closest Approach 3D
Results Limited by:	Max. Cent. Dist. of 1,000.0usft or Max. SF of 2	Error Surface:	Combined Pedal Curve
Warning Levels Evaluated at:	2.79 Sigma	Casing Method:	Added to Error Values

Survey Tool Program		Date	7/22/2024		
From (usft)	To (usft)	Survey (Wellbore)	Tool Name	Description	
0.0	26,090.3	PWP0 (OWB)	r.5 MWD+IFR1+MS	OWSG MWD + IFR1 + Multi-Station Correc	

Summary						
	Reference Measured Depth (usft)	Offset Measured Depth (usft)	Distance Between Centres (usft)	Distance Between Ellipses (usft)	Separation Factor	Warning
Site Name Offset Well - Wellbore - Design						
GRIZZOUGAR FEDERAL PROJECT						
_GRIZZOUGAR FED COM 502H - OWB - PWP0	26,090.3	10,485.0	869.5	691.2	4.875	CC, ES, SF
_GRIZZOUGAR FED COM 503H - OWB - PWP0A	26,090.3	10,508.1	329.0	187.9	2.333	Caution - Monitor Closely, CC, ES, SF
_GRIZZOUGAR FED COM 702H - OWB - PWP0	26,090.3	10,675.3	805.2	627.1	4.520	CC, ES, SF
_GRIZZOUGAR FED COM 703H - OWB - PWP0A	26,090.3	10,698.9	324.3	150.7	1.868	Caution - Monitor Closely, CC, ES, SF
TARHEEL_DONKEY POTROAST PROJECT						
*TARHEEL FED COM #403H - OWB - PWP0	1,500.0	1,500.0	192.2	180.5	16.382	CC, ES
*TARHEEL FED COM #403H - OWB - PWP0	1,700.0	1,702.2	197.8	185.4	15.955	SF
*TARHEEL FED COM #404H - OWB - PWP0	1,500.0	1,500.0	153.7	141.9	13.096	CC
*TARHEEL FED COM #404H - OWB - PWP0	1,600.0	1,601.6	153.9	141.9	12.806	ES
*TARHEEL FED COM #404H - OWB - PWP0	9,011.8	8,989.4	350.0	311.5	9.104	SF
*TARHEEL FED COM #503H - OWB - PWP0	1,500.0	1,500.0	175.1	163.3	14.920	CC, ES
*TARHEEL FED COM #503H - OWB - PWP0	1,700.0	1,703.9	179.3	166.9	14.459	SF
*TARHEEL FED COM #504H - OWB - PWP0	1,500.0	1,500.0	150.7	138.9	12.840	CC
*TARHEEL FED COM #504H - OWB - PWP0	1,600.0	1,602.8	150.8	138.7	12.514	ES
*TARHEEL FED COM #504H - OWB - PWP0	9,900.0	9,892.0	274.3	234.2	6.843	SF
*TARHEEL FED COM #703H - OWB - PWP0	1,500.0	1,500.0	161.9	150.2	13.801	CC, ES
*TARHEEL FED COM #703H - OWB - PWP0	1,800.0	1,807.6	168.2	155.4	13.199	SF
*TARHEEL FED COM #704H - OWB - PWP0	1,500.0	1,500.0	153.2	141.5	13.056	CC
*TARHEEL FED COM #704H - OWB - PWP0	2,100.0	2,123.4	153.9	140.0	11.100	ES
*TARHEEL FED COM #704H - OWB - PWP0	10,116.7	10,110.2	200.0	158.4	4.804	SF
_DONKEY POTROAST FED COM 503H - OWB - PWP0	1,500.0	1,500.0	30.1	18.4	2.564	Normal Operations, CC, ES, SF
_DONKEY POTROAST FED COM 703H - OWB - PWP0	1,500.0	1,500.0	60.0	48.3	5.113	CC, ES, SF
_DONKEY POTROAST FED COM 704H - OWB - PWP0	1,500.0	1,500.0	30.0	18.3	2.557	Normal Operations, CC
_DONKEY POTROAST FED COM 704H - OWB - PWP0	1,800.0	1,797.4	30.5	17.7	2.386	Caution - Monitor Closely, ES
_DONKEY POTROAST FED COM 704H - OWB - PWP0	2,100.0	2,094.8	32.1	18.3	2.316	Caution - Monitor Closely, SF

Offset Design: GRIZZOUGAR FEDERAL PROJECT - _GRIZZOUGAR FED COM 502H - OWB - PWP0												Offset Site Error: 0.0 usft	
Survey Program: 0-r.5 MWD+IFR1+MS												Offset Well Error: 0.0 usft	
Reference		Offset		Semi Major Axis		Offset Wellbore Centre		Rule Assigned:					
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	No-Go Distance (usft)	Separation Factor	Warning
25,800.0	10,575.0	10,400.0	10,356.3	124.9	21.6	-70.12	-16,482.1	1,736.6	989.5	827.3	162.18	6.101	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 504H - Slot DONKEY POTROAST #504H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 504H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design:	GRIZZOUGAR FEDERAL PROJECT - _GRIZZOUGAR FED COM 502H - OWB - PWP0												Offset Site Error:	0.0 usft
Survey Program:	0-r.5 MWD+IFR1+MS												Offset Well Error:	0.0 usft
Reference	Offset	Semi Major Axis		Offset Wellbore Centre		Rule Assigned:								
Measured Depth	Vertical Depth	Measured Depth	Vertical Depth	Reference	Offset	Highside Toolface	+N/-S	+E/-W	Between Centres	Between Ellipses	No-Go Distance	Separation Factor	Warning	
(usft)	(usft)	(usft)	(usft)	(usft)	(usft)	(°)	(usft)	(usft)	(usft)	(usft)	(usft)			
25,900.0	10,575.0	10,425.0	10,377.8	125.6	21.5	-71.50	-16,494.9	1,736.7	941.4	773.0	168.41	5.590		
26,000.0	10,575.0	10,450.0	10,398.5	126.4	21.5	-72.85	-16,508.8	1,736.7	900.2	725.9	174.32	5.164		
26,090.3	10,575.0	10,485.0	10,426.3	127.1	21.4	-74.68	-16,530.1	1,736.9	869.5	691.2	178.35	4.875 CC, ES, SF		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 504H - Slot DONKEY POTROAST #504H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 504H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design:	GRIZZOUGAR FEDERAL PROJECT - _GRIZZOUGAR FED COM 503H - OWB - PWP0A											Offset Site Error:	0.0 usft
Survey Program:	0-r.5 MWD+IFR1+MS											Offset Well Error:	0.0 usft
Reference	Vertical	Offset	Semi Major Axis		Highside Toolface (°)	Offset Wellbore Centre		Rule Assigned:		No-Go Distance (usft)	Separation Factor	Warning	
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference Offset (usft)		+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)				
25,300.0	10,575.0	10,325.0	10,285.4	121.1	22.7	19.10	-16,403.5	813.0	998.5	903.5	95.05	10.505	
25,400.0	10,575.0	10,350.0	10,308.7	121.9	22.7	20.32	-16,412.6	813.1	906.3	809.2	97.08	9.335	
25,500.0	10,575.0	10,359.0	10,316.9	122.6	22.6	20.78	-16,416.2	813.1	815.3	713.5	101.73	8.014	
25,600.0	10,575.0	10,375.0	10,331.4	123.4	22.6	21.66	-16,423.0	813.1	725.8	619.5	106.37	6.823	
25,700.0	10,575.0	10,400.0	10,353.6	124.1	22.5	23.14	-16,434.5	813.2	638.4	527.7	110.64	5.770	
25,800.0	10,575.0	10,416.5	10,367.9	124.9	22.5	24.20	-16,442.7	813.2	553.3	435.5	117.77	4.698	
25,900.0	10,575.0	10,442.8	10,390.1	125.6	22.4	26.04	-16,456.9	813.3	471.5	346.6	124.83	3.777	
26,000.0	10,575.0	10,475.0	10,416.1	126.4	22.4	28.56	-16,475.8	813.4	394.0	261.2	132.73	2.968	Normal Operations
26,090.3	10,575.0	10,508.1	10,441.5	127.1	22.3	31.48	-16,497.0	813.6	329.0	187.9	141.03	2.333	Caution - Monitor Closely, CC, ES, SF

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips
Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 504H - Slot DONKEY POTROAST #504H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 504H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design: GRIZZOUGAR FEDERAL PROJECT - _GRIZZOUGAR FED COM 702H - OWB - PWP0													Offset Site Error: 0.0 usft	
Survey Program: 0-r.5 MWD+IFR1+MS		Offset		Semi Major Axis		Offset Wellbore Centre			Rule Assigned: Distance			Offset Well Error: 0.0 usft		
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	No-Go Distance (usft)	Separation Factor	Warning	
25,600.0	10,575.0	10,675.3	10,645.0	123.4	21.3	-90.00	-16,364.5	1,736.2	993.4	851.3	142.12	6.990		
25,700.0	10,575.0	10,675.3	10,645.0	124.1	21.3	-90.00	-16,364.5	1,736.2	937.5	786.9	150.57	6.226		
25,800.0	10,575.0	10,675.3	10,645.0	124.9	21.3	-90.00	-16,364.5	1,736.2	889.2	730.3	158.98	5.594		
25,900.0	10,575.0	10,675.3	10,645.0	125.6	21.3	-90.00	-16,364.5	1,736.2	850.1	683.2	166.85	5.095		
26,000.0	10,575.0	10,675.3	10,645.0	126.4	21.3	-90.00	-16,364.5	1,736.2	821.3	647.8	173.58	4.732		
26,090.3	10,575.0	10,675.3	10,645.0	127.1	21.3	-90.00	-16,364.5	1,736.2	805.2	627.1	178.14	4.520 CC, ES, SF		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 504H - Slot DONKEY POTROAST #504H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 504H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design:	GRIZZOUGAR FEDERAL PROJECT - _GRIZZOUGAR FED COM 703H - OWB - PWP0A											Offset Site Error:	0.0 usft
Survey Program:	0-r.5 MWD+IFR1+MS											Offset Well Error:	0.0 usft
Reference	Offset	Semi Major Axis		Offset Wellbore Centre		Rule Assigned:		Distance		Warning			
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	No-Go Distance (usft)	Separation Factor	
25,300.0	10,575.0	10,698.9	10,645.0	121.1	23.8	90.00	-16,373.8	629.5	943.9	862.7	81.24	11.619	
25,400.0	10,575.0	10,698.9	10,645.0	121.9	23.8	90.00	-16,373.8	629.5	850.0	764.2	85.78	9.909	
25,500.0	10,575.0	10,698.9	10,645.0	122.6	23.8	90.00	-16,373.8	629.5	757.6	666.1	91.57	8.274	
25,600.0	10,575.0	10,698.9	10,645.0	123.4	23.8	90.00	-16,373.8	629.5	667.5	568.4	99.08	6.737	
25,700.0	10,575.0	10,698.9	10,645.0	124.1	23.8	90.00	-16,373.8	629.5	580.6	471.7	108.90	5.332	
25,800.0	10,575.0	10,698.9	10,645.0	124.9	23.8	90.00	-16,373.8	629.5	498.6	376.9	121.77	4.095	
25,900.0	10,575.0	10,698.9	10,645.0	125.6	23.8	90.00	-16,373.8	629.5	424.5	286.2	138.24	3.071	
26,000.0	10,575.0	10,698.9	10,645.0	126.4	23.8	90.00	-16,373.8	629.5	362.9	205.4	157.51	2.304	Caution - Monitor Closely
26,090.3	10,575.0	10,698.9	10,645.0	127.1	23.8	90.00	-16,373.8	629.5	324.3	150.7	173.62	1.868	Caution - Monitor Closely, CC, ES, SF

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips
Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 504H - Slot DONKEY POTROAST #504H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 504H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design: TARHEEL_DONKEY POTROAST PROJECT - *TARHEEL FED COM #403H - OWB - PWP0													Offset Site Error:	0.0 usft
Survey Program: 0-r.5 MWD+IFR1													Offset Well Error:	3.0 usft
Reference	Offset	Semi Major Axis		Rule Assigned:		Distance		No-Go		Separation		Warning		
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Distance (usft)	Factor		
0.0	0.0	0.0	0.0	3.0	3.0	-38.84	149.7	-120.5	192.2	185.8	6.43	29.902		
100.0	100.0	100.0	100.0	3.2	3.2	-38.84	149.7	-120.5	192.2	185.3	6.89	27.892		
200.0	200.0	200.0	200.0	3.5	3.5	-38.84	149.7	-120.5	192.2	184.9	7.33	26.233		
300.0	300.0	300.0	300.0	3.7	3.7	-38.84	149.7	-120.5	192.2	184.5	7.74	24.833		
400.0	400.0	400.0	400.0	3.9	3.9	-38.84	149.7	-120.5	192.2	184.1	8.14	23.630		
500.0	500.0	500.0	500.0	4.1	4.1	-38.84	149.7	-120.5	192.2	183.7	8.51	22.580		
600.0	600.0	600.0	600.0	4.2	4.2	-38.84	149.7	-120.5	192.2	183.4	8.88	21.654		
700.0	700.0	700.0	700.0	4.4	4.4	-38.84	149.7	-120.5	192.2	183.0	9.23	20.829		
800.0	800.0	800.0	800.0	4.6	4.6	-38.84	149.7	-120.5	192.2	182.7	9.57	20.087		
900.0	900.0	900.0	900.0	4.8	4.8	-38.84	149.7	-120.5	192.2	182.3	9.90	19.414		
1,000.0	1,000.0	1,000.0	1,000.0	4.9	4.9	-38.84	149.7	-120.5	192.2	182.0	10.22	18.801		
1,100.0	1,100.0	1,100.0	1,100.0	5.1	5.1	-38.84	149.7	-120.5	192.2	181.7	10.54	18.240		
1,200.0	1,200.0	1,200.0	1,200.0	5.2	5.2	-38.84	149.7	-120.5	192.2	181.4	10.85	17.722		
1,300.0	1,300.0	1,300.0	1,300.0	5.4	5.4	-38.84	149.7	-120.5	192.2	181.1	11.15	17.243		
1,400.0	1,400.0	1,400.0	1,400.0	5.5	5.5	-38.84	149.7	-120.5	192.2	180.8	11.44	16.798		
1,500.0	1,500.0	1,500.0	1,500.0	5.7	5.7	-38.84	149.7	-120.5	192.2	180.5	11.73	16.382 CC, ES		
1,600.0	1,600.0	1,601.3	1,601.3	5.9	5.9	-166.37	148.4	-121.7	193.6	181.5	12.08	16.031		
1,700.0	1,699.8	1,702.2	1,702.0	6.1	6.1	-168.24	144.3	-125.1	197.8	185.4	12.40	15.955 SF		
1,800.0	1,799.5	1,802.3	1,801.7	6.3	6.3	-171.14	137.5	-130.7	205.2	192.5	12.74	16.115		
1,900.0	1,898.7	1,901.2	1,899.9	6.6	6.6	-174.82	128.2	-138.5	216.4	203.4	13.10	16.527		
2,000.0	1,997.5	1,998.7	1,996.2	6.9	6.8	-178.96	116.5	-148.2	232.0	218.6	13.46	17.236		
2,100.0	2,095.6	2,095.3	2,091.4	7.2	7.1	177.14	103.8	-158.7	252.2	238.3	13.93	18.101		
2,183.7	2,177.2	2,175.5	2,170.4	7.4	7.3	174.35	93.3	-167.5	272.5	258.2	14.26	19.111		
2,200.0	2,193.1	2,191.1	2,185.8	7.4	7.3	173.86	91.3	-169.2	276.7	262.4	14.31	19.340		
2,300.0	2,290.2	2,286.7	2,279.9	7.7	7.6	171.18	78.8	-179.5	303.1	288.4	14.72	20.591		
2,400.0	2,387.4	2,382.2	2,374.1	8.0	7.8	168.92	66.3	-189.9	330.0	314.9	15.13	21.811		
2,500.0	2,484.6	2,477.8	2,468.3	8.3	8.1	167.00	53.8	-200.3	357.3	341.7	15.56	22.959		
2,600.0	2,581.7	2,573.3	2,562.4	8.6	8.4	165.35	41.3	-210.7	384.9	368.9	16.02	24.033		
2,700.0	2,678.9	2,668.9	2,656.6	9.0	8.7	163.92	28.8	-221.1	412.8	396.3	16.49	25.035		
2,800.0	2,776.1	2,764.4	2,750.7	9.3	9.0	162.67	16.3	-231.5	440.9	424.0	16.98	25.966		
2,900.0	2,873.2	2,860.0	2,844.9	9.7	9.3	161.57	3.7	-241.9	469.2	451.7	17.49	26.830		
3,000.0	2,970.4	2,955.5	2,939.0	10.1	9.6	160.60	-8.8	-252.3	497.6	479.6	18.01	27.630		
3,100.0	3,067.6	3,051.0	3,033.2	10.4	10.0	159.72	-21.3	-262.7	526.2	507.6	18.55	28.372		
3,200.0	3,164.7	3,146.6	3,127.3	10.8	10.3	158.94	-33.8	-273.1	554.8	535.7	19.09	29.058		
3,300.0	3,261.9	3,242.1	3,221.5	11.2	10.7	158.24	-46.3	-283.5	583.5	563.9	19.65	29.693		
3,400.0	3,359.1	3,337.7	3,315.7	11.6	11.0	157.60	-58.8	-293.9	612.3	592.1	20.22	30.282		
3,500.0	3,456.2	3,433.2	3,409.8	12.1	11.4	157.02	-71.3	-304.3	641.2	620.4	20.80	30.828		
3,600.0	3,553.4	3,528.8	3,504.0	12.5	11.8	156.48	-83.8	-314.7	670.1	648.7	21.39	31.334		
3,700.0	3,650.6	3,624.3	3,598.1	12.9	12.1	156.00	-96.3	-325.1	699.1	677.1	21.98	31.804		
3,800.0	3,747.7	3,719.9	3,692.3	13.3	12.5	155.55	-108.8	-335.5	728.1	705.5	22.58	32.241		
3,900.0	3,844.9	3,815.4	3,786.4	13.8	12.9	155.13	-121.3	-345.9	757.1	733.9	23.19	32.647		
4,000.0	3,942.1	3,911.0	3,880.6	14.2	13.3	154.75	-133.8	-356.3	786.2	762.4	23.81	33.026		
4,100.0	4,039.2	4,006.5	3,974.7	14.6	13.7	154.39	-146.3	-366.7	815.3	790.9	24.43	33.379		
4,200.0	4,136.4	4,102.1	4,068.9	15.1	14.1	154.06	-158.8	-377.0	844.5	819.4	25.05	33.709		
4,300.0	4,233.6	4,197.6	4,163.0	15.5	14.4	153.75	-171.3	-387.4	873.6	848.0	25.68	34.017		
4,400.0	4,330.7	4,293.2	4,257.2	16.0	14.8	153.46	-183.8	-397.8	902.8	876.5	26.32	34.305		
4,500.0	4,427.9	4,388.7	4,351.4	16.4	15.2	153.19	-196.3	-408.2	932.0	905.1	26.96	34.575		
4,600.0	4,525.0	4,484.3	4,445.5	16.9	15.6	152.93	-208.8	-418.6	961.3	933.7	27.60	34.828		
4,700.0	4,622.2	4,581.2	4,541.0	17.3	16.0	152.69	-221.5	-429.2	990.5	962.2	28.23	35.081		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 504H - Slot DONKEY POTROAST #504H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 504H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design: TARHEEL_DONKEY POTROAST PROJECT - *TARHEEL FED COM #404H - OWB - PWP0													Offset Site Error:	0.0 usft
Survey Program: 0-r.5 MWD+IFR1													Offset Well Error:	3.0 usft
Reference		Offset		Semi Major Axis		Highside Toolface (")	Offset Wellbore Centre		Distance		No-Go Distance (usft)	Separation Factor	Warning	
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)		+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)				
0.0	0.0	0.0	0.0	3.0	3.0	10.94	150.9	29.2	153.7	147.2	6.43	23.903		
100.0	100.0	100.0	100.0	3.2	3.2	10.94	150.9	29.2	153.7	146.8	6.89	22.296		
200.0	200.0	200.0	200.0	3.5	3.5	10.94	150.9	29.2	153.7	146.3	7.33	20.970		
300.0	300.0	300.0	300.0	3.7	3.7	10.94	150.9	29.2	153.7	145.9	7.74	19.851		
400.0	400.0	400.0	400.0	3.9	3.9	10.94	150.9	29.2	153.7	145.5	8.14	18.889		
500.0	500.0	500.0	500.0	4.1	4.1	10.94	150.9	29.2	153.7	145.2	8.51	18.050		
600.0	600.0	600.0	600.0	4.2	4.2	10.94	150.9	29.2	153.7	144.8	8.88	17.310		
700.0	700.0	700.0	700.0	4.4	4.4	10.94	150.9	29.2	153.7	144.4	9.23	16.650		
800.0	800.0	800.0	800.0	4.6	4.6	10.94	150.9	29.2	153.7	144.1	9.57	16.057		
900.0	900.0	900.0	900.0	4.8	4.8	10.94	150.9	29.2	153.7	143.8	9.90	15.519		
1,000.0	1,000.0	1,000.0	1,000.0	4.9	4.9	10.94	150.9	29.2	153.7	143.4	10.22	15.029		
1,100.0	1,100.0	1,100.0	1,100.0	5.1	5.1	10.94	150.9	29.2	153.7	143.1	10.54	14.580		
1,200.0	1,200.0	1,200.0	1,200.0	5.2	5.2	10.94	150.9	29.2	153.7	142.8	10.85	14.166		
1,300.0	1,300.0	1,300.0	1,300.0	5.4	5.4	10.94	150.9	29.2	153.7	142.5	11.15	13.783		
1,400.0	1,400.0	1,400.0	1,400.0	5.5	5.5	10.94	150.9	29.2	153.7	142.2	11.44	13.427		
1,500.0	1,500.0	1,500.0	1,500.0	5.7	5.7	10.94	150.9	29.2	153.7	141.9	11.73	13.096 CC		
1,600.0	1,600.0	1,601.6	1,601.6	5.9	5.9	-115.90	150.0	30.8	153.9	141.9	12.02	12.806 ES		
1,700.0	1,699.8	1,703.2	1,703.0	6.1	6.1	-115.75	147.5	35.5	154.7	142.4	12.28	12.597		
1,800.0	1,799.5	1,804.8	1,804.2	6.3	6.4	-115.49	143.3	43.5	155.9	143.3	12.54	12.432		
1,900.0	1,898.7	1,906.3	1,904.9	6.6	6.6	-115.14	137.4	54.6	157.6	144.8	12.80	12.308		
2,000.0	1,997.5	2,007.8	2,005.2	6.9	6.9	-114.70	129.8	68.8	159.8	146.7	13.08	12.219		
2,100.0	2,095.6	2,109.3	2,104.7	7.2	7.2	-114.18	120.6	86.2	162.5	149.2	13.36	12.169		
2,183.7	2,177.2	2,193.3	2,186.7	7.4	7.4	-113.92	112.1	102.3	165.4	151.8	13.54	12.215		
2,200.0	2,193.1	2,209.6	2,202.6	7.4	7.4	-113.96	110.4	105.4	166.0	152.4	13.57	12.233		
2,300.0	2,290.2	2,309.5	2,300.1	7.7	7.7	-114.15	100.2	124.7	170.0	156.1	13.91	12.216		
2,400.0	2,387.4	2,409.4	2,397.6	8.0	8.0	-114.33	90.0	144.0	173.9	159.7	14.24	12.214		
2,500.0	2,484.6	2,509.3	2,495.1	8.3	8.3	-114.50	79.7	163.2	177.9	163.3	14.58	12.200		
2,600.0	2,581.7	2,609.3	2,592.6	8.6	8.6	-114.67	69.5	182.5	181.9	166.9	14.94	12.176		
2,700.0	2,678.9	2,709.2	2,690.2	9.0	8.9	-114.83	59.3	201.7	185.9	170.6	15.30	12.144		
2,800.0	2,776.1	2,809.1	2,787.7	9.3	9.3	-114.98	49.1	221.0	189.8	174.1	15.68	12.104		
2,900.0	2,873.2	2,909.0	2,885.2	9.7	9.6	-115.13	38.9	240.2	193.8	177.7	16.07	12.058		
3,000.0	2,970.4	3,008.9	2,982.7	10.1	10.0	-115.27	28.7	259.5	197.8	181.3	16.47	12.006		
3,100.0	3,067.6	3,108.9	3,080.2	10.4	10.4	-115.41	18.4	278.8	201.8	184.9	16.88	11.951		
3,200.0	3,164.7	3,208.8	3,177.7	10.8	10.8	-115.54	8.2	298.0	205.7	188.4	17.30	11.892		
3,300.0	3,261.9	3,308.7	3,275.2	11.2	11.2	-115.66	-2.0	317.3	209.7	192.0	17.73	11.830		
3,400.0	3,359.1	3,408.6	3,372.7	11.6	11.6	-115.78	-12.2	336.5	213.7	195.5	18.16	11.766		
3,500.0	3,456.2	3,508.5	3,470.3	12.1	12.0	-115.90	-22.4	355.8	217.7	199.1	18.60	11.700		
3,600.0	3,553.4	3,608.5	3,567.8	12.5	12.4	-116.01	-32.7	375.0	221.7	202.6	19.05	11.633		
3,700.0	3,650.6	3,708.4	3,665.3	12.9	12.8	-116.12	-42.9	394.3	225.6	206.1	19.51	11.565		
3,800.0	3,747.7	3,808.3	3,762.8	13.3	13.2	-116.22	-53.1	413.5	229.6	209.6	19.97	11.496		
3,900.0	3,844.9	3,908.2	3,860.3	13.8	13.7	-116.32	-63.3	432.8	233.6	213.2	20.44	11.428		
4,000.0	3,942.1	4,008.1	3,957.8	14.2	14.1	-116.42	-73.5	452.1	237.6	216.7	20.91	11.360		
4,100.0	4,039.2	4,108.1	4,055.3	14.6	14.5	-116.52	-83.7	471.3	241.6	220.2	21.39	11.292		
4,200.0	4,136.4	4,208.0	4,152.9	15.1	15.0	-116.61	-94.0	490.6	245.6	223.7	21.88	11.224		
4,300.0	4,233.6	4,307.9	4,250.4	15.5	15.4	-116.69	-104.2	509.8	249.5	227.2	22.37	11.157		
4,400.0	4,330.7	4,407.8	4,347.9	16.0	15.8	-116.78	-114.4	529.1	253.5	230.7	22.86	11.091		
4,500.0	4,427.9	4,507.7	4,445.4	16.4	16.3	-116.86	-124.6	548.3	257.5	234.2	23.36	11.026		
4,600.0	4,525.0	4,607.7	4,542.9	16.9	16.7	-116.94	-134.8	567.6	261.5	237.6	23.86	10.961		
4,700.0	4,622.2	4,707.6	4,640.4	17.3	17.2	-117.02	-145.1	586.9	265.5	241.1	24.36	10.898		
4,800.0	4,719.4	4,807.5	4,737.9	17.8	17.6	-117.10	-155.3	606.1	269.5	244.6	24.87	10.836		
4,900.0	4,816.5	4,907.4	4,835.4	18.2	18.1	-117.17	-165.5	625.4	273.5	248.1	25.38	10.775		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips
Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 504H - Slot DONKEY POTROAST #504H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 504H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design: TARHEEL_DONKEY POTROAST PROJECT - *TARHEEL FED COM #404H - OWB - PWP0													Offset Site Error:	0.0 usft
Survey Program: 0-r.5 MWD+IFR1													Offset Well Error:	3.0 usft
Reference		Offset		Semi Major Axis		Highside Toolface (")	Offset Wellbore Centre		Distance		No-Go Distance (usft)	Separation Factor	Warning	
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)		+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)				
5,000.0	4,913.7	5,007.3	4,933.0	18.7	18.5	-117.24	-175.7	644.6	277.5	251.6	25.89	10.715		
5,100.0	5,010.9	5,107.3	5,030.5	19.2	19.0	-117.31	-185.9	663.9	281.4	255.0	26.41	10.656		
5,200.0	5,108.0	5,207.2	5,128.0	19.6	19.4	-117.38	-196.1	683.1	285.4	258.5	26.93	10.598		
5,300.0	5,205.2	5,307.1	5,225.5	20.1	19.9	-117.44	-206.4	702.4	289.4	262.0	27.45	10.543		
5,400.0	5,302.4	5,405.8	5,321.9	20.5	20.3	-117.59	-216.2	721.0	293.6	265.6	27.97	10.496		
5,500.0	5,399.5	5,504.0	5,418.2	21.0	20.8	-118.03	-225.3	738.1	298.3	269.7	28.58	10.436		
5,547.4	5,445.6	5,550.5	5,463.9	21.2	21.0	-118.35	-229.3	745.7	300.7	271.8	28.88	10.412		
5,600.0	5,496.8	5,602.1	5,514.6	21.5	21.2	-118.75	-233.6	753.7	303.4	274.2	29.23	10.383		
5,700.0	5,594.3	5,700.0	5,611.3	21.9	21.6	-119.50	-241.1	767.9	308.5	278.6	29.90	10.317		
5,800.0	5,692.3	5,797.9	5,708.1	22.4	22.0	-120.24	-247.8	780.6	313.4	282.8	30.57	10.250		
5,900.0	5,790.6	5,895.7	5,805.1	22.8	22.4	-120.98	-253.8	791.8	318.0	286.8	31.23	10.183		
6,000.0	5,889.1	5,993.5	5,902.2	23.3	22.8	-121.70	-259.0	801.5	322.5	290.6	31.88	10.114		
6,100.0	5,988.0	6,091.1	5,999.4	23.7	23.2	-122.42	-263.4	809.8	326.7	294.2	32.52	10.046		
6,200.0	6,087.1	6,188.7	6,096.7	24.1	23.6	-123.13	-267.0	816.6	330.7	297.6	33.15	9.977		
6,300.0	6,186.4	6,286.2	6,194.0	24.5	23.9	-123.84	-269.8	821.9	334.6	300.8	33.77	9.909		
6,400.0	6,285.9	6,383.6	6,291.3	24.9	24.2	-124.55	-271.8	825.8	338.2	303.8	34.37	9.841		
6,500.0	6,385.6	6,480.9	6,388.6	25.3	24.5	-125.26	-273.1	828.2	341.6	306.7	34.94	9.776		
6,600.0	6,485.4	6,578.1	6,485.8	25.6	24.7	-125.97	-273.6	829.1	344.8	309.4	35.47	9.722		
6,700.0	6,585.3	6,677.6	6,585.3	26.0	24.7	-126.60	-273.6	829.1	347.6	311.6	35.98	9.660		
6,800.0	6,685.3	6,777.6	6,685.3	26.3	24.8	-126.99	-273.6	829.1	349.3	312.9	36.37	9.605		
6,900.0	6,785.3	6,877.6	6,785.3	26.5	24.8	-127.15	-273.6	829.1	350.0	313.3	36.62	9.557		
6,914.7	6,800.0	6,892.3	6,800.0	26.5	24.8	-0.25	-273.6	829.1	350.0	313.3	36.63	9.553		
7,000.0	6,885.3	6,977.6	6,885.3	26.5	24.8	-0.25	-273.6	829.1	350.0	313.3	36.71	9.534		
7,100.0	6,985.3	7,077.6	6,985.3	26.5	24.9	-0.25	-273.6	829.1	350.0	313.2	36.79	9.513		
7,200.0	7,085.3	7,177.6	7,085.3	26.6	24.9	-0.25	-273.6	829.1	350.0	313.1	36.87	9.492		
7,300.0	7,185.3	7,277.6	7,185.3	26.6	24.9	-0.25	-273.6	829.1	350.0	313.0	36.95	9.471		
7,400.0	7,285.3	7,377.6	7,285.3	26.6	25.0	-0.25	-273.6	829.1	350.0	312.9	37.04	9.450		
7,500.0	7,385.3	7,477.6	7,385.3	26.6	25.0	-0.25	-273.6	829.1	350.0	312.9	37.12	9.428		
7,600.0	7,485.3	7,577.6	7,485.3	26.7	25.0	-0.25	-273.6	829.1	350.0	312.8	37.20	9.407		
7,700.0	7,585.3	7,677.6	7,585.3	26.7	25.0	-0.25	-273.6	829.1	350.0	312.7	37.29	9.386		
7,800.0	7,685.3	7,777.6	7,685.3	26.7	25.1	-0.25	-273.6	829.1	350.0	312.6	37.37	9.364		
7,900.0	7,785.3	7,877.6	7,785.3	26.7	25.1	-0.25	-273.6	829.1	350.0	312.5	37.46	9.343		
8,000.0	7,885.3	7,977.6	7,885.3	26.8	25.1	-0.25	-273.6	829.1	350.0	312.4	37.55	9.322		
8,100.0	7,985.3	8,077.6	7,985.3	26.8	25.2	-0.25	-273.6	829.1	350.0	312.3	37.63	9.300		
8,200.0	8,085.3	8,177.6	8,085.3	26.8	25.2	-0.25	-273.6	829.1	350.0	312.3	37.72	9.279		
8,300.0	8,185.3	8,277.6	8,185.3	26.8	25.2	-0.25	-273.6	829.1	350.0	312.2	37.81	9.257		
8,400.0	8,285.3	8,377.6	8,285.3	26.9	25.3	-0.25	-273.6	829.1	350.0	312.1	37.89	9.236		
8,500.0	8,385.3	8,477.6	8,385.3	26.9	25.3	-0.25	-273.6	829.1	350.0	312.0	37.98	9.214		
8,600.0	8,485.3	8,577.6	8,485.3	26.9	25.3	-0.25	-273.6	829.1	350.0	311.9	38.07	9.193		
8,700.0	8,585.3	8,677.6	8,585.3	27.0	25.4	-0.25	-273.6	829.1	350.0	311.8	38.16	9.171		
8,800.0	8,685.3	8,777.6	8,685.3	27.0	25.4	-0.25	-273.6	829.1	350.0	311.7	38.25	9.149		
8,900.0	8,785.3	8,877.6	8,785.3	27.0	25.4	-0.25	-273.6	829.1	350.0	311.6	38.34	9.128		
9,000.0	8,885.3	8,977.6	8,885.3	27.0	25.5	-0.25	-273.6	829.1	350.0	311.5	38.43	9.106		
9,011.8	8,897.0	8,989.4	8,897.0	27.0	25.5	-0.25	-273.6	829.1	350.0	311.5	38.44	9.104 SF		
9,100.0	8,985.3	9,072.2	8,979.9	27.1	25.5	-0.25	-273.6	829.1	350.1	311.7	38.42	9.111		
9,200.0	9,085.3	9,125.0	9,032.5	27.1	25.4	-0.25	-269.8	829.1	357.7	320.1	37.62	9.507		
9,300.0	9,185.3	9,185.0	9,091.4	27.1	25.3	-0.26	-258.6	829.0	376.9	340.0	36.90	10.214		
9,400.0	9,285.3	9,237.4	9,141.3	27.2	25.2	-0.27	-242.8	828.9	407.1	371.0	36.16	11.258		
9,500.0	9,385.3	9,285.8	9,185.6	27.2	25.1	-0.28	-223.4	828.7	447.2	411.7	35.55	12.581		
9,600.0	9,485.3	9,325.0	9,220.0	27.2	25.0	-0.29	-204.5	828.6	496.0	461.0	35.06	14.147		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 504H - Slot DONKEY POTROAST #504H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 504H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design:	TARHEEL_DONKEY POTROAST PROJECT - *TARHEEL FED COM #404H - OWB - PWP0											Offset Site Error:	0.0 usft
Survey Program:	0-r.5 MWD+IFR1											Offset Well Error:	3.0 usft
Reference	Offset	Semi Major Axis		Offset Wellbore Centre		Rule Assigned:		Distance		Warning			
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	No-Go Distance (usft)	Separation Factor	
9,700.0	9,585.3	9,375.0	9,261.3	27.2	25.0	-0.30	-176.4	828.3	552.2	517.4	34.86	15.841	
9,800.0	9,685.3	9,400.0	9,280.8	27.3	24.9	-0.31	-160.7	828.2	614.7	580.0	34.70	17.713	
9,900.0	9,785.3	9,435.6	9,307.1	27.3	24.9	-0.32	-136.8	828.0	682.4	647.6	34.74	19.641	
10,000.0	9,885.3	9,463.2	9,326.2	27.3	24.8	-0.32	-116.8	827.8	754.5	719.6	34.88	21.631	
10,100.0	9,985.3	9,487.8	9,342.2	27.4	24.8	-0.33	-98.3	827.7	830.3	795.2	35.11	23.651	
10,116.7	10,002.0	9,491.6	9,344.7	27.4	24.8	-0.33	-95.3	827.6	843.3	808.2	35.15	23.993	
10,150.0	10,035.2	9,500.0	9,349.9	27.4	24.8	-179.94	-88.7	827.6	870.0	834.8	35.25	24.678	
10,200.0	10,085.0	9,500.0	9,349.9	27.5	24.8	-179.93	-88.7	827.6	912.7	877.2	35.46	25.739	
10,250.0	10,134.1	9,515.1	9,358.9	27.7	24.8	-179.92	-76.6	827.5	957.7	922.0	35.64	26.868	

ConocoPhillips

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 504H - Slot DONKEY POTROAST #504H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 504H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design: TARHEEL_DONKEY POTROAST PROJECT - *TARHEEL FED COM #503H - OWB - PWP0													Offset Site Error:	0.0 usft
Survey Program: 0-r.5 MWD+IFR1+MS													Offset Well Error:	3.0 usft
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Semi Major Axis Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre		Distance Between Centres (usft)		No-Go Distance (usft)	Separation Factor	Warning	
							+N/-S (usft)	+E/-W (usft)						
0.0	0.0	0.0	0.0	3.0	3.0	-31.21	149.7	-90.7	175.1	168.7	6.43	27.233		
100.0	100.0	100.0	100.0	3.2	3.2	-31.21	149.7	-90.7	175.1	168.2	6.89	25.402		
200.0	200.0	200.0	200.0	3.5	3.5	-31.21	149.7	-90.7	175.1	167.8	7.33	23.892		
300.0	300.0	300.0	300.0	3.7	3.7	-31.21	149.7	-90.7	175.1	167.3	7.74	22.616		
400.0	400.0	400.0	400.0	3.9	3.9	-31.21	149.7	-90.7	175.1	166.9	8.14	21.521		
500.0	500.0	500.0	500.0	4.1	4.1	-31.21	149.7	-90.7	175.1	166.6	8.51	20.565		
600.0	600.0	600.0	600.0	4.2	4.2	-31.21	149.7	-90.7	175.1	166.2	8.88	19.722		
700.0	700.0	700.0	700.0	4.4	4.4	-31.21	149.7	-90.7	175.1	165.9	9.23	18.970		
800.0	800.0	800.0	800.0	4.6	4.6	-31.21	149.7	-90.7	175.1	165.5	9.57	18.294		
900.0	900.0	900.0	900.0	4.8	4.8	-31.21	149.7	-90.7	175.1	165.2	9.90	17.682		
1,000.0	1,000.0	1,000.0	1,000.0	4.9	4.9	-31.21	149.7	-90.7	175.1	164.9	10.22	17.123		
1,100.0	1,100.0	1,100.0	1,100.0	5.1	5.1	-31.21	149.7	-90.7	175.1	164.5	10.54	16.612		
1,200.0	1,200.0	1,200.0	1,200.0	5.2	5.2	-31.21	149.7	-90.7	175.1	164.2	10.85	16.140		
1,300.0	1,300.0	1,300.0	1,300.0	5.4	5.4	-31.21	149.7	-90.7	175.1	163.9	11.15	15.704		
1,400.0	1,400.0	1,400.0	1,400.0	5.5	5.5	-31.21	149.7	-90.7	175.1	163.6	11.44	15.298		
1,500.0	1,500.0	1,500.0	1,500.0	5.7	5.7	-31.21	149.7	-90.7	175.1	163.3	11.73	14.920 CC, ES		
1,600.0	1,600.0	1,602.2	1,602.1	5.9	5.9	-158.87	148.3	-91.8	176.1	164.0	12.08	14.580		
1,700.0	1,699.8	1,703.9	1,703.8	6.1	6.1	-161.09	144.0	-95.2	179.3	166.9	12.40	14.459 SF		
1,800.0	1,799.5	1,804.9	1,804.3	6.3	6.4	-164.58	137.0	-100.7	185.1	172.4	12.74	14.536		
1,900.0	1,898.7	1,904.8	1,903.4	6.6	6.6	-169.03	127.2	-108.3	194.4	181.3	13.10	14.847		
2,000.0	1,997.5	2,003.0	2,000.4	6.9	6.8	-174.02	115.1	-117.7	207.9	194.5	13.43	15.477		
2,100.0	2,095.6	2,099.7	2,095.8	7.2	7.0	-178.60	102.5	-127.6	226.2	212.4	13.85	16.334		
2,183.7	2,177.2	2,180.1	2,175.1	7.4	7.2	178.10	92.0	-135.7	245.1	231.0	14.17	17.302		
2,200.0	2,193.1	2,195.7	2,190.5	7.4	7.2	177.52	90.0	-137.3	249.1	234.9	14.22	17.523		
2,300.0	2,290.2	2,291.5	2,285.0	7.7	7.5	174.31	77.5	-147.1	274.2	259.5	14.63	18.745		
2,400.0	2,387.4	2,387.3	2,379.4	8.0	7.7	171.64	65.1	-156.8	299.9	284.8	15.03	19.951		
2,500.0	2,484.6	2,483.0	2,473.9	8.3	8.0	169.39	52.6	-166.5	326.1	310.6	15.45	21.098		
2,600.0	2,581.7	2,578.8	2,568.3	8.6	8.3	167.47	40.1	-176.3	352.7	336.8	15.90	22.182		
2,700.0	2,678.9	2,674.5	2,662.7	9.0	8.6	165.81	27.6	-186.0	379.6	363.3	16.36	23.199		
2,800.0	2,776.1	2,770.3	2,757.2	9.3	8.9	164.38	15.2	-195.7	406.8	390.0	16.85	24.152		
2,900.0	2,873.2	2,866.0	2,851.6	9.7	9.2	163.12	2.7	-205.5	434.3	416.9	17.34	25.041		
3,000.0	2,970.4	2,961.8	2,946.1	10.1	9.6	162.02	-9.8	-215.2	461.8	444.0	17.85	25.870		
3,100.0	3,067.6	3,057.6	3,040.5	10.4	9.9	161.03	-22.3	-224.9	489.6	471.2	18.38	26.641		
3,200.0	3,164.7	3,153.3	3,134.9	10.8	10.3	160.16	-34.7	-234.7	517.4	498.5	18.91	27.359		
3,300.0	3,261.9	3,249.1	3,229.4	11.2	10.6	159.37	-47.2	-244.4	545.4	525.9	19.46	28.027		
3,400.0	3,359.1	3,344.8	3,323.8	11.6	11.0	158.65	-59.7	-254.1	573.4	553.4	20.01	28.649		
3,500.0	3,456.2	3,440.6	3,418.3	12.1	11.3	158.01	-72.2	-263.9	601.5	580.9	20.58	29.227		
3,600.0	3,553.4	3,536.4	3,512.7	12.5	11.7	157.42	-84.7	-273.6	629.7	608.5	21.15	29.766		
3,700.0	3,650.6	3,632.1	3,607.2	12.9	12.1	156.88	-97.1	-283.3	657.9	636.2	21.73	30.269		
3,800.0	3,747.7	3,727.9	3,701.6	13.3	12.5	156.39	-109.6	-293.1	686.2	663.8	22.32	30.738		
3,900.0	3,844.9	3,823.6	3,796.0	13.8	12.8	155.93	-122.1	-302.8	714.5	691.6	22.92	31.175		
4,000.0	3,942.1	3,919.4	3,890.5	14.2	13.2	155.51	-134.6	-312.5	742.8	719.3	23.52	31.585		
4,100.0	4,039.2	4,015.1	3,984.9	14.6	13.6	155.12	-147.0	-322.3	771.2	747.1	24.13	31.967		
4,200.0	4,136.4	4,110.9	4,079.4	15.1	14.0	154.76	-159.5	-332.0	799.7	774.9	24.74	32.326		
4,300.0	4,233.6	4,206.7	4,173.8	15.5	14.4	154.43	-172.0	-341.7	828.1	802.8	25.35	32.662		
4,400.0	4,330.7	4,302.4	4,268.2	16.0	14.8	154.11	-184.5	-351.5	856.6	830.6	25.97	32.978		
4,500.0	4,427.9	4,398.2	4,362.7	16.4	15.2	153.82	-196.9	-361.2	885.1	858.5	26.60	33.275		
4,600.0	4,525.0	4,493.9	4,457.1	16.9	15.6	153.54	-209.4	-370.9	913.6	886.4	27.23	33.554		
4,700.0	4,622.2	4,589.7	4,551.6	17.3	16.0	153.28	-221.9	-380.7	942.1	914.3	27.86	33.816		
4,800.0	4,719.4	4,685.4	4,646.0	17.8	16.4	153.04	-234.4	-390.4	970.7	942.2	28.50	34.064		
4,900.0	4,816.5	4,781.2	4,740.4	18.2	16.8	152.81	-246.8	-400.1	999.3	970.1	29.13	34.298		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 504H - Slot DONKEY POTROAST #504H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 504H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design:	TARHEEL_DONKEY POTROAST PROJECT - *TARHEEL FED COM #503H - OWB - PWP0											Offset Site Error:	0.0 usft
Survey Program:	0-r.5 MWD+IFR1+MS											Offset Well Error:	3.0 usft
Reference	Offset	Semi Major Axis		Offset Wellbore Centre		Rule Assigned:							
Measured	Vertical	Measured	Vertical	Reference	Offset	Highside		Distance					
Depth	Depth	Depth	Depth			Toolface	+N/-S	Between	Between	No-Go	Separation		Warning
(usft)	(usft)	(usft)	(usft)	(usft)	(usft)	(°)	(usft)	Centres	Ellipses	Distance	Factor		
								(usft)	(usft)	(usft)			

ConocoPhillips

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 504H - Slot DONKEY POTROAST #504H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 504H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design: TARHEEL_DONKEY POTROAST PROJECT - *TARHEEL FED COM #504H - OWB - PWP0													Offset Site Error:	0.0 usft
Survey Program: 0-r.5 MWD+IFR1													Offset Well Error:	3.0 usft
Reference		Offset		Semi Major Axis		Highside Toolface (°)	Offset Wellbore Centre		Distance		No-Go Distance (usft)	Separation Factor	Warning	
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)		+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)				
0.0	0.0	0.0	0.0	3.0	3.0	-0.21	150.7	-0.6	150.7	144.2	6.43	23.436		
100.0	100.0	100.0	100.0	3.2	3.2	-0.21	150.7	-0.6	150.7	143.8	6.89	21.860		
200.0	200.0	200.0	200.0	3.5	3.5	-0.21	150.7	-0.6	150.7	143.3	7.33	20.560		
300.0	300.0	300.0	300.0	3.7	3.7	-0.21	150.7	-0.6	150.7	142.9	7.74	19.462		
400.0	400.0	400.0	400.0	3.9	3.9	-0.21	150.7	-0.6	150.7	142.5	8.14	18.519		
500.0	500.0	500.0	500.0	4.1	4.1	-0.21	150.7	-0.6	150.7	142.2	8.51	17.697		
600.0	600.0	600.0	600.0	4.2	4.2	-0.21	150.7	-0.6	150.7	141.8	8.88	16.971		
700.0	700.0	700.0	700.0	4.4	4.4	-0.21	150.7	-0.6	150.7	141.4	9.23	16.324		
800.0	800.0	800.0	800.0	4.6	4.6	-0.21	150.7	-0.6	150.7	141.1	9.57	15.743		
900.0	900.0	900.0	900.0	4.8	4.8	-0.21	150.7	-0.6	150.7	140.8	9.90	15.216		
1,000.0	1,000.0	1,000.0	1,000.0	4.9	4.9	-0.21	150.7	-0.6	150.7	140.4	10.22	14.735		
1,100.0	1,100.0	1,100.0	1,100.0	5.1	5.1	-0.21	150.7	-0.6	150.7	140.1	10.54	14.295		
1,200.0	1,200.0	1,200.0	1,200.0	5.2	5.2	-0.21	150.7	-0.6	150.7	139.8	10.85	13.889		
1,300.0	1,300.0	1,300.0	1,300.0	5.4	5.4	-0.21	150.7	-0.6	150.7	139.5	11.15	13.514		
1,400.0	1,400.0	1,400.0	1,400.0	5.5	5.5	-0.21	150.7	-0.6	150.7	139.2	11.44	13.165		
1,500.0	1,500.0	1,500.0	1,500.0	5.7	5.7	-0.21	150.7	-0.6	150.7	138.9	11.73	12.840 CC		
1,600.0	1,600.0	1,602.8	1,602.8	5.9	5.9	-127.05	149.7	1.0	150.8	138.7	12.05	12.514 ES		
1,700.0	1,699.8	1,705.6	1,705.4	6.1	6.1	-126.88	146.9	5.8	151.2	138.8	12.34	12.249		
1,800.0	1,799.5	1,808.4	1,807.8	6.3	6.4	-126.59	142.1	13.7	151.8	139.1	12.64	12.009		
1,900.0	1,898.7	1,911.2	1,909.8	6.6	6.6	-126.20	135.5	24.7	152.6	139.7	12.94	11.790		
2,000.0	1,997.5	2,013.9	2,011.2	6.9	6.9	-125.71	126.9	38.8	153.7	140.5	13.26	11.590		
2,100.0	2,095.6	2,116.6	2,111.9	7.2	7.2	-125.11	116.5	56.1	155.1	141.5	13.59	11.411		
2,183.7	2,177.2	2,202.1	2,195.1	7.4	7.4	-124.56	106.5	72.7	156.5	142.6	13.83	11.318		
2,200.0	2,193.1	2,218.5	2,211.0	7.4	7.5	-124.48	104.5	76.1	156.8	142.9	13.87	11.302		
2,300.0	2,290.2	2,318.4	2,308.1	7.7	7.8	-123.99	92.3	96.4	158.8	144.5	14.28	11.119		
2,400.0	2,387.4	2,418.4	2,405.2	8.0	8.1	-123.52	80.0	116.7	160.8	146.2	14.64	10.982		
2,500.0	2,484.6	2,518.4	2,502.3	8.3	8.4	-123.06	67.8	137.0	162.8	147.8	15.02	10.842		
2,600.0	2,581.7	2,618.3	2,599.5	8.6	8.7	-122.61	55.5	157.3	164.9	149.5	15.41	10.702		
2,700.0	2,678.9	2,718.3	2,696.6	9.0	9.1	-122.17	43.3	177.7	166.9	151.1	15.80	10.562		
2,800.0	2,776.1	2,818.3	2,793.7	9.3	9.4	-121.74	31.0	198.0	169.0	152.8	16.21	10.424		
2,900.0	2,873.2	2,918.3	2,890.8	9.7	9.8	-121.33	18.8	218.3	171.0	154.4	16.62	10.289		
3,000.0	2,970.4	3,018.2	2,987.9	10.1	10.2	-120.92	6.5	238.6	173.1	156.1	17.04	10.156		
3,100.0	3,067.6	3,118.2	3,085.0	10.4	10.5	-120.52	-5.7	258.9	175.2	157.7	17.47	10.028		
3,200.0	3,164.7	3,218.2	3,182.2	10.8	10.9	-120.13	-18.0	279.3	177.3	159.4	17.90	9.903		
3,300.0	3,261.9	3,318.1	3,279.3	11.2	11.3	-119.75	-30.2	299.6	179.4	161.0	18.34	9.782		
3,400.0	3,359.1	3,418.1	3,376.4	11.6	11.7	-119.38	-42.4	319.9	181.5	162.7	18.78	9.666		
3,500.0	3,456.2	3,518.1	3,473.5	12.1	12.2	-119.02	-54.7	340.2	183.6	164.4	19.22	9.554		
3,600.0	3,553.4	3,618.1	3,570.6	12.5	12.6	-118.67	-66.9	360.5	185.7	166.1	19.66	9.446		
3,700.0	3,650.6	3,718.0	3,667.7	12.9	13.0	-118.32	-79.2	380.8	187.8	167.7	20.11	9.343		
3,800.0	3,747.7	3,818.0	3,764.8	13.3	13.4	-117.98	-91.4	401.2	190.0	169.4	20.55	9.243		
3,900.0	3,844.9	3,918.0	3,862.0	13.8	13.9	-117.65	-103.7	421.5	192.1	171.1	21.00	9.147		
4,000.0	3,942.1	4,017.9	3,959.1	14.2	14.3	-117.33	-115.9	441.8	194.3	172.8	21.45	9.056		
4,100.0	4,039.2	4,117.9	4,056.2	14.6	14.7	-117.01	-128.2	462.1	196.4	174.5	21.90	8.968		
4,200.0	4,136.4	4,217.9	4,153.3	15.1	15.2	-116.70	-140.4	482.4	198.6	176.2	22.35	8.883		
4,300.0	4,233.6	4,317.9	4,250.4	15.5	15.6	-116.40	-152.7	502.8	200.7	177.9	22.81	8.802		
4,400.0	4,330.7	4,417.8	4,347.5	16.0	16.1	-116.10	-164.9	523.1	202.9	179.7	23.26	8.724		
4,500.0	4,427.9	4,517.8	4,444.7	16.4	16.5	-115.81	-177.1	543.4	205.1	181.4	23.71	8.650		
4,600.0	4,525.0	4,617.8	4,541.8	16.9	17.0	-115.53	-189.4	563.7	207.3	183.1	24.16	8.578		
4,700.0	4,622.2	4,717.7	4,638.9	17.3	17.4	-115.25	-201.6	584.0	209.4	184.8	24.61	8.509		
4,800.0	4,719.4	4,817.7	4,736.0	17.8	17.9	-114.98	-213.9	604.4	211.6	186.6	25.07	8.443		
4,900.0	4,816.5	4,917.7	4,833.1	18.2	18.3	-114.71	-226.1	624.7	213.8	188.3	25.52	8.380		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 504H - Slot DONKEY POTROAST #504H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 504H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design: TARHEEL_DONKEY POTROAST PROJECT - *TARHEEL FED COM #504H - OWB - PWP0													Offset Site Error:	0.0 usft
Survey Program: 0-r.5 MWD+IFR1													Offset Well Error:	3.0 usft
Reference		Offset		Semi Major Axis		Highside Toolface (")	Offset Wellbore Centre		Distance		No-Go Distance (usft)	Separation Factor	Warning	
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)		+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)				
5,000.0	4,913.7	5,017.7	4,930.2	18.7	18.8	-114.45	-238.4	645.0	216.0	190.1	25.97	8.318		
5,100.0	5,010.9	5,117.6	5,027.3	19.2	19.3	-114.20	-250.6	665.3	218.2	191.8	26.42	8.260		
5,200.0	5,108.0	5,217.6	5,124.5	19.6	19.7	-113.95	-262.9	685.6	220.4	193.6	26.87	8.205		
5,300.0	5,205.2	5,316.6	5,220.7	20.1	20.2	-113.85	-274.7	705.3	222.8	195.5	27.32	8.155		
5,400.0	5,302.4	5,415.3	5,317.2	20.5	20.6	-114.16	-285.6	723.4	225.8	197.9	27.89	8.096		
5,500.0	5,399.5	5,513.9	5,413.8	21.0	21.1	-114.86	-295.7	740.2	229.3	200.7	28.54	8.033		
5,547.4	5,445.6	5,560.7	5,459.8	21.2	21.3	-115.33	-300.2	747.6	231.1	202.3	28.87	8.006		
5,600.0	5,496.8	5,612.4	5,510.7	21.5	21.5	-115.90	-304.9	755.4	233.3	204.0	29.25	7.975		
5,700.0	5,594.3	5,710.8	5,607.8	21.9	21.9	-116.98	-313.3	769.3	237.3	207.3	30.00	7.910		
5,800.0	5,692.3	5,809.1	5,705.0	22.4	22.3	-118.02	-320.7	781.7	241.2	210.5	30.75	7.846		
5,900.0	5,790.6	5,907.3	5,802.4	22.8	22.8	-119.05	-327.3	792.6	245.1	213.6	31.48	7.784		
6,000.0	5,889.1	6,005.5	5,899.9	23.3	23.1	-120.05	-333.1	802.1	248.8	216.6	32.22	7.723		
6,100.0	5,988.0	6,103.5	5,997.5	23.7	23.5	-121.03	-337.9	810.2	252.4	219.5	32.94	7.664		
6,200.0	6,087.1	6,201.5	6,095.1	24.1	23.9	-122.00	-341.9	816.9	256.0	222.3	33.65	7.607		
6,300.0	6,186.4	6,300.0	6,193.4	24.5	24.2	-122.95	-345.1	822.1	259.4	225.1	34.36	7.550		
6,400.0	6,285.9	6,397.1	6,290.5	24.9	24.6	-123.88	-347.4	825.9	262.8	227.7	35.03	7.501		
6,500.0	6,385.6	6,494.8	6,388.1	25.3	24.8	-124.81	-348.8	828.2	266.0	230.3	35.69	7.453		
6,600.0	6,485.4	6,592.4	6,485.8	25.6	25.0	-125.72	-349.3	829.1	269.1	232.9	36.29	7.417		
6,700.0	6,585.3	6,692.0	6,585.3	26.0	25.0	-126.52	-349.3	829.1	271.9	235.0	36.83	7.382		
6,800.0	6,685.3	6,792.0	6,685.3	26.3	25.1	-127.02	-349.3	829.1	273.6	236.3	37.24	7.346		
6,900.0	6,785.3	6,892.0	6,785.3	26.5	25.1	-127.21	-349.3	829.1	274.3	236.8	37.51	7.313		
6,914.7	6,800.0	6,906.7	6,800.0	26.5	25.1	-0.32	-349.3	829.1	274.3	236.7	37.52	7.310		
7,000.0	6,885.3	6,992.0	6,885.3	26.5	25.1	-0.32	-349.3	829.1	274.3	236.7	37.59	7.296		
7,100.0	6,985.3	7,092.0	6,985.3	26.5	25.1	-0.32	-349.3	829.1	274.3	236.6	37.67	7.281		
7,200.0	7,085.3	7,192.0	7,085.3	26.6	25.2	-0.32	-349.3	829.1	274.3	236.5	37.75	7.266		
7,300.0	7,185.3	7,292.0	7,185.3	26.6	25.2	-0.32	-349.3	829.1	274.3	236.4	37.83	7.250		
7,400.0	7,285.3	7,392.0	7,285.3	26.6	25.2	-0.32	-349.3	829.1	274.3	236.4	37.91	7.235		
7,500.0	7,385.3	7,492.0	7,385.3	26.6	25.3	-0.32	-349.3	829.1	274.3	236.3	37.99	7.220		
7,600.0	7,485.3	7,592.0	7,485.3	26.7	25.3	-0.32	-349.3	829.1	274.3	236.2	38.07	7.204		
7,700.0	7,585.3	7,692.0	7,585.3	26.7	25.3	-0.32	-349.3	829.1	274.3	236.1	38.15	7.189		
7,800.0	7,685.3	7,792.0	7,685.3	26.7	25.3	-0.32	-349.3	829.1	274.3	236.0	38.24	7.173		
7,900.0	7,785.3	7,892.0	7,785.3	26.7	25.4	-0.32	-349.3	829.1	274.3	235.9	38.32	7.158		
8,000.0	7,885.3	7,992.0	7,885.3	26.8	25.4	-0.32	-349.3	829.1	274.3	235.9	38.40	7.142		
8,100.0	7,985.3	8,092.0	7,985.3	26.8	25.4	-0.32	-349.3	829.1	274.3	235.8	38.49	7.127		
8,200.0	8,085.3	8,192.0	8,085.3	26.8	25.5	-0.32	-349.3	829.1	274.3	235.7	38.57	7.111		
8,300.0	8,185.3	8,292.0	8,185.3	26.8	25.5	-0.32	-349.3	829.1	274.3	235.6	38.65	7.095		
8,400.0	8,285.3	8,392.0	8,285.3	26.9	25.5	-0.32	-349.3	829.1	274.3	235.5	38.74	7.080		
8,500.0	8,385.3	8,492.0	8,385.3	26.9	25.6	-0.32	-349.3	829.1	274.3	235.4	38.83	7.064		
8,600.0	8,485.3	8,592.0	8,485.3	26.9	25.6	-0.32	-349.3	829.1	274.3	235.4	38.91	7.048		
8,700.0	8,585.3	8,692.0	8,585.3	27.0	25.6	-0.32	-349.3	829.1	274.3	235.3	39.00	7.033		
8,800.0	8,685.3	8,792.0	8,685.3	27.0	25.7	-0.32	-349.3	829.1	274.3	235.2	39.09	7.017		
8,900.0	8,785.3	8,892.0	8,785.3	27.0	25.7	-0.32	-349.3	829.1	274.3	235.1	39.17	7.001		
9,000.0	8,885.3	8,992.0	8,885.3	27.0	25.7	-0.32	-349.3	829.1	274.3	235.0	39.26	6.985		
9,100.0	8,985.3	9,092.0	8,985.3	27.1	25.8	-0.32	-349.3	829.1	274.3	234.9	39.35	6.970		
9,200.0	9,085.3	9,192.0	9,085.3	27.1	25.8	-0.32	-349.3	829.1	274.3	234.8	39.44	6.954		
9,300.0	9,185.3	9,292.0	9,185.3	27.1	25.8	-0.32	-349.3	829.1	274.3	234.7	39.53	6.938		
9,400.0	9,285.3	9,392.0	9,285.3	27.2	25.8	-0.32	-349.3	829.1	274.3	234.6	39.62	6.922		
9,500.0	9,385.3	9,492.0	9,385.3	27.2	25.9	-0.32	-349.3	829.1	274.3	234.6	39.71	6.906		
9,600.0	9,485.3	9,592.0	9,485.3	27.2	25.9	-0.32	-349.3	829.1	274.3	234.5	39.80	6.891		
9,700.0	9,585.3	9,692.0	9,585.3	27.2	26.0	-0.32	-349.3	829.1	274.3	234.4	39.89	6.875		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips
Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 504H - Slot DONKEY POTROAST #504H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 504H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design: TARHEEL_DONKEY POTROAST PROJECT - *TARHEEL FED COM #504H - OWB - PWP0												Offset Site Error:	0.0 usft
Survey Program: 0-r.5 MWD+IFR1												Offset Well Error:	3.0 usft
Reference		Offset		Semi Major Axis		Highside Toolface (°)	Offset Wellbore Centre		Distance		No-Go Distance (usft)	Separation Factor	Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)		+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)			
9,800.0	9,685.3	9,792.0	9,685.3	27.3	26.0	-0.32	-349.3	829.1	274.3	234.3	39.99	6.859	
9,900.0	9,785.3	9,892.0	9,785.3	27.3	26.0	-0.32	-349.3	829.1	274.3	234.2	40.08	6.843 SF	
10,000.0	9,885.3	9,957.8	9,851.0	27.3	26.0	-0.32	-345.7	829.1	280.0	240.6	39.40	7.105	
10,100.0	9,985.3	10,019.0	9,911.1	27.4	25.8	-0.33	-334.4	829.0	298.6	259.9	38.67	7.722	
10,116.7	10,002.0	10,025.0	9,916.9	27.4	25.8	-0.33	-332.9	829.0	303.0	264.5	38.49	7.871	
10,150.0	10,035.2	10,050.0	9,940.8	27.4	25.8	-179.95	-325.7	828.9	313.4	275.0	38.40	8.162	
10,200.0	10,085.0	10,075.0	9,964.4	27.5	25.7	-179.95	-317.3	828.9	334.8	296.5	38.25	8.752	
10,250.0	10,134.1	10,100.0	9,987.4	27.7	25.7	-179.95	-307.7	828.8	362.3	324.1	38.21	9.483	
10,300.0	10,182.1	10,125.0	10,010.0	27.8	25.6	-179.95	-296.9	828.7	395.2	357.0	38.23	10.337	
10,350.0	10,228.9	10,138.0	10,021.5	28.0	25.6	-179.95	-290.9	828.7	432.5	394.3	38.23	11.314	
10,400.0	10,273.9	10,150.0	10,031.9	28.1	25.6	-179.95	-285.0	828.6	473.7	435.4	38.29	12.372	
10,450.0	10,316.8	10,164.1	10,044.0	28.3	25.5	-179.95	-277.7	828.5	517.8	479.4	38.38	13.490	
10,500.0	10,357.3	10,175.0	10,053.2	28.5	25.5	-179.94	-271.9	828.5	564.2	525.7	38.49	14.659	
10,550.0	10,395.1	10,175.0	10,053.2	28.6	25.5	-179.92	-271.9	828.5	612.3	573.7	38.57	15.876	
10,600.0	10,430.0	10,182.8	10,059.8	28.8	25.5	-179.88	-267.5	828.5	661.4	622.7	38.68	17.100	
10,650.0	10,461.5	10,184.6	10,061.2	28.9	25.5	-179.65	-266.5	828.4	711.2	672.4	38.77	18.342	
10,700.0	10,489.6	10,184.6	10,061.2	29.1	25.5	-0.31	-266.5	828.4	761.2	722.3	38.86	19.586	
10,750.0	10,514.0	10,183.0	10,059.9	29.2	25.5	-0.10	-267.5	828.5	811.0	772.0	38.95	20.823	
10,800.0	10,534.4	10,175.0	10,053.2	29.3	25.5	-0.06	-271.9	828.5	860.3	821.3	39.01	22.054	
10,850.0	10,550.9	10,175.0	10,053.2	29.4	25.5	-0.04	-271.9	828.5	908.7	869.6	39.08	23.249	
10,900.0	10,563.1	10,175.0	10,053.2	29.5	25.5	-0.03	-271.9	828.5	956.1	916.9	39.16	24.417	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips
Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 504H - Slot DONKEY POTROAST #504H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 504H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design: TARHEEL_DONKEY POTROAST PROJECT - *TARHEEL FED COM #703H - OWB - PWP0													Offset Site Error:	0.0 usft
Survey Program: 0-r.5 MWD+IFR1													Offset Well Error:	3.0 usft
Reference	Offset	Semi Major Axis		Rule Assigned:		Distance		Warning						
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	No-Go Distance (usft)	Separation Factor		
0.0	0.0	0.0	0.0	3.0	3.0	-21.96	150.2	-60.6	161.9	155.5	6.43	25.191		
100.0	100.0	100.0	100.0	3.2	3.2	-21.96	150.2	-60.6	161.9	155.1	6.89	23.497		
200.0	200.0	200.0	200.0	3.5	3.5	-21.96	150.2	-60.6	161.9	154.6	7.33	22.100		
300.0	300.0	300.0	300.0	3.7	3.7	-21.96	150.2	-60.6	161.9	154.2	7.74	20.920		
400.0	400.0	400.0	400.0	3.9	3.9	-21.96	150.2	-60.6	161.9	153.8	8.14	19.906		
500.0	500.0	500.0	500.0	4.1	4.1	-21.96	150.2	-60.6	161.9	153.4	8.51	19.023		
600.0	600.0	600.0	600.0	4.2	4.2	-21.96	150.2	-60.6	161.9	153.1	8.88	18.242		
700.0	700.0	700.0	700.0	4.4	4.4	-21.96	150.2	-60.6	161.9	152.7	9.23	17.547		
800.0	800.0	800.0	800.0	4.6	4.6	-21.96	150.2	-60.6	161.9	152.4	9.57	16.922		
900.0	900.0	900.0	900.0	4.8	4.8	-21.96	150.2	-60.6	161.9	152.0	9.90	16.355		
1,000.0	1,000.0	1,000.0	1,000.0	4.9	4.9	-21.96	150.2	-60.6	161.9	151.7	10.22	15.839		
1,100.0	1,100.0	1,100.0	1,100.0	5.1	5.1	-21.96	150.2	-60.6	161.9	151.4	10.54	15.366		
1,200.0	1,200.0	1,200.0	1,200.0	5.2	5.2	-21.96	150.2	-60.6	161.9	151.1	10.85	14.930		
1,300.0	1,300.0	1,300.0	1,300.0	5.4	5.4	-21.96	150.2	-60.6	161.9	150.8	11.15	14.526		
1,400.0	1,400.0	1,400.0	1,400.0	5.5	5.5	-21.96	150.2	-60.6	161.9	150.5	11.44	14.151		
1,500.0	1,500.0	1,500.0	1,500.0	5.7	5.7	-21.96	150.2	-60.6	161.9	150.2	11.73	13.801 CC, ES		
1,600.0	1,600.0	1,603.1	1,603.0	5.9	5.9	-149.73	148.7	-61.6	162.5	150.4	12.08	13.452		
1,700.0	1,699.8	1,705.7	1,705.5	6.1	6.1	-152.30	144.2	-64.9	164.4	152.0	12.40	13.253		
1,800.0	1,799.5	1,807.6	1,807.0	6.3	6.4	-156.39	136.8	-70.2	168.2	155.4	12.74	13.199 SF		
1,900.0	1,898.7	1,908.4	1,907.0	6.6	6.6	-161.70	126.6	-77.5	174.9	161.8	13.11	13.345		
2,000.0	1,997.5	2,007.7	2,005.1	6.9	6.9	-167.79	113.8	-86.8	185.5	172.0	13.49	13.752		
2,100.0	2,095.6	2,104.8	2,100.4	7.2	7.0	-174.02	98.9	-97.5	201.1	187.2	13.84	14.522		
2,183.7	2,177.2	2,185.0	2,179.1	7.4	7.2	-178.61	86.4	-106.5	218.3	204.1	14.17	15.407		
2,200.0	2,193.1	2,200.6	2,194.4	7.4	7.3	-179.43	84.0	-108.2	222.0	207.8	14.22	15.616		
2,300.0	2,290.2	2,296.0	2,288.0	7.7	7.5	176.10	69.0	-119.0	245.8	231.2	14.63	16.802		
2,400.0	2,387.4	2,391.4	2,381.7	8.0	7.8	172.41	54.1	-129.7	270.8	255.8	15.04	18.009		
2,500.0	2,484.6	2,486.9	2,475.3	8.3	8.1	169.34	39.2	-140.5	296.7	281.3	15.47	19.183		
2,600.0	2,581.7	2,582.3	2,569.0	8.6	8.4	166.75	24.3	-151.2	323.3	307.4	15.92	20.311		
2,700.0	2,678.9	2,677.7	2,662.6	9.0	8.7	164.56	9.4	-161.9	350.5	334.1	16.39	21.385		
2,800.0	2,776.1	2,773.2	2,756.3	9.3	9.0	162.68	-5.6	-172.7	378.0	361.1	16.87	22.400		
2,900.0	2,873.2	2,868.6	2,849.9	9.7	9.3	161.05	-20.5	-183.4	405.8	388.5	17.38	23.357		
3,000.0	2,970.4	2,964.1	2,943.6	10.1	9.7	159.63	-35.4	-194.2	434.0	416.1	17.89	24.254		
3,100.0	3,067.6	3,059.5	3,037.2	10.4	10.0	158.39	-50.3	-204.9	462.3	443.9	18.42	25.095		
3,200.0	3,164.7	3,154.9	3,130.9	10.8	10.4	157.28	-65.2	-215.6	490.8	471.9	18.96	25.882		
3,300.0	3,261.9	3,250.4	3,224.5	11.2	10.8	156.30	-80.2	-226.4	519.5	500.0	19.52	26.617		
3,400.0	3,359.1	3,345.8	3,318.2	11.6	11.1	155.42	-95.1	-237.1	548.3	528.2	20.08	27.305		
3,500.0	3,456.2	3,441.2	3,411.8	12.1	11.5	154.62	-110.0	-247.9	577.2	556.6	20.65	27.948		
3,600.0	3,553.4	3,536.7	3,505.5	12.5	11.9	153.90	-124.9	-258.6	606.2	585.0	21.23	28.548		
3,700.0	3,650.6	3,632.1	3,599.1	12.9	12.3	153.25	-139.8	-269.4	635.3	613.5	21.82	29.110		
3,800.0	3,747.7	3,727.5	3,692.8	13.3	12.7	152.66	-154.8	-280.1	664.4	642.0	22.42	29.636		
3,900.0	3,844.9	3,823.0	3,786.4	13.8	13.1	152.11	-169.7	-290.8	693.7	670.6	23.02	30.129		
4,000.0	3,942.1	3,918.4	3,880.1	14.2	13.4	151.61	-184.6	-301.6	722.9	699.3	23.63	30.591		
4,100.0	4,039.2	4,013.9	3,973.7	14.6	13.8	151.14	-199.5	-312.3	752.2	728.0	24.25	31.025		
4,200.0	4,136.4	4,109.3	4,067.4	15.1	14.2	150.72	-214.4	-323.1	781.6	756.7	24.87	31.432		
4,300.0	4,233.6	4,204.7	4,161.0	15.5	14.7	150.32	-229.4	-333.8	811.0	785.5	25.49	31.815		
4,400.0	4,330.7	4,300.2	4,254.7	16.0	15.1	149.95	-244.3	-344.5	840.4	814.3	26.12	32.175		
4,500.0	4,427.9	4,395.6	4,348.3	16.4	15.5	149.60	-259.2	-355.3	869.9	843.1	26.75	32.515		
4,600.0	4,525.0	4,491.0	4,442.0	16.9	15.9	149.28	-274.1	-366.0	899.3	871.9	27.39	32.835		
4,700.0	4,622.2	4,586.5	4,535.6	17.3	16.3	148.98	-289.0	-376.8	928.8	900.8	28.03	33.137		
4,800.0	4,719.4	4,681.9	4,629.3	17.8	16.7	148.70	-304.0	-387.5	958.4	929.7	28.67	33.422		
4,900.0	4,816.5	4,777.4	4,722.9	18.2	17.1	148.43	-318.9	-398.2	987.9	958.6	29.32	33.693		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips

Anticollision Report

Company:	DELAWARE BASIN EAST				Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 504H - Slot DONKEY POTROAST #504H			
Project:	ZEUS_NME				TVD Reference:	WELL @ 3630.0usft (Original Well Elev)			
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT				MD Reference:	WELL @ 3630.0usft (Original Well Elev)			
Site Error:	0.0 usft				North Reference:	Grid			
Reference Well:	_DONKEY POTROAST FED COM 504H				Survey Calculation Method:	Minimum Curvature			
Well Error:	3.0 usft				Output errors are at	2.00 sigma			
Reference Wellbore	OWB				Database:	EDT 17 Permian Prod			
Reference Design:	PWP0				Offset TVD Reference:	Offset Datum			

Offset Design:	TARHEEL_DONKEY POTROAST PROJECT - *TARHEEL FED COM #703H - OWB - PWP0										Offset Site Error:	0.0 usft
Survey Program:	0-r.5 MWD+IFR1										Offset Well Error:	3.0 usft
Reference	Offset	Semi Major Axis		Rule Assigned:				Offset Well Error:				
Measured Vertical	Measured Vertical	Reference	Offset	Highside	Offset Wellbore Centre		Distance	Between		No-Go	Separation	Warning
Depth	Depth	Depth	Depth	Toolface	+N/-S	+E/-W	Between	Between	Distance			
(usft)	(usft)	(usft)	(usft)	(°)	(usft)	(usft)	Centres	Ellipses	(usft)	(usft)	Factor	

ConocoPhillips
Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 504H - Slot DONKEY POTROAST #504H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 504H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design: TARHEEL_DONKEY POTROAST PROJECT - *TARHEEL FED COM #704H - OWB - PWP0													Offset Site Error:	0.0 usft
Survey Program: 0-r.5 MWD+IFR1													Offset Well Error:	3.0 usft
Reference	Offset	Semi Major Axis		Rule Assigned:		Distance		Warning						
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	No-Go Distance (usft)	Separation Factor		
0.0	0.0	0.0	0.0	3.0	3.0	-11.36	150.2	-30.2	153.2	146.8	6.43	23.831		
100.0	100.0	100.0	100.0	3.2	3.2	-11.36	150.2	-30.2	153.2	146.3	6.89	22.228		
200.0	200.0	200.0	200.0	3.5	3.5	-11.36	150.2	-30.2	153.2	145.9	7.33	20.906		
300.0	300.0	300.0	300.0	3.7	3.7	-11.36	150.2	-30.2	153.2	145.5	7.74	19.791		
400.0	400.0	400.0	400.0	3.9	3.9	-11.36	150.2	-30.2	153.2	145.1	8.14	18.832		
500.0	500.0	500.0	500.0	4.1	4.1	-11.36	150.2	-30.2	153.2	144.7	8.51	17.995		
600.0	600.0	600.0	600.0	4.2	4.2	-11.36	150.2	-30.2	153.2	144.3	8.88	17.257		
700.0	700.0	700.0	700.0	4.4	4.4	-11.36	150.2	-30.2	153.2	144.0	9.23	16.600		
800.0	800.0	800.0	800.0	4.6	4.6	-11.36	150.2	-30.2	153.2	143.6	9.57	16.008		
900.0	900.0	900.0	900.0	4.8	4.8	-11.36	150.2	-30.2	153.2	143.3	9.90	15.472		
1,000.0	1,000.0	1,000.0	1,000.0	4.9	4.9	-11.36	150.2	-30.2	153.2	143.0	10.22	14.984		
1,100.0	1,100.0	1,100.0	1,100.0	5.1	5.1	-11.36	150.2	-30.2	153.2	142.7	10.54	14.536		
1,200.0	1,200.0	1,200.0	1,200.0	5.2	5.2	-11.36	150.2	-30.2	153.2	142.4	10.85	14.123		
1,300.0	1,300.0	1,300.0	1,300.0	5.4	5.4	-11.36	150.2	-30.2	153.2	142.1	11.15	13.742		
1,400.0	1,400.0	1,400.0	1,400.0	5.5	5.5	-11.36	150.2	-30.2	153.2	141.8	11.44	13.387		
1,500.0	1,500.0	1,500.0	1,500.0	5.7	5.7	-11.36	150.2	-30.2	153.2	141.5	11.73	13.056 CC		
1,600.0	1,600.0	1,603.9	1,603.9	5.9	5.9	-138.21	149.2	-28.6	153.2	141.1	12.09	12.677		
1,700.0	1,699.8	1,707.9	1,707.7	6.1	6.1	-138.07	146.0	-23.9	153.3	140.9	12.42	12.345		
1,800.0	1,799.5	1,811.8	1,811.2	6.3	6.4	-137.84	140.8	-16.1	153.4	140.6	12.76	12.022		
1,900.0	1,898.7	1,915.7	1,914.2	6.6	6.6	-137.52	133.5	-5.1	153.5	140.4	13.11	11.704		
2,000.0	1,997.5	2,019.6	2,016.7	6.9	6.9	-137.10	124.1	8.9	153.7	140.2	13.49	11.390		
2,100.0	2,095.6	2,123.4	2,118.5	7.2	7.2	-136.60	112.7	26.0	153.9	140.0	13.86	11.100 ES		
2,183.7	2,177.2	2,207.7	2,200.7	7.4	7.4	-136.33	102.3	41.6	154.7	140.5	14.14	10.940		
2,200.0	2,193.1	2,224.1	2,216.7	7.4	7.4	-136.34	100.3	44.6	155.0	140.8	14.19	10.920		
2,300.0	2,290.2	2,324.1	2,314.2	7.7	7.7	-136.39	88.0	63.1	156.9	142.2	14.65	10.712		
2,400.0	2,387.4	2,424.0	2,411.6	8.0	8.0	-136.44	75.6	81.5	158.8	143.7	15.10	10.517		
2,500.0	2,484.6	2,524.0	2,509.1	8.3	8.3	-136.49	63.3	100.0	160.7	145.2	15.58	10.317		
2,600.0	2,581.7	2,624.0	2,606.6	8.6	8.6	-136.53	50.9	118.5	162.7	146.6	16.08	10.115		
2,700.0	2,678.9	2,724.0	2,704.1	9.0	9.0	-136.58	38.6	137.0	164.6	148.0	16.60	9.913		
2,800.0	2,776.1	2,824.0	2,801.6	9.3	9.3	-136.62	26.3	155.5	166.5	149.4	17.14	9.713		
2,900.0	2,873.2	2,924.0	2,899.0	9.7	9.7	-136.67	13.9	173.9	168.4	150.7	17.70	9.515		
3,000.0	2,970.4	3,023.9	2,996.5	10.1	10.1	-136.71	1.6	192.4	170.3	152.1	18.27	9.322		
3,100.0	3,067.6	3,123.9	3,094.0	10.4	10.5	-136.75	-10.8	210.9	172.3	153.4	18.86	9.134		
3,200.0	3,164.7	3,223.9	3,191.5	10.8	10.8	-136.79	-23.1	229.4	174.2	154.7	19.46	8.951		
3,300.0	3,261.9	3,323.9	3,289.0	11.2	11.2	-136.83	-35.4	247.9	176.1	156.0	20.07	8.774		
3,400.0	3,359.1	3,423.9	3,386.4	11.6	11.6	-136.87	-47.8	266.3	178.0	157.3	20.69	8.603		
3,500.0	3,456.2	3,523.8	3,483.9	12.1	12.1	-136.91	-60.1	284.8	179.9	158.6	21.33	8.438		
3,600.0	3,553.4	3,623.8	3,581.4	12.5	12.5	-136.95	-72.5	303.3	181.9	159.9	21.97	8.279		
3,700.0	3,650.6	3,723.8	3,678.9	12.9	12.9	-136.98	-84.8	321.8	183.8	161.2	22.62	8.126		
3,800.0	3,747.7	3,823.8	3,776.4	13.3	13.3	-137.02	-97.1	340.3	185.7	162.4	23.27	7.980		
3,900.0	3,844.9	3,923.8	3,873.8	13.8	13.7	-137.06	-109.5	358.7	187.6	163.7	23.94	7.839		
4,000.0	3,942.1	4,023.7	3,971.3	14.2	14.2	-137.09	-121.8	377.2	189.6	164.9	24.61	7.703		
4,100.0	4,039.2	4,123.7	4,068.8	14.6	14.6	-137.12	-134.2	395.7	191.5	166.2	25.28	7.573		
4,200.0	4,136.4	4,223.7	4,166.3	15.1	15.1	-137.16	-146.5	414.2	193.4	167.4	25.97	7.448		
4,300.0	4,233.6	4,323.7	4,263.8	15.5	15.5	-137.19	-158.8	432.7	195.3	168.7	26.65	7.328		
4,400.0	4,330.7	4,423.7	4,361.2	16.0	15.9	-137.22	-171.2	451.1	197.2	169.9	27.35	7.213		
4,500.0	4,427.9	4,523.7	4,458.7	16.4	16.4	-137.25	-183.5	469.6	199.2	171.1	28.04	7.103		
4,600.0	4,525.0	4,623.6	4,556.2	16.9	16.8	-137.28	-195.9	488.1	201.1	172.4	28.74	6.997		
4,700.0	4,622.2	4,723.6	4,653.7	17.3	17.3	-137.31	-208.2	506.6	203.0	173.6	29.45	6.895		
4,800.0	4,719.4	4,823.6	4,751.2	17.8	17.7	-137.34	-220.5	525.1	204.9	174.8	30.15	6.797		
4,900.0	4,816.5	4,923.6	4,848.7	18.2	18.2	-137.37	-232.9	543.5	206.9	176.0	30.86	6.702		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips
Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 504H - Slot DONKEY POTROAST #504H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 504H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design: TARHEEL_DONKEY POTROAST PROJECT - *TARHEEL FED COM #704H - OWB - PWP0													Offset Site Error:	0.0 usft
Survey Program: 0-r.5 MWD+IFR1													Offset Well Error:	3.0 usft
Reference	Offset	Semi Major Axis		Distance		Rule Assigned:		Warning						
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	No-Go Distance (usft)	Separation Factor		
5,000.0	4,913.7	5,023.6	4,946.1	18.7	18.6	-137.40	-245.2	562.0	208.8	177.2	31.58	6.612		
5,100.0	5,010.9	5,123.5	5,043.6	19.2	19.1	-137.43	-257.6	580.5	210.7	178.4	32.30	6.524		
5,200.0	5,108.0	5,223.5	5,141.1	19.6	19.5	-137.45	-269.9	599.0	212.6	179.6	33.02	6.440		
5,300.0	5,205.2	5,323.5	5,238.6	20.1	20.0	-137.48	-282.2	617.5	214.6	180.8	33.74	6.359		
5,400.0	5,302.4	5,423.5	5,336.1	20.5	20.5	-137.51	-294.6	635.9	216.5	182.0	34.46	6.281		
5,500.0	5,399.5	5,523.5	5,433.5	21.0	20.9	-137.53	-306.9	654.4	218.4	183.2	35.19	6.206		
5,547.4	5,445.6	5,570.9	5,479.8	21.2	21.1	-137.54	-312.8	663.2	219.3	183.8	35.52	6.174		
5,600.0	5,496.8	5,623.5	5,531.0	21.5	21.4	-137.52	-319.3	672.9	220.1	184.3	35.88	6.135		
5,700.0	5,594.3	5,723.4	5,628.5	21.9	21.8	-137.24	-331.6	691.4	220.8	184.2	36.51	6.047		
5,800.0	5,692.3	5,823.4	5,726.0	22.4	22.3	-136.64	-343.9	709.9	220.1	183.1	37.02	5.946		
5,900.0	5,790.6	5,920.8	5,821.1	22.8	22.7	-135.89	-355.5	727.2	218.8	181.3	37.44	5.843		
6,000.0	5,889.1	6,018.3	5,916.7	23.3	23.2	-135.14	-366.2	743.2	217.4	179.6	37.83	5.746		
6,100.0	5,988.0	6,115.8	6,012.6	23.7	23.6	-134.39	-376.0	757.8	215.9	177.8	38.18	5.656		
6,200.0	6,087.1	6,213.3	6,108.8	24.1	24.1	-133.64	-384.9	771.1	214.4	176.0	38.49	5.571		
6,300.0	6,186.4	6,310.9	6,205.3	24.5	24.5	-132.88	-392.8	783.1	212.9	174.1	38.76	5.492		
6,400.0	6,285.9	6,408.6	6,302.1	24.9	24.9	-132.12	-399.9	793.7	211.3	172.3	38.99	5.419		
6,500.0	6,385.6	6,506.3	6,399.2	25.3	25.3	-131.36	-406.1	802.9	209.6	170.4	39.17	5.351		
6,600.0	6,485.4	6,604.0	6,496.5	25.6	25.7	-130.59	-411.3	810.7	207.8	168.5	39.30	5.288		
6,700.0	6,585.3	6,701.9	6,594.0	26.0	26.0	-129.81	-415.6	817.2	206.0	166.6	39.39	5.231		
6,800.0	6,685.3	6,800.0	6,692.0	26.3	26.4	-129.03	-419.0	822.3	204.2	164.7	39.42	5.179		
6,900.0	6,785.3	6,897.7	6,789.5	26.5	26.7	-128.24	-421.4	825.9	202.2	162.9	39.37	5.137		
6,914.7	6,800.0	6,912.1	6,804.0	26.5	26.7	-1.23	-421.7	826.4	202.0	162.6	39.35	5.132		
7,000.0	6,885.3	6,995.7	6,887.5	26.5	27.0	-0.70	-423.0	828.2	200.6	161.4	39.25	5.112		
7,100.0	6,985.3	7,093.7	6,985.5	26.5	27.1	-0.45	-423.6	829.1	200.0	160.8	39.22	5.100		
7,139.1	7,024.4	7,132.5	7,024.4	26.6	27.2	-0.44	-423.6	829.1	200.0	160.8	39.24	5.097		
7,200.0	7,085.3	7,193.4	7,085.3	26.6	27.2	-0.44	-423.6	829.1	200.0	160.7	39.28	5.091		
7,300.0	7,185.3	7,293.4	7,185.3	26.6	27.2	-0.44	-423.6	829.1	200.0	160.7	39.36	5.082		
7,400.0	7,285.3	7,393.4	7,285.3	26.6	27.2	-0.44	-423.6	829.1	200.0	160.6	39.43	5.072		
7,500.0	7,385.3	7,493.4	7,385.3	26.6	27.2	-0.44	-423.6	829.1	200.0	160.5	39.51	5.063		
7,600.0	7,485.3	7,593.4	7,485.3	26.7	27.3	-0.44	-423.6	829.1	200.0	160.4	39.58	5.053		
7,700.0	7,585.3	7,693.4	7,585.3	26.7	27.3	-0.44	-423.6	829.1	200.0	160.4	39.66	5.044		
7,800.0	7,685.3	7,793.4	7,685.3	26.7	27.3	-0.44	-423.6	829.1	200.0	160.3	39.73	5.034		
7,900.0	7,785.3	7,893.4	7,785.3	26.7	27.3	-0.44	-423.6	829.1	200.0	160.2	39.81	5.024		
8,000.0	7,885.3	7,993.4	7,885.3	26.8	27.4	-0.44	-423.6	829.1	200.0	160.1	39.89	5.014		
8,100.0	7,985.3	8,093.4	7,985.3	26.8	27.4	-0.44	-423.6	829.1	200.0	160.0	39.96	5.005		
8,200.0	8,085.3	8,193.4	8,085.3	26.8	27.4	-0.44	-423.6	829.1	200.0	160.0	40.04	4.995		
8,300.0	8,185.3	8,293.4	8,185.3	26.8	27.4	-0.44	-423.6	829.1	200.0	159.9	40.12	4.985		
8,400.0	8,285.3	8,393.4	8,285.3	26.9	27.5	-0.44	-423.6	829.1	200.0	159.8	40.20	4.975		
8,500.0	8,385.3	8,493.4	8,385.3	26.9	27.5	-0.44	-423.6	829.1	200.0	159.7	40.28	4.965		
8,600.0	8,485.3	8,593.4	8,485.3	26.9	27.5	-0.44	-423.6	829.1	200.0	159.6	40.36	4.956		
8,700.0	8,585.3	8,693.4	8,585.3	27.0	27.5	-0.44	-423.6	829.1	200.0	159.6	40.44	4.946		
8,800.0	8,685.3	8,793.4	8,685.3	27.0	27.6	-0.44	-423.6	829.1	200.0	159.5	40.52	4.936		
8,900.0	8,785.3	8,893.4	8,785.3	27.0	27.6	-0.44	-423.6	829.1	200.0	159.4	40.60	4.926		
9,000.0	8,885.3	8,993.4	8,885.3	27.0	27.6	-0.44	-423.6	829.1	200.0	159.3	40.69	4.916		
9,100.0	8,985.3	9,093.4	8,985.3	27.1	27.7	-0.44	-423.6	829.1	200.0	159.2	40.77	4.906		
9,200.0	9,085.3	9,193.4	9,085.3	27.1	27.7	-0.44	-423.6	829.1	200.0	159.2	40.85	4.896		
9,300.0	9,185.3	9,293.4	9,185.3	27.1	27.7	-0.44	-423.6	829.1	200.0	159.1	40.94	4.886		
9,400.0	9,285.3	9,393.4	9,285.3	27.2	27.7	-0.44	-423.6	829.1	200.0	159.0	41.02	4.876		
9,500.0	9,385.3	9,493.4	9,385.3	27.2	27.8	-0.44	-423.6	829.1	200.0	158.9	41.10	4.866		
9,600.0	9,485.3	9,593.4	9,485.3	27.2	27.8	-0.44	-423.6	829.1	200.0	158.8	41.19	4.856		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 504H - Slot DONKEY POTROAST #504H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 504H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design:	TARHEEL_DONKEY POTROAST PROJECT - *TARHEEL FED COM #704H - OWB - PWP0											Offset Site Error:	0.0 usft
Survey Program:	0-r.5 MWD+IFR1											Offset Well Error:	3.0 usft
Reference	Offset	Semi Major Axis		Rule Assigned:		Distance		Warning					
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	No-Go Distance (usft)	Separation Factor	
9,700.0	9,585.3	9,693.4	9,585.3	27.2	27.8	-0.44	-423.6	829.1	200.0	158.7	41.27	4.846	
9,800.0	9,685.3	9,793.4	9,685.3	27.3	27.9	-0.44	-423.6	829.1	200.0	158.7	41.36	4.836	
9,900.0	9,785.3	9,893.4	9,785.3	27.3	27.9	-0.44	-423.6	829.1	200.0	158.6	41.45	4.826	
10,000.0	9,885.3	9,993.4	9,885.3	27.3	27.9	-0.44	-423.6	829.1	200.0	158.5	41.53	4.816	
10,100.0	9,985.3	10,093.4	9,985.3	27.4	27.9	-0.44	-423.6	829.1	200.0	158.4	41.62	4.806	
10,116.7	10,002.0	10,110.2	10,002.0	27.4	27.9	-0.44	-423.6	829.1	200.0	158.4	41.63	4.804 SF	
10,150.0	10,035.2	10,143.4	10,035.2	27.4	28.0	179.95	-423.6	829.1	201.0	159.3	41.70	4.820	
10,200.0	10,085.0	10,193.1	10,085.0	27.5	28.0	179.95	-423.6	829.1	206.0	164.1	41.91	4.917	
10,250.0	10,134.1	10,242.2	10,134.1	27.7	28.0	179.95	-423.6	829.1	215.4	173.3	42.14	5.112	
10,300.0	10,182.1	10,290.3	10,182.1	27.8	28.0	179.95	-423.6	829.1	229.1	186.7	42.39	5.404	
10,350.0	10,228.9	10,337.0	10,228.9	28.0	28.0	179.95	-423.6	829.1	246.8	204.2	42.64	5.789	
10,400.0	10,273.9	10,382.0	10,273.9	28.1	28.0	179.95	-423.6	829.1	268.6	225.7	42.90	6.261	
10,450.0	10,316.8	10,425.0	10,316.8	28.3	28.0	179.96	-423.6	829.1	294.2	251.1	43.16	6.817	
10,500.0	10,357.3	10,465.5	10,357.3	28.5	28.1	179.96	-423.6	829.1	323.5	280.1	43.41	7.452	
10,550.0	10,395.1	10,503.3	10,395.1	28.6	28.1	179.96	-423.6	829.1	356.2	312.5	43.65	8.159	
10,600.0	10,430.0	10,538.1	10,430.0	28.8	28.1	179.96	-423.6	829.1	392.0	348.1	43.88	8.934	
10,650.0	10,461.5	10,569.7	10,461.5	28.9	28.1	179.96	-423.6	829.1	430.8	386.7	44.09	9.769	
10,700.0	10,489.6	10,597.8	10,489.6	29.1	28.1	179.96	-423.6	829.1	472.1	427.8	44.29	10.660	
10,750.0	10,514.0	10,622.2	10,514.0	29.2	28.1	179.95	-423.6	829.1	515.8	471.3	44.46	11.601	
10,800.0	10,534.4	10,642.6	10,534.4	29.3	28.1	179.95	-423.6	829.1	561.4	516.8	44.61	12.585	
10,850.0	10,550.9	10,659.0	10,550.9	29.4	28.1	179.94	-423.6	829.1	608.6	563.8	44.73	13.606	
10,900.0	10,563.1	10,671.3	10,563.1	29.5	28.1	179.92	-423.6	829.1	657.0	612.2	44.82	14.659	
10,950.0	10,571.1	10,679.3	10,571.1	29.5	28.1	179.87	-423.6	829.1	706.4	661.5	44.89	15.737	
11,000.0	10,574.7	10,682.9	10,574.7	29.6	28.1	179.52	-423.6	829.1	756.2	711.3	44.92	16.834	
11,016.7	10,575.0	10,683.1	10,575.0	29.6	28.1	90.66	-423.6	829.1	773.0	728.0	44.93	17.205	
11,100.0	10,575.0	10,683.1	10,575.0	29.6	28.1	90.73	-423.6	829.1	856.2	811.3	44.95	19.050	
11,200.0	10,575.0	10,683.1	10,575.0	29.7	28.1	90.82	-423.6	829.1	956.2	911.3	44.97	21.264	

CC - Min centre to center distance or covergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 504H - Slot DONKEY POTROAST #504H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 504H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design: TARHEEL_DONKEY POTROAST PROJECT - _DONKEY POTROAST FED COM 503H - OWB - PWP0												Offset Site Error:	0.0 usft
Survey Program: 0-r.5 MWD+IFR1												Offset Well Error:	3.0 usft
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Semi Major Axis Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre		Distance Between Centres (usft)		No-Go Distance (usft)	Separation Factor	Warning
							+N/-S (usft)	+E/-W (usft)					
0.0	0.0	0.0	0.0	3.0	3.0	-90.84	-0.4	-30.1	30.1	23.7	6.43	4.680	
100.0	100.0	100.0	100.0	3.2	3.2	-90.84	-0.4	-30.1	30.1	23.2	6.89	4.366	
200.0	200.0	200.0	200.0	3.5	3.5	-90.84	-0.4	-30.1	30.1	22.8	7.33	4.106	
300.0	300.0	300.0	300.0	3.7	3.7	-90.84	-0.4	-30.1	30.1	22.3	7.74	3.887	
400.0	400.0	400.0	400.0	3.9	3.9	-90.84	-0.4	-30.1	30.1	22.0	8.14	3.698	
500.0	500.0	500.0	500.0	4.1	4.1	-90.84	-0.4	-30.1	30.1	21.6	8.51	3.534	
600.0	600.0	600.0	600.0	4.2	4.2	-90.84	-0.4	-30.1	30.1	21.2	8.88	3.389	
700.0	700.0	700.0	700.0	4.4	4.4	-90.84	-0.4	-30.1	30.1	20.9	9.23	3.260	
800.0	800.0	800.0	800.0	4.6	4.6	-90.84	-0.4	-30.1	30.1	20.5	9.57	3.144	
900.0	900.0	900.0	900.0	4.8	4.8	-90.84	-0.4	-30.1	30.1	20.2	9.90	3.039	
1,000.0	1,000.0	1,000.0	1,000.0	4.9	4.9	-90.84	-0.4	-30.1	30.1	19.9	10.22	2.943 Normal Operations	
1,100.0	1,100.0	1,100.0	1,100.0	5.1	5.1	-90.84	-0.4	-30.1	30.1	19.5	10.54	2.855 Normal Operations	
1,200.0	1,200.0	1,200.0	1,200.0	5.2	5.2	-90.84	-0.4	-30.1	30.1	19.2	10.85	2.774 Normal Operations	
1,300.0	1,300.0	1,300.0	1,300.0	5.4	5.4	-90.84	-0.4	-30.1	30.1	18.9	11.15	2.699 Normal Operations	
1,400.0	1,400.0	1,400.0	1,400.0	5.5	5.5	-90.84	-0.4	-30.1	30.1	18.6	11.44	2.629 Normal Operations	
1,500.0	1,500.0	1,500.0	1,500.0	5.7	5.7	-90.84	-0.4	-30.1	30.1	18.4	11.73	2.564 Normal Operations, CC, ES, SF	
1,600.0	1,600.0	1,599.3	1,599.3	5.9	5.9	141.65	-1.8	-31.1	32.5	20.4	12.07	2.692 Normal Operations	
1,700.0	1,699.8	1,698.3	1,698.1	6.1	6.1	140.25	-6.0	-34.0	39.7	27.3	12.38	3.208	
1,800.0	1,799.5	1,796.6	1,796.1	6.3	6.3	138.75	-13.0	-38.9	51.7	39.0	12.70	4.074	
1,900.0	1,898.7	1,893.9	1,892.6	6.6	6.6	137.49	-22.5	-45.7	68.5	55.5	13.03	5.258	
2,000.0	1,997.5	1,989.8	1,987.4	6.9	6.8	136.49	-34.5	-54.2	90.0	76.6	13.38	6.727	
2,100.0	2,095.6	2,085.8	2,081.8	7.2	7.0	135.97	-48.6	-64.1	115.6	101.9	13.70	8.433	
2,183.7	2,177.2	2,166.1	2,160.8	7.4	7.2	136.29	-60.4	-72.5	138.9	124.9	14.00	9.924	
2,200.0	2,193.1	2,181.7	2,176.2	7.4	7.2	136.47	-62.8	-74.2	143.7	129.6	14.05	10.226	
2,300.0	2,290.2	2,277.4	2,270.3	7.7	7.5	137.31	-76.9	-84.2	172.6	158.2	14.45	11.944	
2,400.0	2,387.4	2,373.1	2,364.4	8.0	7.8	137.92	-91.0	-94.2	201.6	186.8	14.86	13.572	
2,500.0	2,484.6	2,468.8	2,458.5	8.3	8.0	138.37	-105.2	-104.2	230.7	215.4	15.28	15.093	
2,600.0	2,581.7	2,564.5	2,552.6	8.6	8.3	138.72	-119.3	-114.2	259.7	244.0	15.73	16.512	
2,700.0	2,678.9	2,660.1	2,646.7	9.0	8.6	139.01	-133.4	-124.2	288.7	272.5	16.19	17.833	
2,800.0	2,776.1	2,755.8	2,740.8	9.3	8.9	139.23	-147.6	-134.2	317.8	301.1	16.67	19.061	
2,900.0	2,873.2	2,851.5	2,834.9	9.7	9.3	139.43	-161.7	-144.2	346.8	329.7	17.17	20.202	
3,000.0	2,970.4	2,947.2	2,929.0	10.1	9.6	139.59	-175.8	-154.2	375.9	358.2	17.68	21.262	
3,100.0	3,067.6	3,042.9	3,023.1	10.4	10.0	139.73	-190.0	-164.2	404.9	386.7	18.20	22.247	
3,200.0	3,164.7	3,138.5	3,117.2	10.8	10.3	139.85	-204.1	-174.2	434.0	415.2	18.74	23.162	
3,300.0	3,261.9	3,234.2	3,211.3	11.2	10.7	139.95	-218.2	-184.2	463.0	443.7	19.28	24.013	
3,400.0	3,359.1	3,329.9	3,305.4	11.6	11.0	140.04	-232.4	-194.2	492.1	472.2	19.84	24.804	
3,500.0	3,456.2	3,425.6	3,399.5	12.1	11.4	140.13	-246.5	-204.2	521.1	500.7	20.40	25.540	
3,600.0	3,553.4	3,521.3	3,493.6	12.5	11.8	140.20	-260.6	-214.2	550.2	529.2	20.98	26.227	
3,700.0	3,650.6	3,617.0	3,587.8	12.9	12.1	140.27	-274.8	-224.2	579.3	557.7	21.56	26.867	
3,800.0	3,747.7	3,712.6	3,681.9	13.3	12.5	140.32	-288.9	-234.2	608.3	586.2	22.15	27.465	
3,900.0	3,844.9	3,808.3	3,776.0	13.8	12.9	140.38	-303.0	-244.2	637.4	614.6	22.74	28.023	
4,000.0	3,942.1	3,904.0	3,870.1	14.2	13.3	140.43	-317.2	-254.2	666.4	643.1	23.35	28.546	
4,100.0	4,039.2	3,999.7	3,964.2	14.6	13.7	140.47	-331.3	-264.2	695.5	671.6	23.95	29.035	
4,200.0	4,136.4	4,095.4	4,058.3	15.1	14.1	140.52	-345.4	-274.2	724.6	700.0	24.57	29.494	
4,300.0	4,233.6	4,191.1	4,152.4	15.5	14.5	140.55	-359.6	-284.2	753.6	728.4	25.18	29.925	
4,400.0	4,330.7	4,286.7	4,246.5	16.0	14.9	140.59	-373.7	-294.2	782.7	756.9	25.81	30.330	
4,500.0	4,427.9	4,382.4	4,340.6	16.4	15.3	140.62	-387.8	-304.2	811.8	785.3	26.43	30.712	
4,600.0	4,525.0	4,478.1	4,434.7	16.9	15.7	140.65	-402.0	-314.2	840.8	813.8	27.06	31.071	
4,700.0	4,622.2	4,573.8	4,528.8	17.3	16.1	140.68	-416.1	-324.2	869.9	842.2	27.69	31.409	
4,800.0	4,719.4	4,669.5	4,622.9	17.8	16.5	140.71	-430.2	-334.2	898.9	870.6	28.33	31.729	
4,900.0	4,816.5	4,765.2	4,717.0	18.2	16.9	140.74	-444.4	-344.2	928.0	899.0	28.97	32.031	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips
Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 504H - Slot DONKEY POTROAST #504H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 504H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design:	TARHEEL_DONKEY POTROAST PROJECT - _DONKEY POTROAST FED COM 503H - OWB - PWP0											Offset Site Error:	0.0 usft
Survey Program:	0-r.5 MWD+IFR1											Offset Well Error:	3.0 usft
Reference	Offset	Semi Major Axis		Offset Wellbore Centre		Rule Assigned:		Distance		Warning			
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	No-Go Distance (usft)	Separation Factor	
5,000.0	4,913.7	4,860.8	4,811.1	18.7	17.3	140.76	-458.5	-354.2	957.1	927.5	29.61	32.317	
5,100.0	5,010.9	4,956.5	4,905.2	19.2	17.8	140.78	-472.6	-364.2	986.1	955.9	30.26	32.588	

ConocoPhillips

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 504H - Slot DONKEY POTROAST #504H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 504H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design: TARHEEL_DONKEY POTROAST PROJECT - _DONKEY POTROAST FED COM 703H - OWB - PWP0												Offset Site Error:	0.0 usft
Survey Program: 0-r.5 MWD+IFR1												Offset Well Error:	3.0 usft
Reference		Offset		Semi Major Axis		Highside Toolface (°)	Offset Wellbore Centre		Distance		No-Go Distance (usft)	Separation Factor	Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)		+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)			
0.0	0.0	0.0	0.0	3.0	3.0	-90.42	-0.4	-60.0	60.0	53.6	6.43	9.333	
100.0	100.0	100.0	100.0	3.2	3.2	-90.42	-0.4	-60.0	60.0	53.1	6.89	8.705	
200.0	200.0	200.0	200.0	3.5	3.5	-90.42	-0.4	-60.0	60.0	52.7	7.33	8.188	
300.0	300.0	300.0	300.0	3.7	3.7	-90.42	-0.4	-60.0	60.0	52.3	7.74	7.751	
400.0	400.0	400.0	400.0	3.9	3.9	-90.42	-0.4	-60.0	60.0	51.9	8.14	7.375	
500.0	500.0	500.0	500.0	4.1	4.1	-90.42	-0.4	-60.0	60.0	51.5	8.51	7.048	
600.0	600.0	600.0	600.0	4.2	4.2	-90.42	-0.4	-60.0	60.0	51.1	8.88	6.759	
700.0	700.0	700.0	700.0	4.4	4.4	-90.42	-0.4	-60.0	60.0	50.8	9.23	6.501	
800.0	800.0	800.0	800.0	4.6	4.6	-90.42	-0.4	-60.0	60.0	50.4	9.57	6.269	
900.0	900.0	900.0	900.0	4.8	4.8	-90.42	-0.4	-60.0	60.0	50.1	9.90	6.059	
1,000.0	1,000.0	1,000.0	1,000.0	4.9	4.9	-90.42	-0.4	-60.0	60.0	49.8	10.22	5.868	
1,100.0	1,100.0	1,100.0	1,100.0	5.1	5.1	-90.42	-0.4	-60.0	60.0	49.5	10.54	5.693	
1,200.0	1,200.0	1,200.0	1,200.0	5.2	5.2	-90.42	-0.4	-60.0	60.0	49.2	10.85	5.531	
1,300.0	1,300.0	1,300.0	1,300.0	5.4	5.4	-90.42	-0.4	-60.0	60.0	48.9	11.15	5.382	
1,400.0	1,400.0	1,400.0	1,400.0	5.5	5.5	-90.42	-0.4	-60.0	60.0	48.6	11.44	5.243	
1,500.0	1,500.0	1,500.0	1,500.0	5.7	5.7	-90.42	-0.4	-60.0	60.0	48.3	11.73	5.113 CC, ES, SF	
1,600.0	1,600.0	1,598.6	1,598.6	5.9	5.9	142.39	-1.8	-61.0	62.5	50.4	12.07	5.174	
1,700.0	1,699.8	1,696.9	1,696.8	6.1	6.1	141.64	-5.8	-64.2	69.8	57.5	12.39	5.639	
1,800.0	1,799.5	1,794.5	1,794.0	6.3	6.3	140.66	-12.3	-69.3	82.1	69.4	12.71	6.462	
1,900.0	1,898.7	1,891.0	1,889.8	6.6	6.6	139.67	-21.4	-76.5	99.3	86.2	13.05	7.609	
2,000.0	1,997.5	1,987.3	1,985.0	6.9	6.7	138.86	-32.7	-85.4	121.0	107.7	13.33	9.078	
2,100.0	2,095.6	2,084.2	2,080.8	7.2	6.9	138.94	-44.5	-94.6	145.6	131.9	13.69	10.633	
2,183.7	2,177.2	2,164.7	2,160.3	7.4	7.1	139.50	-54.3	-102.3	168.2	154.2	14.00	12.015	
2,200.0	2,193.1	2,180.4	2,175.8	7.4	7.1	139.69	-56.2	-103.8	172.8	158.7	14.05	12.298	
2,300.0	2,290.2	2,276.3	2,270.6	7.7	7.4	140.70	-67.9	-113.0	200.9	186.5	14.46	13.892	
2,400.0	2,387.4	2,372.2	2,365.3	8.0	7.6	141.46	-79.5	-122.2	229.1	214.2	14.87	15.404	
2,500.0	2,484.6	2,468.2	2,460.1	8.3	7.9	142.05	-91.2	-131.4	257.3	242.0	15.30	16.813	
2,600.0	2,581.7	2,564.1	2,554.8	8.6	8.2	142.53	-102.9	-140.5	285.5	269.7	15.75	18.124	
2,700.0	2,678.9	2,660.0	2,649.6	9.0	8.5	142.92	-114.5	-149.7	313.7	297.5	16.22	19.340	
2,800.0	2,776.1	2,755.9	2,744.4	9.3	8.8	143.24	-126.2	-158.9	341.9	325.2	16.71	20.469	
2,900.0	2,873.2	2,851.8	2,839.1	9.7	9.1	143.52	-137.8	-168.0	370.2	353.0	17.21	21.515	
3,000.0	2,970.4	2,947.7	2,933.9	10.1	9.5	143.76	-149.5	-177.2	398.4	380.7	17.72	22.485	
3,100.0	3,067.6	3,043.6	3,028.6	10.4	9.8	143.96	-161.2	-186.4	426.7	408.4	18.25	23.383	
3,200.0	3,164.7	3,139.6	3,123.4	10.8	10.1	144.14	-172.8	-195.6	455.0	436.2	18.79	24.216	
3,300.0	3,261.9	3,235.5	3,218.1	11.2	10.5	144.30	-184.5	-204.7	483.2	463.9	19.34	24.989	
3,400.0	3,359.1	3,331.4	3,312.9	11.6	10.8	144.44	-196.2	-213.9	511.5	491.6	19.90	25.706	
3,500.0	3,456.2	3,427.3	3,407.7	12.1	11.2	144.57	-207.8	-223.1	539.8	519.3	20.47	26.372	
3,600.0	3,553.4	3,523.2	3,502.4	12.5	11.6	144.68	-219.5	-232.3	568.0	547.0	21.04	26.992	
3,700.0	3,650.6	3,619.1	3,597.2	12.9	11.9	144.79	-231.2	-241.4	596.3	574.7	21.63	27.569	
3,800.0	3,747.7	3,715.0	3,691.9	13.3	12.3	144.88	-242.8	-250.6	624.6	602.4	22.22	28.107	
3,900.0	3,844.9	3,811.0	3,786.7	13.8	12.7	144.96	-254.5	-259.8	652.9	630.0	22.82	28.608	
4,000.0	3,942.1	3,906.9	3,881.5	14.2	13.0	145.04	-266.2	-269.0	681.2	657.7	23.43	29.077	
4,100.0	4,039.2	4,002.8	3,976.2	14.6	13.4	145.12	-277.8	-278.1	709.4	685.4	24.04	29.515	
4,200.0	4,136.4	4,098.7	4,071.0	15.1	13.8	145.18	-289.5	-287.3	737.7	713.1	24.65	29.925	
4,300.0	4,233.6	4,194.6	4,165.7	15.5	14.2	145.24	-301.2	-296.5	766.0	740.7	25.27	30.309	
4,400.0	4,330.7	4,290.5	4,260.5	16.0	14.6	145.30	-312.8	-305.6	794.3	768.4	25.90	30.670	
4,500.0	4,427.9	4,386.4	4,355.3	16.4	15.0	145.36	-324.5	-314.8	822.6	796.0	26.53	31.009	
4,600.0	4,525.0	4,482.4	4,450.0	16.9	15.4	145.41	-336.2	-324.0	850.8	823.7	27.16	31.328	
4,700.0	4,622.2	4,578.3	4,544.8	17.3	15.8	145.45	-347.8	-333.2	879.1	851.3	27.80	31.628	
4,800.0	4,719.4	4,674.2	4,639.5	17.8	16.2	145.50	-359.5	-342.3	907.4	879.0	28.44	31.912	
4,900.0	4,816.5	4,770.1	4,734.3	18.2	16.6	145.54	-371.2	-351.5	935.7	906.6	29.08	32.179	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 504H - Slot DONKEY POTROAST #504H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 504H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design:	TARHEEL_DONKEY POTROAST PROJECT - _DONKEY POTROAST FED COM 703H - OWB - PWP0											Offset Site Error:	0.0 usft
Survey Program:	0-r.5 MWD+IFR1											Offset Well Error:	3.0 usft
Reference	Offset	Semi Major Axis		Rule Assigned:		Distance		No-Go		Separation		Warning	
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Distance (usft)	Factor	
5,000.0	4,913.7	4,866.0	4,829.0	18.7	16.9	145.58	-382.8	-360.7	964.0	934.3	29.72	32.431	
5,100.0	5,010.9	4,961.9	4,923.8	19.2	17.3	145.61	-394.5	-369.9	992.3	961.9	30.37	32.670	

ConocoPhillips

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 504H - Slot DONKEY POTROAST #504H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 504H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design: TARHEEL_DONKEY POTROAST PROJECT - _DONKEY POTROAST FED COM 704H - OWB - PWP0												Offset Site Error:	0.0 usft
Survey Program: 0-r.5 MWD+IFR1												Offset Well Error:	3.0 usft
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Semi Reference (usft)	Major Axis Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre		Distance Between Centres (usft)		No-Go Distance (usft)	Separation Factor	Warning
							+N/-S (usft)	+E/-W (usft)					
0.0	0.0	0.0	0.0	3.0	3.0	89.47	0.3	30.0	30.0	23.6	6.43	4.666	
100.0	100.0	100.0	100.0	3.2	3.2	89.47	0.3	30.0	30.0	23.1	6.89	4.353	
200.0	200.0	200.0	200.0	3.5	3.5	89.47	0.3	30.0	30.0	22.7	7.33	4.094	
300.0	300.0	300.0	300.0	3.7	3.7	89.47	0.3	30.0	30.0	22.3	7.74	3.875	
400.0	400.0	400.0	400.0	3.9	3.9	89.47	0.3	30.0	30.0	21.9	8.14	3.688	
500.0	500.0	500.0	500.0	4.1	4.1	89.47	0.3	30.0	30.0	21.5	8.51	3.524	
600.0	600.0	600.0	600.0	4.2	4.2	89.47	0.3	30.0	30.0	21.1	8.88	3.379	
700.0	700.0	700.0	700.0	4.4	4.4	89.47	0.3	30.0	30.0	20.8	9.23	3.250	
800.0	800.0	800.0	800.0	4.6	4.6	89.47	0.3	30.0	30.0	20.4	9.57	3.135	
900.0	900.0	900.0	900.0	4.8	4.8	89.47	0.3	30.0	30.0	20.1	9.90	3.030	
1,000.0	1,000.0	1,000.0	1,000.0	4.9	4.9	89.47	0.3	30.0	30.0	19.8	10.22	2.934 Normal Operations	
1,100.0	1,100.0	1,100.0	1,100.0	5.1	5.1	89.47	0.3	30.0	30.0	19.5	10.54	2.846 Normal Operations	
1,200.0	1,200.0	1,200.0	1,200.0	5.2	5.2	89.47	0.3	30.0	30.0	19.2	10.85	2.766 Normal Operations	
1,300.0	1,300.0	1,300.0	1,300.0	5.4	5.4	89.47	0.3	30.0	30.0	18.9	11.15	2.691 Normal Operations	
1,400.0	1,400.0	1,400.0	1,400.0	5.5	5.5	89.47	0.3	30.0	30.0	18.6	11.44	2.621 Normal Operations	
1,500.0	1,500.0	1,500.0	1,500.0	5.7	5.7	89.47	0.3	30.0	30.0	18.3	11.73	2.557 Normal Operations, CC	
1,600.0	1,600.0	1,599.1	1,599.1	5.9	5.9	-37.62	-0.7	31.4	30.1	18.0	12.10	2.484 Caution - Monitor Closely	
1,700.0	1,699.8	1,698.3	1,698.1	6.1	6.1	-38.18	-3.5	35.7	30.2	17.8	12.44	2.430 Caution - Monitor Closely	
1,800.0	1,799.5	1,797.4	1,796.9	6.3	6.3	-39.11	-8.2	42.9	30.5	17.7	12.78	2.386 Caution - Monitor Closely, ES	
1,900.0	1,898.7	1,896.5	1,895.3	6.6	6.6	-40.38	-14.7	52.9	30.9	17.8	13.14	2.352 Caution - Monitor Closely	
2,000.0	1,997.5	1,995.7	1,993.2	6.9	6.9	-41.97	-23.1	65.8	31.4	17.9	13.50	2.328 Caution - Monitor Closely	
2,100.0	2,095.6	2,094.8	2,090.6	7.2	7.2	-43.82	-33.4	81.5	32.1	18.3	13.87	2.316 Caution - Monitor Closely, SF	
2,183.7	2,177.2	2,177.8	2,171.5	7.4	7.4	-45.56	-43.4	96.8	32.8	18.7	14.11	2.327 Caution - Monitor Closely	
2,200.0	2,193.1	2,194.1	2,187.4	7.4	7.4	-45.92	-45.5	100.0	33.0	18.8	14.14	2.332 Caution - Monitor Closely	
2,300.0	2,290.2	2,294.1	2,284.6	7.7	7.7	-48.07	-58.3	119.6	33.9	19.4	14.53	2.332 Caution - Monitor Closely	
2,400.0	2,387.4	2,394.1	2,381.8	8.0	8.0	-50.11	-71.0	139.2	34.9	20.0	14.90	2.339 Caution - Monitor Closely	
2,500.0	2,484.6	2,494.1	2,479.0	8.3	8.3	-52.04	-83.8	158.8	35.9	20.6	15.27	2.348 Caution - Monitor Closely	
2,600.0	2,581.7	2,594.1	2,576.2	8.6	8.6	-53.86	-96.6	178.4	36.9	21.2	15.65	2.357 Caution - Monitor Closely	
2,700.0	2,678.9	2,694.1	2,673.4	9.0	8.9	-55.57	-109.4	197.9	38.0	21.9	16.03	2.369 Caution - Monitor Closely	
2,800.0	2,776.1	2,794.0	2,770.6	9.3	9.3	-57.20	-122.2	217.5	39.1	22.7	16.41	2.382 Caution - Monitor Closely	
2,900.0	2,873.2	2,894.0	2,867.8	9.7	9.6	-58.73	-135.0	237.1	40.2	23.4	16.79	2.396 Caution - Monitor Closely	
3,000.0	2,970.4	2,994.0	2,965.1	10.1	10.0	-60.17	-147.8	256.7	41.4	24.2	17.17	2.411 Caution - Monitor Closely	
3,100.0	3,067.6	3,094.0	3,062.3	10.4	10.4	-61.54	-160.6	276.3	42.6	25.0	17.54	2.427 Caution - Monitor Closely	
3,200.0	3,164.7	3,194.0	3,159.5	10.8	10.8	-62.83	-173.4	295.9	43.8	25.9	17.92	2.444 Caution - Monitor Closely	
3,300.0	3,261.9	3,294.0	3,256.7	11.2	11.2	-64.05	-186.2	315.5	45.0	26.7	18.29	2.462 Caution - Monitor Closely	
3,400.0	3,359.1	3,394.0	3,353.9	11.6	11.6	-65.21	-199.0	335.1	46.3	27.6	18.66	2.480 Caution - Monitor Closely	
3,500.0	3,456.2	3,494.0	3,451.1	12.1	12.0	-66.30	-211.8	354.6	47.5	28.5	19.03	2.499 Caution - Monitor Closely	
3,600.0	3,553.4	3,593.9	3,548.3	12.5	12.4	-67.34	-224.6	374.2	48.8	29.4	19.40	2.518 Normal Operations	
3,700.0	3,650.6	3,693.9	3,645.5	12.9	12.9	-68.32	-237.4	393.8	50.1	30.4	19.76	2.537 Normal Operations	
3,800.0	3,747.7	3,793.9	3,742.8	13.3	13.3	-69.26	-250.2	413.4	51.5	31.3	20.13	2.556 Normal Operations	
3,900.0	3,844.9	3,893.9	3,840.0	13.8	13.7	-70.14	-263.0	433.0	52.8	32.3	20.50	2.576 Normal Operations	
4,000.0	3,942.1	3,993.9	3,937.2	14.2	14.1	-70.98	-275.8	452.6	54.1	33.3	20.86	2.595 Normal Operations	
4,100.0	4,039.2	4,093.9	4,034.4	14.6	14.6	-71.79	-288.6	472.2	55.5	34.3	21.23	2.614 Normal Operations	
4,200.0	4,136.4	4,193.9	4,131.6	15.1	15.0	-72.55	-301.4	491.8	56.8	35.3	21.59	2.632 Normal Operations	
4,300.0	4,233.6	4,293.9	4,228.8	15.5	15.5	-73.28	-314.2	511.3	58.2	36.3	21.96	2.651 Normal Operations	
4,400.0	4,330.7	4,393.9	4,326.0	16.0	15.9	-73.97	-327.0	530.9	59.6	37.3	22.33	2.669 Normal Operations	
4,500.0	4,427.9	4,493.8	4,423.2	16.4	16.4	-74.63	-339.7	550.5	61.0	38.3	22.70	2.687 Normal Operations	
4,600.0	4,525.0	4,593.8	4,520.4	16.9	16.8	-75.27	-352.5	570.1	62.4	39.3	23.07	2.705 Normal Operations	
4,700.0	4,622.2	4,693.8	4,617.7	17.3	17.3	-75.87	-365.3	589.7	63.8	40.4	23.44	2.722 Normal Operations	
4,800.0	4,719.4	4,793.8	4,714.9	17.8	17.7	-76.45	-378.1	609.3	65.2	41.4	23.81	2.738 Normal Operations	
4,900.0	4,816.5	4,893.8	4,812.1	18.2	18.2	-77.00	-390.9	628.9	66.6	42.4	24.19	2.755 Normal Operations	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips
Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 504H - Slot DONKEY POTROAST #504H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 504H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design: TARHEEL_DONKEY POTROAST PROJECT - _DONKEY POTROAST FED COM 704H - OWB - PWP0													Offset Site Error: 0.0 usft	
Survey Program: 0-r.5 MWD+IFR1													Offset Well Error: 3.0 usft	
Reference		Offset		Semi Major Axis			Offset Wellbore Centre			Rule Assigned: Distance		Offset Well Error: 3.0 usft		
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	No-Go Distance (usft)	Separation Factor	Warning	
5,000.0	4,913.7	4,993.8	4,909.3	18.7	18.6	-77.53	-403.7	648.5	68.0	43.5	24.56	2.771	Normal Operations	
5,100.0	5,010.9	5,093.8	5,006.5	19.2	19.1	-78.04	-416.5	668.0	69.5	44.5	24.94	2.786	Normal Operations	
5,200.0	5,108.0	5,193.8	5,103.7	19.6	19.6	-78.53	-429.3	687.6	70.9	45.6	25.31	2.801	Normal Operations	
5,300.0	5,205.2	5,293.9	5,201.1	20.1	20.0	-79.13	-442.0	707.1	72.3	46.7	25.64	2.820	Normal Operations	
5,400.0	5,302.4	5,394.2	5,299.0	20.5	20.5	-80.81	-454.0	725.4	73.4	47.6	25.82	2.842	Normal Operations	
5,500.0	5,399.5	5,494.3	5,397.1	21.0	20.9	-83.77	-465.0	742.3	74.2	48.3	25.85	2.870	Normal Operations	
5,547.4	5,445.6	5,541.8	5,443.7	21.2	21.1	-85.61	-469.9	749.8	74.6	48.7	25.82	2.887	Normal Operations	
5,600.0	5,496.8	5,594.4	5,495.4	21.5	21.4	-87.80	-475.1	757.7	75.0	49.2	25.84	2.903	Normal Operations	
5,700.0	5,594.3	5,694.3	5,594.0	21.9	21.8	-91.87	-484.2	771.6	76.1	50.0	26.05	2.921	Normal Operations	
5,800.0	5,692.3	5,794.2	5,692.7	22.4	22.2	-95.81	-492.4	784.1	77.4	50.9	26.49	2.923	Normal Operations	
5,900.0	5,790.6	5,893.9	5,791.6	22.8	22.6	-99.61	-499.6	795.2	79.0	51.9	27.14	2.911	Normal Operations	
6,000.0	5,889.1	5,993.6	5,890.6	23.3	23.0	-103.26	-505.8	804.8	80.8	52.8	27.98	2.887	Normal Operations	
6,100.0	5,988.0	6,093.2	5,989.7	23.7	23.4	-106.75	-511.2	812.9	82.8	53.8	28.98	2.857	Normal Operations	
6,200.0	6,087.1	6,192.6	6,088.8	24.1	23.8	-110.09	-515.5	819.6	85.0	54.9	30.11	2.822	Normal Operations	
6,300.0	6,186.4	6,292.0	6,188.0	24.5	24.1	-113.26	-519.0	824.9	87.3	56.0	31.32	2.788	Normal Operations	
6,400.0	6,285.9	6,391.3	6,287.2	24.9	24.5	-116.29	-521.5	828.7	89.8	57.2	32.58	2.756	Normal Operations	
6,500.0	6,385.6	6,490.6	6,386.4	25.3	24.8	-119.17	-523.0	831.1	92.4	58.6	33.86	2.729	Normal Operations	
6,600.0	6,485.4	6,589.7	6,485.5	25.6	24.9	-121.91	-523.6	832.0	95.2	60.1	35.10	2.711	Normal Operations	
6,700.0	6,585.3	6,689.5	6,585.3	26.0	25.0	-124.22	-523.6	832.0	97.7	61.5	36.19	2.698	Normal Operations	
6,800.0	6,685.3	6,789.4	6,685.3	26.3	25.0	-125.60	-523.6	832.0	99.3	62.4	36.94	2.688	Normal Operations	
6,900.0	6,785.3	6,889.4	6,785.3	26.5	25.0	-126.13	-523.6	832.0	100.0	62.6	37.33	2.678	Normal Operations	
6,914.7	6,800.0	6,904.2	6,800.0	26.5	25.0	0.75	-523.6	832.0	100.0	62.6	37.35	2.677	Normal Operations	
7,000.0	6,885.3	6,989.4	6,885.3	26.5	25.0	0.75	-523.6	832.0	100.0	62.6	37.42	2.672	Normal Operations	
7,100.0	6,985.3	7,089.4	6,985.3	26.5	25.1	0.75	-523.6	832.0	100.0	62.5	37.50	2.666	Normal Operations	
7,200.0	7,085.3	7,189.4	7,085.3	26.6	25.1	0.75	-523.6	832.0	100.0	62.4	37.58	2.661	Normal Operations	
7,300.0	7,185.3	7,289.4	7,185.3	26.6	25.1	0.75	-523.6	832.0	100.0	62.3	37.66	2.655	Normal Operations	
7,400.0	7,285.3	7,389.4	7,285.3	26.6	25.2	0.75	-523.6	832.0	100.0	62.2	37.74	2.650	Normal Operations	
7,500.0	7,385.3	7,489.4	7,385.3	26.6	25.2	0.75	-523.6	832.0	100.0	62.2	37.82	2.644	Normal Operations	
7,600.0	7,485.3	7,589.4	7,485.3	26.7	25.2	0.75	-523.6	832.0	100.0	62.1	37.90	2.638	Normal Operations	
7,700.0	7,585.3	7,689.4	7,585.3	26.7	25.2	0.75	-523.6	832.0	100.0	62.0	37.98	2.633	Normal Operations	
7,800.0	7,685.3	7,789.4	7,685.3	26.7	25.3	0.75	-523.6	832.0	100.0	61.9	38.06	2.627	Normal Operations	
7,900.0	7,785.3	7,889.4	7,785.3	26.7	25.3	0.75	-523.6	832.0	100.0	61.8	38.15	2.621	Normal Operations	
8,000.0	7,885.3	7,989.4	7,885.3	26.8	25.3	0.75	-523.6	832.0	100.0	61.8	38.23	2.615	Normal Operations	
8,100.0	7,985.3	8,089.4	7,985.3	26.8	25.4	0.75	-523.6	832.0	100.0	61.7	38.31	2.610	Normal Operations	
8,200.0	8,085.3	8,189.4	8,085.3	26.8	25.4	0.75	-523.6	832.0	100.0	61.6	38.40	2.604	Normal Operations	
8,300.0	8,185.3	8,289.4	8,185.3	26.8	25.4	0.75	-523.6	832.0	100.0	61.5	38.48	2.598	Normal Operations	
8,400.0	8,285.3	8,389.4	8,285.3	26.9	25.5	0.75	-523.6	832.0	100.0	61.4	38.57	2.593	Normal Operations	
8,500.0	8,385.3	8,489.4	8,385.3	26.9	25.5	0.75	-523.6	832.0	100.0	61.3	38.65	2.587	Normal Operations	
8,600.0	8,485.3	8,589.4	8,485.3	26.9	25.5	0.75	-523.6	832.0	100.0	61.2	38.74	2.581	Normal Operations	
8,700.0	8,585.3	8,689.4	8,585.3	27.0	25.5	0.75	-523.6	832.0	100.0	61.2	38.82	2.575	Normal Operations	
8,800.0	8,685.3	8,789.4	8,685.3	27.0	25.6	0.75	-523.6	832.0	100.0	61.1	38.91	2.570	Normal Operations	
8,900.0	8,785.3	8,889.4	8,785.3	27.0	25.6	0.75	-523.6	832.0	100.0	61.0	39.00	2.564	Normal Operations	
9,000.0	8,885.3	8,989.4	8,885.3	27.0	25.6	0.75	-523.6	832.0	100.0	60.9	39.09	2.558	Normal Operations	
9,100.0	8,985.3	9,089.4	8,985.3	27.1	25.7	0.75	-523.6	832.0	100.0	60.8	39.18	2.552	Normal Operations	
9,200.0	9,085.3	9,189.4	9,085.3	27.1	25.7	0.75	-523.6	832.0	100.0	60.7	39.26	2.546	Normal Operations	
9,300.0	9,185.3	9,289.4	9,185.3	27.1	25.7	0.75	-523.6	832.0	100.0	60.6	39.35	2.541	Normal Operations	
9,400.0	9,285.3	9,389.4	9,285.3	27.2	25.8	0.75	-523.6	832.0	100.0	60.5	39.44	2.535	Normal Operations	
9,500.0	9,385.3	9,489.4	9,385.3	27.2	25.8	0.75	-523.6	832.0	100.0	60.5	39.53	2.529	Normal Operations	
9,600.0	9,485.3	9,589.4	9,485.3	27.2	25.8	0.75	-523.6	832.0	100.0	60.4	39.62	2.523	Normal Operations	
9,700.0	9,585.3	9,689.4	9,585.3	27.2	25.9	0.75	-523.6	832.0	100.0	60.3	39.72	2.518	Normal Operations	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips
Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 504H - Slot DONKEY POTROAST #504H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 504H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design: TARHEEL_DONKEY POTROAST PROJECT - _DONKEY POTROAST FED COM 704H - OWB - PWP0													Offset Site Error: 0.0 usft	
Survey Program: 0-r.5 MWD+IFR1				Rule Assigned:									Offset Well Error: 3.0 usft	
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	No-Go Distance (usft)	Separation Factor	Warning	
9,800.0	9,685.3	9,789.4	9,685.3	27.3	25.9	0.75	-523.6	832.0	100.0	60.2	39.81	2.512	Normal Operations	
9,900.0	9,785.3	9,889.4	9,785.3	27.3	25.9	0.75	-523.6	832.0	100.0	60.1	39.90	2.506	Normal Operations	
10,000.0	9,885.3	9,989.4	9,885.3	27.3	26.0	0.75	-523.6	832.0	100.0	60.0	39.99	2.500	Normal Operations	
10,100.0	9,985.3	10,089.4	9,985.3	27.4	26.0	0.75	-523.6	832.0	100.0	59.9	40.09	2.494	Caution - Monitor Closely	
10,116.7	10,002.0	10,106.2	10,002.0	27.4	26.0	0.75	-523.6	832.0	100.0	59.9	40.10	2.494	Caution - Monitor Closely	
10,150.0	10,035.2	10,139.4	10,035.2	27.4	26.0	-178.87	-523.6	832.0	101.0	60.8	40.17	2.513	Normal Operations	
10,200.0	10,085.0	10,189.1	10,085.0	27.5	26.0	-178.91	-523.6	832.0	106.0	65.6	40.40	2.624	Normal Operations	
10,250.0	10,134.1	10,238.2	10,134.1	27.7	26.1	-178.98	-523.6	832.0	115.4	74.7	40.68	2.837	Normal Operations	
10,300.0	10,182.1	10,286.3	10,182.1	27.8	26.1	-179.07	-523.6	832.0	129.0	88.1	40.97	3.150		
10,350.0	10,228.9	10,333.0	10,228.9	28.0	26.1	-179.15	-523.6	832.0	146.8	105.5	41.27	3.557		
10,400.0	10,273.9	10,378.0	10,273.9	28.1	26.1	-179.23	-523.6	832.0	168.6	127.0	41.58	4.055		
10,450.0	10,316.8	10,420.9	10,316.8	28.3	26.1	-179.30	-523.6	832.0	194.2	152.3	41.88	4.637		
10,500.0	10,357.3	10,461.5	10,357.3	28.5	26.1	-179.35	-523.6	832.0	223.4	181.3	42.16	5.299		
10,550.0	10,395.1	10,499.3	10,395.1	28.6	26.1	-179.39	-523.6	832.0	256.1	213.7	42.44	6.035		
10,600.0	10,430.0	10,534.1	10,430.0	28.8	26.2	-179.41	-523.6	832.0	292.0	249.3	42.70	6.839		
10,650.0	10,461.5	10,565.7	10,461.5	28.9	26.2	-179.42	-523.6	832.0	330.7	287.8	42.93	7.703		
10,700.0	10,489.6	10,593.8	10,489.6	29.1	26.2	-179.42	-523.6	832.0	372.1	328.9	43.15	8.624		
10,750.0	10,514.0	10,618.1	10,514.0	29.2	26.2	-179.39	-523.6	832.0	415.7	372.4	43.34	9.593		
10,800.0	10,534.4	10,638.6	10,534.4	29.3	26.2	-179.33	-523.6	832.0	461.3	417.8	43.50	10.605		
10,850.0	10,550.9	10,655.0	10,550.9	29.4	26.2	-179.22	-523.6	832.0	508.5	464.9	43.63	11.655		
10,900.0	10,563.1	10,667.3	10,563.1	29.5	26.2	-178.99	-523.6	832.0	557.0	513.3	43.74	12.735		
10,950.0	10,571.1	10,675.2	10,571.1	29.5	26.2	-178.38	-523.6	832.0	606.3	562.5	43.81	13.840		
11,000.0	10,574.7	10,678.9	10,574.7	29.6	26.2	-174.06	-523.6	832.0	656.2	612.3	43.85	14.964		
11,016.7	10,575.0	10,679.1	10,575.0	29.6	26.2	-90.05	-523.6	832.0	672.9	629.1	43.86	15.343		
11,100.0	10,575.0	10,679.1	10,575.0	29.6	26.2	-90.06	-523.6	832.0	756.2	712.3	43.89	17.230		
11,200.0	10,575.0	10,679.1	10,575.0	29.7	26.2	-90.07	-523.6	832.0	856.2	812.3	43.92	19.495		
11,300.0	10,575.0	10,679.1	10,575.0	29.8	26.2	-90.08	-523.6	832.0	956.2	912.2	43.95	21.756		
11,400.0	10,575.0	12,464.4	11,550.0	29.9	29.4	-179.89	-1,579.8	839.0	975.0	923.3	51.68	18.866		
11,500.0	10,575.0	12,564.4	11,550.0	30.1	29.6	-179.89	-1,679.8	839.7	975.0	922.6	52.43	18.598		
11,600.0	10,575.0	12,664.4	11,550.0	30.2	30.0	-179.89	-1,779.8	840.3	975.0	921.8	53.21	18.324		
11,700.0	10,575.0	12,764.4	11,550.0	30.4	30.3	-179.89	-1,879.8	841.0	975.0	921.0	54.02	18.048		
11,800.0	10,575.0	12,864.4	11,550.0	30.6	30.7	-179.89	-1,979.8	841.7	975.0	920.1	54.87	17.769		
11,900.0	10,575.0	12,964.4	11,550.0	30.8	31.2	-179.89	-2,079.8	842.3	975.0	919.3	55.75	17.490		
12,000.0	10,575.0	13,064.4	11,550.0	31.0	31.7	-179.90	-2,179.8	843.0	975.0	918.3	56.65	17.210		
12,100.0	10,575.0	13,164.4	11,550.0	31.2	32.2	-179.90	-2,279.8	843.7	975.0	917.4	57.59	16.931		
12,200.0	10,575.0	13,264.4	11,550.0	31.5	32.7	-179.90	-2,379.8	844.3	975.0	916.5	58.55	16.653		
12,300.0	10,575.0	13,364.4	11,550.0	31.8	33.3	-179.90	-2,479.8	845.0	975.0	915.5	59.53	16.378		
12,400.0	10,575.0	13,464.4	11,550.0	32.1	33.9	-179.90	-2,579.8	845.7	975.0	914.5	60.54	16.105		
12,500.0	10,575.0	13,564.4	11,550.0	32.5	34.5	-179.90	-2,679.8	846.3	975.0	913.4	61.57	15.835		
12,600.0	10,575.0	13,664.4	11,550.0	32.8	35.2	-179.90	-2,779.8	847.0	975.0	912.4	62.63	15.569		
12,700.0	10,575.0	13,764.4	11,550.0	33.2	35.9	-179.90	-2,879.7	847.7	975.0	911.3	63.70	15.306		
12,800.0	10,575.0	13,864.4	11,550.0	33.6	36.5	-179.90	-2,979.7	848.3	975.0	910.2	64.79	15.048		
12,900.0	10,575.0	13,964.4	11,550.0	34.1	37.3	-179.90	-3,079.7	849.0	975.0	909.1	65.90	14.794		
13,000.0	10,575.0	14,064.4	11,550.0	34.5	38.0	-179.90	-3,179.7	849.6	975.0	908.0	67.03	14.545		
13,100.0	10,575.0	14,164.4	11,550.0	35.0	38.7	-179.90	-3,279.7	850.3	975.0	906.8	68.18	14.301		
13,200.0	10,575.0	14,264.4	11,550.0	35.4	39.5	-179.90	-3,379.7	851.0	975.0	905.7	69.34	14.061		
13,300.0	10,575.0	14,364.4	11,550.0	35.9	40.3	-179.90	-3,479.7	851.6	975.0	904.5	70.52	13.827		
13,400.0	10,575.0	14,464.4	11,550.0	36.4	41.0	-179.91	-3,579.7	852.3	975.0	903.3	71.71	13.597		
13,500.0	10,575.0	14,564.4	11,550.0	37.0	41.8	-179.91	-3,679.7	853.0	975.0	902.1	72.91	13.373		
13,600.0	10,575.0	14,664.4	11,550.0	37.5	42.6	-179.91	-3,779.7	853.6	975.0	900.9	74.13	13.153		
13,700.0	10,575.0	14,764.4	11,550.0	38.1	43.4	-179.91	-3,879.7	854.3	975.0	899.6	75.36	12.938		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips
Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 504H - Slot DONKEY POTROAST #504H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 504H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design: TARHEEL_DONKEY POTROAST PROJECT - _DONKEY POTROAST FED COM 704H - OWB - PWP0												Offset Site Error:	0.0 usft
Survey Program: 0-r.5 MWD+IFR1												Offset Well Error:	3.0 usft
Reference		Offset		Semi Major Axis		Highside Toolface (")	Offset Wellbore Centre		Distance		No-Go Distance (usft)	Separation Factor	Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)		+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)			
13,800.0	10,575.0	14,864.4	11,550.0	38.6	44.2	-179.91	-3,979.7	855.0	975.0	898.4	76.60	12.729	
13,900.0	10,575.0	14,964.4	11,550.0	39.2	45.1	-179.91	-4,079.7	855.6	975.0	897.2	77.85	12.524	
14,000.0	10,575.0	15,064.4	11,550.0	39.8	45.9	-179.91	-4,179.7	856.3	975.0	895.9	79.11	12.324	
14,100.0	10,575.0	15,164.4	11,550.0	40.4	46.7	-179.91	-4,279.7	857.0	975.0	894.6	80.39	12.129	
14,200.0	10,575.0	15,264.4	11,550.0	41.0	47.6	-179.91	-4,379.7	857.6	975.0	893.3	81.67	11.939	
14,300.0	10,575.0	15,364.4	11,550.0	41.6	48.4	-179.91	-4,479.7	858.3	975.0	892.0	82.96	11.753	
14,400.0	10,575.0	15,464.4	11,550.0	42.2	49.3	-179.91	-4,579.7	858.9	975.0	890.7	84.26	11.572	
14,500.0	10,575.0	15,564.4	11,550.0	42.8	50.1	-179.91	-4,679.7	859.6	975.0	889.4	85.57	11.395	
14,600.0	10,575.0	15,664.4	11,550.0	43.4	51.0	-179.91	-4,779.7	860.3	975.0	888.1	86.88	11.222	
14,700.0	10,575.0	15,764.4	11,550.0	44.1	51.9	-179.92	-4,879.7	860.9	975.0	886.8	88.21	11.053	
14,800.0	10,575.0	15,864.4	11,550.0	44.7	52.7	-179.92	-4,979.7	861.6	975.0	885.5	89.54	10.889	
14,900.0	10,575.0	15,964.4	11,550.0	45.4	53.6	-179.92	-5,079.7	862.3	975.0	884.1	90.88	10.729	
15,000.0	10,575.0	16,064.4	11,550.0	46.0	54.5	-179.92	-5,179.7	862.9	975.0	882.8	92.22	10.572	
15,100.0	10,575.0	16,164.4	11,550.0	46.7	55.4	-179.92	-5,279.7	863.6	975.0	881.4	93.57	10.420	
15,200.0	10,575.0	16,264.4	11,550.0	47.3	56.3	-179.92	-5,379.7	864.3	975.0	880.1	94.93	10.271	
15,300.0	10,575.0	16,364.4	11,550.0	48.0	57.2	-179.92	-5,479.7	864.9	975.0	878.7	96.29	10.125	
15,400.0	10,575.0	16,464.4	11,550.0	48.6	58.0	-179.92	-5,579.7	865.6	975.0	877.3	97.66	9.983	
15,500.0	10,575.0	16,564.4	11,550.0	49.3	58.9	-179.92	-5,679.7	866.3	975.0	876.0	99.04	9.845	
15,600.0	10,575.0	16,664.4	11,550.0	50.0	59.8	-179.92	-5,779.7	866.9	975.0	874.6	100.41	9.710	
15,700.0	10,575.0	16,764.4	11,550.0	50.7	60.7	-179.92	-5,879.7	867.6	975.0	873.2	101.80	9.578	
15,800.0	10,575.0	16,864.4	11,550.0	51.3	61.6	-179.92	-5,979.7	868.2	975.0	871.8	103.19	9.449	
15,900.0	10,575.0	16,964.4	11,550.0	52.0	62.5	-179.92	-6,079.7	868.9	975.0	870.4	104.58	9.323	
16,000.0	10,575.0	17,064.4	11,550.0	52.7	63.4	-179.92	-6,179.7	869.6	975.0	869.0	105.98	9.200	
16,100.0	10,575.0	17,164.4	11,550.0	53.4	64.4	-179.93	-6,279.7	870.2	975.0	867.6	107.38	9.080	
16,200.0	10,575.0	17,264.4	11,550.0	54.1	65.3	-179.93	-6,379.7	870.9	975.0	866.2	108.79	8.963	
16,300.0	10,575.0	17,364.4	11,550.0	54.8	66.2	-179.93	-6,479.7	871.6	975.0	864.8	110.19	8.848	
16,400.0	10,575.0	17,464.4	11,550.0	55.5	67.1	-179.93	-6,579.7	872.2	975.0	863.4	111.61	8.736	
16,500.0	10,575.0	17,564.4	11,550.0	56.2	68.0	-179.93	-6,679.7	872.9	975.0	862.0	113.02	8.626	
16,600.0	10,575.0	17,664.4	11,550.0	56.9	68.9	-179.93	-6,779.7	873.6	975.0	860.6	114.44	8.519	
16,700.0	10,575.0	17,764.4	11,550.0	57.6	69.8	-179.93	-6,879.7	874.2	975.0	859.1	115.87	8.415	
16,800.0	10,575.0	17,864.4	11,550.0	58.3	70.8	-179.93	-6,979.7	874.9	975.0	857.7	117.30	8.312	
16,900.0	10,575.0	17,964.4	11,550.0	59.0	71.7	-179.93	-7,079.7	875.6	975.0	856.3	118.72	8.212	
17,000.0	10,575.0	18,064.4	11,550.0	59.7	72.6	-179.93	-7,179.7	876.2	975.0	854.8	120.16	8.114	
17,100.0	10,575.0	18,164.4	11,550.0	60.4	73.5	-179.93	-7,279.7	876.9	975.0	853.4	121.59	8.019	
17,200.0	10,575.0	18,264.4	11,550.0	61.1	74.5	-179.93	-7,379.7	877.5	975.0	852.0	123.03	7.925	
17,300.0	10,575.0	18,364.4	11,550.0	61.8	75.4	-179.93	-7,479.6	878.2	975.0	850.5	124.47	7.833	
17,400.0	10,575.0	18,464.4	11,550.0	62.5	76.3	-179.94	-7,579.6	878.9	975.0	849.1	125.92	7.743	
17,500.0	10,575.0	18,564.4	11,550.0	63.3	77.3	-179.94	-7,679.6	879.5	975.0	847.6	127.36	7.655	
17,600.0	10,575.0	18,664.4	11,550.0	64.0	78.2	-179.94	-7,779.6	880.2	975.0	846.2	128.81	7.569	
17,700.0	10,575.0	18,764.4	11,550.0	64.7	79.1	-179.94	-7,879.6	880.9	975.0	844.7	130.26	7.485	
17,800.0	10,575.0	18,864.4	11,550.0	65.4	80.1	-179.94	-7,979.6	881.5	975.0	843.3	131.71	7.402	
17,900.0	10,575.0	18,964.4	11,550.0	66.1	81.0	-179.94	-8,079.6	882.2	975.0	841.8	133.17	7.321	
18,000.0	10,575.0	19,064.4	11,550.0	66.8	81.9	-179.94	-8,179.6	882.9	975.0	840.4	134.63	7.242	
18,100.0	10,575.0	19,164.4	11,550.0	67.6	82.9	-179.94	-8,279.6	883.5	975.0	838.9	136.09	7.165	
18,200.0	10,575.0	19,264.4	11,550.0	68.3	83.8	-179.94	-8,379.6	884.2	975.0	837.5	137.55	7.088	
18,300.0	10,575.0	19,364.4	11,550.0	69.0	84.7	-179.94	-8,479.6	884.9	975.0	836.0	139.01	7.014	
18,400.0	10,575.0	19,464.4	11,550.0	69.7	85.7	-179.94	-8,579.6	885.5	975.0	834.5	140.48	6.941	
18,500.0	10,575.0	19,564.4	11,550.0	70.5	86.6	-179.94	-8,679.6	886.2	975.0	833.1	141.94	6.869	
18,600.0	10,575.0	19,664.4	11,550.0	71.2	87.6	-179.94	-8,779.6	886.8	975.0	831.6	143.41	6.799	
18,700.0	10,575.0	19,764.4	11,550.0	71.9	88.5	-179.95	-8,879.6	887.5	975.0	830.1	144.88	6.730	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips
Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 504H - Slot DONKEY POTROAST #504H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 504H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design:		TARHEEL_DONKEY POTROAST PROJECT - _DONKEY POTROAST FED COM 704H - OWB - PWP0											Offset Site Error:		0.0 usft
Survey Program:		0-r.5 MWD+IFR1							Rule Assigned:				Offset Well Error:		3.0 usft
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	No-Go Distance (usft)	Separation Factor	Warning		
18,800.0	10,575.0	19,864.4	11,550.0	72.6	89.4	-179.95	-8,979.6	888.2	975.0	828.6	146.35	6.662			
18,900.0	10,575.0	19,964.4	11,550.0	73.4	90.4	-179.95	-9,079.6	888.8	975.0	827.2	147.83	6.596			
19,000.0	10,575.0	20,064.4	11,550.0	74.1	91.3	-179.95	-9,179.6	889.5	975.0	825.7	149.30	6.530			
19,100.0	10,575.0	20,164.4	11,550.0	74.8	92.3	-179.95	-9,279.6	890.2	975.0	824.2	150.78	6.466			
19,200.0	10,575.0	20,264.4	11,550.0	75.6	93.2	-179.95	-9,379.6	890.8	975.0	822.7	152.26	6.404			
19,300.0	10,575.0	20,364.4	11,550.0	76.3	94.2	-179.95	-9,479.6	891.5	975.0	821.3	153.74	6.342			
19,400.0	10,575.0	20,464.4	11,550.0	77.0	95.1	-179.95	-9,579.6	892.2	975.0	819.8	155.22	6.282			
19,500.0	10,575.0	20,564.4	11,550.0	77.8	96.0	-179.95	-9,679.6	892.8	975.0	818.3	156.70	6.222			
19,600.0	10,575.0	20,664.4	11,550.0	78.5	97.0	-179.95	-9,779.6	893.5	975.0	816.8	158.18	6.164			
19,700.0	10,575.0	20,764.4	11,550.0	79.2	97.9	-179.95	-9,879.6	894.2	975.0	815.3	159.67	6.107			
19,800.0	10,575.0	20,864.4	11,550.0	80.0	98.9	-179.95	-9,979.6	894.8	975.0	813.8	161.15	6.050			
19,900.0	10,575.0	20,964.4	11,550.0	80.7	99.8	-179.95	-10,079.6	895.5	975.0	812.4	162.64	5.995			
20,000.0	10,575.0	21,064.4	11,550.0	81.5	100.8	-179.95	-10,179.6	896.1	975.0	810.9	164.13	5.941			
20,100.0	10,575.0	21,164.4	11,550.0	82.2	101.7	-179.96	-10,279.6	896.8	975.0	809.4	165.62	5.887			
20,200.0	10,575.0	21,264.4	11,550.0	82.9	102.7	-179.96	-10,379.6	897.5	975.0	807.9	167.11	5.835			
20,300.0	10,575.0	21,364.4	11,550.0	83.7	103.6	-179.96	-10,479.6	898.1	975.0	806.4	168.60	5.783			
20,400.0	10,575.0	21,464.4	11,550.0	84.4	104.6	-179.96	-10,579.6	898.8	975.0	804.9	170.09	5.732			
20,500.0	10,575.0	21,564.4	11,550.0	85.1	105.5	-179.96	-10,679.6	899.5	975.0	803.4	171.58	5.682			
20,600.0	10,575.0	21,664.4	11,550.0	85.9	106.5	-179.96	-10,779.6	900.1	975.0	801.9	173.08	5.633			
20,700.0	10,575.0	21,764.4	11,550.0	86.6	107.4	-179.96	-10,879.6	900.8	975.0	800.4	174.57	5.585			
20,800.0	10,575.0	21,864.4	11,550.0	87.4	108.4	-179.96	-10,979.6	901.5	975.0	798.9	176.07	5.538			
20,900.0	10,575.0	21,964.4	11,550.0	88.1	109.4	-179.96	-11,079.6	902.1	975.0	797.4	177.56	5.491			
21,000.0	10,575.0	22,064.4	11,550.0	88.9	110.3	-179.96	-11,179.6	902.8	975.0	795.9	179.06	5.445			
21,100.0	10,575.0	22,164.4	11,550.0	89.6	111.3	-179.96	-11,279.6	903.5	975.0	794.4	180.56	5.400			
21,200.0	10,575.0	22,264.4	11,550.0	90.3	112.2	-179.96	-11,379.6	904.1	975.0	792.9	182.06	5.355			
21,300.0	10,575.0	22,364.4	11,550.0	91.1	113.2	-179.96	-11,479.6	904.8	975.0	791.4	183.56	5.312			
21,400.0	10,575.0	22,464.4	11,550.0	91.8	114.1	-179.97	-11,579.6	905.5	975.0	789.9	185.06	5.268			
21,500.0	10,575.0	22,564.4	11,550.0	92.6	115.1	-179.97	-11,679.6	906.1	975.0	788.4	186.56	5.226			
21,600.0	10,575.0	22,664.4	11,550.0	93.3	116.0	-179.97	-11,779.6	906.8	975.0	786.9	188.07	5.184			
21,700.0	10,575.0	22,764.4	11,550.0	94.1	117.0	-179.97	-11,879.6	907.4	975.0	785.4	189.57	5.143			
21,800.0	10,575.0	22,864.4	11,550.0	94.8	117.9	-179.97	-11,979.5	908.1	975.0	783.9	191.08	5.103			
21,900.0	10,575.0	22,964.4	11,550.0	95.6	118.9	-179.97	-12,079.5	908.8	975.0	782.4	192.58	5.063			
22,000.0	10,575.0	23,064.4	11,550.0	96.3	119.9	-179.97	-12,179.5	909.4	975.0	780.9	194.09	5.024			
22,100.0	10,575.0	23,164.4	11,550.0	97.1	120.8	-179.97	-12,279.5	910.1	975.0	779.4	195.59	4.985			
22,200.0	10,575.0	23,264.4	11,550.0	97.8	121.8	-179.97	-12,379.5	910.8	975.0	777.9	197.10	4.947			
22,300.0	10,575.0	23,364.4	11,550.0	98.5	122.7	-179.97	-12,479.5	911.4	975.0	776.4	198.61	4.909			
22,400.0	10,575.0	23,464.4	11,550.0	99.3	123.7	-179.97	-12,579.5	912.1	975.0	774.9	200.12	4.872			
22,500.0	10,575.0	23,564.4	11,550.0	100.0	124.7	-179.97	-12,679.5	912.8	975.0	773.4	201.62	4.836			
22,600.0	10,575.0	23,664.4	11,550.0	100.8	125.6	-179.97	-12,779.5	913.4	975.0	771.9	203.13	4.800			
22,700.0	10,575.0	23,764.4	11,550.0	101.5	126.6	-179.97	-12,879.5	914.1	975.0	770.4	204.64	4.764			
22,800.0	10,575.0	23,864.4	11,550.0	102.3	127.5	-179.98	-12,979.5	914.8	975.0	768.8	206.15	4.729			
22,900.0	10,575.0	23,964.4	11,550.0	103.0	128.5	-179.98	-13,079.5	915.4	975.0	767.3	207.67	4.695			
23,000.0	10,575.0	24,064.4	11,550.0	103.8	129.4	-179.98	-13,179.5	916.1	975.0	765.8	209.18	4.661			
23,100.0	10,575.0	24,164.4	11,550.0	104.5	130.4	-179.98	-13,279.5	916.7	975.0	764.3	210.69	4.628			
23,200.0	10,575.0	24,264.4	11,550.0	105.3	131.4	-179.98	-13,379.5	917.4	975.0	762.8	212.20	4.595			
23,300.0	10,575.0	24,364.4	11,550.0	106.0	132.3	-179.98	-13,479.5	918.1	975.0	761.3	213.72	4.562			
23,400.0	10,575.0	24,464.4	11,550.0	106.8	133.3	-179.98	-13,579.5	918.7	975.0	759.8	215.23	4.530			
23,500.0	10,575.0	24,564.4	11,550.0	107.5	134.3	-179.98	-13,679.5	919.4	975.0	758.3	216.74	4.498			
23,600.0	10,575.0	24,664.4	11,550.0	108.3	135.2	-179.98	-13,779.5	920.1	975.0	756.7	218.26	4.467			
23,700.0	10,575.0	24,764.4	11,550.0	109.0	136.2	-179.98	-13,879.5	920.7	975.0	755.2	219.77	4.436			
23,800.0	10,575.0	24,864.4	11,550.0	109.8	137.1	-179.98	-13,979.5	921.4	975.0	753.7	221.29	4.406			

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips
Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 504H - Slot DONKEY POTROAST #504H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 504H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design: TARHEEL_DONKEY POTROAST PROJECT - _DONKEY POTROAST FED COM 704H - OWB - PWP0												Offset Site Error:	0.0 usft
Survey Program: 0-r.5 MWD+IFR1												Offset Well Error:	3.0 usft
Reference		Offset		Semi Major Axis		Highside Toolface (°)	Offset Wellbore Centre		Distance		No-Go Distance (usft)	Separation Factor	Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)		+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)			
23,900.0	10,575.0	24,964.4	11,550.0	110.5	138.1	-179.98	-14,079.5	922.1	975.0	752.2	222.81	4.376	
24,000.0	10,575.0	25,064.4	11,550.0	111.3	139.1	-179.98	-14,179.5	922.7	975.0	750.7	224.32	4.346	
24,100.0	10,575.0	25,164.4	11,550.0	112.1	140.0	-179.99	-14,279.5	923.4	975.0	749.2	225.84	4.317	
24,200.0	10,575.0	25,264.4	11,550.0	112.8	141.0	-179.99	-14,379.5	924.1	975.0	747.6	227.36	4.288	
24,300.0	10,575.0	25,364.4	11,550.0	113.6	141.9	-179.99	-14,479.5	924.7	975.0	746.1	228.88	4.260	
24,400.0	10,575.0	25,464.4	11,550.0	114.3	142.9	-179.99	-14,579.5	925.4	975.0	744.6	230.39	4.232	
24,500.0	10,575.0	25,564.4	11,550.0	115.1	143.9	-179.99	-14,679.5	926.0	975.0	743.1	231.91	4.204	
24,600.0	10,575.0	25,664.4	11,550.0	115.8	144.8	-179.99	-14,779.5	926.7	975.0	741.6	233.43	4.177	
24,700.0	10,575.0	25,764.4	11,550.0	116.6	145.8	-179.99	-14,879.5	927.4	975.0	740.0	234.95	4.150	
24,800.0	10,575.0	25,864.4	11,550.0	117.3	146.8	-179.99	-14,979.5	928.0	975.0	738.5	236.47	4.123	
24,900.0	10,575.0	25,964.4	11,550.0	118.1	147.7	-179.99	-15,079.5	928.7	975.0	737.0	237.99	4.097	
25,000.0	10,575.0	26,064.4	11,550.0	118.8	148.7	-179.99	-15,179.5	929.4	975.0	735.5	239.51	4.071	
25,100.0	10,575.0	26,164.4	11,550.0	119.6	149.7	-179.99	-15,279.5	930.0	975.0	734.0	241.03	4.045	
25,200.0	10,575.0	26,264.4	11,550.0	120.3	150.6	-179.99	-15,379.5	930.7	975.0	732.4	242.55	4.020	
25,300.0	10,575.0	26,364.4	11,550.0	121.1	151.6	-179.99	-15,479.5	931.4	975.0	730.9	244.08	3.995	
25,400.0	10,575.0	26,464.4	11,550.0	121.9	152.5	-179.99	-15,579.5	932.0	975.0	729.4	245.60	3.970	
25,500.0	10,575.0	26,564.4	11,550.0	122.6	153.5	-180.00	-15,679.5	932.7	975.0	727.9	247.12	3.945	
25,600.0	10,575.0	26,664.4	11,550.0	123.4	154.5	-180.00	-15,779.5	933.4	975.0	726.4	248.64	3.921	
25,700.0	10,575.0	26,764.4	11,550.0	124.1	155.4	-180.00	-15,879.5	934.0	975.0	724.8	250.17	3.897	
25,800.0	10,575.0	26,864.4	11,550.0	124.9	156.4	-180.00	-15,979.5	934.7	975.0	723.3	251.69	3.874	
25,900.0	10,575.0	26,964.4	11,550.0	125.6	157.4	-180.00	-16,079.5	935.3	975.0	721.8	253.21	3.851	
26,000.0	10,575.0	27,064.4	11,550.0	126.4	158.3	-180.00	-16,179.5	936.0	975.0	720.3	254.74	3.827	
26,090.3	10,575.0	27,154.7	11,550.0	127.1	159.0	-180.00	-16,269.7	936.6	975.0	719.1	255.90	3.810	


CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips
Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 504H - Slot DONKEY POTROAST #504H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 504H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Reference Depths are relative to WELL @ 3630.0usft (Original Well Ele
Offset Depths are relative to Offset Datum
Central Meridian is 104° 20' 0.000 W

Coordinates are relative to: _DONKEY POTROAST FED COM 504H - Slot DONK
Coordinate System is US State Plane 1927 (Exact solution), New Mexico East 30
Grid Convergence at Surface is: 0.37°

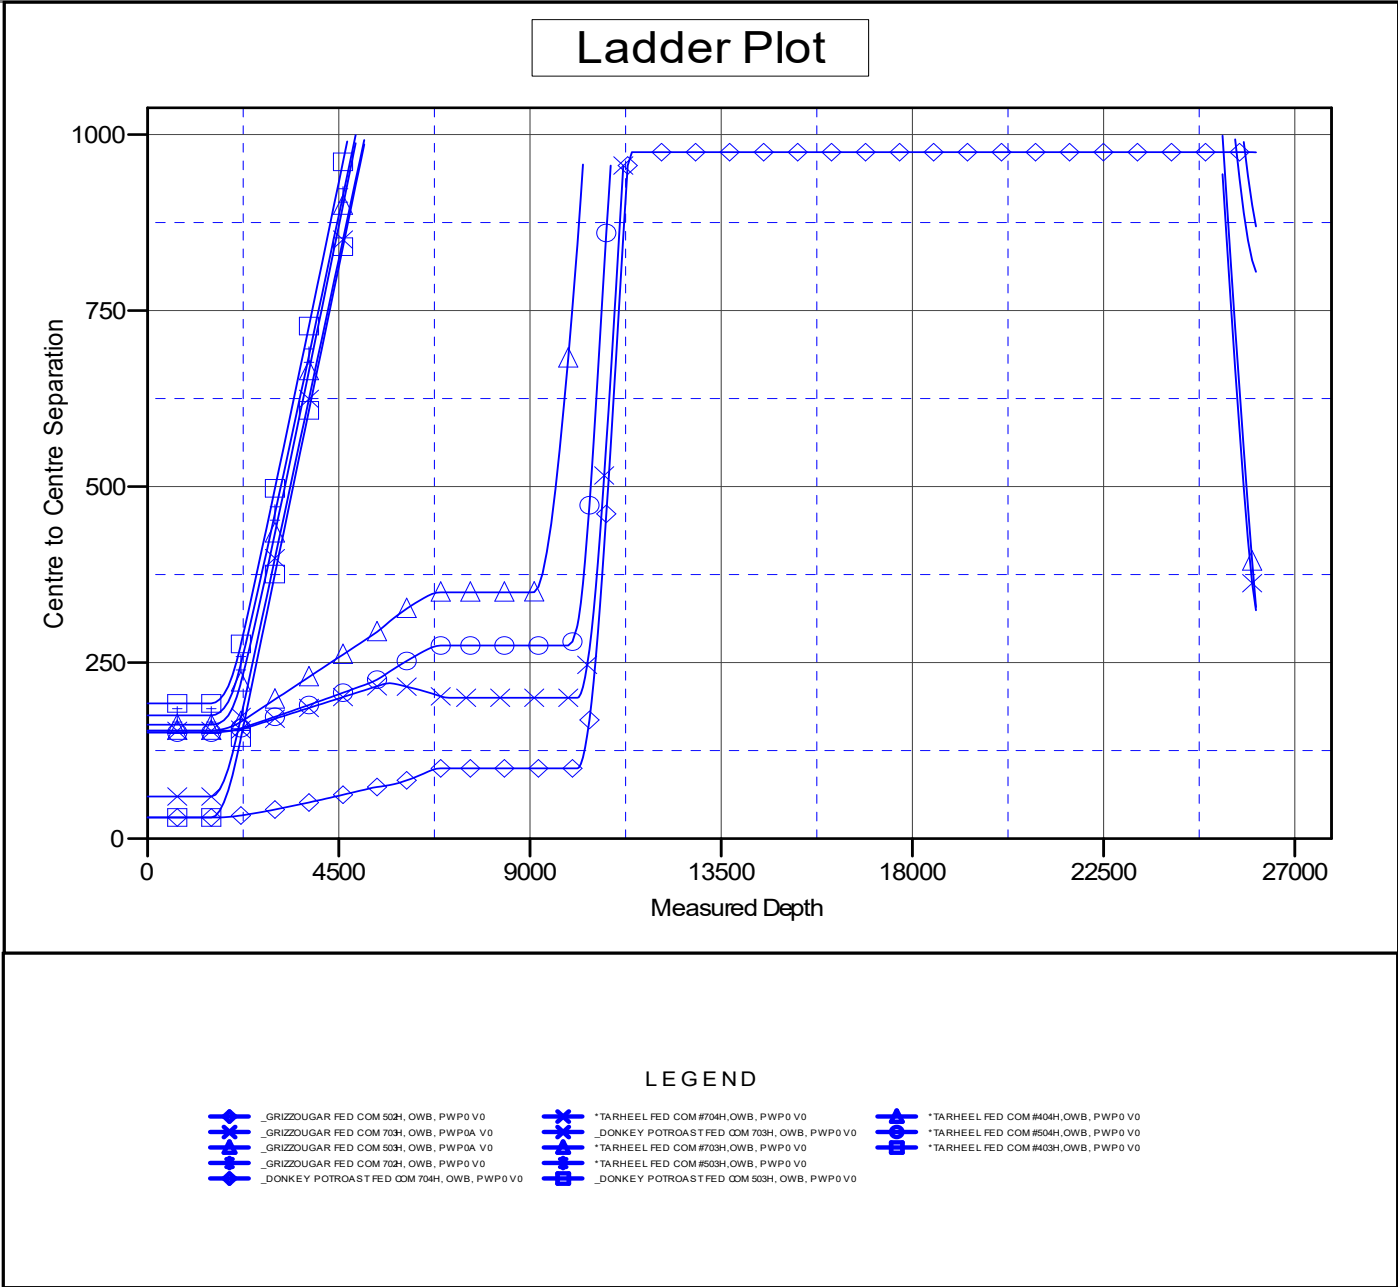


CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips
Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 504H - Slot DONKEY POTROAST #504H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 504H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Reference Depths are relative to WELL @ 3630.0usft (Original Well Ele
Offset Depths are relative to Offset Datum
Central Meridian is 104° 20' 0.000 W

Coordinates are relative to: _DONKEY POTROAST FED COM 504H - Slot DONK
Coordinate System is US State Plane 1927 (Exact solution), New Mexico East 30
Grid Convergence at Surface is: 0.37°

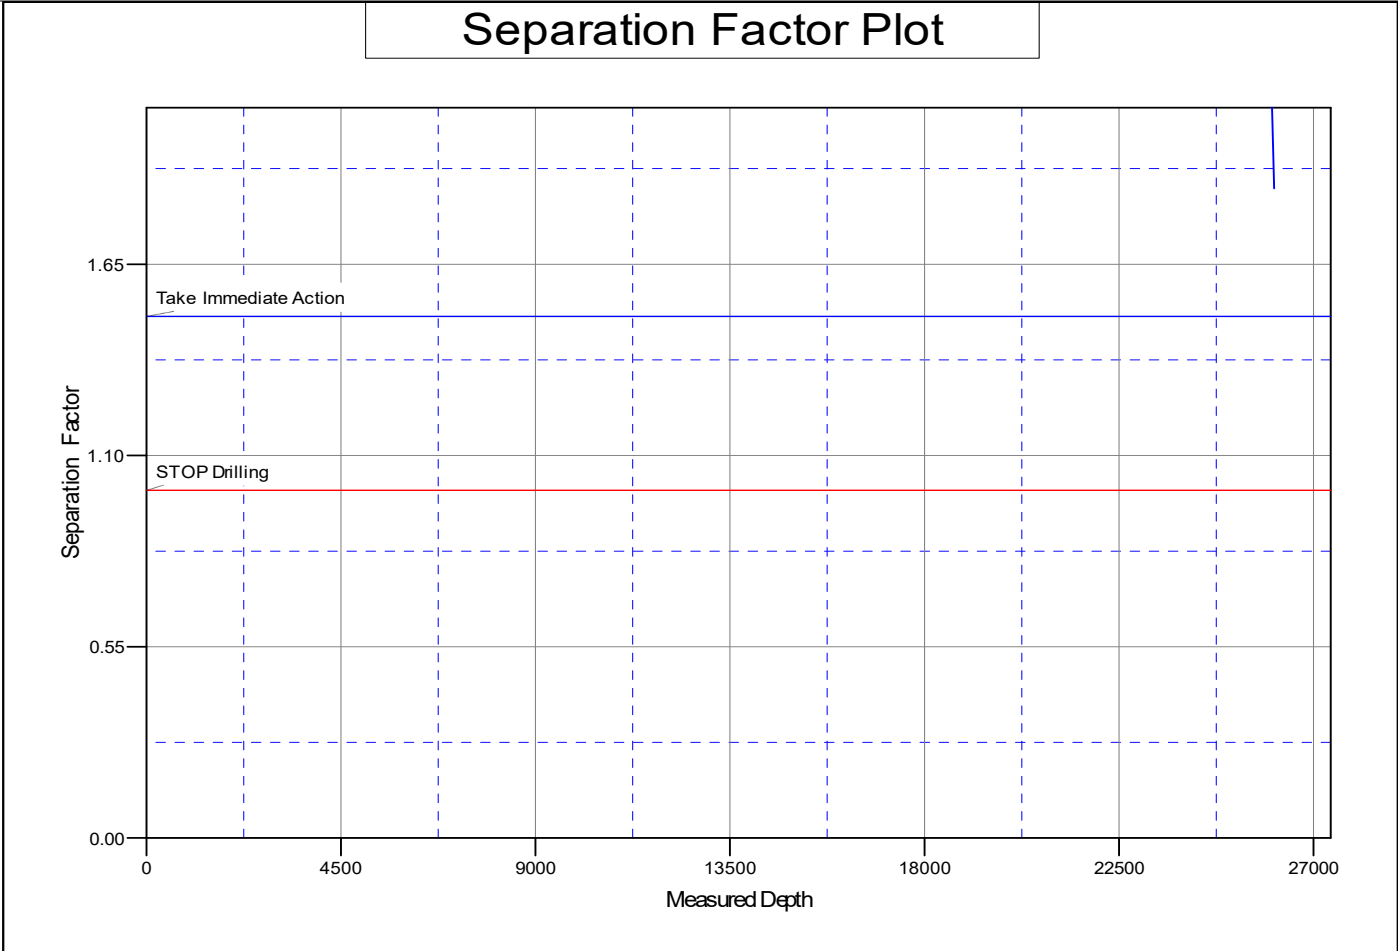

LEGEND

_GRIZZUGAR FED COM 502H, OWB, PWP0 V0	*TARHEEL FED COM #703H, OWB, PWP0 V0	*TARHEEL FED COM #604H, OWB, PWP0 V0
_GRIZZUGAR FED COM 703H, OWB, PWP0A V0	_DONKEY POTROAST FED COM 703H, OWB, PWP0 V0	*TARHEEL FED COM #504H, OWB, PWP0 V0
_GRIZZUGAR FED COM 503H, OWB, PWP0A V0	*TARHEEL FED COM #703H, OWB, PWP0 V0	*TARHEEL FED COM #403H, OWB, PWP0 V0
_GRIZZUGAR FED COM 704H, OWB, PWP0 V0	*TARHEEL FED COM #503H, OWB, PWP0 V0	
_DONKEY POTROAST FED COM 704H, OWB, PWP0 V0	_DONKEY POTROAST FED COM 503H, OWB, PWP0 V0	


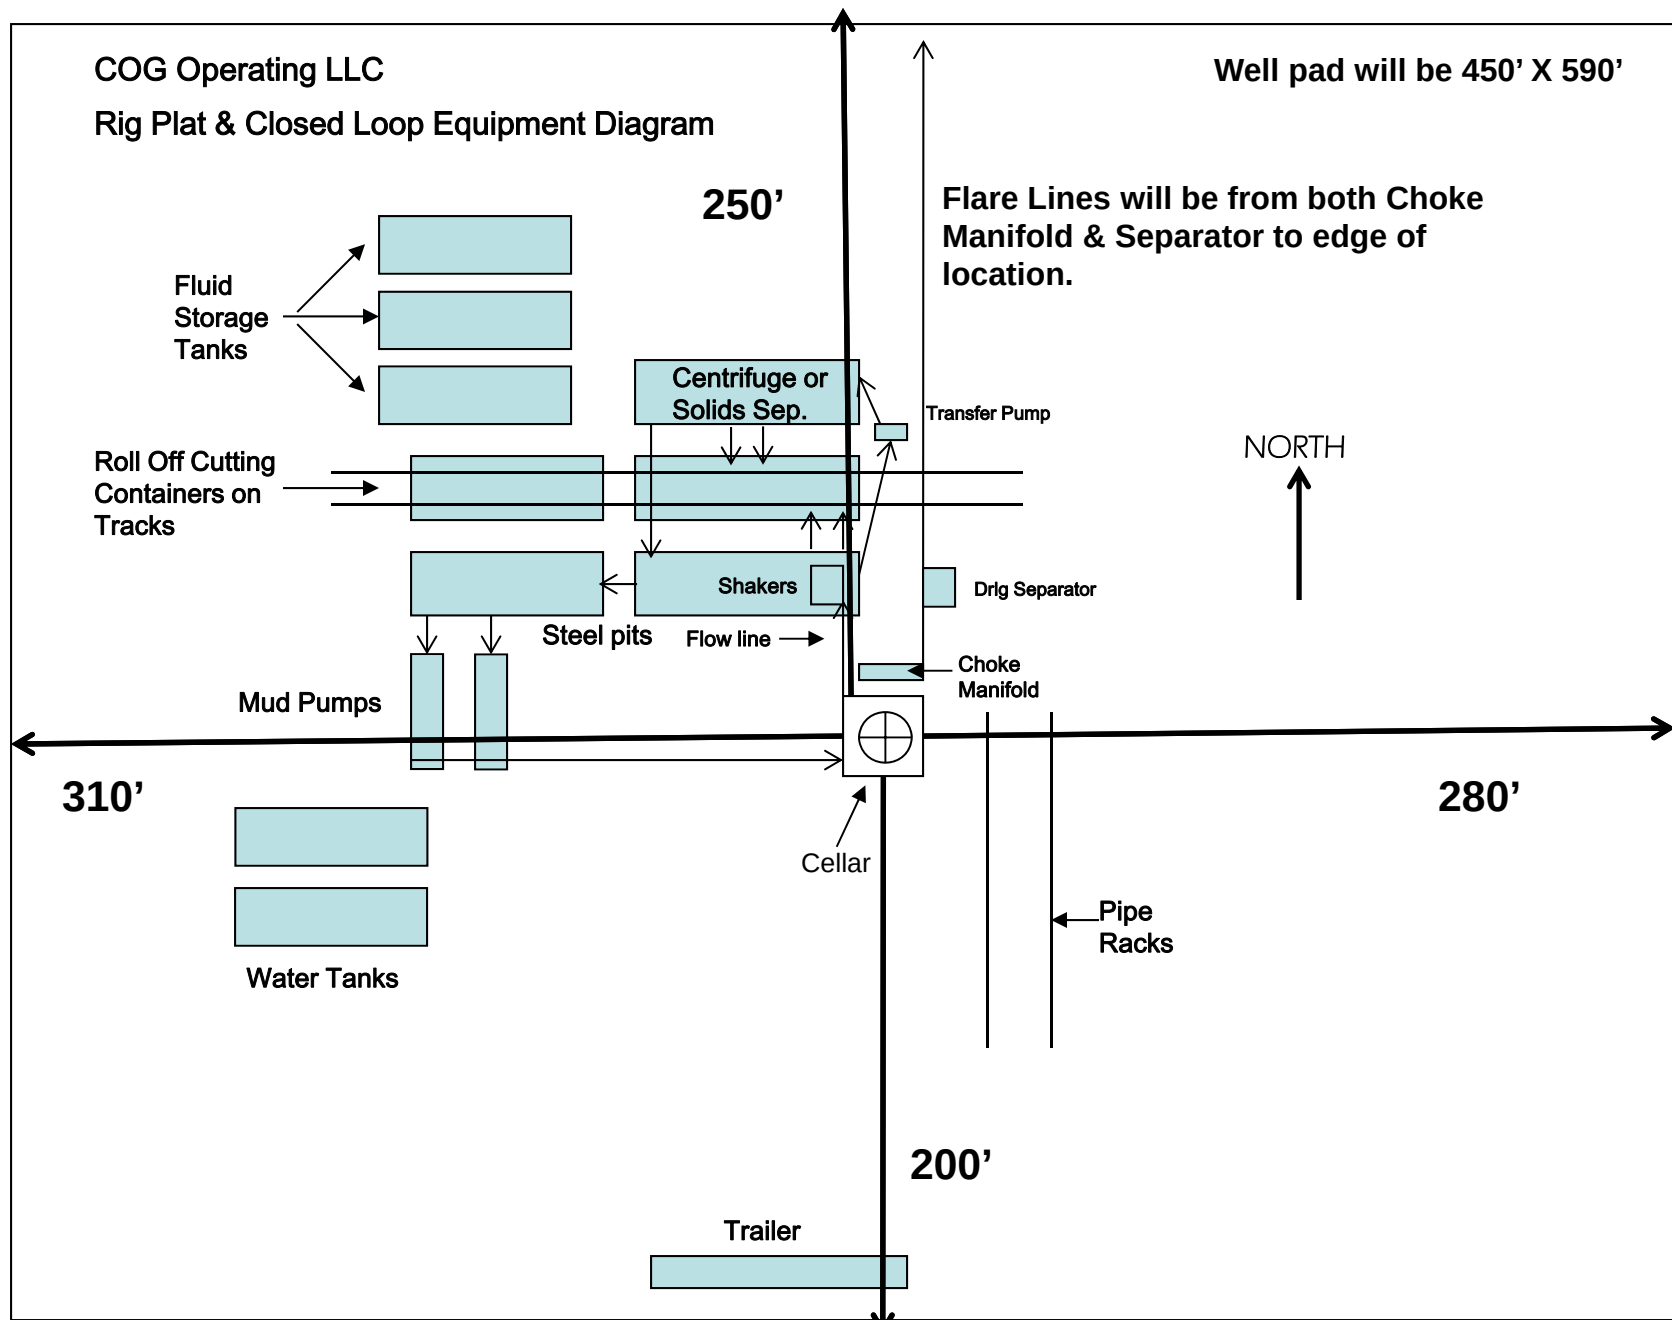


Exhibit 1

"I further certify that COG will comply with Rule 19.15.17 NMAC by using a Closed Loop System."

4-String Design – Open 1st Int x 2nd Int Annulus (ICP 2 below relief zone)

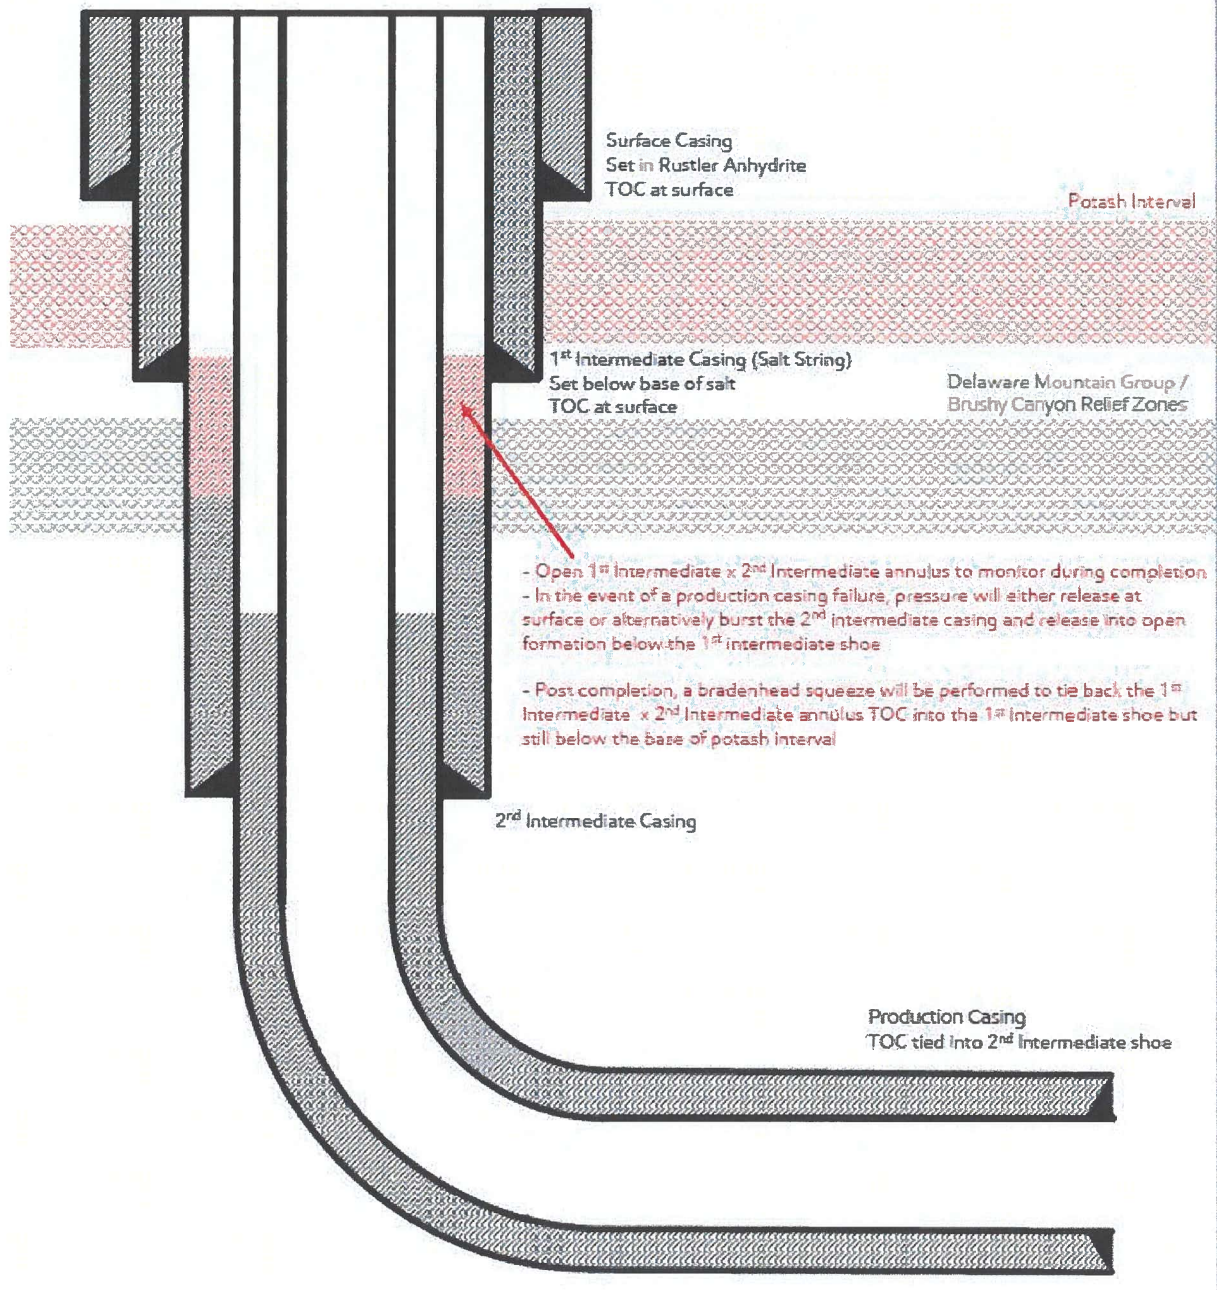

[Figure D] 4 String – Uncemented annulus between 1st and 2nd Intermediate casing strings

- ConocoPhillips is aware of R111Q order update and proposed well complies with the requirements in the order
- Uses above figure from R111Q as design
- All casing ran will be new that meets API standards
- Fluids will be diverted away from the salt interval via the open 1st intermediate x 2nd intermediate annulus in case of production casing failure and the annulus will be monitored during frac
- As in above schematic, Intermediate 2 cement and production cement will not be brought to surface (0% excess on intermediate 2 with TOC 1000' below previous shoe, 10% excess on production with enough to tie back 1000' into previous casing)
- Completions will Bradenhead 1st intermediate x 2nd intermediate annulus within 180 days of frac tying back at minimum 500' into previous casing but not above Marker Bed 126
- No anticollision risks < 1.5 SF will be present in salt interval

State of New Mexico
Energy, Minerals and Natural Resources Department
Oil Conservation Division
1220 South St. Francis Dr.
Santa Fe, NM 87505

Submit Electronically
Via E-permitting

NATURAL GAS MANAGEMENT PLAN

This Natural Gas Management Plan must be submitted with each Application for Permit to Drill (APD) for a new or recompleted well.

Section 1 – Plan Description **Effective May 25, 2021**

I. Operator: COG Operating LLC

OGRID: 229137

Date: 08/26/2024

II. Type: ☒ Original ☐ Amendment due to ☐ 19.15.27.9.D(6)(a) NMAC ☐ 19.15.27.9.D(6)(b) NMAC ☐ Other.

If Other, please describe: _____

III. Well(s): Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	API	ULSTR	Footages	Anticipated Oil BBL/D	Anticipated Gas MCF/D	Anticipated Produced Water BBL/D
Donkey Potroast Federal Com 503H	30-025-	P-15-20S-33E	480 FSL & 1185 FEL	± 1687	± 1510	± 4527
Donkey Potroast Federal Com 504H	30-025-	P-15-20S-33E	480 FSL & 1155 FEL	± 1687	± 1510	± 4527
Donkey Potroast Federal Com 703H	30-025-	P-15-20S-33E	480 FSL & 1215 FEL	± 1680	± 2071	± 4785
Donkey Potroast Federal Com 704H	30-025-	P-15-20S-33E	480 FSL & 1125 FEL	± 1680	± 2071	± 4785

IV. Central Delivery Point Name: 22 C CTB NENE 22-20S-33E [See 19.15.27.9(D)(1) NMAC]

V. Anticipated Schedule: Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	API	Spud Date	TD Reached Date	Completion Commencement Date	Initial Flow Back Date	First Production Date
Donkey Potroast Federal Com	Pending	± 06/01/2025	± 25 days from spud	TBD	TBD	TBD
503H, 504H, 703H, 704H,						

VI. Separation Equipment: ☒ Attach a complete description of how Operator will size separation equipment to optimize gas capture.

VII. Operational Practices: ☒ Attach a complete description of the actions Operator will take to comply with the requirements of Subsection A through F of 19.15.27.8 NMAC.

VIII. Best Management Practices: ☒ Attach a complete description of Operator's best management practices to minimize venting during active and planned maintenance.

Section 2 – Enhanced Plan

EFFECTIVE APRIL 1, 2022

Beginning April 1, 2022, an operator that is not in compliance with its statewide natural gas capture requirement for the applicable reporting area must complete this section.

☒ Operator certifies that it is not required to complete this section because Operator is in compliance with its statewide natural gas capture requirement for the applicable reporting area.

IX. Anticipated Natural Gas Production:

Well	API	Anticipated Average Natural Gas Rate MCF/D	Anticipated Volume of Natural Gas for the First Year MCF

X. Natural Gas Gathering System (NGGS):

Operator	System	ULSTR of Tie-in	Anticipated Gathering Start Date	Available Maximum Daily Capacity of System Segment Tie-in

XI. Map. ☐ Attach an accurate and legible map depicting the location of the well(s), the anticipated pipeline route(s) connecting the production operations to the existing or planned interconnect of the natural gas gathering system(s), and the maximum daily capacity of the segment or portion of the natural gas gathering system(s) to which the well(s) will be connected.

XII. Line Capacity. The natural gas gathering system ☐ will ☐ will not have capacity to gather 100% of the anticipated natural gas production volume from the well prior to the date of first production.

XIII. Line Pressure. Operator ☐ does ☐ does not anticipate that its existing well(s) connected to the same segment, or portion, of the natural gas gathering system(s) described above will continue to meet anticipated increases in line pressure caused by the new well(s).

☐ Attach Operator's plan to manage production in response to the increased line pressure.

XIV. Confidentiality: ☐ Operator asserts confidentiality pursuant to Section 71-2-8 NMSA 1978 for the information provided in Section 2 as provided in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and attaches a full description of the specific information for which confidentiality is asserted and the basis for such assertion.

Section 3 - Certifications

Effective May 25, 2021

Operator certifies that, after reasonable inquiry and based on the available information at the time of submittal:

☒ Operator will be able to connect the well(s) to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system; or

☐ Operator will not be able to connect to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system.

If Operator checks this box, Operator will select one of the following:

Well Shut-In. ☐ Operator will shut-in and not produce the well until it submits the certification required by Paragraph (4) of Subsection D of 19.15.27.9 NMAC; or

Venting and Flaring Plan. ☐ Operator has attached a venting and flaring plan that evaluates and selects one or more of the potential alternative beneficial uses for the natural gas until a natural gas gathering system is available, including:

- (a) power generation on lease;
- (b) power generation for grid;
- (c) compression on lease;
- (d) liquids removal on lease;
- (e) reinjection for underground storage;
- (f) reinjection for temporary storage;
- (g) reinjection for enhanced oil recovery;
- (h) fuel cell production; and
- (i) other alternative beneficial uses approved by the division.

Section 4 - Notices


1. If, at any time after Operator submits this Natural Gas Management Plan and before the well is spud:

(a) Operator becomes aware that the natural gas gathering system it planned to connect the well(s) to has become unavailable or will not have capacity to transport one hundred percent of the production from the well(s), no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised venting and flaring plan containing the information specified in Paragraph (5) of Subsection D of 19.15.27.9 NMAC; or

(b) Operator becomes aware that it has, cumulatively for the year, become out of compliance with its baseline natural gas capture rate or natural gas capture requirement, no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised Natural Gas Management Plan for each well it plans to spud during the next 90 days containing the information specified in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and shall file an update for each Natural Gas Management Plan until Operator is back in compliance with its baseline natural gas capture rate or natural gas capture requirement.

2. OCD may deny or conditionally approve an APD if Operator does not make a certification, fails to submit an adequate venting and flaring plan which includes alternative beneficial uses for the anticipated volume of natural gas produced, or if OCD determines that Operator will not have adequate natural gas takeaway capacity at the time a well will be spud.

I certify that, after reasonable inquiry, the statements in and attached to this Natural Gas Management Plan are true and correct to the best of my knowledge and acknowledge that a false statement may be subject to civil and criminal penalties under the Oil and Gas Act.

Signature: 
Printed Name: Stan Wagner
Title: Regulatory Advisor
E-mail Address: stan.s.wagner@conocophillips.com
Date: 08/29/2024
Phone: 432-253-9685
OIL CONSERVATION DIVISION (Only applicable when submitted as a standalone form)
Approved By:
Title:
Approval Date:
Conditions of Approval:

VI. Separation Equipment

How Operator will size separation equipment to optimize gas capture:

All ConocoPhillips production facility equipment will be sized per industry standards (API 12J) with adequate retention time to effectively separate all phases of production. Each project will take into consideration the number of wells and type curves for each formation pool to ensure adequate facility capacity. Design considerations will also include review of all piping, tanks, VRU's and associated equipment to ensure optimized gas capture minimized risk of release.

VII. Operational Practices

Actions Operator will take to comply with the requirements below:

B. Drilling Operations

- During drilling, flare stacks will be located a minimum of 100 feet from the nearest surface hole location. All gas is captured or combusted. If an emergency or malfunction occurs, gas will be flared or vented for public health, safety, and the environment and be properly reported to the NMOCD pursuant to 19.15.27.8.G.
- Measure or estimate the volume of natural gas that is vented, flared or beneficially used during drilling, completion and production operations, regardless of the reason or authorization for such venting or flaring.

C. Completion Operations

- During completion operations, operator does not produce oil or gas but maintains adequate well control through completion operations.
- Individual well test separators will be set to properly separate gas and liquids. A temporary test separator will be utilized initially to process volumes. In addition, separators will be tied into flowback tanks which will be tied into the gas processing equipment for sales down a pipeline.

D. Venting and flaring during production operations

- During each phase of well life (drilling, completion and production) of a ConocoPhillips well, COP personnel will follow all necessary procedures to ensure both the operation and the equipment are within the NMAC 19.15.27.8 Subsection D guidelines.
- During well operations that require unloading of the well to atmospheric pressure, all reasonable actions will be taken to minimize vented gas
- Through the life of the well all flaring shall be measured, and venting events quantified using the data available and industry best practice.

E. Performance standards for separation, storage tank and flare equipment

- All storage tanks and separation equipment are designed minimize risk of liquid or vapor release and optimize gas capture. This includes automation for automatic gauging and pressure monitoring.

- All flare stacks are equipped with auto ignition devices and/or continuous pilots and are designed to operate at maximum combustion efficiency pursuant NMAC 19.15.27.8 Subsection E. Flares will follow COP spacing guidelines to ensure they are a safe distance from combustibles and operations equipment.
- COP personnel will conduct routine AVO inspections on a regular basis per NMAC 19.15.27.8 Subsection E guidelines.

F. Measurement of vented and flared natural gas.

- Measurement equipment will be installed to quantify gas flared during drilling, completion and production of the well.
- All measurement devices installed will meet accuracy ratings per AGA and API standards.
- Measurement devices will be installed without manifolds that allow diversion of gas around the metering element, except for the sole purpose of inspection of servicing the measurement device.

VIII. Best Management Practices



- Operator will curtail or shut in production, within reasonable limits, during upset conditions to minimize venting and flaring.
- When feasible, Operator will use equipment to capture gas that would otherwise be vented or flared.
- During completions and production operations Operator will minimize blowdowns to atmosphere
- When feasible, Operator will use electric or air actuated equipment to reduce bleed emissions

Waste Minimization Plan



Per § 3162.3-1 Drilling applications and plans. Part J:

- (1) The anticipated initial oil production rate from the oil well and the anticipated production decline over the first 3 years of production.
 - a. See attached Anticipated Production & Decline Curve
- (2) The anticipated initial oil-well gas production rate from the oil well and the anticipated production decline over the first 3 years of production.
 - a. See attached Anticipated Production & Decline Curve
- (3) Certification that the operator has a valid, executed gas sales contract to sell to a purchaser 100 percent of the produced oil-well gas, less gas anticipated for use on-lease pursuant to 43 CFR subpart 3178.
 - a. See attached NMOCD – Natural Gas Management Plan
- (4) Any other information demonstrating the operator's plans to avoid the waste of gas production from any source, including, as appropriate, from pneumatic equipment, storage tanks, and leaks.
 - a. This location will comply with NSPS OOOOb which will include reduced associated gas flaring, non-emitting pneumatic equipment, storage tanks that are controlled and a rigorous leak detection and repair program. In addition, this facility complies with 20.2.50 NMAC (Ozone Precursor Pollutants) which also imposes standards on pneumatic equipment, tank controls, and leak detection and repair. Finally, this facility must comply with 19.15.27 NMAC (Venting and Flaring of Natural Gas) which significantly reduces instances of flaring.

Anticipated Production Decline Curve

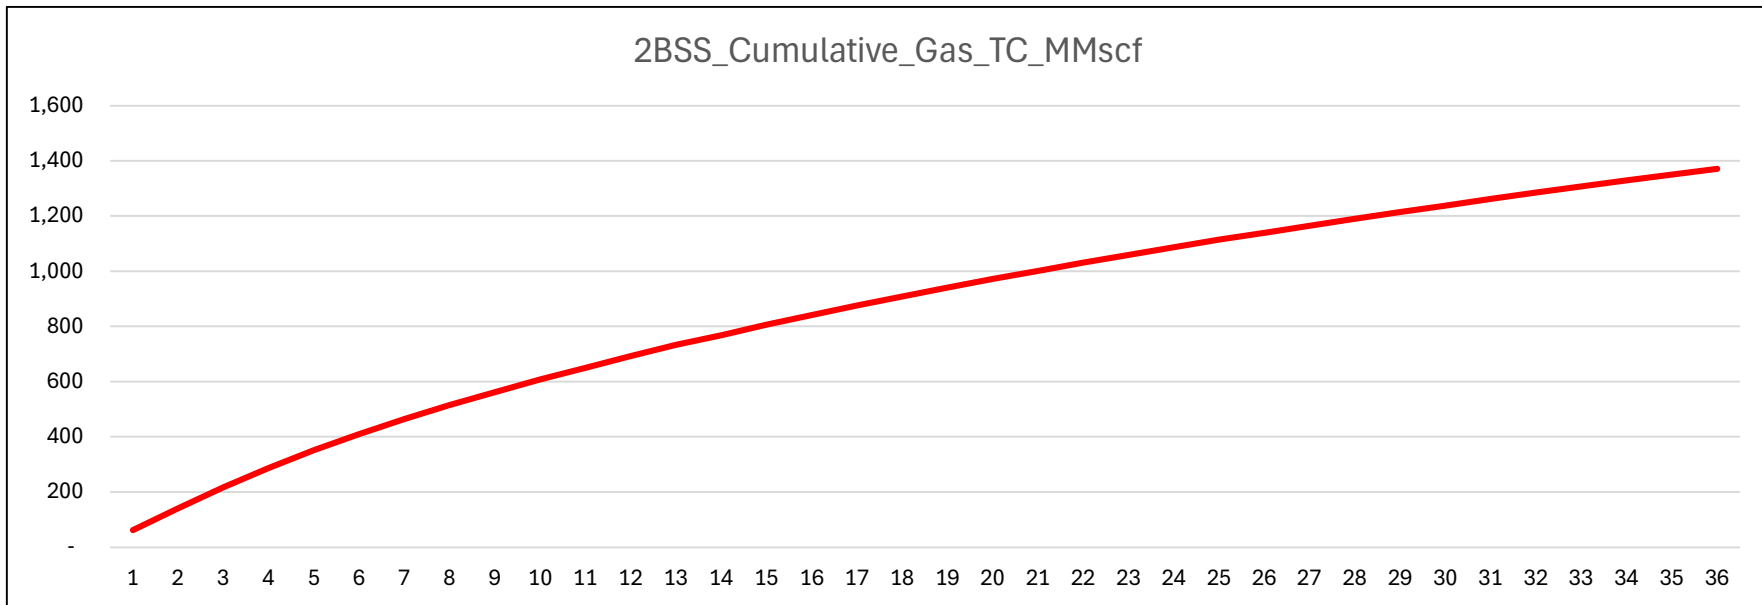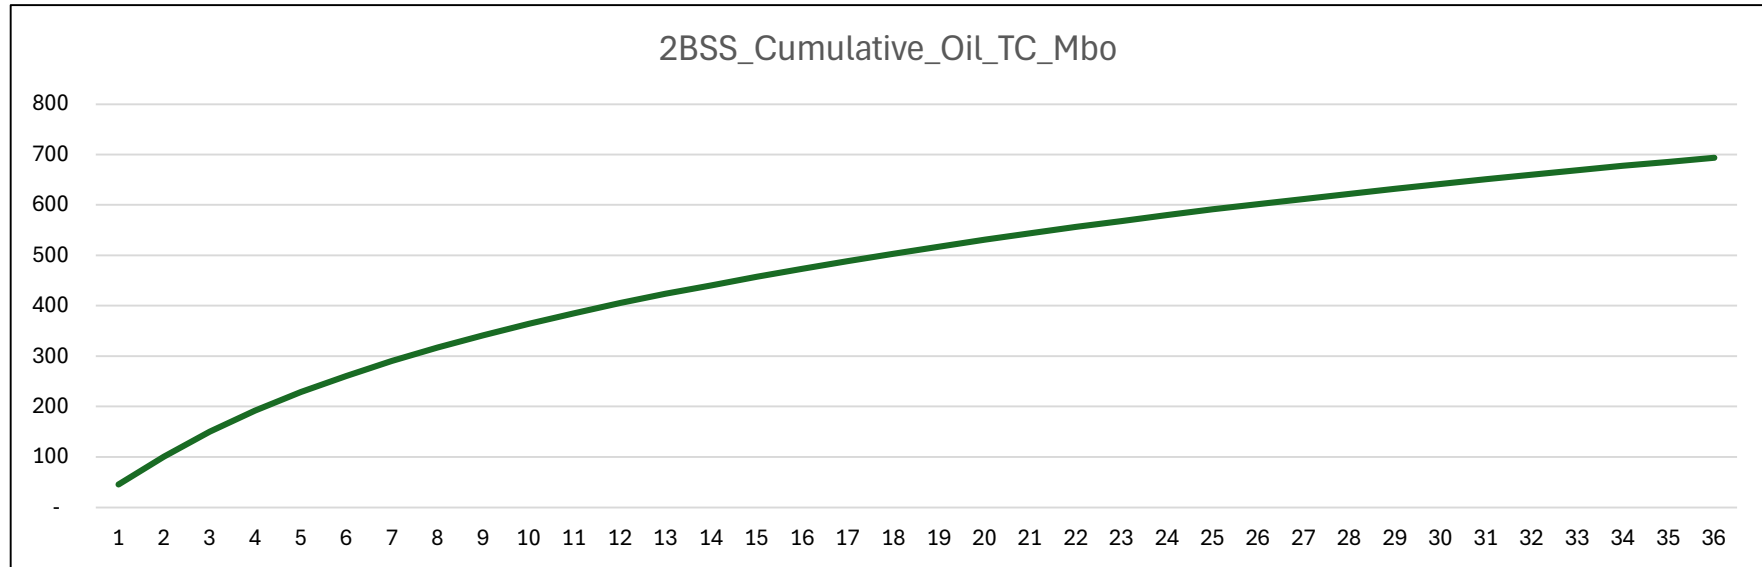

Anticipated Production Decline Curve

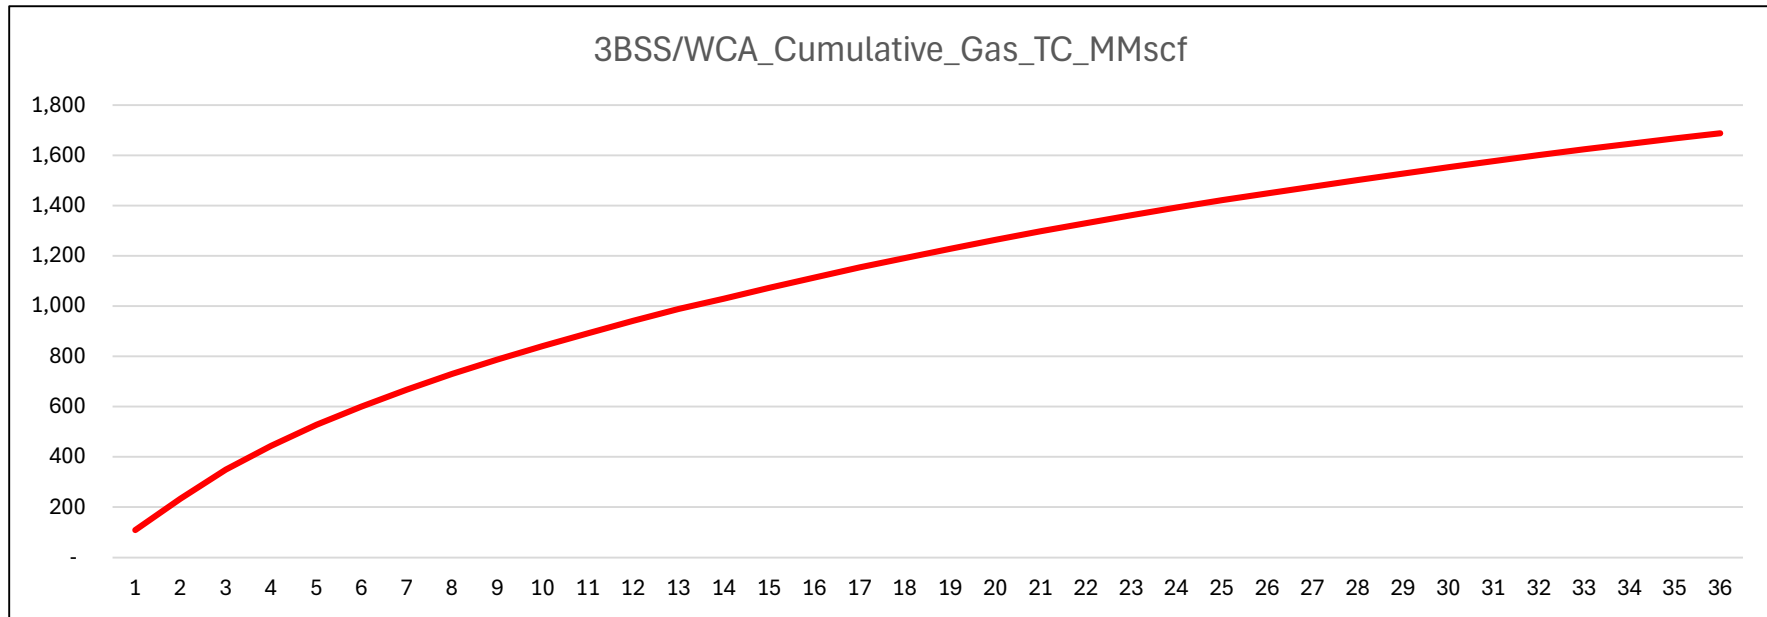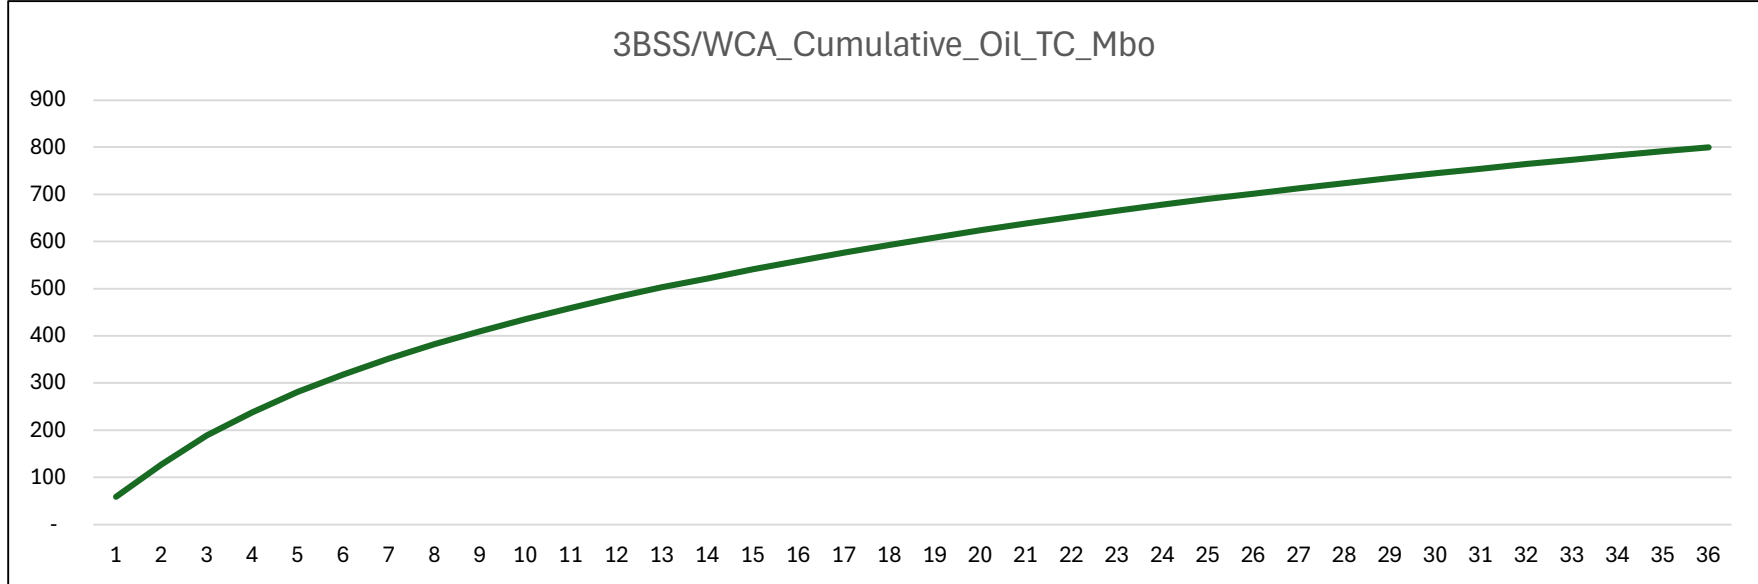

PECOS DISTRICT DRILLING CONDITIONS OF APPROVAL

OPERATOR'S NAME:	COG OPERATING LLC
WELL NAME & NO.:	DONKEY POTROAST FED COM 504H
SURFACE HOLE FOOTAGE:	480'S & 1155'E
BOTTOM HOLE FOOTAGE:	50'S & 1330'E
LOCATION:	Section 15, T.20 S., R.33 E., NMP
COUNTY:	Lea County, New Mexico

COA

H ₂ S	☐ No	☒ Yes
Potash / WIPP	☐ None ☐ Secretary ☒ R-111-Q ☐ Open Annulus	☐ WIPP
	5-String Design: Open 2nd Int x 3rd Int Annulus (ICP 2 below Relief Zone)	
Cave / Karst	☒ Low ☐ Medium ☐ High ☐ Critical	
Wellhead	☐ Conventional ☒ Multibowl ☐ Both ☐ Diverter	
Cementing	☐ Primary Squeeze ☐ Cont. Squeeze ☒ EchoMeter ☐ DV Tool	
Special Req	☒ Capitan Reef ☐ Water Disposal ☒ COM ☐ Unit	
Waste Prev.	☐ Self-Certification ☒ Waste Min. Plan ☐ APD Submitted prior to 06/10/2024	
Additional Language	☒ Flex Hose ☒ Casing Clearance ☐ Pilot Hole ☒ Break Testing	
	☒ Five-String ☐ Offline Cementing ☒ Fluid-Filled	

A. HYDROGEN SULFIDE

A Hydrogen Sulfide (H₂S) Drilling Plan shall be activated AT SPUD. As a result, the Hydrogen Sulfide area must meet 43 CFR part 3170 requirements, which includes equipment and personnel/public protection items. If Hydrogen Sulfide is encountered, please provide measured values and formations to the BLM.

APD is within the R-111-Q defined boundary. Operator must follow all procedures and requirements listed within the updated order.

B. CASING

1. The **20** inch surface casing shall be set at approximately **1465 feet per BLM Geologist** (a minimum of 25 feet (Lea County) into the Rustler Anhydrite, above the salt, and below usable fresh water) and cemented to the surface.
 - a. If cement does not circulate to the surface, the appropriate BLM office shall be notified and a temperature survey utilizing an electronic type temperature survey with surface log readout will be used or a cement bond log shall be run to verify the top of the cement. Temperature survey will be run a minimum of six hours after pumping

- cement and ideally between 8-10 hours after completing the cement job.
- b. Wait on cement (WOC) time for a primary cement job will be a minimum of **8 hours** or **500 pounds compressive strength**, whichever is greater. (This is to include the lead cement)
 - c. Wait on cement (WOC) time for a remedial job will be a minimum of 4 hours after bringing cement to surface or 500 pounds compressive strength, whichever is greater.
 - d. If cement falls back, remedial cementing will be done prior to drilling out that string.
- **Cement excess is less than 25%, more cement is required if washout occurs. Adjust cement volume and excess based on a fluid caliper or similar method that reflects the as-drilled size of the wellbore.**

Intermediate casing must be kept fluid filled to meet BLM minimum collapse requirement.

2. The **13-3/8** inch intermediate 1 casing shall be set at approximately **3575 feet per BLM Geologist**. The minimum required fill of cement behind the **13-3/8** inch intermediate 1 casing is:
 - Cement to surface. If cement does not circulate see B.1.a, c-d above. **Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry due to cave/karst, Capitan Reef, or potash.**
 - **Cement excess is less than 25%, more cement is required if washout occurs. Adjust cement volume and excess based on a fluid caliper or similar method that reflects the as-drilled size of the wellbore.**

Intermediate casing must be kept fluid filled to meet BLM minimum collapse requirement.

3. Intermediate 2 should be set prior to entering Delaware group to facilitate monitoring during hydraulic fracturing, and post-frac bradenhead cementing. The **9-5/8** inch intermediate 2 casing shall be set at approximately **5135 feet**. The minimum required fill of cement behind the **9-5/8** inch intermediate 2 casing is:
 - Cement to surface. If cement does not circulate see B.1.a, c-d above. **Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry due to cave/karst, Capitan Reef, or potash.**
 - **Cement excess is less than 25%, more cement is required if washout occurs. Adjust cement volume and excess based on a fluid caliper or similar method that reflects the as-drilled size of the wellbore.**
4. The minimum required fill of cement behind the **7-5/8** inch intermediate 3 casing is:

(Primary + Post Frac Bradenhead):

- **A monitored open annulus will be incorporated during completion by leaving the Intermediate 2 x Intermediate 3 annulus un-cemented and monitored inside the Intermediate String.** Operator must follow monitoring requirements listed within R-111-Q. Tieback requirements shall be met within **180 days**.

Operator has proposed to pump down **intermediate 2 x intermediate 3** annulus post completion. **Operator must run Echo-meter to verify Cement Slurry/Fluid top in the annulus OR operator shall run a CBL from TD of the intermediate 2/intermediate 3 casing to surface after the second stage BH to verify TOC.** Submit results to the BLM. No displacement fluid/wash out shall be utilized at the top of the cement slurry during second stage bradenhead when running Echo-meter if cement is required to surface. Adjust cement volume and excess based on a fluid caliper or similar method that reflects the as-drilled size of the wellbore.

Operator has proposed an open annulus completion in R-111-Q. Operator shall provide a method of verification pre-completion top of cement. **Submit results to the BLM. Pressure monitoring device and Pressure Safety Valves must be installed at surface on both the intermediate annulus and the production annulus for the life of the well.**

In the event of a casing failure during completion, the operator must contact the BLM at (575-706-2779) and (575-361-2822 Eddy County).

- **After bradenhead mentioned above Cement should tie-back 500 feet or 50 feet on top of the Capitan Reef, whichever is closer to surface** into the previous casing but not higher than USGS Marker Bed No. 126. **Operator must verify top of cement per R-111-Q requirements.** Submit results to the BLM. If cement does not circulate, contact the appropriate BLM office. **Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry due to cave/karst, Capitan Reef, or potash.**
- **Cement excess is less than 25%, more cement is required if washout occurs. Adjust cement volume and excess based on a fluid caliper or similar method that reflects the as-drilled size of the wellbore.**

5. The minimum required fill of cement behind the 5-1/2 inch production casing is:

- **Cement should tie-back 500 feet** into the previous casing but not higher than USGS Marker Bed No. 126. **Operator must verify top of cement per R-111-Q requirements.** Submit results to the BLM. If cement does not circulate, contact the appropriate BLM office. **Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry due to cave/karst, Capitan Reef, or potash.**

- **Cement excess is less than 25%, more cement is required if washout occurs. Adjust cement volume and excess based on a fluid caliper or similar method that reflects the as-drilled size of the wellbore.**

C. PRESSURE CONTROL

1. Variance approved to use flex line from BOP to choke manifold. Manufacturer's specification to be readily available. No external damage to flex line. Flex line to be installed as straight as possible (no hard bends).'
2. Operator has proposed a multi-bowl wellhead assembly. This assembly will only be tested when installed on the **20** inch surface casing. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **10,000 (10M) psi. Variance is approved to use a 5000 (5M) Annular which shall be tested to 3500 (70% Working Pressure) psi.**
 - a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
 - b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
 - c. Manufacturer representative shall install the test plug for the initial BOP test.
 - d. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
 - e. Whenever any seal subject to test pressure is broken, all the tests in OOGO2.III.A.2.i must be followed.

D. SPECIAL REQUIREMENT (S)

Communitization Agreement

- The operator will submit a Communitization Agreement to the Santa Fe Office, 301 Dinosaur Trail Santa Fe, New Mexico 87508, at least 90 days before the anticipated date of first production from a well subject to a spacing order issued by the New Mexico Oil Conservation Division. The Communitization Agreement will include the signatures of all working interest owners in all Federal and Indian leases subject to the Communitization Agreement (i.e., operating rights owners and lessees of record), or certification that the operator has obtained the written signatures of all such owners and will make those signatures available to the BLM immediately upon request.
- The operator will submit an as-drilled survey well plat of the well completion, but are not limited to, those specified in 43 CFR 3171 and 3172.
- If the operator does not comply with this condition of approval, the BLM may take enforcement actions that include, but are not limited to, those specified in 43 CFR 3163.1.

- In addition, the well sign shall include the surface and bottom hole lease numbers. When the Communitization Agreement number is known, it shall also be on the sign.

BOPE Break Testing Variance

- BOPE Break Testing is ONLY permitted for intervals utilizing a 5M BOPE or less. **(Annular preventer must be tested to a minimum of 70% of BOPE working pressure and shall be higher than the MASP.)**
- BOPE Break Testing is NOT permitted to drilling the production hole section.
- Variance only pertains to the intermediate hole-sections and no deeper than the Bone Springs formation.
- While in transfer between wells, the BOPE shall be secured by the hydraulic carrier or cradle.
- Any well control event while drilling require notification to the BLM Petroleum Engineer **(575-706-2779)** prior to the commencement of any BOPE Break Testing operations.
- A full BOPE test is required prior to drilling the first deep intermediate hole section. If any subsequent hole interval is deeper than the first, a full BOPE test will be required. (200' TVD tolerance between intermediate shoes is allowable).
- The BLM is to be contacted (575-689-5981 Lea County) 4 hours prior to BOPE tests.
- As a minimum, a full BOPE test shall be performed at 21-day intervals.
- In the event any repairs or replacement of the BOPE is required, the BOPE shall test as per **43 CFR 3172**.
- If in the event break testing is not utilized, then a full BOPE test would be conducted.

Casing Clearance

- **The W441 connection should tie back 500'+ into the W513 intermediate casing for clearance overlap.**

Operator shall clean up cycles until wellbore is clear of cuttings and any large debris, ensure cutting sizes are adequate "coffee ground or less" before cementing.

GENERAL REQUIREMENTS

The BLM is to be notified in advance for a representative to witness:

- a. Spudding well (minimum of 24 hours)
- b. Setting and/or Cementing of all casing strings (minimum of 4 hours)
- c. BOPE tests (minimum of 4 hours)

Contact Petroleum Engineering Inspection Staff:

☒ Eddy County

EMAIL or call the Carlsbad Field Office, 620 East Greene St., Carlsbad, NM 88220,
BLM_NM_CFO_DrillingNotifications@BLM.GOV
(575) 361-2822

☒ Lea County

Call the Hobbs Field Station, 414 West Taylor, Hobbs NM 88240,

(575) 689-5981

1. Unless the production casing has been run and cemented or the well has been properly plugged, the drilling rig shall not be removed from over the hole without prior approval.
 - a. In the event the operator has proposed to drill multiple wells utilizing a skid/walking rig. Operator shall secure the wellbore on the current well, after installing and testing the wellhead, by installing a blind flange of like pressure rating to the wellhead and a pressure gauge that can be monitored while drilling is performed on the other well(s).
 - b. When the operator proposes to set surface casing with Spudder Rig
 - i. Notify the BLM when moving in and removing the Spudder Rig.
 - ii. Notify the BLM when moving in the 2nd Rig. Rig to be moved in within 90 days of notification that Spudder Rig has left the location.
 - iii. BOP/BOPE test to be conducted per **43 CFR 3172** as soon as 2nd Rig is rigged up on well.
2. Floor controls are required for 3M or Greater systems. These controls will be on the rig floor, unobstructed, readily accessible to the driller and will be operational at all times during drilling and/or completion activities. Rig floor is defined as the area immediately around the rotary table; the area immediately above the substructure on which the draw works are located, this does not include the dog house or stairway area.
3. For intervals in which cement to surface is required, cement to surface should be verified with a visual check and density or pH check to differentiate cement from spacer and drilling mud. The results should be documented in the driller's log and daily reports.

A. CASING

1. Changes to the approved APD casing program need prior approval if the items substituted are of lesser grade or different casing size or are Non-API. The Operator can exchange the components of the proposal with that of superior strength (i.e. changing from J-55 to N-80, or from 36# to 40#). Changes to the approved cement program need prior approval if the altered cement plan has less volume or strength or if the changes are substantial (i.e. Multistage tool, ECP, etc.). The initial wellhead installed on the well will remain on the well with spools used as needed.
2. Wait on cement (WOC) for Potash Areas: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi for all cement blends of both lead and tail cement, 2) until cement has been in place at least 8 hours. WOC time will be recorded in the driller's log. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.

3. Wait on cement (WOC) for Water Basin: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi at the shoe, 2) until cement has been in place at least 8 hours. WOC time will be recorded in the driller's log. See individual casing strings for details regarding lead cement slurry requirements. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
4. Provide compressive strengths including hours to reach required 500 pounds compressive strength prior to cementing each casing string. Have well specific cement details onsite prior to pumping the cement for each casing string.
5. No pea gravel permitted for remedial or fall back remedial without prior authorization from the BLM engineer.
6. On that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Formation at the shoe shall be tested to a minimum of the mud weight equivalent anticipated to control the formation pressure to the next casing depth or at total depth of the well. This test shall be performed before drilling more than 20 feet of new hole.
7. If hardband drill pipe is rotated inside casing, returns will be monitored for metal. If metal is found in samples, drill pipe will be pulled and rubber protectors which have a larger diameter than the tool joints of the drill pipe will be installed prior to continuing drilling operations.
8. Whenever a casing string is cemented in the R-111-Q potash area, the NMOCD requirements shall be followed.

B. PRESSURE CONTROL

1. All blowout preventer (BOP) and related equipment (BOPE) shall comply with well control requirements as described in **43 CFR 3172**.
2. If a variance is approved for a flexible hose to be installed from the BOP to the choke manifold, the following requirements apply: The flex line must meet the requirements of API 16C. Check condition of flexible line from BOP to choke manifold, replace if exterior is damaged or if line fails test. Line to be as straight as possible with no hard bends and is to be anchored according to Manufacturer's requirements. The flexible hose can be exchanged with a hose of equal size and equal or greater pressure rating. Anchor requirements, specification sheet and hydrostatic pressure test certification matching the hose in service, to be onsite for review. These documents shall be posted in the company man's trailer and on the rig floor.

3. 5M or higher system requires an HCR valve, remote kill line and annular to match. The remote kill line is to be installed prior to testing the system and tested to stack pressure.
4. If the operator has proposed a multi-bowl wellhead assembly in the APD. The following requirements must be met:
 - i. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
 - ii. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
 - iii. Manufacturer representative shall install the test plug for the initial BOP test.
 - iv. Whenever any seal subject to test pressure is broken, all the tests in 43 CFR 3172.6(b)(9) must be followed.
 - v. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
5. The appropriate BLM office shall be notified a minimum of 4 hours in advance for a representative to witness the tests.
 - i. In a water basin, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. The casing cut-off and BOP installation can be initiated four hours after installing the slips, which will be approximately six hours after bumping the plug. For those casing strings not using slips, the minimum wait time before cut-off is eight hours after bumping the plug. BOP/BOPE testing can begin after cut-off or once cement reaches 500 psi compressive strength (including lead cement), whichever is greater. However, if the float does not hold, cut-off cannot be initiated until cement reaches 500 psi compressive strength (including lead when specified).
 - ii. In potash areas, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. For all casing strings, casing cut-off and BOP installation can be initiated at twelve hours after bumping the cement plug. The BOPE test can be initiated after bumping the cement plug with the casing valve open. (only applies to single stage cement jobs, prior to the cement setting up.)
 - iii. The tests shall be done by an independent service company utilizing a test plug not a cup or J-packer and can be initiated immediately with the casing valve open. The operator also has the option of utilizing an

independent tester to test without a plug (i.e. against the casing) pursuant to **43 CFR 3172** with the pressure not to exceed 70% of the burst rating for the casing. Any test against the casing must meet the WOC time for 8 hours or 500 pounds compressive strength, whichever is greater, prior to initiating the test (see casing segment as lead cement may be critical item).

- iv. The test shall be run on a 5000 psi chart for a 2-3M BOP/BOP, on a 10000 psi chart for a 5M BOP/BOPE and on a 15000 psi chart for a 10M BOP/BOPE. If a linear chart is used, it shall be a one hour chart. A circular chart shall have a maximum 2 hour clock. If a twelve hour or twenty-four hour chart is used, tester shall make a notation that it is run with a two hour clock.
- v. The results of the test shall be reported to the appropriate BLM office.
- vi. All tests are required to be recorded on a calibrated test chart. A copy of the BOP/BOPE test chart and a copy of independent service company test will be submitted to the appropriate BLM office.
- vii. The BOP/BOPE test shall include a low pressure test from 250 to 300 psi. The test will be held for a minimum of 10 minutes if test is done with a test plug and 30 minutes without a test plug. This test shall be performed prior to the test at full stack pressure.
- viii. BOP/BOPE must be tested by an independent service company within 500 feet of the top of the Wolfcamp formation if the time between the setting of the intermediate casing and reaching this depth exceeds 20 days. This test does not exclude the test prior to drilling out the casing shoe as per **43 CFR 3172**.

C. DRILLING MUD

Mud system monitoring equipment, with derrick floor indicators and visual and audio alarms, shall be operating before drilling into the Wolfcamp formation, and shall be used until production casing is run and cemented.

D. WASTE MATERIAL AND FLUIDS

All waste (i.e. drilling fluids, trash, salts, chemicals, sewage, gray water, etc.) created as a result of drilling operations and completion operations shall be safely contained and disposed of properly at a waste disposal facility. No waste material or fluid shall be disposed of on the well location or surrounding area. Porto-johns and trash containers will be on-location during fracturing operations or any other crew-intensive operations.

JS 11/20/2024

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
<https://www.emnrd.nm.gov/ocd/contact-us>

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 450255

CONDITIONS

Operator: COG OPERATING LLC 600 W Illinois Ave Midland, TX 79701	OGRID: 229137
	Action Number: 450255
	Action Type: [C-101] BLM - Federal/Indian Land Lease (Form 3160-3)

CONDITIONS

Created By	Condition	Condition Date
stanwagner	Cement is required to circulate on both surface and intermediate1 strings of casing.	4/9/2025
stanwagner	If cement does not circulate on any string, a Cement Bond Log (CBL) is required for that string of casing.	4/9/2025
matthew.gomez	Administrative order required for non-standard spacing unit prior to production.	5/3/2025
matthew.gomez	Notify the OCD 24 hours prior to casing & cement.	5/3/2025
matthew.gomez	A [C-103] Sub. Drilling (C-103N) is required within (10) days of spud.	5/3/2025
matthew.gomez	Once the well is spud, to prevent ground water contamination through whole or partial conduits from the surface, the operator shall drill without interruption through the fresh water zone or zones and shall immediately set in cement the water protection string.	5/3/2025
matthew.gomez	Oil base muds are not to be used until fresh water zones are cased and cemented providing isolation from the oil or diesel. This includes synthetic oils. Oil based mud, drilling fluids and solids must be contained in a steel closed loop system.	5/3/2025
matthew.gomez	File As Drilled C-102 and a directional Survey with C-104 completion packet.	5/3/2025
matthew.gomez	This well is within the Capitan Reef. The first intermediate casing string shall be sat and cemented back to surface immediately above the Capitan Reef. The second intermediate string shall be set and cemented back to surface immediately below the base of the Capitan Reef.	5/3/2025
matthew.gomez	Brine water shall not be used in the Capitan Reef. Only fresh water shall be utilized until the Capitan Reef is cased and cemented.	5/3/2025
matthew.gomez	This well is within the R-111-Q defined boundary. Operator must follow all procedures and requirements listed within the order.	5/3/2025
