



U.S. Department of the Interior
Bureau of Land Management

Application for Permit to Drill

APD Package Report

Date Printed: 05/14/2025 08:59 AM

APD ID: 10400100957

Well Status: AAPD

APD Received Date: 09/23/2024 02:55 PM

Well Name: POKER LAKE UNIT 20-8 BD

Operator: XTO PERMIAN OPERATING LLC

Well Number: 208H

APD Package Report Contents

- Form 3160-3
- Operator Certification Report
- Application Report
- Application Attachments
 - Well Plat: 1 file(s)
- Drilling Plan Report
- Drilling Plan Attachments
 - Blowout Prevention Choke Diagram Attachment: 1 file(s)
 - Blowout Prevention BOP Diagram Attachment: 1 file(s)
 - Casing Spec Documents: 2 file(s)
 - Casing Taperd String Specs: 1 file(s)
 - Casing Design Assumptions and Worksheet(s): 1 file(s)
 - Hydrogen sulfide drilling operations plan: 1 file(s)
 - Proposed horizontal/directional/multi-lateral plan submission: 1 file(s)
 - Other Facets: 4 file(s)
 - Other Variances: 4 file(s)
- SUPO Report
- SUPO Attachments
 - Existing Road Map: 1 file(s)
 - Attach Well map: 1 file(s)
 - Production Facilities map: 1 file(s)
 - Water source and transportation map: 1 file(s)
 - Well Site Layout Diagram: 2 file(s)
 - Recontouring attachment: 2 file(s)
 - Other SUPO Attachment: 1 file(s)
- PWD Report
- PWD Attachments
 - None

- Bond Report
- Bond Attachments
 - None

Form 3160-3
(June 2015)UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

APPLICATION FOR PERMIT TO DRILL OR REENTER

FORM APPROVED
OMB No. 1004-0137
Expires: January 31, 2018

1a. Type of work: ☒ DRILL ☐ REENTER		5. Lease Serial No. NMLC064894A
1b. Type of Well: ☒ Oil Well ☐ Gas Well ☐ Other		6. If Indian, Allottee or Tribe Name
1c. Type of Completion: ☐ Hydraulic Fracturing ☐ Single Zone ☒ Multiple Zone		7. If Unit or CA Agreement, Name and No. NMNM071016X/POKER LAKE UNIT
2. Name of Operator XTO PERMIAN OPERATING LLC		8. Lease Name and Well No. POKER LAKE UNIT 20-8 BD 208H
3a. Address 6401 HOLIDAY HILL ROAD BLDG 5, MIDLAND, TX 7970	3b. Phone No. (include area code) (432) 683-2277	9. API Well No. 30-015-56759
4. Location of Well (Report location clearly and in accordance with any State requirements. *) At surface NWSE / 1813 FSL / 1544 FEL / LAT 32.113303 / LONG -103.899786 At proposed prod. zone NESE / 2652 FSL / 1248 FEL / LAT 32.144866 / LONG -103.89885		10. Field and Pool, or Exploratory CORRAL CANYON/BONE SPRING
14. Distance in miles and direction from nearest town or post office*		11. Sec., T. R. M. or Blk. and Survey or Area SEC 20/T25S/R30E/NMP
15. Distance from proposed* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any) 1544 feet		12. County or Parish EDDY
16. No of acres in lease		13. State NM
17. Spacing Unit dedicated to this well 400.0		
18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft. 30 feet		20. BLM/BIA Bond No. in file FED: COB000050
21. Elevations (Show whether DF, KDB, RT, GL, etc.) 3198 feet		22. Approximate date work will start* 10/22/2025
23. Estimated duration 45 days		
24. Attachments		

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, and the Hydraulic Fracturing rule per 43 CFR 3162.3-3 (as applicable)

- | | |
|--|---|
| 1. Well plat certified by a registered surveyor. | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above). |
| 2. A Drilling Plan. | 5. Operator certification. |
| 3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office). | 6. Such other site specific information and/or plans as may be requested by the BLM. |

25. Signature (Electronic Submission)	Name (Printed/Typed) SAMANTHA WEIS / Ph: (432) 682-8873	Date 09/23/2024
Title Permitting Advisor		
Approved by (Signature) (Electronic Submission)	Name (Printed/Typed) CODY LAYTON / Ph: (575) 234-5959	Date 05/12/2025
Title Assistant Field Manager Lands & Minerals		
Office Carlsbad Field Office		

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

APPROVED WITH CONDITIONS

(Continued on page 2)

*(Instructions on page 2)

INSTRUCTIONS

GENERAL: This form is designed for submitting proposals to perform certain well operations, as indicated on Federal and Indian lands and leases for action by appropriate Federal agencies, pursuant to applicable Federal laws and regulations. Any necessary special instructions concerning the use of this form and the number of copies to be submitted, particularly with regard to local, area, or regional procedures and practices, either are shown below or will be issued by, or may be obtained from local Federal offices.

ITEM I: If the proposal is to redrill to the same reservoir at a different subsurface location or to a new reservoir, use this form with appropriate notations. Consult applicable Federal regulations concerning subsequent work proposals or reports on the well.

ITEM 4: Locations on Federal or Indian land should be described in accordance with Federal requirements. Consult local Federal offices for specific instructions.

ITEM 14: Needed only when location of well cannot readily be found by road from the land or lease description. A plat, or plats, separate or on the reverse side, showing the roads to, and the surveyed location of, the well, and any other required information, should be furnished when required by Federal agency offices.

ITEMS 15 AND 18: If well is to be, or has been directionally drilled, give distances for subsurface location of hole in any present or objective productive zone.

ITEM 22: Consult applicable Federal regulations, or appropriate officials, concerning approval of the proposal before operations are started.

ITEM 24: If the proposal will involve hydraulic fracturing operations, you must comply with 43 CFR 3162.3-3, including providing information about the protection of usable water. Operators should provide the best available information about all formations containing water and their depths. This information could include data and interpretation of resistivity logs run on nearby wells. Information may also be obtained from state or tribal regulatory agencies and from local BLM offices.

NOTICES

The Privacy Act of 1974 and regulation in 43 CFR 2.48(d) provide that you be furnished the following information in connection with information required by this application.

AUTHORITY: 30 U.S.C. 181 et seq., 25 U.S.C. 396; 43 CFR 3160

PRINCIPAL PURPOSES: The information will be used to: (1) process and evaluate your application for a permit to drill a new oil, gas, or service well or to reenter a plugged and abandoned well; and (2) document, for administrative use, information for the management, disposal and use of National Resource Lands and resources including (a) analyzing your proposal to discover and extract the Federal or Indian resources encountered; (b) reviewing procedures and equipment and the projected impact on the land involved; and (c) evaluating the effects of the proposed operation on the surface and subsurface water and other environmental impacts.

ROUTINE USE: Information from the record and/or the record will be transferred to appropriate Federal, State, and local or foreign agencies, when relevant to civil, criminal or regulatory investigations or prosecution, in connection with congressional inquiries and for regulatory responsibilities.

EFFECT OF NOT PROVIDING INFORMATION: Filing of this application and disclosure of the information is mandatory only if you elect to initiate a drilling or reentry operation on an oil and gas lease.

The Paperwork Reduction Act of 1995 requires us to inform you that:

The BLM connects this information to an evaluation of the technical, safety, and environmental factors involved with drilling for oil and/or gas on Federal and Indian oil and gas leases. This information will be used to analyze and approve applications. Response to this request is mandatory only if the operator elects to initiate drilling or reentry operations on an oil and gas lease. The BLM would like you to know that you do not have to respond to this or any other Federal agency-sponsored information collection unless it displays a currently valid OMB control number.

BURDEN HOURS STATEMENT: Public reporting burden for this form is estimated to average 8 hours per response, including the time for reviewing instructions, gathering and maintaining data, and completing and reviewing the form. Direct comments regarding the burden estimate or any other aspect of this form to U.S. Department of the Interior, Bureau of Land Management (1004-0137), Bureau Information Connection Clearance Officer (WO-630), 1849 C Street, N.W., Mail Stop 401 LS, Washington, D.C. 20240.

Additional Operator Remarks

Location of Well

0. SHL: NWSE / 1813 FSL / 1544 FEL / TWSP: 25S / RANGE: 30E / SECTION: 20 / LAT: 32.113303 / LONG: -103.899786 (TVD: 0 feet, MD: 0 feet)

PPP: SESE / 100 FSL / 1244 FEL / TWSP: 25S / RANGE: 30E / SECTION: 20 / LAT: 32.108599 / LONG: -103.898826 (TVD: 9510 feet, MD: 10600 feet)

BHL: NESE / 2652 FSL / 1248 FEL / TWSP: 25S / RANGE: 30E / SECTION: 8 / LAT: 32.144866 / LONG: -103.89885 (TVD: 9510 feet, MD: 23736 feet)

BLM Point of Contact

Name: MARIAH HUGHES

Title: Land Law Examiner

Phone: (575) 234-5972

Email: mhughes@blm.gov

Review and Appeal Rights

A person contesting a decision shall request a State Director review. This request must be filed within 20 working days of receipt of the Notice with the appropriate State Director (see 43 CFR 3165.3). The State Director review decision may be appealed to the Interior Board of Land Appeals, 801 North Quincy Street, Suite 300, Arlington, VA 22203 (see 43 CFR 3165.4). Contact the above listed Bureau of Land Management office for further information.

**PECOS DISTRICT
SURFACE USE
CONDITIONS OF APPROVAL**

OPERATOR'S NAME:	XTO PERMIAN OPERATING LLC
LEASE NO.:	NMLC064894
COUNTY:	Eddy County, New Mexico

Wells:

POKER LAKE UNIT 20-17 BD #201H: PAD B – E1

Surface Hole Location: 1,904' FWL & 1,434' FSL, SECTION 20, T. 25 S. R. 30 E.

Bottom Hole Location: 330' FWL & 10' FNL, SECTION 17, T. 25 S. R. 30 E.

POKER LAKE UNIT 20-17 BD #202H: PAD B – E2

Surface Hole Location: 1,934' FWL & 1,433' FSL, SECTION 20, T. 25 S. R. 30 E.

Bottom Hole Location: 800' FWL & 10' FNL, SECTION 17, T. 25 S. R. 30 E.

POKER LAKE UNIT 20-17 BD #203H: PAD B – E3

Surface Hole Location: 1,964' FWL & 1,432' FSL, SECTION 20, T. 25 S. R. 30 E.

Bottom Hole Location: 1,570' FWL & 10' FNL, SECTION 17, T. 25 S. R. 30 E.

POKER LAKE UNIT 20-8 BD #204H: PAD B – E4

Surface Hole Location: 1,994' FWL & 1,431' FSL, SECTION 20, T. 25 S. R. 30 E.

Bottom Hole Location: 1,895' FWL & 2,649' FSL, SECTION 8, T. 25 S. R. 30 E.

POKER LAKE UNIT 20-8 BD #205H: PAD B – E5

Surface Hole Location: 2,024' FWL & 1,431' FSL, SECTION 20, T. 25 S. R. 30 E.

Bottom Hole Location: 2,544' FEL & 2,650' FSL, SECTION 8, T. 25 S. R. 30 E.

POKER LAKE UNIT 20-8 BD #206H: PAD D – B5

Surface Hole Location: 1,604' FEL & 1,813' FSL, SECTION 20, T. 25 S. R. 30 E.

Bottom Hole Location: 2,358' FEL & 2,650' FSL, SECTION 8, T. 25 S. R. 30 E.

POKER LAKE UNIT 20-8 BD #207H: PAD D – B6

Surface Hole Location: 1,574' FEL & 1,813' FSL, SECTION 20, T. 25 S. R. 30 E.

Bottom Hole Location: 1,348' FEL & 2,652' FSL, SECTION 8, T. 25 S. R. 30 E.

POKER LAKE UNIT 20-8 BD #208H: PAD D – B7

Surface Hole Location: 1,544' FEL & 1,813' FSL, SECTION 20, T. 25 S. R. 30 E.

Bottom Hole Location: 1,248' FEL & 2,652' FSL, SECTION 8, T. 25 S. R. 30 E.

POKER LAKE UNIT 20-8 BD #209H: PAD D – B8

Surface Hole Location: 1,514' FEL & 1,813' FSL, SECTION 20, T. 25 S. R. 30 E.

Bottom Hole Location: 177' FEL & 10' FNL, SECTION 8, T. 25 S. R. 30 E.

POKER LAKE UNIT 20-8 BD #210H: PAD D – B9

Surface Hole Location: 1,484' FEL & 1,813' FSL, SECTION 20, T. 25 S. R. 30 E.

Bottom Hole Location: 717' FEL & 10' FNL, SECTION 8, T. 25 S. R. 30 E.

TABLE OF CONTENTS

1.	GENERAL PROVISIONS	4
1.1.	ARCHAEOLOGICAL, PALEONTOLOGY & HISTORICAL SITES.....	4
1.2.	RANGELAND RESOURCES.....	4
1.2.1.	Cattleguards	4
1.2.2.	Fence Requirement	5
1.2.3.	Livestock Watering Requirement	5
1.3.	NOXIOUS WEEDS	5
1.3.1	African Rue (Peganum harmala)	5
1.4.	LIGHT POLLUTION.....	5
1.4.1.	Downfacing.....	5
1.4.2.	Shielding.....	6
1.4.3.	Lighting Color.....	6
2.	SPECIAL REQUIREMENTS	6
2.1.	WATERSHED.....	6
2.1.1.	Tank Battery.....	6
2.1.2.	Buried/Surface Line(s)	6
2.1.3.	Electric Line(s)	6
2.1.4.	Temporary Use Fresh Water Frac Line(s).....	7
2.3	VISUAL RESOURCE MANAGEMENT	7
2.5.1	VRM IV.....	7
3.	CONSTRUCTION REQUIREMENTS	7
3.1	CONSTRUCTION NOTIFICATION.....	7
3.2	TOPSOIL	7
3.3	CLOSED LOOP SYSTEM	7
3.4	FEDERAL MINERAL PIT	7
3.5	WELL PAD & SURFACING.....	7
3.6	EXCLOSURE FENCING (CELLARS & PITS).....	7
4.1	BURIED PIPELINES	8
4.2	SURFACE PIPELINES	9
4.3	RANGELAND MITIGATION FOR PIPELINES	12
4.5.1	Fence Requirement	12
4.5.2	Cattleguards	12
4.5.3	Livestock Watering Requirement	12
4.	OVERHEAD ELECTRIC LINES	12

5. PRODUCTION (POST DRILLING) 14

5.1 WELL STRUCTURES & FACILITIES 14

5.1.1 Placement of Production Facilities..... 14

5.1.2 Exclosure Netting (Open-top Tanks) 14

5.1.3. Chemical and Fuel Secondary Containment and Exclosure Screening 14

5.1.4. Open-Vent Exhaust Stack Exclosures 14

5.1.5. Containment Structures 14

6. RECLAMATION 15

6.1 ROAD AND SITE RECLAMATION 15

6.2 EROSION CONTROL 15

6.3 INTERIM RECLAMATION..... 15

6.4 FINAL ABANDONMENT & RECLAMATION 15

6.5 SEEDING TECHNIQUES 16

6.6 SOIL SPECIFIC SEED MIXTURE 16

1. GENERAL PROVISIONS

The failure of the operator to comply with these requirements may result in the assessment of liquidated damages or penalties pursuant to 43 CFR 3163.1 or 3163.2. A copy of these conditions of approval shall be present on the location during construction, drilling and reclamation activity. Any request for a variance shall be submitted to the Authorized Officer on Form 3160-5, Sundry Notices and Report on Wells.

1.1. ARCHAEOLOGICAL, PALEONTOLOGY & HISTORICAL SITES

Any cultural resource (historic or prehistoric site or object) discovered by the operator, or any person working on the operator's behalf, on the public or federal land shall be immediately reported to the Authorized Officer. The operator shall suspend all operations in the immediate area (within 100ft) of such discovery until written authorization to proceed is issued by the Authorized Officer. An evaluation of the discovery will be made by the Authorized Officer, in conjunction with a BLM Cultural Resource Specialist, to determine appropriate actions to prevent the loss of significant scientific values. The operator shall be responsible for the cost of evaluation and any decision as to the proper mitigation measures will be made by the Authorized Officer after consulting with the operator.

Traditional Cultural Properties (TCPs) are protected by NHPA as codified in 36 CFR 800 for possessing traditional, religious, and cultural significance tied to a certain group of individuals. Though there are currently no designated TCPs within the project area or within a mile of the project area, but it is possible for a TCP to be designated after the approval of this project. **If a TCP is designated in the project area after the project's approval, the BLM Authorized Officer will notify the operator of the following conditions and the duration for which these conditions are required.**

1. Temporary halting of all construction, drilling, and production activities to lower noise.
2. Temporary shut-off of all artificial lights at night.

The operator is hereby obligated to comply with procedures established in the Native American Graves Protection and Repatriation Act (NAGPRA), specifically NAGPRA Subpart B regarding discoveries, to protect human remains, associated funerary objects, sacred objects, and objects of cultural patrimony discovered during project work. If any human skeletal remains, funerary objects, sacred objects, or objects of cultural patrimony are discovered at any time during construction, all construction activities shall halt and a BLM-CFO Authorized Officer will be notified immediately. The BLM will then be required to be notified, in writing, within 24 hours of the discovery. The written notification should include the geographic location by county and state, the contents of the discovery, and the steps taken to protect said discovery. You must also include any potential threats to the discovery and a conformation that all activity within 100ft of the discovery has ceased and work will not resume until written certification is issued. All work on the entire project must halt for a minimum of 3 days and work cannot resume until an Authorized Officer grants permission to do so.

Any paleontological resource discovered by the operator, or any person working on the operator's behalf, on public or Federal land shall be immediately reported to the Authorized Officer. The operator shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the Authorized Officer. The operator will be responsible for the cost of evaluation and any decision as to the proper mitigation measures will be made by the Authorized Officer after consulting with the operator.

1.2. RANGELAND RESOURCES

1.2.1. Cattleguards

Where a permanent cattleguard is approved, an appropriately sized cattleguard(s) sufficient to carry out the project shall be installed and maintained at fence crossing(s). Any existing cattleguard(s) on the access road shall be repaired or replaced if they are damaged or have deteriorated beyond practical use. The operator shall be responsible for the condition of the existing cattleguard(s) that are in place and are utilized during

lease operations. A gate shall be constructed on one side of the cattleguard and fastened securely to H-braces.

1.2.2. Fence Requirement

Where entry granted across a fence line, the fence must be braced and tied off on both sides of the passageway prior to cutting. Once the work is completed, the fence will be restored to its prior condition, or better. The operator shall notify the private surface landowner or the grazing allotment holder prior to crossing any fence(s).

1.2.3. Livestock Watering Requirement

Any damage to structures that provide water to livestock throughout the life of the well, caused by operations from the well site, must be immediately corrected by the operator. The operator must notify the BLM office (575-234-5972) and the private surface landowner or the grazing allotment holder if any damage occurs to structures that provide water to livestock.

1.3. NOXIOUS WEEDS

The operator shall be held responsible if noxious weeds become established within the areas of operations. Weed control shall be required on the disturbed land where noxious weeds exist, which includes the roads, pads, associated pipeline corridor, and adjacent land affected by the establishment of weeds due to this action. The operator shall consult with the Authorized Officer for acceptable weed control methods, which include following EPA, New Mexico Department of Agriculture, and BLM requirements and policies.

1.3.1 African Rue (*Peganum harmala*)

Spraying: The spraying of African Rue must be completed by a licensed or certified applicator. In order to attempt to kill or remove African Rue the proper mix of chemical is needed. The mix consists of 2% Arsenal (Imazapyr) and 2% Roundup (Glyphosate) along with a nonionic surfactant. Any other chemicals or combinations shall be approved by the BLM Noxious Weeds Coordinator prior to treatment. African Rue shall be sprayed in connection to any dirt working activities or disturbances to the site being sprayed. Spraying of African Rue shall be done on immature plants at initial growth through flowering and mature plants between budding and flowering stages. Spraying shall not be conducted after flowering when plant is fruiting. This will ensure optimal intake of chemical and decrease chances of developing herbicide resistance. After spraying, the operator or necessary parties must contact the Carlsbad Field Office to inspect the effectiveness of the application treatment to the plant species. No ground disturbing activities can take place until the inspection by the authorized officer is complete. The operator may contact the Environmental Protection Department or the BLM Noxious Weed Coordinator at (575) 234-5972 or BLM_NM_CFO_NoxiousWeeds@blm.gov.

Management Practices: In addition to spraying for African Rue, good management practices should be followed. All equipment should be washed off using a power washer in a designated containment area. The containment area shall be bermed to allow for containment of the seed to prevent it from entering any open areas of the nearby landscape. The containment area shall be excavated near or adjacent to the well pad at a depth of three feet and just large enough to get equipment inside it to be washed off. This will allow all seeds to be in a centrally located area that can be treated at a later date if the need arises.

1.4. LIGHT POLLUTION

1.4.1. Downfacing

All permanent lighting will be pointed straight down at the ground in order to prevent light spill beyond the edge of approved surface disturbance.

1.4.2. Shielding

All permanent lighting will use full cutoff luminaires, which are fully shielded (i.e., not emitting direct or indirect light above an imaginary horizontal plane passing through the lowest part of the light source).

1.4.3. Lighting Color

Lighting shall be 3,500 Kelvin or less (Warm White) except during drilling, completion, and workover operations. No bluish-white lighting shall be used in permanent outdoor lighting.

2. SPECIAL REQUIREMENTS

2.1. WATERSHED

The entire well pad(s) will be bermed to prevent oil, salt, and other chemical contaminants from leaving the well pad. The compacted berm shall be constructed at a minimum of 12 inches with impermeable mineral material (e.g. caliche). Topsoil shall not be used to construct the berm. No water flow from the uphill side(s) of the pad shall be allowed to enter the well pad. The integrity of the berm shall be maintained around the surfaced pad throughout the life of the well and around the downsized pad after interim reclamation has been completed. Any water erosion that may occur due to the construction of the well pad during the life of the well will be quickly corrected and proper measures will be taken to prevent future erosion. Stockpiling of topsoil is required. The topsoil shall be stockpiled in an appropriate location to prevent loss of soil due to water or wind erosion and not used for berming or erosion control. If fluid collects within the bermed area, the fluid must be vacuumed into a safe container and disposed of properly at a state approved facility.

2.1.1. Tank Battery

Tank battery locations will be lined and bermed. A 20-mil permanent liner will be installed with a 4 oz. felt backing to prevent tears or punctures. Secondary containment holding capacity must be large enough to contain 1 ½ times the content of the largest tank or 24-hour production, whichever is greater (displaced volume from all tanks within the berms MUST be subtracted from total volume of containment in calculating holding capacity). Automatic shut off, check valves, or similar systems will be installed for tanks to minimize the effects of catastrophic line failures used in production or drilling.

2.1.2. Buried/Surface Line(s)

When crossing ephemeral drainages, the pipeline(s) will be buried to a minimum depth of 48 inches from the top of pipe to ground level. Erosion control methods such as gabions and/or rock aprons must be placed on both up and downstream sides of the pipeline crossing. In addition, curled (weed free) wood/straw fiber wattles/logs and/or silt fences must be placed on the downstream side for sediment control during construction and maintained until soils and vegetation have stabilized. Water bars must be placed within the corridor to divert and dissipate surface runoff. A pipeline access road is not permitted to cross ephemeral drainages. Traffic must be diverted to a preexisting route. Additional seeding may be required in floodplains and drainages to restore energy dissipating vegetation.

Prior to pipeline installation/construction a leak detection plan will be developed. The method(s) could incorporate gauges to detect pressure drops, situating valves and lines so they can be visually inspected periodically or installing electronic sensors to alarm when a leak is present. The leak detection plan will incorporate an automatic shut off system that will be installed for proposed pipelines to minimize the effects of an undesirable event.

2.1.3. Electric Line(s)

Any water erosion that may occur due to the construction of overhead electric line and during the life of the power line will be quickly corrected and proper measures will be taken to prevent future erosion. A power pole must not be placed in drainages, playas, wetlands, riparian areas, or floodplains and must span across the features at a distance away that does not promote further erosion.

2.1.4. Temporary Use Fresh Water Frac Line(s)

Once the temporary use exceeds the timeline of 180 days and/or with a 90 day extension status; further analysis will be required if the applicant pursues to turn the temporary pipeline into a permanent pipeline.

2.3 VISUAL RESOURCE MANAGEMENT

2.5.1 VRM IV

Above-ground structures including meter housing that are not subject to safety requirements are painted a flat non-reflective paint color, Shale Green from the BLM Standard Environmental Color Chart (CC-001: June 2008).

3. CONSTRUCTION REQUIREMENTS

3.1 CONSTRUCTION NOTIFICATION

The BLM shall administer compliance and monitor construction of the access road and well pad. Notify the Carlsbad Field Office at BLM_NM_CFO_Construction_Reclamation@blm.gov at least 3 working days prior to commencing construction of the access road and/or well pad.

When construction operations are being conducted on this well, the operator shall have the approved APD and COAs on the well site and they shall be made available upon request by the Authorized Officer.

3.2 TOPSOIL

The operator shall strip the topsoil (the A horizon) from the entire well pad area and stockpile the topsoil along the edge of the well pad as depicted in the APD. No more than the top 6 inches of topsoil shall be removed. All the stockpiled topsoil will be redistributed over the interim reclamation areas. Topsoil shall not be used for berming the pad or facilities. For final reclamation, the topsoil shall be spread over the entire pad area for seeding preparation.

Other subsoil (the B horizon and below) stockpiles must be completely segregated from the topsoil stockpile. Large rocks or subsoil clods (not evident in the surrounding terrain) must be buried within the approved area for interim and final reclamation.

3.3 CLOSED LOOP SYSTEM

Tanks are required for drilling operations: No reserve pits will be used for drill cuttings. The operator shall properly dispose of drilling contents at an authorized disposal site.

3.4 FEDERAL MINERAL PIT

Payment shall be made to the BLM prior to removal of any federal mineral materials. Call the Carlsbad Field Office at (575) 234-5972.

3.5 WELL PAD & SURFACING

Any surfacing material used to surface the well pad will be removed at the time of interim and final reclamation.

3.6 EXCLOSURE FENCING (CELLARS & PITS)

The operator will install and maintain enclosure fencing for all open well cellars to prevent access to public, livestock, and large forms of wildlife before and after drilling operations until the well cellar is free of fluids and the operator initiates backfilling. (For examples of enclosure fencing design, refer to BLM's Oil and Gas Gold Book, Exclosure Fence Illustrations, Figure 1, Page 18.)

The operator will also install and maintain mesh netting for all open well cellars to prevent access to smaller wildlife before and after drilling operations until the well cellar is free of fluids and the operator. Use a maximum netting mesh size of 1 ½ inches. The netting must not have holes or gaps.

4.1 BURIED PIPELINES

A copy of the application (APD, or Sundry Notice) and attachments, including conditions of approval, survey plat and/or map, will be on location during construction. BLM personnel may request a copy of your permit during construction to ensure compliance with all stipulations.

Operator agrees to comply with the following stipulations to the satisfaction of the Authorized Officer:

1. The Operator shall indemnify the United States against any liability for damage to life or property arising from the occupancy or use of public lands under this APD.
2. The Operator shall comply with all applicable Federal laws and regulations existing or hereafter enacted or promulgated. In any event, the operator shall comply with the Toxic Substances Control Act of 1976 as amended, 15 USC 2601 et seq. (1982) with regards to any toxic substances that are used, generated by or stored on the pipeline corridor or on facilities authorized under this APD. (See 40 CFR Part 702-799 and especially, provisions on polychlorinated biphenyls, 40 CFR 761.1 - 761.193.) Additionally, any release of toxic substances (leaks, spills, etc.) in excess of the reportable quantity established by 40 CFR Part 117 shall be reported as required by the Comprehensive Environmental Response, Compensation, and Liability Act, section 102b. A copy of any report required or requested by any Federal agency or State government as a result of a reportable release or spill of any toxic substances shall be furnished to the authorized officer concurrent with the filing of the reports to the involved Federal agency or State government.
3. The operator agrees to indemnify the United States against any liability arising from the release of any hazardous substance or hazardous waste (as these terms are defined in the Comprehensive Environmental Response, Compensation and Liability Act of 1980, 42 U.S.C. 9601, et seq. or the Resource Conservation and Recovery Act, 42 U.S.C. 6901, et seq.) on the Pipeline corridor (unless the release or threatened release is wholly unrelated to the operator's activity on the pipeline corridor), or resulting from the activity of the Operator on the pipeline corridor. This agreement applies without regard to whether a release is caused by the operator, its agent, or unrelated third parties.
4. If, during any phase of the construction, operation, maintenance, or termination of the pipeline, any oil or other pollutant is discharged from the pipeline system, impacting Federal lands, the control and total removal, disposal, and cleaning up of such oil or other pollutant, wherever found, shall be the responsibility of operator, regardless of fault. Upon failure of operator to control, dispose of, or clean up such discharge on or affecting Federal lands, or to repair all damages resulting therefrom, on the Federal lands, the Authorized Officer may take such measures as he deems necessary to control and clean up the discharge and restore the area, including where appropriate, the aquatic environment and fish and wildlife habitats, at the full expense of the operator. Such action by the Authorized Officer shall not relieve operator of any responsibility as provided herein.
5. All construction and maintenance activity will be confined to the authorized pipeline corridor.
6. The pipeline will be buried with a minimum cover of 36 inches between the top of the pipe and ground level.
7. The maximum allowable disturbance for construction in this pipeline corridor will be 30 feet:
 - Blading of vegetation within the pipeline corridor will be allowed: maximum width of blading operations will not exceed **20** feet. The trench is included in this area. (*Blading is defined as the complete removal of brush and ground vegetation.*)

- Clearing of brush species within the pipeline corridor will be allowed: maximum width of clearing operations will not exceed **30** feet. The trench and bladed area are included in this area. (*Clearing is defined as the removal of brush while leaving ground vegetation (grasses, weeds, etc.) intact. Clearing is best accomplished by holding the blade 4 to 6 inches above the ground surface.*)
 - The remaining area of the pipeline corridor (if any) shall only be disturbed by compressing the vegetation. (*Compressing can be caused by vehicle tires, placement of equipment, etc.*)
8. The operator shall stockpile an adequate amount of topsoil where blading is allowed. The topsoil to be stripped is approximately 6 inches in depth. The topsoil will be segregated from other spoil piles from trench construction. The topsoil will be evenly distributed over the bladed area for the preparation of seeding.
 9. Vegetation, soil, and rocks left as a result of construction or maintenance activity will be randomly scattered on this pipeline corridor and will not be left in rows, piles, or berms, unless otherwise approved by the Authorized Officer. The entire pipeline corridor shall be recontoured to match the surrounding landscape. The backfilled soil shall be compacted, and a 6-inch berm will be left over the ditch line to allow for settling back to grade.
 10. The pipeline will be identified by signs at the point of origin and completion of the pipeline corridor and at all road crossings. At a minimum, signs will state the operator's name, BLM serial number, and the product being transported. All signs and information thereon will be posted in a permanent, conspicuous manner, and will be maintained in a legible condition for the life of the pipeline.
 11. The operator shall not use the pipeline route as a road for purposes other than routine maintenance as determined necessary by the Authorized Officer in consultation with the operator before maintenance begins. The operator will take whatever steps are necessary to ensure that the pipeline route is not used as a roadway. As determined necessary during the life of the pipeline, the Authorized Officer may ask the operator to construct temporary deterrence structures.
 12. The operator shall be held responsible if noxious weeds become established within the areas of operations. Weed control shall be required on the disturbed land where noxious weeds exist, which includes associated roads, pipeline corridor and adjacent land affected by the establishment of weeds due to this action. The operator shall consult with the Authorized Officer for acceptable weed control methods, which include following EPA and BLM requirements and policies.
 13. Escape Ramps - The operator will construct and maintain pipeline/utility trenches [that are not otherwise fenced, screened, or netted] to prevent livestock, wildlife, and humans from becoming entrapped. At a minimum, the operator will construct and maintain escape ramps, ladders, or other methods of avian and terrestrial wildlife escape in the trenches according to the following criteria:
 - a. Any trench left open for eight (8) hours or less is not required to have escape ramps; however, before the trench is backfilled, the contractor/operator shall inspect the trench for wildlife, remove all trapped wildlife, and release them alive at least 100 yards from the trench.
 - b. For trenches left open for eight (8) hours or more, earthen escape ramps (built at no more than a 30-degree slope and spaced no more than 500 feet apart) shall be placed in the trench. Before the trench is backfilled, the contractor/operator shall inspect the trench for wildlife, remove all trapped wildlife, and release them alive at least 100 yards from the trench.

4.2 SURFACE PIPELINES

A copy of the APD and attachments, including stipulations, survey plat(s) and/or map(s), shall be on location during construction. BLM personnel may request to review a copy of your permit during construction to ensure compliance with all stipulations.

Operator agrees to comply with the following stipulations to the satisfaction of the Authorized Officer:

1. Operator shall indemnify the United States against any liability for damage to life or property arising from the occupancy or use of public lands under this APD.
2. Operator shall comply with all applicable Federal laws and regulations existing or hereafter enacted or promulgated. In any event, Operator shall comply with the Toxic Substances Control Act of 1976 as amended, 15 USC § 2601 et seq. (1982) with regard to any toxic substances that are used, generated by or stored on the pipeline corridor on facilities authorized under this APD (see 40 CFR, Part 702-799 and in particular, provisions on polychlorinated biphenyls, 40 CFR 761.1-761.193). Additionally, any release of toxic substances (leaks, spills, etc.) in excess of the reportable quantity established by 40 CFR, Part 117 shall be reported as required by the Comprehensive Environmental Response, Compensation, and Liability Act, section 102b. A copy of any report required or requested by any Federal agency or State government as a result of a reportable release or spill of any toxic substances shall be furnished to the Authorized Officer concurrent with the filing of the reports to the involved Federal agency or State government.
3. Operator agrees to indemnify the United States against any liability arising from the release of any hazardous substance or hazardous waste (as these terms are defined in the Comprehensive Environmental Response, Compensation and Liability Act of 1980, 42 U.S.C. § 9601, et seq. or the Resource Conservation and Recovery Act, 42 U.S.C. 6901, et seq.) on the Pipeline corridor (unless the release or threatened release is wholly unrelated to activity of the Operator's activity on the Pipeline corridor), or resulting from the activity of the Operator on the pipeline corridor. This provision applies without regard to whether a release is caused by Operator, its agent, or unrelated third parties.
4. Operator shall be liable for damage or injury to the United States to the extent provided by 43 CFR Sec. 2883.1-4. Operator shall be held to a standard of strict liability for damage or injury to the United States resulting from pipe rupture, fire, or spills caused or substantially aggravated by any of the following within the pipeline corridor or permit area:
 - a. Activities of Operator including, but not limited to: construction, operation, maintenance, and termination of the facility;
 - b. Activities of other parties including, but not limited to:
 - (1) Land clearing
 - (2) Earth-disturbing and earth-moving work
 - (3) Blasting
 - (4) Vandalism and sabotage
 - c. Acts of God.

The maximum limitation for such strict liability damages shall not exceed one million dollars (\$1,000,000) for any one event, and any liability in excess of such amount shall be determined by the ordinary rules of negligence of the jurisdiction in which the damage or injury occurred.

This section shall not impose strict liability for damage or injury resulting primarily from an act of war or from the negligent acts or omissions of the United States.

5. If, during any phase of the construction, operation, maintenance, or termination of the pipeline, any oil, salt water, or other pollutant is discharged from the pipeline system, impacting Federal lands, the control and total removal, disposal, and cleaning up of such oil, salt water, or other pollutant, wherever found, shall be the responsibility of Operator, regardless of fault. Upon failure of Operator to control, dispose of, or clean up such discharge on or affecting Federal lands, or to repair all damages resulting therefrom, on the Federal lands, the Authorized Officer may take such measures as they deem necessary to control and clean up the discharge and restore the area, including, where appropriate, the aquatic environment and fish and wildlife habitats, at the full expense of Operator. Such action by the Authorized Officer shall not relieve Operator of any responsibility as provided herein.

6. All construction and maintenance activity shall be confined to the authorized pipeline corridor width of 30-feet. If the pipeline route follows an existing road or buried pipeline corridor, the surface pipeline shall be installed no farther than 10 feet from the edge of the road or buried pipeline corridor. If existing surface pipelines prevent this distance, the proposed surface pipeline shall be installed immediately adjacent to the outer surface pipeline. All construction and maintenance activity shall be confined to existing roads or pipeline corridors.
7. No blading or clearing of any vegetation shall be allowed unless approved in writing by the Authorized Officer.
8. Operator shall install the pipeline on the surface in such a manner that will minimize suspension of the pipeline across low areas in the terrain. In hummocky or dune areas, the pipeline shall be "snaked" around hummocks and dunes rather than suspended across these features.
9. The pipeline shall be buried with a minimum of 6 inches under all roads, "two-tracks," and trails. Burial of the pipe will continue for 20 feet on each side of each crossing. The condition of the road, upon completion of construction, shall be returned to at least its former state with no bumps or dips remaining in the road surface.
10. The operator shall minimize disturbance to existing fences and other improvements on public lands. The operator is required to promptly repair improvements to at least their former state. Functional use of these improvements will be maintained at all times. The operator will contact the owner of any improvements prior to disturbing them. When necessary to pass through a fence line, the fence shall be braced on both sides of the passageway prior to cutting of the fence. No permanent gates will be allowed unless approved by the Authorized Officer.
11. In those areas where erosion control structures are required to stabilize soil conditions, the operator will install such structures as are suitable for the specific soil conditions being encountered and which are in accordance with sound resource management practices.
12. Excluding the pipe, all above-ground structures not subject to safety requirement shall be painted by the operator to blend with the natural color of the landscape. The paint used shall be a color which simulates "Standard Environmental Colors" – Shale Green, Munsell Soil Color No. 5Y 4/2; designated by the Rocky Mountain Five State Interagency Committee.
13. The pipeline will be identified by signs at the point of origin and completion of the pipeline corridor and at all road crossings. At a minimum, signs will state the operator's name, BLM serial number, and the product being transported. Signs will be maintained in a legible condition for the life of the pipeline.
14. The operator shall not use the pipeline route as a road for purposes other than routine maintenance as determined necessary by the Authorized Officer in consultation with the operator. The operator will take whatever steps are necessary to ensure that the pipeline route is not used as a roadway.
15. The operator shall be held responsible if noxious weeds become established within the areas of operations. Weed control shall be required on the disturbed land where noxious weeds exist, which includes the roads, powerline corridor, and adjacent land affected by the establishment of weeds due to this action. The operator shall consult with the Authorized Officer for acceptable weed control methods, which include following EPA and BLM requirements and policies.
16. Surface pipelines shall be less than or equal to 4 inches and a working pressure below 125 psi.

4.3 RANGELAND MITIGATION FOR PIPELINES

4.5.1 Fence Requirement

Where entry is granted across a fence line, the fence must be braced and tied off on both sides of the passageway with H-braces prior to cutting. Once the work is completed, the fence will be restored to its prior condition, or better. The operator shall notify the private surface landowner or the grazing allotment operator prior to crossing any fence(s).

4.5.2 Cattleguards

An appropriately sized cattleguard(s) sufficient to carry out the project shall be installed and maintained at road-fence crossing(s). Any existing cattleguard(s) on the access road shall be repaired or replaced if they are damaged or have deteriorated beyond practical use. The operator shall be responsible for the condition of the existing cattleguard(s) that are in place and are utilized during lease operations. A gate shall be constructed on one side of the cattleguard and fastened securely to H-braces.

4.5.3 Livestock Watering Requirement

Structures that provide water to livestock, such as windmills, pipelines, drinking troughs, and earthen reservoirs, will be avoided by moving the proposed action.

Any damage to structures that provide water to livestock throughout the life of the well, caused by operations from the well site, must be immediately corrected by the operator. The operator must notify the BLM office (575-234-5972) and the private surface landowner or the grazing allotment operator if any damage occurs to structures that provide water to livestock.

- Livestock operators will be contacted, and adequate crossing facilities will be provided as needed to ensure livestock are not prevented from reaching water sources because of the open trench.
- Wildlife and livestock trails will remain open and passable by adding soft plugs (areas where the trench is excavated and replaced with minimal compaction) during the construction phase. Soft plugs with ramps on either side will be left at all well-defined livestock and wildlife trails along the open trench to allow passage across the trench and provide a means of escape for livestock and wildlife that may enter the trench.
- Trenches will be backfilled as soon as feasible to minimize the amount of open trench. The Operator will avoid leaving trenches open overnight to the extent possible and open trenches that cannot be backfilled immediately will have escape ramps (wooden) placed at no more than 2,500 feet intervals and sloped no more than 45 degrees.

4. OVERHEAD ELECTRIC LINES

A copy of the APD and attachments, including stipulations, survey plat and/or map, will be on location during construction. BLM personnel may request to you a copy of your permit during construction to ensure compliance with all stipulations.

Operator agrees to comply with the following stipulations to the satisfaction of the Authorized Officer:

1. The operator shall indemnify the United States against any liability for damage to life or property arising from the occupancy or use of public lands under this APD.
2. The operator shall comply with all applicable Federal laws and regulations existing or hereafter enacted or promulgated. In any event, the operator shall comply with the Toxic Substances Control Act of 1976 as amended, 15 USC 2601 et seq. (1982) with regards to any toxic substances that are used, generated by or stored on the powerline corridor or on facilities authorized under this powerline corridor. (See 40 CFR, Part 702-799 and especially, provisions on polychlorinated biphenyls, 40 CFR 761.1-761.193.) Additionally, any release of toxic substances (leaks, spills, etc.) in excess of the reportable quantity established by 40 CFR, Part 117 shall be reported as required by the

Comprehensive Environmental Response, Compensation, and Liability Act, section 102b. A copy of any report required or requested by any Federal agency or State government as a result of a reportable release or spill of any toxic substances shall be furnished to the authorized officer concurrent with the filing of the reports to the involved Federal agency or State government.

3. The operator agrees to indemnify the United States against any liability arising from the release of any hazardous substance or hazardous waste (as these terms are defined in the Comprehensive Environmental Response, Compensation and Liability Act of 1980, 42 U.S.C. 9601, et seq. or the Resource Conservation and Recovery Act, 42 U.S.C. 6901, et seq.) on the Powerline corridor(unless the release or threatened release is wholly unrelated to the operator's activity on the powerline corridor), or resulting from the activity of the Operator on the powerline corridor. This agreement applies without regard to whether a release is caused by the operator, its agent, or unrelated third parties.
4. There will be no clearing or blading of the powerline corridor unless otherwise agreed to in writing by the Authorized Officer.
5. Power lines shall be constructed and designed in accordance to standards outlined in "Suggested Practices for Avian Protection on Power lines: The State of the Art in 2006" Edison Electric Institute, APLIC, and the California Energy Commission 2006 . The operator shall assume the burden and expense of proving that pole designs not shown in the above publication deter raptor perching, roosting, and nesting. Such proof shall be provided by a raptor expert approved by the Authorized Officer. The BLM reserves the right to require modification or additions to all powerline structures placed on this powerline corridor, should they be necessary to ensure the safety of large perching birds. Such modifications and/or additions shall be made by the operator without liability or expense to the United States.
6. Raptor deterrence will consist of but not limited to the following: triangle perch discouragers shall be placed on each side of the cross arms and a nonconductive perching deterrence shall be placed on all vertical poles that extend past the cross arms.
7. The operator shall minimize disturbance to existing fences and other improvements on public lands. The operator is required to promptly repair improvements to at least their former state. Functional use of these improvements will be maintained at all times. The operator will contact the owner of any improvements prior to disturbing them. When necessary to pass through a fence line, the fence shall be braced on both sides of the passageway prior to cutting the fence. No permanent gates will be allowed unless approved by the Authorized Officer.
8. The BLM serial number assigned to this authorization shall be posted in a permanent, conspicuous manner where the power line crosses roads and at all serviced facilities. Numbers will be at least two inches high and will be affixed to the pole nearest the road crossing and at the facilities served.
9. Upon cancellation, relinquishment, or expiration of this APD, the operator shall comply with those abandonment procedures as prescribed by the Authorized Officer.
10. All surface structures (poles, lines, transformers, etc.) shall be removed within 180 days of abandonment, relinquishment, or termination of use of the serviced facility or facilities or within 180 days of abandonment, relinquishment, cancellation, or expiration of this APD, whichever comes first. This will not apply where the power line extends service to an active, adjoining facility or facilities.
11. Special Stipulations:
 - For reclamation remove poles, lines, transformer, etc. and dispose of properly. Fill in any holes from the poles removed.

5. PRODUCTION (POST DRILLING)

5.1 WELL STRUCTURES & FACILITIES

5.1.1 Placement of Production Facilities

Production facilities must be placed on the well pad to allow for maximum interim recontouring and revegetation of the well location.

5.1.2 Exclosure Netting (Open-top Tanks)

Immediately following active drilling or completion operations, the operator will take actions necessary to prevent wildlife and livestock access, including avian wildlife, to all open-topped tanks that contain or have the potential to contain salinity sufficient to cause harm to wildlife or livestock, hydrocarbons, or Resource Conservation and Recovery Act of 1976-exempt hazardous substances. At a minimum, the operator will net, screen, or cover open-topped tanks to exclude wildlife and livestock and prevent mortality. If the operator uses netting, the operator will cover and secure the open portion of the tank to prevent wildlife entry. The operator will net, screen, or cover the tanks until the operator removes the tanks from the location or the tanks no longer contain substances that could be harmful to wildlife or livestock. Use a maximum netting mesh size of 1 ½ inches. The netting must not be in contact with fluids and must not have holes or gaps.

5.1.3. Chemical and Fuel Secondary Containment and Exclosure Screening

The operator will prevent all hazardous, poisonous, flammable, and toxic substances from coming into contact with soil and water. At a minimum, the operator will install and maintain an impervious secondary containment system for any tank or barrel containing hazardous, poisonous, flammable, or toxic substances sufficient to contain the contents of the tank or barrel and any drips, leaks, and anticipated precipitation. The operator will dispose of fluids within the containment system that do not meet applicable state or U. S. Environmental Protection Agency livestock water standards in accordance with state law; the operator must not drain the fluids to the soil or ground. The operator will design, construct, and maintain all secondary containment systems to prevent wildlife and livestock exposure to harmful substances. At a minimum, the operator will install effective wildlife and livestock exclosure systems such as fencing, netting, expanded metal mesh, lids, and grate covers. Use a maximum netting mesh size of 1 ½ inches.

5.1.4. Open-Vent Exhaust Stack Exclosures

The operator will construct, modify, equip, and maintain all open-vent exhaust stacks on production equipment to prevent birds and bats from entering, and to discourage perching, roosting, and nesting. (*Recommended exclosure structures on open-vent exhaust stacks are in the shape of a cone.*) Production equipment includes, but may not be limited to, tanks, heater-treaters, separators, dehydrators, flare stacks, in-line units, and compressor mufflers.

5.1.5. Containment Structures

Proposed production facilities such as storage tanks and other vessels will have a secondary containment structure that is constructed to hold the capacity of 1.5 times the largest tank, plus freeboard to account for precipitation, unless more stringent protective requirements are deemed necessary.

6. RECLAMATION

Stipulations required by the Authorized Officer on specific actions may differ from the following general guidelines

6.1 ROAD AND SITE RECLAMATION

Any roads constructed during the life of the well will have the caliche removed or linear burial. If contaminants are indicated then testing will be required for chlorides and applicable contaminate anomalies for final disposal determination (disposed of in a manner approved by the Authorized Officer within Federal, State and Local statutes, regulations, and ordinances) and seeded to the specifications in sections 6.5 and 6.6.

6.2 EROSION CONTROL

Install erosion control berms, windrows, and hummocks. Windrows must be level and constructed perpendicular to down-slope drainage; steeper slopes will require greater windrow density. Topsoil between windrows must be ripped to a depth of at least 12", unless bedrock is encountered. Any large boulders pulled up during ripping must be deep-buried on location. Ripping must be perpendicular to down-slope. The surface must be left rough in order to catch and contain rainfall on-site. Any trenches resulting from erosion cause by run-off shall be addressed immediately.

6.3 INTERIM RECLAMATION

During the life of the development, all disturbed areas not needed for active support of production operations must undergo interim reclamation in order to minimize the environmental impacts of development on other resources and uses.

Within six (6) months of well completion, operators must work with BLM surface protection specialists (BLM_NM_CFO_Construction_Reclamation@blm.gov) to devise the best strategies to reduce the size of the location. Interim reclamation must allow for remedial well operations, as well as safe and efficient removal of oil and gas.

During reclamation, the removal of caliche and any other surface material is required. Removed caliche that is free of contaminants may be used for road repairs, fire walls or for building other roads and locations. In order to operate the well or complete workover operations, it may be necessary to drive, park and operate on restored interim vegetation within the previously disturbed area. Disturbing revegetated areas for production or workover operations will be allowed. If there is significant disturbance and loss of vegetation, the area will need to be revegetated. Communicate with the appropriate BLM office for any exceptions/exemptions if needed.

All disturbed areas after they have been satisfactorily prepared need to be reseeded with the seed mixture provided in section 6.6.

Upon completion of interim reclamation, the operator shall submit a Sundry Notice, Subsequent Report of Reclamation (Form 3160-5).

6.4 FINAL ABANDONMENT & RECLAMATION

Prior to surface abandonment, the operator shall submit a Notice of Intent Sundry Notice and reclamation plan.

At final abandonment, well locations, production facilities, and access roads must undergo "final" reclamation so that the character and productivity of the land are restored.

Earthwork for final reclamation must be completed within six (6) months of well plugging. All pads, pits, facility locations and roads must be reclaimed to a satisfactory revegetated, safe, and stable condition, unless an agreement is made with the landowner or BLM to keep the road and/or pad intact.

After all disturbed areas have been satisfactorily prepared, these areas need to be revegetated with the seed mixture provided below. Seeding will be accomplished by drilling on the contour whenever practical or by other approved methods. Seeding may need to be repeated until revegetation is successful, as determined by the BLM. After earthwork and seeding is completed, the operator is required to submit a Sundry Notice, Subsequent Report of Reclamation.

Operators shall contact a BLM surface protection specialist prior to surface abandonment operations for site specific objectives (BLM_NM_CFO_Construction_Reclamation@blm.gov).

6.5 SEEDING TECHNIQUES

Seeds shall be hydro-seeded, mechanically drilled, or broadcast, with the broadcast-seeded area raked, ripped or dragged to aid in covering the seed. The seed mixture shall be evenly and uniformly planted over the disturbed area.

6.6 SOIL SPECIFIC SEED MIXTURE

The lessee/permittee shall seed all disturbed areas with the seed mixture listed below. The seed mixture shall be planted in the amounts specified in pounds of pure live seed (PLS)* per acre. There shall be no primary or secondary noxious weeds in the seed mixture. Seed will be tested and the viability testing of seed will be done in accordance with State law(s) and within nine (9) months prior to purchase. Commercial seed will be either certified or registered seed. The seed container will be tagged in accordance with State law(s) and available for inspection by the Authorized Officer.

Seed land application will be accomplished by mechanical planting using a drill equipped with a depth regulator to ensure proper depth of planting where drilling is possible. The seed mixture will be evenly and uniformly planted over the disturbed area. Smaller/heavier seeds tend to drop the bottom of the drill and are planted first; the operator shall take appropriate measures to ensure this does not occur. Where drilling is not possible, seed will be broadcast and the area shall be raked or chained to cover the seed. When broadcasting the seed, the pounds per acre are to be doubled. The seeding will be repeated until a satisfactory BLM or Soil Conservation

District stand is established as determined by the Authorized Officer. Evaluation of growth will not be made before completion of at least one full growing season after seeding or until several months of precipitation

Seed Mixture 2, for Sandy Site

Species to be planted in pounds of pure live seed* per acre:

<u>Species</u>	<u>lb/acre</u>
Sand dropseed (Sporobolus cryptandrus)	1.0
Sand love grass (Eragrostis trichodes)	1.0
Plains bristlegrass (Setaria macrostachya)	2.0

*Pounds of pure live seed:

Pounds of seed x percent purity x percent germination = pounds pure live seed

PECOS DISTRICT DRILLING CONDITIONS OF APPROVAL

OPERATOR'S NAME:	XTO
LEASE NO.:	NMLC064894A
LOCATION:	Sec. 20, T.25 S, R 30 E
COUNTY:	Eddy County, New Mexico ▼
WELL NAME & NO.:	Poker Lake Unit 20-8 BD 208H
SURFACE HOLE FOOTAGE:	1831'S & 1544'E
BOTTOM HOLE FOOTAGE:	2652'S & 1248'E

COA

H ₂ S	☐ No ☒ Yes			
Potash / WIPP	☒ None	☐ Secretary	☐ R-111-Q	☐ Open Annulus ☐ WIPP
	Choose an option (including blank option.)			
Cave / Karst	☒ Low	☐ Medium	☐ High	☐ Critical
Wellhead	☐ Conventional	☒ Multibowl	☐ Both	☐ Diverter
Cementing	☒ Primary Squeeze	☐ Cont. Squeeze	☒ EchoMeter	☐ DV Tool
Special Req	☐ Capitan Reef	☐ Water Disposal	☐ COM	☒ Unit
Waste Prev.	☐ Self-Certification	☒ Waste Min. Plan	☐ APD Submitted prior to 06/10/2024	
Additional Language	☒ Flex Hose	☒ Casing Clearance	☐ Pilot Hole	☒ Break Testing
	☐ Four-String	☒ Offline Cementing	☐ Fluid-Filled	

A. HYDROGEN SULFIDE

A Hydrogen Sulfide (H₂S) Drilling Plan shall be activated 500 feet prior to drilling into the **Delaware** formation. As a result, the Hydrogen Sulfide area must meet all requirements from 43 CFR 3176, which includes equipment and personnel/public protection items. If Hydrogen Sulfide is encountered, please provide measured values and formations to the BLM.

B. CASING

1. The **9-5/8** inch surface casing shall be set at approximately **1150** feet (a minimum of **70 feet** **(Eddy County)** into the Rustler Anhydrite, above the salt, and below usable fresh water) and cemented to the surface.
 - a. If cement does not circulate to the surface, the appropriate BLM office shall be notified and a temperature survey utilizing an electronic type temperature survey with surface log readout will be used or a cement bond log shall be run to verify the top of the cement. Temperature survey will be run a minimum of six hours after pumping cement and ideally between 8-10 hours after completing the cement job.
 - b. Wait on cement (WOC) time for a primary cement job will be a minimum of **8 hours** or **500 pounds compressive strength**, whichever is greater. (This is to include the

- lead cement)
- c. Wait on cement (WOC) time for a remedial job will be a minimum of 4 hours after bringing cement to surface or 500 pounds compressive strength, whichever is greater.
 - d. If cement falls back, remedial cementing will be done prior to drilling out that string.
2. The minimum required fill of cement behind the **7-5/8** inch intermediate casing is:
Operator has proposed to cement in two stages by conventionally cementing the first stage and performing a bradenhead squeeze on the second stage, contingent upon no returns to surface.
- a. **First stage:** Operator will cement with intent to reach the top of the **Brushy Canyon at 6196'**.
 - b. **Second stage:** Operator will perform bradenhead squeeze and top-out. Cement to surface. If cement does not reach surface, the appropriate BLM office shall be notified. **Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry due to cave/karst.**

Operator has proposed to pump down **Surface X Intermediate 1** annulus after primary cementing stage. Operator must run Echo-meter to verify Cement Slurry/Fluid top in the annulus OR operator shall run a CBL from TD of the Surface casing to tieback requirements listed above after the second stage BH to verify TOC. Submit results to the BLM. No displacement fluid/wash out shall be utilized at the top of the cement slurry between second stage BH and top out. Operator must use a limited flush fluid volume of 1 bbl following backside cementing procedures.

If cement does not reach surface, the next casing string must come to surface.

3. The minimum required fill of cement behind the **5-1/2** inch production casing is:
- Cement should tie-back at least **200 feet** into previous casing string. Operator shall provide method of verification.

C. PRESSURE CONTROL

1. Variance approved to use flex line from BOP to choke manifold. Manufacturer's specification to be readily available. No external damage to flex line. Flex line to be installed as straight as possible (no hard bends).
2. Operator has proposed a multi-bowl wellhead assembly. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **5000 (5M)** psi.
 - a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
 - b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
 - c. Manufacturer representative shall install the test plug for the initial BOP test.
 - d. If the cement does not circulate and one-inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
 - e. Whenever any seal subject to test pressure is broken, all the tests in 43 CFR 3172 must be followed.

D. SPECIAL REQUIREMENT (S)

Unit Wells

The well sign for a unit well shall include the unit number in addition to the surface and bottom hole lease numbers. This also applies to participating area numbers. If a participating area has not been established, the operator can use the general unit designation but will replace the unit number with the participating area number when the sign is replaced.

Commercial Well Determination

A commercial well determination shall be submitted after production has been established for at least six months. **(This is not necessary for secondary recovery unit wells)**

BOPE Break Testing Variance

- BOPE Break Testing is ONLY permitted for intervals utilizing a 5M BOPE or less. **(Annular preventer must be tested to a minimum of 70% of BOPE working pressure and shall be higher than the MASP.)**
- BOPE Break Testing is NOT permitted to drilling the production hole section.
- Variance only pertains to the intermediate hole-sections and no deeper than the Bone Springs formation.
- While in transfer between wells, the BOPE shall be secured by the hydraulic carrier or cradle.
- Any well control event while drilling require notification to the BLM Petroleum Engineer **(575-706-2779)** prior to the commencement of any BOPE Break Testing operations.
- A full BOPE test is required prior to drilling the first deep intermediate hole section. If any subsequent hole interval is deeper than the first, a full BOPE test will be required. (200' TVD tolerance between intermediate shoes is allowable).
- The BLM is to be contacted **(575-361-2822 Eddy County)** 4 hours prior to BOPE tests.
- As a minimum, a full BOPE test shall be performed at 21-day intervals.
- In the event any repairs or replacement of the BOPE is required, the BOPE shall test as per **43 CFR 3172**.
- If in the event break testing is not utilized, then a full BOPE test would be conducted.

Offline Cementing

Contact the BLM prior to the commencement of any offline cementing procedure.

Engineer may elect to vary this language. Speak with Chris about implementing changes and whether that change seems reasonable.

Casing Clearance

String does not meet 0.422" clearance requirement per 43 CFR 3172. Cement tieback requirement increased 100' for Production casing tieback. Operator may contact approving engineer to discuss changing casing set depth or grade to meet clearance requirement.

GENERAL REQUIREMENTS

The BLM is to be notified in advance for a representative to witness:

- a. Spudding well (minimum of 24 hours)
- b. Setting and/or Cementing of all casing strings (minimum of 4 hours)
- c. BOPE tests (minimum of 4 hours)

Contact Eddy County Petroleum Engineering Inspection Staff:

Email or call the Carlsbad Field Office, 620 East Greene St., Carlsbad, NM 88220;

[BLM NM CFO DrillingNotifications@BLM.GOV](mailto:BLM_NM_CFO_DrillingNotifications@BLM.GOV); (575) 361-2822

1. Unless the production casing has been run and cemented or the well has been properly plugged, the drilling rig shall not be removed from over the hole without prior approval.
 - a. In the event the operator has proposed to drill multiple wells utilizing a skid/walking rig. Operator shall secure the wellbore on the current well, after installing and testing the wellhead, by installing a blind flange of like pressure rating to the wellhead and a pressure gauge that can be monitored while drilling is performed on the other well(s).
 - b. When the operator proposes to set surface casing with Spudder Rig
 - i. Notify the BLM when moving in and removing the Spudder Rig.
 - ii. Notify the BLM when moving in the 2nd Rig. Rig to be moved in within 90 days of notification that Spudder Rig has left the location.
 - iii. BOP/BOPE test to be conducted per **43 CFR 3172** as soon as 2nd Rig is rigged up on well.
2. Floor controls are required for 3M or Greater systems. These controls will be on the rig floor, unobstructed, readily accessible to the driller and will be operational at all times during drilling and/or completion activities. Rig floor is defined as the area immediately around the rotary table; the area immediately above the substructure on which the draw works are located, this does not include the dog house or stairway area.
3. For intervals in which cement to surface is required, cement to surface should be verified with a visual check and density or pH check to differentiate cement from spacer and drilling mud. The results should be documented in the driller's log and daily reports.

A. CASING

1. Changes to the approved APD casing program need prior approval if the items substituted are of lesser grade or different casing size or are Non-API. The Operator can exchange the components of the proposal with that of superior strength (i.e. changing from J-55 to N-80, or from 36# to 40#). Changes to the approved cement program need prior approval if the altered cement plan has less volume or strength or if the changes are substantial (i.e. Multistage tool, ECP, etc.). The initial wellhead installed on the well will remain on the well with spools used as needed.

2. Wait on cement (WOC) for Potash Areas: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi for all cement blends of both lead and tail cement, 2) until cement has been in place at least 8 hours. WOC time will be recorded in the driller's log. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
3. Wait on cement (WOC) for Water Basin: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi at the shoe, 2) until cement has been in place at least 8 hours. WOC time will be recorded in the driller's log. See individual casing strings for details regarding lead cement slurry requirements. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
4. Provide compressive strengths including hours to reach required 500 pounds compressive strength prior to cementing each casing string. Have well specific cement details onsite prior to pumping the cement for each casing string.
5. No pea gravel permitted for remedial or fall back remedial without prior authorization from the BLM engineer.
6. On that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Formation at the shoe shall be tested to a minimum of the mud weight equivalent anticipated to control the formation pressure to the next casing depth or at total depth of the well. This test shall be performed before drilling more than 20 feet of new hole.
7. If hardband drill pipe is rotated inside casing, returns will be monitored for metal. If metal is found in samples, drill pipe will be pulled and rubber protectors which have a larger diameter than the tool joints of the drill pipe will be installed prior to continuing drilling operations.
8. Whenever a casing string is cemented in the R-111-Q potash area, the NMOCD requirements shall be followed.

B. PRESSURE CONTROL

1. All blowout preventer (BOP) and related equipment (BOPE) shall comply with well control requirements as described in **43 CFR 3172**.
2. If a variance is approved for a flexible hose to be installed from the BOP to the choke manifold, the following requirements apply: The flex line must meet the requirements of API 16C. Check condition of flexible line from BOP to choke manifold, replace if exterior is damaged or if line fails test. Line to be as straight as possible with no hard bends and is to be anchored according to Manufacturer's

requirements. The flexible hose can be exchanged with a hose of equal size and equal or greater pressure rating. Anchor requirements, specification sheet and hydrostatic pressure test certification matching the hose in service, to be onsite for review. These documents shall be posted in the company man's trailer and on the rig floor.

3. 5M or higher system requires an HCR valve, remote kill line and annular to match. The remote kill line is to be installed prior to testing the system and tested to stack pressure.
4. If the operator has proposed a multi-bowl wellhead assembly in the APD. The following requirements must be met:
 - i. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
 - ii. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
 - iii. Manufacturer representative shall install the test plug for the initial BOP test.
 - iv. Whenever any seal subject to test pressure is broken, all the tests in 43 CFR 3172.6(b)(9) must be followed.
 - v. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
5. The appropriate BLM office shall be notified a minimum of 4 hours in advance for a representative to witness the tests.
 - i. In a water basin, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. The casing cut-off and BOP installation can be initiated four hours after installing the slips, which will be approximately six hours after bumping the plug. For those casing strings not using slips, the minimum wait time before cut-off is eight hours after bumping the plug. BOP/BOPE testing can begin after cut-off or once cement reaches 500 psi compressive strength (including lead cement), whichever is greater. However, if the float does not hold, cut-off cannot be initiated until cement reaches 500 psi compressive strength (including lead when specified).
 - ii. In potash areas, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. For all casing strings, casing cut-off and BOP installation can be initiated at twelve hours after bumping the cement plug. The BOPE test can be initiated after bumping the cement plug with the casing valve

- open. (only applies to single stage cement jobs, prior to the cement setting up.)
- iii. The tests shall be done by an independent service company utilizing a test plug not a cup or J-packer and can be initiated immediately with the casing valve open. The operator also has the option of utilizing an independent tester to test without a plug (i.e. against the casing) pursuant to **43 CFR 3172** with the pressure not to exceed 70% of the burst rating for the casing. Any test against the casing must meet the WOC time for 8 hours or 500 pounds compressive strength, whichever is greater, prior to initiating the test (see casing segment as lead cement may be critical item).
 - iv. The test shall be run on a 5000 psi chart for a 2-3M BOP/BOP, on a 10000 psi chart for a 5M BOP/BOPE and on a 15000 psi chart for a 10M BOP/BOPE. If a linear chart is used, it shall be a one hour chart. A circular chart shall have a maximum 2 hour clock. If a twelve hour or twenty-four hour chart is used, tester shall make a notation that it is run with a two hour clock.
 - v. The results of the test shall be reported to the appropriate BLM office.
 - vi. All tests are required to be recorded on a calibrated test chart. A copy of the BOP/BOPE test chart and a copy of independent service company test will be submitted to the appropriate BLM office.
 - vii. The BOP/BOPE test shall include a low pressure test from 250 to 300 psi. The test will be held for a minimum of 10 minutes if test is done with a test plug and 30 minutes without a test plug. This test shall be performed prior to the test at full stack pressure.
 - viii. BOP/BOPE must be tested by an independent service company within 500 feet of the top of the Wolfcamp formation if the time between the setting of the intermediate casing and reaching this depth exceeds 20 days. This test does not exclude the test prior to drilling out the casing shoe as per **43 CFR 3172**.

C. DRILLING MUD

Mud system monitoring equipment, with derrick floor indicators and visual and audio alarms, shall be operating before drilling into the Wolfcamp formation, and shall be used until production casing is run and cemented.

D. WASTE MATERIAL AND FLUIDS

All waste (i.e. drilling fluids, trash, salts, chemicals, sewage, gray water, etc.) created as a result of drilling operations and completion operations shall be safely contained and disposed of properly at a waste disposal facility. No waste material or fluid shall be

disposed of on the well location or surrounding area. Porto-johns and trash containers will be on-location during fracturing operations or any other crew-intensive operations.

Approved by Zota Stevens on 4/9/2025
575-234-5998 / zstevens@blm.gov

Operator

I hereby certify that I, or someone under my direct supervision, have inspected the drill site and access route proposed herein; that I am familiar with the conditions which currently exist; that I have full knowledge of state and Federal laws applicable to this operation; that the statements made in this APD package are, to the best of my knowledge, true and correct; and that the work associated with the operations proposed herein will be performed in conformity with this APD package and the terms and conditions under which it is approved. I also certify that I, or the company I represent, am responsible for the operations conducted under this application. These statements are subject to the provisions of 18 U.S.C. 1001 for the filing of false statements.

NAME: SIVAPRAKASH SELVAM

Signed on: 09/23/2024

Title: Regulatory Clerk

Street Address: 22777 SPRINGWOODS VILLAGE PARKWAY

City: SPRING

State: TX

Zip: 77389

Phone: (720)539-1673

Email address: SIVAPRAKASH.SELVAM1@EXXONMOBIL.COM

Field

Representative Name:

Street Address:

City:

State:

Zip:

Phone:

Email address:

APD ID: 10400100957

Submission Date: 09/23/2024

Operator Name: XTO PERMIAN OPERATING LLC

Well Name: POKER LAKE UNIT 20-8 BD

Well Number: 208H

Well Type: OIL WELL

Well Work Type: Drill

Highlighted data
reflects the most
recent changes
[Show Final Text](#)

Section 1 - General

APD ID: 10400100957

Tie to previous NOS? N

Submission Date: 09/23/2024

BLM Office: Carlsbad

User: SIVAPRAKASH SELVAM

Title: Regulatory Clerk

Federal/Indian APD: FED

Is the first lease penetrated for production Federal or Indian? FED

Lease number: NMLC064894A

Lease Acres:

Surface access agreement in place?

Allotted?

Reservation:

Agreement in place? YES

Federal or Indian agreement: FEDERAL

Agreement number: NMNM71016X

Agreement name: POKER LAKE UNIT

Keep application confidential? Y

Permitting Agent? NO

APD Operator: XTO PERMIAN OPERATING LLC

Operator letter of

Operator Info

Operator Organization Name: XTO PERMIAN OPERATING LLC

Operator Address: 6401 HOLIDAY HILL ROAD BLDG 5

Zip: 79707

Operator PO Box:

Operator City: MIDLAND

State: TX

Operator Phone: (432)683-2277

Operator Internet Address:

Section 2 - Well Information

Well in Master Development Plan? NO

Master Development Plan name:

Well in Master SUPO? NO

Master SUPO name:

Well in Master Drilling Plan? NO

Master Drilling Plan name:

Well Name: POKER LAKE UNIT 20-8 BD

Well Number: 208H

Well API Number:

Field/Pool or Exploratory? Field and Pool

Field Name: CORRAL CANYON Pool Name: BONE SPRING

Well Name: POKER LAKE UNIT 20-8 BD

Well Number: 208H

Is the proposed well in an area containing other mineral resources? USEABLE WATER,NATURAL GAS,OIL

Is the proposed well in a Helium production area? N Use Existing Well Pad? N New surface disturbance?

Type of Well Pad: MULTIPLE WELL

Multiple Well Pad Name:
POKER LAKE UNIT 20-8 BD
Number of Legs: 1

Number: D

Well Class: HORIZONTAL

Well Work Type: Drill

Well Type: OIL WELL

Describe Well Type:

Well sub-Type: EVALUATION

Describe sub-type:

Distance to town:

Distance to nearest well: 30 FT

Distance to lease line: 1544 FT

Reservoir well spacing assigned acres Measurement: 400 Acres

Well plat: 2024060280_XTO_POKER_LAKE_UNIT_20_8_BD_208H_C_102_FINAL_7_12_2024___UPDATED_FOR
M_9_13_2024_15_09_2024___14_50_20240923145344.pdf

Well work start Date: 10/22/2025

Duration: 45 DAYS

Section 3 - Well Location Table

Survey Type: RECTANGULAR

Describe Survey Type:

Datum: NAD83

Vertical Datum: NAVD88

Survey number:

Reference Datum: GROUND LEVEL

Wellbore	NS-Foot	NS Indicator	EW-Foot	EW Indicator	Twsp	Range	Section	Aliquot/Lot/Tract	Latitude	Longitude	County	State	Meridian	Lease Type	Lease Number	Elevation	MD	TVD	Will this well produce from this
SHL Leg #1	1813	FSL	1544	FEL	25S	30E	20	Aliquot NWSE	32.113303	-103.899786	EDD Y	NEW MEXI CO	NEW MEXI CO	F	NMLC0 64894A	3198			Y
KOP Leg #1	1813	FSL	1544	FEL	25S	30E	20	Aliquot NWSE	32.113303	-103.899786	EDD Y	NEW MEXI CO	NEW MEXI CO	F	NMLC0 64894A	-5596	9418	8794	Y
PPP Leg #1-1	100	FSL	1244	FEL	25S	30E	20	Aliquot SESE	32.108599	-103.898826	EDD Y	NEW MEXI CO	NEW MEXI CO	F	NMLC0 64894A	-6312	10600	9510	Y

Well Name: POKER LAKE UNIT 20-8 BD

Well Number: 208H

Wellbore	NS-Foot	NS Indicator	EW-Foot	EW Indicator	Twsp	Range	Section	Aliquot/Lot/Tract	Latitude	Longitude	County	State	Meridian	Lease Type	Lease Number	Elevation	MD	TVD	Will this well produce from this
EXIT Leg #1	256 2	FSL	124 8	FEL	25S	30E	8	Aliquot NESE	32.14461 8	- 103.8988 5	EDD Y	NEW MEXI CO	NEW MEXI CO	S	STATE	- 631 2	236 46	951 0	Y
BHL Leg #1	265 2	FSL	124 8	FEL	25S	30E	8	Aliquot NESE	32.14486 6	- 103.8988 5	EDD Y	NEW MEXI CO	NEW MEXI CO	S	STATE	- 631 2	237 36	951 0	Y

WELL LOCATION INFORMATION

API Number 30-015 -56759	Pool Code 13354	Pool Name Corral Canyon; Bone Spring, South
Property Code 333644	Property Name POKER LAKE UNIT 20-8 BD	Well Number 208H
ORGID No. 373075	Operator Name XTO PERMIAN OPERATING, LLC.	Ground Level Elevation 3,198'
Surface Owner: ☐ State ☐ Fee ☐ Tribal ☐ Federal		Mineral Owner: ☐ State ☐ Fee ☐ Tribal ☐ Federal

Surface Location

UL J	Section 20	Township 25 S	Range 30 E	Lot	Ft. from N/S 1,813' FSL	Ft. from E/W 1,544' FEL	Latitude 32.113303	Longitude -103.899786	County EDDY
---------	---------------	------------------	---------------	-----	----------------------------	----------------------------	-----------------------	--------------------------	----------------

Bottom Hole Location

UL I	Section 8	Township 25 S	Range 30 E	Lot	Ft. from N/S 2,652' FSL	Ft. from E/W 1,248' FEL	Latitude 32.144866	Longitude -103.898850	County EDDY
---------	--------------	------------------	---------------	-----	----------------------------	----------------------------	-----------------------	--------------------------	----------------

Dedicated Acres 400	Infill or Defining Well	Defining Well API	Overlapping Spacing Unit (Y/N)	Consolidation Code
Order Numbers.			Well setbacks are under Common Ownership: ☐ Yes ☐ No	

Kick Off Point (KOP)

UL J	Section 20	Township 25 S	Range 30 E	Lot	Ft. from N/S 1,813' FSL	Ft. from E/W 1,544' FEL	Latitude 32.113303	Longitude -103.899786	County EDDY
---------	---------------	------------------	---------------	-----	----------------------------	----------------------------	-----------------------	--------------------------	----------------

First Take Point (FTP)

UL P	Section 20	Township 25 S	Range 30 E	Lot	Ft. from N/S 100' FSL	Ft. from E/W 1,244' FEL	Latitude 32.108599	Longitude -103.898826	County EDDY
---------	---------------	------------------	---------------	-----	--------------------------	----------------------------	-----------------------	--------------------------	----------------

Last Take Point (LTP)

UL I	Section 8	Township 25 S	Range 30 E	Lot	Ft. from N/S 2,562' FSL	Ft. from E/W 1,248' FEL	Latitude 32.144618	Longitude -103.898850	County EDDY
---------	--------------	------------------	---------------	-----	----------------------------	----------------------------	-----------------------	--------------------------	----------------

Unitized Area or Area of Uniform Interest	Spacing Unit Type ☐ Horizontal ☐ Vertical	Ground Floor Elevation: 3,198'
---	---	--------------------------------

OPERATOR CERTIFICATIONS

I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief, and that this organization either owns a working interest or unleased mineral interest in the land including the proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of such a mineral or working interest, or to a voluntary pooling agreement or a compulsory pooling order heretofore entered by the division.

If this well is a horizontal well, I further certify that this organization has received the consent of at least one lessee or owner of a working interest or unleased mineral interest in each tract (in the target pool or formation) in which any part of the well's completed interval will be located or obtained a compulsory pooling form the division.

Signature Date

Printed Name

Email Address


SURVEYOR CERTIFICATIONS

I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief.

I, TIM C. PAPPAS, NEW MEXICO PROFESSIONAL SURVEYOR NO. 21209, DO HEREBY CERTIFY THAT THIS SURVEY PLAT AND THE ACTUAL SURVEY ON THE GROUND UPON WHICH IT IS BASED WERE PERFORMED BY ME OR UNDER MY DIRECT SUPERVISION; THAT I AM RESPONSIBLE FOR THIS SURVEY, THAT THIS SURVEY MEETS THE MINIMUM STANDARDS FOR SURVEYING IN NEW MEXICO, AND THAT IS TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF.

13 Sept 2024

TIM C. PAPPAS
REGISTERED PROFESSIONAL LAND SURVEYOR
STATE OF NEW MEXICO NO. 21209



Signature and Seal of Professional Surveyor

Certificate Number

TIM C. PAPPAS 21209

Date of Survey

7/12/2024

Note: No allowable will be assigned to this completion until all interests have been consolidated or a non-standard unit has been approved by the division.

<u>LINE TABLE</u>		
LINE	AZIMUTH	LENGTH
L1	169 54'56"	1,736.71'
L2	359 44'12"	13,193.13'



<u>CORNER COORDINATES (NAD83 NME)</u>					
A - Y =	403,430.7	N	A - X =	677,115.2	E
B - Y =	406,090.7	N	B - X =	677,109.2	E
C - Y =	408,752.3	N	C - X =	677,103.0	E
D - Y =	411,413.4	N	D - X =	677,081.7	E
E - Y =	414,076.3	N	E - X =	677,059.0	E
F - Y =	416,739.9	N	F - X =	677,058.4	E
G - Y =	403,414.8	N	G - X =	675,779.8	E
H - Y =	406,074.3	N	H - X =	675,772.5	E
I - Y =	408,734.6	N	I - X =	675,765.0	E
J - Y =	411,394.4	N	J - X =	675,744.5	E
K - Y =	414,055.5	N	K - X =	675,723.4	E
L - Y =	416,717.4	N	L - X =	675,720.8	E
<u>CORNER COORDINATES (NAD27 NME)</u>					
A - Y =	403,372.4	N	A - X =	635,930.2	E
B - Y =	406,032.3	N	B - X =	635,924.3	E
C - Y =	408,693.8	N	C - X =	635,918.2	E
D - Y =	411,354.9	N	D - X =	635,897.0	E
E - Y =	414,017.7	N	E - X =	635,874.4	E
F - Y =	416,681.2	N	F - X =	635,873.9	E
G - Y =	403,356.5	N	G - X =	634,594.9	E
H - Y =	406,015.9	N	H - X =	634,587.6	E
I - Y =	408,676.1	N	I - X =	634,580.2	E
J - Y =	411,335.9	N	J - X =	634,559.9	E
K - Y =	413,996.9	N	K - X =	634,538.8	E
L - Y =	416,658.7	N	L - X =	634,536.3	E

APD ID: 10400100957

Submission Date: 09/23/2024

Highlighted data
reflects the most
recent changes

Operator Name: XTO PERMIAN OPERATING LLC

Well Name: POKER LAKE UNIT 20-8 BD

Well Number: 208H

Well Type: OIL WELL

Well Work Type: Drill

[Show Final Text](#)

Section 1 - Geologic Formations

Formation ID	Formation Name	Elevation	True Vertical	Measured Depth	Lithologies	Mineral Resources	Producing Formatio
15611120	QUATERNARY	3198	0	0	ALLUVIUM	USEABLE WATER	N
15611121	RUSTLER	2322	876	876	ANHYDRITE, SANDSTONE	USEABLE WATER	N
15611122	SALADO	2181	1017	1017	SALT	NONE	N
15611123	BASE OF SALT	-284	3482	3482	SALT	NONE	N
15611124	DELAWARE	-481	3679	3679	LIMESTONE, SANDSTONE	NATURAL GAS, OIL, OTHER : Produced Water	N
15611125	BRUSHY CANYON	-2998	6196	6196	SANDSTONE	NATURAL GAS, OIL, OTHER : Produced Water	N
15611126	BONE SPRING	-4307	7505	7505	LIMESTONE, SANDSTONE	NATURAL GAS, OIL, OTHER : Produced Water	Y
15611131	BONE SPRING 1ST	-5040	8238	8238	LIMESTONE, SANDSTONE	NATURAL GAS, OIL, OTHER : Produced Water	Y
15611127	BONE SPRING 2ND	-5519	8717	8717	LIMESTONE, SANDSTONE	NATURAL GAS, OIL, OTHER : Produced Water	Y
15611130	BONE SPRING 2ND	-6223	9421	9421	LIMESTONE, SANDSTONE	NATURAL GAS, OIL, OTHER : Produced Water	Y

Section 2 - Blowout Prevention

Pressure Rating (PSI): 5M

Rating Depth: 9510

Equipment: Once the permanent WH is installed on the surface casing, the BOP equipment will have a 5M Hydril Annular & a 10M Triple Ram BOP. XTO will use a Multi-Bowl System which is attached

Requesting Variance? YES

Variance request: XTO requests a variance to allow the use of a flex hose. See attached. XTO requests a variance to be able to batch drill this well if necessary. XTO requests a variance to utilize a spudder rig. See attached. XTO requests a break test variance. See attached.

Testing Procedure: All BOP testing will be done by an independent service company. Operator will test as per 43 CFR 3172.

Choke Diagram Attachment:

Poker_Lake_Unit_20_17__20_8_BD__10MCM_20250319084445.pdf

Well Name: POKER LAKE UNIT 20-8 BD

Well Number: 208H

Poker_Lake_Unit_20_17___20_8_BD__10MCM_20250319084445.pdf

BOP Diagram Attachment:

Poker_Lake_Unit_20_17___20_8_BD__5M10M_BOP_20250319084559.pdf

Section 3 - Casing

Casing ID	String Type	Hole Size	Csg Size	Condition	Standard	Tapered String	Top Set MD	Bottom Set MD	Top Set TVD	Bottom Set TVD	Top Set MSL	Bottom Set MSL	Calculated casing length MD	Grade	Weight	Joint Type	Collapse SF	Burst SF	Joint SF Type	Joint SF	Body SF Type	Body SF
1	SURFACE	12.25	9.625	NEW	API	N	0	976	0	976	3198	2222	976	J-55	40	BUTT	6.45	1.43	DRY	16.14	DRY	16.14
2	INTERMEDIATE	8.75	7.625	NEW	API	Y	0	9218	0	8600	3198	-5402	9218	L-80	29.7	FJ	2.06	2.86	DRY	2.62	DRY	2.62
3	PRODUCTION	6.75	5.5	NEW	NON API	Y	0	23736	0	9510	3198	-6312	23736	P-110	20	OTHER - TPN/Wedge 441	2.47	1.05	DRY	2.11	DRY	2.11

Casing Attachments

Casing ID: 1StringSURFACE

Inspection Document:

Spec Document:

Tapered String Spec:

Casing Design Assumptions and Worksheet(s):

Well Number: 208H

Casing ID: 2 **String** INTERMEDIATE

Inspection Document:

Spec Document:

Tapered String Spec:

Casing Design Assumptions and Worksheet(s):

Casing ID: 3 **String** PRODUCTION

Inspection Document:

Spec Document:

TPN_5.500_20.00_0.361_P110_ICY_20250319105125.pdf

Wedge 441 5.500 20.00 0.361 P110 ICY 20250319105124.pdf

Tapered String Spec:

Poker_Lake_Unit_20_8_BD_208H_Csg_20250319105350.pdf

Casing Design Assumptions and Worksheet(s):

Poker Lake Unit 20 8 BD 208H Csg 20250319105426.pdf

Section 4 - Cement

String Type	Lead/Tail	Stage Tool Depth	Top MD	Bottom MD	Quantity(sx)	Yield	Density	Cu Ft	Excess%	Cement type	Additives
SURFACE	Lead		0	976	220	1.87	10.5	411.4	100	EconoCem-HLTRRC	NA
SURFACE	Tail		0	976	130	1.35	14.8	175.5	100	Class C	2%cacl
INTERMEDIATE	Lead		0	6196	280	1.35	14.8	378	100	Class C	NA
INTERMEDIATE	Tail		6196	9218	700	1.33	14.8	931	100	Class C	NA

Well Name: POKER LAKE UNIT 20-8 BD

Well Number: 208H

Section 6 - Test, Logging, Coring

List of production tests including testing procedures, equipment and safety measures:

Open hole logging will not be done on this well.

List of open and cased hole logs run in the well:

CEMENT BOND LOG,GAMMA RAY LOG,DIRECTIONAL SURVEY,MEASUREMENT WHILE DRILLING,MUD LOG/GEOLOGICAL LITHOLOGY LOG,

Coring operation description for the well:

No coring is planned for the well.

Section 7 - Pressure

Anticipated Bottom Hole Pressure: 4747

Anticipated Surface Pressure: 2654

Anticipated Bottom Hole Temperature(F): 180

Anticipated abnormal pressures, temperatures, or potential geologic hazards? NO

Describe:

Contingency Plans geohazards description:

Contingency Plans geohazards

Hydrogen Sulfide drilling operations plan required? YES

Hydrogen sulfide drilling operations

XTO_Energy_H2S_Plan_Updated_20240827123524.pdf

Section 8 - Other Information

Proposed horizontal/directional/multi-lateral plan submission:

Poker_Lake_Unit_20_8_BD_208H_DD_20240911123725.pdf

Other proposed operations facets description:

Other proposed operations facets attachment:

Poker_Lake_Unit_20_8_BD_208H_Cmt_20240911123803.pdf

Poker_Lake_Unit_20_17___20_8_BD_MBS_9.625_x_7.625_3String_20240827131502.pdf

NGMPForm_PLU_20_17_20_8_BD___18_19___18_30_20240911063348.pdf

POKER_LAKE_UNIT_20_17___20_8_BD_H2S_DIA_PAD_B___PAD_D_Combined_20250319085136.pdf

Other Variance request(s)?: Y

Other Variance attachment:

BOP_Break_Test_Variance_20240827131930.pdf

Flex_Hose_Updated_20240827131622.pdf

Well Name: POKER LAKE UNIT 20-8 BD


Well Number: 208H

Poker_Lake_Unit_20_17__20_8_BD__OLCV_20240827131923.pdf

Spudder_Rig_Request_20240827131622.pdf


CONFIDENTIAL

Bleed line will discharge 100' from wellhead for non-H2S situations and 150' from wellhead for H2S situations.

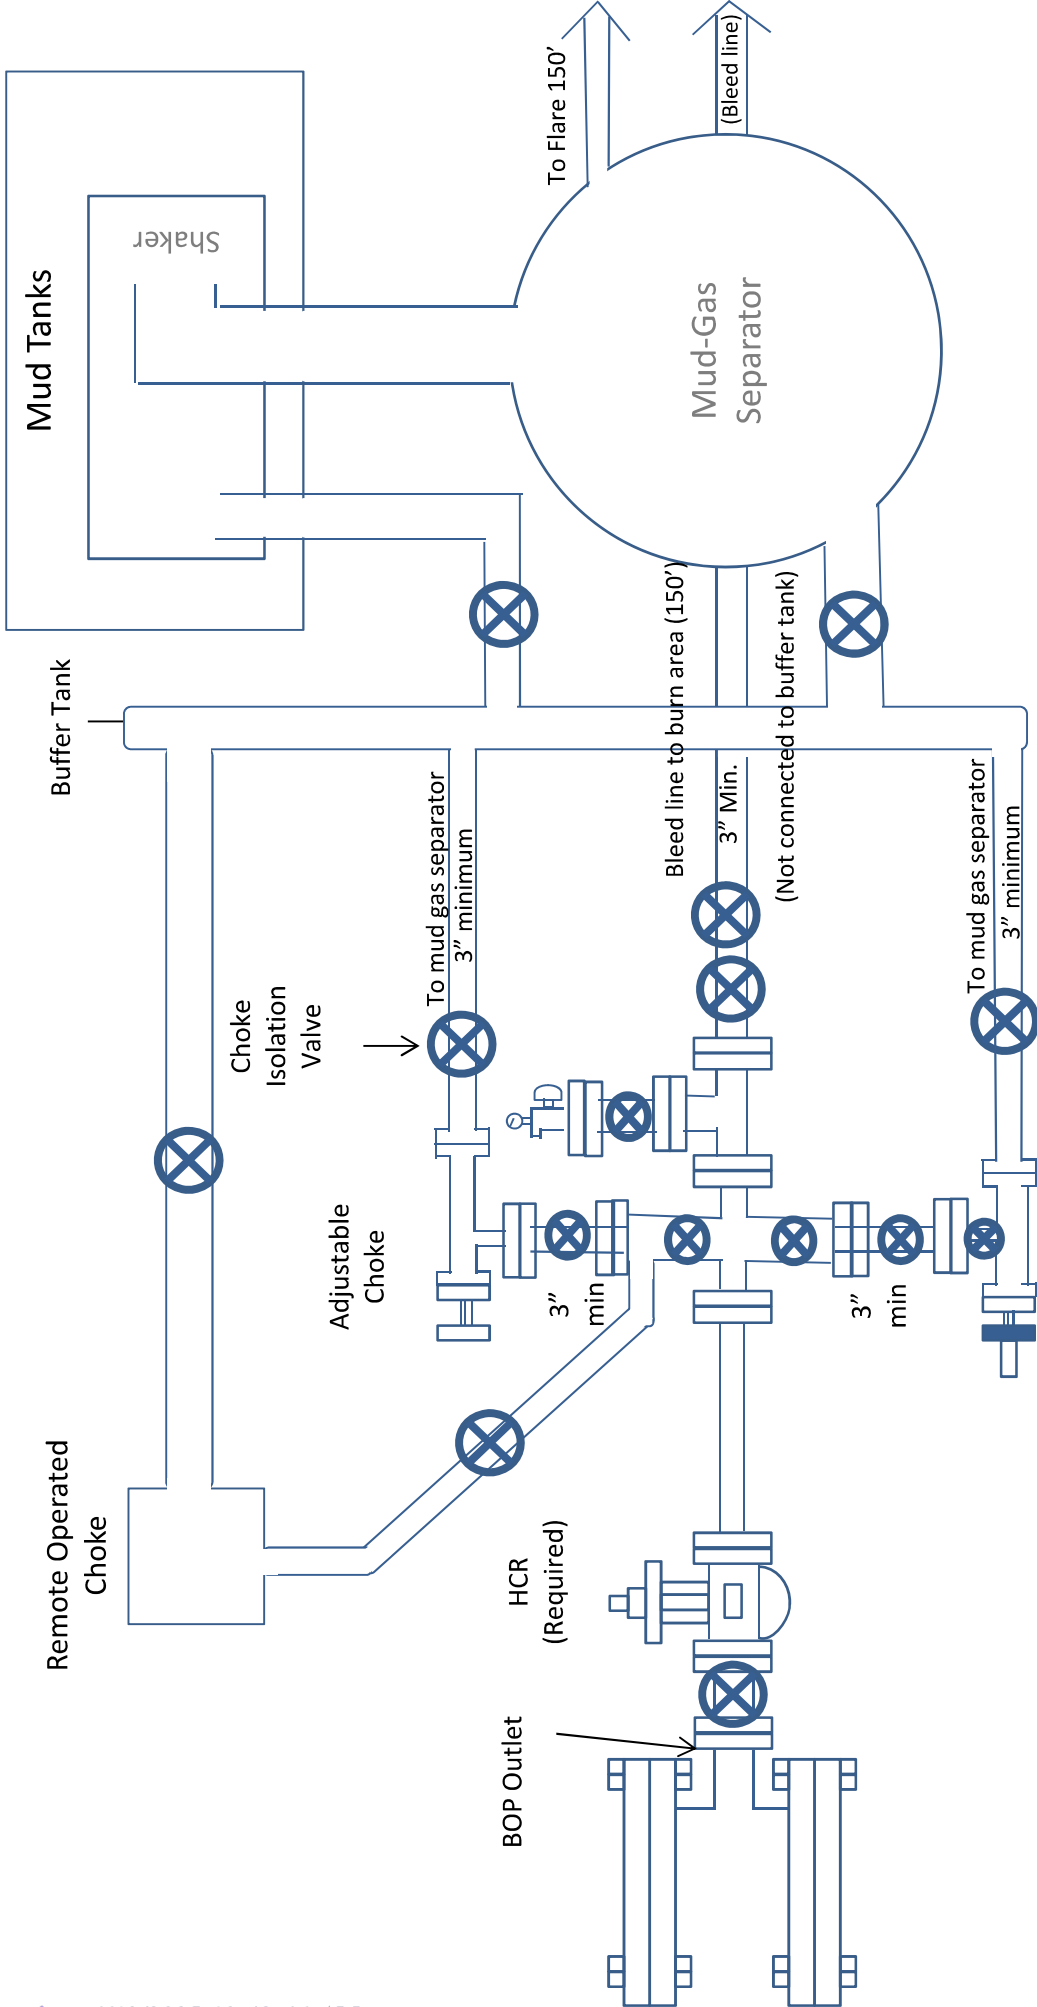

10M Choke Manifold Diagram
XTO

**Drilling Operations
Choke Manifold
10M Service**

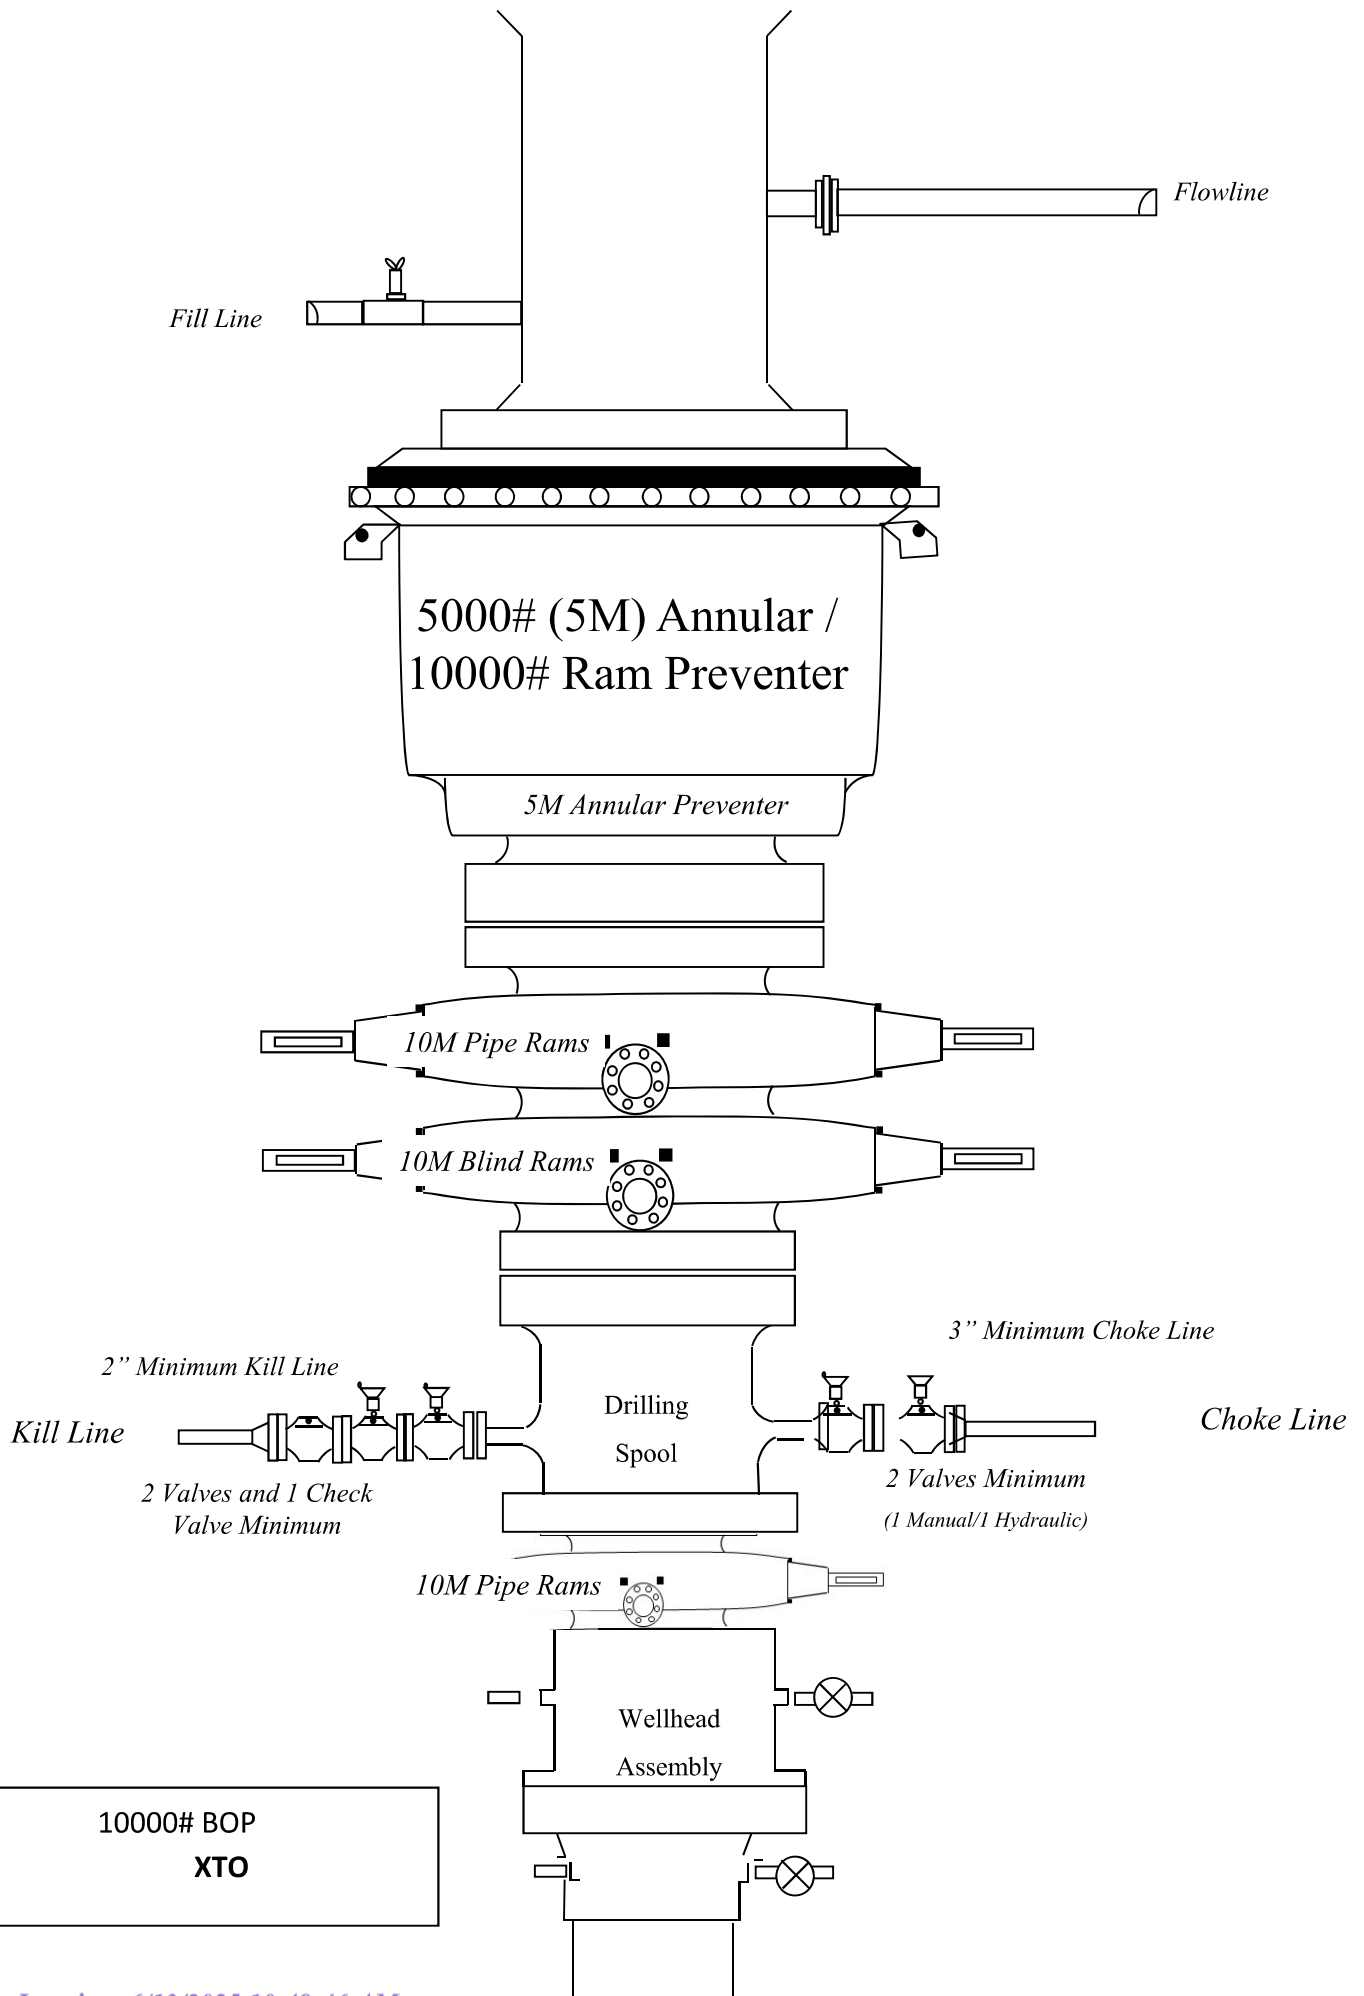

TenarisHydril Wedge
441®



Coupling	Pipe Body
Grade: P110-ICY	Grade: P110-ICY
Body: White	1st Band: White
1st Band: Pale Green	2nd Band: Pale Green
2nd Band: -	3rd Band: Pale Green
3rd Band: -	4th Band: -
	5th Band: -
	6th Band: -

Outside Diameter	5.500 in.	Wall Thickness	0.361 in.	Grade	P110-ICY
Min. Wall Thickness	87.50 %	Pipe Body Drift	API Standard	Type	Casing
Connection OD Option	REGULAR				

Pipe Body Data

Geometry				Performance	
Nominal OD	5.500 in.	Wall Thickness	0.361 in.	Body Yield Strength	729 x1000 lb
Nominal Weight	20.00 lb/ft	Plain End Weight	19.83 lb/ft	Min. Internal Yield Pressure	14,360 psi
Drift	4.653 in.	OD Tolerance	API	SMYS	125,000 psi
Nominal ID	4.778 in.			Collapse Pressure	12,300 psi

Connection Data

Geometry		Performance		Make-Up Torques	
Connection OD	5.852 in.	Tension Efficiency	81.50 %	Minimum	15,000 ft-lb
Coupling Length	8.714 in.	Joint Yield Strength	594 x1000 lb	Optimum	16,000 ft-lb
Connection ID	4.778 in.	Internal Pressure Capacity	14,360 psi	Maximum	19,200 ft-lb
Make-up Loss	3.780 in.	Compression Efficiency	81.50 %	Operation Limit Torques	
Threads per inch	3.40	Compression Strength	594 x1000 lb	Operating Torque	36,000 ft-lb
Connection OD Option	Regular	Max. Allowable Bending	84.76 °/100 ft	Yield Torque	42,000 ft-lb
		External Pressure Capacity	12,300 psi	Buck-On	
				Minimum	19,200 ft-lb
				Maximum	20,700 ft-lb

Notes

This connection is fully interchangeable with:
Wedge 441® - 5.5 in. - 0.304 (17.00) in. (lb/ft)
Wedge 461® - 5.5 in. - 0.304 (17.00) / 0.361 (20.00) / 0.415 (23.00) in. (lb/ft)
Connections with Dopeless® Technology are fully compatible with the same connection in its doped version

For the latest performance data, always visit our website: www.tenaris.com
For further information on concepts indicated in this datasheet, download the Datasheet Manual from www.tenaris.com

Tenaris has issued this document for general information only, and the information in this document, including, without limitation, any pictures, drawings or designs ("Information") is not intended to constitute professional or any other type of advice or recommendation and is provided on an "as is" basis. No warranty is given. Tenaris has not independently verified any information –if any- provided by the user in connection with, or for the purpose of, the Information contained hereunder. The use of the Information is at user's own risk and Tenaris does not assume any responsibility or liability of any kind for any loss, damage or injury resulting from, or in connection with any Information contained hereunder or any use thereof. The Information in this document is subject to change or modification without notice. Tenaris's products and services are subject to Tenaris's standard terms and conditions or otherwise to the terms resulting from the respective contracts of sale or services, as the case may be, between petitioner and Tenaris. For more complete information please contact a Tenaris's representative or visit our website at www.tenaris.com . ©Tenaris 2025. All rights reserved.



Coupling	Pipe Body
Grade: P1104CY	Grade: P1104CY
Body: White	1st Band: White
1st Band: Pale Green	2nd Band: Pale Green
2nd Band: -	3rd Band: Pale Green
3rd Band: -	4th Band: -
	5th Band: -
	6th Band: -

Customer	XTO ENERGY INC.	Wall Thickness	0.361 in.	Grade	P110-ICY
Outside Diameter	5.500 in.	Pipe Body Drift	API Standard	Type	Casing
Min. Wall Thickness	87.50 %				
Connection OD Option	REGULAR				

Pipe Body Data

Geometry		Performance	
Nominal OD	5.500 in.	Wall Thickness	0.361 in.
Nominal Weight	20.00 lb/ft	Plain End Weight	19.83 lb/ft
Drift	4.653 in.	OD Tolerance	API
Nominal ID	4.778 in.		
		Body Yield Strength	729 x1000 lb
		Min. Internal Yield Pressure	14,360 psi
		SMYS	125,000 psi
		Collapse Pressure	12,300 psi

Connection Data

Geometry		Performance		Make-Up Torques	
Connection OD	6.300 in.	Tension Efficiency	100 %	Minimum	21,100 ft-lb
Coupling Length	8.408 in.	Joint Yield Strength	729 x1000 lb	Optimum	22,600 ft-lb
Connection ID	4.778 in.	Internal Pressure Capacity	14,360 psi	Maximum	24,100 ft-lb
Make-up Loss	4.204 in.	Compression Efficiency	100 %		
Threads per inch	5	Compression Strength	729 x1000 lb	Operation Limit Torques	
Connection OD Option	Regular	Max. Allowable Bending	104 °/100 ft	Operating Torque	29,300 ft-lb
		External Pressure Capacity	12,300 psi	Yield Torque	32,500 ft-lb

Notes

For the latest performance data, always visit our website: www.tenaris.com
For further information on concepts indicated in this datasheet, download the Datasheet Manual from www.tenaris.com

Tenaris has issued this document for general information only, and the information in this document, including, without limitation, any pictures, drawings or designs ("Information") is not intended to constitute professional or any other type of advice or recommendation and is provided on an "as is" basis. No warranty is given. Tenaris has not independently verified any information –if any– provided by the user in connection with, or for the purpose of, the Information contained hereunder. The use of the Information is at user's own risk and Tenaris does not assume any responsibility or liability of any kind for any loss, damage or injury resulting from, or in connection with any Information contained hereunder or any use thereof. The Information in this document is subject to change or modification without notice. Tenaris's products and services are subject to Tenaris's standard terms and conditions or otherwise to the terms resulting from the respective contracts of sale or services, as the case may be, between petitioner and Tenaris. For more complete information please contact a Tenaris's representative or visit our website at www.tenaris.com . ©Tenaris 2024. All rights reserved.

PI-0/CII-3

Casing Assumptions

Casing Design

Hole Size	Depth	OD Csg	Weight	Grade	Collar	New/Used	SF Burst	SF Collapse	SF Tension
12.25	0' – 976'	9.625	40	J-55	BTC	New	1.43	6.45	16.14
8.75	0' – 4000'	7.625	29.7	RY P-110	Flush Joint	New	3.93	2.57	2.04
8.75	4000' – 9217.86'	7.625	29.7	HC L-80	Flush Joint	New	2.86	2.06	2.62
6.75	0' – 9117.86'	5.5	20			New	1.05	2.57	2.11
6.75	9117.86' - 23735.6'	5.5	20			New	1.05	2.47	2.11

Casing Assumptions

Casing Design

Hole Size	Depth	OD Csg	Weight	Grade	Collar	New/Used	SF Burst	SF Collapse	SF Tension
12.25	0' – 976'	9.625	40	J-55	BTC	New	1.43	6.45	16.14
8.75	0' – 4000'	7.625	29.7	RY P-110	Flush Joint	New	3.93	2.57	2.04
8.75	4000' – 9217.86'	7.625	29.7	HC L-80	Flush Joint	New	2.86	2.06	2.62
6.75	0' – 9117.86'	5.5	20			New	1.05	2.57	2.11
6.75	9117.86' - 23735.6'	5.5	20			New	1.05	2.47	2.11



HYDROGEN SULFIDE (H₂S) CONTINGENCY PLAN

Assumed 100 ppm ROE = 3000'

100 ppm H₂S concentration shall trigger activation of this plan.

Emergency Procedures

In the event of a release of gas containing H₂S, the first responder(s) must

- Isolate the area and prevent entry by other persons into the 100 ppm ROE.
- Evacuate any public places encompassed by the 100 ppm ROE.
- Be equipped with H₂S monitors and air packs in order to control the release.
- Use the "buddy system" to ensure no injuries occur during the response
- Take precautions to avoid personal injury during this operation.
- Contact operator and/or local officials to aid in operation. See list of phone numbers attached.
- Have received training in the
 - o Detection of H₂S, and
 - o Measures for protection against the gas,
 - o Equipment used for protection and emergency response.

Ignition of Gas source

Should control of the well be considered lost and ignition considered, take care to protect against exposure to Sulfur Dioxide (SO₂). Intentional ignition must be coordinated with the NMOCD and local officials. Additionally, the NM State Police may become involved. NM State Police shall be the Incident Command on scene of any major release. Take care to protect downwind whenever this is an ignition of the gas.

Characteristics of H₂S and SO₂

Common Name	Chemical Formula	Specific Gravity	Threshold Limit	Hazardous Limit	Lethal Concentration
Hydrogen Sulfide	H ₂ S	1.189 Air = 1	10 ppm	100 ppm/hr	600 ppm
Sulfur Dioxide	SO ₂	2.21 Air = 1	2 ppm	N/A	1000 ppm

Contacting Authorities

All XTO location personnel must liaison with local and state agencies to ensure a proper response to a major release. Additionally, the OCD must be notified of the release as soon as possible but no later than 4 hours. Agencies will ask for information such as type and volume of release, wind direction, location of release, etc. Be prepared with all information available including directions to site. The following call list of essential and potential responders has been prepared for use during a release. (Operator Name)'s response must be in coordination with the State of New Mexico's "Hazardous Materials Emergency Response Plan" (HMER).

CARLSBAD OFFICE – EDDY & LEA COUNTIES

3104 E. Greene St., Carlsbad, NM 88220
Carlsbad, NM

575-887-7329

XTO PERSONNEL:

Will Dacus, Drilling Manager	832-948-5021
Brian Dunn, Drilling Supervisor	832-653-0490
Robert Bartels, Construction Execution Planner	406-478-3617
Andy Owens, EH & S Manager	903-245-2602
Frank Fuentes, Production Foreman	575-689-3363

SHERIFF DEPARTMENTS:

Eddy County	575-887-7551
Lea County	575-396-3611

NEW MEXICO STATE POLICE:

575-392-5588

FIRE DEPARTMENTS:

	911
Carlsbad	575-885-2111
Eunice	575-394-2111
Hobbs	575-397-9308
Jal	575-395-2221
Lovington	575-396-2359

HOSPITALS:

	911
Carlsbad Medical Emergency	575-885-2111
Eunice Medical Emergency	575-394-2112
Hobbs Medical Emergency	575-397-9308
Jal Medical Emergency	575-395-2221
Lovington Medical Emergency	575-396-2359

AGENT NOTIFICATIONS:**For Lea County:**

Bureau of Land Management – Hobbs	575-393-3612
New Mexico Oil Conservation Division – Hobbs	575-393-6161

For Eddy County:

Bureau of Land Management - Carlsbad	575-234-5972
New Mexico Oil Conservation Division - Artesia	575-748-1283

Well Plan Report - Poker Lake Unit 20-8 BD 208H

Measured Depth: 23735.60 ft
TVD RKB: 9510.00 ft
Location
Cartographic Reference System: New Mexico East - NAD 27
Northing: 405167.40 ft
Easting: 634382.10 ft
RKB: 3230.00 ft
Ground Level: 3198.00 ft
North Reference: Grid
Convergence Angle: 0.23 Deg

Plan Sections Poker Lake Unit 20-8 BD 208H

Measured Depth (ft)	Inclination (Deg)	Azimuth (Deg)	TVD RKB (ft)	Y Offset (ft)	X Offset (ft)	Build		Turn		Dogleg	
						Rate (Deg/100ft)	Rate (Deg/100ft)	Rate (Deg/100ft)	Rate (Deg/100ft)	Rate (Deg/100ft)	Target
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
1100.00	0.00	0.00	1100.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
2729.56	32.59	172.78	2643.10	-447.53	56.70	2.00	0.00	0.00	0.00	2.00	2.00
5594.50	32.59	172.78	5056.90	-1978.46	250.67	0.00	0.00	0.00	0.00	0.00	0.00
7224.06	0.00	0.00	6600.00	-2425.99	307.37	-2.00	0.00	0.00	0.00	2.00	2.00
9417.86	0.00	0.00	8793.80	-2425.99	307.37	0.00	0.00	0.00	0.00	0.00	0.00
10542.86	90.00	359.74	9510.00	-1709.80	304.10	8.00	0.00	0.00	0.00	8.00	FTP 8
23645.60	90.00	359.74	9510.00	11392.80	244.20	0.00	0.00	0.00	0.00	0.00	LTP 8
23735.60	90.00	359.74	9510.00	11482.80	243.79	0.00	0.00	0.00	0.00	0.00	BHL 8

Position Uncertainty Poker Lake Unit 20-8 BD 208H

Measured	TVD	Highside	Lateral	Vertical	Magnitude	Semi-major	Semi-minor	Semi-Tool

Depth (ft)	Inclination (°)	Azimuth (°)	RKB (ft)	Error (ft)	Bias (ft)	Error (ft)	Bias (ft)	Error (ft)	Bias (ft)	Error (ft)	Error (ft)	Azimuth (°)	Used
0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	XOMR2_OWSG MWD+IFR1+MS
100.000	0.000	0.000	100.000	0.358	0.000	0.179	0.000	2.300	0.000	0.358	0.179	90.000	XOMR2_OWSG MWD+IFR1+MS
200.000	0.000	0.000	200.000	0.717	0.000	0.538	0.000	2.309	0.000	0.717	0.538	90.000	XOMR2_OWSG MWD+IFR1+MS
300.000	0.000	0.000	300.000	1.075	0.000	0.896	0.000	2.325	0.000	1.075	0.896	90.000	XOMR2_OWSG MWD+IFR1+MS
400.000	0.000	0.000	400.000	1.434	0.000	1.255	0.000	2.346	0.000	1.434	1.255	90.000	XOMR2_OWSG MWD+IFR1+MS
500.000	0.000	0.000	500.000	1.792	0.000	1.613	0.000	2.373	0.000	1.792	1.613	90.000	XOMR2_OWSG MWD+IFR1+MS
600.000	0.000	0.000	600.000	2.151	0.000	1.972	0.000	2.405	0.000	2.151	1.972	90.000	XOMR2_OWSG MWD+IFR1+MS
700.000	0.000	0.000	700.000	2.509	0.000	2.330	0.000	2.442	0.000	2.509	2.330	90.000	XOMR2_OWSG MWD+IFR1+MS
800.000	0.000	0.000	800.000	2.868	0.000	2.689	0.000	2.483	0.000	2.868	2.689	90.000	XOMR2_OWSG MWD+IFR1+MS
900.000	0.000	0.000	900.000	3.226	0.000	3.047	0.000	2.528	0.000	3.226	3.047	90.000	XOMR2_OWSG MWD+IFR1+MS
1000.000	0.000	0.000	1000.000	3.585	0.000	3.405	0.000	2.578	0.000	3.585	3.405	90.000	XOMR2_OWSG MWD+IFR1+MS
1100.000	0.000	0.000	1100.000	3.943	0.000	3.764	0.000	2.631	0.000	3.943	3.764	90.000	XOMR2_OWSG MWD+IFR1+MS
1200.000	2.000	172.779	1199.980	4.279	0.000	4.107	-0.000	2.686	0.000	4.284	4.104	89.995	XOMR2_OWSG MWD+IFR1+MS
1300.000	4.000	172.779	1299.838	4.600	0.000	4.432	-0.000	2.743	0.000	4.612	4.429	89.955	XOMR2_OWSG MWD+IFR1+MS
1400.000	6.000	172.779	1399.452	4.919	0.000	4.762	-0.000	2.801	0.000	4.945	4.759	89.931	XOMR2_OWSG MWD+IFR1+MS
1500.000	8.000	172.779	1498.702	5.238	0.000	5.097	-0.000	2.860	0.000	5.282	5.094	89.960	XOMR2_OWSG MWD+IFR1+MS
1600.000	10.000	172.779	1597.465	5.555	0.000	5.437	-0.000	2.920	0.000	5.622	5.434	90.078	XOMR2_OWSG MWD+IFR1+MS
1700.000	12.000	172.779	1695.623	5.870	0.000	5.783	-0.000	2.983	0.000	5.965	5.780	90.326	XOMR2_OWSG MWD+IFR1+MS
1800.000	14.000	172.779	1793.055	6.184	0.000	6.137	-0.000	3.049	0.000	6.310	6.133	90.763	XOMR2_OWSG MWD+IFR1+MS

1900.000	16.000	172.779	1889.643	6.497	0.000	6.498	-0.000	3.119	0.000	0.000	6.659	6.494	91.498	XOMR2_OWSG MWD+IFR1+MS
2000.000	18.000	172.779	1985.268	6.809	0.000	6.869	-0.000	3.195	0.000	0.000	7.010	6.864	92.745	XOMR2_OWSG MWD+IFR1+MS
2100.000	20.000	172.779	2079.816	7.121	0.000	7.249	-0.000	3.277	0.000	0.000	7.364	7.244	95.019	XOMR2_OWSG MWD+IFR1+MS
2200.000	22.000	172.779	2173.169	7.433	0.000	7.641	-0.000	3.368	0.000	0.000	7.722	7.633	99.828	XOMR2_OWSG MWD+IFR1+MS
2300.000	24.000	172.779	2265.215	7.746	0.000	8.044	-0.000	3.469	0.000	0.000	8.087	8.030	112.892	XOMR2_OWSG MWD+IFR1+MS
2400.000	26.000	172.779	2355.841	8.060	0.000	8.461	-0.000	3.583	0.000	0.000	8.475	8.419	-37.785	XOMR2_OWSG MWD+IFR1+MS
2500.000	28.000	172.779	2444.937	8.377	0.000	8.891	-0.000	3.712	0.000	0.000	8.897	8.790	-20.895	XOMR2_OWSG MWD+IFR1+MS
2600.000	30.000	172.779	2532.394	8.695	0.000	9.335	-0.000	3.857	0.000	0.000	9.338	9.158	-14.937	XOMR2_OWSG MWD+IFR1+MS
2700.000	32.000	172.779	2618.107	9.017	0.000	9.794	-0.000	4.022	0.000	0.000	9.796	9.525	-12.215	XOMR2_OWSG MWD+IFR1+MS
2729.562	32.591	172.779	2643.095	9.112	0.000	9.931	-0.000	4.067	0.000	0.000	9.933	9.636	-11.753	XOMR2_OWSG MWD+IFR1+MS
2800.000	32.591	172.779	2702.442	9.421	0.000	10.265	-0.000	4.208	0.000	0.000	10.266	9.892	-10.747	XOMR2_OWSG MWD+IFR1+MS
2900.000	32.591	172.779	2786.696	9.865	0.000	10.748	-0.000	4.422	0.000	0.000	10.749	10.258	-9.830	XOMR2_OWSG MWD+IFR1+MS
3000.000	32.591	172.779	2870.949	10.318	0.000	11.239	-0.000	4.646	0.000	0.000	11.240	10.630	-9.250	XOMR2_OWSG MWD+IFR1+MS
3100.000	32.591	172.779	2955.202	10.776	0.000	11.738	-0.000	4.877	0.000	0.000	11.739	11.008	-8.851	XOMR2_OWSG MWD+IFR1+MS
3200.000	32.591	172.779	3039.456	11.241	0.000	12.243	-0.000	5.115	0.000	0.000	12.244	11.390	-8.559	XOMR2_OWSG MWD+IFR1+MS
3300.000	32.591	172.779	3123.709	11.710	0.000	12.754	-0.000	5.359	0.000	0.000	12.755	11.777	-8.337	XOMR2_OWSG MWD+IFR1+MS
3400.000	32.591	172.779	3207.963	12.183	0.000	13.270	-0.000	5.608	0.000	0.000	13.270	12.168	-8.161	XOMR2_OWSG MWD+IFR1+MS
3500.000	32.591	172.779	3292.216	12.661	0.000	13.790	-0.000	5.862	0.000	0.000	13.791	12.563	-8.020	XOMR2_OWSG MWD+IFR1+MS
3600.000	32.591	172.779	3376.470	13.142	0.000	14.315	-0.000	6.121	0.000	0.000	14.315	12.960	-7.903	XOMR2_OWSG MWD+IFR1+MS
3700.000	32.591	172.779	3460.723	13.626	0.000	14.842	-0.000	6.382	0.000	0.000	14.842	13.361	-7.805	XOMR2_OWSG MWD+IFR1+MS

Well Plan Report

3800.000	32.591	172.779	3544.977	14.113	0.000	15.373	-0.000	6.647	0.000	0.000	15.373	13.765	-7.721	XOMR2_OWSG MWD+IFR1+MS
3900.000	32.591	172.779	3629.230	14.602	0.000	15.907	-0.000	6.915	0.000	0.000	15.907	14.171	-7.649	XOMR2_OWSG MWD+IFR1+MS
4000.000	32.591	172.779	3713.484	15.093	0.000	16.443	-0.000	7.186	0.000	0.000	16.443	14.580	-7.587	XOMR2_OWSG MWD+IFR1+MS
4100.000	32.591	172.779	3797.737	15.587	0.000	16.982	-0.000	7.459	0.000	0.000	16.982	14.990	-7.532	XOMR2_OWSG MWD+IFR1+MS
4200.000	32.591	172.779	3881.991	16.083	0.000	17.522	-0.000	7.734	0.000	0.000	17.522	15.403	-7.483	XOMR2_OWSG MWD+IFR1+MS
4300.000	32.591	172.779	3966.244	16.580	0.000	18.065	-0.000	8.012	0.000	0.000	18.065	15.817	-7.439	XOMR2_OWSG MWD+IFR1+MS
4400.000	32.591	172.779	4050.498	17.078	0.000	18.609	-0.000	8.291	0.000	0.000	18.609	16.234	-7.400	XOMR2_OWSG MWD+IFR1+MS
4500.000	32.591	172.779	4134.751	17.579	0.000	19.155	-0.000	8.571	0.000	0.000	19.155	16.652	-7.365	XOMR2_OWSG MWD+IFR1+MS
4600.000	32.591	172.779	4219.005	18.080	0.000	19.703	-0.000	8.854	0.000	0.000	19.703	17.071	-7.333	XOMR2_OWSG MWD+IFR1+MS
4700.000	32.591	172.779	4303.258	18.583	0.000	20.252	-0.000	9.138	0.000	0.000	20.252	17.492	-7.304	XOMR2_OWSG MWD+IFR1+MS
4800.000	32.591	172.779	4387.512	19.086	0.000	20.802	-0.000	9.423	0.000	0.000	20.802	17.914	-7.277	XOMR2_OWSG MWD+IFR1+MS
4900.000	32.591	172.779	4471.765	19.591	0.000	21.353	-0.000	9.709	0.000	0.000	21.353	18.337	-7.253	XOMR2_OWSG MWD+IFR1+MS
5000.000	32.591	172.779	4556.019	20.097	0.000	21.905	-0.000	9.997	0.000	0.000	21.905	18.761	-7.230	XOMR2_OWSG MWD+IFR1+MS
5100.000	32.591	172.779	4640.272	20.603	0.000	22.458	-0.000	10.286	0.000	0.000	22.458	19.187	-7.209	XOMR2_OWSG MWD+IFR1+MS
5200.000	32.591	172.779	4724.526	21.111	0.000	23.012	-0.000	10.576	0.000	0.000	23.012	19.613	-7.190	XOMR2_OWSG MWD+IFR1+MS
5300.000	32.591	172.779	4808.779	21.619	0.000	23.567	-0.000	10.868	0.000	0.000	23.567	20.041	-7.172	XOMR2_OWSG MWD+IFR1+MS
5400.000	32.591	172.779	4893.032	22.127	0.000	24.123	-0.000	11.160	0.000	0.000	24.123	20.469	-7.155	XOMR2_OWSG MWD+IFR1+MS
5500.000	32.591	172.779	4977.286	22.637	0.000	24.680	-0.000	11.453	0.000	0.000	24.680	20.898	-7.140	XOMR2_OWSG MWD+IFR1+MS
5594.499	32.591	172.779	5056.905	23.119	0.000	25.206	-0.000	11.731	0.000	0.000	25.206	21.305	-7.126	XOMR2_OWSG MWD+IFR1+MS
5600.000	32.481	172.779	5061.542	23.152	0.000	25.237	-0.000	11.748	0.000	0.000	25.237	21.328	-7.125	XOMR2_OWSG MWD+IFR1+MS

Well Plan Report

5700.000	30.481	172.779	5146.819	23.738	0.000	25.786	-0.000	12.036	0.000	0.000	25.786	21.757	-7.111	XOMR2_OWSG MWD+IFR1+MS
5800.000	28.481	172.779	5233.866	24.286	0.000	26.322	-0.000	12.311	0.000	0.000	26.322	22.184	-7.099	XOMR2_OWSG MWD+IFR1+MS
5900.000	26.481	172.779	5322.578	24.795	0.000	26.842	-0.000	12.567	0.000	0.000	26.842	22.610	-7.087	XOMR2_OWSG MWD+IFR1+MS
6000.000	24.481	172.779	5412.846	25.263	0.000	27.347	-0.000	12.807	0.000	0.000	27.347	23.032	-7.076	XOMR2_OWSG MWD+IFR1+MS
6100.000	22.481	172.779	5504.561	25.689	0.000	27.834	-0.000	13.029	0.000	0.000	27.834	23.450	-7.066	XOMR2_OWSG MWD+IFR1+MS
6200.000	20.481	172.779	5597.610	26.073	0.000	28.305	-0.000	13.235	0.000	0.000	28.305	23.861	-7.056	XOMR2_OWSG MWD+IFR1+MS
6300.000	18.481	172.779	5691.880	26.414	0.000	28.758	-0.000	13.426	0.000	0.000	28.758	24.265	-7.047	XOMR2_OWSG MWD+IFR1+MS
6400.000	16.481	172.779	5787.257	26.710	0.000	29.193	-0.000	13.602	0.000	0.000	29.193	24.660	-7.039	XOMR2_OWSG MWD+IFR1+MS
6500.000	14.481	172.779	5883.623	26.962	0.000	29.610	-0.000	13.765	0.000	0.000	29.610	25.044	-7.032	XOMR2_OWSG MWD+IFR1+MS
6600.000	12.481	172.779	5980.863	27.169	0.000	30.009	-0.000	13.914	0.000	0.000	30.009	25.418	-7.025	XOMR2_OWSG MWD+IFR1+MS
6700.000	10.481	172.779	6078.857	27.331	0.000	30.388	-0.000	14.052	0.000	0.000	30.388	25.779	-7.018	XOMR2_OWSG MWD+IFR1+MS
6800.000	8.481	172.779	6177.486	27.448	0.000	30.749	-0.000	14.180	0.000	0.000	30.749	26.127	-7.013	XOMR2_OWSG MWD+IFR1+MS
6900.000	6.481	172.779	6276.630	27.520	0.000	31.091	-0.000	14.298	0.000	0.000	31.091	26.462	-7.008	XOMR2_OWSG MWD+IFR1+MS
7000.000	4.481	172.779	6376.168	27.546	0.000	31.414	-0.000	14.408	0.000	0.000	31.414	26.782	-7.003	XOMR2_OWSG MWD+IFR1+MS
7100.000	2.481	172.779	6475.978	27.528	0.000	31.718	-0.000	14.510	0.000	0.000	31.718	27.087	-6.999	XOMR2_OWSG MWD+IFR1+MS
7200.000	0.481	172.779	6575.940	27.466	0.000	32.004	-0.000	14.607	0.000	0.000	32.004	27.377	-6.996	XOMR2_OWSG MWD+IFR1+MS
7224.061	0.000	0.000	6600.000	27.517	0.000	32.001	0.000	14.630	0.000	0.000	32.064	27.442	-6.998	XOMR2_OWSG MWD+IFR1+MS
7300.000	0.000	0.000	6675.939	27.715	0.000	32.173	0.000	14.702	0.000	0.000	32.237	27.641	-7.016	XOMR2_OWSG MWD+IFR1+MS
7400.000	0.000	0.000	6775.939	27.978	0.000	32.402	0.000	14.798	0.000	0.000	32.466	27.904	-7.040	XOMR2_OWSG MWD+IFR1+MS
7500.000	0.000	0.000	6875.939	28.242	0.000	32.634	0.000	14.898	0.000	0.000	32.698	28.169	-7.064	XOMR2_OWSG MWD+IFR1+MS

Well Plan Report

7600.000	0.000	0.000	6975.939	28.509	0.000	32.868	0.000	15.000	0.000	0.000	32.932	28.436	-7.088	XOMR2_OWSG MWD+IFR1+MS
7700.000	0.000	0.000	7075.939	28.778	0.000	33.104	0.000	15.105	0.000	0.000	33.168	28.705	-7.111	XOMR2_OWSG MWD+IFR1+MS
7800.000	0.000	0.000	7175.939	29.049	0.000	33.343	0.000	15.213	0.000	0.000	33.407	28.976	-7.135	XOMR2_OWSG MWD+IFR1+MS
7900.000	0.000	0.000	7275.939	29.322	0.000	33.583	0.000	15.324	0.000	0.000	33.647	29.249	-7.158	XOMR2_OWSG MWD+IFR1+MS
8000.000	0.000	0.000	7375.939	29.597	0.000	33.826	0.000	15.439	0.000	0.000	33.890	29.523	-7.182	XOMR2_OWSG MWD+IFR1+MS
8100.000	0.000	0.000	7475.939	29.873	0.000	34.070	0.000	15.556	0.000	0.000	34.134	29.800	-7.205	XOMR2_OWSG MWD+IFR1+MS
8200.000	0.000	0.000	7575.939	30.151	0.000	34.317	0.000	15.676	0.000	0.000	34.381	30.078	-7.229	XOMR2_OWSG MWD+IFR1+MS
8300.000	0.000	0.000	7675.939	30.431	0.000	34.566	0.000	15.800	0.000	0.000	34.630	30.358	-7.252	XOMR2_OWSG MWD+IFR1+MS
8400.000	0.000	0.000	7775.939	30.712	0.000	34.816	0.000	15.927	0.000	0.000	34.880	30.640	-7.276	XOMR2_OWSG MWD+IFR1+MS
8500.000	0.000	0.000	7875.939	30.995	0.000	35.069	0.000	16.057	0.000	0.000	35.133	30.923	-7.299	XOMR2_OWSG MWD+IFR1+MS
8600.000	0.000	0.000	7975.939	31.280	0.000	35.323	0.000	16.190	0.000	0.000	35.387	31.207	-7.322	XOMR2_OWSG MWD+IFR1+MS
8700.000	0.000	0.000	8075.939	31.566	0.000	35.579	0.000	16.327	0.000	0.000	35.643	31.494	-7.346	XOMR2_OWSG MWD+IFR1+MS
8800.000	0.000	0.000	8175.939	31.853	0.000	35.837	0.000	16.466	0.000	0.000	35.901	31.781	-7.369	XOMR2_OWSG MWD+IFR1+MS
8900.000	0.000	0.000	8275.939	32.142	0.000	36.096	0.000	16.610	0.000	0.000	36.160	32.070	-7.392	XOMR2_OWSG MWD+IFR1+MS
9000.000	0.000	0.000	8375.939	32.433	0.000	36.357	0.000	16.756	0.000	0.000	36.421	32.361	-7.415	XOMR2_OWSG MWD+IFR1+MS
9100.000	0.000	0.000	8475.939	32.724	0.000	36.620	0.000	16.906	0.000	0.000	36.684	32.653	-7.438	XOMR2_OWSG MWD+IFR1+MS
9200.000	0.000	0.000	8575.939	33.017	0.000	36.885	0.000	17.060	0.000	0.000	36.948	32.946	-7.461	XOMR2_OWSG MWD+IFR1+MS
9300.000	0.000	0.000	8675.939	33.312	0.000	37.151	0.000	17.217	0.000	0.000	37.214	33.240	-7.484	XOMR2_OWSG MWD+IFR1+MS
9400.000	0.000	0.000	8775.939	33.607	0.000	37.418	0.000	17.377	0.000	0.000	37.482	33.536	-7.507	XOMR2_OWSG MWD+IFR1+MS
9417.864	0.000	0.000	8793.803	33.660	0.000	37.466	0.000	17.407	0.000	0.000	37.530	33.589	-7.511	XOMR2_OWSG MWD+IFR1+MS

9500.000	6.571	359.738	8875.759	32.578	0.000	37.683	0.000	17.536	0.000	0.000	37.742	33.812	-7.521	XOMR2_OWSG MWD+IFR1+MS
9600.000	14.571	359.738	8973.982	30.775	0.000	37.917	0.000	17.686	0.000	0.000	37.977	34.030	-7.509	XOMR2_OWSG MWD+IFR1+MS
9700.000	22.571	359.738	9068.698	28.502	0.000	38.125	0.000	17.838	0.000	0.000	38.185	34.184	-7.464	XOMR2_OWSG MWD+IFR1+MS
9800.000	30.571	359.738	9158.064	25.872	0.000	38.305	0.000	18.005	0.000	0.000	38.365	34.278	-7.385	XOMR2_OWSG MWD+IFR1+MS
9900.000	38.571	359.738	9240.339	23.042	0.000	38.458	0.000	18.201	0.000	0.000	38.518	34.316	-7.275	XOMR2_OWSG MWD+IFR1+MS
10000.000	46.571	359.738	9313.924	20.249	0.000	38.586	0.000	18.437	0.000	0.000	38.645	34.308	-7.141	XOMR2_OWSG MWD+IFR1+MS
10100.000	54.571	359.738	9377.384	17.837	0.000	38.691	0.000	18.721	0.000	0.000	38.749	34.266	-6.991	XOMR2_OWSG MWD+IFR1+MS
10200.000	62.571	359.738	9429.486	16.265	0.000	38.774	0.000	19.059	0.000	0.000	38.831	34.203	-6.835	XOMR2_OWSG MWD+IFR1+MS
10300.000	70.571	359.738	9469.215	15.980	0.000	38.838	0.000	19.452	0.000	0.000	38.893	34.135	-6.680	XOMR2_OWSG MWD+IFR1+MS
10400.000	78.571	359.738	9495.798	17.119	0.000	38.883	0.000	19.897	0.000	0.000	38.937	34.075	-6.536	XOMR2_OWSG MWD+IFR1+MS
10500.000	86.571	359.738	9508.718	19.394	0.000	38.911	0.000	20.384	0.000	0.000	38.964	34.039	-6.413	XOMR2_OWSG MWD+IFR1+MS
10542.864	90.000	359.738	9510.000	20.603	0.000	38.916	0.000	20.603	0.000	0.000	38.968	34.034	-6.372	XOMR2_OWSG MWD+IFR1+MS
10600.000	90.000	359.738	9510.000	20.900	0.000	38.924	0.000	20.900	0.000	0.000	38.975	34.031	-6.315	XOMR2_OWSG MWD+IFR1+MS
10700.000	90.000	359.738	9510.000	21.432	0.000	38.956	0.000	21.432	0.000	0.000	39.006	34.026	-6.192	XOMR2_OWSG MWD+IFR1+MS
10800.000	90.000	359.738	9510.000	21.980	0.000	39.009	0.000	21.980	0.000	0.000	39.057	34.022	-6.047	XOMR2_OWSG MWD+IFR1+MS
10900.000	90.000	359.738	9510.000	22.542	0.000	39.081	0.000	22.542	0.000	0.000	39.127	34.019	-5.883	XOMR2_OWSG MWD+IFR1+MS
11000.000	90.000	359.738	9510.000	23.117	0.000	39.173	0.000	23.117	0.000	0.000	39.216	34.017	-5.703	XOMR2_OWSG MWD+IFR1+MS
11100.000	90.000	359.738	9510.000	23.704	0.000	39.284	0.000	23.704	0.000	0.000	39.326	34.015	-5.509	XOMR2_OWSG MWD+IFR1+MS
11200.000	90.000	359.738	9510.000	24.302	0.000	39.415	0.000	24.302	0.000	0.000	39.454	34.014	-5.304	XOMR2_OWSG MWD+IFR1+MS
11300.000	90.000	359.738	9510.000	24.910	0.000	39.565	0.000	24.910	0.000	0.000	39.602	34.014	-5.092	XOMR2_OWSG MWD+IFR1+MS

Well Plan Report

11400.000	90.000	359.738	9510.000	25.528	0.000	39.734	0.000	25.528	0.000	0.000	39.768	34.014	-4.875	XOMR2_OWSG MWD+IFR1+MS
11500.000	90.000	359.738	9510.000	26.155	0.000	39.921	0.000	26.155	0.000	0.000	39.954	34.015	-4.656	XOMR2_OWSG MWD+IFR1+MS
11600.000	90.000	359.738	9510.000	26.791	0.000	40.127	0.000	26.791	0.000	0.000	40.158	34.017	-4.438	XOMR2_OWSG MWD+IFR1+MS
11700.000	90.000	359.738	9510.000	27.434	0.000	40.352	0.000	27.434	0.000	0.000	40.380	34.019	-4.222	XOMR2_OWSG MWD+IFR1+MS
11800.000	90.000	359.738	9510.000	28.084	0.000	40.594	0.000	28.084	0.000	0.000	40.620	34.021	-4.010	XOMR2_OWSG MWD+IFR1+MS
11900.000	90.000	359.738	9510.000	28.741	0.000	40.854	0.000	28.741	0.000	0.000	40.878	34.025	-3.804	XOMR2_OWSG MWD+IFR1+MS
12000.000	90.000	359.738	9510.000	29.404	0.000	41.130	0.000	29.404	0.000	0.000	41.153	34.028	-3.604	XOMR2_OWSG MWD+IFR1+MS
12100.000	90.000	359.738	9510.000	30.073	0.000	41.424	0.000	30.073	0.000	0.000	41.445	34.033	-3.412	XOMR2_OWSG MWD+IFR1+MS
12200.000	90.000	359.738	9510.000	30.748	0.000	41.735	0.000	30.748	0.000	0.000	41.753	34.037	-3.228	XOMR2_OWSG MWD+IFR1+MS
12300.000	90.000	359.738	9510.000	31.428	0.000	42.061	0.000	31.428	0.000	0.000	42.078	34.043	-3.052	XOMR2_OWSG MWD+IFR1+MS
12400.000	90.000	359.738	9510.000	32.112	0.000	42.403	0.000	32.112	0.000	0.000	42.419	34.048	-2.885	XOMR2_OWSG MWD+IFR1+MS
12500.000	90.000	359.738	9510.000	32.801	0.000	42.761	0.000	32.801	0.000	0.000	42.775	34.055	-2.727	XOMR2_OWSG MWD+IFR1+MS
12600.000	90.000	359.738	9510.000	33.494	0.000	43.133	0.000	33.494	0.000	0.000	43.147	34.062	-2.577	XOMR2_OWSG MWD+IFR1+MS
12700.000	90.000	359.738	9510.000	34.192	0.000	43.521	0.000	34.192	0.000	0.000	43.533	34.069	-2.436	XOMR2_OWSG MWD+IFR1+MS
12800.000	90.000	359.738	9510.000	34.892	0.000	43.922	0.000	34.892	0.000	0.000	43.933	34.077	-2.302	XOMR2_OWSG MWD+IFR1+MS
12900.000	90.000	359.738	9510.000	35.597	0.000	44.338	0.000	35.597	0.000	0.000	44.348	34.085	-2.177	XOMR2_OWSG MWD+IFR1+MS
13000.000	90.000	359.738	9510.000	36.305	0.000	44.767	0.000	36.305	0.000	0.000	44.776	34.094	-2.059	XOMR2_OWSG MWD+IFR1+MS
13100.000	90.000	359.738	9510.000	37.015	0.000	45.209	0.000	37.015	0.000	0.000	45.217	34.104	-1.948	XOMR2_OWSG MWD+IFR1+MS
13200.000	90.000	359.738	9510.000	37.729	0.000	45.663	0.000	37.729	0.000	0.000	45.671	34.114	-1.844	XOMR2_OWSG MWD+IFR1+MS
13300.000	90.000	359.738	9510.000	38.446	0.000	46.130	0.000	38.446	0.000	0.000	46.137	34.125	-1.747	XOMR2_OWSG MWD+IFR1+MS

Well Plan Report

13400.000	90.000	359.738	9510.000	39.165	0.000	46.609	0.000	39.165	0.000	0.000	46.616	34.136	-1.655	XOMR2_OWSG MWD+IFR1+MS
13500.000	90.000	359.738	9510.000	39.886	0.000	47.100	0.000	39.886	0.000	0.000	47.105	34.148	-1.570	XOMR2_OWSG MWD+IFR1+MS
13600.000	90.000	359.738	9510.000	40.610	0.000	47.601	0.000	40.610	0.000	0.000	47.607	34.161	-1.489	XOMR2_OWSG MWD+IFR1+MS
13700.000	90.000	359.738	9510.000	41.336	0.000	48.114	0.000	41.336	0.000	0.000	48.119	34.174	-1.414	XOMR2_OWSG MWD+IFR1+MS
13800.000	90.000	359.738	9510.000	42.065	0.000	48.637	0.000	42.065	0.000	0.000	48.642	34.187	-1.343	XOMR2_OWSG MWD+IFR1+MS
13900.000	90.000	359.738	9510.000	42.795	0.000	49.171	0.000	42.795	0.000	0.000	49.175	34.201	-1.277	XOMR2_OWSG MWD+IFR1+MS
14000.000	90.000	359.738	9510.000	43.527	0.000	49.714	0.000	43.527	0.000	0.000	49.718	34.216	-1.215	XOMR2_OWSG MWD+IFR1+MS
14100.000	90.000	359.738	9510.000	44.261	0.000	50.267	0.000	44.261	0.000	0.000	50.270	34.232	-1.157	XOMR2_OWSG MWD+IFR1+MS
14200.000	90.000	359.738	9510.000	44.997	0.000	50.829	0.000	44.997	0.000	0.000	50.832	34.248	-1.102	XOMR2_OWSG MWD+IFR1+MS
14300.000	90.000	359.738	9510.000	45.734	0.000	51.400	0.000	45.734	0.000	0.000	51.403	34.264	-1.051	XOMR2_OWSG MWD+IFR1+MS
14400.000	90.000	359.738	9510.000	46.473	0.000	51.980	0.000	46.473	0.000	0.000	51.982	34.281	-1.002	XOMR2_OWSG MWD+IFR1+MS
14500.000	90.000	359.738	9510.000	47.213	0.000	52.568	0.000	47.213	0.000	0.000	52.570	34.299	-0.957	XOMR2_OWSG MWD+IFR1+MS
14600.000	90.000	359.738	9510.000	47.955	0.000	53.164	0.000	47.955	0.000	0.000	53.166	34.318	-0.914	XOMR2_OWSG MWD+IFR1+MS
14700.000	90.000	359.738	9510.000	48.698	0.000	53.768	0.000	48.698	0.000	0.000	53.770	34.337	-0.874	XOMR2_OWSG MWD+IFR1+MS
14800.000	90.000	359.738	9510.000	49.442	0.000	54.380	0.000	49.442	0.000	0.000	54.381	34.356	-0.837	XOMR2_OWSG MWD+IFR1+MS
14900.000	90.000	359.738	9510.000	50.188	0.000	54.998	0.000	50.188	0.000	0.000	55.000	34.376	-0.801	XOMR2_OWSG MWD+IFR1+MS
15000.000	90.000	359.738	9510.000	50.935	0.000	55.624	0.000	50.935	0.000	0.000	55.626	34.397	-0.768	XOMR2_OWSG MWD+IFR1+MS
15100.000	90.000	359.738	9510.000	51.683	0.000	56.257	0.000	51.683	0.000	0.000	56.258	34.418	-0.736	XOMR2_OWSG MWD+IFR1+MS
15200.000	90.000	359.738	9510.000	52.432	0.000	56.896	0.000	52.432	0.000	0.000	56.897	34.440	-0.707	XOMR2_OWSG MWD+IFR1+MS
15300.000	90.000	359.738	9510.000	53.182	0.000	57.542	0.000	53.182	0.000	0.000	57.543	34.463	-0.679	XOMR2_OWSG MWD+IFR1+MS

Well Plan Report

15400.000	90.000	359.738	9510.000	53.933	0.000	58.194	0.000	53.933	0.000	0.000	58.195	34.486	-0.652	XOMR2_OWSG MWD+IFR1+MS
15500.000	90.000	359.738	9510.000	54.685	0.000	58.852	0.000	54.685	0.000	0.000	58.852	34.510	-0.627	XOMR2_OWSG MWD+IFR1+MS
15600.000	90.000	359.738	9510.000	55.438	0.000	59.515	0.000	55.438	0.000	0.000	59.516	34.534	-0.604	XOMR2_OWSG MWD+IFR1+MS
15700.000	90.000	359.738	9510.000	56.191	0.000	60.184	0.000	56.191	0.000	0.000	60.185	34.559	-0.581	XOMR2_OWSG MWD+IFR1+MS
15800.000	90.000	359.738	9510.000	56.946	0.000	60.859	0.000	56.946	0.000	0.000	60.859	34.585	-0.560	XOMR2_OWSG MWD+IFR1+MS
15900.000	90.000	359.738	9510.000	57.701	0.000	61.539	0.000	57.701	0.000	0.000	61.539	34.611	-0.540	XOMR2_OWSG MWD+IFR1+MS
16000.000	90.000	359.738	9510.000	58.458	0.000	62.223	0.000	58.458	0.000	0.000	62.224	34.638	-0.521	XOMR2_OWSG MWD+IFR1+MS
16100.000	90.000	359.738	9510.000	59.214	0.000	62.913	0.000	59.214	0.000	0.000	62.913	34.665	-0.504	XOMR2_OWSG MWD+IFR1+MS
16200.000	90.000	359.738	9510.000	59.972	0.000	63.607	0.000	59.972	0.000	0.000	63.608	34.693	-0.487	XOMR2_OWSG MWD+IFR1+MS
16300.000	90.000	359.738	9510.000	60.730	0.000	64.306	0.000	60.730	0.000	0.000	64.307	34.722	-0.471	XOMR2_OWSG MWD+IFR1+MS
16400.000	90.000	359.738	9510.000	61.489	0.000	65.010	0.000	61.489	0.000	0.000	65.010	34.751	-0.455	XOMR2_OWSG MWD+IFR1+MS
16500.000	90.000	359.738	9510.000	62.249	0.000	65.717	0.000	62.249	0.000	0.000	65.718	34.781	-0.441	XOMR2_OWSG MWD+IFR1+MS
16600.000	90.000	359.738	9510.000	63.009	0.000	66.429	0.000	63.009	0.000	0.000	66.429	34.811	-0.427	XOMR2_OWSG MWD+IFR1+MS
16700.000	90.000	359.738	9510.000	63.770	0.000	67.145	0.000	63.770	0.000	0.000	67.145	34.842	-0.414	XOMR2_OWSG MWD+IFR1+MS
16800.000	90.000	359.738	9510.000	64.532	0.000	67.865	0.000	64.532	0.000	0.000	67.865	34.874	-0.402	XOMR2_OWSG MWD+IFR1+MS
16900.000	90.000	359.738	9510.000	65.294	0.000	68.588	0.000	65.294	0.000	0.000	68.588	34.906	-0.390	XOMR2_OWSG MWD+IFR1+MS
17000.000	90.000	359.738	9510.000	66.056	0.000	69.315	0.000	66.056	0.000	0.000	69.315	34.939	-0.379	XOMR2_OWSG MWD+IFR1+MS
17100.000	90.000	359.738	9510.000	66.819	0.000	70.046	0.000	66.819	0.000	0.000	70.046	34.972	-0.369	XOMR2_OWSG MWD+IFR1+MS
17200.000	90.000	359.738	9510.000	67.583	0.000	70.780	0.000	67.583	0.000	0.000	70.780	35.006	-0.359	XOMR2_OWSG MWD+IFR1+MS
17300.000	90.000	359.738	9510.000	68.347	0.000	71.517	0.000	68.347	0.000	0.000	71.517	35.040	-0.349	XOMR2_OWSG MWD+IFR1+MS

Well Plan Report

17400.000	90.000	359.738	9510.000	69.111	0.000	72.257	0.000	69.111	0.000	0.000	72.257	35.075	-0.340	XOMR2_OWSG MWD+IFR1+MS
17500.000	90.000	359.738	9510.000	69.876	0.000	73.001	0.000	69.876	0.000	0.000	73.001	35.111	-0.331	XOMR2_OWSG MWD+IFR1+MS
17600.000	90.000	359.738	9510.000	70.641	0.000	73.748	0.000	70.641	0.000	0.000	73.748	35.147	-0.323	XOMR2_OWSG MWD+IFR1+MS
17700.000	90.000	359.738	9510.000	71.407	0.000	74.497	0.000	71.407	0.000	0.000	74.497	35.184	-0.315	XOMR2_OWSG MWD+IFR1+MS
17800.000	90.000	359.738	9510.000	72.173	0.000	75.250	0.000	72.173	0.000	0.000	75.250	35.221	-0.308	XOMR2_OWSG MWD+IFR1+MS
17900.000	90.000	359.738	9510.000	72.940	0.000	76.005	0.000	72.940	0.000	0.000	76.005	35.259	-0.300	XOMR2_OWSG MWD+IFR1+MS
18000.000	90.000	359.738	9510.000	73.707	0.000	76.763	0.000	73.707	0.000	0.000	76.763	35.298	-0.294	XOMR2_OWSG MWD+IFR1+MS
18100.000	90.000	359.738	9510.000	74.474	0.000	77.523	0.000	74.474	0.000	0.000	77.523	35.337	-0.287	XOMR2_OWSG MWD+IFR1+MS
18200.000	90.000	359.738	9510.000	75.242	0.000	78.286	0.000	75.242	0.000	0.000	78.286	35.377	-0.281	XOMR2_OWSG MWD+IFR1+MS
18300.000	90.000	359.738	9510.000	76.010	0.000	79.051	0.000	76.010	0.000	0.000	79.051	35.417	-0.275	XOMR2_OWSG MWD+IFR1+MS
18400.000	90.000	359.738	9510.000	76.778	0.000	79.819	0.000	76.778	0.000	0.000	79.819	35.458	-0.269	XOMR2_OWSG MWD+IFR1+MS
18500.000	90.000	359.738	9510.000	77.547	0.000	80.589	0.000	77.547	0.000	0.000	80.589	35.499	-0.264	XOMR2_OWSG MWD+IFR1+MS
18600.000	90.000	359.738	9510.000	78.316	0.000	81.362	0.000	78.316	0.000	0.000	81.362	35.541	-0.259	XOMR2_OWSG MWD+IFR1+MS
18700.000	90.000	359.738	9510.000	79.085	0.000	82.136	0.000	79.085	0.000	0.000	82.136	35.583	-0.254	XOMR2_OWSG MWD+IFR1+MS
18800.000	90.000	359.738	9510.000	79.855	0.000	82.913	0.000	79.855	0.000	0.000	82.913	35.626	-0.249	XOMR2_OWSG MWD+IFR1+MS
18900.000	90.000	359.738	9510.000	80.625	0.000	83.691	0.000	80.625	0.000	0.000	83.691	35.670	-0.245	XOMR2_OWSG MWD+IFR1+MS
19000.000	90.000	359.738	9510.000	81.395	0.000	84.472	0.000	81.395	0.000	0.000	84.472	35.714	-0.240	XOMR2_OWSG MWD+IFR1+MS
19100.000	90.000	359.738	9510.000	82.166	0.000	85.255	0.000	82.166	0.000	0.000	85.255	35.759	-0.236	XOMR2_OWSG MWD+IFR1+MS
19200.000	90.000	359.738	9510.000	82.936	0.000	86.039	0.000	82.936	0.000	0.000	86.039	35.804	-0.232	XOMR2_OWSG MWD+IFR1+MS
19300.000	90.000	359.738	9510.000	83.707	0.000	86.826	0.000	83.707	0.000	0.000	86.826	35.850	-0.229	XOMR2_OWSG MWD+IFR1+MS

Well Plan Report

19400.000	90.000	359.738	9510.000	84.479	0.000	87.614	0.000	84.479	0.000	0.000	87.614	35.896	-0.225	XOMR2_OWSG MWD+IFR1+MS
19500.000	90.000	359.738	9510.000	85.250	0.000	88.404	0.000	85.250	0.000	0.000	88.404	35.943	-0.222	XOMR2_OWSG MWD+IFR1+MS
19600.000	90.000	359.738	9510.000	86.022	0.000	89.195	0.000	86.022	0.000	0.000	89.196	35.990	-0.218	XOMR2_OWSG MWD+IFR1+MS
19700.000	90.000	359.738	9510.000	86.794	0.000	89.989	0.000	86.794	0.000	0.000	89.989	36.038	-0.215	XOMR2_OWSG MWD+IFR1+MS
19800.000	90.000	359.738	9510.000	87.566	0.000	90.784	0.000	87.566	0.000	0.000	90.784	36.087	-0.212	XOMR2_OWSG MWD+IFR1+MS
19900.000	90.000	359.738	9510.000	88.339	0.000	91.580	0.000	88.339	0.000	0.000	91.580	36.136	-0.209	XOMR2_OWSG MWD+IFR1+MS
20000.000	90.000	359.738	9510.000	89.111	0.000	92.378	0.000	89.111	0.000	0.000	92.378	36.185	-0.207	XOMR2_OWSG MWD+IFR1+MS
20100.000	90.000	359.738	9510.000	89.884	0.000	93.178	0.000	89.884	0.000	0.000	93.178	36.235	-0.204	XOMR2_OWSG MWD+IFR1+MS
20200.000	90.000	359.738	9510.000	90.657	0.000	93.979	0.000	90.657	0.000	0.000	93.979	36.286	-0.202	XOMR2_OWSG MWD+IFR1+MS
20300.000	90.000	359.738	9510.000	91.430	0.000	94.781	0.000	91.430	0.000	0.000	94.781	36.337	-0.199	XOMR2_OWSG MWD+IFR1+MS
20400.000	90.000	359.738	9510.000	92.204	0.000	95.585	0.000	92.204	0.000	0.000	95.585	36.389	-0.197	XOMR2_OWSG MWD+IFR1+MS
20500.000	90.000	359.738	9510.000	92.977	0.000	96.390	0.000	92.977	0.000	0.000	96.390	36.441	-0.195	XOMR2_OWSG MWD+IFR1+MS
20600.000	90.000	359.738	9510.000	93.751	0.000	97.196	0.000	93.751	0.000	0.000	97.196	36.494	-0.193	XOMR2_OWSG MWD+IFR1+MS
20700.000	90.000	359.738	9510.000	94.525	0.000	98.004	0.000	94.525	0.000	0.000	98.004	36.547	-0.191	XOMR2_OWSG MWD+IFR1+MS
20800.000	90.000	359.738	9510.000	95.300	0.000	98.813	0.000	95.300	0.000	0.000	98.813	36.601	-0.189	XOMR2_OWSG MWD+IFR1+MS
20900.000	90.000	359.738	9510.000	96.074	0.000	99.623	0.000	96.074	0.000	0.000	99.623	36.655	-0.187	XOMR2_OWSG MWD+IFR1+MS
21000.000	90.000	359.738	9510.000	96.848	0.000	100.434	0.000	96.848	0.000	0.000	100.434	36.710	-0.185	XOMR2_OWSG MWD+IFR1+MS
21100.000	90.000	359.738	9510.000	97.623	0.000	101.247	0.000	97.623	0.000	0.000	101.247	36.765	-0.183	XOMR2_OWSG MWD+IFR1+MS
21200.000	90.000	359.738	9510.000	98.398	0.000	102.060	0.000	98.398	0.000	0.000	102.060	36.821	-0.182	XOMR2_OWSG MWD+IFR1+MS
21300.000	90.000	359.738	9510.000	99.173	0.000	102.875	0.000	99.173	0.000	0.000	102.875	36.877	-0.180	XOMR2_OWSG MWD+IFR1+MS

Well Plan Report

21400.000	90.000	359.738	9510.000	99.948	0.000	103.691	0.000	99.948	0.000	103.691	0.000	36.934	-0.179	XOMR2_OWSG MWD+IFR1+MS
21500.000	90.000	359.738	9510.000	100.724	0.000	104.508	0.000	100.724	0.000	104.508	0.000	36.991	-0.177	XOMR2_OWSG MWD+IFR1+MS
21600.000	90.000	359.738	9510.000	101.499	0.000	105.325	0.000	101.499	0.000	105.326	0.000	37.049	-0.176	XOMR2_OWSG MWD+IFR1+MS
21700.000	90.000	359.738	9510.000	102.275	0.000	106.144	0.000	102.275	0.000	106.144	0.000	37.107	-0.175	XOMR2_OWSG MWD+IFR1+MS
21800.000	90.000	359.738	9510.000	103.050	0.000	106.964	0.000	103.050	0.000	106.964	0.000	37.166	-0.173	XOMR2_OWSG MWD+IFR1+MS
21900.000	90.000	359.738	9510.000	103.826	0.000	107.785	0.000	103.826	0.000	107.785	0.000	37.225	-0.172	XOMR2_OWSG MWD+IFR1+MS
22000.000	90.000	359.738	9510.000	104.602	0.000	108.607	0.000	104.602	0.000	108.607	0.000	37.285	-0.171	XOMR2_OWSG MWD+IFR1+MS
22100.000	90.000	359.738	9510.000	105.378	0.000	109.429	0.000	105.378	0.000	109.430	0.000	37.345	-0.170	XOMR2_OWSG MWD+IFR1+MS
22200.000	90.000	359.738	9510.000	106.155	0.000	110.253	0.000	106.155	0.000	110.253	0.000	37.406	-0.169	XOMR2_OWSG MWD+IFR1+MS
22300.000	90.000	359.738	9510.000	106.931	0.000	111.077	0.000	106.931	0.000	111.078	0.000	37.467	-0.168	XOMR2_OWSG MWD+IFR1+MS
22400.000	90.000	359.738	9510.000	107.708	0.000	111.903	0.000	107.708	0.000	111.903	0.000	37.529	-0.167	XOMR2_OWSG MWD+IFR1+MS
22500.000	90.000	359.738	9510.000	108.484	0.000	112.729	0.000	108.484	0.000	112.729	0.000	37.591	-0.166	XOMR2_OWSG MWD+IFR1+MS
22600.000	90.000	359.738	9510.000	109.261	0.000	113.556	0.000	109.261	0.000	113.556	0.000	37.654	-0.165	XOMR2_OWSG MWD+IFR1+MS
22700.000	90.000	359.738	9510.000	110.038	0.000	114.384	0.000	110.038	0.000	114.384	0.000	37.717	-0.164	XOMR2_OWSG MWD+IFR1+MS
22800.000	90.000	359.738	9510.000	110.815	0.000	115.212	0.000	110.815	0.000	115.212	0.000	37.780	-0.164	XOMR2_OWSG MWD+IFR1+MS
22900.000	90.000	359.738	9510.000	111.592	0.000	116.041	0.000	111.592	0.000	116.042	0.000	37.844	-0.163	XOMR2_OWSG MWD+IFR1+MS
23000.000	90.000	359.738	9510.000	112.369	0.000	116.872	0.000	112.369	0.000	116.872	0.000	37.909	-0.162	XOMR2_OWSG MWD+IFR1+MS
23100.000	90.000	359.738	9510.000	113.146	0.000	117.702	0.000	113.146	0.000	117.702	0.000	37.974	-0.162	XOMR2_OWSG MWD+IFR1+MS
23200.000	90.000	359.738	9510.000	113.924	0.000	118.534	0.000	113.924	0.000	118.534	0.000	38.039	-0.161	XOMR2_OWSG MWD+IFR1+MS
23300.000	90.000	359.738	9510.000	114.701	0.000	119.366	0.000	114.701	0.000	119.366	0.000	38.105	-0.160	XOMR2_OWSG MWD+IFR1+MS

Well Plan Report

23400.000	90.000	359.738	9510.000	115.479	0.000	120.199	0.000	120.199	38.172	-0.160	XOMR2_OWSG MWD+IFR1+MS
23500.000	90.000	359.738	9510.000	116.257	0.000	121.033	0.000	121.033	38.238	-0.159	XOMR2_OWSG MWD+IFR1+MS
23600.000	90.000	359.738	9510.000	117.034	0.000	121.867	0.000	121.867	38.306	-0.159	XOMR2_OWSG MWD+IFR1+MS
23645.600	90.000	359.738	9510.000	117.389	0.000	122.247	0.000	122.247	38.336	-0.158	XOMR2_OWSG MWD+IFR1+MS
23700.000	90.000	359.738	9510.000	117.812	0.000	122.701	0.000	122.701	38.373	-0.158	XOMR2_OWSG MWD+IFR1+MS
23735.604	90.000	359.738	9510.000	118.089	0.000	122.998	0.000	122.998	38.398	-0.158	XOMR2_OWSG MWD+IFR1+MS

Poker Lake Unit 20-8 BD 208H

Plan Targets		Poker Lake Unit 20-8 BD 208H								
Target Name		Measured Depth			Grid Northing			Grid Easting		
		(ft)			(ft)			(ft)		
FTP 8		10542.86			403457.60			634686.20		
LTP 8		23645.60			416560.20			634626.30		
BHL 8		23735.60			416650.20			634626.00		
								TVD MSL Target Shape		
								(ft)		
								6280.00 CIRCLE		
								6280.00 CIRCLE		
								6280.00 CIRCLE		

Cement Variance Request

Intermediate Casing:

XTO requests to pump a two stage cement job on the 7-5/8" intermediate casing string with the first stage being pumped conventionally with the calculated top of cement at the Brush Canyon (6196') and the second stage performed as a bradenhead squeeze with planned cement from the Brushy Canyon to surface. If cement is not visually confirmed to circulate to surface, the final cement top after the second stage job will be verified by Echo-meter. If necessary, a top out consisting of 1,500 sack of Class C cement + 3% Salt + 1% PreMag-M + 6% Bentonite Gel (2.30 yld, 12.91 ppg) will be executed as a contingency. If cement is still unable to circulate to surface, another Echo-meter run will be performed for cement top verification.


XTO will report to the BLM the volume of fluid (limited to 5 bbls) used to flush intermediate casing valves following backside cementing procedures.

XTO requests to pump an Optional Lead if well conditions dictate in an attempt to bring cement inside the first intermediate casing. If cement reaches the desired height, the BLM will be notified and the second stage bradenhead squeeze and subsequent TOC verification will be negated.

XTO requests the option to conduct the bradenhead squeeze and TOC verification offline as per standard approval from BLM when unplanned remediation is needed and batch drilling is approved. In the event the bradenhead is conducted, we will ensure the first stage cement job is cemented properly and the well is static with floats holding and no pressure on the csg annulus as with all other casing strings where batch drilling operations occur before moving off the rig. The TA cap will also be installed per Cactus procedure and pressure inside the casing will be monitored via the valve on the TA cap as per standard batch drilling ops.

Production Casing:

XTO requests the option to offline cement and remediate (if needed) surface and intermediate casing strings where batch drilling is approved and if unplanned remediation is needed. XTO will ensure well is static with no pressure on the csg annulus, as with all other casing strings where batch drilling operations occur before moving off the rig. The TA cap will also be installed when applicable per Cactus procedure and pressure inside the casing will be monitored via the valve on the TA cap as per standard batch drilling ops. Offline cement operations will then be conducted after the rig is moved off the current well to the next well in the batch sequence.

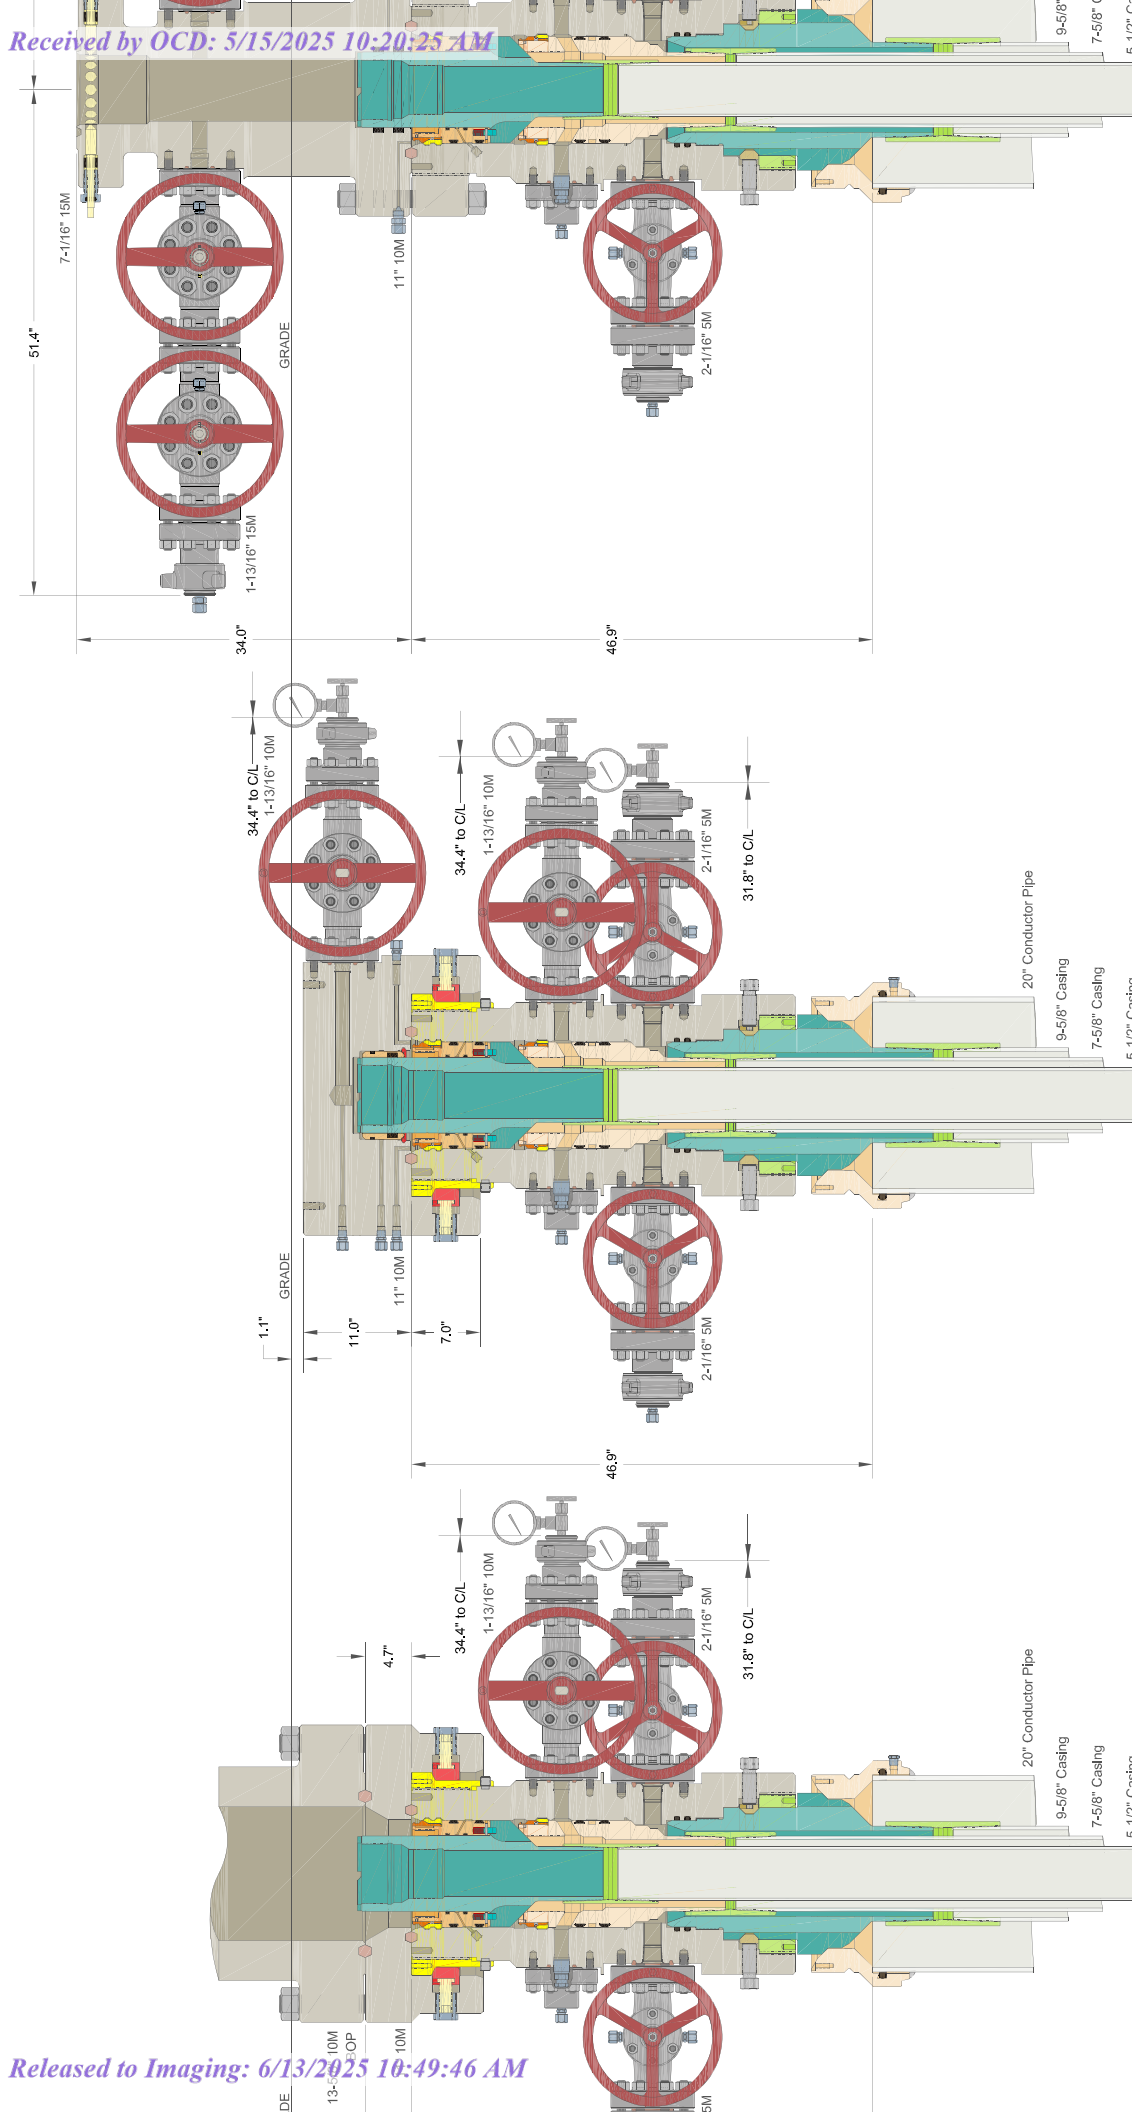

State of New Mexico
Energy, Minerals and Natural Resources Department

Submit Electronically
Via E-permitting

Oil Conservation Division
1220 South St. Francis Dr.
Santa Fe, NM 87505

NATURAL GAS MANAGEMENT PLAN

This Natural Gas Management Plan must be submitted with each Application for Permit to Drill (APD) for a new or recompleted well.

Section 1 – Plan Description

Effective May 25, 2021

I. Operator: XTO Permian Operating **OGRID:** 373075 **Date:** 07 / 29 / 2024

II. Type: ☒ Original ☐ Amendment due to ☐ 19.15.27.9.D(6)(a) NMAC ☐ 19.15.27.9.D(6)(b) NMAC ☐ Other.

If Other, please describe: _____

III. Well(s): Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	API	ULSTR	Footages	Anticipated Oil BBL/D	3 yr Anticipated decline Oil BBL/D	Anticipated Gas MCF/D	3 yr Anticipated decline Gas MCF/D	Anticipated Produced Water BBL/D	3 yr Anticipated decline Water BBL/D
Poker Lake Unit 20-17 BD 201	TBD	20 T25S R30E	1434 FSL; 1904 FWL	500	125	1,500	900	1,250	400
Poker Lake Unit 20-17 BD 202	TBD	20 T25S R30E	1433 FSL; 1934 FWL	1,100	125	2,750	900	3,750	700
Poker Lake Unit 20-17 BD 203	TBD	20 T25S R30E	1432 FSL; 1964 FWL	500	125	1,500	900	1,250	400
Poker Lake Unit 20-17 BD 204	TBD	20 T25S R30E	1431 FSL; 1994 FWL	1,200	175	3,000	1,200	4,250	900
Poker Lake Unit 20-8 BD 205	TBD	20 T25S R30E	1430 FSL; 2024 FWL	600	150	1,750	1,000	1,500	400
Poker Lake Unit 20-8 BD 206	TBD	20 T25S R30E	1813 FSL; 1604 FEL	1,200	175	3,000	1,200	4,250	900
Poker Lake Unit 20-8 BD 207	TBD	20 T25S R30E	1813 FSL; 1574 FEL	600	150	1,750	1,000	1,500	400
Poker Lake Unit 20-8 BD 208	TBD	20 T25S R30E	1813 FSL; 1544 FEL	1,200	175	3,000	1,200	4,250	900
Poker Lake Unit 20-8 BD 209	TBD	20 T25S R30E	1813 FSL; 1514 FEL	1,300	200	3,500	1,400	4,750	1,100

Poker Lake Unit 20-8 BD 210	TBD	20 T25S R30E	1813 FSL; 1484 FEL	600	75	7,250	2,700	4,750	900
Poker Lake Unit 18-30 BD 200H	TBD	18 T25S R30E	265 FNL; 2395 FEL	1,200	175	3,000	1,200	4,250	900
Poker Lake Unit 18-30 BD 201H	TBD	18 T25S R30E	265 FNL; 2365 FEL	600	150	1,750	1,000	1,500	400
Poker Lake Unit 18-30 BD 202H	TBD	18 T25S R30E	265 FNL; 2335 FEL	1,200	175	3,000	1,200	4,250	900
Poker Lake Unit 18-30 BD 203H	TBD	18 T25S R30E	265 FNL; 2305 FEL	600	150	1,750	1,000	1,500	400
Poker Lake Unit 18-19 BD 204H	TBD	18 T25S R30E	265 FNL; 2275 FEL	1,100	125	2,750	900	3,750	700
Poker Lake Unit 18-19 BD 205H	TBD	18 T25S R30E	265 FNL; 1935 FEL	500	125	1,500	900	1,250	400
Poker Lake Unit 18-19 BD 206H	TBD	18 T25S R30E	265 FNL; 1905 FEL	1,100	125	2,750	900	3,750	700
Poker Lake Unit 18-19 BD 207H	TBD	18 T25S R30E	265 FNL; 1875 FEL	500	125	1,500	900	1,250	400
Poker Lake Unit 18-19 BD 208H	TBD	18 T25S R30E	265 FNL; 1845 FEL	1,100	125	2,750	900	3,750	700
Poker Lake Unit 18-19 BD 209H	TBD	18 T25S R30E	265 FNL; 1815 FEL	500	50	5,500	1,700	4,000	600

IV. Central Delivery Point Name:__PLU Brushy Draw 18 (PLU 18-30/18-19) and PLU Brushy Draw 20 (PLU 20-17/20-8)
[See 19.15.27.9(D)(1) NMAC]

V. Anticipated Schedule: Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	API	Spud Date	TD Reached Date	Completion Commencement Date	Initial Flow Back Date	First Production Date
Poker Lake Unit 20-17 BD 201	TBD	August 2025	TBD	TBD	TBD	TBD
Poker Lake Unit 20-17 BD 202	TBD	August 2025	TBD	TBD	TBD	TBD
Poker Lake Unit 20-17 BD 203	TBD	August 2025	TBD	TBD	TBD	TBD
Poker Lake Unit 20-17 BD 204	TBD	August 2025	TBD	TBD	TBD	TBD
Poker Lake Unit 20-8 BD 205	TBD	August 2025	TBD	TBD	TBD	TBD
Poker Lake Unit 20-8 BD 206	TBD	August 2025	TBD	TBD	TBD	TBD
Poker Lake Unit 20-8 BD 207	TBD	August 2025	TBD	TBD	TBD	TBD

Poker Lake Unit 20-8 BD 208	TBD	August 2025	TBD	TBD	TBD	TBD
Poker Lake Unit 20-8 BD 209	TBD	August 2025	TBD	TBD	TBD	TBD
Poker Lake Unit 20-8 BD 210	TBD	August 2025	TBD	TBD	TBD	TBD
Poker Lake Unit 18-30 BD 200H	TBD	October 2025	TBD	TBD	TBD	TBD
Poker Lake Unit 18-30 BD 201H	TBD	October 2025	TBD	TBD	TBD	TBD
Poker Lake Unit 18-30 BD 202H	TBD	October 2025	TBD	TBD	TBD	TBD
Poker Lake Unit 18-30 BD 203H	TBD	October 2025	TBD	TBD	TBD	TBD
Poker Lake Unit 18-19 BD 204H	TBD	October 2025	TBD	TBD	TBD	TBD
Poker Lake Unit 18-19 BD 205H	TBD	October 2025	TBD	TBD	TBD	TBD
Poker Lake Unit 18-19 BD 206H	TBD	October 2025	TBD	TBD	TBD	TBD
Poker Lake Unit 18-19 BD 207H	TBD	October 2025	TBD	TBD	TBD	TBD
Poker Lake Unit 18-19 BD 208H	TBD	October 2025	TBD	TBD	TBD	TBD
Poker Lake Unit 18-19 BD 209H	TBD	October 2025	TBD	TBD	TBD	TBD

VI. Separation Equipment: ☐ Attach a complete description of how Operator will size separation equipment to optimize gas capture.

VII. Operational Practices: ☐ Attach a complete description of the actions Operator will take to comply with the requirements of Subsection A through F of 19.15.27.8 NMAC.

VIII. Best Management Practices: ☐ Attach a complete description of Operator's best management practices to minimize venting during active and planned maintenance.

Section 2 – Enhanced Plan

EFFECTIVE APRIL 1, 2022

Beginning April 1, 2022, an operator that is not in compliance with its statewide natural gas capture requirement for the applicable reporting area must complete this section.

☒ Operator certifies that it is not required to complete this section because Operator is in compliance with its statewide natural gas capture requirement for the applicable reporting area.

IX. Anticipated Natural Gas Production:

Well	API	Anticipated Average Natural Gas Rate MCF/D	Anticipated Volume of Natural Gas for the First Year MCF

X. Natural Gas Gathering System (NGGS):

Operator	System	ULSTR of Tie-in	Anticipated Gathering Start Date	Available Maximum Daily Capacity of System Segment Tie-in

XI. Map. ☐ Attach an accurate and legible map depicting the location of the well(s), the anticipated pipeline route(s) connecting the production operations to the existing or planned interconnect of the natural gas gathering system (s), and the maximum daily capacity of the segment or portion of the natural gas gathering system(s) to which the well(s) will be connected.

XII. Line Capacity. The natural gas gathering system ☐ will ☐ will not have capacity to gather 100% of the anticipated natural gas production volume from the well prior to the date of first production.

XIII. Line Pressure. Operator ☐ does ☐ does not anticipate that its existing well(s) connected to the same segment, or portion, of the natural gas gathering system(s) described above will continue to meet anticipated increases in line pressure caused by the new well(s).

☐ Attach Operator's plan to manage production in response to the increased line pressure.

XIV. Confidentiality: ☐ Operator asserts confidentiality pursuant to Section 71-2-8 NMSA 1978 for the information provided in Section 2 as provided in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and attaches a full description of the specific information for which confidentiality is asserted and the basis for such assertion.

Section 3 - Certifications

Effective May 25, 2021

Operator certifies that, after reasonable inquiry and based on the available information at the time of submittal:

☒ Operator will be able to connect the well(s) to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system; or

☐ Operator will not be able to connect to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system.

If Operator checks this box, Operator will select one of the following:

Well Shut-In. ☒ Operator will shut-in and not produce the well until it submits the certification required by Paragraph (4) of Subsection D of 19.15.27.9 NMAC; or

Venting and Flaring Plan. ☐ Operator has attached a venting and flaring plan that evaluates and selects one or more of the potential alternative beneficial uses for the natural gas until a natural gas gathering system is available, including:

- (a) power generation on lease;
- (b) power generation for grid;
- (c) compression on lease;
- (d) liquids removal on lease;
- (e) reinjection for underground storage;
- (f) reinjection for temporary storage;
- (g) reinjection for enhanced oil recovery;
- (h) fuel cell production; and
- (i) other alternative beneficial uses approved by the division.

Section 4 - Notices


1. If, at any time after Operator submits this Natural Gas Management Plan and before the well is spud:


(a) Operator becomes aware that the natural gas gathering system it planned to connect the well(s) to has become unavailable or will not have capacity to transport one hundred percent of the production from the well(s), no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised venting and flaring plan containing the information specified in Paragraph (5) of Subsection D of 19.15.27.9 NMAC; or

(b) Operator becomes aware that it has, cumulatively for the year, become out of compliance with its baseline natural gas capture rate or natural gas capture requirement, no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised Natural Gas Management Plan for each well it plans to spud during the next 90 days containing the information specified in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and shall file an update for each Natural Gas Management Plan until Operator is back in compliance with its baseline natural gas capture rate or natural gas capture requirement.

2. OCD may deny or conditionally approve an APD if Operator does not make a certification, fails to submit an adequate venting and flaring plan which includes alternative beneficial uses for the anticipated volume of natural gas produced, or if OCD determines that Operator will not have adequate natural gas takeaway capacity at the time a well will be spud.

I certify that, after reasonable inquiry, the statements in and attached to this Natural Gas Management Plan are true and correct to the best of my knowledge and acknowledge that a false statement may be subject to civil and criminal penalties under the Oil and Gas Act.

Signature: 
Printed Name:
Title:
E-mail Address:
Date:
Phone:
OIL CONSERVATION DIVISION (Only applicable when submitted as a standalone form)
Approved By:
Title:
Approval Date:
Conditions of Approval:

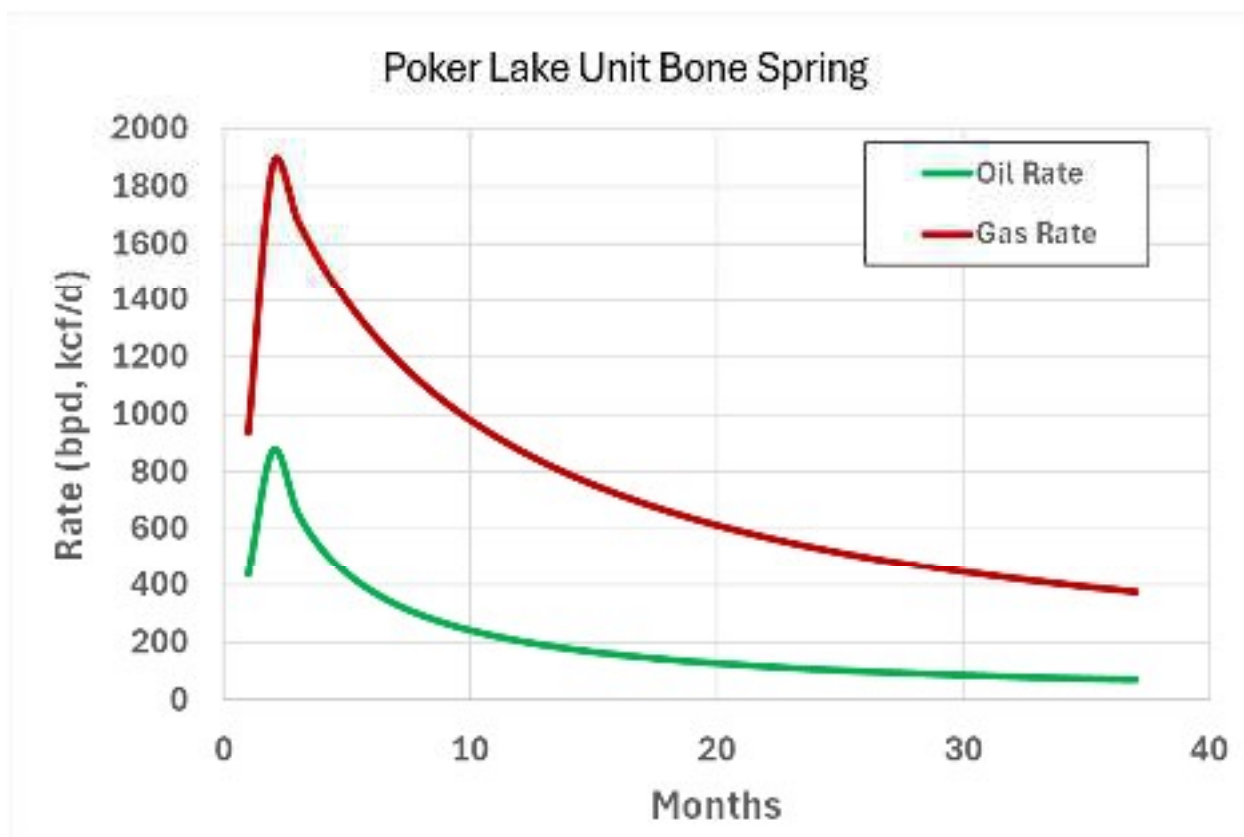

VI. Separation Equipment:

XTO Permian Operating LLC. utilizes a "stage separation" process in which oil and gas separation is carried out through a series of separators operating at successively reduced pressures. Hydrocarbon liquids are produced into a high-pressure inlet separator, then carried through one or more lower pressure separation vessels before entering the storage tanks. The purpose of this separation process is to attain maximum recovery of liquid hydrocarbons from the fluids and allow maximum capture of produced gas into the sales pipeline. XTO utilizes a series of Low-Pressure Compression units to capture gas off the staged separation and send it to the sales pipeline. This process minimizes the amount of flash gas that enters the end-stage storage tanks that is subsequently vented or flared.

VII. Operational Practices

XTO Permian Operating LLC will employ best management practices and control technologies to maximize the recovery and minimize waste of natural gas through venting and flaring.


- During drilling operations, XTO will utilize flares to capture and control natural gas, where technically feasible. If flaring is deemed technically in-feasible, XTO will employ best management practices to minimize or reduce venting to the extent possible.
- During completions operations, XTO will utilize Green Completion methods to capture gas produced during well completions that is otherwise vented or flared. If capture is technically in-feasible, flares will be used to control flow back fluids entering into frac tanks during initial flowback. Upon indication of first measurable hydrocarbon volumes, XTO Permian Operating LLC will turn operations to onsite separation vessels and flow to the gathering pipeline.
- During production operations, XTO Permian Operating LLC will take every practical effort to minimize waste of natural gas through venting and flaring by:
 - Designing and constructing facilities in a manner consistent to achieve maximum capture and control of hydrocarbon liquids & produced gas
 - Utilizing a closed-loop capture system to collect, and route produced gas to sales line via low pressure compression, or to a flare/combustor
 - Flaring in lieu of venting, where technically feasible
 - Utilizing auto-ignitors or continuous pilots, with thermocouples connected to Scada, to quickly detect and resolve issues related to malfunctioning flares/combustors
 - Employ the use of automatic tank gauging to minimize storage tank venting during loading events
 - Installing air-driven or electric-driven pneumatics & combustion engines, where technically feasible to minimize venting to the atmosphere
 - Confirm equipment is properly maintained and repaired through a preventative maintenance and repair program to ensure equipment meets all manufacturer specifications

- Conduct and document AVO inspections on the frequency set forth in Part 27 to detect and repair any onsite leaks as quickly and efficiently as is feasible.



VIII. Best Management Practices during Maintenance

XTO Permian Operating LLC. will utilize best management practices to minimize venting during active and planned maintenance activities. XTO is operating under guidance that production facilities permitted under NOI permits have no provisions to allow high pressure flaring and high-pressure flaring is only allowed in disruption scenarios so long as the duration is less than eight hours. When technically feasible, flaring during maintenance activities will be utilized in lieu of venting to the atmosphere. XTO will work with third-party operators during scheduled maintenance of downstream pipeline or processing plants to address those events ahead of time to minimize venting. Actions considered include identifying alternative capture approaches or planning to temporarily reduce production or shut in the well to address these circumstances.

H2S Briefing Areas and Alarm Locations Pad B

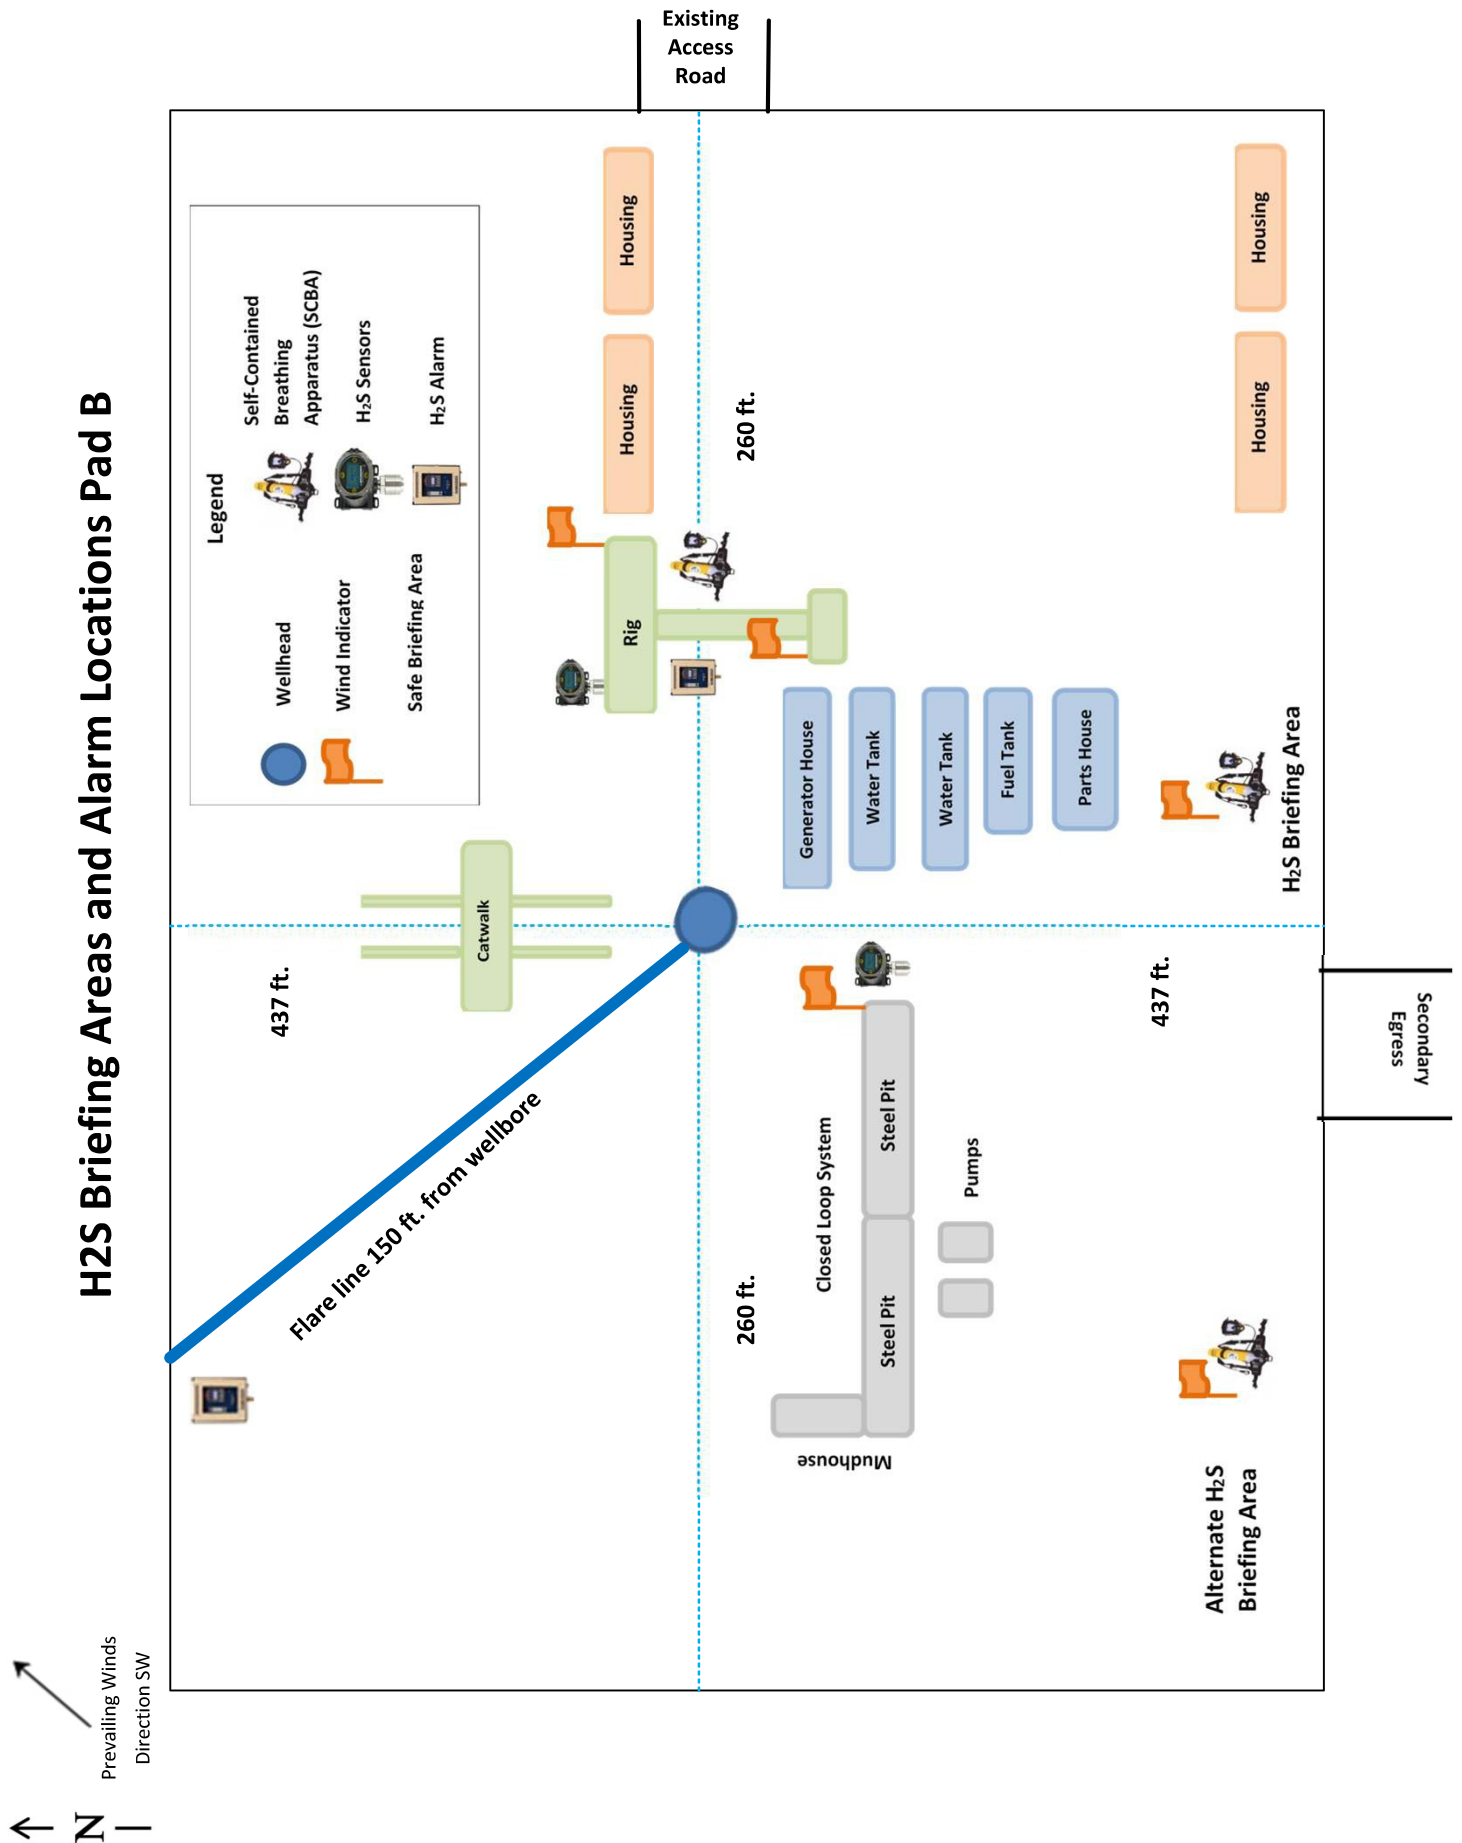

H2S Briefing Areas and Alarm Locations Pad D

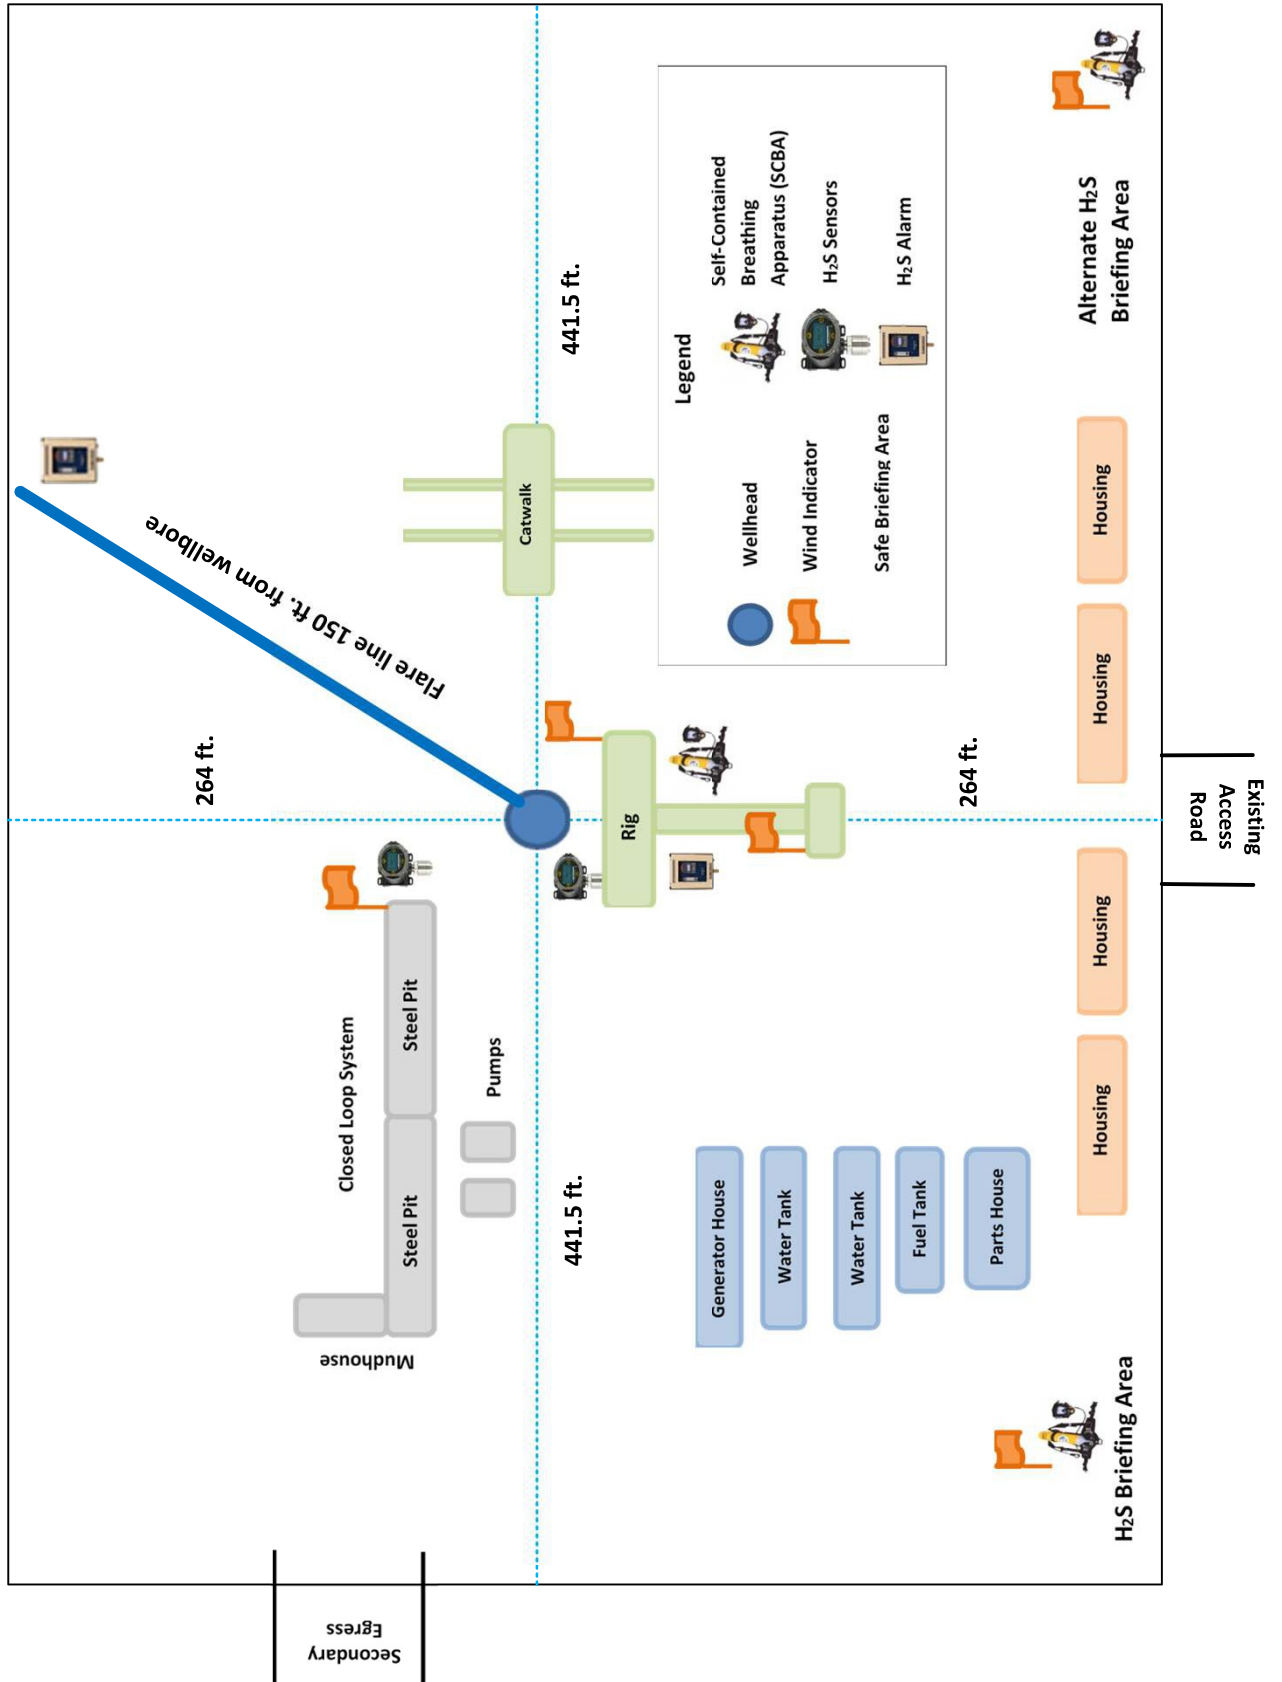

Subject: Request for a Variance Allowing break Testing of the Blowout Preventer Equipment (BOPE)

XTO Energy requests a variance to ONLY test broken pressure seals on the BOPE and function test BOP when skidding a drilling rig between multiple wells on a pad.

Background

Onshore Oil and Gas Order CFR Title 43 Part 3170, Drilling Operations, Sections III.A.2.i.iv.B states that the BOP test must be performed whenever any seal subject to test pressure is broken. The current interpretation of the Bureau of Land Management (BLM) requires a complete BOP test and not just a test of the affected component. CFR Title 43 Part 3170 states, "Some situation may exist either on a well-by-well basis or field-wide basis whereby it is commonly accepted practice to vary a particular minimum standard(s) established in this order. This situation can be resolved by requesting a variance...". XTO Energy feels the break testing the BOPE is such a situation. Therefore, as per CFR Title 43 Part 3170, XTO Energy submits this request for the variance.

Supporting Documentation

CFR Title 43 Part 3170 became effective on December 19, 1988 and has remained the standard for regulating BLM onshore drilling operations for over 30 years. During this time there have been significant changes in drilling technology. BLM continues to use the variance request process to allow for the use of modern technology and acceptable engineering practices that have arisen since CFR Title 43 Part 3170 was originally released. The XTO Energy drilling rig fleet has many modern upgrades that allow the intact BOP stack to be moved between well slots on a multi-well pad, as well as, wellhead designs that incorporate quick connects facilitating release of the BOP from the wellhead without breaking any BOP stack components apart. These technologies have been used extensively offshore, and other regulators, API, and many operators around the world have endorsed break testing as safe and reliable.

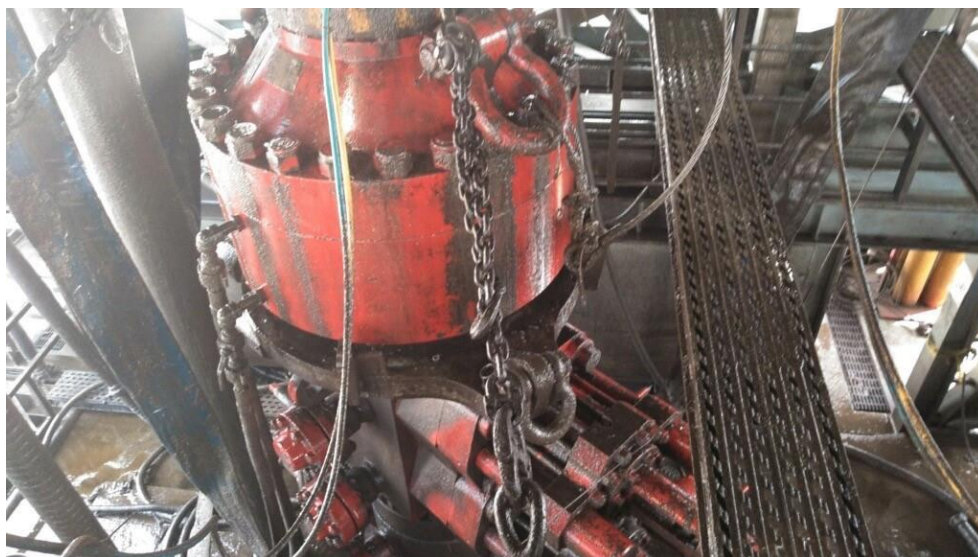


Figure 1: Winch System attached to BOP Stack

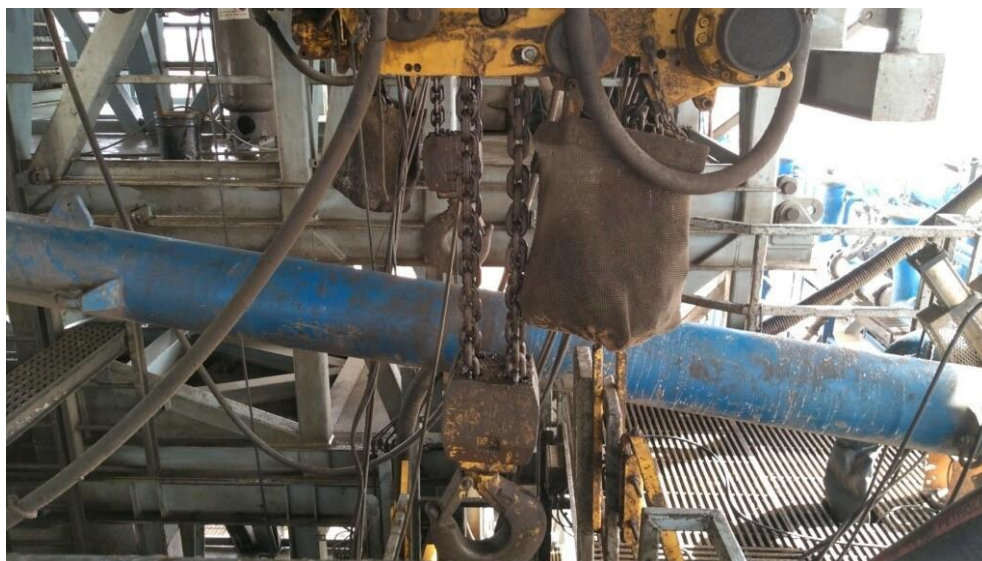


Figure 2: BOP Winch System

American Petroleum Institute (API) standards, specification and recommended practices are considered the industry standard and are consistently utilized and referenced by the industry. CFR Title 43 Part 3170 recognizes API recommended Practices (RP) 53 in its original development. API Standard 53, *Well Control Equipment Systems for Drilling Wells* (Fifth Edition, December 2018, Annex C, Table C.4) recognizes break testing as an acceptable practice. Specifically, API Standard 53, Section 5.3.7.1 states “A pressure test of the pressure containing component shall be performed following the disconnection or repair, limited to the affected component.” See Table C.4 below for reference.

62

API STANDARD 53

Table C.4—Initial Pressure Testing, Surface BOP Stacks

Component to be Pressure Tested	Pressure Test—Low Pressure ^{ac} psig (MPa)	Pressure Test—High Pressure ^{ac}	
		Change Out of Component, Elastomer, or Ring Gasket	No Change Out of Component, Elastomer, or Ring Gasket
Annular preventer ^b	250 to 350 (1.72 to 2.41)	RWP of annular preventer	MASP or 70% annular RWP, whichever is lower.
Fixed pipe, variable bore, blind, and BSR preventers ^{bd}	250 to 350 (1.72 to 2.41)	RWP of ram preventer or wellhead system, whichever is lower	ITP
Choke and kill line and BOP side outlet valves below ram preventers (both sides)	250 to 350 (1.72 to 2.41)	RWP of side outlet valve or wellhead system, whichever is lower	ITP
Choke manifold—upstream of chokes ^e	250 to 350 (1.72 to 2.41)	RWP of ram preventers or wellhead system, whichever is lower	ITP
Choke manifold—downstream of chokes ^e	250 to 350 (1.72 to 2.41)	RWP of valve(s), line(s), or MASP for the well program, whichever is lower	
Kelly, kelly valves, drill pipe safety valves, IBOPs	250 to 350 (1.72 to 2.41)	MASP for the well program	

^a Pressure test evaluation periods shall be a minimum of five minutes.

No visible leaks.

The pressure shall remain stable during the evaluation period. The pressure shall not decrease below the intended test pressure.

^b Annular(s) and VBR(s) shall be pressure tested on the largest and smallest OD drill pipe to be used in well program.

^c For pad drilling operations, moving from one wellhead to another within the 21 days, pressure testing is required for pressure-containing and pressure-controlling connections when the integrity of a pressure seal is broken.

^d For surface offshore operations, the ram BOPs shall be pressure tested with the ram locks engaged and the closing and locking pressure vented during the initial test. For land operations, the ram BOPs shall be pressure tested with the ram locks engaged and the closing and locking pressure vented at commissioning and annually.

^e Adjustable chokes are not required to be full sealing devices. Pressure testing against a closed choke is not required.

The Bureau of Safety and Environmental Enforcement (BSEE), Department of Interior, has also utilized the API standards, specification and best practices in the development of its offshore oil and gas regulations and incorporates them by reference within its regulations.

Break testing has been approved by the BLM in the past with other operators based on the detailed information provided in this document.


XTO Energy feels break testing and our current procedures meet the intent of CFR Title 43 Part 317 0and often exceed it. There has been no evidence that break testing results in more components failing than seen on full BOP tests. XTO Energy's internal standards requires complete BOPE tests more often than that of CFR Title 43 Part 3170 (Every 21 days). In addition to function testing the annular, pipe rams and blind rams after each BOP nipple up, XTO Energy performs a choke drill with the rig crew prior to drilling out every casing shoe. This is additional training for the rig crew that exceeds the requirements of the CFR Title 43 Part 3170.

Procedures

1. XTO Energy will use this document for our break testing plan for New Mexico Delaware basin. The summary below will be referenced in the APD or Sundry Notice and receive approval prior to implementing this variance.
2. XTO Energy will perform BOP break testing on multi-wells pads where multiple intermediate sections can be drilled and cased within the 21-day BOP test window.
 - a. A full BOP test will be conducted on the first well on the pad.
 - b. The first intermediate hole section drilled on the pad will be the deepest. All of the remaining hole sections will be the same depth or shallower.
 - i. Our Lower WC targets set the intermediate casing shoe no deeper than the Wolfcamp B.
 - ii. Our Upper WC targets set the intermediate casing shoe shallower than the Wolfcamp B.
 - c. A Full BOP test will be required if the intermediate hole section being drilled has a MASP over 5M.
 - d. A full BOP test will be required prior to drilling any production hole.
3. After performing a complete BOP test on the first well, the intermediate hole section will be drilled and cased, two breaks would be made on the BOP equipment.
 - a. Between the HCV valve and choke line connection
 - b. Between the BOP quick connect and the wellhead
4. The BOP is then lifted and removed from the wellhead by a hydraulic system.
5. After skidding to the next well, the BOP is moved to the wellhead by the same hydraulic system and installed.
6. The connections mentioned in 3a and 3b will then be reconnected.
7. Install test plug into the wellhead using test joint or drill pipe.
8. A shell test is performed against the upper pipe rams testing the two breaks.
9. The shell test will consist of a 250 psi low test and a high test to the value submitted in the APD or Sundry (e.g. 5,000 psi or 10,000psi).
10. Function test will be performed on the following components: lower pipe rams, blind rams, and annular.

11. For a multi-well pad the same two breaks on the BOP would be made and on the next wells and steps 4 through 10 would be repeated.
12. A second break test would only be done if the intermediate hole section being drilled could not be completed within the 21 day BOP test window.

Note: Picture below highlights BOP components that will be tested during batch operations

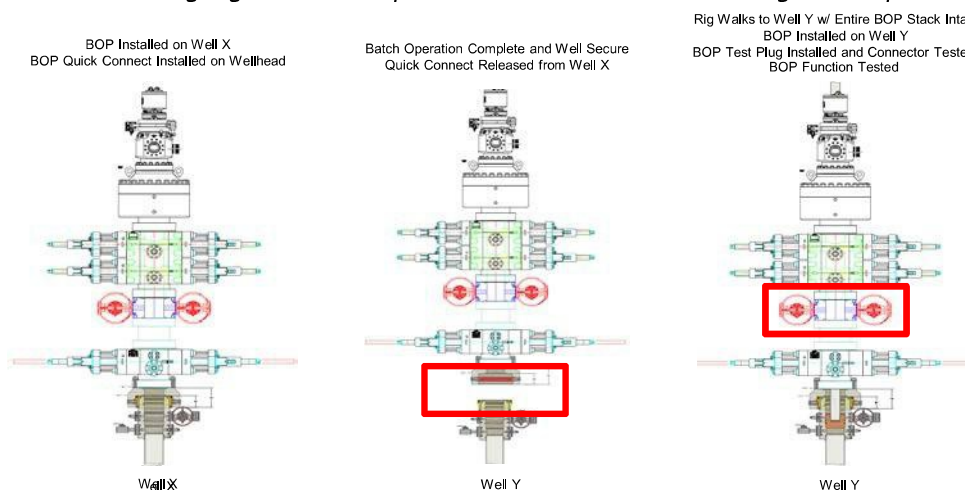


Summary

A variance is requested to **ONLY** test broken pressure seals on the BOP equipment when moving from wellhead to wellhead which is in compliance with API Standard 53. API Standard 53 states, that for pad drilling operation, moving from one wellhead to another within 21 days, pressure testing is required for pressure-containing and pressure-controlling connections when the integrity of a pressure seal is broken.

The BOP will be secured by a hydraulic carrier or cradle. The BLM will be contacted if a Well Control event occurs prior to the commencement of a BOPE Break Testing operation.

Based on discussions with the BLM on February 27th 2020 and the supporting documentation submitted to the BLM, we will request permission to **ONLY** retest broken pressure seals if the following conditions are met:

1. After a full BOP test is conducted on the first well on the pad.
2. The first intermediate hole section drilled on the pad will be the deepest. All of the remaining hole sections will be the same depth or shallower.
3. Full BOP test will be required if the intermediate hole section being drilled has a MASP over 5M.
4. Full BOP test will be required prior to drilling the production hole.

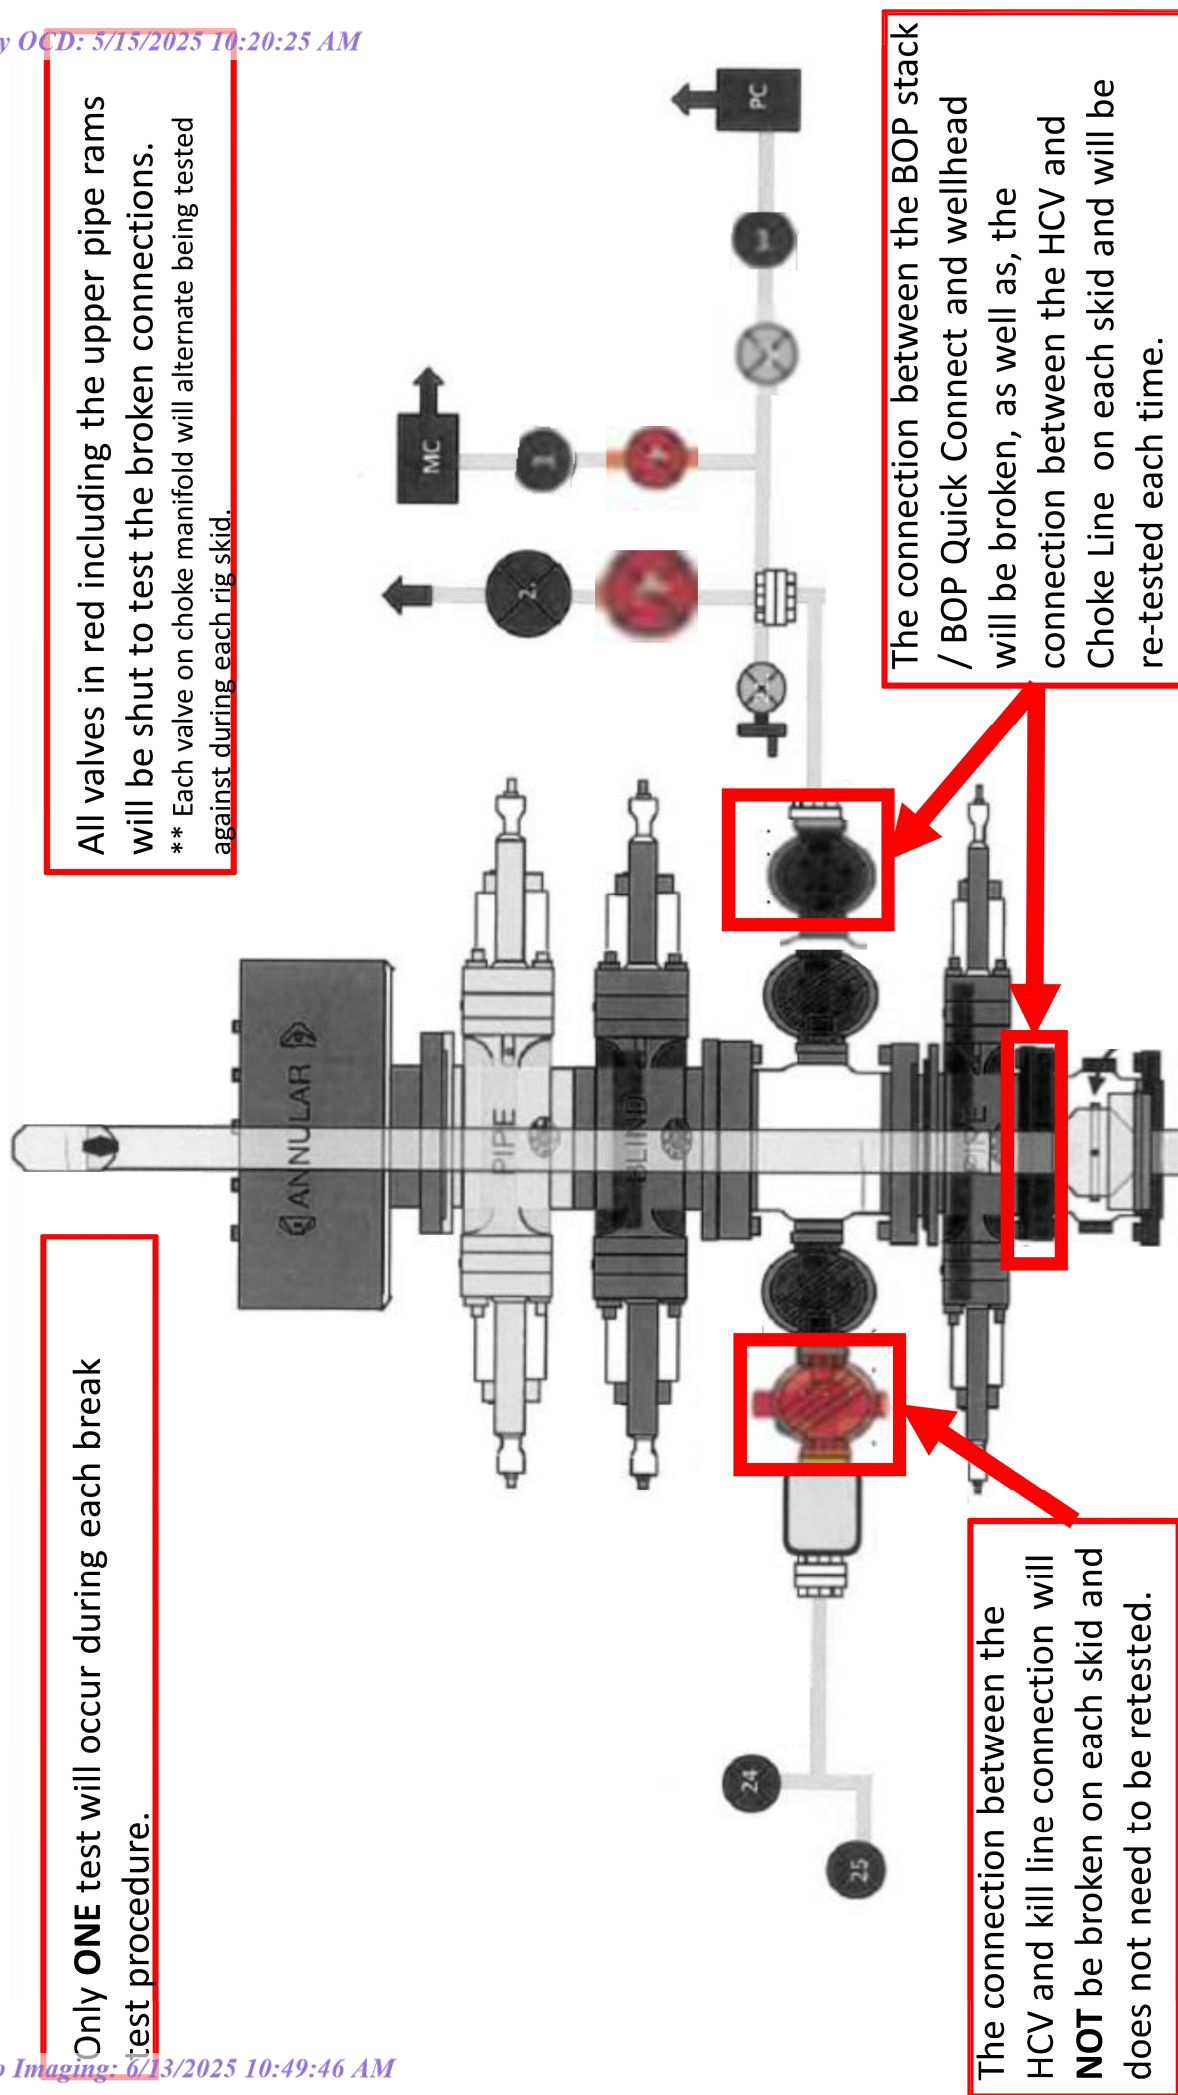

**BLACK GOLD®**

GATES ENGINEERING & SERVICES NORTH AMERICA
7603 Pralrie Oak Dr.
Houston, TX. 77086

PHONE: +1 (281) 602-4100**FAX: +1 (281) 602-4147****EMAIL: gesna.quality@gates.com****WEB: www.gates.com/oilandgas**

NEW CHOKE HOSE
INSTALLED 02-10-2024

CERTIFICATE OF CONFORMANCE

This is to verify that the items detailed below meet the requirements of the Customer's Purchase Order referenced herein, and are in Conformance with applicable specifications, and that Records of Required Tests are on file and subject to examination. The following items were inspected and hydrostatically tested at **Gates Engineering & Services North America** facilities in Houston, TX, USA.

CUSTOMER: NABORS DRILLING TECHNOLOGIES USA DBA NABORS DRILLING USA
CUSTOMER P.O.#: 15582803 (TAG NABORS PO #15582803 SN 74621 ASSET 66-1531)
CUSTOMER P/N: IMR RETEST SN 74621 ASSET #66-1531

PART DESCRIPTION: RETEST OF CUSTOMER 3" X 45 FT 16C CHOKE & KILL HOSE ASSEMBLY C/W 4 1/16" 10K FLANGES

SALES ORDER #: 529480
QUANTITY: 1
SERIAL #: 74621 H3-012524-1

SIGNATURE:*F. Cismos***TITLE:****QUALITY ASSURANCE****DATE:**

1/25/2024



H3-15/16

1/25/2024 11:48:06 AM

TEST REPORT

CUSTOMER

Company: Nabors Industries Inc.

Production description: 74621/66-1531

Sales order #: 529480

Customer reference: FG1213

TEST OBJECT

Serial number: H3-012524-1

Lot number:

Description: 74621/66-1531

Hose ID: 3" 16C CK

Part number:

TEST INFORMATION

Test procedure: GTS-04-053

Test pressure: 15000.00 psi

Test pressure hold: 3600.00 sec

Work pressure: 10000.00 psi

Work pressure hold: 900.00 sec

Length difference: 0.00 %

Length difference: 0.00 inch

Fitting 1: 3.0 x 4-1/16 10K

Part number:

Description:

Fitting 2: 3.0 x 4-1/16 10K

Part number:

Description:


Visual check:

Pressure test result: PASS

Length measurement result:

Length: 45 feet

Test operator: Travis

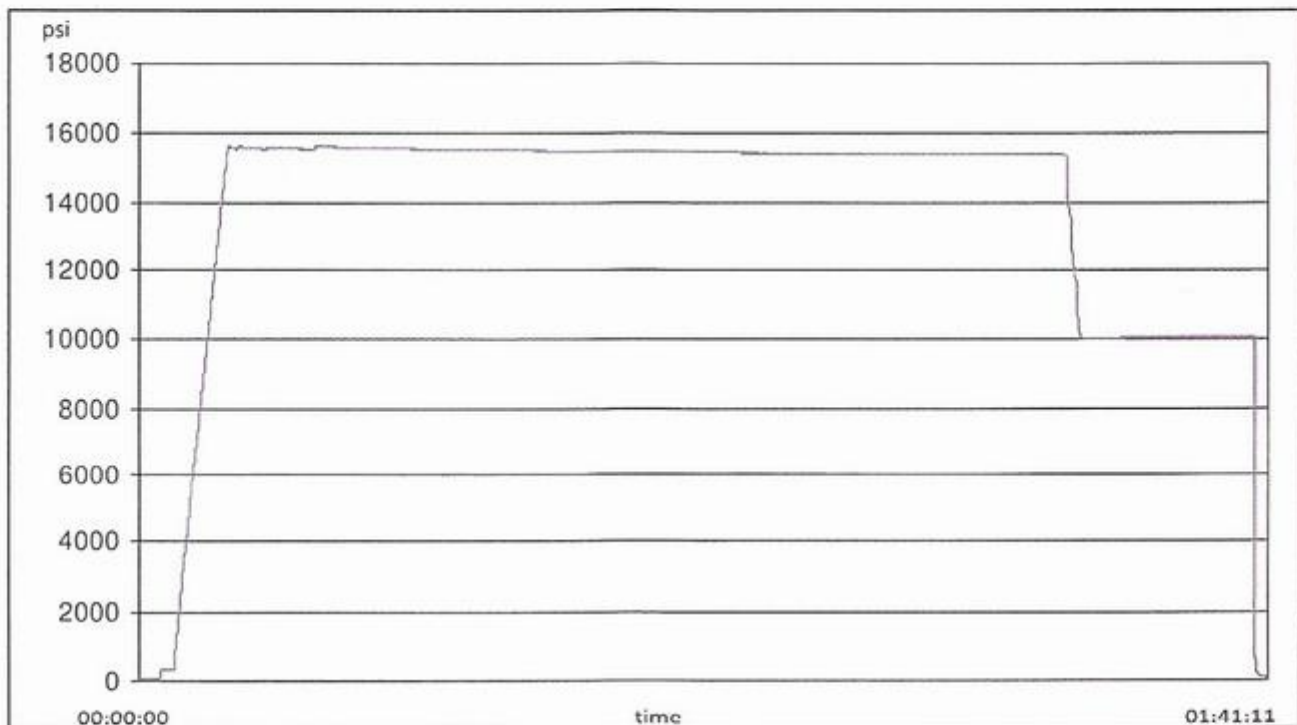



H3-15/16


1/25/2024 11:48:06 AM



TEST REPORT

GAUGE TRACEABILITY

Description	Serial number	Calibration date	Calibration due date
S-25-A-W	110D3PHO	2023-06-06	2024-06-06
S-25-A-W	110IQWDG	2023-05-16	2024-05-16

Comment

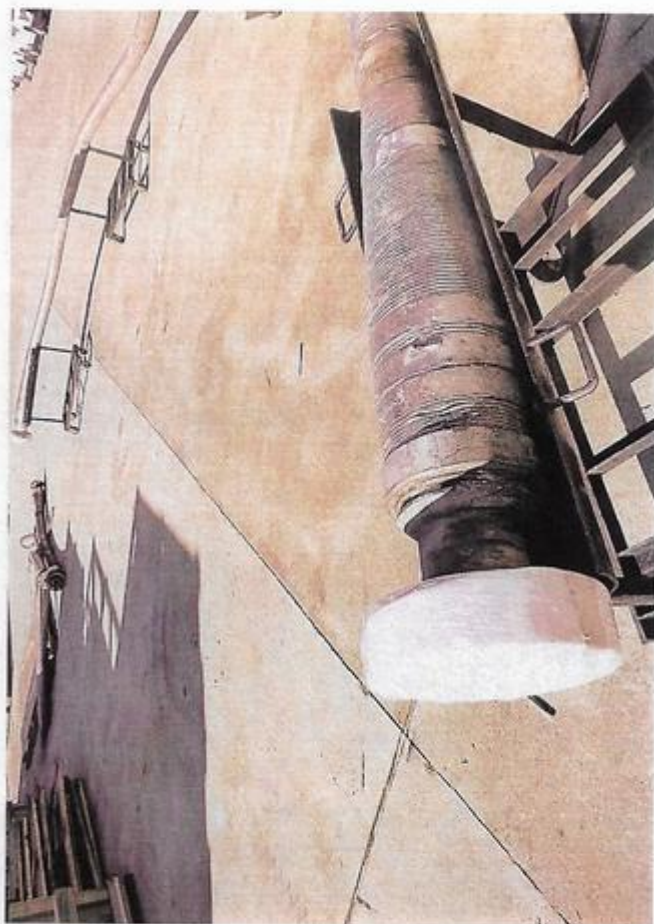

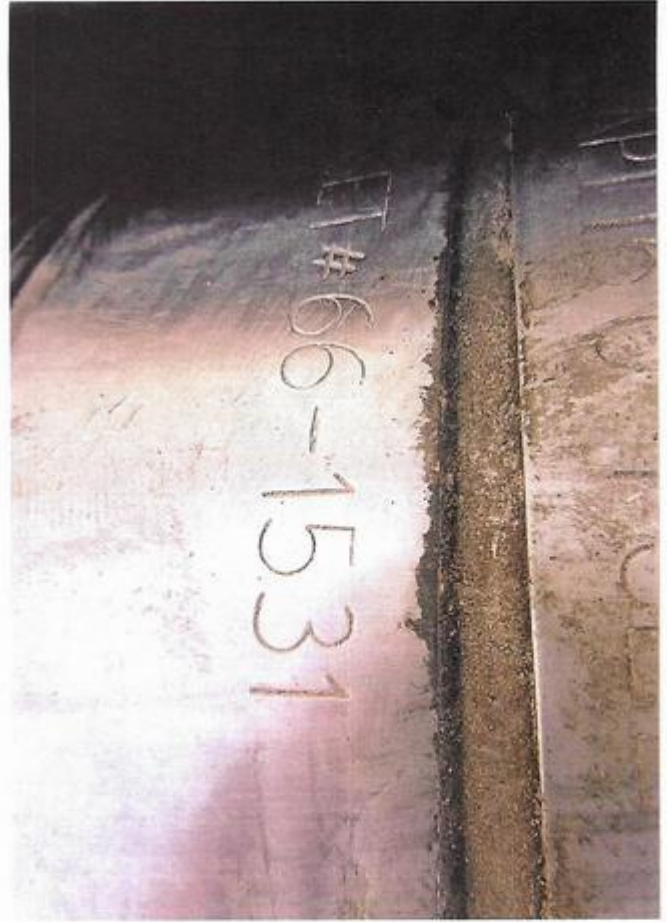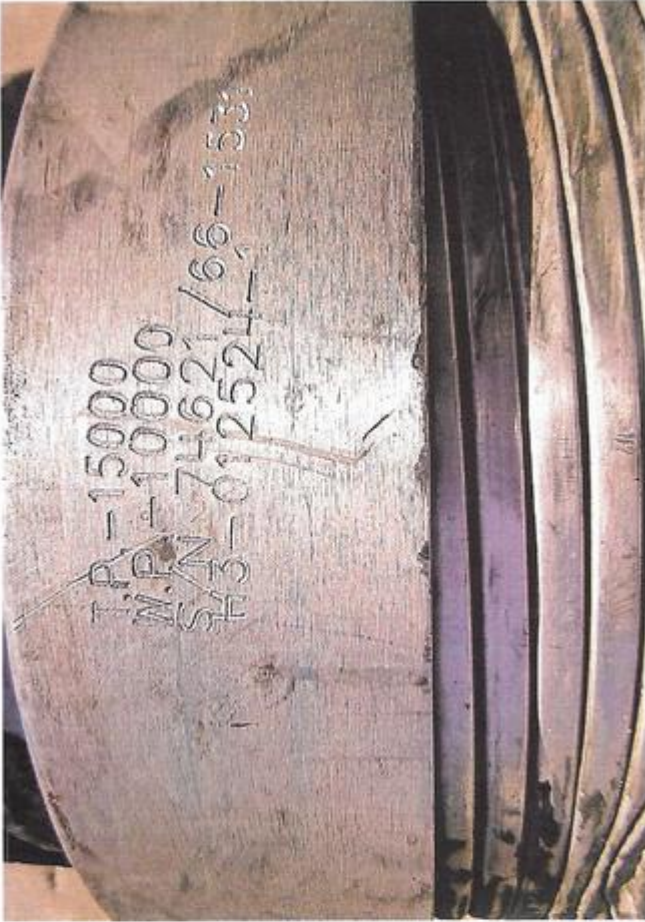

XTO Permian Operating, LLC Offline Cementing Variance Request

XTO requests the option to cement the surface and intermediate casing strings offline as a prudent batch drilling efficiency of acreage development.


1. Cement Program

No changes to the cement program will take place for offline cementing.

2. Offline Cementing Procedure


The operational sequence will be as follows. If a well control event occurs, the BLM will be contacted for approval prior to conducting offline cementing operations.

1. Run casing as per normal operations. While running casing, conduct negative pressure test and confirm integrity of the float equipment (float collar and shoe)
2. Land casing with mandrel
3. Fill pipe with kill weight fluid, do not circulate through floats and confirm well is static
4. Set annular packoff shown below and pressure test to confirm integrity of the seal. Pressure ratings of wellhead components and valves is 5,000 psi.
5. After confirmation of both annular barriers and internal barriers, nipple down BOP and install cap flange.
 - a. If any barrier fails to test, the BOP stack will not be nipped down until after the cement job is completed with cement 500ft above the highest formation capable of flow with kill weight mud above or after it has achieved 50-psi compressive strength if kill weight fluid cannot be verified.

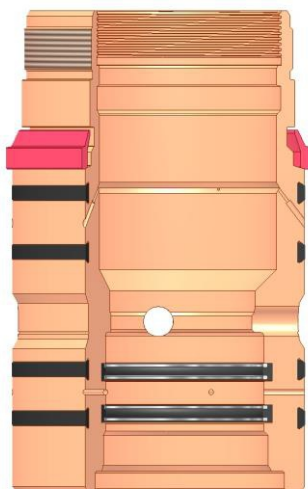


Annular packoff with both external and internal seals

XTO Permian Operating, LLC Offline Cementing Variance Request

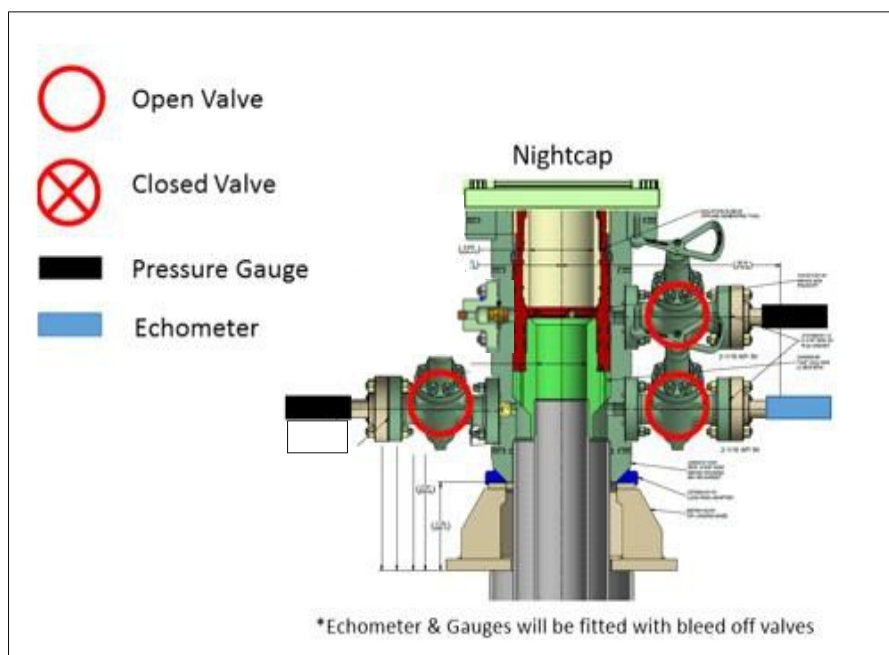

Wellhead diagram during skidding operations

6. Skid rig to next well on pad.
7. Confirm well is static before removing cap flange, flange will not be removed and offline cementing operations will not commence until well is under control. If well is not static, casing outlet valves will provide access to both the casing ID and annulus. Rig or third party pump truck will kill well prior to cementing or nipping up for further remediation.
 - a. Well Control Plan
 - i. The Drillers Method will be the primary well control method to regain control of the wellbore prior to cementing, if wellbore conditions do not permit the drillers method other methods of well control may be used
 - ii. Rig pumps or a 3rd party pump will be tied into the upper casing valve to pump down the casing ID
 - iii. A high pressure return line will be rigged up to lower casing valve and run to choke manifold to control annular pressure
 - iv. Once influx is circulated out of the hole, kill weight mud will be circulated
 - v. Well will be confirmed static
 - vi. Once confirmed static, cap flange will be removed to allow for offline cementing operations to commence
8. Install offline cement tool
9. Rig up cement equipment

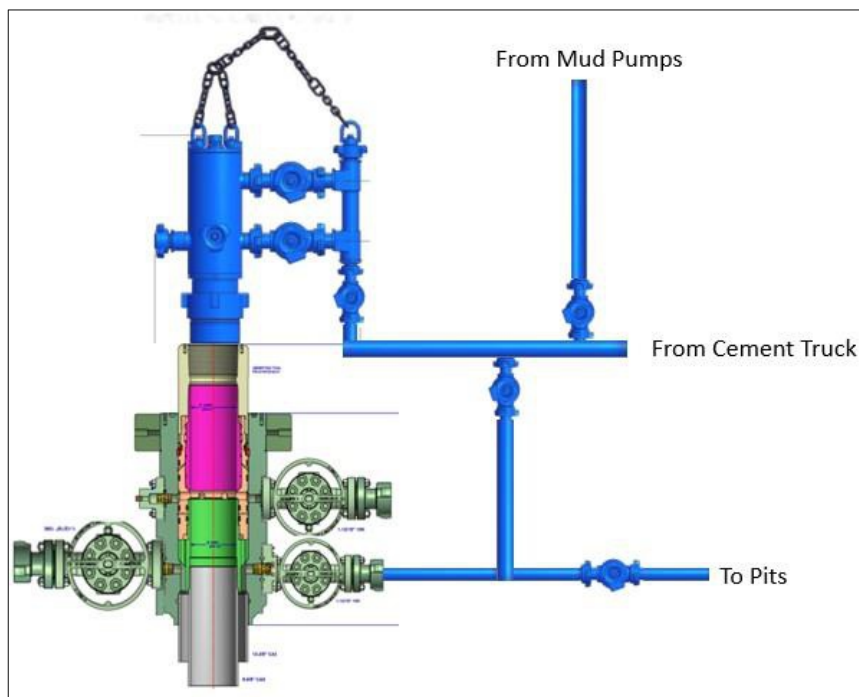XTO Permian Operating, LLC Offline Cementing Variance Request

Wellhead diagram during offline cementing operations

10. Circulate bottoms up with cement truck
 - a. If gas is present on bottoms up, well will be shut in and returns rerouted through gas buster to handle entrained gas
 - b. Max anticipated time before circulating with cement truck is 6 hrs
11. Perform cement job taking returns from the annulus wellhead valve
12. Confirm well is static and floats are holding after cement job
13. Remove cement equipment, offline cement tools and install night cap with pressure gauge for monitoring.

XTO respectfully requests approval to utilize a spudder rig to pre-set surface casing.

Description of Operations:

1. Spudder rig will move in to drill the surface hole and pre-set surface casing on the well.
 - a. After drilling the surface hole section, the spudder rig will run casing and cement following all of the applicable rules and regulations (OnShore Order 2, all COAs and NMOCD regulations).
 - b. The spudder rig will utilize fresh water-based mud to drill the surface hole to TD. Solids control will be handled entirely on a closed loop basis. No earth pits will be used.
2. The wellhead will be installed and tested as soon as the surface casing is cut off and WOC time has been reached.
3. A blind flange at the same pressure rating as the wellhead will be installed to seal the wellbore. Pressure will be monitored with needle valves installed on two wing valves.
 - a. A means for intervention will be maintained while the drilling rig is not over the well.
4. Spudder rig operations are expected to take 2-3 days per well on the pad.
5. The BLM will be contacted and notified 24 hours prior to commencing spudder rig operations.
6. Drilling Operations will begin with a larger rig and a BOP stack equal to or greater than the pressure rating that was permitted will be nipped up and tested on the wellhead before drilling operations resume on each well.
 - a. The larger rig will move back onto the location within 90 days from the point at which the wells are secured and the spudder rig is moved off location.
 - b. The BLM will be notified 24 hours before the larger rig moves back on the pre-set locations
7. XTO will have supervision on the rig to ensure compliance with all BLM and NMOCD regulations and to oversee operations.
8. Once the rig is removed, XTO will secure the wellhead area by placing a guard rail around the cellar area.

APD ID: 10400100957

Submission Date: 09/23/2024

Operator Name: XTO PERMIAN OPERATING LLC

Well Name: POKER LAKE UNIT 20-8 BD

Well Number: 208H

Well Type: OIL WELL

Well Work Type: Drill

Highlighted data
reflects the most
recent changes
[Show Final Text](#)

Section 1 - Existing Roads

Will existing roads be used? YES

Existing Road Map:

Poker_Lake_Unit_20_8_BD_208H_Existing_Road_Map_20240911123908.pdf

Existing Road Purpose: ACCESS

Row(s) Exist? NO

ROW ID(s)

ID:

Do the existing roads need to be improved? NO

Existing Road Improvement Description:

Existing Road Improvement Attachment:

Section 2 - New or Reconstructed Access Roads

Will new roads be needed? NO

Section 3 - Location of Existing Wells

Existing Wells Map? YES

Existing Well map Attachment:

Well Name: POKER LAKE UNIT 20-8 BD

Well Number: 208H

Poker_Lake_Unit_20_17___20_8_BD_1Mile_Radius_20240911065741.pdf

Section 4 - Location of Existing and/or Proposed Production Facilities

Submit or defer a Proposed Production Facilities plan? SUBMIT

Production Facilities description: A. Production Facilities. No New facility is required for the Poker Lake Unit 20-17/20-8 BD wells. Once drilled and completed, the wells will flow to the Poker Lake Unit 20-17/20-8 BD battery. B. Flowlines. No further flowlines disturbance is requested. C. Gas Pipeline. No Gas Sales line is required for this well. No additional surface disturbance is needed. D. Disposal Facilities. Produced water will be hauled from location to a commercial or private disposal facility as needed. E. Flare. - Check in facility plot attached. F. Aboveground Structures. All permanent (on site six months or longer) aboveground structures constructed or installed on location and not subject to safety requirements will be painted earth-tone colors such as BLM Standard Environmental Color Chart (CC-001: June 2008) that reduce the visual impacts of the built environment. G. Containment Berms. Containment berms will be constructed completely around any production facilities designed. The containment berms will be constructed of compacted caliche, be sufficiently impervious, away from cut or fill areas. H. Electrical. No additional electrical is required for this well. No additional surface disturbance is needed. I. Facility Description- Kindly see the facility plot attached.

Production Facilities map:

XTO_DB_BDWST_00CTB_PLOT_000_0_Model_6_18_18_20240911053241.pdf

Section 5 - Location and Types of Water Supply

Water Source Table

Water source type: OTHER**Describe type:** Fresh Water

Water source use type:

DUST CONTROL

SURFACE CASING

STIMULATION

Source latitude:**Source longitude:****Source datum:****City:****Water source permit type:** PRIVATE CONTRACT**Water source transport method:** TRUCKING**Source land ownership:** COMMERCIAL**Source transportation land ownership:** FEDERAL**Water source volume (barrels):** 550000**Source volume (acre-feet):** 70.89120298**Source volume (gal):** 23100000

Well Name: POKER LAKE UNIT 20-8 BD

Well Number: 208H

Water source type: OTHER

Describe type: Raw Produced Water

Water source use type: INTERMEDIATE/PRODUCTION
CASING

Source latitude:

Source longitude:

Source datum:

City:

Water source permit type: PRIVATE CONTRACT

Water source transport method: PIPELINE

Source land ownership: COMMERCIAL

Source transportation land ownership: FEDERAL

Water source volume (barrels): 550000

Source volume (acre-feet): 70.89120298

Source volume (gal): 23100000

Water source type: RECYCLEDWater source use type: INTERMEDIATE/PRODUCTION
CASING

Source latitude:

Source longitude:

Source datum:

City:

Water source permit type: PRIVATE CONTRACT

Water source transport method: PIPELINE

Source land ownership: COMMERCIAL

Source transportation land ownership: FEDERAL

Water source volume (barrels): 550000

Source volume (acre-feet): 70.89120298

Water source and transportation

Poker_Lake_Unit_20_8_BD_208H_Vicinity_Map_20240911123951.pdf

Water source comments: The well will be drilled using a combination of water mud systems as outlined in the Drilling Program. Water composition depends on the mud type needed per formation to protect useable water. Fresh water is trucked to location for use in surface casing drilling and cementing. All other water is either brackish (3P) or raw produced water (XOM) that is all piped from either a pipeline or a pond 32.1483028, -103.922338) to the drilling location. Anticipated water usage for drilling includes an estimated 50,000 barrels of water to drill a horizontal well in a combination of fresh water and brine as detailed in the mud program in the drilling plans. These volumes are calculated for ~1.5bbls per foot of hole drilled with excess to accommodate any lost circulation or wash out that may occur. Actual water volumes used during operations will depend on the depth of the well, length of horizontal sections, and the losses that may occur

Well Name: POKER LAKE UNIT 20-8 BD

Well Number: 208H

during the operation. Temporary water lines will be permitted via a Temporary Water Line Approved Decision letter and/or any necessary Right of Way Grants as needed based on drilling and completion schedules. Well completion is expected to require approximately 550,000 barrels of water per horizontal well. Actual water volumes used during operations will depend on the depth of the well and length of horizontal sections.

New water well? N

New Water Well Info

Well latitude:

Well Longitude:

Well datum:

Well target aquifer:

Est. depth to top of aquifer(ft):

Est thickness of aquifer:

Aquifer comments:

Aquifer documentation:

Well depth (ft):

Well casing type:

Well casing outside diameter (in.):

Well casing inside diameter (in.):

New water well casing?

Used casing source:

Drilling method:

Drill material:

Grout material:

Grout depth:

Casing length (ft.):

Casing top depth (ft.):

Well Production type:

Completion Method:

Water well additional information:

State appropriation permit:

Additional information attachment:

Section 6 - Construction Materials

Using any construction materials: NO

Construction Materials description:

Construction Materials source location

Section 7 - Methods for Handling

Waste type: DRILLING

Waste content description: FLUID

Amount of waste: 500 barrels

Waste disposal frequency : One Time Only

Safe containment description: Steel Mud Boxes

Safe containmant attachment:

Waste disposal type: HAUL TO COMMERCIAL FACILITY

Disposal location ownership: COMMERCIAL

Well Name: POKER LAKE UNIT 20-8 BD

Well Number: 208H

Disposal type description:**Disposal location description:** R360 Environmental Solutions 4507 W Carlsbad Hwy, Hobbs, NM 88240**Waste type:** SEWAGE

Waste content description: Portable, self-contained toilets will be provided for human waste disposal. Upon completion of drilling and completion activities, or as required, the toilet holding tanks will be pumped and the contents thereof disposed of in an approved sewage disposal facility. All state and local laws and regulations pertaining to the disposal of human and solid waste will be complied with. This equipment will be properly maintained during the drilling and completion operations and will be removed when all operations are complete.

Amount of waste: 250 gallons**Waste disposal frequency :** Weekly

Safe containment description: Portable, self-contained toilets will be provided for human waste disposal. Upon completion of drilling and completion activities, or as required, the toilet holding tanks will be pumped and the contents thereof disposed of in an approved sewage disposal facility. All state and local laws and regulations pertaining to the disposal of human and solid waste will be complied with. This equipment will be properly maintained during the drilling and completion operations and will be removed when all operations are complete.

Safe containmant attachment:**Waste disposal type:** HAUL TO COMMERCIAL FACILITY **Disposal location ownership:** COMMERCIAL**Disposal type description:****Disposal location description:** A licensed 3rd party contractor to haul and dispose of human waste.**Waste type:** GARBAGE

Waste content description: All garbage, junk and non-flammable waste materials will be contained in a self-contained, portable dumpster or trash cage, to prevent scattering and will be removed and deposited in an approve sanitary landfill. Immediately after drilling all debris and other waste materials on and around the well location not contained in the trash cage will be cleaned up and removed from the location. No potentially adverse materials or substances will be left on the location.

Amount of waste: 250 pounds**Waste disposal frequency :** Weekly

Safe containment description: All garbage, junk and non-flammable waste materials will be contained in a self-contained, portable dumpster or trash cage, to prevent scattering and will be removed and deposited in an approve sanitary landfill. Immediately after drilling all debris and other waste materials on and around the well location not contained in the trash cage will be cleaned up and removed from the location. No potentially adverse materials or substances will be left on the location.

Safe containmant attachment:**Waste disposal type:** HAUL TO COMMERCIAL FACILITY **Disposal location ownership:** COMMERCIAL**Disposal type description:****Disposal location description:** A licensed 3rd party contractor will be used to haul and dispose of garbage.

Well Name: POKER LAKE UNIT 20-8 BD

Well Number: 208H

Waste type: DRILLING

Waste content description: Cuttings

Amount of waste: 2100 pounds

Waste disposal frequency : One Time Only

Safe containment description: The well will be drilled utilizing a closed-loop mud system. Drill cuttings will be held in roll-off style mud boxes and taken to a New Mexico Oil Conservation Division (NMOCD) approved disposal site.

Safe containmant attachment:

Waste disposal type: HAUL TO COMMERCIAL FACILITY **Disposal location ownership:** COMMERCIAL

Disposal type description:

Disposal location description: R360 Environmental Solutions 4507 W Carlsbad Hwy, Hobbs, NM 88240

Reserve Pit

Reserve Pit being used? NO

Temporary disposal of produced water into reserve pit? NO

Reserve pit length (ft.) **Reserve pit width (ft.)**

Reserve pit depth (ft.) **Reserve pit volume (cu. yd.)**

Is at least 50% of the reserve pit in cut?

Reserve pit liner

Reserve pit liner specifications and installation description

Cuttings Area

Cuttings Area being used? NO

Are you storing cuttings on location? Y

Description of cuttings location Cuttings. The well will be drilled utilizing a closed-loop mud system. Drill cuttings will be held in roll-off style mud boxes and taken to a New Mexico Oil Conservation Division (NMOCD) approved disposal site. Drilling Fluids. These will be contained in steel mud pits and then taken to a NMOCD approved commercial disposal facility. Produced Fluids. Water produced from the well will be held temporarily in steel tanks and then taken to a NMOCD approved commercial disposal facility. Oil produced during operations will be stored in s until sold.

Cuttings area length (ft.) **Cuttings area width (ft.)**

Cuttings area depth (ft.) **Cuttings area volume (cu. yd.)**

Is at least 50% of the cuttings area in cut?

Cuttings area liner

Cuttings area liner specifications and installation description

Well Name: POKER LAKE UNIT 20-8 BD

Well Number: 208H

Section 8 - Ancillary

Are you requesting any Ancillary Facilities?: N

Ancillary Facilities

Comments:

Section 9 - Well Site

Well Site Layout Diagram:

Poker_Lake_Unit_20_8_BD_208H_RL_20240917121536.pdf

Poker_Lake_Unit_20_8_BD_208H_Well_Site_Plant_Updated_20250327162612.pdf

Comments: Multi-Well Pad.

Section 10 - Plans for Surface

Type of disturbance: No New Surface Disturbance Multiple Well Pad Name: POKER LAKE UNIT 20-8 BD

Multiple Well Pad Number: D

Recontouring

XTO_POKER_LAKE_UNIT_20_17_20_8_BD_PAD_B_INTERIM_RECLAMATION_FINAL_3_20_2025_20250327162716.pdf

XTO_POKER_LAKE_UNIT_20_17_20_8_BD_PAD_D_INTERIM_RECLAMATION_FINAL_3_20_2025_20250327162717.pdf

Drainage/Erosion control construction: Initial seedbed preparation will consist of recontouring to the appropriate interim or final reclamation standard. All compacted areas to be seeded will be ripped to a minimum depth of 18 inches with a minimum furrow spacing of 2 feet, followed by recontouring the surface and then evenly spreading the stockpiled topsoil. Prior to seeding, the seedbed will be scarified to a depth of no less than 4-6 inches.

Drainage/Erosion control reclamation: Erosion features are equal to or less than surrounding area and erosion control is sufficient so that water naturally infiltrates into the soil and gully, head cutting, slumping, and deep or excessive rills (greater than 3 inches) are not observed.

Well pad proposed disturbance (acres):	Well pad interim reclamation (acres): 0	Well pad long term disturbance (acres): 0
Road proposed disturbance (acres):	Road interim reclamation (acres): 0	Road long term disturbance (acres): 0
Powerline proposed disturbance (acres):	Powerline interim reclamation (acres): 0	Powerline long term disturbance (acres): 0
Pipeline proposed disturbance (acres):	Pipeline interim reclamation (acres): 0	Pipeline long term disturbance (acres): 0
Other proposed disturbance (acres):	Other interim reclamation (acres): 0	Other long term disturbance (acres): 0
Total proposed disturbance: 0	Total interim reclamation: 0	Total long term disturbance: 0

Disturbance Comments:

Reconstruction method: The original stockpiled topsoil will be spread over the areas being reclaimed and the original landform will be restored for all disturbed areas including well pads, production facilities, roads,

Well Name: POKER LAKE UNIT 20-8 BD

Well Number: 208H

pipelines, and utility corridors as close as possible to the original topography. The location will then be ripped and seeded.

Topsoil redistribution: The original stockpiled topsoil will be spread over the areas being reclaimed and the original landform will be restored for all disturbed areas including well pads, production facilities, roads, pipelines, and utility corridors as close as possible to the original topography. The location will then be ripped and seeded.

Soil treatment: A self-sustaining, vigorous, diverse, native (or otherwise approved) plant community will be established on the site with a density sufficient to control erosion and invasion by non-native plants and to re-establish wildlife habitat or forage production. At a minimum, the established plant community will consist of species included in the seed mix and/or desirable species occurring in the surrounding natural vegetation.

Existing Vegetation at the well pad: Soils are classified as Simona Gravelly Fine Sandy Loam and Simona-Bippus Complex. Simona soils are found on alluvial fans and plans and form in mixed alluvium and/or Aeolian sands. Bippus soils are found on alluvial fans and floodplains and form in mixed alluvium. The Simona-Bippus soils are dominant to the east and the Simona Gravelly Fine Sandy Loams are dominant to the West. Dominant vegetation species include: mesquite, sumac snakeweed, and various forbs and grasses. Ground cover is minimal, offering 90 percent visibility.

Existing Vegetation at the well pad

</style isBold="true">Existing Vegetation Community at the road:</style> Soils are classified as Simona Gravelly Fine Sandy Loam and Simona-Bippus Complex. Simona soils are found on alluvial fans and plans and form in mixed alluvium and/or Aeolian sands. Bippus soils are found on alluvial fans and floodplains and form in mixed alluvium. The SimonaBippus soils are dominant to the east and the Simona Gravelly Fine Sandy Loams are dominant to the West. Dominant vegetation species include: mesquite, sumac snakeweed, and various forbs and grasses. Ground cover is minimal, offering 90 percent visibility.

Existing Vegetation Community at the road

</style isBold="true">Existing Vegetation Community at the pipeline:</style> Soils are classified as Simona Gravelly Fine Sandy Loam and Simona-Bippus Complex. Simona soils are found on alluvial fans and plans and form in mixed alluvium and/or Aeolian sands. Bippus soils are found on alluvial fans and floodplains and form in mixed alluvium. The SimonaBippus soils are dominant to the east and the Simona Gravelly Fine Sandy Loams are dominant to the West. Dominant vegetation species include: mesquite, sumac snakeweed, and various forbs and grasses. Ground cover is minimal, offering 90 percent visibility.

Existing Vegetation Community at the pipeline

</style isBold="true">Existing Vegetation Community at other disturbances:</style> Soils are classified as Simona Gravelly Fine Sandy Loam and Simona-Bippus Complex. Simona soils are found on alluvial fans and plans and form in mixed alluvium and/or Aeolian sands. Bippus soils are found on alluvial fans and floodplains and form in mixed alluvium. The SimonaBippus soils are dominant to the east and the Simona Gravelly Fine Sandy Loams are dominant to the West. Dominant vegetation species include: mesquite, sumac snakeweed, and various forbs and grasses. Ground cover is minimal, offering 90 percent visibility.

Existing Vegetation Community at other disturbances

Non native seed used? N

Non native seed description:

Seedling transplant description:

Will seedlings be transplanted for this project? N

Seedling transplant description attachment:

Will seed be harvested for use in site reclamation? N

Well Name: POKER LAKE UNIT 20-8 BD

Well Number: 208H

Seed harvest description:

Seed harvest description attachment:

Seed

Seed Table

Seed Summary

Total pounds/Acre:

Seed Type

Pounds/Acre

Seed reclamation

Operator Contact/Responsible Official

First Name: Robert

Last Name: Bartels

Phone: (406)478-3617

Email: Robert.e.bartels@exxonmobil.com

Seedbed prep: Initial seedbed preparation will consist of recontouring to the appropriate interim or final reclamation standard. All compacted areas to be seeded will be ripped to a minimum depth of 18 inches with a minimum furrow spacing of 2 feet, followed by recontouring the surface and then evenly spreading the stockpiled topsoil. Prior to seeding, the seedbed will be scarified to a depth of no less than 4-6 inches. If the site is to be broadcast seeded, the surface will be left rough enough to trap seed and snow, control erosion, and increase water infiltration.

Seed BMP: If broadcast seeding is to be used and is delayed, final seedbed preparation will consist of contour cultivating to a depth of 4-6 inches within 24 hours prior to seeding, dozer tracking, or other imprinting to break the soil crust and create seed germination micro-sites.

Seed method: Seeding will be conducted no more than two weeks following completion of final seedbed preparation. A certified weed-free seed mix designed by the BLM to meet reclamation standards will be used.

Existing invasive species? N**Existing invasive species treatment description:****Existing invasive species treatment**

Weed treatment plan description: Weed control for all phases will be through the use of approved pesticides and herbicides according to applicable State, Federal and local laws.

Weed treatment plan

Monitoring plan description: Monitoring of invasive and noxious weeds will be visual and as-needed. If it is determined additional methods are required to monitor invasive and noxious weeds, appropriate BLM authorities will be contacted with a plan of action for approval prior to implementation.

Monitoring plan

Success standards: 100% compliance with applicable regulations.

Pit closure description: There will be no reserve pit as each well will be drilled utilizing a closed loop mud system. The closed loop system will meet the NMOCD requirements 19.15.17.

Pit closure attachment:

Well Name: POKER LAKE UNIT 20-8 BD

Well Number: 208H

Section 11 - Surface

Disturbance type: EXISTING ACCESS ROAD

Describe:

Surface Owner: BUREAU OF LAND MANAGEMENT

Other surface owner description:

BIA Local Office:

BOR Local Office:

COE Local Office:

DOD Local Office:

NPS Local Office:

State Local Office:

Military Local Office:

USFWS Local Office:

Other Local Office:

USFS Region:

USFS Forest/Grassland:

USFS Ranger District:

Disturbance type: WELL PAD

Describe:

Surface Owner: BUREAU OF LAND MANAGEMENT

Other surface owner description:

BIA Local Office:

BOR Local Office:

COE Local Office:

DOD Local Office:

NPS Local Office:

State Local Office:

Military Local Office:

USFWS Local Office:

Other Local Office:

USFS Region:

Well Name: POKER LAKE UNIT 20-8 BD

Well Number: 208H

USFS Forest/Grassland:

USFS Ranger District:

Disturbance type: TRANSMISSION LINE

Describe:

Surface Owner: BUREAU OF LAND MANAGEMENT

Other surface owner description:

BIA Local Office:

BOR Local Office:

COE Local Office:

DOD Local Office:

NPS Local Office:

State Local Office:

Military Local Office:

USFWS Local Office:

Other Local Office:

USFS Region:

USFS Forest/Grassland:

USFS Ranger District:

Disturbance type: OTHER

Describe: FLOWLINE

Surface Owner: BUREAU OF LAND MANAGEMENT

Other surface owner description:

BIA Local Office:

BOR Local Office:

COE Local Office:

DOD Local Office:

NPS Local Office:

State Local Office:

Military Local Office:

Well Name: POKER LAKE UNIT 20-8 BD

Well Number: 208H

USFWS Local Office:

Other Local Office:

USFS Region:

USFS Forest/Grassland:

USFS Ranger District:

Section 12 - Other

Right of Way needed? N

Use APD as ROW?

ROW Type(s):

ROW

SUPO Additional Information: SUPO written for all wells in section/project area.


Use a previously conducted onsite? Y

Previous Onsite information: - The XTO Permian Operating, LLC. representatives and BLM NRS were on location for onsite on 3/10/2021.

Other SUPO


Poker_Lake_Unit_20_17___20_8_BD_SUPO_20250319084001.pdf

TOPOGRAPHICAL AND ACCESS ROAD MAP

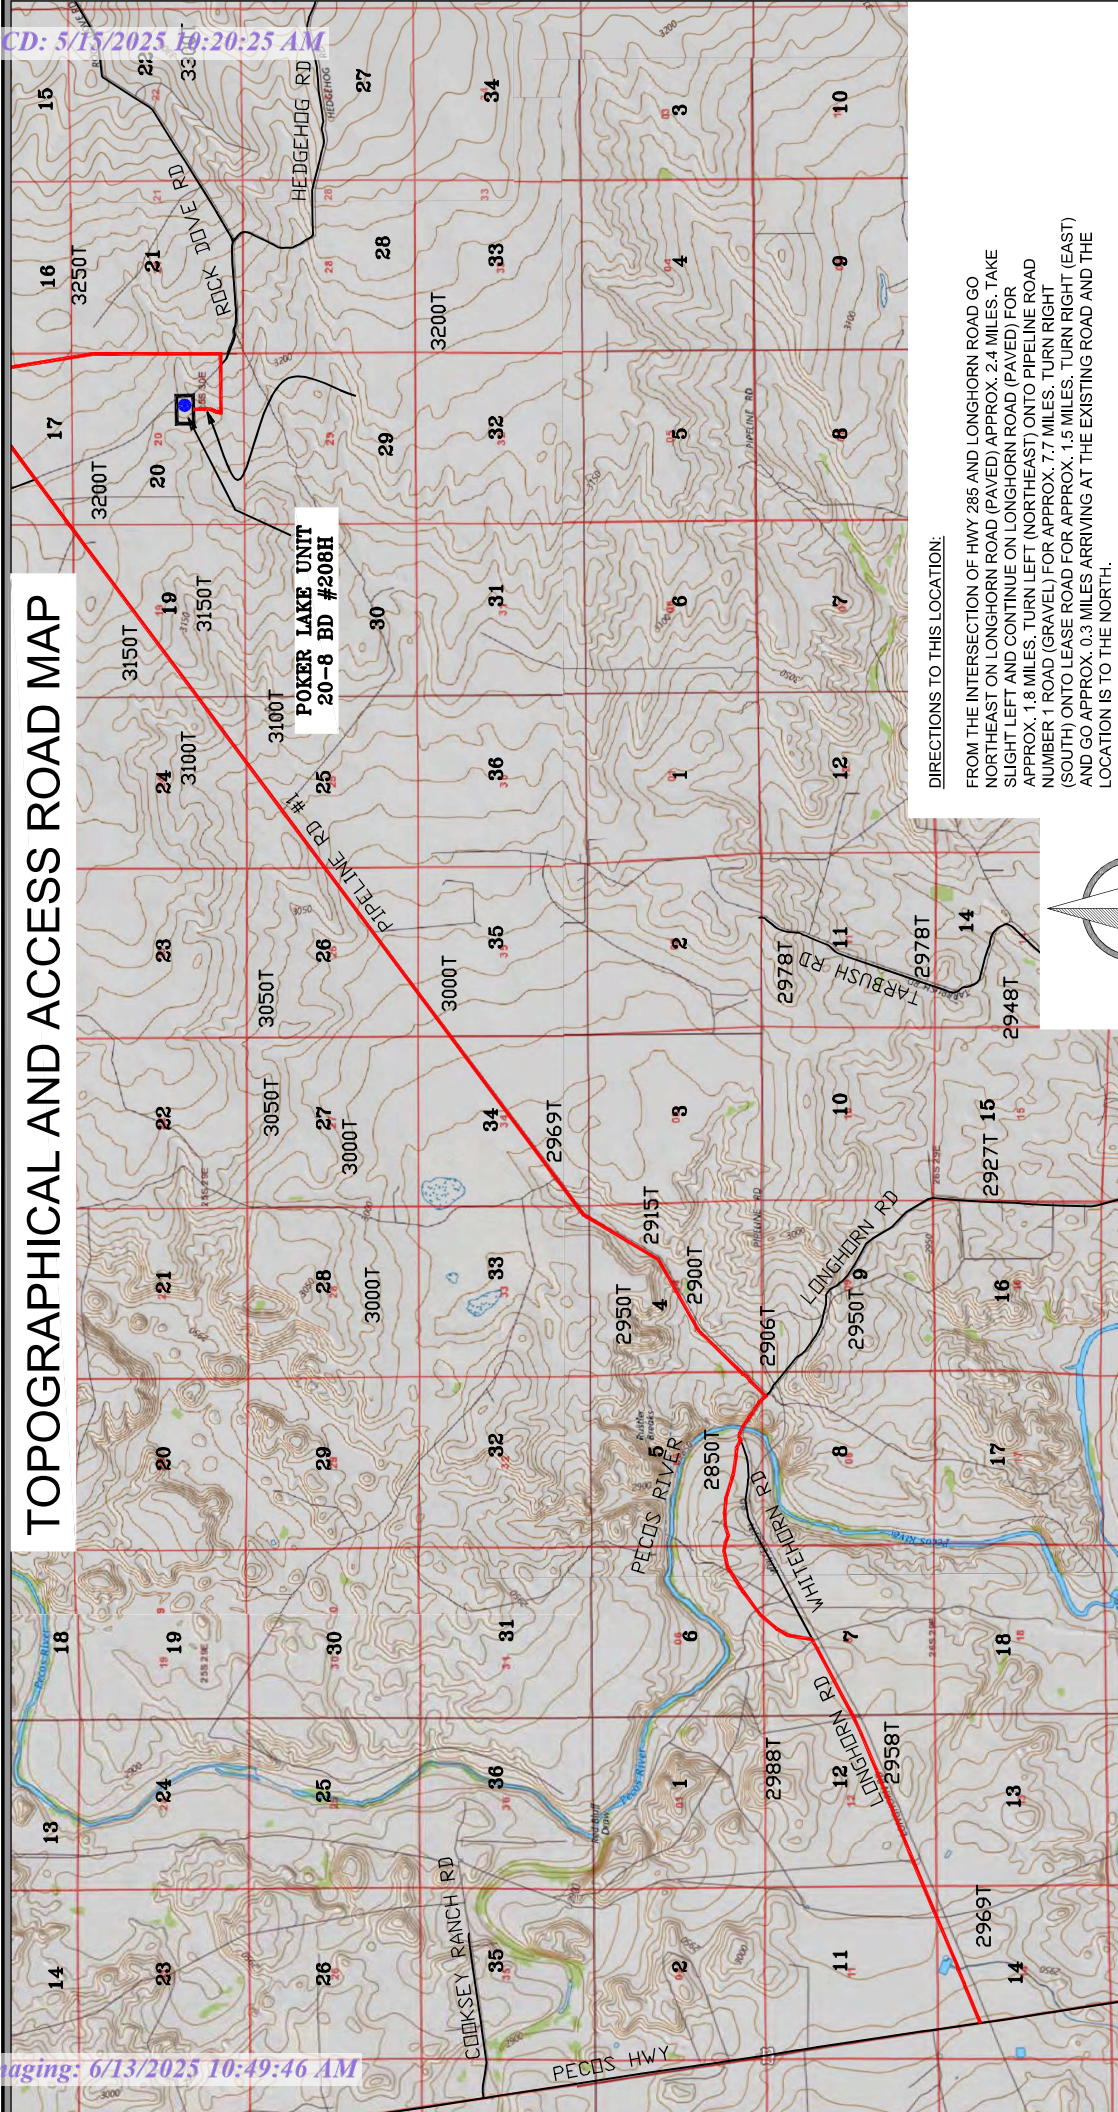

DIRECTIONS TO THIS LOCATION:

FROM THE INTERSECTION OF HWY 285 AND LONGHORN ROAD GO
NORTHEAST ON LONGHORN ROAD (PAVED) APPROX. 2.4 MILES. TAKE
SLIGHT LEFT AND CONTINUE ON LONGHORN ROAD (PAVED) FOR
APPROX. 1.8 MILES. TURN LEFT (NORTHEAST) ONTO PIPELINE ROAD
NUMBER 1 ROAD (GRAVEL) FOR APPROX. 7.7 MILES. TURN RIGHT
(SOUTH) ONTO LEASE ROAD FOR APPROX. 1.5 MILES. TURN RIGHT (EAST)
AND GO APPROX. 0.3 MILES ARRIVING AT THE EXISTING ROAD AND THE
LOCATION IS TO THE NORTH.



POKER LAKE UNIT 20-8 BD #208H
LOCATED 1,544 FEET FROM THE EAST LINE
AND 1,813 FEET FROM THE SOUTH LINE OF
SECTION 20, TOWNSHIP 25 SOUTH, RANGE 30
EAST, N.M.P.M. EDDY COUNTY, NEW MEXICO


2821 West 7th Street, Suite 200
Fort Worth, TX 76107
Ph: 817.349.9800 • Fax: 979.732.5271
TBPE Firm 17957 | TBPLS Firm 10193887
www.fscinc.net

FSC INC
SURVEYORS & ENGINEERS


DATE:	7-8-2024	PROJECT NO:	2024060280
DRAWN BY:	LM	SCALE:	1" = 5,000'
CHECKED BY:	CH	SHEET:	3 OF 3
FIELD CREW:	IR	REVISION:	0

© COPYRIGHT 2024 - ALL RIGHTS RESERVED


1-Mile Radius Map

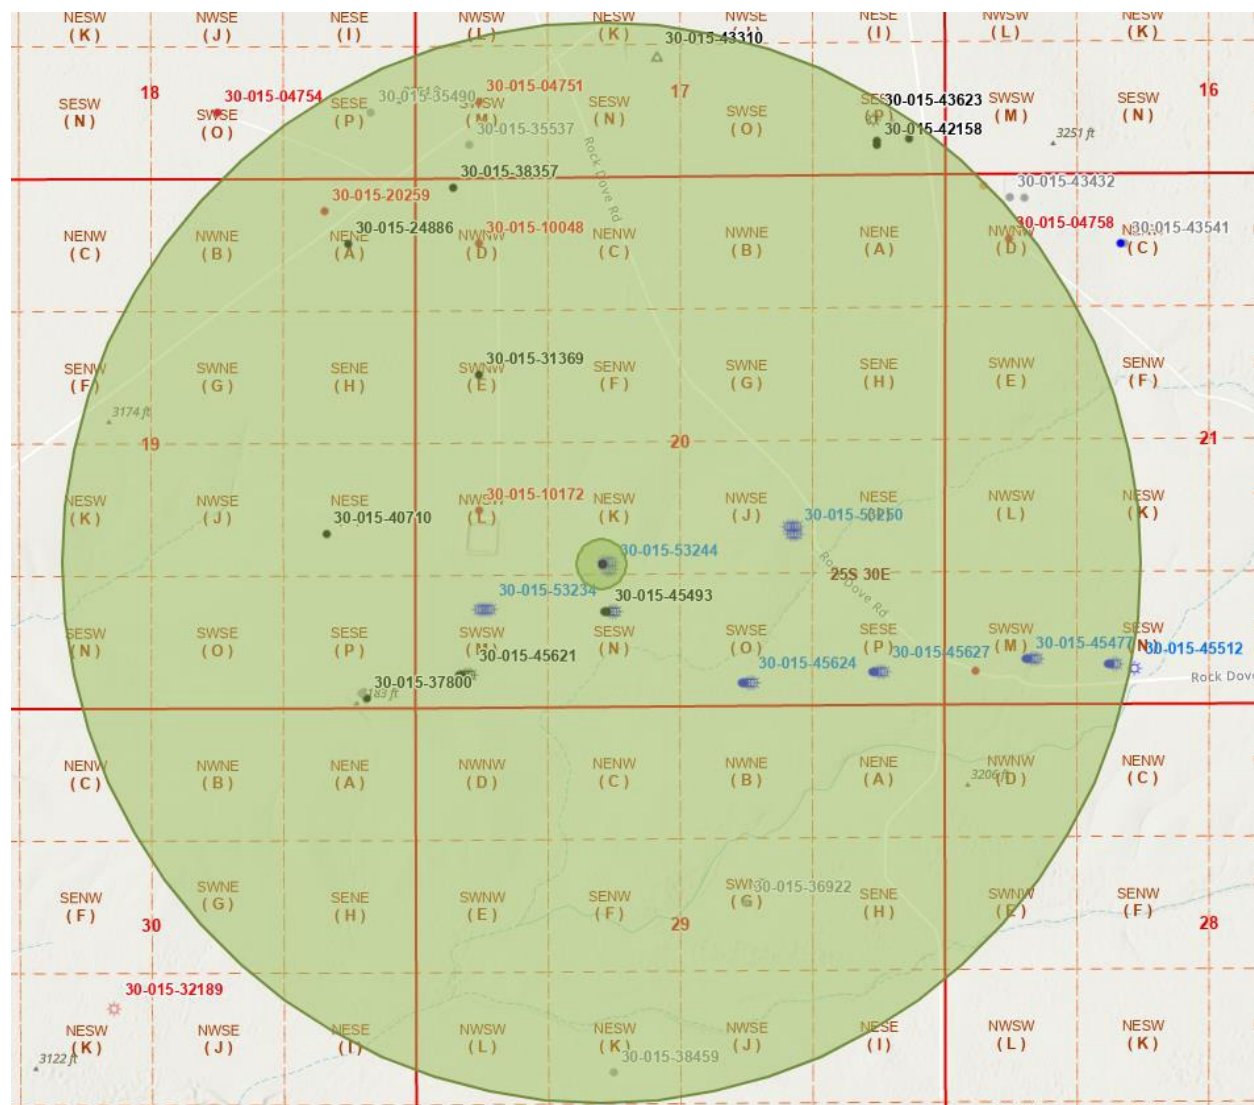




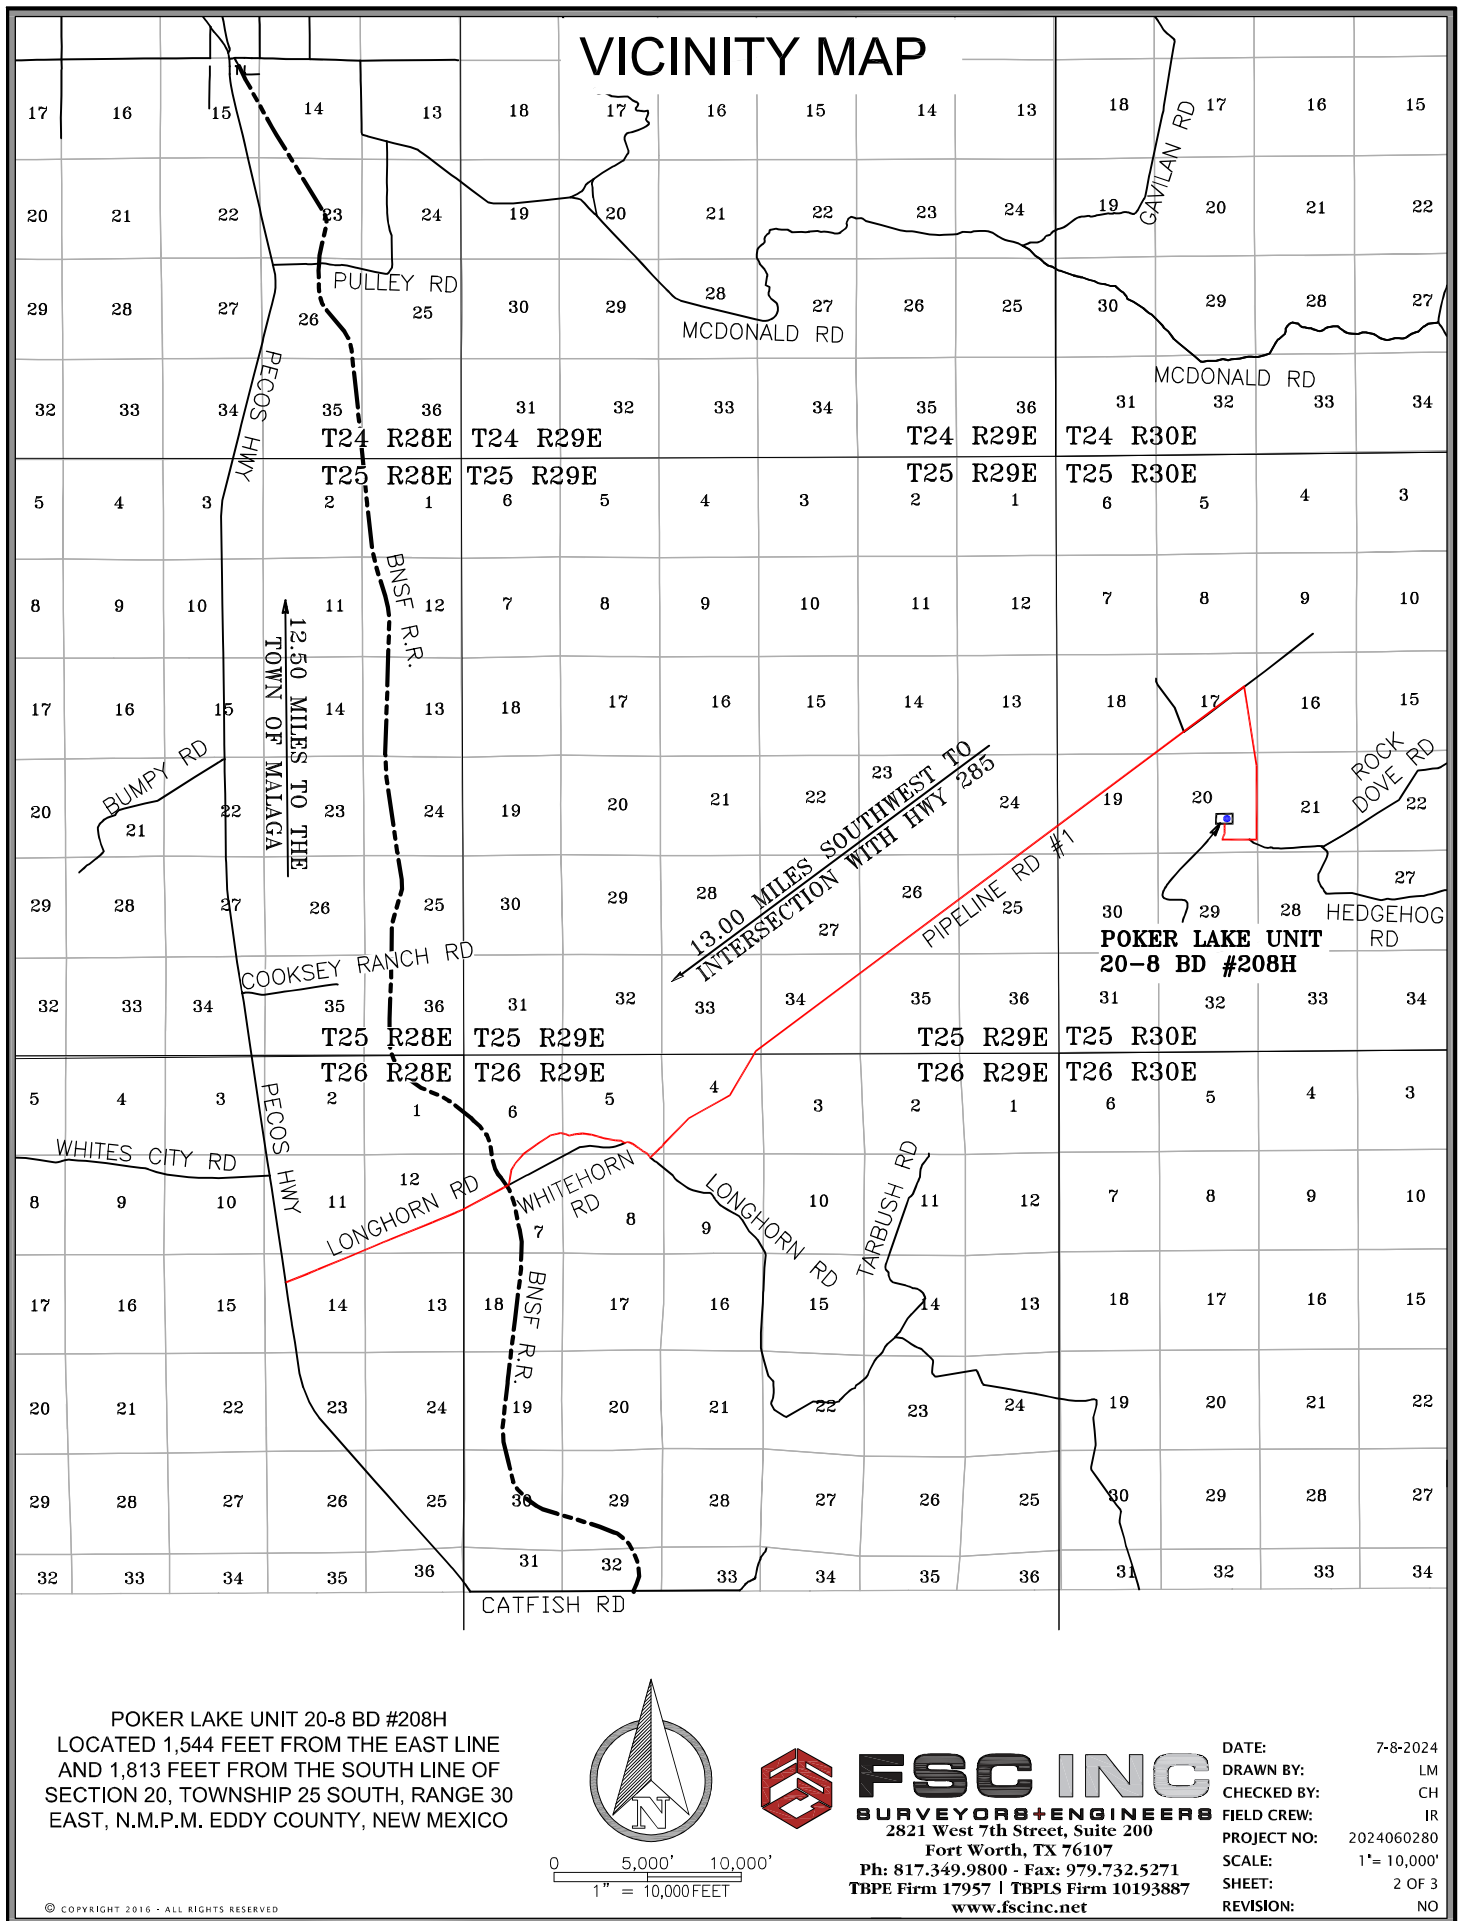

Rig Plat Layout

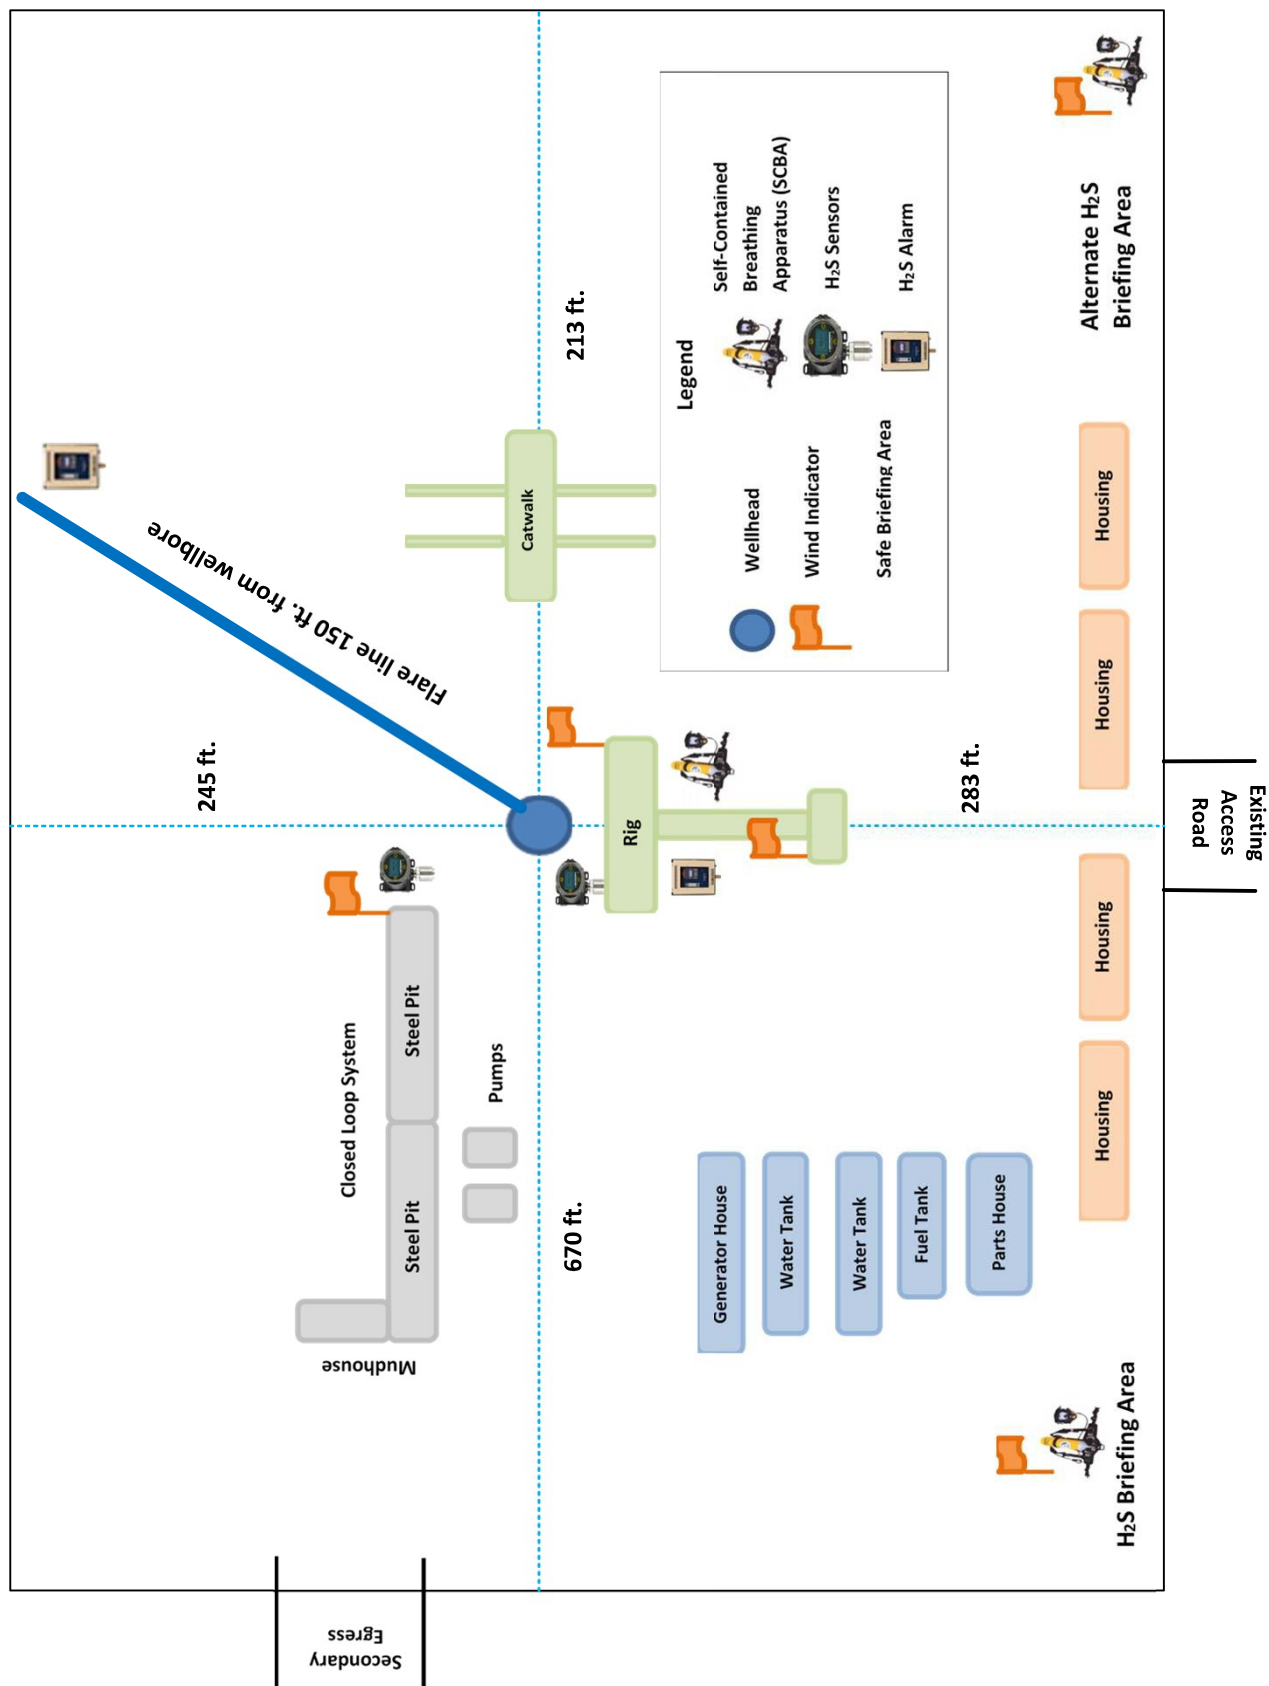

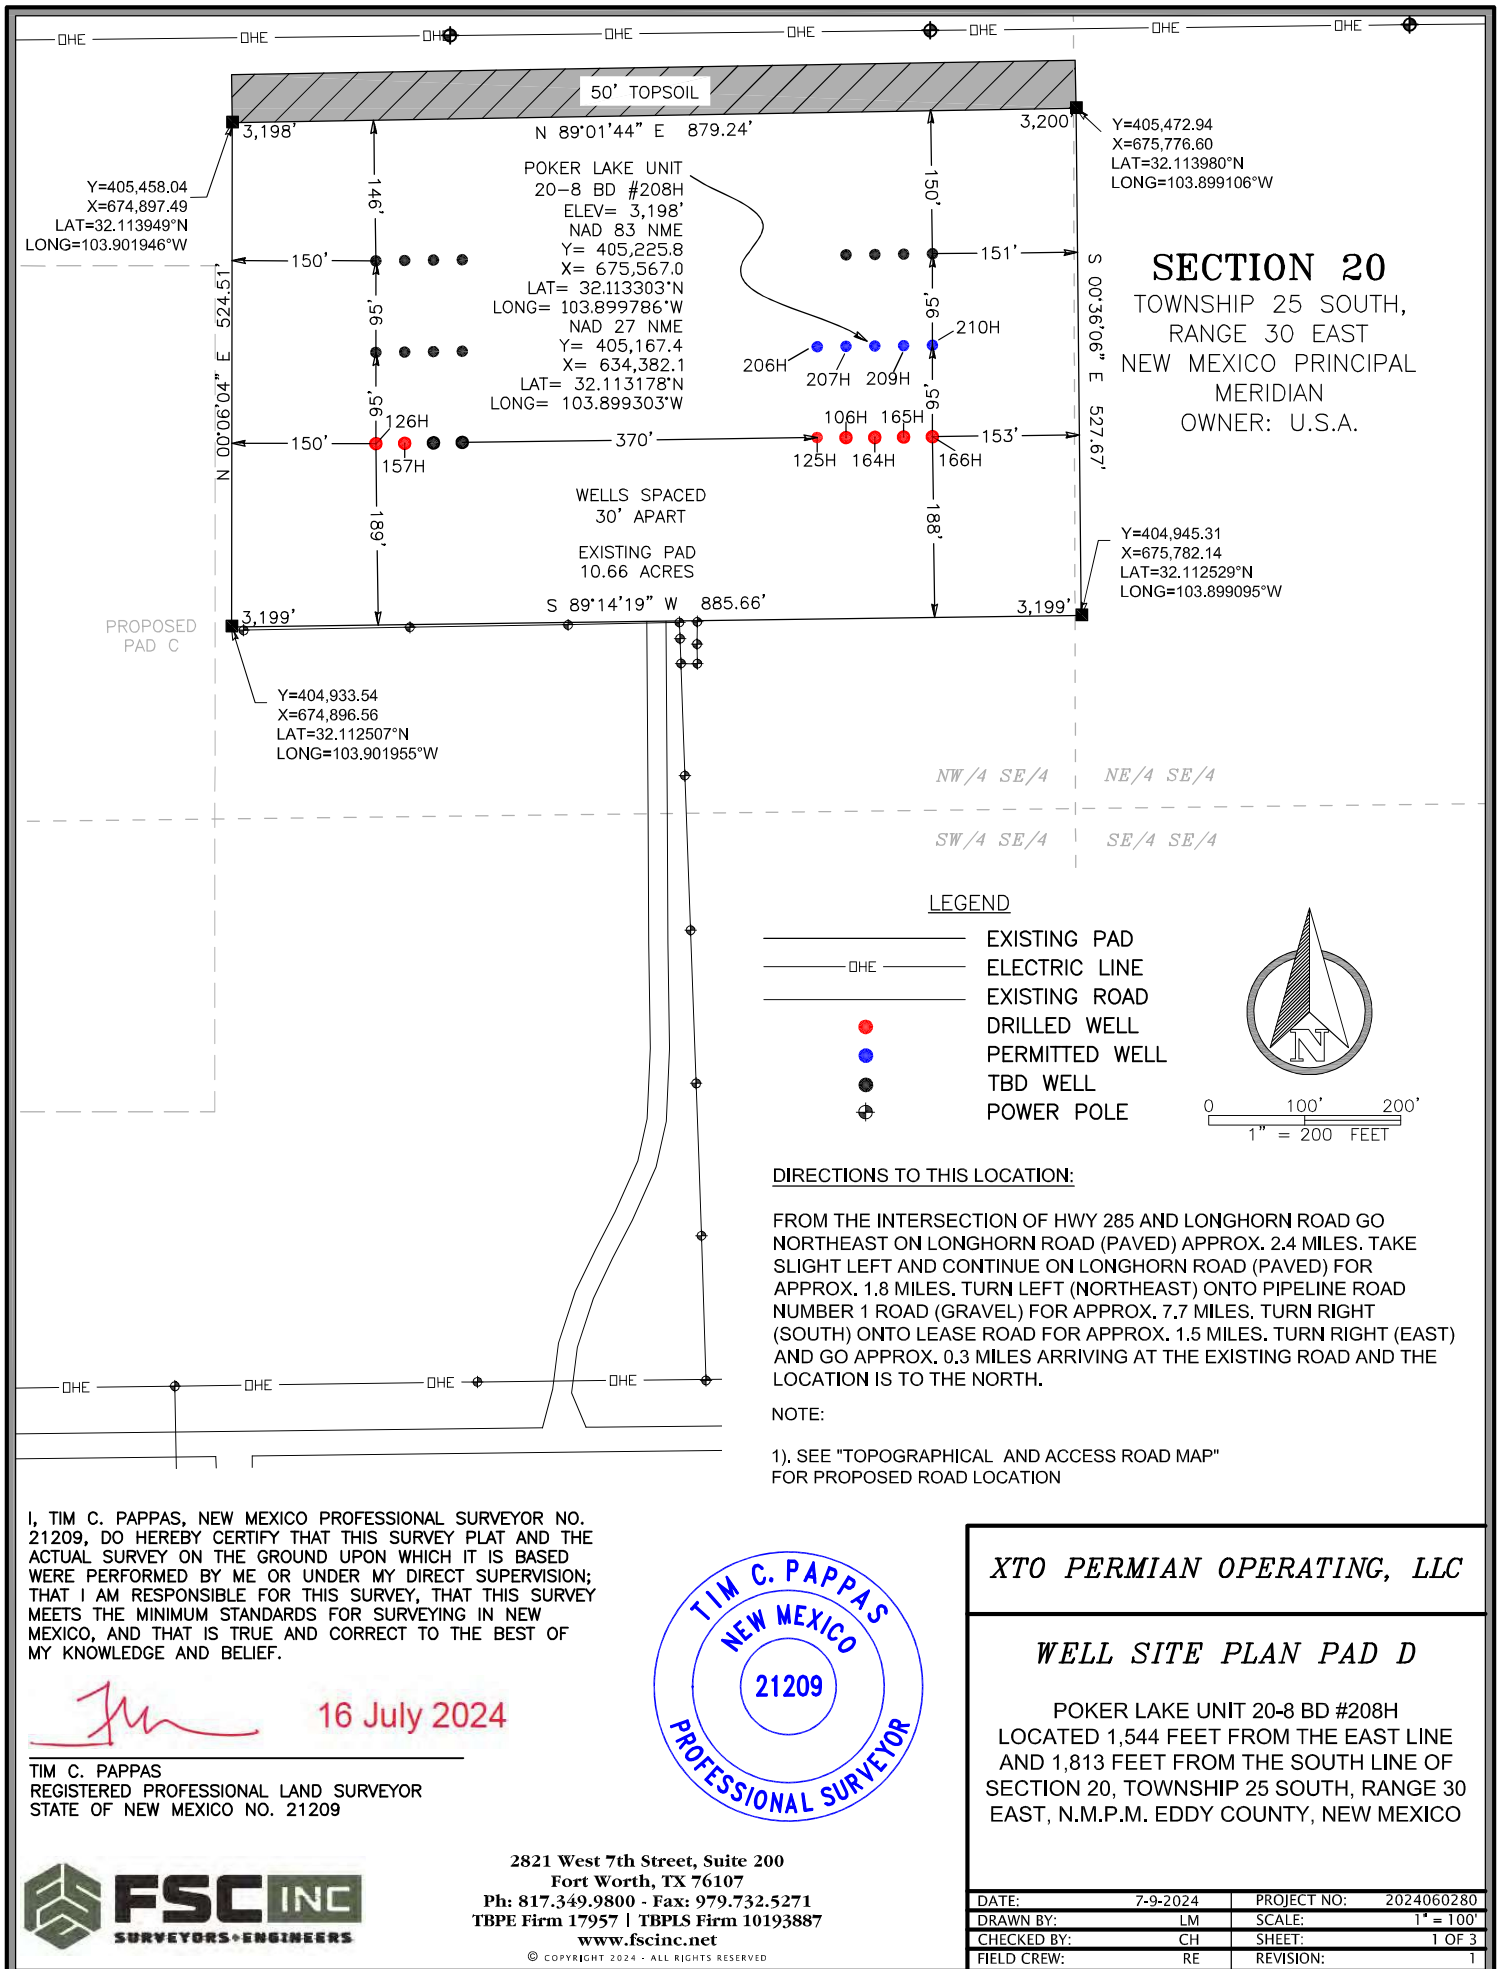

I, TIM C. PAPPAS, NEW MEXICO PROFESSIONAL SURVEYOR NO. 21209, DO HEREBY CERTIFY THAT THIS SURVEY PLAT AND THE ACTUAL SURVEY ON THE GROUND UPON WHICH IT IS BASED WERE PERFORMED BY ME OR UNDER MY DIRECT SUPERVISION; THAT I AM RESPONSIBLE FOR THIS SURVEY, THAT THIS SURVEY MEETS THE MINIMUM STANDARDS FOR SURVEYING IN NEW MEXICO, AND THAT IS TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF.

Tim C. Pappas 16 July 2024

TIM C. PAPPAS
REGISTERED PROFESSIONAL LAND SURVEYOR
STATE OF NEW MEXICO NO. 21209




2821 West 7th Street, Suite 200
Fort Worth, TX 76107
Ph: 817.349.9800 - Fax: 979.732.5271
TBPE Firm 17957 | TBPLS Firm 10193887
www.fscinc.net

© COPYRIGHT 2024 - ALL RIGHTS RESERVED

XTO PERMIAN OPERATING, LLC

WELL SITE PLAN PAD D

POKER LAKE UNIT 20-8 BD #208H
LOCATED 1,544 FEET FROM THE EAST LINE
AND 1,813 FEET FROM THE SOUTH LINE OF
SECTION 20, TOWNSHIP 25 SOUTH, RANGE 30
EAST, N.M.P.M. EDDY COUNTY, NEW MEXICO

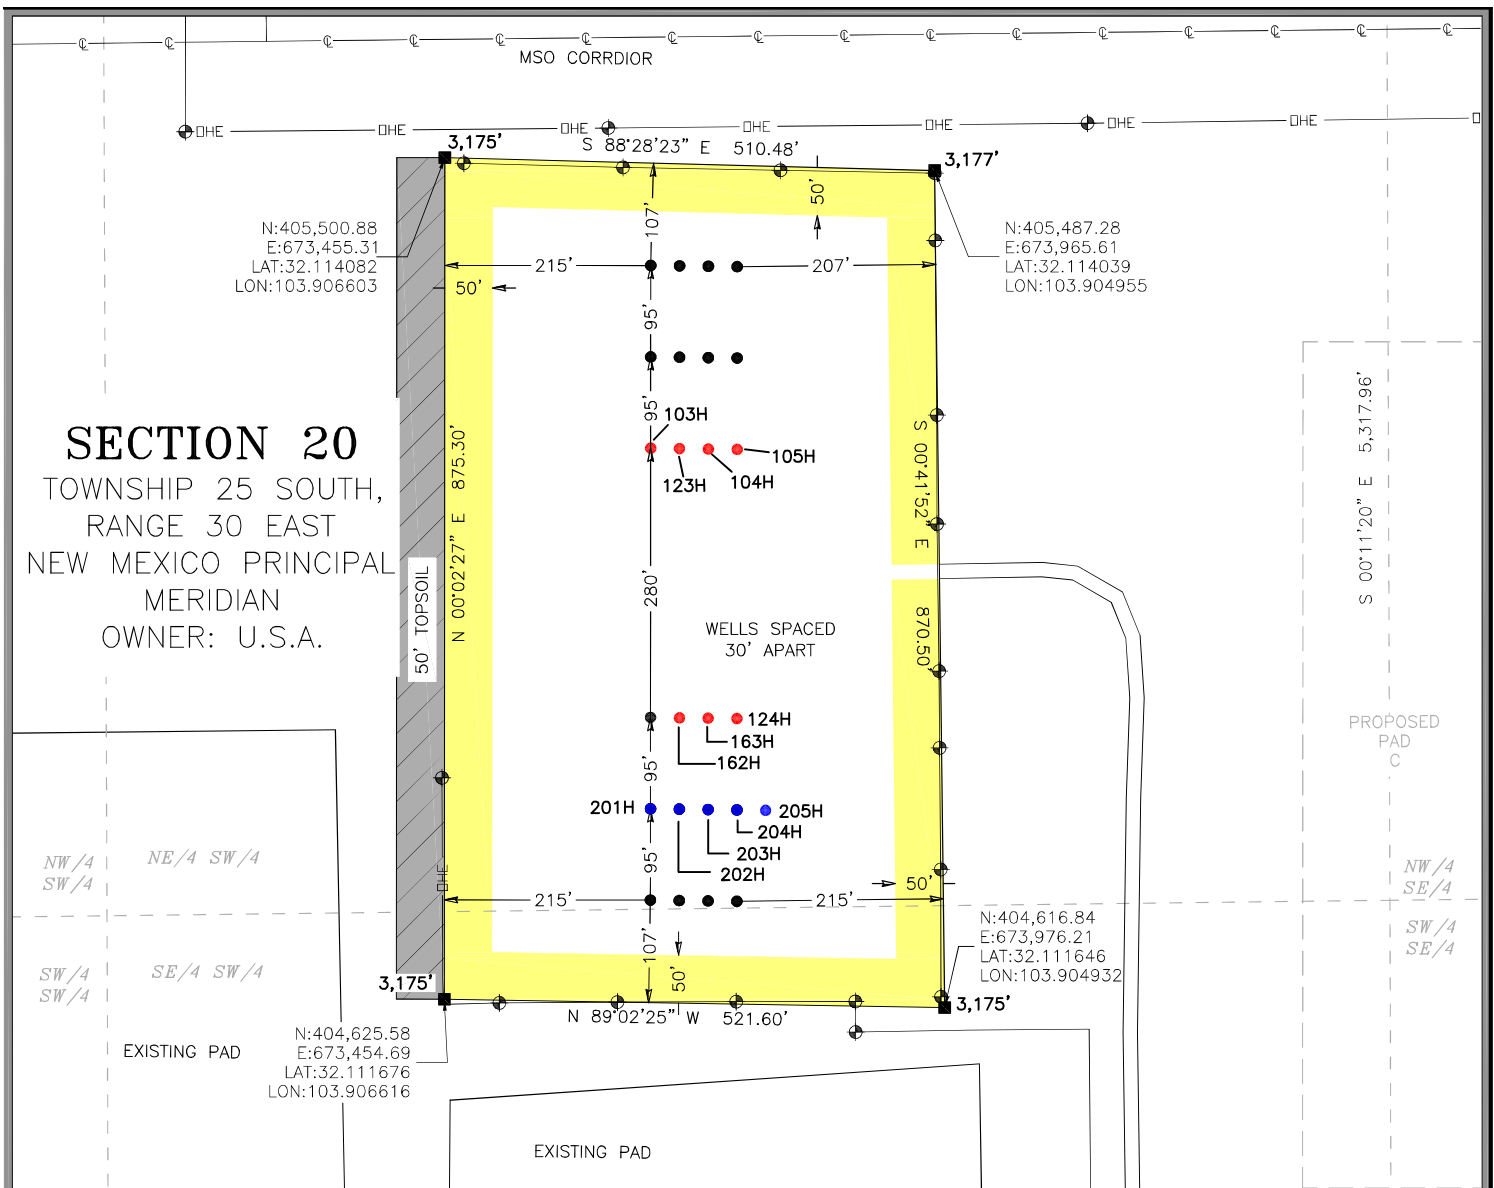**ACREAGE INFORMATION**

INITIAL DISTURBED AREA = 10.337 ACRES
 INTERIM RECLAMATION = 2.942 ACRES
 TOTAL PAD ACREAGE AFTER IR = 7.395 ACRES

GENERAL NOTES

1. ALL BEARINGS, DISTANCES, AND COORDINATE VALUES SHOWN HEREON ARE GRID VALUES AND ARE BASED ON THE NEW MEXICO STATE PLANE COORDINATE SYSTEM OF 1983 EAST ZONE 3001, U.S. SURVEY FEET.

I, TIM C. PAPPAS, NEW MEXICO PROFESSIONAL SURVEYOR NO. 21209, DO HEREBY CERTIFY THAT THIS SURVEY PLAT AND THE ACTUAL SURVEY ON THE GROUND UPON WHICH IT IS BASED WERE PERFORMED BY ME OR UNDER MY DIRECT SUPERVISION; THAT I AM RESPONSIBLE FOR THIS SURVEY, THAT THIS SURVEY MEETS THE MINIMUM STANDARDS FOR SURVEYING IN NEW MEXICO, AND THAT IS TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF.

Tim C. Pappas 20 March 2025

TIM C. PAPPAS
 REGISTERED PROFESSIONAL LAND SURVEYOR
 STATE OF NEW MEXICO NO. 21209



2821 West 7th Street, Suite 200
 Fort Worth, TX 76107
 Ph: 817.349.9800 - Fax: 979.732.5271
 TBPE Firm 17957 | TBPLS Firm 10193887
 www.fscinc.net
 © COPYRIGHT 2024 - ALL RIGHTS RESERVED

**LEGEND**

- PAD
- DHE — EXISTING OVERHEAD ELECTRIC
- EXISTING ROAD
- TBD WELL
- PERMITTED WELL
- DRILLED WELL
- ⊕ POWER POLE

INTERIM RECLAMATION AREA


XTO PERMIAN OPERATING, INC.

**AN INTERIM RECLAMATION
 DIAGRAM FOR:
 POKER LAKE UNIT**

20-17/20-8 BD PAD B

POKER LAKE UNIT 20-17/20-8 BD PAD B
 LOCATED 1,668 FEET FROM THE SOUTH LINE
 AND 1,950 FEET FROM THE WEST LINE OF
 SECTION 20 TOWNSHIP 25 SOUTH, RANGE 30
 EAST, N.M.P.M. EDDY COUNTY, NEW MEXICO

DATE:	3-19-2025	PROJECT NO:	2017040549
DRAWN BY:	RE/LM	SCALE:	1" = 200'
CHECKED BY:	CH	SHEET:	1 OF 1
FIELD CREW:	RE	REVISION:	3-20-2025

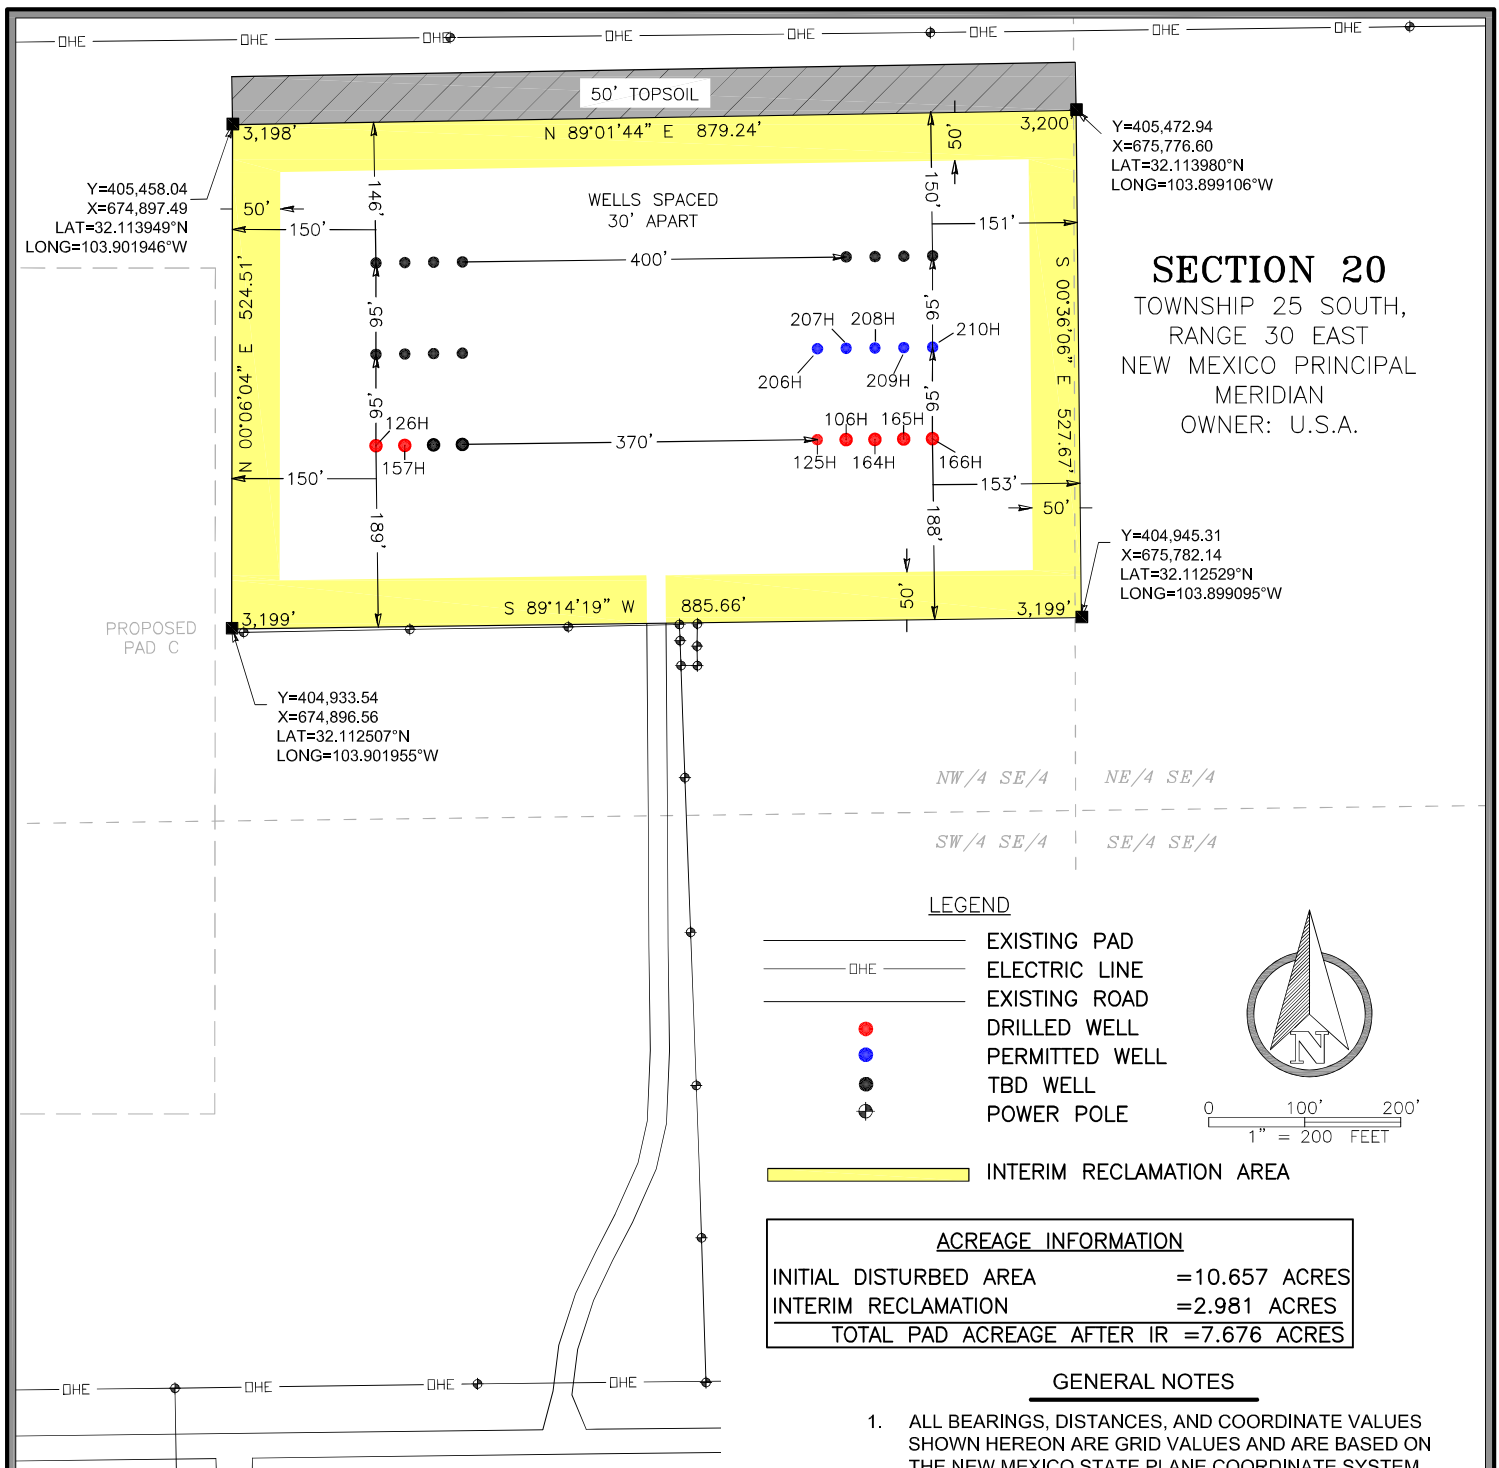

I, TIM C. PAPPAS, NEW MEXICO PROFESSIONAL SURVEYOR NO. 21209, DO HEREBY CERTIFY THAT THIS SURVEY PLAT AND THE ACTUAL SURVEY ON THE GROUND UPON WHICH IT IS BASED WERE PERFORMED BY ME OR UNDER MY DIRECT SUPERVISION; THAT I AM RESPONSIBLE FOR THIS SURVEY, THAT THIS SURVEY MEETS THE MINIMUM STANDARDS FOR SURVEYING IN NEW MEXICO, AND THAT IS TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF.

Tim C. Pappas 20 March 2025

TIM C. PAPPAS
REGISTERED PROFESSIONAL LAND SURVEYOR
STATE OF NEW MEXICO NO. 21209



2821 West 7th Street, Suite 200
Fort Worth, TX 76107
Ph: 817.349.9800 - Fax: 979.732.5271
TBPE Firm 17957 | TBPLS Firm 10193887
www.fscinc.net
© COPYRIGHT 2024 - ALL RIGHTS RESERVED

XTO PERMIAN OPERATING, LLC

**AN INTERIM RECLAMATION
DIAGRAM FOR:
POKER LAKE UNIT
20-17/20-8 BD PAD D**

POKER LAKE UNIT 20-17/20-8 BD PAD D
LOCATED 1,773 FEET FROM THE EAST LINE
AND 1,793 FEET FROM THE SOUTH LINE OF
SECTION 20, TOWNSHIP 25 SOUTH, RANGE 30
EAST, N.M.P.M. EDDY COUNTY, NEW MEXICO

DATE:	3-20-2025	PROJECT NO:	2017040549
DRAWN BY:	LM	SCALE:	1" = 200'
CHECKED BY:	CH	SHEET:	1 OF 1
FIELD CREW:	RE	REVISION:	

Well Site Locations

The results of the Poker Lake Unit 20-17/20-8 BD Development Program will develop economic quantities of oil and gas in the Poker Lake Unit 20-17/20-8 BD with multiple primary formations targeted. Well locations are determined based on cross-section variations and details. Locations will be selected to minimize the likelihood of encountering faults and/or drilling hazards while still targeting suitably productive zones.

If drilling results in an unproductive well, the well will be plugged and abandoned as soon as practical after the conclusion of production testing. Productive wells may be shut-in temporarily for BLM authorization for production activities and facilities.

Poker Lake Unit 20-17/20-8 BD Sec-20, T25 S, Range 30 E

Name	SHL N/S Footage (ft)	SHL N/S Footage Line	SHL E/W Footage (ft)	SHL E/W Footage Line
Poker Lake Unit 20-17 BD 201H	1434	FSL	1904	FWL
Poker Lake Unit 20-17 BD 202H	1433	FSL	1934	FWL
Poker Lake Unit 20-17 BD 203H	1432	FSL	1964	FWL
Poker Lake Unit 20-8 BD 204H	1431	FSL	1994	FWL
Poker Lake Unit 20-8 BD 205H	1431	FSL	2024	FWL
Poker Lake Unit 20-8 BD 206H	1813	FSL	1604	FEL
Poker Lake Unit 20-8 BD 207H	1813	FSL	1574	FEL
Poker Lake Unit 20-8 BD 208H	1813	FSL	1544	FEL
Poker Lake Unit 20-8 BD 209H	1813	FSL	1514	FEL
Poker Lake Unit 20-8 BD 210H	1813	FSL	1484	FEL

Surface Use Plan


1. Existing Roads

- A. From the intersection of Highway 285 and Longhorn Road, go Northeast on Longhorn Road (paved) Approx. 2.4 Miles. Take Slight Left and continue on Longhorn Road (Paved) for Approx 1.8 miles. Turn Left (Northeast) onto pipeline road number 1 road (Gravel) for Approx. 7.7 Miles. Turn Right (South) onto Lease Road for Approx. 1.5 Miles. Turn Right (East) and go approx. 0.8 Miles arriving at the existing road and the location is to the northwest. Transportation maps identifying existing roads that will be used to access the project area are included from FSC, Inc. marked as, 'Topographical and Access Road Map'.
- B. Transportation Plan identifying existing roads that will be used to access the project area is included from FSC, Inc. marked as, Topographical and Access Road Map. All equipment and vehicles will be confined to the routes shown on the Topographical and Access Map as provided by FSC, Inc. Maintenance of the access roads will continue until abandonment and reclamation of the well pads is completed.

2. New or Upgraded Access Roads

- A. **New Roads.** There are no new roads necessary to access the Poker Lake Unit 20-17/20-8 BD location.
- B. **Well Pads.** The well pads selected for development determines which existing roads will be upgraded.

- C. **Anticipated Traffic.** After well completion, travel to each well site will include one lease operator truck. The Central Battery will require one lease operator truck to continually travel to each well site to monitor the working order of the wells and to check well equipment for proper operation. Additional traffic will include one maintenance truck periodically throughout the year for pad upkeep and weed removal. Well service trips will include only the traffic necessary to work on the wells or provide chemical treatments periodically and as needed throughout the year.
- D. **Routing.** All equipment and vehicles will be confined to the travel routes laid out in the vicinity map provided by FSC INC unless otherwise approved by the BLM and applied for by XTO PERMIAN OPERATING LLC
- E. **Road Dimensions.** The maximum width of the driving surface of new roads will be 14 feet. The roads will be crowned and ditched with a 2% slope from the tip of the crown to the edge of the driving surface. The ditches will be 1 foot deep with 3:1 slope. The driving surface will be made of 8" rolled and compacted caliche.



Level Ground Section

- F. **Surface Material.** Surface material will be native caliche. The average grade of all roads will be approximately 3%.
- G. **Fence Cuts:** No.
- H. **Fences:** No.
- I. **Cattle Guards:** No.
- J. **Turnouts:** No.
- K. **Culverts:** No.
- L. **Cuts and Fills:** look at attached plats.
- M. **Topsoil.** Approximately 6 inches of topsoil (root zone) is stripped from the access road prior to any construction activity. The topsoil that was stripped will be spread along the edge of well pad as depicted in plat. The topsoil will be seeded with the proper seed mix designated by the BLM.
- N. **Maintenance.** The access road will be constructed and maintained as necessary to prevent soil erosion and accommodate all-weather traffic. The road will be crowned and ditched with water turnouts installed as necessary to provide for proper drainage along with access road route.
- O. **Drainage.** The access road and associated drainage structures will be constructed and maintained in accordance with road guidelines contained in the joint BLM/USFS publication: Surface Operating Standards for Oil and Gas Exploration and Development, The Gold Book, Fourth Edition and/or BLM Manual Section 9113 concerning road construction standards on projects subject to federal jurisdiction.

3. Location of Existing Wells

- A. See attached 1-mile radius well map.

4. Location of Existing Production Facilities

- A. **Production Facilities.** No New facility is required for the Poker Lake Unit 20-17/20-8 BD wells.
Once drilled and completed, the wells will flow to the Poker Lake Unit 20-17/20-8 BD battery.
- B. **Flowlines.** No further flowlines disturbance is requested.
- C. **Gas Pipeline.** No Gas Sales line is required for this well. No additional surface disturbance is needed.

- D. **Disposal Facilities.** Produced water will be hauled from location to a commercial or private disposal facility as needed.
- E. **Flare.** - Check in facility plot attached.
- F. **Aboveground Structures.** All permanent (on site six months or longer) aboveground structures constructed or installed on location and not subject to safety requirements will be painted earth-tone colors such as BLM Standard Environmental Color Chart (CC-001: June 2008) that reduce the visual impacts of the built environment.
- G. **Containment Berms.** Containment berms will be constructed completely around any production facilities designed. The containment berms will be constructed of compacted caliche, be sufficiently impervious, away from cut or fill areas.
- H. **Electrical.** No additional electrical is required for this well. No additional surface disturbance is needed.
- I. **Facility Description-** Kindly see the facility plot attached.

5. Location and Types of Water Supply

The well will be drilled using a combination of water mud systems as outlined in the Drilling Program. Water composition depends on the mud type needed per formation to protect useable water. Fresh water is trucked to location for use in surface casing drilling and cementing. All other water is either brackish (3P) or raw produced water (XOM) that is all piped from either a pipeline or a pond 32.1483028, -103.922338) to the drilling location.

Anticipated water usage for drilling includes an estimated 50,000 barrels of water to drill a horizontal well in a combination of fresh water and brine as detailed in the mud program in the drilling plans. These volumes are calculated for ~1.5bbls per foot of hole drilled with excess to accommodate any lost circulation or wash out that may occur. Actual water volumes used during operations will depend on the depth of the well, length of horizontal sections, and the losses that may occur during the operation.

Temporary water lines will be permitted via a Temporary Water Line Approved Decision letter and/or any necessary Right of Way Grants as needed based on drilling and completion schedules. Well completion is expected to require approximately 550,000 barrels of water per horizontal well. Actual water volumes used during operations will depend on the depth of the well and length of horizontal sections

6. Construction Activities – No new construction

Construction, reclamation, and/or routine maintenance will not be conducted during periods when the soil conditions for construction could lead to impacts to the surrounding environment, or when watershed damage is likely to occur because of these activities.

Any construction material that may be required for surfacing of the drill pad and access road will be from a contractor having a permitted source of materials within the general area. No construction materials will be removed from federal lands without prior approval from the appropriate surface management agency.

Well Pad. No New construction

7. Methods for Handling Waste

- **Cuttings.** The well will be drilled utilizing a closed-loop mud system. Drill cuttings will be held in roll-off style mud boxes and taken to a New Mexico Oil Conservation Division (NMOCD) approved disposal site.
- **Drilling Fluids.** These will be contained in steel mud pits and then taken to a NMOCD approved commercial disposal facility.

- **Produced Fluids.** Water produced from the well will be held temporarily in steel tanks and then taken to a NMOCD approved commercial disposal facility. Oil produced during operations will be stored in s until sold.
- **Sewage.** Portable, self-contained toilets will be provided for human waste disposal. Upon completion of drilling and completion activities, or as required, the toilet holding tanks will be pumped and the contents thereof disposed of in an approved sewage disposal facility. All state and local laws and regulations pertaining to the disposal of human and solid waste will be complied with. This equipment will be properly maintained during the drilling and completion operations and will be removed when all operations are complete.
- **Garbage and Other Waste Materials.** All garbage, junk and non-flammable waste materials will be contained in a self-contained, portable dumpster or trash cage, to prevent scattering and will be removed and deposited in an approve sanitary landfill. Immediately after drilling all debris and other waste materials on and around the well location not contained in the trash cage will be cleaned up and removed from the location. No potentially adverse materials or substances will be left on the location.
- **Debris.** Immediately after removal of the drilling rig, all debris and other waste materials not contained in the trash cage will be cleaned and removed from the well location. No potential adverse materials or substances will be left on location.
- **Hazardous Materials.**
 - i. All drilling wastes identified as hazardous substances by the Comprehensive Environmental Response Compensation Liability Act (CERCLA) removed from the location and not reused at another drilling location will be disposed of at a hazardous waste facility approved by the U.S. Environmental Protection Agency (EPA).
 - ii. XTO PERMIAN OPERATING LLC and its contractors will comply with all applicable Federal, State and local laws and regulations, existing or hereafter enacted promulgated, regarding any hazardous material, as defined in this paragraph, that will be used, produced, transported or stored on the oil and gas lease. "Hazardous material" means any substance, pollutant or contaminant that is listed as hazardous under the CERCLA of 1980, as amended, 42 U.S.C 9601 et seq., and its regulation. The definition of hazardous substances under CERLCA includes any 'hazardous waste' as defined in the RCRA of 1976, as amended, 42 U.S.C. 6901 et seq., and its regulations. The term hazardous material also includes any nuclear or nuclear by-product material as defined by the Atomic Energy Act of 1954, as amended, 42 U.C.S. 2011 et seq. The term does not include petroleum, including crude oil or any fraction thereof that is not otherwise specifically listed or designated as a hazardous substance under CERCLA Section 101 (14) U.S.C. 9601 (14) nor does the term include natural gas.
 - iii. No hazardous substances or wastes will be stored on the location after completion of the well.
 - iv. Chemicals brought to location will be on the Toxic Substance Control Act (TSCA) approved inventory list.
 - v. All undesirable events (fires, accidents, blowouts, spills, discharges) as specified in Notice to Lessees (NTL) 3A will be reported to the BLM Carlsbad Field Office. Major events will be reported verbally within 24 hours, followed by a written report within 15 days. "Other than Major Events" will be reported in writing within 15 days.

8. Ancillary Facilities

- A. **Ancillary Facilities.** No off-pad ancillary facilities are planned during the exploration phase including, but not limited to campsites, airstrips or staging areas.

9. Well Site Layout

Rig Plat Diagrams: There is 1 multi-well pad in the Poker Lake Unit 20-17/20-8 BD lease. This will allow enough space for cuts and fills, topsoil storage, and storm water control. Interim reclamation of these pads is anticipated after the drilling and completion of all wells on the pad. A well site layout for the pad is attached.

- Pad B is a 26-well pad expected to be 875.50'x521.60'.

Closed-Loop System: There will be no reserve pit as each well will be drilled utilizing a closed loop mud system. The closed loop system will meet the NMOCD requirements 19.15.17.

V-Door Orientation: These pads were staked with multiple v-door orientations. The following list is from West to East in accordance with the staked section and as agreed upon with Zane Kirsch, BLM Natural Resource Specialist, present at on-site inspection.

- Pad A has a V-Door Orientation: East
All equipment and vehicles will be confined to the approved disturbed areas of this APD (i.e., access road, well pad and topsoil storage areas)

10. Plans for Surface Reclamation:

XTO Permian Operating, LLC. requests a variance from interim reclamation until all drilling and completion activities have been finished on the pads as these are multi-well pads where drilling and completion will be consecutive with the other wells on the pad. Once activities are completed, XTO Permian Operating, LLC. will coordinate interim reclamation with the appropriate BLM personnel or use the following plan:

Non-Commercial Well (Not Productive), Interim & Final Reclamation:

Definition: Reclamation includes disturbed areas where the original landform and a natural vegetative community will be restored, and it is anticipated the site will not be disturbed for future development.

Reclamation Standards:

The portions of the pad not essential to production facilities or space required for workover operations will be reclaimed and seeded as per BLM requirements for interim reclamation. (See Interim Reclamation plats attached).

All equipment and trash will be removed, and the surfacing material will be removed from the well pad and road and transported to the original caliche pit or used to maintain other roads. The location will then be ripped and seeded.

The original stockpiled topsoil will be spread over the areas being reclaimed and the original landform will be restored for all disturbed areas including well pads, production facilities, roads, pipelines, and utility corridors as close as possible to the original topography. The location will then be ripped and seeded.

A self-sustaining, vigorous, diverse, native (or otherwise approved) plant community will be established on the site with a density sufficient to control erosion and invasion by non-native plants and to re-establish wildlife habitat or forage production. At a minimum, the established plant community will consist of species included in the seed mix and/or desirable species occurring in the surrounding natural vegetation.

Erosion features are equal to or less than surrounding area and erosion control is sufficient so that water naturally infiltrates into the soil and gulying, head cutting, slumping, and deep or excessive rills (greater than 3 inches) are not observed.

The site will be free of State or County listed noxious weeds, oil field debris and equipment, and contaminated soil. Invasive and non-native noxious weeds will be controlled.

Seeding:

- **Seedbed Preparation:** Initial seedbed preparation will consist of recontouring to the appropriate interim or final reclamation standard. All compacted areas to be seeded will be ripped to a minimum depth of 18 inches with a minimum furrow spacing of 2 feet, followed by recontouring the surface and then evenly spreading the stockpiled topsoil. Prior to seeding, the seedbed will be scarified to a depth of no less than 4-6 inches. If the site is to be broadcast seeded, the surface will be left rough enough to trap seed and snow, control erosion, and increase water infiltration.
- If broadcast seeding is to be used and is delayed, final seedbed preparation will consist of contour cultivating to a depth of 4-6 inches within 24 hours prior to seeding, dozer tracking, or other imprinting to break the soil crust and create seed germination micro-sites.
- **Seed Application.** Seeding will be conducted no more than two weeks following completion of final seedbed preparation. A certified weed-free seed mix designed by the BLM to meet reclamation standards will be used.
- If the site is harrowed or dragged, seed will be covered by no more than 0.25 inch of soil.

11. Surface Ownership

- The Poker Lake Unit 20-17/20-8 BD is 100% of the surface is under the administrative jurisdiction of the Bureau of Land Management.
- The surface is multiple use with the primary uses of the region for grazing and to produce oil and gas.

12. Other Information

Surveying

- **Well Sites.** Well pad locations have been staked. Surveys of the Existing access roads and well pad locations have been completed by FSC, Inc, a registered professional land surveyor. Center stake surveys with access roads have been completed on State and Federal lands with Zane Kirsch, Bureau of Land Management Natural Resource Specialist in attendance, on February 15, 2022.
- **Cultural Resources – Archaeology:** A Class III Cultural Resources Examination was completed previously.
- **Dwellings and Structures.** There are no dwellings or structures within 2 miles of this location.

Soils and Vegetation

Environmental Setting. Soils are classified as Simona Gravelly Fine Sandy Loam and Simona-Bippus Complex. Simona soils are found on alluvial fans and plains and form in mixed alluvium and/or Aeolian sands. Bippus soils are found on alluvial fans and floodplains and form in mixed alluvium. The Simona-Bippus soils are dominant to the east and the Simona Gravelly Fine Sandy Loams are dominant to the West. Dominant vegetation species include: mesquite, sumac snakeweed, and various forbs and grasses. Ground cover is minimal, offering 90 percent visibility.

- **Traffic.** No truck traffic will be operated during periods or in areas of saturated ground when surface rutting could occur. The access road will be constructed and maintained as necessary to prevent soil erosion and accommodate all-weather traffic. The road will be crowned and ditched with water turnouts installed as necessary to provide for proper drainage along the access road route.

- **Water.** There is no permanent or live water in the immediate or within the project area.

13. Bond Coverage

Bond Coverage is Nationwide. Bond Number: COB000050

Onsite- The XTO Permian Operating, LLC. representatives and BLM NRS were on location for onsite on 3/10/2021.

Operator's Representatives:

The XTO PERMIAN OPERATING LLC representatives for ensuring compliance of the surface use plan are listed below:

Surface:

Robert Bartels
Project Execution Planner
XTO Energy, Incorporated
6401 Holiday Hill Road Bldg 5
Midland, Texas 79701
robert.e.bartels@exxonmobil.com
Phone: (406) 478-3671

APD ID: 10400100957

Submission Date: 09/23/2024

Operator Name: XTO PERMIAN OPERATING LLC

Well Name: POKER LAKE UNIT 20-8 BD

Well Number: 208H

Well Type: OIL WELL

Well Work Type: Drill

Section 1 - General

Would you like to address long-term produced water disposal? NO

Section 2 - Lined

Would you like to utilize Lined Pit PWD options? N

Produced Water Disposal (PWD) Location:

PWD surface owner:

PWD disturbance (acres):

Other PWD Surface Owner Description:

Lined pit PWD on or off channel:

Lined pit PWD discharge volume (bbl/day):

Lined pit

Pit liner description:

Pit liner manufacturers

Precipitated solids disposal:

Decribe precipitated solids disposal:

Precipitated solids disposal

Lined pit precipitated solids disposal schedule:

Lined pit precipitated solids disposal schedule

Lined pit reclamation description:

Lined pit reclamation

Leak detection system description:

Leak detection system

Well Name: POKER LAKE UNIT 20-8 BD

Well Number: 208H

Lined pit Monitor description:

Lined pit Monitor

Lined pit: do you have a reclamation bond for the pit?

Is the reclamation bond a rider under the BLM bond?

Lined pit bond number:

Lined pit bond amount:

Additional bond information

Section 3 - Unlined

Would you like to utilize Unlined Pit PWD options? N

Produced Water Disposal (PWD) Location:

PWD disturbance (acres):

PWD surface owner:

Other PWD Surface Owner Description:

Unlined pit PWD on or off channel:

Unlined pit PWD discharge volume (bbl/day):

Unlined pit

Precipitated solids disposal:

Describe precipitated solids disposal:

Precipitated solids disposal

Unlined pit precipitated solids disposal schedule:

Unlined pit precipitated solids disposal schedule

Unlined pit reclamation description:

Unlined pit reclamation

Unlined pit Monitor description:

Unlined pit Monitor

Do you propose to put the produced water to beneficial use?

Beneficial use user

Estimated depth of the shallowest aquifer (feet):

Precipitated Solids Permit

Does the produced water have an annual average Total Dissolved Solids (TDS) concentration equal to or less than that of the existing water to be protected?

TDS lab results:

Geologic and hydrologic

Well Name: POKER LAKE UNIT 20-8 BD

Well Number: 208H

State

Unlined Produced Water Pit Estimated

Unlined pit: do you have a reclamation bond for the pit?

Is the reclamation bond a rider under the BLM bond?

Unlined pit bond number:

Unlined pit bond amount:

Additional bond information

Section 4 -

Would you like to utilize Injection PWD options? N

Produced Water Disposal (PWD) Location:

PWD surface owner:

PWD disturbance (acres):

Other PWD Surface Owner Description:

Injection PWD discharge volume (bbl/day):

Injection well mineral owner:

Injection well type:

Injection well number:

Injection well name:

Assigned injection well API number?

Injection well API number:

Injection well new surface disturbance (acres):

Minerals protection information:

Mineral protection

Underground Injection Control (UIC) Permit?

UIC Permit

Section 5 - Surface

Would you like to utilize Surface Discharge PWD options? N

Produced Water Disposal (PWD) Location:

PWD surface owner:

PWD disturbance (acres):

Other PWD Surface Owner Description :

Surface discharge PWD discharge volume (bbl/day):

Surface Discharge NPDES Permit?

Surface Discharge NPDES Permit attachment:

Surface Discharge site facilities information:

Surface discharge site facilities map:

Well Name: POKER LAKE UNIT 20-8 BD

Well Number: 208H

Section 6 -

Would you like to utilize Other PWD options? N

Produced Water Disposal (PWD) Location:

PWD surface owner:

PWD disturbance (acres):

PWD Surface Owner Description:

Other PWD discharge volume (bbl/day):

Other PWD type description:

Other PWD type

Have other regulatory requirements been met?

Other regulatory requirements

APD ID: 10400100957

Submission Date: 09/23/2024

Operator Name: XTO PERMIAN OPERATING LLC

Well Name: POKER LAKE UNIT 20-8 BD

Well Number: 208H

Well Type: OIL WELL

Well Work Type: Drill

Highlighted data
reflects the most
recent changes
[Show Final Text](#)

Bond

Federal/Indian APD: FED

BLM Bond number: COB000050

BIA Bond number:

Do you have a reclamation bond? NO

Is the reclamation bond a rider under the BLM bond?

Is the reclamation bond BLM or Forest Service?

BLM reclamation bond number:

Forest Service reclamation bond number:

Forest Service reclamation bond attachment:

Reclamation bond amount:

Reclamation bond rider amount:

Additional reclamation bond information attachment:

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
<https://www.emnrd.nm.gov/ocd/contact-us>

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 463639

CONDITIONS

Operator: XTO PERMIAN OPERATING LLC. 6401 HOLIDAY HILL ROAD MIDLAND, TX 79707	OGRID: 373075
	Action Number: 463639
	Action Type: [C-101] BLM - Federal/Indian Land Lease (Form 3160-3)

CONDITIONS

Created By	Condition	Condition Date
mvenkatesh	Cement is required to circulate on both surface and intermediate1 strings of casing.	5/15/2025
mvenkatesh	If cement does not circulate on any string, a Cement Bond Log (CBL) is required for that string of casing.	5/15/2025
ward.rikala	Notify the OCD 24 hours prior to casing & cement.	6/13/2025
ward.rikala	File As Drilled C-102 and a directional Survey with C-104 completion packet.	6/13/2025
ward.rikala	Once the well is spud, to prevent ground water contamination through whole or partial conduits from the surface, the operator shall drill without interruption through the fresh water zone or zones and shall immediately set in cement the water protection string.	6/13/2025
ward.rikala	Oil base muds are not to be used until fresh water zones are cased and cemented providing isolation from the oil or diesel. This includes synthetic oils. Oil based mud, drilling fluids and solids must be contained in a steel closed loop system.	6/13/2025
