

Submit a Copy To Appropriate District
Office
District I – (575) 393-6161
1625 N. French Dr., Hobbs, NM 88240
District II – (575) 748-1283
811 S. First St., Artesia, NM 88210
District III – (505) 334-6178
1000 Rio Brazos Rd., Aztec, NM 87410
District IV – (505) 476-3460
1220 S. St. Francis Dr., Santa Fe, NM
87505

State of New Mexico
Energy, Minerals and Natural Resources

Form C-103
Revised July 18, 2013

OIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, NM 87505

WELL API NO. 30-059-20266
5. Indicate Type of Lease STATE ☐ FEE ☒
6. State Oil & Gas Lease No.
7. Lease Name or Unit Agreement Name BRAVO DOME CARBON DIOXIDE GAS UNIT
8. Well Number #311
9. OGRID Number 16696
10. Pool name or Wildcat BRAVO DOME CARBON DIOXIDE GAS UNIT

SUNDRY NOTICES AND REPORTS ON WELLS (DO NOT USE THIS FORM FOR PROPOSALS TO DRILL OR TO DEEPEN OR PLUG BACK TO A DIFFERENT RESERVOIR. USE "APPLICATION FOR PERMIT" (FORM C-101) FOR SUCH PROPOSALS.)	
1. Type of Well: Oil Well ☐ Gas Well ☐ Other ☒ CO2 WELL	
2. Name of Operator OXY USA INC.	
3. Address of Operator PO BOX 4294, HOUSTON, TX 77210	
4. Well Location Unit Letter <u>G</u> : <u>1650</u> feet from the <u>NORTH</u> line and <u>1650</u> feet from the <u>EAST</u> line Section <u>31</u> Township <u>21N</u> Range <u>34E</u> NMPM County <u>UNION</u>	
11. Elevation (Show whether DR, RKB, RT, GR, etc.)	

12. Check Appropriate Box to Indicate Nature of Notice, Report or Other Data

NOTICE OF INTENTION TO: PERFORM REMEDIAL WORK ☐ PLUG AND ABANDON ☐ TEMPORARILY ABANDON ☐ CHANGE PLANS ☐ PULL OR ALTER CASING ☐ MULTIPLE COMPL ☐ DOWNHOLE COMMINGLE ☐ CLOSED-LOOP SYSTEM ☐ OTHER: ☐		SUBSEQUENT REPORT OF: REMEDIAL WORK ☐ ALTERING CASING ☐ COMMENCE DRILLING OPNS. ☐ P AND A ☒ CASING/CEMENT JOB ☐ OTHER: ☐	
---	--	---	--

13. Describe proposed or completed operations. (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work). SEE RULE 19.15.7.14 NMAC. For Multiple Completions: Attach wellbore diagram of proposed completion or recompletion.

THE FINAL WELLBORE AND PA JOB NOTES ARE ATTACHED. CUT AND CAP WAS COMPLETE ON 6/21/2025.

Spud Date:

Rig Release Date:

I hereby certify that the information above is true and complete to the best of my knowledge and belief.

SIGNATURE Stephen Janacek TITLE REGULATORY ENGINEER DATE 7/1/2025

Type or print name STEPHEN JANACEK E-mail address: STEPHEN_JANACEK@OXY.COM PHONE: 713-493-1986

For State Use Only

APPROVED BY: _____ TITLE _____ DATE _____

Conditions of Approval (if any):


FINAL WELLBORE

Bravo Dome Unit 2134 311

30-059-20266-0000

Union

String 1
OD 9.625 in
TD 710 ft
TOC 0 ft

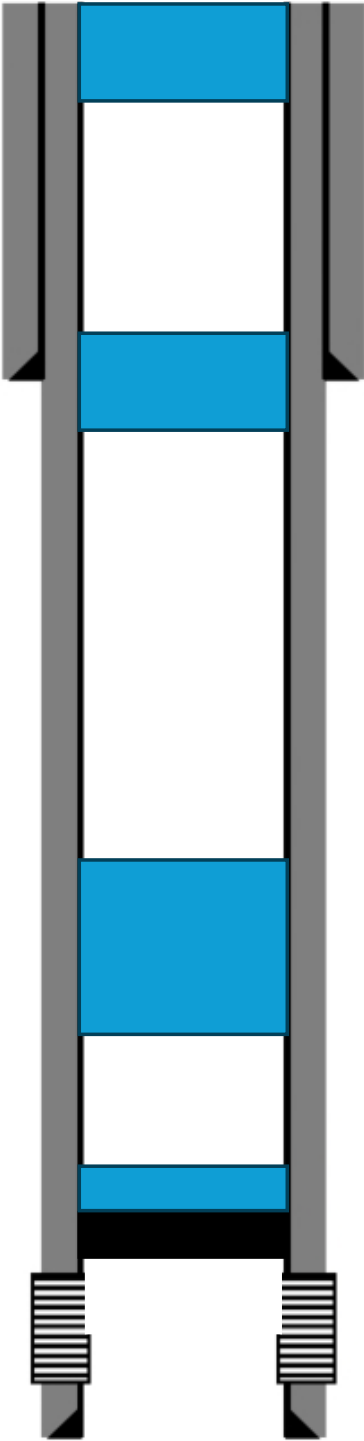

SPOT 40 SX CMT 150' TO SURFACE

SPOT 27 SX CMT 760' TO 616'

SPOT 100 SX CMT 2070' TO 1490'

CIBP SET AT 2395'. SPOT 35 SX CMT 2395' TO 2201'

Prod Zone
2402 ft
2604 ft

String 2
OD 7 in
TD 2708 ft
TOC 0 ft

BRAVO DOME CARBON DIOXIDE GAS UNIT #311**30-059-20266****PA JOB NOTES**

Start Date	Remarks
6/12/2025	crew travel time
6/12/2025	Pre-Trip inspection, road rig & cmt Equip from Bravo Dome #1934 202L to Bravo Dome #2134 311G
6/12/2025	spot base beam, ND flowline
6/12/2025	TBG 150 psi / CSG 0 psi
6/12/2025	spot & RU Pulling Unit, RU cmt equip.
6/12/2025	tbg bled down to 0 psi
6/12/2025	change over equip from 2 3/8" tbg to 3 1/2" tbg, BOPE rams,tbg elevators and slips
6/12/2025	break wellhead bolts and replace w/new bolts, bolts very hard to break
6/12/2025	went to Bravo Dome #1834 031G to replace 3.5" master valve
6/12/2025	crew travel time
6/13/2025	crew travel time
6/13/2025	Review JSA, Daily Rig Inspection
6/13/2025	TBG 150 psi / CSG 0 psi
6/13/2025	bled off tbg pressure, tbg bled down to 0 psi
6/13/2025	pump 25 bbls fresh water down tbg, tbg went on vac.
6/13/2025	ND wellhead, NU BOPE, RU work floor
6/13/2025	work stuck pkr, got pkr released
6/13/2025	LD 74 jts 3.5" Duoline tbg, LD pkr
6/13/2025	change over equip from 3.5" tbg to 2 3/8" tbg
6/13/2025	wait on renegade wireline
6/13/2025	RU wireline, pick up & RIH w/ gauge ring for 7" csg, Pick up & RIH w/ 7" CIBP, set plug @2395', RIH w/ radial Bond tools, run CBL from 2395' to Surface, RD wireline
6/13/2025	secure well SION
6/13/2025	crew travel time
6/14/2025	crew travel time
6/14/2025	Review JSA, Daily Rig Inspection
6/14/2025	CSG 0 psi
6/14/2025	pick up & RIH w/ 2.375" tbg open ended, tag CIBP @2395' w/77 jts
6/14/2025	circulate 100 bbls FWG
6/14/2025	spot 35 sxs class C cmt, displace 8 bbls, ctoc@2195'
6/14/2025	pull up out of cmt, pulled 20 stands
6/14/2025	wait on cmt
6/14/2025	RIH w/ tbg, tag top of cmt @2201'
6/14/2025	LD tbg leaving EOT@2070' w/67 jts
6/14/2025	load and test csg to 500 psi, watch for 15 min., held good
6/14/2025	spot 100 sxs class C cmt, displace 6 bbls, ctoc@1490'

6/14/2025	LD 43 jts putting EOT@760' w/24 jts in hole
6/14/2025	spot 27 sxs class C cmt, displace 2.5 bbls, ctoc@616'
6/14/2025	LD tbg leaving EOT@150' w/5 jts in hole
6/14/2025	spot 40 sxs class C cmt to Surface, wash up equip.
6/14/2025	RD workfloor, ND BOPE, attempt to put 1" hose down surface pipe, no luck, secure well SION
6/14/2025	crew travel time
6/15/2025	crew travel time
6/15/2025	Review JSA, Daily Rig Inspection
6/15/2025	well 0 psi
6/15/2025	ND B1 flange, verify cmt at surface
6/15/2025	RD Pulling Unit, RD cement equip. clean up loc., prep for rig move
6/15/2025	secure well SION
6/15/2025	crew travel time
6/21/2025	crew travel time
6/21/2025	Review JSA, Daily equip. inspection
6/21/2025	RU cmt Equip.
6/21/2025	waiting on Hudson trucks
6/21/2025	RIH w/ 100' of 1" pvc, hook up Cmt trucl, circulate 20 sxs class C cmt to surface , wash up cmt tlines
6/21/2025	DR cement Equip., prep for rig move
6/21/2025	Wellhead Cut & Cap/ completed 6/21/2025



Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
<https://www.emnrd.nm.gov/ocd/contact-us>

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 480447

CONDITIONS

Operator: OXY USA INC P.O. Box 4294 Houston, TX 772104294	OGRID: 16696
	Action Number: 480447
	Action Type: [C-103] Sub. Plugging (C-103P)

CONDITIONS

Created By	Condition	Condition Date
loren.diede	None	7/3/2025
