

Well Name: NAVAJO	Well Location: T31N / R17W / SEC 5 / SESE / 36.92421 / -108.647751	County or Parish/State: SAN JUAN / NM
Well Number: 4	Type of Well: INJECTION - ENHANCED RECOVERY	Allottee or Tribe Name: SHIPROCK
Lease Number: 142060365	Unit or CA Name:	Unit or CA Number:
US Well Number: 3004511037	Operator: R J ENTERPRISES	

Subsequent Report

Sundry ID: 2870389

Type of Submission: Subsequent Report	Type of Action: Plug and Abandonment
Date Sundry Submitted: 08/27/2025	Time Sundry Submitted: 03:25
Date Operation Actually Began: 08/04/2025	

Actual Procedure: Well plugged by the Navajo Nation, contractor Walsh Engineering and Production. Work completed August 5, 2025. Daily Events 8/4 SICP=0PSI. MIRU Cementers and TWG. JHA with crew. Attempted to establish injection rate down tbg. Loaded with 1 bbl. Pressured to 600psi. Lost 240 psi in 1 minute. Worked pressure again with same results. RU TWG for JB/GR run. Got all the way to CICR at 997' POH and rig up for CBL run. Tagged CICR at 997', logged on the way out of the hole. Finished with CBL. Log showed free pipe from 936' to 536'. Emailed logs to engineering and BLM. Will be perforating with 4 shots at 900'. Shot 4 holes at 900'. POH verified all shots fired. RD TWG. Established injection rate of 1 bpm at 900 psi. M&P 34 sks, 39.1 cuft, 7 bbls, 15.8#, class G neat cement. 530 psi at .6 bpm. SD at 7 bbls cement pumped. Tbg pressure at 240 psi. SWIFN. Off location at 20:00 8/5 JHA with crew. Cutoff wellhead from casing string. Topped off DHM and cellar with 40 sks, 46 cuft, 8.2 bbls, class G neat cement. RD cementers. Crew off location at 11:30.


SR Attachments

Actual Procedure

SR_ABD_WBS_U_4_3004511037_20250827152426.pdf

BLM Point of Contact

BLM POC Name: KENNETH G RENNICK	BLM POC Title: Petroleum Engineer
BLM POC Phone: 5055647742	BLM POC Email Address: krennick@blm.gov
Disposition: Accepted	Disposition Date: 08/28/2025
Signature: Kenneth Rennick	

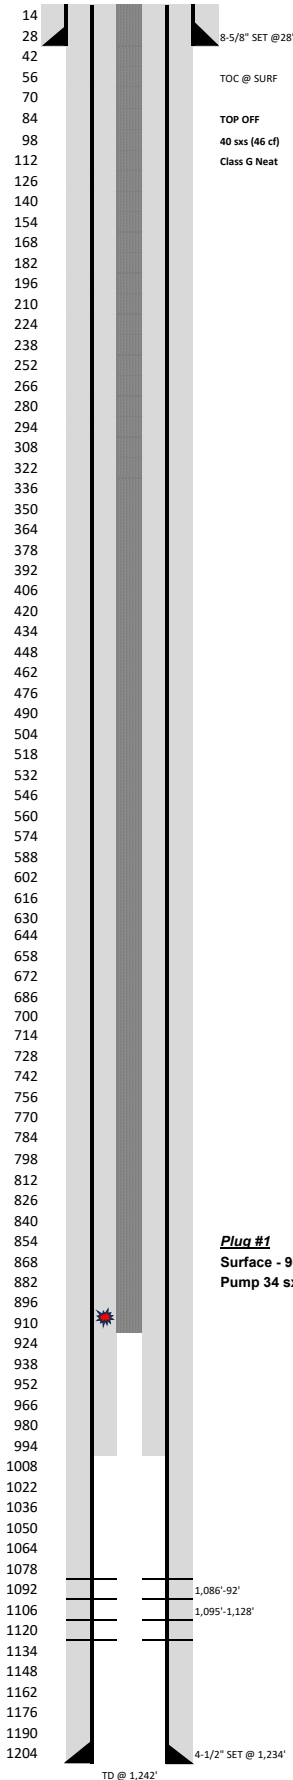

WELL: NAVAJO U #004 (SWD)	COUNTY: SAN JUAN	API #: 30-045-11037
FIELD: HORSESHOE GALLUP	STATE: NM	P&A 8/5/2025
FORMATION: GALLUP	LEASE: 14-20-0603-65	
LOCATION: 660' FSL & 660' FEL	SECTION: 5	TOWNSHIP: 31N
TD: 1,242'	PBTD: UNK	ELEV GL: 5,286'
		ELEV-RKB: UNK
		RANGE: 17W

P&A Summary

8/4
SICP=OPSI. MIRU Cementers and TWG. JHA with crew. Attempted to establish injection rate down tbg. Loaded with 1 bbl. Pressured to 600psi. Lost 240 psi in 1 minute. Worked pressure again with same results. RU TWG for JB/GR run. Got all the way to CICR at 997' POH and rig up for CBL run. Tagged CICR at 997', logged on the way out of the hole. Finished with CBL. Log showed free pipe from 936' to 536'. Emailed logs to engineering and BLM. Will be performing with 4 shots at 900'. Shot 4 holes at 900'. POH verified all shots fired. RD TWG. Established injection rate of 1 bpm at 900 psi. M&P 34 sxs, 39.1 cuft, 7 bbls, 15.8#, class G neat cement. 530 psi at .6 bpm. SD at 7 bbls cement pumped. Tbg pressure at 240 psi. SWIFN. Off location at 20:00

8/5
JHA with crew. Cutoff wellhead from casing string. Topped off DHM and cellar with 40 sxs, 46 cuft, 8.2 bbls, class G neat cement. RD cementers. Crew off location at 11:30.

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
<https://www.emnrd.nm.gov/ocd/contact-us>

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 504835

CONDITIONS

Operator: R - J ENTERPRISES P.O. Box 51 Farmington, NM 874990051	OGRID: 18322
	Action Number: 504835
	Action Type: [C-103] Sub. Plugging (C-103P)

CONDITIONS

Created By	Condition	Condition Date
loren.diede	Accepted for Record	9/10/2025
