

FINAL WELLBORE 8/16/2024

GLENN RYAN #022

30-025-25576

Surf Lat 32.0414238
Surf Long -103.1188126


PERF AT 155' AND AT 50'. SPOT 120 SX
CMT 354' TO SURFACE AND SQZ AT
SURFACE.

SPOT 35 SX 680'-354'.

SPOT 25 SX CMT 1085' TO 836' (TAG).

SPOT 35 SX CMT 2656' TO 2320' (TAG).

RIH WITH BIT AND TAG AT 3414'. SET
CIBP AT 3323'. SPOT 25 SX CMT 3323'
TO 3073' (TAG).

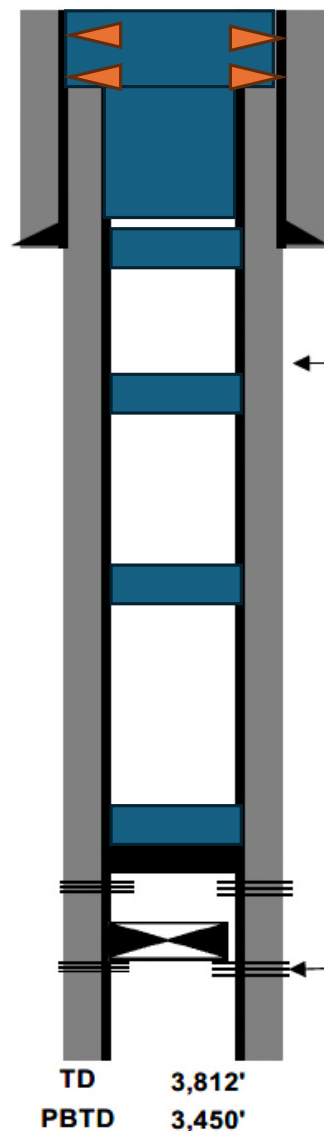

Surface Casing
12 1/4 in. hole @ 513 '
8 5/8 in. casing @ 513 '
w/ 500 sx cement TOC- Surf

Production Casing
7 7/8 in. hole @ 3812 '
5 1/2 in. casing @ 3812 '
w/ 800 sx cement TOC- Surf

[38760] LEONARD; QUEEN, SOUTH
Perfs
Top 3,377'
Bottom 3,428'

RBP at 3450' (above Penrose perfs)
Top 3,509'
Bottom 3,551'

TD 3,812'
PBD 3,450'

PA Job Notes
Glenn Ryan 22
30-025-25576

Start Date	Remarks
8/6/2024	RIG CREW TRAVEL
8/6/2024	TGSM , PRE TRIP INSPECTION
8/6/2024	ROAD RIG FROM GLEN RYAN 29 TO GLEN RYAN 22
8/6/2024	TGSM , HAZARD HUNT
8/6/2024	TIGHT LOCATION , SPOT IN REVERSE UNIT , BASE BEAM , TANKS , RACKS AND CATWALK
8/6/2024	RUSU
8/6/2024	LUNCH
8/6/2024	LAYDOWN POLISH ROD , STUFFING BOX
8/6/2024	RIG UP WORKFLOOR AND ROD TABLE
8/6/2024	UNSEAT PUMP , LAYDOWN 43 - 7/8" RODS , 93 - 3/4" RODS , PUMP
8/6/2024	CHANGE OVER EQUIPMENT , RIG DOWN WORKFLOOR
8/6/2024	SPOT IN , UNLOAD AND FUNCTION TEST BOP - GOOD
8/6/2024	SECURE WELL , SION
8/6/2024	RIG CREW TRAVEL HOME
8/7/2024	RIG CREW TRAVEL TO LOCATION
8/7/2024	TGSM , DISCUSSED HAND PLACEMENT , HAZARD HUNT
8/7/2024	0 PSI
8/7/2024	0 PSI
8/7/2024	NIPPLE DOWN WELLHEAD , REPLACE TUBING HEAD W/ RIGS SCREW ON FLANGE WELLHEAD
8/7/2024	NIPPLE UP BOP
8/7/2024	RIG UP WORKFLOOR , SPOT IN PIPE RACKS AND CATWALK
8/7/2024	LAYDOWN 35 JTS OF 2 7/8" TBG
8/7/2024	LUNCH
8/7/2024	LAYDOWN A TOTAL OF 108 JTS , SN , PERF SUB , MUD JT , BP
8/7/2024	MOVE OUT OLD TBG , SPOT IN WORKSTRING
8/7/2024	SECURE WELL , SION
8/7/2024	RIG CREW TRAVEL HOME
8/12/2024	RIG CREW TRAVEL TIME
8/12/2024	SAFETY MEETING, REVIEW JSA, TALK ABOUT TODAYS OPERATIONS, HAND SAFETY AND HYDRATION. HAZARD HUNT
8/12/2024	CHECK WELLHEAD PRESSURES AND SET UP TUBBING TO RIH
8/12/2024	RIH WITH A 4 3/4 BIT AND A 4 3/4 STRING MILL WITH 105 JTS 2 7/8 I-80 TAGGING AT 3,414'
8/12/2024	LUNCH BREAK FOR CREW
8/12/2024	POOH WITH 105 JTS AND LAY DOWN STRING MILL AND PICK UP CIBP
8/12/2024	RIH WITH 5 1/2 CIBP, SET PLUG AT 3323' 105 jts
8/12/2024	CIRCULATE THE WELL WITH 84 BBLs OF BRINE
8/12/2024	PREPARE WELL TO SHUT IN OVERNIGHT

8/12/2024	RIG CREW TRAVEL TIME
8/13/2024	CREW TRAVEL TIME
8/13/2024	REVIEW JSA DAILY WORK PLAN AND RIG INSPECTION, TALK ABOUT THE HEAT, WILD LIFE, SPOTTER ON LOCATION WITH MOVEMENT, ROTATING EQUIPMENT, HIGH PRESSURE LINES,
8/13/2024	TEST CASING 650 PSI FOR 30 MIN TEST GOOD, 3327 TO SURFACE
8/13/2024	PULL TUBING TO DERRICK 102 JTS AND LAYDOWN 1, AND BREAK OFF SET TOOL FOR CIBP
8/13/2024	RIG UP WIRELINE AND RUN IN WITH CBL TOOLS AND COLLAR LOCATOR, RUN IN AND TAG UP AT 3327 ADN LOAG TO SURFACE, RIG DOWN TRUCK
8/13/2024	PICKUP 4' PERF SUB AND RUN IN WITH 103 JTS OF 2 7/8 L-80 TUBING 6.5#
8/13/2024	RIG UP CEMENT TRUCK TO TUBING MIX AND PUMP 90 BBL OF MLF, AND SPOT 25 SX OF CLASS C CEMENT WITH 3.75 MAKE UP WATER, WITH 18 BBL DISPLACEMENT
8/13/2024	LAYDOWN 7 JTS OF TUBING AND PULL 10 STANDS OF TUBING
8/13/2024	REVERSE CIRC WELL WITH 18 BBL TO PIT, SHUT IN WELL FOR THE NIGHT
8/13/2024	CREW TRAVEL TIME
8/14/2024	CREW TRAVEL TIME
8/14/2024	REVIEW JSA TALK ABOUT WILDLIFE, BACK SAFETY, HAND SAFETY, ROTATING EQUIPMENT, OVERHEAD LEFT WITH TUBING, TURN OFF RIG WHEN CHANGING TONG HEAD
8/14/2024	RUN IN WELL WITH TUBING AND TAG UP AT 3073, 94 JTS IN WELL AND 10'
8/14/2024	LAYDOWN TUBING TO 2656, 82 JTS IN WELL
8/14/2024	MIX AND SPOT 35 SX OF CLASS C CEMENT WITH 5,25 MAKE UP WATER
8/14/2024	LAYDOWN 7 JTS OF TUBIGN AND PULL 10 STANDS TO DERRICK, REVERSE TUBING CLEAN
8/14/2024	WAIT ON CEMENT
8/14/2024	RUN IN HOLE WITH TUBING AND TAG UP AT 2320 72 JTS AND 20'
8/14/2024	LAYDOWN 34 JTS TUBING TO 1085'.
8/14/2024	MIX AND SPOT 25 SX WITH 3.75 BBL MAKE UP WATER
8/14/2024	LAYDOWN 7 JTS OF TUBING AND STAND BACK 10 STANDS AND REVERSE OUT, SHUT WELL IN FOR NIGHT
8/14/2024	CREW TRAVEL TIME
8/15/2024	CREW TRAVEL TIME
8/15/2024	REVIEW JSA DAILYW ORK PLAN AND RIG INSPECTION, TALKED ABOUT WILDLIFE, PERF GUNS ON LOCATION, NO GO ZONE, SPOTTER WITH MOVING EQUIPMENT,
8/15/2024	PICKUP PERF SUB AND RUN IN WITH TUBING AND TAG AT 836'.
8/15/2024	PULL TUBING UP TO 680' 21 JTS IN WELL
8/15/2024	SPOT 35 SX PLUG FROM 680 TO 354 WITH 5.25 BBL MAKE UP WATER
8/15/2024	WAIT ON CEMENT
8/15/2024	RUN IN WITH TUBING AND TAG AT 354'.
8/15/2024	RIG UP WIRELINE AND ARM GUN

8/15/2024	PICKUP 3 1/8 GUN AND RUN IN AND PERF CASING, AT 155' PULL WIRELINE AND PUMP ON CASING, 1.5 BBM AT 500 PSI, PICKUP NEW GUN AND PERF AT 50 CASING PULL OUT AND PUMP ON CASING 2 BBM AT 500, RIG DOWN WIRELINE. SPOT 120 SX CMT 354' TO SURFACE. SQZ AT SURFACE.
8/15/2024	CLEAN UP AROUND LOCATION ADN SHUT IN WELL



Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
<https://www.emnrd.nm.gov/ocd/contact-us>

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 445871

CONDITIONS

Operator: OXY USA INC P.O. Box 4294 Houston, TX 772104294	OGRID: 16696
	Action Number: 445871
	Action Type: [C-103] Sub. Plugging (C-103P)

CONDITIONS

Created By	Condition	Condition Date
loren.diede	None	10/9/2025
