

Submit Copy To Appropriate District Office
District I - (575) 393-6161
1625 N. French Dr., Hobbs, NM 88240
District II - (575) 748-1283
811 S. First St., Artesia, NM 88210
District III - (505) 334-6178
1000 Rio Brazos Rd., Aztec, NM 87410
District IV - (505) 476-3460
1220 S. St. Francis Dr., Santa Fe, NM 87505

State of New Mexico
Energy, Minerals and Natural Resources

Form C-103
Revised July 18, 2013

OIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, NM 87505

WELL API NO. 30-025-51342
5. Indicate Type of Lease STATE [checked] FEE [ ]
6. State Oil & Gas Lease No.
7. Lease Name or Unit Agreement Name AVOGATO 30 31 STATE COM
8. Well Number #072Y
9. OGRID Number 16696
10. Pool name or Wildcat RED TANK; BONE SPRING, EAST
11. Elevation (Show whether DR, RKB, RT, GR, etc.) 3698' GL

SUNDRY NOTICES AND REPORTS ON WELLS
(DO NOT USE THIS FORM FOR PROPOSALS TO DRILL OR TO DEEPEN OR PLUG BACK TO A DIFFERENT RESERVOIR. USE "APPLICATION FOR PERMIT" (FORM C-101) FOR SUCH PROPOSALS.)
1. Type of Well: Oil Well [checked] Gas Well [ ] Other [ ]
2. Name of Operator OXY USA INC.
3. Address of Operator 5 GREENWAY PLAZA, SUITE 110 HOUSTON TX 77002
4. Well Location
Unit Letter C : 420 feet from the NORTH line and 2230 feet from the WEST line
Section 30 Township 22S Range 33E NMPM LEA County
11. Elevation (Show whether DR, RKB, RT, GR, etc.) 3698' GL

12. Check Appropriate Box to Indicate Nature of Notice, Report or Other Data

NOTICE OF INTENTION TO:
PERFORM REMEDIAL WORK [ ] PLUG AND ABANDON [ ]
TEMPORARILY ABANDON [ ] CHANGE PLANS [ ]
PULL OR ALTER CASING [ ] MULTIPLE COMPL [ ]
DOWNHOLE COMMINGLE [ ]
CLOSED-LOOP SYSTEM [ ]
OTHER: [ ]
SUBSEQUENT REPORT OF:
REMEDIAL WORK [ ] ALTERING CASING [ ]
COMMENCE DRILLING OPNS. [ ] P AND A [checked]
CASING/CEMENT JOB [ ]
OTHER: [ ]

13. Describe proposed or completed operations. (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work). SEE RULE 19.15.7.14 NMAC. For Multiple Completions: Attach wellbore diagram of proposed completion or recompletion.

The subject well is plugged. Job start: 6/23/2025. Job complete: 7/24/25. This well was cut and capped on 8/4/2025. See the attached daily job summary and plugged wellbore diagram for reference.

A full CBL was not ran on this well since the fish was not retrieved. This was approved by Robert at the OCD.

Spud Date: 5/26/2023

Rig Release Date: 07/02/2023

I hereby certify that the information above is true and complete to the best of my knowledge and belief.

SIGNATURE [Signature] TITLE REGULATORY ENGINEER DATE 10/27/2025

Type or print name STEPHEN JANACEK E-mail address: STEPHEN\_JANACEK@OXY.COM PHONE: 713-493-1986

For State Use Only

APPROVED BY: TITLE DATE

Conditions of Approval (if any):

AVOGATO 30-31 STATE COM #072Y

30-025-51342 PA SR JOB SUMMARY DETAILS

\*Previous history: Fish in hole from 4527' to 7048'. (5.5"DP, BHA etc stuck in hole)

6/23/25 MIRU TO PA WELL. NDWH.

6/24/25 RU BOP AND FUNCTION TEST.

6/25/25 RIH AND TAGGED RBP @ 795'. LATCH AND RELEASE RBP, POOH WITH IT. RIH TO CLEAN OUT DOWN TO 900'.

6/26-27/25 CONT'D TO C/O AND RIH TO 3524', TAGGED SOLID.

6/30-7/1/25 CONTINUED TO ATTEMPT TO GET CIRCULATION DOWN LOWER THAN 3524'.

7/2/25 UNABLE TO BREAK CIRCULATION, PULLED UP ABOVE OH.

7/7-8/25 UNABLE TO BREAK CIRCULATION. PULLED UP TO 1000'.

7/9/25 RD CIRC EQUIP/FAC PUMPS. POOH WITH C/O BIT.

7/10/25 RIH W/ TUBING, EOT @ 1000'.

7/11/25 RIH TO 3524', TAGGED. PUMPED 50SX (13BBLS) 14.5PPG CLASS C CEMENT. WOC.

7/14/25 RIH AND TAGGED TOC @ 3518'. PUMPED 50SX (12.6BBLS) CLASS C CEMENT ON TOP. WOC.

7/15/25 RIH AND TAGGED TOC @ 3444'. CONFIRMED WITH ROBERT AT THE NMOCD. PULLED UP, EOT @ 3170'.

7/16/25 PUMPED 75SX (17.7BBLS) CLASS C CEMENT. WOC. PSI TESTED BOP, 250LOW/8500HIGH, GOOD TEST. RIH TO 3404', DID NOT TAG. DECIDED TO PUMP MORE CEMENT. EOT @ 3170', PUMPED 100SX (24BBLS) CLASS C CEMENT. WOC.

7/17/25 RIH AND TAGGED TOC @ 3114'. EOT @ 3110'. PUMPED 100SX (24BBLS) CLASS C CEMENT. WOC. RIH AND TAGGED TOC @ 3114'.


7/21/25 EOT @ 3114, PUMPED 200SX CLASS C CEMENT. WOC. RIH AND TAGGED TOC @ 2915'. CONFIRM WITH ROBERT @ NMOCD. PULLED UP, EOT @ 1718'. PUMPED 45SX CLASS C CEMENT. WOC.

7/22/25 RIH AND TAGGED TOC @ 1678'. CONFIRMED WITH ROBERT, HE WANTS MORE CEMENT HERE. PUMPED AN ADDITIONAL 75SX CLASS C CEMENT. WOC. RIH AND TAGGED TOC @ 1587'. CONFIRMED WITH ROBERT, NMOCD. PULLED UP, EOT @ 1134'.

7/23/25 PUMPED 150SX CLASS C CEMENT. WOC. NMOCD APPROVED TO RUN THE CBL F/ 650 TO SURFACE. RIH AND TAGGED TOC @ 875'. RAN CBL. EOT @ 875'. PUMPED 225SX CLASS C CEMENT TO SURFACE. WOC.

7/24/25 VERIFIED CEMENT TO SURFACE. ND, RDMO.

8/4/25 WELLHEAD CUT AND CAPPED COMPLETED.

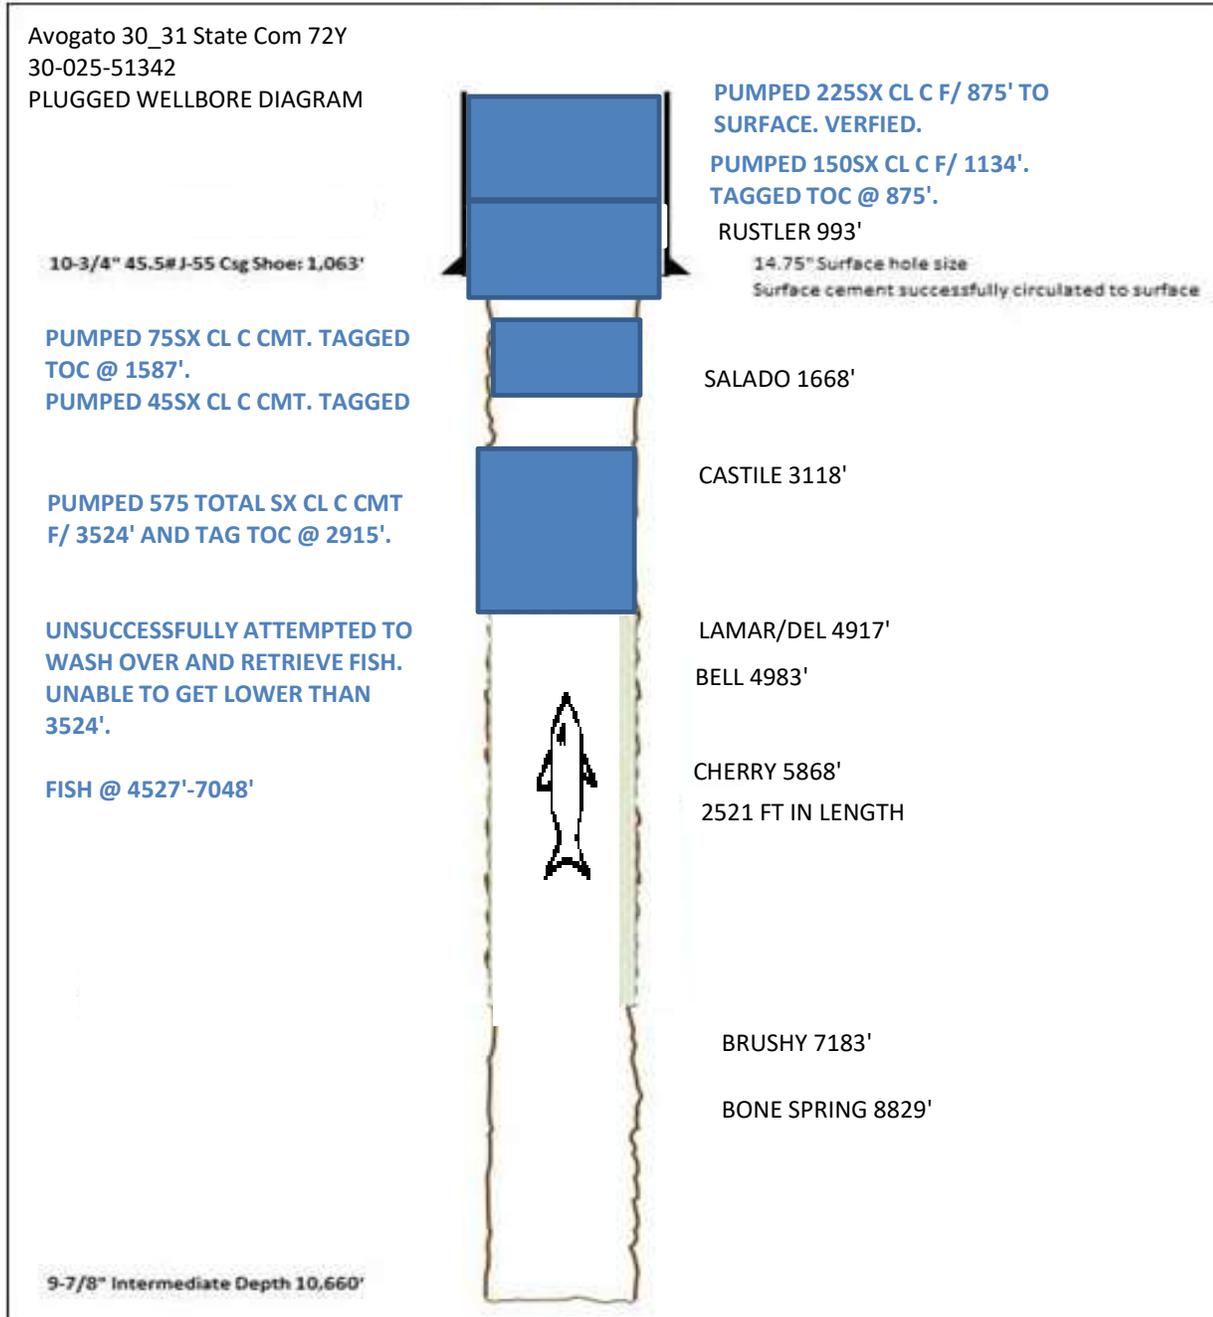

Sante Fe Main Office  
Phone: (505) 476-3441

General Information  
Phone: (505) 629-6116

Online Phone Directory  
<https://www.emnrd.nm.gov/ocd/contact-us>

**State of New Mexico**  
**Energy, Minerals and Natural Resources**  
**Oil Conservation Division**  
**1220 S. St Francis Dr.**  
**Santa Fe, NM 87505**

CONDITIONS

Action 548108

**CONDITIONS**

Operator: OXY USA INC P.O. Box 4294 Houston, TX 772104294	OGRID: 16696
	Action Number: 548108
	Action Type: [C-103] Sub. Plugging (C-103P)

**CONDITIONS**

Created By	Condition	Condition Date
gcordero	Clean Location in accordance with 19.15.25.10 NMAC.	2/3/2026
gcordero	Submit C-103Q within one year of plugging.	2/3/2026
