

Well Name: EAST	Well Location: T31N / R12W / SEC 24 / NESE / 36.881836 / -108.043488	County or Parish/State: SAN JUAN / NM
Well Number: 4A	Type of Well: CONVENTIONAL GAS WELL	Allottee or Tribe Name:
Lease Number: NMSF077652	Unit or CA Name: EAST COM, EAST MV E/2 DEDICATION	Unit or CA Number: NMNM73152, NMNM85781
US Well Number: 3004522866	Well Status: Producing Gas Well	Operator: HILCORP ENERGY COMPANY

Subsequent Report

Sundry ID: 2690417

Type of Submission: Subsequent Report

Type of Action: Workover Operations

Date Sundry Submitted: 09/01/2022

Time Sundry Submitted: 01:27

Date Operation Actually Began: 08/11/2022

Actual Procedure: 8/11/2022: MIRU. CK WELL PRESSURES (SITP - 5 PSI. SICP - 5 PSI. SIBHP - 0 PSI.). LD PLUNGER. ND WH. NU BOP & FT, GOOD TST. TOO H W/TBG. SDFN. 8/12/2022: CK WELL PRESSURES (SICP- 125 PSI. SIBHP- 0 PSI). MU BHA & TIH W/80 JTS 2 3/8" 4.7# J-55 PROD TBG. EOT @ 2570'. ND BOP. NU WH. MU DWNHOLE PMP. TIH W/RODS & PMP. SEAT PMP. INSTALL POLISHED ROD ASSEMBLY & RATTIGAN. LOAD TBG/ANNULUS W/8 BBLs OF H2O. TST T/890 PSI. TST GOOD. BLEED OFF PRESSURE. STROKE TST W/RIG T/1150 PSI. TST GOOD. FOUND SOFT TAG W/18" OF POLISH ABV TOP OF STUFFING BOX. INSTALL ROD ROTATOR & ROD CLAMPS ON POLISHED ROD. RDRR @ 14:30 HRS.

SR Attachments

Actual Procedure

CURRENT_SCHEMATIC_20220901132743.pdf

Well Name: EAST

Well Location: T31N / R12W / SEC 24 / NESE / 36.881836 / -108.043488

County or Parish/State: SAN JUAN / NM

Well Number: 4A

Type of Well: CONVENTIONAL GAS WELL

Allottee or Tribe Name:

Lease Number: NMSF077652

Unit or CA Name: EAST COM, EAST MV E/2 DEDICATION

Unit or CA Number: NMNM73152, NMNM85781

US Well Number: 3004522866

Well Status: Producing Gas Well

Operator: HILCORP ENERGY COMPANY

Operator

I certify that the foregoing is true and correct. Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction. Electronic submission of Sundry Notices through this system satisfies regulations requiring a

Operator Electronic Signature: AMANDA WALKER

Signed on: SEP 01, 2022 01:27 PM

Name: HILCORP ENERGY COMPANY

Title: Operations/Regulatory Technician

Street Address: 1111 TRAVIS ST.

City: HOUSTON

State: TX

Phone: (346) 237-2177

Email address: mwalker@hilcorp.com

Field

Representative Name:

Street Address:

City:

State:

Zip:

Phone:

Email address:

BLM Point of Contact

BLM POC Name: KENNETH G RENNICK

BLM POC Title: Petroleum Engineer

BLM POC Phone: 5055647742

BLM POC Email Address: krennick@blm.gov

Disposition: Accepted

Disposition Date: 09/19/2022

Signature: Kenneth Rennick



Schematic - Current

Well Name: **EAST #4A**


API / UWI 3004522866	Surface Legal Location 024-031N-012W-I	Field Name BLANCO MESAVERDE (PRORATED GAS)	License No.	State/Province NEW MEXICO	Well Configuration Type
Original KB/RT Elevation (ft) 6,005.00	KB-Ground Distance (ft) 12.00	Original Spud Date 1/30/1978 00:00	Rig Release Date	PBTD (All) (ftKB) Original Hole - 5,035.0	Total Depth All (TVD) (ftKB)

Most Recent Job

Job Category Capital Workover	Primary Job Type INSTALL PUMP	Secondary Job Type	Actual Start Date 8/11/2022	End Date 8/12/2022
----------------------------------	----------------------------------	--------------------	--------------------------------	-----------------------

TD: 5,133.0

Original Hole

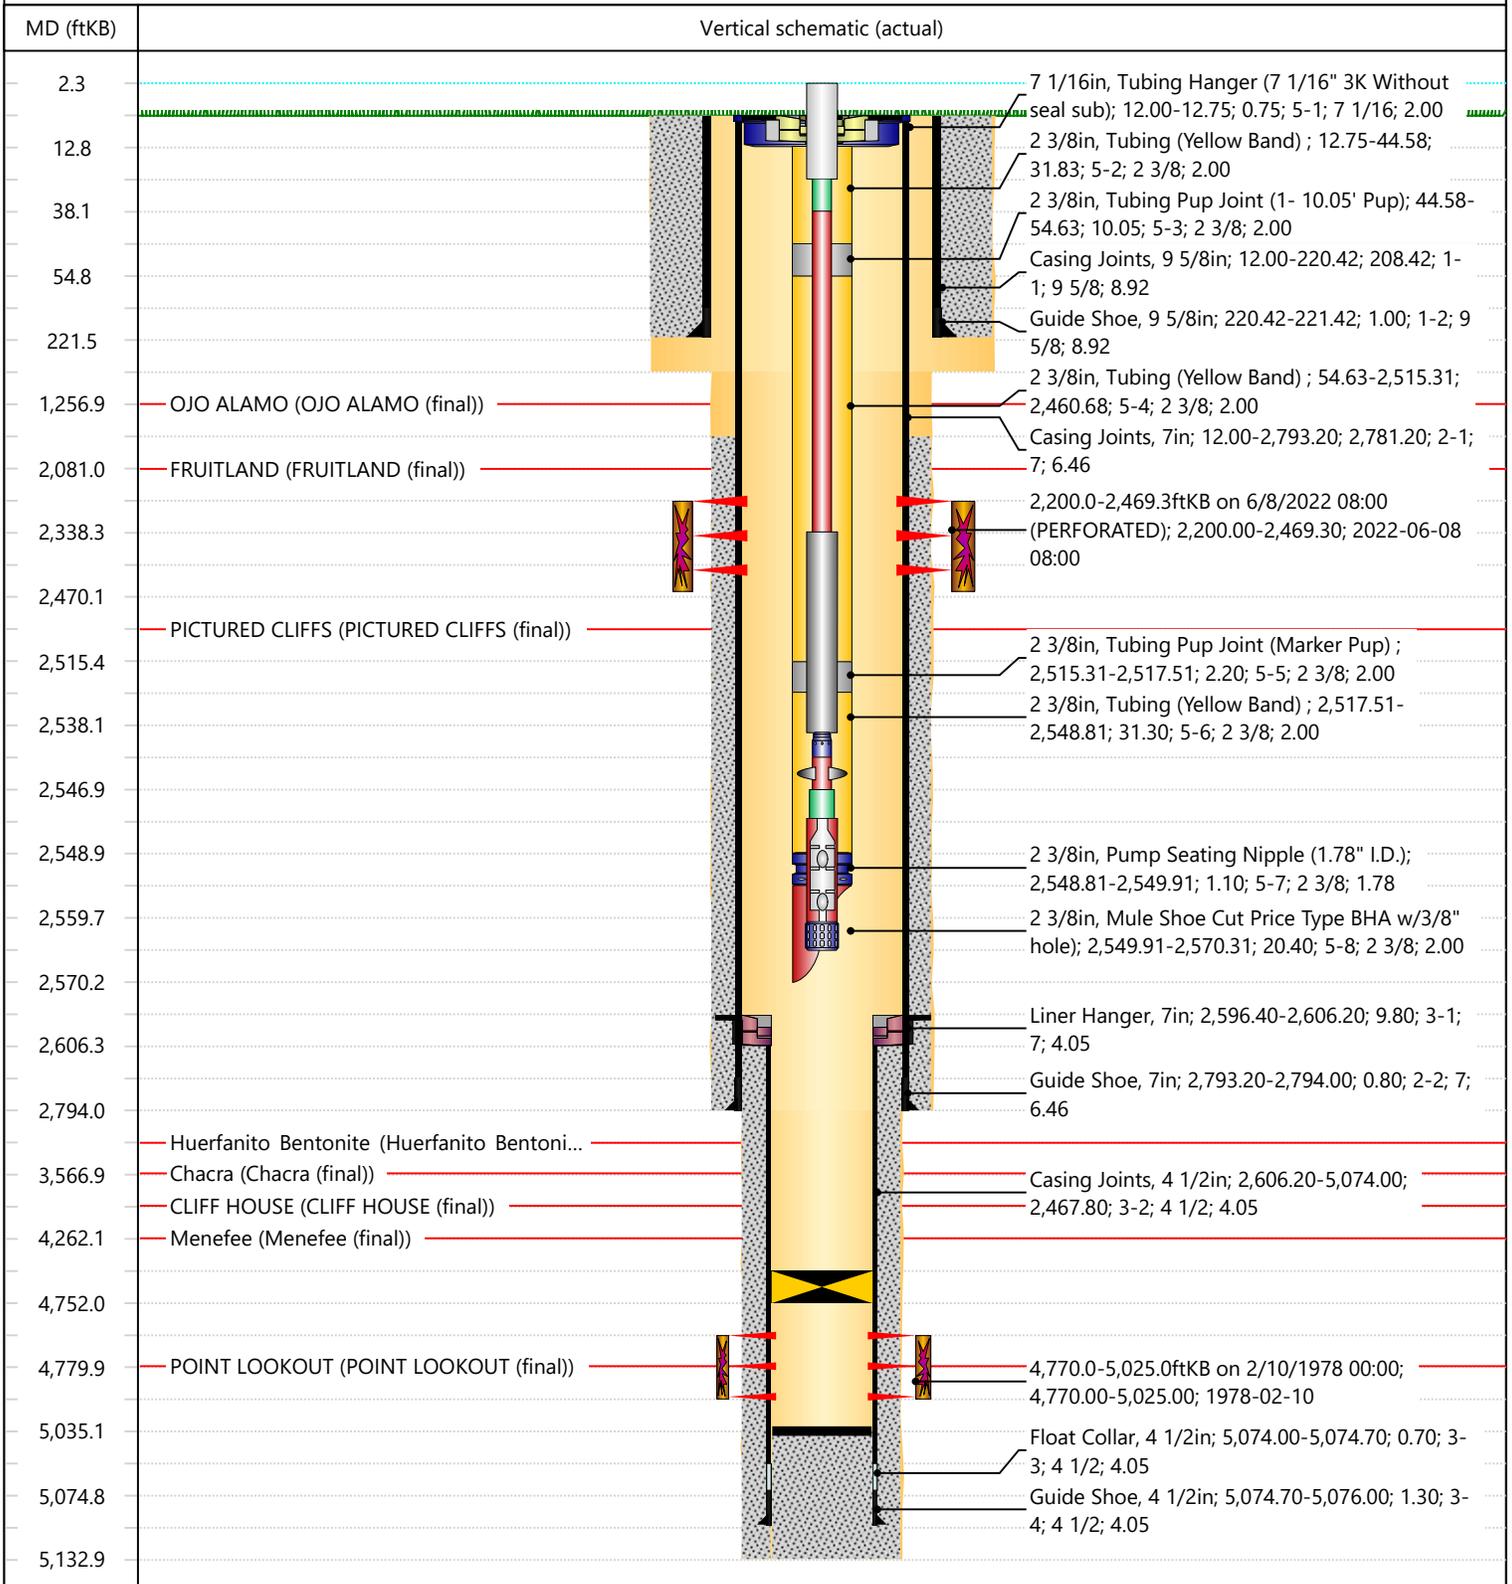

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
<https://www.emnrd.nm.gov/oecd/contact-us>

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 145133

CONDITIONS

Operator: HILCORP ENERGY COMPANY 1111 Travis Street Houston, TX 77002	OGRID: 372171
	Action Number: 145133
	Action Type: [C-103] Sub. Workover (C-103R)

CONDITIONS

Created By	Condition	Condition Date
andrew.fordyce	Accepted for archival record. Isolation plug(s) were drilled out and the well commingled in June of 2023.	2/4/2026
