


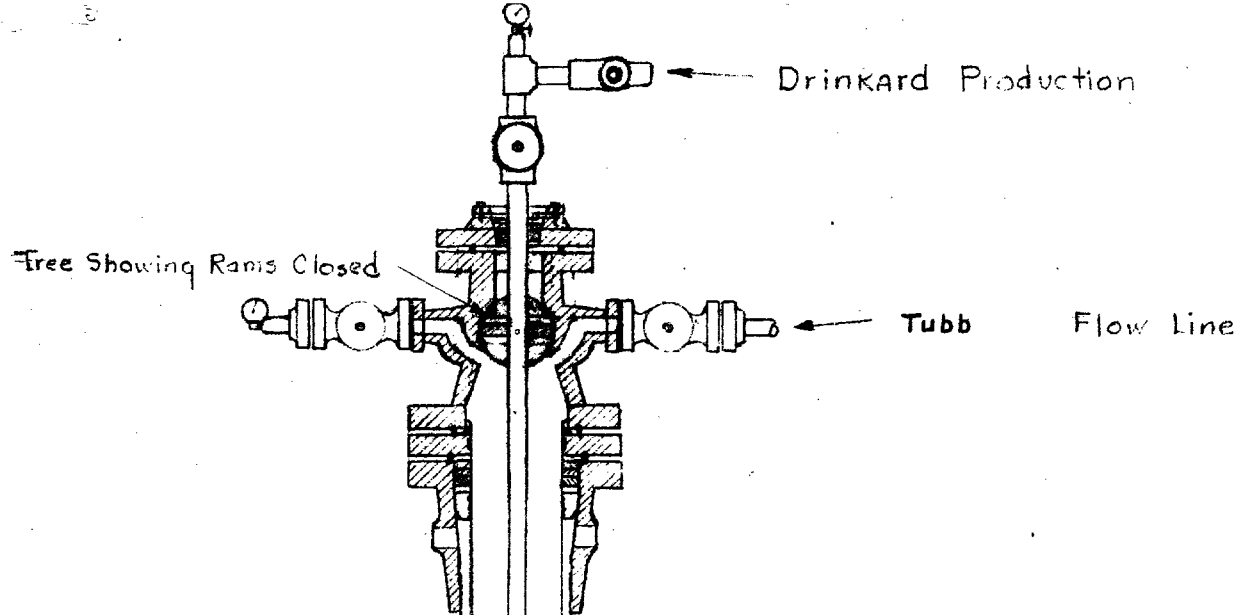

8⁵/₈" Casing Cemented @ 2881'
 Cement Circulated to surface w/ 750
 sxs. 3¹/₂" & 800 sxs. Neat.

5¹/₂" Casing Jet Perforated
 w/ 4-21 grain shots / foot.
 Approx. From 5950' to 6200'.

Otis Side Door Choke
 Blanked Off
 @ 6395'

Baker Model "D" Retainer
 Production Packer
 set @ 6400'

Tubing Perforations

5¹/₂" casing perforated 6503' to 6520'

P.D. T.D. 6535'

5¹/₂" Csg. Cemented @ 6602'

T.D. 6603'
 Detail of Mechanical Equipment To Be
 Installed In Dually Completed Drinkard And
 Tubb Wells For Submission To Oil
 Conservation Commission
