

CEMENT

Cemented 2 stage with
Trinity Lite-Wate tailed in
with Trinity Inferno Neat.
Cement circulated on
both stages Circulated
cement on 9 5/8"

EQUIPMENT

1st STRING - Devonian (West)

305 jts - 2" O.D. Butt. Std. Coupling
BAKER Triple Flow Tube
20 jts - 2" O.D. Butt. Spec. Clear. Cplg.
60 jts - 2" O.D. Butt. Std. Coupling
1 - Seating Nipple, 1460" x 1"
1 jt. - 2" O.D. Butt. Std. Coupling
15' - BAKER Seal Assembly
5' - BAKER Type "E" Flow Tube with
pump out plug on 20' Tail Pipe

2nd STRING - Penn (East)

1 jt. - 2" O.D. Butt. Std. Coupling
2 - 6' Pups
302 jts - 2" O.D. Butt. Std. Coupling
1 - Seating Nipple, 1460" x 1"
1 jt. - 2" O.D. Butt. Std. Coupling
1 - BAKER Snap Ring Seal Assembly

3rd STRING - Wolfcamp (North)

302 jts - 2" O.D. Butt. Std. Coupling
1 - Seating Nipple, 1460" x 1"
1 jt. - 2" O.D. Butt. Std. Coupling
1 - BAKER Snap Ring Seal Assembly

* 18 jts - 3 1/2" Hydrill FJ
1 - 4' Pup
15' - BAKER Seal Assembly
1 jt. - Tail Pipe, below Seal


* Hanging from BAKER Triple Flow
Tube.

4th STRING - Abo (South)

290 jts - 2" O.D. Butt. Spec. Cl. Cplg.
1 - Seating Nipple, 1460" x 1"
1 jt. - 2" O.D. Butt. Spec. Clear. Cplg. w/
Collar on bottom.

13,478-13,768 cement plug

T.D. 13,816 7" 23lbs., 26lbs., 29lbs.
832lbs. N-80 at 13,816'

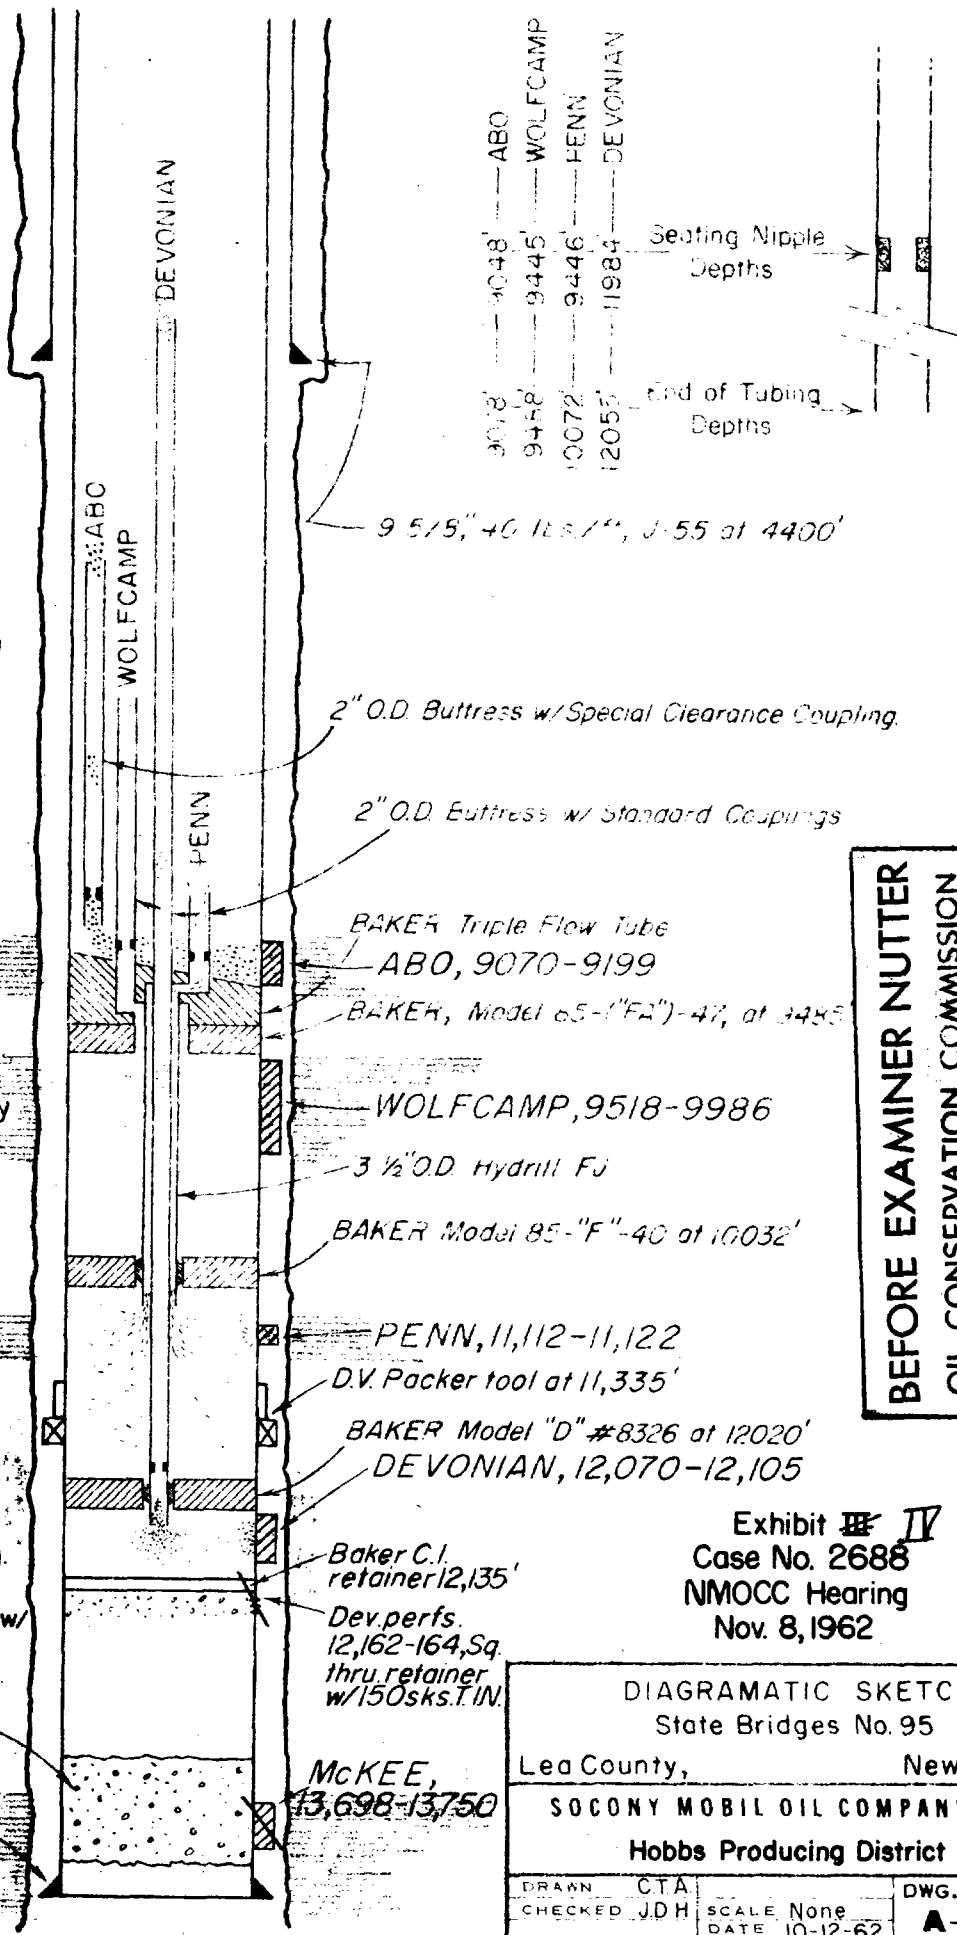

BEFORE EXAMINER NUTTER
OIL CONSERVATION COMMISSION
Exhibit IV
CASE NO. 2688
EXHIBIT NO. 4
CASE NO. 2688

Exhibit IV
Case No. 2688
NMOCC Hearing
Nov. 8, 1962

DIAGRAMATIC SKETCH State Bridges No. 95	
Lea County,	New Mexico
SOCONY MOBIL OIL COMPANY, INC.	
Hobbs Producing District	
DRAWN CTA	DWG. NO.
CHECKED J.D.H.	A-160-D&P
SCALE None	
DATE 10-12-62	
