

AP - 016

ANNUAL MONITORING REPORT

YEAR(S):
2001

ANNUAL MONITORING REPORT

EOTT PIPELINE COMPANY
BOB DURHAM
LEA COUNTY, NEW MEXICO

AP 16
RECEIVED

MAY 09 2001

ENVIRONMENTAL BUREAU
OIL CONSERVATION DIVISION

PREPARED FOR:

EOTT PIPELINE COMPANY
5805 EAST HIGHWAY 80
MIDLAND, TEXAS 79701

PREPARED BY:

ENVIRONMENTAL TECHNOLOGY GROUP, INC.
2540 WEST MARLAND
HOBBS, NEW MEXICO 88240

APRIL 2001

TABLE OF CONTENTS

INTRODUCTION

FIELD ACTIVITIES

GROUND WATER GRADIENT

LABORATORY RESULTS

SUMMARY

FIGURES

Figure 1 – Site Location Map

Figure 2 – Site Ground Water Gradient Map

TABLES

Table 1 – Ground Water Elevation

Table 2 – Ground Water Chemistry

APPENDICES

Appendix A – Laboratory Reports

INTRODUCTION

Environmental Technology Group, Inc. (ETGI), on behalf of EOTT Energy Corp. (EOTT), prepared this annual report in compliance with the New Mexico Oil Conservation Division (OCD) letter of May 1998, requiring submittal of an annual report by April 1 of each year. The report presents the results of the quarterly ground water monitoring events only. For reference, the Site Location Map is provided as Figure 1.

Ground water monitoring was conducted during four quarterly events in calendar year 2000 to assess the levels and extent of dissolved phase and phase-separated hydrocarbon (PSH) constituents. The ground water monitoring events consisted of measuring static water levels in the monitoring wells, checking for the presence of PSH, and purging and sampling of each well exhibiting sufficient recharge. Monitoring wells containing measurable levels of PSH were not sampled.

FIELD ACTIVITIES

The site monitoring wells were gauged and sampled on February 2, 3, and 16, June 9, July 13, September 20, and December 20, 2000. During each sampling event, the monitoring wells, designated to be sampled, were purged of approximately 3 well volumes of water or until the wells were dry using a PVC bailer or electrical Grundfos Pump. Ground water was allowed to recharge and samples were obtained using disposable Teflon samplers. Water samples were stored in clean, glass containers provided by the laboratory and placed on ice in the field. Purge water was collected in a polystyrene tank and disposed of by Pate Trucking, Hobbs, New Mexico, utilizing a licensed disposal facility (OCD AO SWD-730).

GROUND WATER GRADIENT

Locations of the monitoring wells and the inferred ground water gradient, as measured on December 19, 2000, are depicted on Figure 2, the Site Ground Water Gradient Map. The ground water elevation data are provided as Table 1. Ground water elevation contours, generated from the final quarterly event of calendar year 2000 water level measurements, indicated a general gradient of approximately 0.008 ft/ft to the southwest as measured between ground water monitoring wells MW-22 and MW-31. The depth to ground water, as measured from the top of the well casing, ranged between 14.64 to 22.35 feet for the shallow alluvial aquifer.

A measurable thickness of PSH was detected in monitoring wells MW-1, MW-2, MW-4, MW-5, MW-6, MW-7, MW-8, MW-12, MW-16, MW-23 and MW-32 during the annual monitoring period. A maximum thickness of 0.11 feet in monitoring well MW-1, 0.29 feet in monitoring well MW-2, 0.93 feet in monitoring well MW-4, 0.31 feet in monitoring well MW-5, 0.46 feet in monitoring well MW-6, 0.91 feet in monitoring well MW-7, 0.29 feet in monitoring well MW-8, 1.39 feet in monitoring well MW-12, 0.48 feet in monitoring well MW-16, sheen in monitoring well MW-23, and 0.09 foot in monitoring well MW-32 was measured and is shown on Table 1.

LABORATORY RESULTS

Ground water samples obtained during the sampling events were hand delivered to Environmental Laboratory of Texas, Midland, Texas, for determination of benzene, toluene, ethyl benzene and total xylenes (BTEX) concentrations by EPA Method SW846-8021B. The ground water chemistry data are provided as Table 2 and the Laboratory Reports are provided as Appendix A.

Laboratory results for all of the site ground water samples, obtained during the calendar year 2000 monitoring period, indicated that Benzene concentrations were above regulatory standards for monitoring wells MW-3, MW-9, MW-11, MW-13, while BTEX concentrations were below regulatory stands. Benzene and BTEX concentrations contained in monitoring wells MW-10, MW-14, MW-17, MW-18, MW-20, MW-21, MW-30, MW-31, and MW-34 were below regulatory standards. The remaining monitoring wells were below method detection limits for Benzene and BTEX.

SUMMARY

This report presents the results of monitoring activities for the annual monitoring period of calendar year 2000. A measurable thickness of PSH was detected in monitoring wells MW-1, MW-2, MW-4, MW-5, MW-6, MW-7, MW-8, MW-12, MW-16, MW-23 and MW-32 during the annual monitoring period. A maximum thickness of 0.11 feet in monitoring well MW-1, 0.29 feet in monitoring well MW-2, 0.93 feet in monitoring well MW-4, 0.31 feet in monitoring well MW-5, 0.46 feet in monitoring well MW-6, 0.91 feet in monitoring well MW-7, 0.29 feet in monitoring well MW-8, 1.39 feet in monitoring well MW-12, 0.48 feet in monitoring well MW-16, sheen in monitoring well MW-23, and 0.09 foot in monitoring well MW-32 was measured in the monitoring wells.

Ground water elevation contours, generated from the final quarterly event of calendar year 2000 water level measurements, indicated a general gradient of approximately 0.008 ft/ft to the southwest as measured between ground water monitoring wells MW-22 and MW-31.

Laboratory results for all of the site ground water samples, obtained during the calendar year 2000 monitoring period, indicated that Benzene concentrations were above regulatory standards for monitoring wells MW-3, MW-9, MW-11, MW-13, while BTEX concentrations were below regulatory stands. Benzene and BTEX concentrations contained in monitoring wells MW-10, MW-14, MW-17, MW-18, MW-20, MW-21, MW-30, MW-31, and MW-34 were below regulatory standards. The remaining monitoring wells were below method detection limits for Benzene and BTEX.

FIGURES

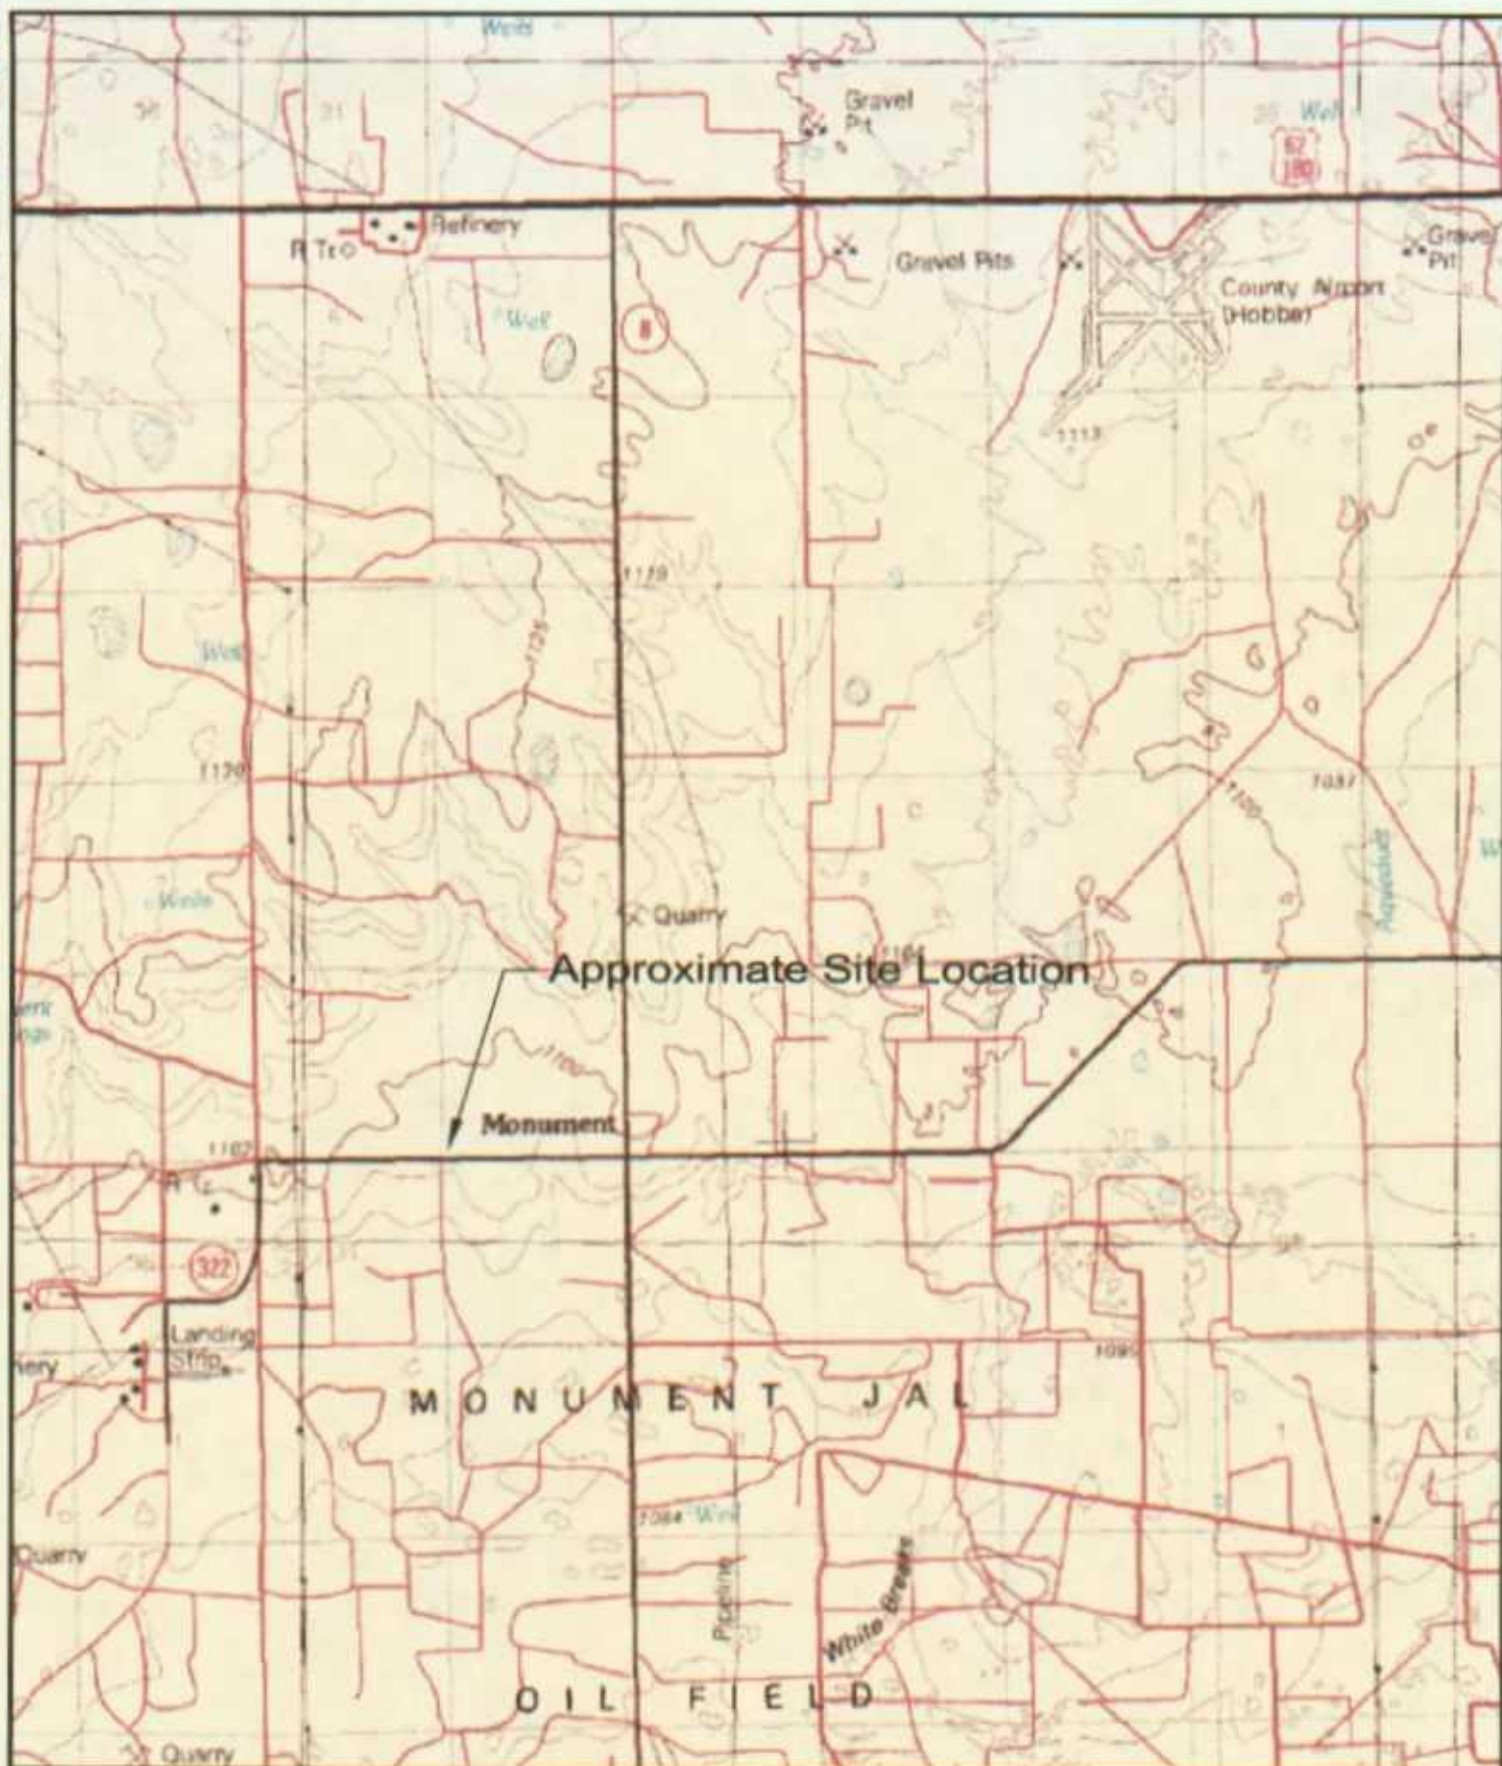
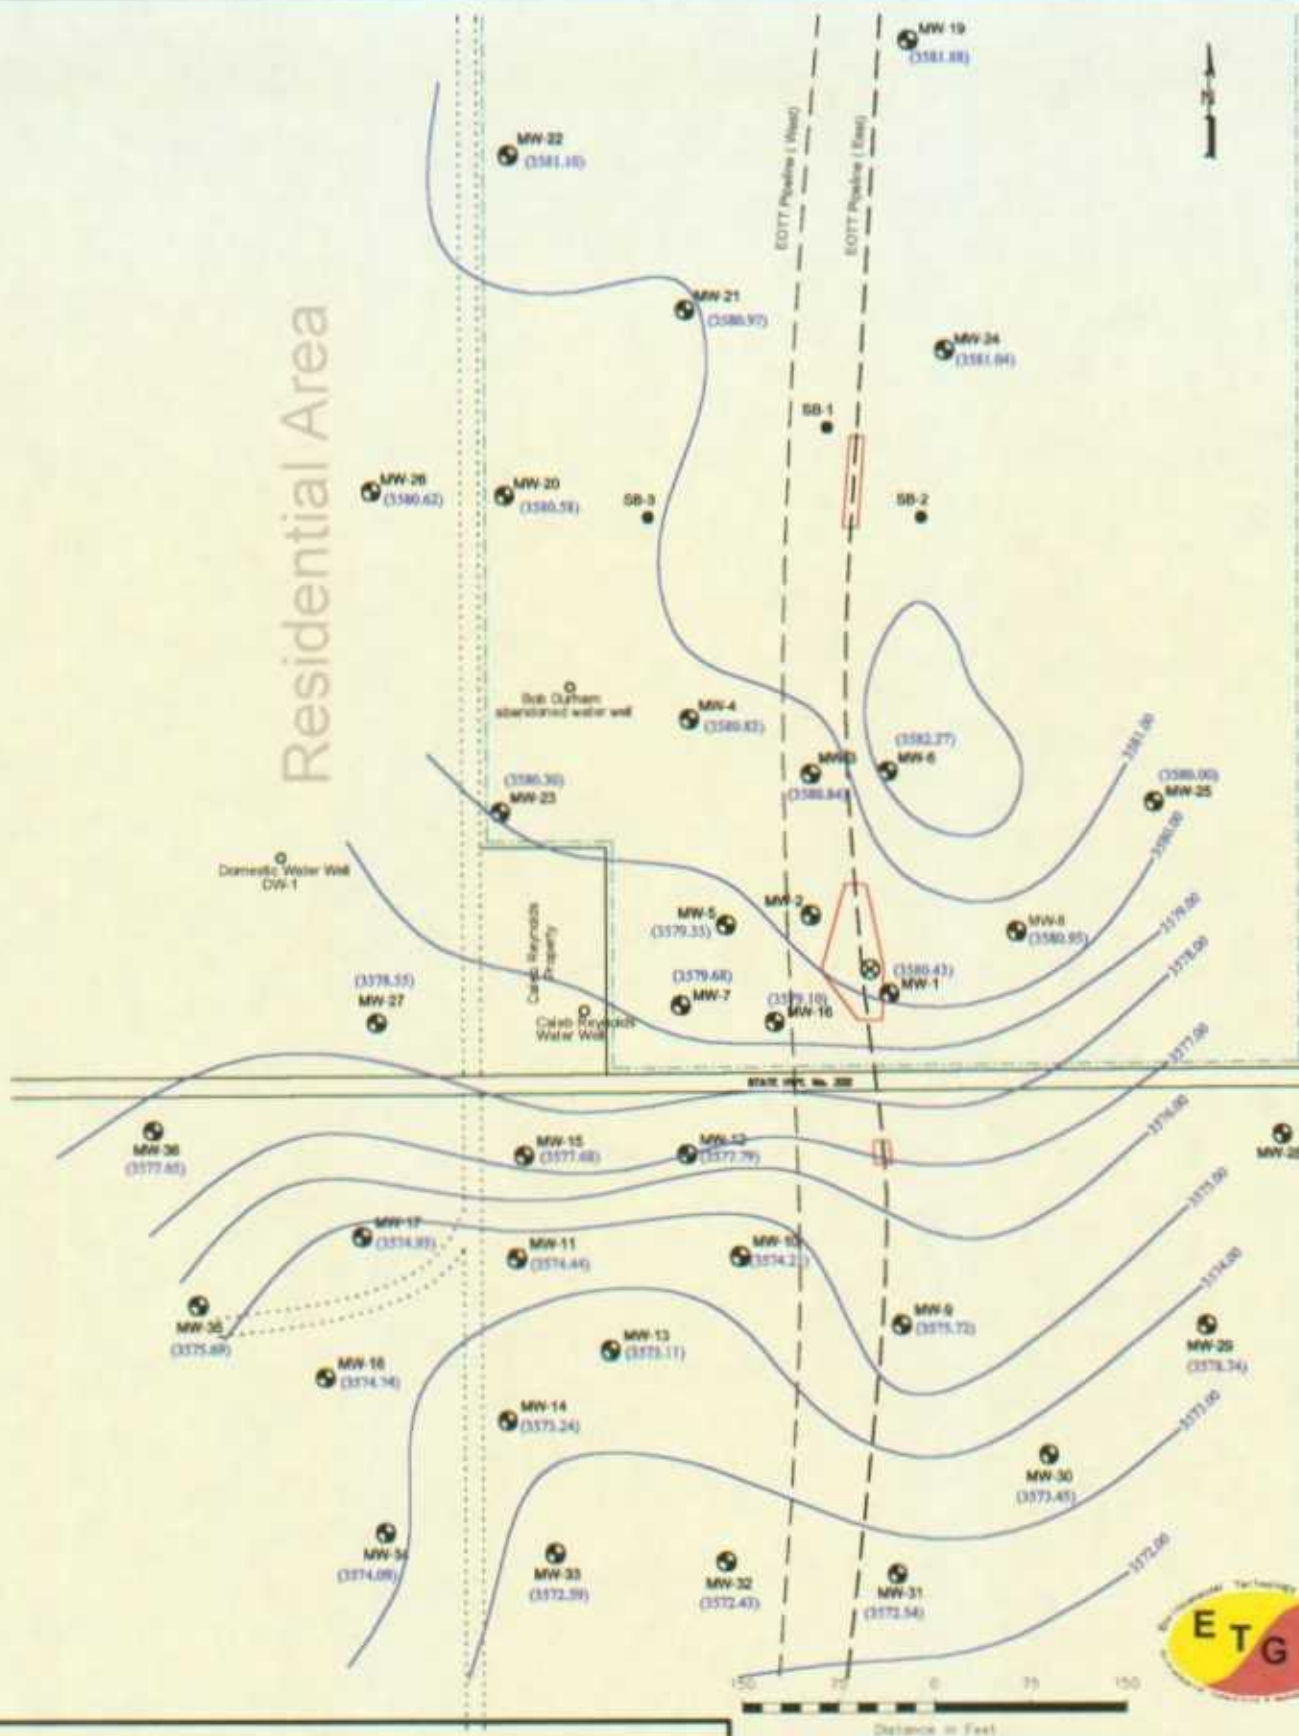


Figure 1
Site Location Map

EOTT Energy Corp.
Bob Durham
Lea County, NM

Environmental Technology
Group, INC.

Scale: No Scale	Prep By: JDU	Checked By: MVS
March 3, 2001	ETGI Project #: EOT204C	



LEGEND:

- ETO Monitoring Well Locations
- Excavation Areas
- Release Point
- EOTT Pipeline
- Soil Boring Locations
- Bob Durham Property Line
- Groundwater Gradient Contour
- (2405) Groundwater Elevation (in feet)
- Dirt Road

Figure 2
Site Groundwater
Gradient Map (12/20/00)
EOTT Energy Corp.
Bob Durham
Lees County, NM

Environmental Technology Group, INC.

Scale: 1" = 150' Prep By: RS Checked By: JT
December 20, 2000 ETO Project # EOT2044C

TABLES

TABLE 1

GROUND WATER ELEVATION
ANNUAL REPORTEOTT ENERGY CORPORATION
BOB DURHAM
MONUMENT, NEW MEXICO
ETGI PROJECT # EOT 2044C

WELL NUMBER	DATE MEASURED	CASING WELL ELEVATION	DEPTH TO PRODUCT	DEPTH TO WATER	PSH THICKNESS	CORRECTED GROUND WATER ELEVATION
MW - 1	02/16/00	3,595.43	15.60	15.71	0.11	3,579.81
	06/09/00	3,595.43	15.54	15.60	0.06	3,579.88
	09/19/00	3,595.43	14.97	15.05	0.06	3,580.43
	12/19/00	3,595.43	14.97	15.05	0.06	3,580.43
MW - 2	02/16/00	3,595.64	15.47	15.76	0.29	3,580.13
	06/09/00	3,595.64	15.52	15.81	0.29	3,580.08
	09/19/00	3,595.64	15.19	15.23	0.29	3,580.66
	12/19/00	3,595.64	15.19	15.23	0.29	3,580.66
MW - 3	02/16/00	3,596.22	-	15.51	0.00	3,580.71
	06/09/00	3,596.22	-	15.57	0.00	3,580.65
	09/19/00	3,596.22	-	15.25	0.00	3,580.97
	12/19/00	3,596.22	-	15.38	0.00	3,580.84
MW - 4	02/16/00	3,596.60	15.90	16.70	0.80	3,580.58
	06/09/00	3,596.60	15.85	16.78	0.93	3,580.61
	09/19/00	3,596.60	15.66	15.66	0.93	3,581.73
	12/19/00	3,596.60	15.77	16.69	0.92	3,580.69
MW - 5	02/16/00	3,596.56	17.30	17.38	0.08	3,579.25
	06/09/00	3,596.56	17.37	17.68	0.31	3,579.14
	09/19/00	3,596.56	16.88	16.88	0.31	3,579.94
	12/19/00	3,596.56	17.21	17.59	0.38	3,579.29
MW - 6	02/16/00	3,596.66	15.10	15.33	0.23	3,581.53
	06/09/00	3,596.66	15.46	15.52	0.46	3,581.53
	09/19/00	3,596.66	14.82	14.82	0.46	3,582.23
	12/19/00	3,596.66	14.82	14.82	0.46	3,582.23
MW - 7	02/16/00	3,596.96	17.67	18.58	0.91	3,579.15
	06/09/00	3,596.96	17.74	18.41	0.67	3,579.12
	09/19/00	3,596.96	17.20	17.20	0.67	3,580.33
	12/19/00	3,596.96	17.72	17.48	0.24	3,579.68
MW - 8	02/16/00	3,597.35	16.83	17.12	0.29	3,580.48
	06/09/00	3,597.35	16.90	17.13	0.23	3,580.42
	09/19/00	3,597.35	16.60	16.60	0.23	3,580.95
	12/19/00	3,597.35	16.60	16.60	0.23	3,580.95

TABLE 1 (CON'T)

WELL NUMBER	DATE MEASURED	CASING WELL ELEVATION	DEPTH TO PRODUCT	DEPTH TO WATER	PSH THICKNESS	CORRECTED GROUND WATER ELEVATION
MW - 9	02/16/00	3,593.95	-	18.23	0.00	3,575.72
	06/09/00	3,593.95	-	18.20	0.00	3,575.75
	09/19/00	3,593.95	-	18.22	0.00	3,575.73
	12/19/00	3,593.95	-	18.23	0.00	3,575.72
MW - 10	02/16/00	3,594.57	-	20.32	0.00	3,574.25
	06/09/00	3,594.57	-	20.41	0.00	3,574.16
	09/19/00	3,594.57	-	20.21	0.00	3,574.36
	12/19/00	3,594.57	-	20.36	0.00	3,574.21
MW - 11	02/16/00	3,593.77	-	19.37	0.00	3,574.40
	06/09/00	3,593.77	-	19.45	0.00	3,574.32
	09/19/00	3,593.77	-	19.58	0.00	3,574.19
	12/19/00	3,593.77	-	19.33	0.00	3,574.44
MW - 12	02/16/00	3,596.39	18.82	20.21	1.39	3,577.36
	06/09/00	3,596.39	18.55	18.91	0.36	3,577.79
	09/19/00	3,596.39	18.48	18.86	0.36	3,577.84
	12/19/00	3,596.39	18.55	18.91	0.36	3,577.79
MW - 13	02/16/00	3,592.71	-	19.59	0.00	3,573.12
	06/09/00	3,592.71	-	19.61	0.00	3,573.10
	09/19/00	3,592.71	-	19.56	0.00	3,573.15
	12/19/00	3,592.71	-	19.60	0.00	3,573.11
MW - 14	02/16/00	3,592.73	-	19.53	0.00	3,573.20
	06/09/00	3,592.73	-	19.57	0.00	3,573.16
	09/19/00	3,592.73	-	19.45	0.00	3,573.28
	12/19/00	3,592.73	-	19.49	0.00	3,573.24
MW - 15	02/16/00	3,595.93	-	18.54	0.00	3,577.39
	06/09/00	3,595.93	-	18.30	0.00	3,577.63
	09/19/00	3,595.93	-	18.11	0.00	3,577.82
	12/19/00	3,595.93	-	18.25	0.00	3,577.68
MW - 16	02/16/00	3,595.75	16.53	17.01	0.48	3,579.15
	06/09/00	3,595.75	16.89	17.08	0.19	3,578.83
	09/19/00	3,595.75	16.41	16.53	0.19	3,579.38
	12/19/00	3,595.75	-	16.65	0.00	3,579.10
MW - 17	02/16/00	3,593.17	-	18.24	0.00	3,574.93
	06/09/00	3,593.17	-	18.27	0.00	3,574.90
	09/19/00	3,593.17	-	18.21	0.00	3,574.96
	12/19/00	3,593.17	-	18.24	0.00	3,574.93

TABLE 1 (CON'T)

WELL NUMBER	DATE MEASURED	CASING WELL ELEVATION	DEPTH TO PRODUCT	DEPTH TO WATER	PSH THICKNESS	CORRECTED GROUND WATER ELEVATION
MW - 18	02/16/00	3,593.39	-	18.65	0.00	3,574.74
	06/09/00	3,593.39	-	18.79	0.00	3,574.60
	09/19/00	3,593.39	-	18.65	0.00	3,574.74
	12/19/00	3,593.39	-	18.65	0.00	3,574.74
MW - 19	02/16/00	3,599.33	-	17.45	0.00	3,581.88
	06/09/00	3,599.33	-	17.45	0.00	3,581.88
	09/19/00	3,599.33	-	17.44	0.00	3,581.89
	12/19/00	3,599.33	-	17.45	0.00	3,581.88
MW - 20	02/16/00	3,597.64	-	17.13	0.00	3,580.51
	06/09/00	3,597.64	-	17.16	0.00	3,580.48
	09/19/00	3,597.64	-	17.07	0.00	3,580.57
	12/19/00	3,597.64	-	17.06	0.00	3,580.58
MW - 21	02/16/00	3,596.88	-	15.98	0.00	3,580.90
	06/09/00	3,596.88	-	15.96	0.00	3,580.92
	09/19/00	3,596.88	-	15.88	0.00	3,581.00
	12/19/00	3,596.88	-	15.91	0.00	3,580.97
MW - 22	02/16/00	3,598.34	-	17.23	0.00	3,581.11
	06/09/00	3,598.34	-	17.23	0.00	3,581.11
	09/19/00	3,598.34	-	17.22	0.00	3,581.12
	12/19/00	3,598.34	-	17.24	0.00	3,581.10
MW - 23	02/16/00	3,598.07	-	17.83	0.00	3,580.24
	06/09/00	3,598.07	17.68	17.68	0.00	3,580.39
	09/19/00	3,598.07	17.77	17.77	0.00	3,580.30
	12/19/00	3,598.07	17.77	17.77	0.00	3,580.30
MW - 24	02/16/00	3,598.01	-	16.97	0.00	3,581.04
	06/09/00	3,598.01	-	16.98	0.00	3,581.03
	09/19/00	3,598.01	-	16.82	0.00	3,581.19
	12/19/00	3,598.01	-	16.97	0.00	3,581.04
MW - 25	02/16/00	3,599.25	-	18.79	0.00	3,580.46
	06/09/00	3,599.25	-	18.88	0.00	3,580.37
	09/19/00	3,599.25	-	18.57	0.00	3,580.68
	12/19/00	3,599.25	-	18.71	0.00	3,580.54
MW - 26	NOT INSTALLED					
	06/09/00	3,595.26	-	14.73	0.00	3,580.53
	09/19/00	3,595.26	-	14.68	0.00	3,580.58
	12/19/00	3,595.26	-	14.64	0.00	3,580.62

TABLE 1 (CON'T)

WELL NUMBER	DATE MEASURED	CASING WELL ELEVATION	DEPTH TO PRODUCT	DEPTH TO WATER	PSH THICKNESS	CORRECTED GROUND WATER ELEVATION
MW - 27	NOT INSTALLED					
	06/09/00	3,592.64	-	14.13	0.00	3,578.51
	09/19/00	3,592.64	-	14.08	0.00	3,578.56
	12/19/00	3,592.64	-	14.09	0.00	3,578.55
MW - 28	NOT INSTALLED			DRY		
	07/13/00	3,598.02		DRY		
	09/19/00	3,598.02		DRY		
	12/19/00	3,598.02		DRY		
MW - 29	NOT INSTALLED					
	07/13/00	3,595.29	-	21.42	0.00	3,573.87
	09/19/00	3,595.29	-	21.55	0.00	3,573.74
	12/19/00	3,595.29	-	21.55	0.00	3,573.74
MW - 30	NOT INSTALLED					
	07/13/00	3,595.74	-	22.35	0.00	3,573.39
	09/19/00	3,595.74	-	22.27	0.00	3,573.47
	12/19/00	3,595.74	-	22.29	0.00	3,573.45
MW - 31	NOT INSTALLED					
	07/13/00	3,593.77	-	20.68	0.00	3,573.09
	09/19/00	3,593.77	-	21.03	0.00	3,572.74
	12/19/00	3,593.77	-	21.23	0.00	3,572.54
MW - 32	NOT INSTALLED					
	07/13/00	3,592.11	-	19.79	0.00	3,572.32
	09/19/00	3,592.11	19.67	19.76	0.09	3,572.43
	12/19/00	3,592.11	19.67	19.76	0.09	3,572.43
MW - 33	NOT INSTALLED					
	07/13/00	3,592.55	-	20.07	0.00	3,572.48
	09/19/00	3,592.55	-	19.99	0.00	3,572.56
	12/19/00	3,592.55	-	19.96	0.00	3,572.59
MW - 34	NOT INSTALLED					
	07/13/00	3,593.30	-	19.01	0.00	3,574.29
	09/19/00	3,593.30	-	19.19	0.00	3,574.11
	12/19/00	3,593.30	-	19.21	0.00	3,574.09
MW - 35	NOT INSTALLED					
	07/13/00	3,594.47	-	18.67	0.00	3,575.80
	09/19/00	3,594.47	-	18.73	0.00	3,575.74
	12/19/00	3,594.47	-	18.78	0.00	3,575.69

TABLE 1 (CON'T)

NUMBER	MEASURED	ELEVATION	PRODUCT	WATER	THICKNESS	GROUND WATER
MW - 36	NOT INSTALLED					
	07/13/00	3,595.80	-	18.03	0.00	3,577.77
	09/19/00	3,595.80	-	18.13	0.00	3,577.67
	12/19/00	3,595.80	-	18.15	0.00	3,577.65

TABLE 2

GROUND WATER CHEMISTRY
ANNUAL REPORTEOTT ENERGY CORPORATION
BOB DURHAM
MONUMENT, NEW MEXICO
ETGI PROJECT # 2044C*All concentrations are in mg/L*

SAMPLE LOCATION	SAMPLE DATE	SW 846-8021B, 5030				
		BENZENE	TOLUENE	ETHYL-BENZENE	M,P-XYLENES	O-XYLENES
MW - 3	02/03/00	0.480	0.235	0.153	0.441	0.170
	06/09/00	0.433	0.016	0.119	0.095	0.056
	09/20/00	0.138	0.004	0.120	0.100	0.029
	12/20/00	0.117	0.002	0.044	0.038	0.003
MW - 9	02/02/00	0.020	0.007	0.001	0.004	0.002
	06/09/00	0.078	0.002	0.002	0.002	0.001
	09/20/00	0.012	<0.001	<0.001	<0.001	<0.001
	12/20/00	0.022	<0.001	0.003	0.003	<0.001
MW - 10	02/02/00	0.009	0.004	<0.001	<0.001	<0.001
	06/09/00	<0.001	<0.001	<0.001	<0.001	0.001
	09/20/00	0.003	<0.001	<0.001	<0.001	0.002
	12/20/00	0.004	<0.001	<0.001	<0.001	<0.001
MW - 11	02/02/00	0.027	0.009	0.002	0.004	0.001
	06/09/00	0.006	<0.001	<0.001	<0.001	<0.001
	09/20/00	0.014	<0.001	<0.001	<0.001	<0.001
	12/20/00	0.005	<0.001	<0.001	<0.001	<0.001
MW - 13	02/02/00	0.821	0.008	0.020	0.007	0.004
	06/09/00	0.777	0.007	0.059	0.044	0.010
	09/20/00	0.946	<0.002	0.076	0.163	0.044
	12/20/00	0.673	0.002	0.092	0.158	0.054
MW - 14	02/03/00	0.004	0.001	<0.001	<0.001	<0.001
	06/09/00	0.003	<0.001	<0.001	<0.001	<0.001
	09/20/00	0.005	<0.001	<0.001	<0.001	<0.001
	12/20/00	<0.001	<0.001	<0.001	<0.001	<0.001
MW - 15	02/03/00	<0.001	<0.001	<0.001	<0.001	<0.001
	06/09/00	0.010	<0.001	<0.001	<0.001	<0.001
	09/20/00	0.012	<0.001	<0.001	<0.001	<0.001
	12/20/00	0.004	<0.001	<0.001	<0.001	<0.001
MW - 17	02/17/00	0.001	<0.001	<0.001	<0.001	<0.001
	06/09/00	<0.001	<0.001	<0.001	<0.001	<0.001
	09/20/00	0.001	<0.001	<0.001	<0.001	<0.001
	12/20/00	<0.001	<0.001	<0.001	<0.001	<0.001
MW - 18	02/17/00	<0.001	<0.001	<0.001	<0.001	<0.001
	06/09/00	<0.001	<0.001	<0.001	<0.001	<0.001
	09/20/00	<0.001	0.001	0.001	0.006	0.003
	Not accessible (Drilling Rig)					

ETGI PROJECT # 2044C

All concentrations are in mg/L

SAMPLE LOCATION	SAMPLE DATE	SW 846-8021B, 5030				
		BENZENE	TOLUENE	ETHYL-BENZENE	M,P-XYLENES	O-XYLENES
MW - 19	02/17/00	<0.001	<0.001	<0.001	<0.001	<0.001
	06/09/00	<0.001	<0.001	<0.001	<0.001	<0.001
	09/20/00	<0.001	<0.001	<0.001	<0.001	<0.001
	12/20/00	<0.001	<0.001	<0.001	<0.001	<0.001
MW - 20	Gauged but not tested per KD/JT					
	06/09/00	0.004	0.001	0.001	0.003	<0.001
	09/20/00	0.002	<0.001	<0.001	<0.001	<0.001
	12/20/00	<0.001	<0.001	<0.001	<0.001	<0.001
MW - 21	Gauged but not tested per KD/JT					
	06/09/00	0.001	0.001	0.001	0.002	0.001
	09/20/00	0.004	<0.001	<0.001	0.001	<0.001
	12/20/00	<0.001	<0.001	<0.001	<0.001	<0.001
MW - 22	02/17/00	<0.001	<0.001	<0.001	<0.001	<0.001
	06/09/00	<0.001	<0.001	<0.001	<0.001	<0.001
	09/20/00	<0.001	<0.001	<0.001	<0.001	<0.001
	12/20/00	<0.001	<0.001	<0.001	<0.001	<0.001
MW - 24	02/17/00	<0.001	<0.001	<0.001	<0.001	<0.001
	06/09/00	<0.001	<0.001	<0.001	<0.001	<0.001
	09/20/00	<0.001	<0.001	<0.001	<0.001	<0.001
	12/20/00	<0.001	<0.001	<0.001	<0.001	<0.001
MW - 25	02/17/00	<0.001	<0.001	<0.001	<0.001	<0.001
	06/09/00	<0.001	<0.001	<0.001	<0.001	<0.001
	09/20/00	<0.001	<0.001	<0.001	<0.001	<0.001
	12/20/00	<0.001	<0.001	<0.001	<0.001	<0.001
MW - 26	NOT INSTALLED					
*	06/09/00	<0.001	<0.001	<0.001	<0.001	<0.001
	09/20/00	<0.001	<0.001	<0.001	<0.001	<0.001
	12/20/00	<0.001	<0.001	<0.001	<0.001	<0.001
MW - 27	NOT INSTALLED					
*	06/09/00	<0.001	<0.001	<0.001	<0.001	<0.001
	09/20/00	<0.001	<0.001	<0.001	<0.001	<0.001
	12/20/00	<0.001	<0.001	<0.001	<0.001	<0.001
MW - 29	NOT INSTALLED					
*	07/13/00	<0.001	<0.001	<0.001	<0.001	<0.001
	09/20/00	<0.001	<0.001	<0.001	<0.001	<0.001
	12/20/00	<0.001	<0.001	<0.001	<0.001	<0.001
MW - 30	NOT INSTALLED					
*	07/13/00	<0.001	0.001	0.001	0.002	<0.001
	09/20/00	<0.001	<0.001	<0.001	<0.001	<0.001
	12/20/00	<0.001	<0.001	<0.001	<0.001	<0.001
MW - 31	NOT INSTALLED					
*	07/13/00	0.002	0.002	<0.001	<0.001	<0.001
	09/20/00	<0.001	<0.001	0.001	<0.001	<0.001
	12/20/00	0.004	<0.001	<0.001	<0.001	<0.001

ETGI PROJECT # 2044C

All concentrations are in mg/L

SAMPLE LOCATION	SAMPLE DATE	SW 846-8021B, 5030				
		BENZENE	TOLUENE	ETHYL-BENZENE	M,P-XYLENES	O-XYLENES
MW - 32	NOT INSTALLED					
	NOT INSTALLED					
	* 07/13/00	<0.001	0.003	<0.001	<0.001	<0.001
	PSH					
MW - 33	NOT INSTALLED					
	* 07/13/00	0.008	0.002	<0.001	0.002	<0.001
	09/20/00	<0.001	<0.001	<0.001	<0.001	<0.001
	12/20/00	<0.001	<0.001	<0.001	<0.001	<0.001
MW - 34	NOT INSTALLED					
	* 07/13/00	<0.001	<0.001	<0.001	<0.001	<0.001
	09/20/00	<0.001	<0.001	<0.001	<0.001	<0.001
	12/20/00	<0.001	<0.001	<0.001	<0.001	<0.001
MW - 35	NOT INSTALLED					
	* 07/13/00	<0.001	<0.001	<0.001	<0.001	<0.001
	09/20/00	<0.001	<0.001	<0.001	<0.001	<0.001
	12/20/00	<0.001	<0.001	<0.001	<0.001	<0.001
MW - 36	NOT INSTALLED					
	* 07/13/00	<0.001	<0.001	<0.001	<0.001	<0.001
	09/20/00	<0.001	<0.001	<0.001	<0.001	<0.001
	12/20/00	<0.001	<0.001	<0.001	<0.001	<0.001
* Initial analyticals						

APPENDIX

ENVIRONMENTAL LAB OF , INC.

"Don't Treat Your Soil Like Dirt!"

ENVIRONMENTAL TECHNOLOGY GROUP, INC.
ATTN: MR. JESSE TAYLOR
P.O. BOX 4845
MIDLAND, TEXAS 79704
FAX: 505-392-3760


Sample Type: Water
Sample Condition: Intact/ Iced/HCl
Project #: EOT 1044C
Project Name: Bob Durham
Project Location: Monument, N.M.

Sampling Date: See Below
Receiving Date: 02/03/00
Analysis Date: 02/04/00

ELT#	FIELD CODE / SAMPLE DATE	BENZENE (mg/L)	TOLUENE (mg/L)	ETHYLBENZENE (mg/L)	m,p-XYLENE (mg/L)	o-XYLENE (mg/L)
23358	MW-3 02/03/00	0.480	0.235	0.153	0.441	0.170
23359	MW-9 02/02/00	0.020	0.007	0.001	0.004	0.002
23360	MW-10 02/02/00	0.009	0.004	<0.001	<0.001	<0.001
23361	MW-11 02/02/00	0.027	0.009	0.002	0.004	0.001
23362	MW-13 02/02/00	0.821	0.008	0.020	0.007	0.004
23363	MW-14 02/03/00	0.004	0.001	<0.001	<0.001	<0.001
23364	MW-15 02/03/00	<0.001	<0.001	<0.001	<0.001	<0.001

% IA	101	97	95	98	95
% EA	104	99	97	101	99
BLANK	<0.001	<0.001	<0.001	<0.001	<0.001

METHODS: EPA SW 846-8021B,5030


Raland K. Tuttle

2-15-00
Date

ENVIRONMENTAL LAB OF , INC.

"Don't Treat Your Soil Like Dirt!"

ENVIRONMENTAL TECHNOLOGY GROUP, INC.
ATTN: MR. JESSE TAYLOR
P.O. BOX 4845
MIDLAND, TEXAS 79704
FAX: 505-392-3760

Sample Type: Water
Sample Condition: Intact/ Iced
Project #: EOT 1044C
Project Name: Bob Durham
Project Location: Monument, N.M.

Sampling Date: See Below
Receiving Date: 02/03/00
Analysis Date: See Below

ELT#	FIELD CODE / SAMPLE DATE	Sulfate mg/L	Chloride mg/L	Carbonate mg/L	Bicarbonate mg/L	TDS mg/L
23358	MW-3 02/03/00	82.8	80	0	300	568
23359	MW-9 02/02/00	107.8	106	0	300	660
23360	MW-10 02/02/00	109.5	89	0	300	618
23361	MW-11 02/02/00	182.5	115	0	350	823
23362	MW-13 02/02/00	89.8	115	0	370	703
23363	MW-14 02/03/00	230.0	106	0	350	840
23364	MW-15 02/03/00	178.8	106	0	350	803

QUALITY CONTROL
TRUE VALUE
% PRECISION

52.1
50.0
104

5318
5000
106

*
*
*

*
*
*

*
*
*

ANALYSIS DATE

02/12/00


02/07/00

02/12/00

02/12/00

02/11/00

METHODS: EPA 375.4, 325.3, 310, 160.1


Raland K. Tuttle

2-16-00
Date

Environmental Lab of Texas, Inc. 12600 West I-20 East Odessa, Texas 79763
 (915) 563-1800 FAX (915) 563-1713

CHAIN-OF-CUSTODY RECORD AND ANALYSIS REQUEST

COC 077

Project Manager:

JESSE TAYLOR

Phone #: (915) 664-9166

FAX #: (505) 392-3760

Company Name & Address:

ET&T
 P.O. Box 4845 MIDLAND TX 79704

Project #:

ET 1044C

Project Name:

BOB DUHAM

Project Location:

MARQUENT New Mexico

Sampler Signature:

[Signature]

LAB # (LAB USE ONLY)	FIELD CODE	# CONTAINERS	Volume/Amount	MATRIX				PRESERVATIVE METHOD				DATE	SAMPLING TIME
				WATER	SOIL	AIR	SLUDGE	OTHER	HCL	HNO3	ICE	OTHER	
MW 3		5	1.5	X					X	X	Y	2-3	1530
MW 9												2-2	1500
MW 10													1520
MW 11													1605
MW 13													1540
MW 14												2-3	1000
MW 15												2-3	1025

ANALYSIS REQUEST

TPH 418.1	
TCLP Metals Ag As Ba Cd Cr Pb Hg Se	
Total Metals Ag As Ba Cd Cr Pb Hg Se	
TCLP Volatiles	
TCLP Semi Volatiles	
TDS (16.1)	
ANIONS (300.9)	
CATIONS (600.5) 5m 4500 (old)	
PH (8.10) or 8220	
HEAVY METALS ICP SCAN (600)	

BTX 8020 (old)

Relinquished by:

[Signature]

Date:

2-3-08

Time:

1640

Received by:

[Signature]

REMARKS

Mail Result - K. Dutton

Relinquished by:

Date:

Time:

Received by:

Received by Laboratory:

Relinquished by:

Date:

Time:

Received by Laboratory:

INVOICE: LEMMA FRIST 10/15 PM

ENVIRONMENTAL LAB OF , Inc.

"Don't Treat Your Soil Like Dirt!"


ENVIRONMENTAL TECHNOLOGY GROUP, INC.
ATTN: MR. JESSE TAYLOR
P.O. BOX 4845
MIDLAND, TEXAS 79704
FAX: 505-392-2760

Sample Type: Water
Sample Condition: Intact/Iced/HCl
Project #: EOT 1044C
Project Name: Bob Durham
Project Location: Monument, N.M.

Sampling Date: 02/17/00
Receiving Date: 02/18/00
Analysis Date: 02/19/00

ELT#	FIELD CODE	BENZENE mg/L	TOLUENE mg/L	ETHYLBENZENE mg/L	m,p-XYLENE mg/L	o-XYLENE mg/L
23650	MW 17	0.001	<0.001	<0.001	<0.001	<0.001
23651	MW 18	<0.001	<0.001	<0.001	<0.001	<0.001
23652	MW 19	<0.001	<0.001	<0.001	<0.001	<0.001
23653	MW 22	<0.001	<0.001	<0.001	<0.001	<0.001
23654	MW 24	<0.001	<0.001	<0.001	<0.001	<0.001
23655	MW 25	<0.001	<0.001	<0.001	<0.001	<0.001
% IA		110	105	101	108	102
% EA		113	109	106	110	104
BLANK		<0.001	<0.001	<0.001	<0.001	<0.001

METHODS: SW 846-8021B,5030


Raland K. Tuttle

2-29-00
Date

ENVIRONMENTAL LAB OF , INC.

"Don't Treat Your Soil Like Dirt!"

ENVIRONMENTAL TECHNOLOGY GROUP, INC.
ATTN: MR. JESSE TAYLOR
P.O. BOX 4845
MIDLAND, TEXAS 79704
FAX: 505-392-3760


Sample Type: Water
Sample Condition: Intact/ Iced
Project #: EOT 1044C
Project Name: Bob Durham
Project Location: Monument, N.M.

Sampling Date: 02/17/00
Receiving Date: 02/18/00
Analysis Date: See Below

ELT#	FIELD CODE	Sulfate mg/L	Chloride mg/L	Carbonate mg/L	Bicarbonate mg/L	TDS mg/L
23650	MW 17	248	133	0	300	864
23651	MW 18	251	142	0	280	868
23652	MW 19	102	89	0	220	501
23653	MW 22	213	89	0	300	722
23654	MW 24	105	80	0	240	546
23655	MW 25	97	89	0	230	548

QUALITY CONTROL	48.5	5052	*	*	*
TRUE VALUE	50.0	5000	*	*	*
% PRECISION	97	101	*	*	*
ANALYSIS DATE	2/23/00	2/23/00	2/24/00	2/24/00	2/19/00

METHODS: EPA 375.4, 325.3, 310, 160.1


Raland K. Tuttle

2-29-00
Date

ENVIRONMENTAL LAB OF , INC.

"Don't Treat Your Soil Like Dirt!"

ENVIRONMENTAL TECHNOLOGY GROUP, INC.

ATTN: MR. JESSE TAYLOR

P.O. BOX 4845

MIDLAND, TEXAS 79704

FAX: 915-520-4310

FAX: 505-392-3760

Sample Type: Water

Sample Condition: Intact/ Iced/HCl/ 32 deg. F

Project #: EOT 2044C

Project Name: Bob Durham

Project Location: Monument, N.M.

Sampling Date: 06/09/00

Receiving Date: 06/10/00

Analysis Date: 06/13/00

ELT#	FIELD CODE	BENZENE mg/L	TOLUENE mg/L	ETHYLBENZENE mg/L	m,p-XYLENE mg/L	o-XYLENE mg/L
26574	MW 3	0.433	0.016	0.119	0.095	0.056
26575	MW 9	0.078	0.002	0.002	0.002	0.001
26576	MW 10	<0.001	<0.001	<0.001	<0.001	0.001
26577	MW 11	0.006	<0.001	<0.001	<0.001	<0.001
26578	MW 13	0.777	0.007	0.059	0.044	0.010
26579	MW 14	0.003	<0.001	<0.001	<0.001	<0.001
26580	MW 15	0.010	<0.001	<0.001	<0.001	<0.001
26581	MW 17	<0.001	<0.001	<0.001	<0.001	<0.001
26582	MW 18	<0.001	<0.001	<0.001	<0.001	<0.001
26583	MW 19	<0.001	<0.001	<0.001	<0.001	<0.001
26584	MW 20	0.004	0.001	0.001	0.003	<0.001
26585	MW 21	0.001	0.001	0.001	0.002	0.001
26586	MW 22	<0.001	<0.001	<0.001	<0.001	<0.001
26587	MW 24	<0.001	<0.001	<0.001	<0.001	<0.001
26588	MW 25	<0.001	<0.001	<0.001	<0.001	<0.001
26589	MW 26	<0.001	<0.001	<0.001	<0.001	<0.001
26590	MW 27	<0.001	<0.001	<0.001	<0.001	<0.001

% IA	90	87	89	96	88
% EA	92	90	90	97	89
BLANK	<0.001	<0.001	<0.001	<0.001	<0.001

METHODS: SW 846-8021B.5030

Umesh Rao
Umesh Rao, Ph. D.

6/16/00
Date

ENVIRONMENTAL LAB OF , INC.

"Don't Treat Your Soil Like Dirt!"

ENVIRONMENTAL TECHNOLOGY GROUP, INC.
ATTN: MR. JESSE TAYLOR
P.O. BOX 4845
MIDLAND, TEXAS 79704
FAX: 505-392-3760
FAX: 915-520-4310


Sample Type: Water
Sample Condition: Intact/ Iced/ 32 deg. F
Project #: EOT 2044C
Project Name: Bob Durham
Project Location: Monument, N.M.

Sampling Date: 06/09/00
Receiving Date: 06/10/00
Analysis Date: See Below

ELT#	FIELD CODE	Sulfate mg/L	Chloride mg/L	Carbonate mg/L	Bicarbonate mg/L	TDS mg/L
26584	MW 20	130.7	106	0	360	783
26585	MW 21	81.2	81	0	366	694
26589	MW 26	158.8	177	0	280	855
26590	MW 27	164.5	112	0	286	792

QUALITY CONTROL	56.8	5495	*	*	*
TRUE VALUE	50.0	5000	*	*	*
% PRECISION	114	110	*	*	*
ANALYSIS DATE	06/27/00	06/16/00	06/23/00	06/23/00	06/16/00

METHODS: EPA 375.4, 325.3, 310, 160.1


Raland K. Tuttle

6-27-00
Date

Environmental Lab of Texas, Inc. 12600 West I-20 E. Odessa, Texas 79763
 (915) 563-1800 FAX (915) 563-1713

CHAIN-OF-CUSTODY RECORD AND ANALYSIS REQUEST
 1067
 COC# 158

Project Manager: Jesse Taylor
 Phone # (505) 392-8731
 FAX #: (505) 392-3760

Company Name & Address: ETCI
 P.O. Box 4845 MIDLAND TX 79704

Project #: EUT 2044C
 Project Name: BOB DUREN

Project Location: Monument, NM
 Sampler Signature: Simon Casax

LAB # (LAB USE ONLY)	FIELD CODE	# CONTAINERS	Volume/Amount	MATRIX						PRESERVATIVE METHOD				SAMPLING	
				WATER	SOIL	AIR	SLUDGE	OTHER	HCL	HNO3	ICE	NONE	OTHER	DATE	TIME
MW 3		2	V	X					X		X			6-9	1240
MW 9														1305	
MW 10														1311	
MW 11														1325	
MW 13														1316	
MW 14														1340	
MW 15														1332	
MW 17														1358	
MW 18														1036	
MW 19														0912	
MW 20		5	V	X					X		X			0957	

Relinquished by: Simon Casax	Date: 10/28/08	Received by: Black	REMARKS: For Results: HOBBS OFFICE
Relinquished by:	Date:	Received by:	304
Relinquished by:	Date:	Received by Laboratory:	INVOICE: EUT 105M

TPH 418.1	TCLP Metals Ag As Ba Cd Cr Pb Hg Se	TCLP Metals Ag As Ba Cd Cr Pb Hg Se	TCLP Volatiles	TCLP Semi Volatiles	TDS 160.1	RCI	PAH 8100	CATIONS 6010	ANIONS 3000	HEAVY METALS 6010
-----------	-------------------------------------	-------------------------------------	----------------	---------------------	-----------	-----	----------	--------------	-------------	-------------------

ENVIRONMENTAL LAB OF , INC.

"Don't Treat Your Soil Like Dirt!"

ENVIRONMENTAL TECHNOLOGY GROUP, INC.
ATTN: MR. JESSE TAYLOR
P.O. BOX 4845
MIDLAND, TEXAS 79704
FAX: 915-520-4310
FAX: 505-397-4701

Sample Type: Water
Sample Condition: Intact/ Iced/ HCl/ 34 deg. F
Project #: EOT 2044C
Project Name: Bob Durham
Project Location: Monument, N.M.

Sampling Date: 07/13/00
Receiving Date: 07/14/00
Analysis Date: 07/23/00

ELT#	FIELD CODE	BENZENE mg/L	TOLUENE mg/L	ETHYLBENZENE mg/L	m,p-XYLENE mg/L	o-XYLENE mg/L
28189	MW-29	<0.001	<0.001	<0.001	<0.001	<0.001
28190	MW-30	<0.001	0.001	0.001	0.002	<0.001
28191	MW-31	0.002	0.002	<0.001	<0.001	<0.001
28192	MW-32	<0.001	0.003	<0.001	<0.001	<0.001
28193	MW-33	0.008	0.002	<0.001	0.002	<0.001
28194	MW-34	<0.001	<0.001	<0.001	<0.001	<0.001
28195	MW-35	<0.001	<0.001	<0.001	<0.001	<0.001
28196	MW-36	<0.001	<0.001	<0.001	<0.001	<0.001

% IA	98	95	98	112	100
% EA	95	91	94	106	95
BLANK	<0.001	<0.001	<0.001	<0.001	<0.001

METHODS: SW 846-8021B.5030

Raland K. Tuttle
Raland K. Tuttle

7-26-00
Date

ENVIRONMENTAL LAB OF , INC.

"Don't Treat Your Soil Like Dirt!"

ENVIRONMENTAL TECHNOLOGY GROUP, INC.

ATTN: MR. JESSE TAYLOR

P.O. BOX 4845

MIDLAND, TEXAS 79704

FAX: 505-397-4701

FAX: 915-520-4310

Sample Type: Water

Sample Condition: Intact/ Iced/ 34 deg. F

Project #: EOT 2044C

Project Name: Bob Durham

Project Location: Monument, N.M.


Sampling Date: 07/13/00

Receiving Date: 07/14/00

Analysis Date: See Below

ELT#	FIELD CODE	Sulfate mg/L	Chloride mg/L	Carbonate mg/L	Bicarbonate mg/L	TDS mg/L
28189	MW 29	308	292	0	344	1406
28190	MW 30	90	106	0	320	615
28191	MW 31	62	168	0	420	801
28192	MW 32	136	97	0	323	676
28193	MW 33	199	118	0	332	796
28194	MW 34	212	142	0	293	825
28195	MW 35	175	102	0	273	645
28196	MW 36	168	97	0	267	646
QUALITY CONTROL		47.7	5406	*	*	*
TRUE VALUE		50.0	5000	*	*	*
% PRECISION		95	108	*	*	*
ANALYSIS DATE		07/19/00	07/18/00	7/18/00	07/18/00	07/19/00

METHODS: EPA 375.4, 325.3, 310, 160.1


Raland K. Tuttle

7-27-00
Date

Environmental Lab of Texas, Inc. 12600 West I-20 East Odessa, Texas 79763
(915) 563-1800 FAX (915) 563-1713

CHAIN-OF-CUSTODY RECORD AND ANALYSIS REQUEST

CC# 187

Project Manager: J TAYLOR
Phone #: (505) 397-4882
FAX #: (505) 397-4701

Company Name & Address:
ETGI, 2540 W. Marland, Hobbs, NM 88240

Project #:
EOT 2044C

Project Location:
MONUMENT NM

Project Name:
BOB DURHAM

Sampler Signature:
Samuel S. Taylor

ANALYSIS REQUEST

1 of 1

Company Name & Address: ETGI, 2540 W. Maryland, Hobbs, NM 88240										Project Name: BOB DURHAM													
Project #: EOT 2094C										Project Location: MONUMENT NM													
Project Location:										Sampler Signature: <i>Randy Smith</i>													
LAB # (LAB USE ONLY)	FIELD CODE	# CONTAINERS	Volume/Amount	MATRIX			PRESERVATIVE METHOD			SAMPLING		TIME											
				WATER	SOIL	AIR	SLUDGE	OTHER	HCL	HNO3	ICE		NONE	OTHER	DATE								
M6-29		5	5m	X					X	X	X	7-13 10:50											
Mw-30												7-13 11:16											
Mw-31												7-13 11:42											
Mw-32												7-13 12:14											
Mw-33												7-13 2:04											
Mw-34												7-13 2:18											
Mw-35												7-13 2:47											
Mw-36												7-13 3:06											

BTX 80120/5030	X
TPH 418.1	
TCLP Metals Ag As Ba Cd Cr Pb Hg Se	
Total Metals Ag As Ba Cd Cr Pb Hg Se	
TCLP Volatiles	
TCLP Semi Volatiles	
TDS	X
RCI	
QNH EPA 8100	X
CATIONS EPA 6100	X
ANIONS EPA 3100	X
HEAVY METALS (ICP SCAN)	X
EPA 6010	

Relinquished by: *Samuel S. Taylor* Date: 7-14-00 Time: 12:30

Received by: *Dee Dee Peltier*

Relinquished by: *Samuel S. Taylor* Date: 7-14-00 Time: 1700

Received by: *Dee Dee Peltier*

Relinquished by: *Samuel S. Taylor* Date: 7-14-00 Time: 1700

Received by: *Dee Dee Peltier*

REMARKS

34°

ENVIRONMENTAL**LAB OF , INC.***"Don't Treat Your Soil Like Dirt!"*

ENVIRONMENTAL TECHNOLOGY GROUP, INC.

ATTN: BETH ALDRICH

P.O. BOX 4845

MIDLAND, TEXAS 79704

FAX: 915-520-4310

FAX: 505-397-4701

SampleType: Water

Sample Condition: Intact/ Iced/ HCl

Project #: EOT 2044C

Project Name: Bob Durham

Project Location: Monument, N.M.

Sampling Date: 09/20/00

Receiving Date: 09/22/00

Analysis Date: 09/28/00

ELT#	FIELD CODE	BENZENE mg/L	TOLUENE mg/L	ETHYLBENZENE mg/L	m,p-XYLENE mg/L	o-XYLENE mg/L	TOTAL BTX mg/L
31197	MW 3	0.138	0.004	0.120	0.100	0.029	0.391
31198	MW 9	0.012	<0.001	<0.001	<0.001	<0.001	0.012
31199	MW 10	0.003	<0.001	<0.001	<0.001	0.002	0.005
31200	MW 11	0.014	<0.001	<0.001	<0.001	<0.001	0.014
31201	MW 13	0.946	<0.002	0.076	0.163	0.044	1.23
31202	MW 14	0.005	<0.001	<0.001	<0.001	<0.001	0.005
31203	MW 15	0.012	<0.001	<0.001	<0.001	<0.001	0.012
31204	MW 17	0.001	<0.001	<0.001	<0.001	<0.001	0.001
31205	MW 18	<0.001	0.001	0.001	0.006	0.003	0.011
31206	MW 19	<0.001	<0.001	<0.001	<0.001	<0.001	<0.001
31207	MW 20	0.002	<0.001	<0.001	<0.001	<0.001	0.002
31214	MW 21	0.004	<0.001	<0.001	0.001	<0.001	0.005
31215	MW 22	<0.001	<0.001	<0.001	<0.001	<0.001	<0.001
31216	MW 24	<0.001	<0.001	<0.001	<0.001	<0.001	<0.001

% IA	98	96	96	100	92
% EA	87	89	86	89	90
BLANK	<0.001	<0.001	<0.001	<0.001	<0.001

METHODS: SW 846-8021B,5030

Raland K. Tuttle
Raland K. Tuttle

9-30-00
Date

ENVIRONMENTAL LAB OF , INC.

"Don't Treat Your Soil Like Dirt!"

ENVIRONMENTAL TECHNOLOGY GROUP, INC.

ATTN: BETH ALDRICH

P.O. BOX 4845

MIDLAND, TEXAS 79704

FAX: 915-520-4310

FAX: 505-397-4701

SampleType: Water

Sample Condition: Intact/ Iced/ HCl

Project #: EOT 2044C

Project Name: Bob Durham

Project Location: Monument, N.M

Sampling Date: 09/20/00

Receiving Date: 09/22/00

Analysis Date: 09/29/00

ELT#	FIELD CODE	BENZENE mg/L	TOLUENE mg/L	ETHYL BENZENE mg/L	m,p-XYLENE mg/L	o-XYLENE mg/L	TOTAL BTX mg/L
31217	MW 25	<0.001	<0.001	<0.001	<0.001	<0.001	<0.001
31218	MW 26	<0.001	<0.001	<0.001	<0.001	<0.001	<0.001
31219	MW 27	<0.001	<0.001	<0.001	<0.001	<0.001	<0.001
31220	MW 29	<0.001	<0.001	<0.001	<0.001	<0.001	<0.001
31221	MW 30	<0.001	<0.001	<0.001	<0.001	<0.001	<0.001
31222	MW 31	<0.001	<0.001	0.001	<0.001	<0.001	0.001
31223	MW 33	<0.001	<0.001	<0.001	<0.001	<0.001	<0.001
31224	MW 34	<0.001	<0.001	<0.001	<0.001	<0.001	<0.001
31225	MW 35	<0.001	<0.001	<0.001	<0.001	<0.001	<0.001
31226	MW 36	<0.001	<0.001	<0.001	<0.001	<0.001	<0.001
31227	EB 1	<0.001	<0.001	<0.001	<0.001	<0.001	<0.001

% IA	93	92	92	95	86
% EA	98	97	97	96	93
BLANK	<0.001	<0.001	<0.001	<0.001	<0.001

METHODS: SW 846-8021B,5030

Raland K. Tuttle
Raland K. Tuttle

9-30-00
Date

Environmental Lab of Texas, Inc. 12600 West I-20 East Odessa, Texas 79763
(915) 563-1800 FAX (915) 563-1713

CHAIN-OF-CUSTODY RECORD AND ANALYSIS REQUEST

COC # 235

Project Manager: BETH ALARICH		Phone #: (805) 397-4882		ANALYSIS REQUEST		1483													
Company Name & Address: ETGZ 2540 W MARLAND HOORS NM		FAX #: (505) 397-4701																	
Project #: EOT 2044C		Project Name: BOB DURHAM																	
Project Location: MONUMENT NM		Sample Signature: <i>[Signature]</i>																	
LAB # (LAB USE ONLY)	FIELD CODE	# CONTAINERS	Volume/Amount	MATRIX			PRESERVATIVE METHOD			SAMPLING		TIME	TPH 418.1	TCLP Metals Ag As Ba Cd Cr Pb Hg Se	TCLP Volatiles	TCLP Semi Volatiles	TDS	ACI	
				WATER	SOIL	AIR	SLUDGE	OTHER	HCL	HNO3	ICE								NONE
31197	MW 3	2	V	X				X	X			920	1136	X					
31198	MW 9											1435							
31199	MW 10											1428							
31200	MW 11											1345							
31201	MW 13											1420							
31202	MW 14											1334							
31203	MW 15											1303							
31204	MW 17											0852							
31205	MW 18											0913							
31206	MW 19											1225							
31207	MW 20											1145							
Relinquished by: <i>[Signature]</i>		Date: 9/22/00	Time: 7:30	Received by: <i>[Signature]</i>		REMARKS: INVOICE: EOTT FAX RESULTS: HOORS OFFICE MAIL RESULTS: EOTT													
Relinquished by: <i>[Signature]</i>		Date: 9/22/00	Time: 8:00 AM	Received by Laboratory: <i>[Signature]</i>															
Relinquished by: <i>[Signature]</i>		Date: 9/22/00	Time: 11:45 AM	Received by Laboratory: <i>[Signature]</i>															

Environmental Lab of Texas, Inc. 12600 West 1-20 East Odessa, Texas 79763
(915) 563-1800 FAX (915) 563-1713

CHAIN-OF-CUSTODY RECORD AND ANALYSIS REQUEST
COT 235

Project Manager:		ANALYSIS REQUEST		2083	
Company Name & Address:		Project Name:		Project Location:	
BETH ALONCA		BOB DURHAM		MONUMENT NM	
2540 W MARLBORO HOBBS NM		EOT 2044C		EOT 2044C	
Phone #: (805) 397-4882		FAX #: (328) 397-4741		FAX #: (328) 397-4741	
Project #:		Supplier Signature:		Supplier Signature:	
EOT 2044C		[Signature]		[Signature]	
FIELD CODE		# CONTAINERS		VOLUME/ANNUAL	
LAS # (LAB USE ONLY)		MATERIAL		PRESERVATIVE METHOD	
		WATER		NONE	
		SLUDGE		ICE	
		AIR		HNO3	
		OTHER		HCL	
		DATE		OTHER	
		TIME		TIME	
31214	MW 21	2	V X	X	9-20 12:5
31215	MW 22				11:51
31216	MW 24				12:32
31217	MW 25				12:40
31218	MW 26				12:44
31219	MW 27				11:48
31220	MW 29				12:54
31221	MW 30				13:04
31222	MW 31				13:15
31223	MW 33				13:25
31224	MW 34				09:36
Relinquished by:		Date:	9-22-00	REMARKS:	
[Signature]				INVOICE: EOTT	
Relinquished by:		Date:	9/22/00	FAX RESULTS: HOBBS OFFICE	
[Signature]				MAIL RESULTS: EOTT	
Relinquished by:		Date:	9/22/00		
[Signature]					

ENVIRONMENTAL LAB OF , INC.

"Don't Treat Your Soil Like Dirt!"

ENVIRONMENTAL TECHNOLOGY GROUP, INC.
ATTN: BETH ALDRICH
P.O. BOX 4845
MIDLAND, TEXAS 79704
FAX: 915-520-4310


Sample Type: Water
Sample Condition: Intact/ Iced/ HCl/ -0.5 deg. C
Project #: EOT 2044C/ TNM-LF-2000-7
Project Name: Bob Durham
Project Location: Monument, N.M.

Sampling Date: 12/20/00
Receiving Date: 12/22/00
Analysis Date: 12/27/00

ELT#	FIELD CODE	BENZENE mg/L	TOLUENE mg/L	ETHYLBENZENE mg/L	m,p-XYLENE mg/L	o-XYLENE mg/L
35585	MW 3	0.117	0.002	0.044	0.038	0.003
35586	MW 9	0.022	<0.001	0.003	0.003	<0.001
35587	MW 10	0.004	<0.001	<0.001	<0.001	<0.001
35588	MW 11	0.005	<0.001	<0.001	<0.001	<0.001
35589	MW 13	0.673	0.002	0.092	0.158	0.054
35590	MW 14	<0.001	<0.001	<0.001	<0.001	<0.001
35591	MW 15	0.004	<0.001	<0.001	<0.001	<0.001
35592	MW 17	<0.001	<0.001	<0.001	<0.001	<0.001
35593	MW 19	<0.001	<0.001	<0.001	<0.001	<0.001
35594	MW 20	<0.001	<0.001	<0.001	<0.001	<0.001
35595	MW 21	<0.001	<0.001	<0.001	0.001	<0.001
35596	MW 22	<0.001	<0.001	<0.001	<0.001	<0.001
35597	MW 24	<0.001	<0.001	<0.001	<0.001	<0.001

%IA	85	85	86	90	86
%EA	90	85	91	92	86
BLANK	<0.001	<0.001	<0.001	<0.001	<0.001

METHODS: EPA SW 846-8021B, 5030


Raland K. Tuttle

12-29-00
Date

ENVIRONMENTAL LAB OF , INC.

"Don't Treat Your Soil Like Dirt!"

ENVIRONMENTAL TECHNOLOGY GROUP, INC.
ATTN: BETH ALDRICH
P.O. BOX 4845
MIDLAND, TEXAS 79704
FAX: 915-520-4310


Sample Type: Water
Sample Condition: Intact/ Iced/ HCl/ -0.5 deg. C
Project #: EOT 2044C/ TNM-LF-2000-7
Project Name: Bob Durham
Project Location: Monument, N.M.


Sampling Date: 12/20/00
Receiving Date: 12/22/00
Analysis Date: 12/28/00

ELT #	FIELD CODE	BENZENE mg/L	TOLUENE mg/L	ETHYLBENZENE mg/L	m,p-XYLENE mg/L	o-XYLENE mg/L
35598	MW 25	<0.001	<0.001	<0.001	<0.001	<0.001
35599	MW 26	<0.001	<0.001	<0.001	<0.001	<0.001
35600	MW 27	<0.001	<0.001	<0.001	<0.001	<0.001
35601	MW 29	<0.001	<0.001	<0.001	<0.001	<0.001
35602	MW 30	<0.001	<0.001	<0.001	<0.001	<0.001
35603	MW 31	0.004	<0.001	<0.001	<0.001	<0.001
35604	MW 33	<0.001	<0.001	<0.001	<0.001	<0.001
35605	MW 34	<0.001	<0.001	<0.001	<0.001	<0.001
35606	MW 35	<0.001	<0.001	<0.001	<0.001	<0.001
35607	MW 36	<0.001	<0.001	<0.001	<0.001	<0.001
35608	EB 1	<0.001	<0.001	<0.001	<0.001	<0.001

%IA	87	90	93	96	91
%EA	86	86	88	91	86
BLANK	<0.001	<0.001	<0.001	<0.001	<0.001

METHODS: EPA SW 846-8021B, 5030


Roland K. Tuttle


Date

