




PROPOSED WELLBORE SCHEMATIC

2/13/01 @ 2:15 PM
OK Bill Ordemann
Ref

Lease: VPR A 39
Field: Canadian River
County: Colfax
State: New Mexico
Survey: 685' FSL and 1779' FWL
Sec. 20-T32N-R20E
Spud: 2/12/00

2/28/00 Perf 4 squeeze shots @ 2240'. Pump water, gel, LCM and sand to seal well bore for squeeze. No success.
4/5/00 TIH w/bit and tag @ 2270'. Drill float shoe.
4/6/00 Pump LCM down 5 1/2".
4/7/00 Pump 50 sx Midcon 2. Displace w/51 bbls.
4/8/00 Run CBL. Tag @ 2013'. No cmt 1800-1900', TOC 1240'.
4/9/00 Perf 4 holes @ 1240'. Pump 50 bbls FW followed by 125 sks Midcon 2, max 200 psi. Sm blow.
4/10/00 Tag @ 650' with WL. CBL shows no cmt above 650'.
4/27-5/1/00 MIRU CU. Drill out cmt f/700'-2040'. Bit plugging and torqueing up @ 2040'.
5/9/00 MIRU foam unit. Attempt to drill. Bit plugging.
5/10/00 Junk in hole. Cut core 2040-44' w/no recovery.
5/11/00 TIH w/shoe and wash to 2052. Bail steel casing threads out of hole.
5/12/00 TIH w/tapered mill. Tag @ 2047' & mill to 2050'. Fall thru. Tag @ 2055'. Ream to 2058'. TIH and tag @ 2272'. TOH. TIH open ended. Dump 15 gals sand down tubing. TOH w/tbg. Load hole w/FW.
5/13/00 Run CBL. Tag @ 2038'. TOC 800'. Fill hole w/10 bbls gel @ 6.5 bpm, 300 psi. Run CBL. Tag @ 2212'. No cmt f/2038'-2212'. Csg prob f/2038'-2050'.
10/9/00 Letter sent to David Vackar (VPR) notifying of P&A intent.

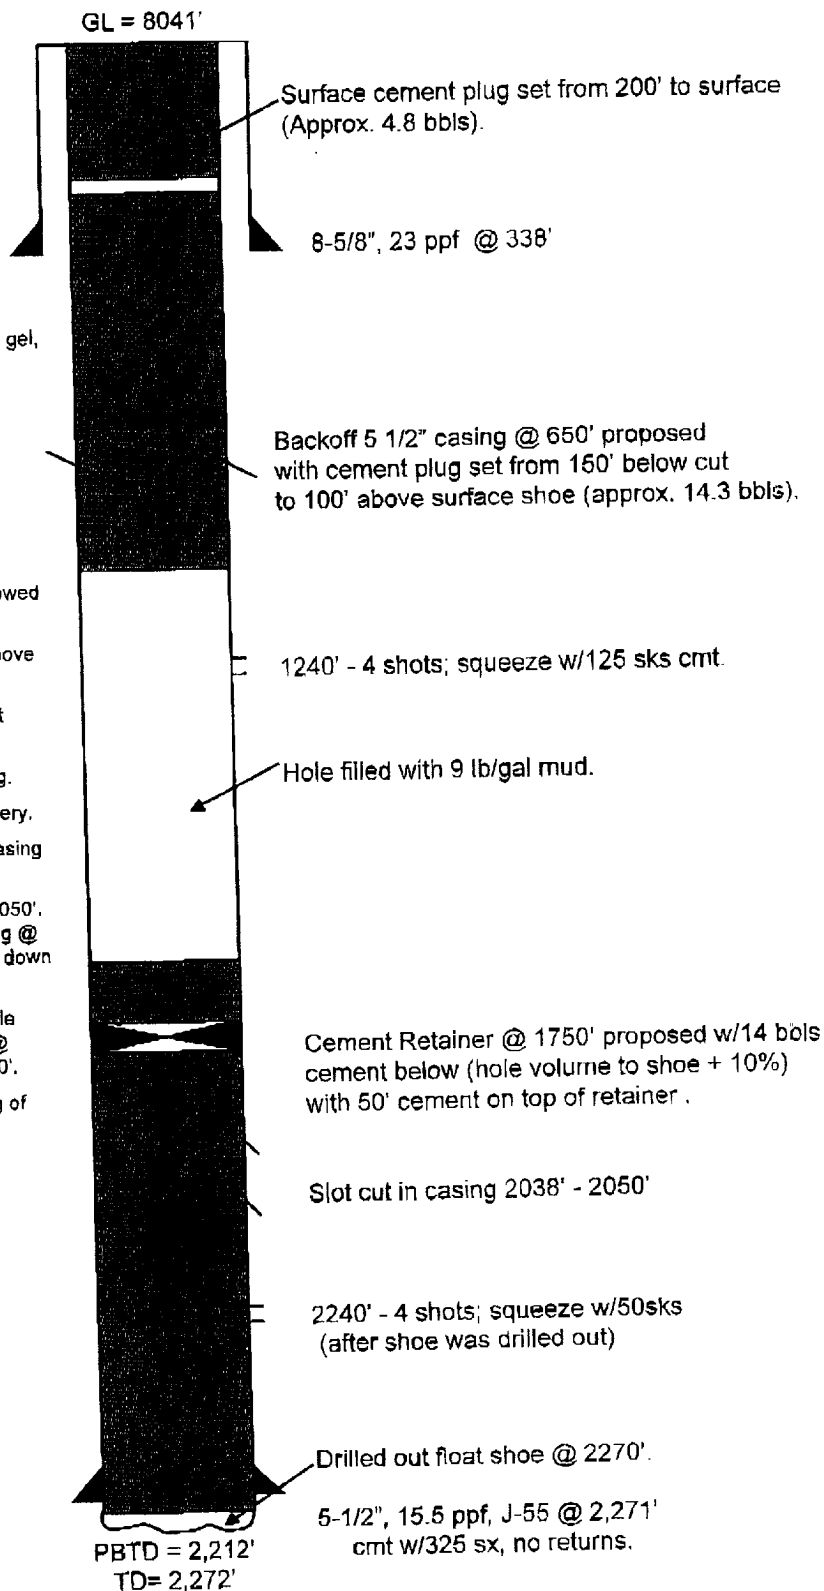

Prepared by: Bill Ordemann
Date: February 13, 2001
