


✓

# SCOUT REPORT NEW MEXICO OIL CONSERVATION COMMISSION

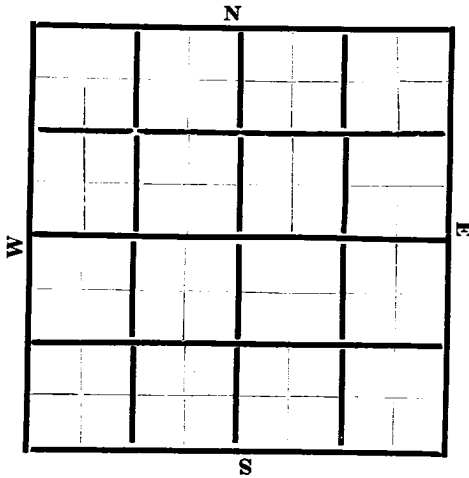

Company Carbonic Chemicals Corp  
 Farm Name Mitchell Well No. 2  
 Land Classification Fee  
SW 20 Twp. 19N Range 30E County Harding  
 Feet from Lines: N. 860 S. 760 E. 760 W. 760  
 Elevation 4220' Oklahoma Oil works  
 Method Rotary  
 Contractor Torrey & Feaster Scout B  
 Spudded \_\_\_\_\_ Completed \_\_\_\_\_ Initial Production \_\_\_\_\_  
 Bond Status \_\_\_\_\_

ACID RECORD

CASING AND CEMENTING RECORD  
AMOUNT

| Size | Feet | Inches | Sax<br>Cement |
|------|------|--------|---------------|
| 15   | 66   |        | 50            |
| 10   | 1913 |        | 450           |

| Gals.   |  | Prod.       | Date |
|---------|--|-------------|------|
|         |  | Prod.       | Date |
| Top Pay |  | Total Depth |      |

SHOOTING RECORD

| No. of Quarts | Shot at | Feet |
|---------------|---------|------|
| No. of Quarts | Shot at | Feet |

| Date  |  | Date |  |
|-------|--|------|--|
| 10-25 | New Location   |      |  |
| 11-10 | Gray lime @ 135'   |      |  |
| 11-17 | Lime @ 955' - Small gas @ 800' B   |      |  |
| 11-28 | HEAVY FLOW OF GAS STRUCK AT 1670'  |      |  |
| 12-2  | Drilling in red sand @ 1992  |      |  |
| 12-9  | Drilling in granite @ 2083<br>C.O <sub>2</sub> gas @ 506' - 815' - 2070<br>to 2080 getting ready to bail<br>out and complete.  |      |  |
| 1-5   | Completed for 5,000,000 cu ft CO <sub>2</sub><br>gas with 700 lbs pressure<br>Y.D. 2093-1914 ft 10" cemented<br>with 564 sacks |      |  |

