


Well ID: 30-015-26753

Well Name: G J WEST COOP UNIT #96

Event#: 6.00

Report Dates: 06/10/2011

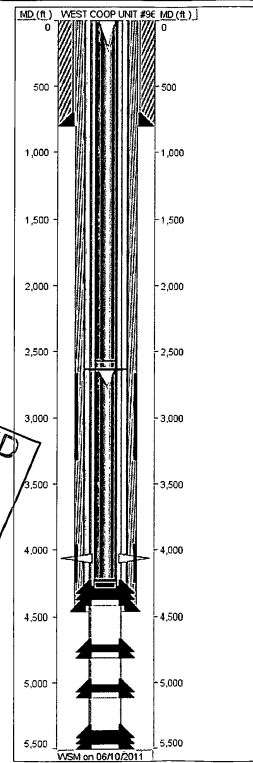

PIPE SPECIFICATION

STRING NAME	SECTION NAME	JOINT COUNT	START DEPTH	END DEPTH	LENGTH	OD SIZE	ID SIZE	WT GRDNT	GRD	CONN
SURFACE	CASING	1	0.00	801.00	801.00	8.63	8.10	24.0	J-55	
PRODUCTION	CASING	1	0.00	4467.00	4467.00	5.50	4.89	17.0	J-55	
TUBING	BULL PLUG		4298.60	4299.30	0.70	2.88	2.50	6.5	J-55	8-
TUBING	MUD ANCHOR	2	4236.18	4298.60	62.42	2.88	2.50	6.5	J-55	8-
TUBING	SLOTTED MUD		4228.18	4236.18	8.00	2.88	2.50	6.5	J-55	8-
TUBING	SEAT NIPPLE		4227.08	4228.18	1.10	2.88	2.50	6.5	J-55	8-
TUBING	TUBING	51	2635.37	4227.08	1591.71	2.88	2.50	6.5	J-55	8-
TUBING	TUBING ANCHOR		2632.67	2635.37	2.70	5.50	4.89	17.0	J-55	8-
TUBING	TUBING	2	2570.25	2632.67	62.42	2.88	2.50	6.5	J-55	8-
TUBING	MARKER JOINT		2568.25	2570.25	2.00	2.88	2.50	6.5	J-55	8-
TUBING	TUBING	82	0.00	2568.25	2568.25	2.88	2.50	6.5	J-55	8-
PRODUCTION LINER	FLOAT SHOE		5506.93	5508.38	1.45	4.00	3.43	11.6	L80	UTFJ
PRODUCTION LINER	CASING	1	5464.85	5506.93	42.08	4.00	3.43	11.6	L80	UTFJ
PRODUCTION LINER	CENTRALIZER		5463.48	5464.85	1.37	4.00	3.43	11.6	L80	UTFJ
PRODUCTION LINER	FLOAT COLLAR		5461.83	5463.48	1.65	4.00	3.43	11.6	L80	UTFJ
PRODUCTION LINER	CASING	1	5418.59	5461.83	43.24	4.00	3.43	11.6	L80	UTFJ
PRODUCTION LINER	CENTRALIZER		5417.22	5418.59	1.37	4.00	3.43	11.6	L80	UTFJ
PRODUCTION LINER	CASING	7	5115.49	5417.22	301.73	4.00	3.43	11.6	L80	UTFJ
PRODUCTION LINER	CENTRALIZER		5114.12	5115.49	1.37	4.00	3.43	11.6	L80	UTFJ
PRODUCTION LINER	CASING	1	5070.87	5114.12	43.25	4.00	3.43	11.6	L80	UTFJ
PRODUCTION LINER	CENTRALIZER		5069.50	5070.87	1.37	4.00	3.43	11.6	L80	UTFJ
PRODUCTION LINER	CASING	6	4812.56	5069.50	256.94	4.00	3.43	11.6	L80	UTFJ
PRODUCTION LINER	CENTRALIZER		4811.19	4812.56	1.37	4.00	3.43	11.6	L80	UTFJ
PRODUCTION LINER	CASING	1	4767.89	4811.19	43.30	4.00	3.43	11.6	L80	UTFJ
PRODUCTION LINER	CENTRALIZER		4766.52	4767.89	1.37	4.00	3.43	11.6	L80	UTFJ
PRODUCTION LINER	CASING	8	4420.39	4766.52	346.13	4.00	3.43	11.6	L80	UTFJ
PRODUCTION LINER	CENTRALIZER		4419.02	4420.39	1.37	4.00	3.43	11.6	L80	UTFJ
PRODUCTION LINER	CASING	1	4375.84	4419.02	43.18	4.00	3.43	11.6	L80	UTFJ
PRODUCTION LINER	CENTRALIZER		4374.47	4375.84	1.37	4.00	3.43	11.6	L80	UTFJ
PRODUCTION LINER	CASING	1	4330.92	4374.47	43.55	4.00	3.43	11.6	L80	UTFJ
PRODUCTION LINER	DV TOOL		4327.87	4330.92	3.05	4.00	3.43	11.6	L80	UTFJ
PRODUCTION LINER	CASING	101	1.31	4327.87	4326.56	4.00	3.43	11.6	L80	UTFJ
PRODUCTION LINER	CROSS OVER UP		-0.69	1.31	2.00	4.00	3.43	11.6	L80	UTFJ
PRODUCTION LINER	LINER HANGER		-1.45	-0.69	0.76	4.00	3.43	11.6	L80	UTFJ

CEMENTING

STRING NAME	STAGE #	LEAD TOP (est) (ft)	LEAD TOP (ver) (ft)	TAIL TOP (est) (ft)	TAIL TOP (ver) (ft)
SURFACE	1	0.0	0.0		
PRODUCTION	1	0.0	0.0		

BHA STRING							
DRILL EQUIP CODE		DESCRIPTION	LENGTH	OD SIZE	ID SIZE		
PERFORATION							
ZONE	JOB REPORT DATE	ZONE NAME	TOP DEPTH	BOTTOM DEPTH	HOLE SIZE	PEN SIZE	SQUEEZED
3	05/25/2011	PADDOCK	3856.00	4270.00			N
5	06/13/1991	SAN ANDRES	2663.00	3319.00			Y
